

Contract No. HK/2009/01
Wan Chai Development Phase II – Central -Wan Chai Bypass at
Hong Kong Convention and Exhibition Centre

Construction Activities For Three Months Rolling

Construction Activities	Dec 2016	Jan 2017	Feb 2017	Mar 2017	Apr 2017
Reinstatement of Amenity Area					
Road and Drain Works					

Activity ID		Activity Name		Ori Dur	Rem Dur	Scheduled/ Actual Start	Scheduled/ Actual Finish	Total Float	Calendar	2017																
										April				May				June				July				
										26	02	09	16	23	30	07	14	21	28	04	11	18	25	02	09	16
Three Months Rolling Programme 2017-04-20 (dd 20-Apr-17)																										
Programme Milestones (Revised up to EOTO No.21)																										
Contractual Completion Dates																										
KDC0170	Section 9B Works (2134 days) - CWB Structure (CH3400 Eastward) (2-Dec-15 Noon)	0	0		20-Apr-17*	-504	Calendar Day																			
KDC0180	Section 10 Works (2469 days) - CWB Structure (CH3400 Westward) (31-Oct-16)	0	0		20-Apr-17*	-170	Calendar Day																			
KDC0190	Section 11 Works (2673 days) - Remainder of Works/ Works Completion Date (23-May-17)	0	0		23-May-17*	0	Calendar Day																			
Soft Landscaping & Establishment Key Dates																										
KDC0200	Section 11A Works (2440 days) - Remaining Landscape Softworks (03-Oct-16 Noon)	0	0		20-Apr-17*	-198	Calendar Day																			
KDC0220	Section 12 Works (2672 days) - Protection and Preservation of Existing Trees (22-May-17 Noon)	0	0		22-May-17*	0	Calendar Day																			
Section 8A of the Works - Reprovisioning of Wan Chai Ferry Pier in Area 8																										
Outstanding Works																										
S8A-OUT-1040	Relocation of fire hydrant near Ferry Pier	10	10	14-Jul-17	25-Jul-17	-58	HK Working Day																			
S8A-OUT-1060	Reinstatement works of the flooring inside the rooms under staircase ST-01 of the Ferry Pier	12	12	03-Jul-17	14-Jul-17	-58	HK Working Day																			
S8A-OUT-1070	Reinstatement works of the flooring under the temporary covered walkway	6	6	14-Jul-17	20-Jul-17	-54	HK Working Day																			
Section 8B of the Works - Temporary Covered Walkway & Works in Area 8																										
Temporary Covered Walkway																										
S8B-TCW-02300	Temp Covered Walkway - Construct the remaining Type 4 Covered Walkway at west wing	36	36	17-Jun-17	27-Jul-17	-60	HK Working Day																			
Section 9B of the Works - CWB Tunnel Structure (CH3400 - CH3796)																										
Tunnel Portion 1 (CH3500-CH3630)																										
CWB Structural Works																										
Outstanding Works																										
S9B-T1-OUT-1010	TB1 - Remedial works of the cross road ducts	25	0	12-Oct-16 A	15-Apr-17 A		Calendar Day																			
S9B-T1-OUT-1030	TB1 - Remedial works against water leakage identified inside the OHVD cells	30	0	14-Mar-17 A	12-Apr-17 A		Calendar Day																			
Tunnel Portion 2 (CH3425-CH3500)																										
CWB Structural Works																										
Outstanding Works																										
S9B-T2-OUT-1010	TB2 - Remedial works of the cross road ducts	25	7	12-Oct-16 A	26-Apr-17	-511	Calendar Day																			
S9B-T2-OUT-1020	TB2 - Remedial works against water leakage identified inside the OHVD cells	25	5	12-Oct-16 A	24-Apr-17	29	Calendar Day																			
Tunnel Portion 3 & Tunnel Portion 4 (CH3630-CH3790)																										
CWB Structural Works																										
S9B-T34-7400	ELS (S1) Removal - Bay 1 to Bay 8	28	28	08-Jun-17	06-Jul-17	-503	Calendar Day																			
Tunnel Portion 5 (CH3400-CH3425)																										
Bay 13 (Eastern End Bay)																										
S9B-T5-B13-1020	Base Slab - Rebar Fixing	10	0	11-Feb-17 A	30-Mar-17 A		Calendar Day																			
S9B-T5-B13-1030	Base Slab - Concrete	1	0	31-Mar-17 A	31-Mar-17 A		Calendar Day																			
S9B-T5-B13-1040	Base Slab - Curing	4	0	01-Apr-17 A	04-Apr-17 A		Calendar Day																			
S9B-T5-B13-1050	Wall (North) - Waterproofing & Working Platform	4	0	10-Apr-17 A	14-Apr-17 A		Calendar Day																			
S9B-T5-B13-1060	Wall (North) - Rebar Fixing	3	0	15-Apr-17 A	17-Apr-17 A		Calendar Day																			
S9B-T5-B13-1070	Wall (North) - Formwork	2	0	18-Apr-17 A	19-Apr-17 A		Calendar Day																			
S9B-T5-B13-1080	Wall (North) - Concrete	1	1	20-Apr-17	20-Apr-17	-546	Calendar Day																			
S9B-T5-B13-1090	Wall (North) - Curing & Formwork Dismantling	3	3	21-Apr-17	23-Apr-17	-546	Calendar Day																			
S9B-T5-B13-1100	Wall (South) - Waterproofing & Working Platform	4	0	10-Apr-17 A	13-Apr-17 A		Calendar Day																			
S9B-T5-B13-1110	Wall (South) - Rebar Fixing	3	0	14-Apr-17 A	16-Apr-17 A		Calendar Day																			
S9B-T5-B13-1120	Wall (South) - Formwork	2	0	17-Apr-17 A	18-Apr-17 A		Calendar Day																			
S9B-T5-B13-1130	Wall (South) - Concrete	1	0	19-Apr-17 A	19-Apr-17 A		Calendar Day																			
S9B-T5-B13-1140	Wall (South) - Curing & Formwork Dismantling	3	3	20-Apr-17	22-Apr-17	-549	Calendar Day																			
S9B-T5-B13-1150	Wall (Middle) - Rebar Fixing & Working Platform	4	0	12-Mar-17 A	12-Apr-17 A		Calendar Day																			
S9B-T5-B13-1160	Wall (Middle) - Formwork	2	0	13-Apr-17 A	14-Apr-17 A		Calendar Day																			
S9B-T5-B13-1170	Wall (Middle) - Concrete	1	0	15-Apr-17 A	15-Apr-17 A		Calendar Day																			
S9B-T5-B13-1180	Wall (Middle) - Curing & Formwork Dismantling	3	0	16-Apr-17 A	19-Apr-17 A		Calendar Day																			
S9B-T5-B13-1185	Construct Roadside Barriers	6	2	12-Apr-17 A	21-Apr-17	-549	Calendar Day																			
S9B-T5-B13-1230	OHVD Base Slab (North) - Scaffolding Erection	10	10	22-Apr-17	01-May-17	-549	Calendar Day																			
S9B-T5-B13-1240	OHVD Base Slab (North) - Formwork & Rebar Fixing	7	7	29-Apr-17	05-May-17	-546	Calendar Day																			
S9B-T5-B13-1250	OHVD Base Slab (North) - Concrete & Curing	2	2	06-May-17	07-May-17	-546	Calendar Day																			

◆ Milestone

◆ Critical Milestones

█ Current Works

█ Critical Works

█ Remaining Level of Effort

CHUN WO - CRGL
JOINT VENTURE

CEDD CONTRACT NO. HK/2009/02
WD II - Central Wanchai Bypass at Wan Chai East (Contract 2)
3-MONTH ROLLING PROGRAMME (dd 20-Apr-17)

Date	Revision	Checked	Approved
	Rev. Programme (08-Apr-...		

[illegible][illegible]

[illegible]

[illegible]

- ◆ Milestone
- ◆ Critical Milestones
- Current Works
- Critical Works
- Remaining Level of Effort

CEDD CONTRACT NO. HK/2009/02
WD II - Central Wanchai Bypass at Wan Chai East (Contract 2)
3-MONTH ROLLING PROGRAMME (dd 20-Apr-17)

[illegible]

- ◆ Milestone
- ◆ Critical Milestones
- Current Works
- Critical Works
- Remaining Level of Effort

CEDD CONTRACT NO. HK/2009/02
WD II - Central Wanchai Bypass at Wan Chai East (Contract 2)
3-MONTH ROLLING PROGRAMME (dd 20-Apr-17)

[illegible]

Activity ID	Activity Name	Ori Dur	Rem Dur	Scheduled/ Actual Start	Scheduled/ Actual Finish	Total Float	Calendar	2017															
								April				May				June				July			
								26	02	09	16	23	30	07	14	21	28	04	11	18	25	02	09
S10-T5-B2-1400	Construct Roadside Barriers	5	4	20-Feb-17 A	23-Apr-17	-174	Calendar Day	Construct Roadside Barriers, Construct Roadside Barriers															
Bay 1 (3 Cells) (Western End Bay)																							
S10-T5-B1-1050	Wall (North) - Waterproofing & Working Platform	4	0	22-Mar-17 A	25-Mar-17 A		Calendar Day	Wall (North) - Waterproofing & Working Platform															
S10-T5-B1-1060	Wall (North) - Rebar Fixing	3	0	26-Mar-17 A	30-Mar-17 A		Calendar Day	Wall (North) - Rebar Fixing															
S10-T5-B1-1070	Wall (North) - Formwork	3	0	31-Mar-17 A	03-Apr-17 A		Calendar Day	Wall (North) - Formwork															
S10-T5-B1-1080	Wall (North) - Concrete	1	0	05-Apr-17 A	05-Apr-17 A		Calendar Day	Wall (North) - Concrete															
S10-T5-B1-1090	Wall (North) - Curing & Formwork Dismantling	3	2	06-Apr-17 A	21-Apr-17	-485	Calendar Day	Wall (North) - Curing & Formwork Dismantling, Wall (North) - Curing & Formwork Dismantling															
S10-T5-B1-1100	Wall (South) - Waterproofing & Working Platform	4	0	27-Mar-17 A	30-Mar-17 A		Calendar Day	Wall (South) - Waterproofing & Working Platform															
S10-T5-B1-1110	Wall (South) - Rebar Fixing	3	0	31-Mar-17 A	02-Apr-17 A		Calendar Day	Wall (South) - Rebar Fixing															
S10-T5-B1-1120	Wall (South) - Formwork	2	0	03-Apr-17 A	04-Apr-17 A		Calendar Day	Wall (South) - Formwork															
S10-T5-B1-1130	Wall (South) - Concrete	1	0	05-Apr-17 A	05-Apr-17 A		Calendar Day	Wall (South) - Concrete															
S10-T5-B1-1140	Wall (South) - Curing & Formwork Dismantling	3	0	06-Apr-17 A	08-Apr-17 A		Calendar Day	Wall (South) - Curing & Formwork Dismantling															
S10-T5-B1-1230	OHVD Base Slab (North & Middle) - Scaffolding Erection	13	5	06-Apr-17 A	26-Apr-17	-485	Calendar Day	OHVD Base Slab (North & Middle) - Scaffolding Erection, OHVD Base Slab (North & Middle) - Scaffolding Erection															
S10-T5-B1-1240	OHVD Base Slab (North & Middle) - Formwork & Rebar Fixing	13	13	24-Apr-17	06-May-17	-485	Calendar Day	OHVD Base Slab (North & Middle) - Formwork & Rebar Fixing, OHVD Base Slab (North & Middle) - Formwork & Rebar Fixing															
S10-T5-B1-1250	OHVD Base Slab (North & Middle) - Concrete & Curing	2	2	07-May-17	08-May-17	-485	Calendar Day	OHVD Base Slab (North & Middle) - Concrete & Curing, OHVD Base Slab (North & Middle) - Concrete & Curing															
S10-T5-B1-1260	OHVD Base Slab (North & Middle) - Hanger Wall & Scaffolding to Roof	4	4	09-May-17	12-May-17	-480	Calendar Day	OHVD Base Slab (North & Middle) - Hanger Wall & Scaffolding to Roof, OHVD Base Slab (North & Middle) - Hanger Wall & Scaffolding to Roof															
S10-T5-B1-1310	OHVD Base Slab (South) - Scaffolding Erection	12	6	06-Apr-17 A	25-Apr-17	-483	Calendar Day	OHVD Base Slab (South) - Scaffolding Erection, OHVD Base Slab (South) - Scaffolding Erection															
S10-T5-B1-1320	OHVD Base Slab (South) - Formwork & Rebar Fixing	13	13	22-Apr-17	04-May-17	-483	Calendar Day	OHVD Base Slab (South) - Formwork & Rebar Fixing, OHVD Base Slab (South) - Formwork & Rebar Fixing															
S10-T5-B1-1330	OHVD Base Slab (South) - Concrete & Curing	2	2	05-May-17	06-May-17	-483	Calendar Day	OHVD Base Slab (South) - Concrete & Curing, OHVD Base Slab (South) - Concrete & Curing															
S10-T5-B1-1340	OHVD Base Slab (South) - Hanger Wall & Scaffolding to Roof	4	4	07-May-17	10-May-17	-478	Calendar Day	OHVD Base Slab (South) - Hanger Wall & Scaffolding to Roof, OHVD Base Slab (South) - Hanger Wall & Scaffolding to Roof															
S10-T5-B1-1350	Roof - Waterproofing	9	9	09-May-17	17-May-17	-485	Calendar Day	Roof - Waterproofing, Roof - Waterproofing															
S10-T5-B1-1360	Roof - Rebar Fixing & Formwork	16	16	18-May-17	02-Jun-17	-485	Calendar Day	Roof - Rebar Fixing & Formwork, Roof - Rebar Fixing & Formwork															
S10-T5-B1-1370	Roof - Concrete	1	1	03-Jun-17	03-Jun-17	-485	Calendar Day	Roof - Concrete, Roof - Concrete															
S10-T5-B1-1380	Roof - Curing	12	12	04-Jun-17	15-Jun-17	-485	Calendar Day	Roof - Curing, Roof - Curing															
S10-T5-B1-1390	Roof - Scaffolding Dismantling	5	5	15-Jun-17	20-Jun-17	-34	Calendar Day	Roof - Scaffolding Dismantling, Roof - Scaffolding Dismantling															
S10-T5-B1-1400	Construct Roadside Barriers	7	0	22-Mar-17 A	14-Apr-17 A		Calendar Day	Construct Roadside Barriers															
Outstanding Works																							
S10-T5-OUT-1020	TP5 - Carry out defects rectification works	30	30	28-May-17	27-Jun-17	-34	Calendar Day	TP5 - Carry out defects rectification works															
Section 11 of the Works - Remainder of Works																							
Marine Works at WCR3																							
S11-R3-2100	Mass Concrete Coping for Blockwork Seawall next to Type 2X caisson unit	18	18	16-Jun-17	04-Jul-17	-76	Calendar Day	Mass Concrete Coping															
Demolition Works																							
S11-DEMO-1310	Demolition of abandoned seawall down to +1.5mPD - at the south of Tunnel Portion 5	12	12	04-Jul-17	17-Jul-17	-50	HK Working Day	Demolition of abandoned seawall down to +1.5mPD - at the south of Tunnel Portion 5															
Formation and Hard Landscaping Works																							
S11-FM-5000A	Tunnel Portion 5 Backfilling (Sorted Public Fill or alternative filling material 45,000m3; 1100m3/d)	41	41	16-Jun-17	31-Jul-17	-438	HK Working Day	Tunnel Portion 5 Backfilling (Sorted Public Fill or alternative filling material 45,000m3; 1100m3/d)															
Misc. Works																							
Removal of Temporary Reclamation CH 3710 to CH 3790 (East)																							
S11-RTC-3068	Works within Temp D-Wall - Demolish top of Temp D-Wall at Bay 1 and Bay 2 (+2.425mPD) of HHR bridge	6	0	16-Mar-17 A	21-Mar-17 A		HK Working Day	Works within Temp D-Wall - Demolish top of Temp D-Wall at Bay 1 and Bay 2 (+2.425mPD) of HHR bridge															
S11-RTC-3069	Works within Temp D-Wall - Demolish top of Temp D-Wall at Bay 3 (+0.925mPD) of HHR bridge	7	0	18-Mar-17 A	22-Mar-17 A		HK Working Day	Works within Temp D-Wall - Demolish top of Temp D-Wall at Bay 3 (+0.925mPD) of HHR bridge															
S11-RTC-3070	Works within Temp D-Wall - Backfill with Sorted Public Fill from +1.5mPD to +2.75mPD to formation level of HHR bridge	2	0	24-Mar-17 A	19-Apr-17 A		HK Working Day	Works within Temp D-Wall - Backfill with Sorted Public Fill from +1.5mPD to +2.75mPD to formation level of HHR bridge															
Removal of Temporary Reclamation CH 3630 to CH 3710 (West)																							
S11-RTC-3250	Works within Temp D-Wall - Construct temporary walls from -7.0mPD to -4.0mPD 152 nos. (15 nos./day)	28	8	06-Jan-17 A	27-Apr-17	-585	Calendar Day	Works within Temp D-Wall - Construct temporary walls from -7.0mPD to -4.0mPD 152 nos. (15 nos./day), Works within Temp D-Wall - Construct temporary walls from -7.0mPD to -4.0mPD 152 nos. (15 nos./day)															
S11-RTC-3252	Works within Temp D-Wall - Place Type A rockfill and Filter to -7.0mPD to -4.0mPD (400m3@300m3/d)	15	12	06-Mar-17 A	09-May-17	-560	Calendar Day	Works within Temp D-Wall - Place Type A rockfill and Filter to -7.0mPD to -4.0mPD (400m3@300m3/d)															
S11-RTC-3256	Works within Temp D-Wall - Place Sorted Public Fill from -7.0mPD to -3.0mPD with 35 deg fill slope (4,150m3@200m3/d)	53	45	08-Apr-17 A	07-Jun-17	-524	HK Working Day	Works within Temp D-Wall - Place Sorted Public Fill from -7.0mPD to -3.0mPD with 35 deg fill slope (4,150m3@200m3/d)															
S11-RTC-3257	Works within Temp D-Wall - Remove ELS S1 Grid 0 - Grid 7	14	14	08-Jun-17	22-Jun-17	-524	HK Working Day	Works within Temp D-Wall - Remove ELS S1 Grid 0 - Grid 7															
S11-RTC-3258	Works within Temp D-Wall - Place Sorted Public Fill from -3.0mPD to +1.5mPD with 35 deg fill slope (2,800m3@200m3/d)	14	14	22-Jun-17	08-Jul-17	-524	HK Working Day	Works within Temp D-Wall - Place Sorted Public Fill from -3.0mPD to +1.5mPD with 35 deg fill slope (2,800m3@200m3/d)															
S11-RTC-3435	Works at South-West corner - Remove sheet pile decking (75 nos. sheet pile decking @ 2 nos./day)	30	0	01-Mar-17 A	11-Apr-17 A		HK Working Day	Works at South-West corner - Remove sheet pile decking (75 nos. sheet pile decking @ 2 nos./day)															
Removal of Temporary D-Wall CH 3630 to CH 3710																							
S11-RTC-3340	Preparation for D-Wall Cutting - Advance Coring inside D Wall (73 nos. for cutting , 2 machines @ 1no./machine/day)	50	50	12-Jul-17*	01-Sep-17	-634	HK Working Day	Preparation for D-Wall Cutting - Advance Coring inside D Wall (73 nos. for cutting , 2 machines @ 1no./machine/day)															
Hung Hing Road Flyover Reinstatement																							
Hung Hing Road Flyover - Bay 1 (West Side) CH 3709-3732																							
S11-HH-4009	Reinstatement of HHR Flyover - Complete the formation level and lay blinding layer for the west abutment	1	1	20-Apr-17	20-Apr-17	-606	HK Working Day	Reinstatement of HHR Flyover - Complete the formation level and lay blinding layer for the west abutment, Reinstatement of HHR Flyover - Complete the formation level and lay blinding layer for the west abutment															
S11-HH-4010	Reinstatement of HHR Flyover - Erect fmk for the base slab of west abutment	5	5	20-Apr-17	26-Apr-17	-605	HK Working Day	Reinstatement of HHR Flyover - Erect fmk for the base slab of west abutment, Reinstatement of HHR Flyover - Erect fmk for the base slab of west abutment															
S11-HH-4011	Reinstatement of HHR Flyover - Fix Re-bars for the base slab of west abutment	3	3	22-Apr-17	25-Apr-17	-605	HK Working Day	Reinstatement of HHR Flyover - Fix Re-bars for the base slab of west abutment, Reinstatement of HHR Flyover - Fix Re-bars for the base slab of west abutment															
S11-HH-4012	Reinstatement of HHR Flyover - Concreting for the base slab of west abutment	1	1	26-Apr-17	26-Apr-17	-605	HK Working Day	Reinstatement of HHR Flyover - Concreting for the base slab of west abutment, Reinstatement of HHR Flyover - Concreting for the base slab of west abutment															

[illegible]

[illegible][illegible]


[illegible]



中國建築-利達聯營
CHINA STATE - LEADER JOINT VENTURE

CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West

Page : 1 / 3

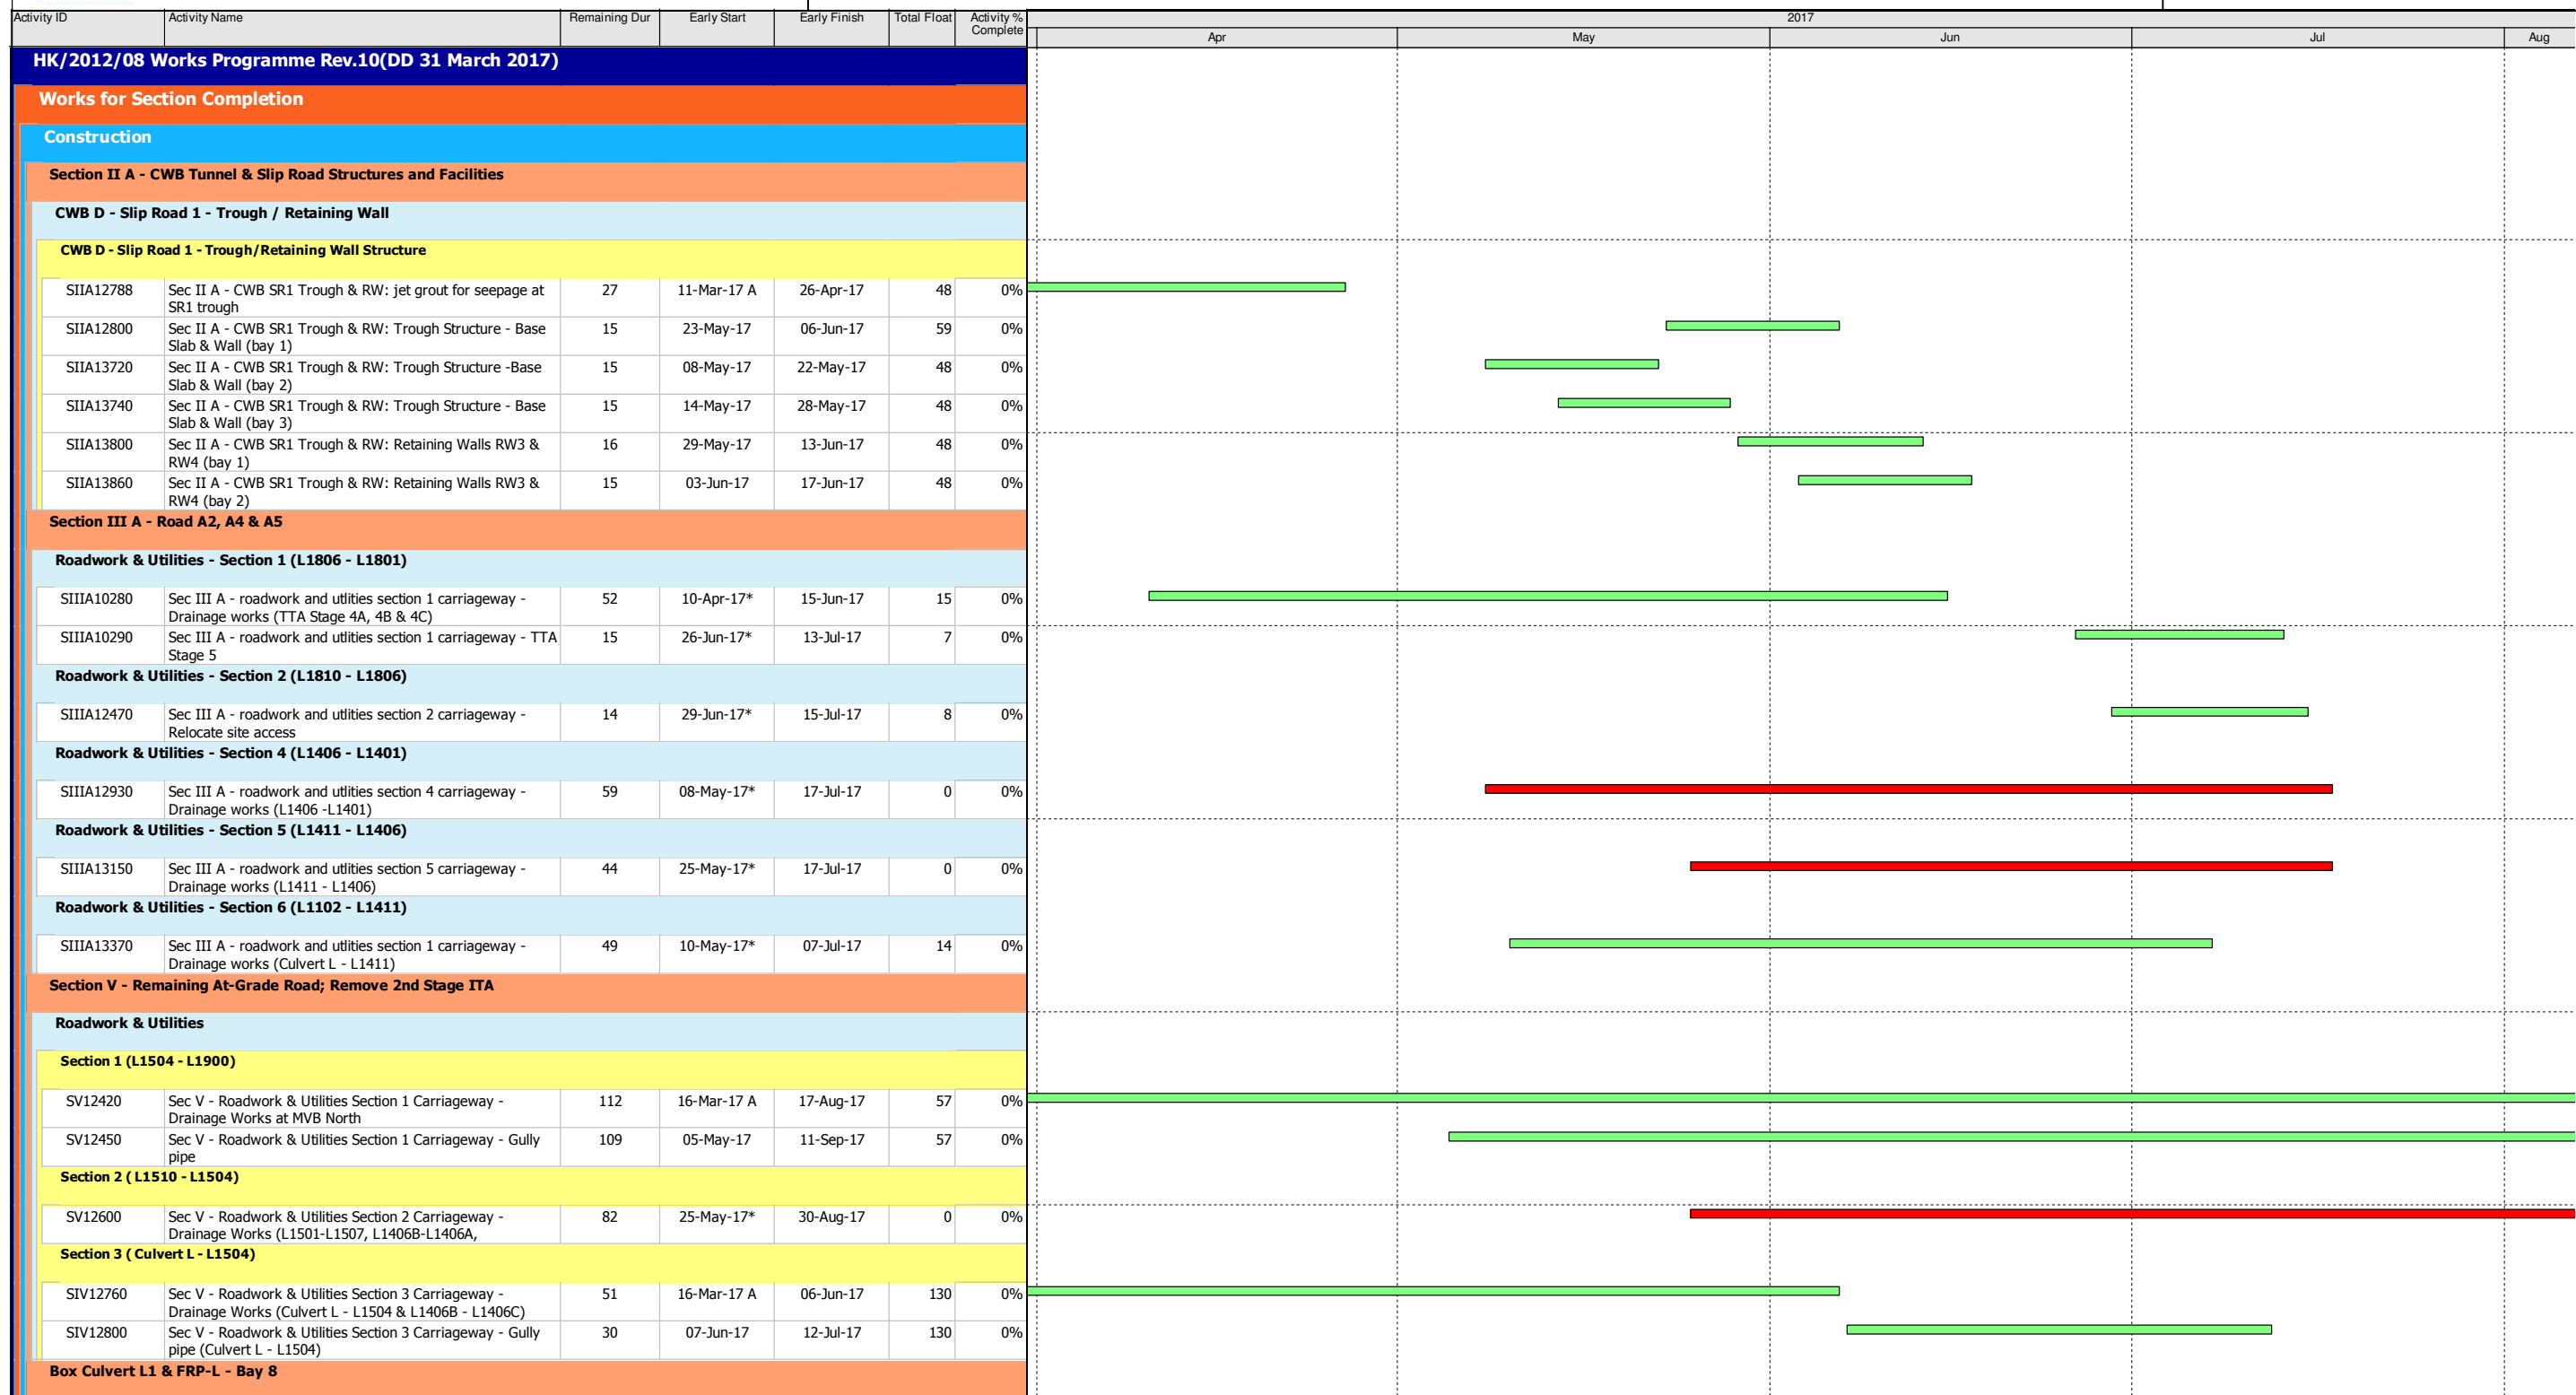

Data Date:
31-Mar-17

- ◆ ◆ Current Milestone
- ■ Actual Work
- ■ Critical Remaining Work
- ■ Remaining Work
- ■ Remaining Level of Effort

Three Months Rolling Programme for Non-CRIII (Apr 2017 to Jun 2017)
(Ref. to Works Programme Rev.10)

Date	Revision	Checked	Approved
11-May-17			



Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Total Float	Activity % Complete	2017				
							Apr	May	Jun	Jul	Aug
Box Culvert L1 & FRP-L - Bay 8 Structure											
CUL11328	Culvert L - bay 8 - construt top slab	12	10-Apr-17*	21-Apr-17	79	0%					
Box Culvert L1 & FRP-L - Bay 8 Others											
CUL11340	Culvert L - bay 8 - backfill above box section	25	03-Jun-17*	03-Jul-17	30	0%					
Section VI D - Area 8B & 10											
WDII Box 1 Construction											
WDII Box 1 Remaining Structure											
WD-C6075	Sec VID -Remaining of Box I: Construct sacarfical wall (2.3m)	11	19-Mar-17 A	10-Apr-17	0	60.71%					
WD-C6080	Sec VID - Remaining of Box I: Construct Wall 13(23m run)	16	07-Mar-17 A	15-Apr-17	8	46.67%					
WD-C6090	Sec VID - Remaining of Box I:Construct 2.5m wall 13	13	11-Apr-17	23-Apr-17	0	0%					
WD-C6120	Sec VID - Remaining of Box I: Blasting and final sink box to -10.0 mPD	2	24-Apr-17	25-Apr-17	0	0%					
WD-C6122	Sec VID - Remaining of Box I: Stiching of 4 bored piles	12	26-Apr-17	07-May-17	0	0%					
WD-C6124	Sec VID - Remaining of Box I: Scaffoding and soffit work at 4 bored piles	10	08-May-17	17-May-17	0	0%					
WD-C6126	Sec VID - Remaining of Box I: Roof rebar and concreting flat roof	8	18-May-17	25-May-17	0	0%					
WD-C6128	Sec VID - Remaining of Box I: Construct remaining roof half joint	7	28-May-17	03-Jun-17	0	0%					
WD-C6130	Sec VID - Remaining of Box I: Waterproofing work of roof	12	04-Jun-17	15-Jun-17	0	0%					
WD-C6140	Sec VID - Backfilling at South of Box I : Backfilling bagged cement to -6.5mPD	5	26-Apr-17	30-Apr-17	6	0%					
WD-C6160	Sec VID - Backfilling at South of Box I : Remove all ELS shoring and cut off P7 to P58 at -6.5mPD	18	01-May-17	18-May-17	6	0%					
WD-C6200	Sec VID - Backfilling at South of Box I : Remove SIC coarse screen hood	11	19-May-17	29-May-17	6	0%					
WD-C6220	Sec VID - Backfilling at South of Box I : Install pipe cap for box beam	4	30-May-17	02-Jun-17	6	0%					
WD-C6222	Sec VID - Backfilling at South of Box I : Stiching of H-pile	4	03-Jun-17	06-Jun-17	6	0%					
WD-C6223	Sec VID - Backfilling at South of Box I : Bagged lighweight concrete btw cap & seawall	6	07-Jun-17	12-Jun-17	6	0%					
WD-C6240	Sec VID - Backfilling at South of Box I : Install box beam	4	13-Jun-17	16-Jun-17	6	0%					
WD-C6250	Sec VID - Backfilling at South of Box I : Place 400mm thk precast cover to SIC	4	17-Jun-17	20-Jun-17	6	0%					
WD-C6255	Sec VID - Backfilling at South of Box I : Bagged lightweight concrete btw precast cover and box beam	4	21-Jun-17	24-Jun-17	6	0%					
WD-C6275	Sec VID - Backfilling at North of Box I : Type C concrete block at Box I half joint	4	19-May-17	22-May-17	13	0%					
WD-C6295	Sec VID - Backfilling at North of Box I : Install ceramsite concrete blocks	8	23-May-17	30-May-17	13	0%					
WD-C6315	Sec VID - Backfilling at North of Box I : Type A concrete block at roof of Box 1/2	3	31-May-17	02-Jun-17	13	0%					
WD-C6320	Sec VI D - Public fill on the top of Box I	15	16-Jun-17	30-Jun-17	0	0%					
Section IV - Slip Road 3											
Roadwork & Utilities											
Section 2 (L2301 - L2103)											
SIV11940	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Drainage Works	35	20-Apr-17*	02-Jun-17	0	0%					
SIV11960	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Watermain	10	28-Jun-17	10-Jul-17	161	0%					
SIV12000	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Gully pipe	21	03-Jun-17	27-Jun-17	161	0%					
Section VII - Remainder Works											
Promenade Seawall Parapet Construction											
SVII10400	Sec VII - construct block seawall mass concrete coping & backfill to pavement formation	50	15-Jun-17*	12-Aug-17	13	0%					
Section VIII - Landscape Softworks											
Soft Landscaping Works											



中國建築-利達聯營
CHINA STATE - LEADER JOINT VENTURE

CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Total Float	Activity % Complete	2017				
							Apr	May	Jun	Jul	Aug
SVIII10040	Sec VIII - Trees Planting	118	31-Mar-17	24-Aug-17	0	0%					
Section X - Protection & Preservation of Trees											
Soft Landscaping Works											
SX10020	Sec X - Protection & Preservation of Trees	234	31-Jan-13 A	19-Nov-17	0	85.66%					

SR8_DWP_R07-MU45			SR8 - Layout for 3MRP_2106_12										Appendix C.5										
Activity ID		Activity Name		Original Duration	Start	Finish																	
							2016				2017												
							Dec				Jan				Feb				Mar				Apr
Total				1791d	21-Mar-13 A	14-Dec-17																	
DWP-07 (5) - Update Progress As of 20 Dec 16				1791d	21-Mar-13 A	14-Dec-17																	
Works in KD7				137d	03-Oct-16 A	24-Mar-17																	
Works in TS3-West				137d	03-Oct-16 A	24-Mar-17																	
Tunnel Structure				137d	03-Oct-16 A	24-Mar-17																	
TS3W CCT Structure (Mainline E/B, W/B Tunnel)				60d	03-Oct-16 A	14-Jan-17																	
Wall & CP of Tunnel Structure Northern & Southem Tunnel E/B & W/B - 4,000 m3 + SM(A), SM(B), TF(A)				22d	21-Nov-16 A	22-Dec-16 A																	
Bay 2				5d	25-Nov-16 A	06-Dec-16 A																	
A1500	Spray Type Waterproofing, Protection Board and Backfilling (EP02 Construction Controlled)			5d	25-Nov-16 A	06-Dec-16 A	erproofing, Protection Board and Backfilling (EP02 Construction Controlled)																
Bay 3				10d	25-Nov-16 A	04-Dec-16 A																	
A1530	Spray Type Waterproofing, Protection Board and Backfilling			10d	25-Nov-16 A	04-Dec-16 A	oofing, Protection Board and Backfilling																
Bay 4				10d	21-Nov-16 A	09-Dec-16 A																	
A1560	Spray Type Waterproofing, Protection Board and Backfilling for SR8 Tunnel Construction			10d	21-Nov-16 A	09-Dec-16 A	e Waterproofing, Protection Board and Backfilling for SR8 Tunnel Construction																
Bay 5				10d	08-Dec-16 A	09-Dec-16 A																	
A1590	Spray Type Waterproofing, Protection Board and Backfilling for SR8 Tunnel Construction			10d	08-Dec-16 A	09-Dec-16 A	e Waterproofing, Protection Board and Backfilling for SR8 Tunnel Construction																
Bay 6				10d	09-Dec-16 A	12-Dec-16 A																	
A1620	Spray Type Waterproofing, Protection Board and Backfilling for SR8 Tunnel Construction (EP03 Construction controlled)			10d	09-Dec-16 A	12-Dec-16 A	ay Type Waterproofing, Protection Board and Backfilling for SR8 Tunnel Construction (EP03 Construction controlled)																
Bay 7				10d	11-Dec-16 A	12-Dec-16 A																	
A1650	Spray Type Waterproofing, Protection Board and Backfilling for SR8 Tunnel Construction			10d	11-Dec-16 A	12-Dec-16 A	ay Type Waterproofing, Protection Board and Backfilling for SR8 Tunnel Construction																
Bay 8				14d	30-Nov-16 A	22-Dec-16 A																	
A1690	Removal of 6th and 7th layer ELS			14d	30-Nov-16 A	08-Dec-16 A	6th and 7th layer ELS																
A1720	Backfilling for construction of SR8B			6d	11-Dec-16 A	18-Dec-16 A	Backfilling for construction of SR8B																
A1680	Waterproofing and repropping installation			5d	19-Dec-16 A	22-Dec-16 A	Waterproofing and repropping installation																
OHVD, Maintenance Walkway & Profile Barrier Construction (Northern & Southern Tunnel E/B & W/B				27d	08-Dec-16 A	06-Jan-17																	
Bay 8				27d	08-Dec-16 A	06-Jan-17																	
A1880	Bay S8 OHVD and Kicker Wall, Maintenance Walkway and Profile Barrier			8d	08-Dec-16 A	19-Dec-16 A	Bay S8 OHVD and Kicker Wall, Maintenance Walkway and Profile Barrier																
A1870	Bay N8 OHVD and Kicker Wall, Maintenance Walkway and Profile Barrier			8d	30-Dec-16	06-Jan-17	Bay N8 OHVD and Kicker Wall, Maintenance Walkway and Profile Barrier																
Bay 9				21d	12-Dec-16 A	03-Jan-17																	
A1900	Bay S9 OHVD and Kicker Wall, Maintenance Walkway and Profile Barrier			5d	12-Dec-16 A	21-Dec-16 A	Bay S9 OHVD and Kicker Wall, Maintenance Walkway and Profile Barrier																
A1890	Bay N9 OHVD and Kicker Wall, Maintenance Walkway and Profile Barrier			5d	30-Dec-16	03-Jan-17	Bay N9 OHVD and Kicker Wall, Maintenance Walkway and Profile Barrier																
Top Slab (Northern and Southern Side Tunnel E/B and W/B - 18000 m3)				47d	03-Oct-16 A	14-Jan-17																	
Bay 1				30d	08-Nov-16 A	14-Jan-17																	
A2090	Bulkhead Breakthrough of TS3E/TS3W			30d	08-Nov-16 A	14-Jan-17	Bulkhead Breakthrough of TS3E/TS3W																
Bay 6				11d	03-Oct-16 A	03-Dec-16 A																	
A2020	Bay S6R Top Slab (29m approx.)			11d	03-Oct-16 A	30-Nov-16 A	prox.)																
A2010	Bay N6R Top Slab (27m approx.)			11d	05-Oct-16 A	03-Dec-16 A	m approx.)																
Bay 7				17d	31-Oct-16 A	09-Dec-16 A																	
A2040	Bay S7R Top Slab (29m approx.)			10d	31-Oct-16 A	07-Dec-16 A	p Slab (29m approx.)																
A2030	Bay N7R Top Slab (26m approx.)			10d	07-Nov-16 A	09-Dec-16 A	Top Slab (26m approx.)																
Bay 8				6d	12-Dec-16 A	12-Jan-17																	
A2060	Bay S8R Top Slab (29m approx.)			5d	12-Dec-16 A	03-Jan-17	Bay S8R Top Slab (29m approx.)																
A2050	Bay N8R Top Slab (26m approx.)			6d	22-Dec-16 A	12-Jan-17	Bay N8R Top Slab (26m approx.)																
Bay 9				1d	08-Dec-16 A	04-Jan-17																	

Activity ID	Activity Name	Original Duration	Start	Finish												
					2016		2017									
					Dec		Jan	Feb		Mar						Apr
A2080	Bay S9R Top Slab (29m approx.)	1d	08-Dec-16 A	30-Dec-16			■ Bay S9R Top Slab (29m approx.)									
A2070	Bay N9R Top Slab (26m approx.)	1d	17-Dec-16 A	04-Jan-17			■ Bay N9R Top Slab (26m approx.)									
SR8 Tunnel Structure		96d	13-Nov-16 A	16-Feb-17												
Base Slab of Slip Road 8 (SR8) - 8000 m3		73d	13-Nov-16 A	24-Jan-17												
A2130	Placement of Seawall Blocks for SR4B Construction	8d	13-Nov-16 A	30-Dec-16			■ Placement of Seawall Blocks for SR4B Construction									
A2150	Placement of Seawall Blocks for SR5B Construction	8d	18-Nov-16 A	01-Jan-17			■ Placement of Seawall Blocks for SR5B Construction									
A2170	Placement of Seawall Blocks for SR6B Construction	8d	16-Dec-16 A	02-Jan-17			■ Placement of Seawall Blocks for SR6B Construction									
A2200	Bay SR8B	8d	30-Dec-16	06-Jan-17			■ Bay SR8B									
A2140	Bay SR4B	7d	31-Dec-16	06-Jan-17			■ Bay SR4B									
A2160	Bay SR5B	7d	01-Jan-17	08-Jan-17			■ Bay SR5B									
A2180	Bay SR6B	5d	02-Jan-17	07-Jan-17			■ Bay SR6B									
A2190	Bay SR7B	5d	11-Jan-17	15-Jan-17			■ Bay SR7B									
A2110	Breaking to the Cut Off Level of Diaphragm Wall to be Carried Out after Bay S3R Completion	2d	18-Jan-17	19-Jan-17			■ Breaking to the Cut Off Level of Diaphragm Wall to be Carried Out after Bay S3R Completion									
A2120	Bay SR3B	5d	20-Jan-17	24-Jan-17			■ Bay SR3B									
Wall Structure of SR8 - 2500 m3		27d	07-Jan-17	02-Feb-17												
A2230	Removal of 4th layer and 5th layer ELS	6d	07-Jan-17	12-Jan-17			■ Removal of 4th layer and 5th layer ELS									
A2270	Removal of 4th layer and 5th layer ELS	6d	07-Jan-17	13-Jan-17			■ Removal of 4th layer and 5th layer ELS									
A2250	Removal of 4th layer and 5th layer ELS	6d	08-Jan-17	14-Jan-17			■ Removal of 4th layer and 5th layer ELS									
A2240	Bay SR4 Walls	7d	13-Jan-17	19-Jan-17			■ Bay SR4 Walls									
A2280	Bay SR6 Walls	7d	13-Jan-17	20-Jan-17			■ Bay SR6 Walls									
A2260	Bay SR5 Walls	7d	14-Jan-17	21-Jan-17			■ Bay SR5 Walls									
A2290	Removal of 5th layer ELS	4d	16-Jan-17	19-Jan-17			■ Removal of 5th layer ELS									
A2300	Bay SR7 Walls	5d	20-Jan-17	24-Jan-17			■ Bay SR7 Walls									
A2210	Removal of 4th layer and 5th layer ELS	4d	25-Jan-17	28-Jan-17			■ Removal of 4th layer and 5th layer ELS									
A2220	Bay SR3 Walls	5d	29-Jan-17	02-Feb-17			■ Bay SR3 Walls									
OHVD Structure, Maintenance Walkway and Profile Barrier of SR8 - 2000 m3		35d	04-Jan-17	07-Feb-17												
A2320	Bay SR1R OHVD, Maintenance Walkway and Profile Barrier	7d	04-Jan-17*	10-Jan-17			■ Bay SR1R OHVD, Maintenance Walkway and Profile Barrier									
A2380	Removal of 5th Layer ELS	5d	07-Jan-17	11-Jan-17			■ Removal of 5th Layer ELS									
A2390	Bay SR8R OHVD, Maintenance Walkway and Profile Barrier	4d	12-Jan-17	15-Jan-17			■ Bay SR8R OHVD, Maintenance Walkway and Profile Barrier									
A2340	Bay SR4R OHVD, Maintenance Walkway and Profile Barrier	5d	20-Jan-17	24-Jan-17			■ Bay SR4R OHVD, Maintenance Walkway and Profile Barrier									
A2360	Bay SR6R OHVD, Maintenance Walkway and Profile Barrier	4d	20-Jan-17	24-Jan-17			■ Bay SR6R OHVD, Maintenance Walkway and Profile Barrier									
A2350	Bay SR5R OHVD, Maintenance Walkway and Profile Barrier	7d	21-Jan-17	28-Jan-17			■ Bay SR5R OHVD, Maintenance Walkway and Profile Barrier									
A2370	Bay SR7R OHVD, Maintenance Walkway and Profile Barrier	4d	25-Jan-17	28-Jan-17			■ Bay SR7R OHVD, Maintenance Walkway and Profile Barrier									
A2330	Bay SR3R OHVD, Maintenance Walkway and Profile Barrier	5d	03-Feb-17	07-Feb-17			■ Bay SR3R OHVD, Maintenance Walkway and Profile Barrier									
Top Slab of SR8 - 12000 m3		37d	11-Jan-17	16-Feb-17												
A2400	Bay SR1R	10d	11-Jan-17	20-Jan-17			■ Bay SR1R									
A2460	Bay SR8R	9d	16-Jan-17	24-Jan-17			■ Bay SR8R									
A2440	Bay SR6R	9d	24-Jan-17	02-Feb-17			■ Bay SR6R									
A2420	Bay SR4R	6d	25-Jan-17	30-Jan-17			■ Bay SR4R									
A2430	Bay SR5R	8d	28-Jan-17	05-Feb-17			■ Bay SR5R									
A2450	Bay SR7R	9d	29-Jan-17	06-Feb-17			■ Bay SR7R									
A2410	Bay SR3R	7d	10-Feb-17	16-Feb-17			■ Bay SR3R									
Earthwork Backfilling, ELS Removal and Water Recharging		122d	10-Nov-16 A	11-Mar-17												
East Portion		116d	10-Nov-16 A	05-Mar-17												

Activity ID	Activity Name	Original Duration	Start	Finish												
					2016			2017								
					Dec			Jan		Feb		Mar			Apr	
A2470	Stage 1 Backfilling- 6000 m3 (-30 mPD~ -20 mPD, Bay 2 -Bay 4) - 500 m3 per day	13d	10-Nov-16 A	17-Jan-17				Stage:1 Backfilling- 6000 m3 (-30mPD~ -20 mPD, Bay 2 -Bay 4) - 500 m3 per day								
A2480	Stage 2 Backfilling- 28000 m3 (-20 mPD~ -10 mPD, Bay 2- Bay 4) - 1560 m3 per day	18d	18-Jan-17	04-Feb-17					Stage 2 Backfilling- 28000 m3 (-20 mPD~ -10 mPD, Bay 2- Bay 4) - 1560 m3 per day							
A2490	Stage 3 Backfilling- 18000 m3 (-10mPD~ -7.0 mPD, Bay 2- Bay 4) - 1000 m3 per day	18d	05-Feb-17	22-Feb-17						Stage 3 Backfilling- 18000 m3 (-10mPD~ -7.0 mPD, Bay 2- Bay 4) - 1000 m3 per day						
A2510	Closure of wall opening in Bay 1 of CCT (Wall 4 and Wall 5)	11d	12-Feb-17	23-Feb-17							Closure of wall opening in Bay 1 of CCT (Wall 4 and Wall 5)					
A2520	Stage 5 Backfilling ~ 10000 m3 (-30 mPD ~ -7.0 mPD, Bay 1) ~ 1000 m3 per day	11d	18-Feb-17	28-Feb-17							Stage 5 Backfilling ~ 10000 m3 (-30 mPD ~ -7.0 mPD, Bay 1) ~ 1000 m3 per day					
A2500	Removal of 2nd Layer ELS and Removal of Reprop inside Tunnel (Bay 2- Bay 4)	10d	23-Feb-17	04-Mar-17								Removal of 2nd Layer ELS and Removal of Reprop inside Tunnel (Bay 2- Bay 4)				
A2515	Backfilling of Bay 1	11d	23-Feb-17	05-Mar-17								Backfilling of Bay 1				
A2530	Removal of 2nd Layer ELS (Bay 1)	5d	01-Mar-17	05-Mar-17								Removal of 2nd Layer ELS (Bay 1)				
West Portion		33d	13-Jan-17	14-Feb-17												
A2540	Stage 4 Backfilling - 69000 m3 (-30mPD~ -7.0 mPD, Bay 5-8) - 2500 m3 per day	28d	13-Jan-17	09-Feb-17				Stage 4 Backfilling - 69000 m3 (-30mPD~ -7.0 mPD, Bay 5-8) - 2500 m3 per day								
A2550	Removal of 2nd Layer ELS - 10 days	13d	02-Feb-17	14-Feb-17					Removal of 2nd Layer ELS - 10 days							
Water Recharge (CNY- 27/1~ 2/2)		6d	06-Mar-17	11-Mar-17												
A2560	Water Re-charge to ELS Cofferdam	6d	06-Mar-17	11-Mar-17								Water Re-charge to ELS Cofferdam				
Skin Wall Removal Works between TS4/TS3W and Shaft D Closure		85d	30-Dec-16	24-Mar-17												
A2570	Design Review and ICE Cert for 1st Stage Skin Wall Removal	15d	30-Dec-16	13-Jan-17			Design Review and ICE Cert for 1st Stage Skin Wall Removal									
A2580	Skin Wall Removal Works between TS4/TS3W - 20 days (1st stage) - SR8	20d	14-Jan-17	02-Feb-17				Skin Wall Removal Works between TS4/TS3W - 20 days (1st stage) - SR8								
A2590	Skin Wall Removal Works between TS4/TS3W - 20 days (2nd stage) - After Tunnel Roof Slab Completion - E/B and W/B	20d	03-Feb-17	22-Feb-17					Skin Wall Removal Works between TS4/TS3W - 20 days (2nd stage) - After Tunnel Roof Slab Completion - E/B and W/B							
A2600	Construction of Remaining Tunnel Structure between CH. 4260.2- 4265.2 at SOL T100 for Mainline E/B, W/B, SR8	30d	23-Feb-17	24-Mar-17							Construction of Remaining Tunnel Structure between CH. 4260.2- 4265.2 at SOL T100 for Mainline E/B, W/B, SR8					
A2610	Shaft D R/C Slab Reinstatement	20d	23-Feb-17	14-Mar-17							Shaft D R/C Slab Reinstatement					
Removal Bulkhead at CH525 (TS3W / SR8 Junction)		51d	21-Jan-17	12-Mar-17												
A4830	Curing Period for Removal of Scaffolding of Bay SR1R of SR8 Roof Slab	10d	21-Jan-17	30-Jan-17					Curing Period for Removal of Scaffolding of Bay SR1R of SR8 Roof Slab							
A5180	Remove Scaffolding of SR1R Roof	4d	31-Jan-17	03-Feb-17					Remove Scaffolding of SR1R Roof							
A6080	Remove Bulkhead between TS3W & SR8	37d	04-Feb-17	12-Mar-17						Remove Bulkhead between TS3W & SR8						
Works in KD8		66d	27-Jan-17	02-Apr-17												
TS3W - Remove Temporary Reclamation		66d	27-Jan-17	02-Apr-17												
Stage 1 - North West Corner (Bay Z4-25 to Bay 20)		24d	27-Jan-17	19-Feb-17												
A2650	Break concrete slab at Bay Z4-25 to Bay 20	4d	27-Jan-17	30-Jan-17					Break concrete slab at Bay Z4-25 to Bay 20							
A2660	Remove filled material to -4.35mPD at Bay Z4-25 to Bay 19 (6,500m3)	8d	31-Jan-17	07-Feb-17					Remove filled material to -4.35mPD at Bay Z4-25 to Bay 19 (6,500m3)							
A2670	Remove seawall blocks at Bay Z4-25 to Bay 20 (426 nos.)	8d	08-Feb-17	15-Feb-17					Remove seawall blocks at Bay Z4-25 to Bay 20 (426 nos.)							
A2680	Remove filled material to -7.0 mPD	4d	16-Feb-17	19-Feb-17					Remove filled material to -7.0 mPD							
Stage 2 - North to East Side (Bay 19 to Bay 11 + Bay 26 to Bay 28)		14d	31-Jan-17	13-Feb-17												
A2690	Break concrete slab at Bay 19 to Bay 11 + Bay 26 to Bay 28 (2,500m2)	7d	31-Jan-17	06-Feb-17					Break concrete slab at Bay 19 to Bay 11 + Bay 26 to Bay 28 (2,500m2)							
A2700	Remove filled material to +2.8mPD (2,500m3)	7d	07-Feb-17	13-Feb-17					Remove filled material to +2.8mPD (2,500m3)							
Stage 3 - North to East Side (Bay 19 to bay 26)		22d	12-Mar-17	02-Apr-17												
North West D-wall Opening		19d	12-Mar-17	30-Mar-17												
A2720	Core D-wall cut holes at Panel DW02 to NA6 (27 nos.)	4d	12-Mar-17	15-Mar-17							Core D-wall cut holes at Panel DW02 to NA6 (27 nos.)					
A2730	Vertical cut at Panel DW02 to NA6 (19 nos.)	8d	16-Mar-17	23-Mar-17							Vertical cut at Panel DW02 to NA6 (19 nos.)					
A2740	Horizontal cut at Panel DW02 to NA6 (25 nos.)	7d	24-Mar-17	30-Mar-17							Horizontal cut at Panel DW02 to NA6 (25 nos.)					
North East & East		22d	12-Mar-17	02-Apr-17												
A2750	Remove filled material to -4.35mPD (22,500m3)	9d	12-Mar-17	20-Mar-17							Remove filled material to -4.35mPD (22,500m3)					
A2760	Remove seawall blocks at Bay 19 to 11 & Bay 26 to 28 (1,335 nos.)	13d	21-Mar-17	02-Apr-17							Remove seawall blocks at Bay 19 to 11 & Bay 26 to 28 (1,335 nos.)					
Works in KD6		333d	19-Apr-16 A	18-Mar-17												
Works in SR8 (Open Cut Method)		333d	19-Apr-16 A	18-Mar-17												
SR8 (Zone C) - Ch. 528 to Ch. 368		109d	18-Nov-16 A	18-Mar-17												

Activity ID	Activity Name	Original Duration	Start	Finish	2016		2017											
					Dec	Jan	Feb				Mar				Apr			
ELS		46d	19-Nov-16 A	04-Jan-17														
Area B (CH475 to CH514) - steel Deck EB + SR8/TS3 Interface		46d	19-Nov-16 A	04-Jan-17														
Strut & Waling Installation for SL5		41d	19-Nov-16 A	07-Dec-16 A														
A3470	Area B - Waling Installation	6d	19-Nov-16 A	02-Dec-16 A	tion													
A3480	Area B - Srrtut Installation for SL5	9d	30-Nov-16 A	03-Dec-16 A	ation for SL5													
A1621	Area B - Bracing Installation for Layer 2 (Bottom Horizontal & Diagonal)	1d	07-Dec-16 A	07-Dec-16 A	ing Installation for Layer 2 (Bottom Horizontal & Diagonal)													
Excavation to -17.9mPD From SL5 to Formation (3,908 m3 / 540m3/D approx.3.3m Depth)		34d	30-Nov-16 A	05-Dec-16 A														
A3440	Area B - Excavation 1st cycle (1.2m Depth) & Lagging Plate	4d	30-Nov-16 A	01-Dec-16 A	ycle (1.2m Depth) & Lagging Plate													
A3450	Area B - Excavation 2nd cycle (1.2m Depth) & Lagging Plate	4d	02-Dec-16 A	03-Dec-16 A	nd cycle (1.2m Depth) & Lagging Plate													
A3460	Area B - Excavation 3rd cycle (0.9m Depth) & Lagging Plate	3d	04-Dec-16 A	05-Dec-16 A	on 3rd cycle (0.9m Depth) & Lagging Plate													
Excavation for Rock Fill (1000mm Below F.L./1,576 m3/ 540m3/D)		6d	30-Dec-16	04-Jan-17														
A3490	Area B - Excavation further down to 1000mm below F.L.	1d	30-Dec-16	30-Dec-16	Area B - Excavation further down to 1000mm below F.L.													
A3500	Area B - Lay & Compact Rock Fill	4d	31-Dec-16	03-Jan-17	Area B - Lay & Compact Rock Fill													
A3510	Area B - Blinding / Divert Ground Water by Submerge Pump	2d	03-Jan-17	04-Jan-17	Area B - Blinding / Divert Ground Water by Submerge Pump													
Tunnel Structure		108d	18-Nov-16 A	18-Mar-17														
Area A (CH384 to CH475 - Victoria Park to Steel Deck WB + IEC)		97d	18-Nov-16 A	07-Mar-17														
Vertical Blinding Bay C1 to C4		13d	29-Nov-16 A	09-Dec-16 A														
A4300	Bay C4	13d	29-Nov-16 A	09-Dec-16 A														
Tunnel Structure at Area A - Bay C1 to C4		97d	18-Nov-16 A	07-Mar-17														
Bay C2		89d	30-Nov-16 A	05-Mar-17														
Structure		41d	30-Nov-16 A	16-Jan-17														
1.2m Thick Base Slab		26d	30-Nov-16 A	16-Dec-16 A														
T1350	C2 Base - Concreting	1d	30-Nov-16 A	30-Nov-16 A														
T1370	C2 Base - Remove 3th & 5th Strut SL3 & SL5 (2 Nos@SL5 & 8 Nos@SL3)	3d	09-Dec-16 A	16-Dec-16 A	C2 Base - Remove 3th & 5th Strut SL3 & SL5 (2 Nos@SL5 & 8 Nos@SL3)													
1m Thick Tunnel Wall at Both Sides & OHVD Slab		7d	22-Dec-16 A	04-Jan-17														
T1380	C2 Wall & OHVD - Erect Scaffolding & Soffit Formwork	4d	22-Dec-16 A	30-Dec-16	C2 Wall & OHVD - Erect Scaffolding & Soffit Formwork													
T1390	C2 Wall & OHVD - Steel Fixing & Wall Formwork	5d	30-Dec-16	03-Jan-17	C2 Wall & OHVD - Steel Fixing & Wall Formwork													
T1400	C2 Wall & OHVD - Concreting	1d	04-Jan-17	04-Jan-17	C2 Wall & OHVD - Concreting													
400mm Thick OHVD Hanger Wall & 1.2m Thick Top Slab		12d	05-Jan-17	16-Jan-17														
T1440	C2 OHVD Hanger Wall & Roof - Erect Faslework & Soffit Formworks + Hanger Wall Formwork	3d	05-Jan-17	07-Jan-17	C2 OHVD Hanger Wall & Roof - Erect Faslework & Soffit Formworks + Hanger Wall Formwork													
T1450	C2 OHVD Hanger Wall & Roof - Steel Fixing (+1 d for Wall Steel fixing)	6d	08-Jan-17	13-Jan-17	C2 OHVD Hanger Wall & Roof - Steel Fixing (+1 d for Wall Steel fixing)													
T1460	C2 OHVD Hanger Wall & Roof - Top slab CJ Formwork Erection & Water Stop	2d	14-Jan-17	15-Jan-17	C2 OHVD Hanger Wall & Roof - Top slab CJ Formwork Erection & Water Stop													
T1470	C2 OHVD Hanger Wall & Roof - Concreting	1d	16-Jan-17	16-Jan-17	C2 OHVD Hanger Wall & Roof - Concreting													
Removal of Falseworks & SL4		23d	17-Jan-17	08-Feb-17														
T1550	C2 Roof - 10 Days Curing of Roof Prior to Removal of Falsework	10d	17-Jan-17	26-Jan-17	C2 Roof - 10 Days Curing of Roof Prior to Removal of Falsework													
T1560	C2 Roof - Remove Falsework	6d	27-Jan-17	05-Feb-17	C2 Roof - Remove Falsework													
T2730	C2 Wall - Remove Strut SL4 (8 No / Layer/ Bay C2)	3d	06-Feb-17	08-Feb-17	C2 Wall - Remove Strut SL4 (8 No / Layer/ Bay C2)													
Egress Passage		17d	08-Feb-17	25-Feb-17														
Wall of EP		9d	08-Feb-17	17-Feb-17														
A3780	C2 Erect Scaffolding & working Platform	1d	08-Feb-17	09-Feb-17	C2 Erect Scaffolding & working Platform													
A3750	C2 Internal Wall Formwork	2d	09-Feb-17	11-Feb-17	C2 Internal Wall Formwork													
A3760	C2 Steel Fixing to Wall	2d	11-Feb-17	13-Feb-17	C2 Steel Fixing to Wall													
A3770	C2 External Wall Formwork	3d	13-Feb-17	16-Feb-17	C2 External Wall Formwork													
A3790	C2 Concrete to Wall	1d	16-Feb-17	17-Feb-17	C2 Concrete to Wall													

Activity ID		Activity Name	Original Duration	Start	Finish	2016			2017									
						Dec	Jan			Feb			Mar			Apr		
	Roof of EP		8d	17-Feb-17	25-Feb-17													
	A3800	C2 Scaffolding & Soffit Formwork	3d	17-Feb-17	20-Feb-17													
	A3810	C2 Steel Fixing to Roof	2d	20-Feb-17	22-Feb-17													
	A3820	C2 Side Fromwork for Wall up to Roof Top	2d	22-Feb-17	24-Feb-17													
	A3830	C2 Concrete to Roof	1d	24-Feb-17	25-Feb-17													
	Utility Trough		25d	08-Feb-17	05-Mar-17													
	Left Hand Side		8d	25-Feb-17	05-Mar-17													
	A3850	C2 - LHS Backing Concrete of Utility Trough	4d	25-Feb-17	01-Mar-17													
	A3840	C2 - LHS Profile Barrier of Utility Trough	4d	01-Mar-17	05-Mar-17													
	Right Hand Side		8d	08-Feb-17	16-Feb-17													
	A3860	C2 - RHS Backing Concrete of Utility Trough	4d	08-Feb-17	12-Feb-17													
	A3870	C2 - RHS Profile Barrier of Utility Trough	4d	12-Feb-17	16-Feb-17													
	Bay C1		96d	18-Nov-16 A	05-Mar-17													
	Structure		50d	18-Nov-16 A	18-Jan-17													
	A4280	Fixing T-Grid Waterproofing on Base Slab & Vertical Blinding	3d	18-Nov-16 A	01-Dec-16 A													
	1.2m Thick Base Slab		10d	02-Dec-16 A	19-Dec-16 A													
	T2780	C1 Base - Rebar Fixing	5d	02-Dec-16 A	06-Dec-16 A													
	T2790	C1 Base - Kicker Formwork & Water Stop	2d	07-Dec-16 A	07-Dec-16 A													
	T2800	C1 Base - Concreting	1d	08-Dec-16 A	08-Dec-16 A													
	T2820	C1 Base - Remove 3th & 5th Strut SL3 & SL5 (0 Nos@SL5 & 6 Nos@SL3)	2d	12-Dec-16 A	19-Dec-16 A													
	1m Thick Tunnel Wall at Both Sides & OHVD Slab		9d	30-Dec-16	07-Jan-17													
	T2830	C1 Wall & OHVD - Erect Scaffolding & Soffit Formwork	3d	30-Dec-16	01-Jan-17													
	T2840	C1 Wall & OHVD - Steel Fixing	4d	02-Jan-17	05-Jan-17													
	T2850	C1 Wall & OHVD - Wall Formwork + Side Formwork for OHVD Slab	1d	06-Jan-17	06-Jan-17													
	T2860	C1 Wall & OHVD - Concreting	1d	07-Jan-17	07-Jan-17													
	400mm Thick OHVD Hanger Wall & 1.2m Thick Top Slab		11d	08-Jan-17	18-Jan-17													
	T2870	C1 OHVD Hanger Wall & Roof - Erect Faslework & Soffit Formworks + Hanger Wall Formwork	3d	08-Jan-17	10-Jan-17													
	T2880	C1 OHVD Hanger Wall & Roof - Steel Fixing (+1 D for Wall Steel Fixing)	6d	11-Jan-17	16-Jan-17													
	T2890	C1 OHVD Hanger Wall & Roof - Top slab CJ Formwork Erection & Water Stop	1d	17-Jan-17	17-Jan-17													
	T2910	C1 OHVD Hanger Wall & Roof - Concreting	1d	18-Jan-17	18-Jan-17													
	Removal of Falseworks & SL4		21d	19-Jan-17	08-Feb-17													
	T1310	C1 Roof - 10 Days Curing of Roof Prior to Removal of Falsework	10d	19-Jan-17	28-Jan-17													
	T1320	C1 Roof - Remove Falsework	6d	01-Feb-17	06-Feb-17													
	T2740	C1 Wall - Remove Strut SL4 (6 No / Layer/ Bay C1)	2d	07-Feb-17	08-Feb-17													
	Egress Passage		17d	09-Feb-17	25-Feb-17													
	Wall of EP		9d	09-Feb-17	17-Feb-17													
	A3650	C1 Erect Scaffolding & working Platform	1d	09-Feb-17	09-Feb-17													
	A3620	C1 Internal Wall Formwork	2d	10-Feb-17	11-Feb-17													
	A3630	C1 Steel Fixing to Wall	2d	12-Feb-17	13-Feb-17													
	A3640	C1 External Wall Formwork	3d	14-Feb-17	16-Feb-17													
A3660	C1 Concrete to Wall	1d	17-Feb-17	17-Feb-17														
Roof of EP		8d	18-Feb-17	25-Feb-17														
A3670	C1 Scaffolding & Soffit Formwork	3d	18-Feb-17	20-Feb-17														
A3680	C1 Steel Fixing to Roof	2d	21-Feb-17	22-Feb-17														

Activity ID		Activity Name	Original Duration	Start	Finish	2016												2017																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
						Dec				Jan				Feb				Mar				Apr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
Bay C3	A3690	C1 Side Fromwork for Wall up to Roof Top	2d	23-Feb-17	24-Feb-17																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		

Activity ID	Activity Name	Original Duration	Start	Finish												
					2016			2017								
					Dec			Jan			Feb			Mar		Apr
	Utility Trough	25d	10-Feb-17	06-Mar-17												
	Left Hand Side	8d	27-Feb-17	06-Mar-17												
A4000	C3 - LHS Backing Concrete of Utility Trough	4d	27-Feb-17	02-Mar-17												
A4010	C3 - LHS Profile Barrier of Utility Trough	4d	03-Mar-17	06-Mar-17												
	Right Hand Side	8d	10-Feb-17	17-Feb-17												
A4020	C3 - RHS Backing Concrete of Utility Trough	4d	10-Feb-17	13-Feb-17												
A4030	C3 - RHS Profile Barrier of Utility Trough	4d	14-Feb-17	17-Feb-17												
	Bay C4	67d	14-Dec-16 A	07-Mar-17												
	Structure	24d	14-Dec-16 A	22-Jan-17												
A4310	Fixing T-Grid Waterproofing on Base Slab & Vertical Blinding	3d	14-Dec-16 A	18-Dec-16 A												
	1.2m Thick Base Slab	9d	19-Dec-16 A	02-Jan-17												
T3120	C4 Base - Rebar Fixing	3d	19-Dec-16 A	21-Dec-16 A												
T3130	C4 Base - Kicker Formwork & Water Stop	2d	22-Dec-16 A	22-Dec-16 A												
T3140	C4 Base - Concreting	1d	23-Dec-16 A	23-Dec-16 A												
T3160	C4 Base - Remove 3th & 5th Strut SL3 & SL5 (3 Nos@SL5 & 8 Nos@SL3)	4d	30-Dec-16	02-Jan-17												
	1m Thick Tunnel Wall at Both Sides & OHVD Slab	11d	02-Jan-17	13-Jan-17												
T3170	C4 Wall & OHVD - Erect Scaffolding & Soffit Formwork	4d	02-Jan-17	06-Jan-17												
T3180	C4 Wall & OHVD - Steel Fixing	5d	06-Jan-17	11-Jan-17												
T3190	C4 Wall & OHVD - Wall Formwork + Side Formwork for OHVD Slab	1d	11-Jan-17	12-Jan-17												
T3200	C4 Wall & OHVD - Concreting	1d	12-Jan-17	13-Jan-17												
	400mm Thick OHVD Hanger Wall & 1.2m Thick Top Slab	9d	13-Jan-17	22-Jan-17												
T3210	C4 OHVD Hanger Wall & Roof - Erect Faslework & Soffit Formworks + Hanger Wall Formwork	3d	13-Jan-17	16-Jan-17												
T3220	C4 OHVD Hanger Wall & Roof - Steel Fixing (+1 D for Wall Fixing)	4d	16-Jan-17	20-Jan-17												
T3230	C4 OHVD Hanger Wall & Roof - Top slab CJ Formwork Erection & Water Stop	1d	20-Jan-17	21-Jan-17												
T3250	C4 OHVD Hanger Wall & Roof - Concreting	1d	21-Jan-17	22-Jan-17												
	Removal of Falseworks & SL5	19d	22-Jan-17	10-Feb-17												
T3300	C4 Roof - 10 Days Curing of Roof Prior to Removal of Falsework	10d	22-Jan-17	01-Feb-17												
T3310	C4 Roof - Remove Falsework	6d	01-Feb-17	07-Feb-17												
T3290	C4 Wall - Remove Strut SL4 (8 No / Layer/ Bay C3)	3d	07-Feb-17	10-Feb-17												
	Egress Passage	17d	10-Feb-17	27-Feb-17												
	Wall of EP	9d	10-Feb-17	19-Feb-17												
A4140	C4 Erect Scaffolding & working Platform	1d	10-Feb-17	11-Feb-17												
A4110	C4 Internal Wall Formwork	2d	11-Feb-17	13-Feb-17												
A4120	C4 Steel Fixing to Wall	2d	13-Feb-17	15-Feb-17												
A4130	C4 External Wall Formwork	3d	15-Feb-17	18-Feb-17												
A4150	C4 Concrete to Wall	1d	18-Feb-17	19-Feb-17												
	Roof of EP	8d	19-Feb-17	27-Feb-17												
A4160	C4 Scaffolding & Soffit Formwork	3d	19-Feb-17	22-Feb-17												
A4170	C4 Steel Fixing to Roof	2d	22-Feb-17	24-Feb-17												
A4180	C4 Side Fromwork for Wall up to Roof Top	2d	24-Feb-17	26-Feb-17												
A4190	C4 Concrete to Roof	1d	26-Feb-17	27-Feb-17												
	Utility Trough	25d	10-Feb-17	07-Mar-17												
	Left Hand Side	8d	27-Feb-17	07-Mar-17												
A4200	C4 - LHS Backing Concrete of Utility Trough	4d	27-Feb-17	03-Mar-17												

Activity ID	Activity Name	Original Duration	Start	Finish												
					2016			2017								
					Dec			Jan			Feb			Mar		
	A4210	C4 - LHS Profile Barrier of Utility Trough	4d	03-Mar-17	07-Mar-17											C4 - LHS Profile Barrier of Utility Trough
	Right Hand Side		8d	10-Feb-17	18-Feb-17											
	A4220	C4 - RHS Backing Concrete of Utility Trough	4d	10-Feb-17	14-Feb-17											C4 - RHS Backing Concrete of Utility Trough
	A4230	C4 - RHS Profile Barrier of Utility Trough	4d	14-Feb-17	18-Feb-17											C4 - RHS Profile Barrier of Utility Trough
	Area B (CH475 to CH514) - steel Deck EB + SR8/TS3 Interface		76d	15-Dec-16 A	18-Mar-17											
	Vertical Blinding Bay C5 to Bay C6		13d	15-Dec-16 A	31-Dec-16											
	A4320	Bay C5	13d	15-Dec-16 A	31-Dec-16											
	Tunnel Structure at Area B - Bay C5 to C6		76d	01-Jan-17	18-Mar-17											
	Bay C5		68d	01-Jan-17	10-Mar-17											
	Structure		36d	01-Jan-17	06-Feb-17											
	1.2m Thick Base Slab		7d	01-Jan-17	07-Jan-17											
	T3350	C5 Base - Rebar Fixing	3d	01-Jan-17	03-Jan-17											C5 Base - Rebar Fixing
	T3360	C5 Base - Kicker Formwork & Water Stop	1d	04-Jan-17	04-Jan-17											C5 Base - Kicker Formwork & Water Stop
	T3370	C5 Base - Concreting	1d	05-Jan-17	05-Jan-17											C5 Base - Concreting
	T3390	C5 Base - Remove 6th Strut SL5 (5 Nos@SL5)	2d	06-Jan-17	07-Jan-17											C5 Base - Remove 6th Strut SL5 (5 Nos@SL5)
	1m Thick Tunnel Wall at Both Sides		15d	07-Jan-17	22-Jan-17											
	T3400	C5 Wall & OHVD - Erect Working Platform	1d	07-Jan-17	08-Jan-17											C5 Wall & OHVD - Erect Working Platform
	T3410	C5 Wall & OHVD - Steel Fixing	5d	08-Jan-17	13-Jan-17											C5 Wall & OHVD - Steel Fixing
	T3420	C5 Wall - Internal Formwork & Water Stop	3d	13-Jan-17	16-Jan-17											C5 Wall - Internal Formwork & Water Stop
	T3430	C5 Wall & OHVD - Concreting of Wall	1d	16-Jan-17	17-Jan-17											C5 Wall & OHVD - Concreting of Wall
	T3480	C5 Wall - Remove Wall Formwork	2d	17-Jan-17	19-Jan-17											C5 Wall - Remove Wall Formwork
	T3540	C5 Wall - Remove 3th & 4th Strut SL3 & SL4 (5 Nos@SL3 & 5 Nos@SL4)	3d	19-Jan-17	22-Jan-17											C5 Wall - Remove 3th & 4th Strut SL3 & SL4 (5 Nos@SL3 & 5 Nos@SL4)
	OHVD Slab		6d	22-Jan-17	28-Jan-17											
	T3440	C5 OHVD - Erect Falsework	1d	22-Jan-17	23-Jan-17											C5 OHVD - Erect Falsework
	T3450	C5 OHVD - Erect Soffit Formwork	2d	23-Jan-17	25-Jan-17											C5 OHVD - Erect Soffit Formwork
	T3460	C5 OHVD - Steel Fixing for Slab	2d	25-Jan-17	27-Jan-17											C5 OHVD - Steel Fixing for Slab
	T3470	C5 OHVD - Placing Concrete to OHVD Slab	1d	27-Jan-17	28-Jan-17											C5 OHVD - Placing Concrete to OHVD Slab
	400mm Thick OHVD Hanger Wall & 1.2m Thick Top Slab		9d	28-Jan-17	06-Feb-17											
	T3490	C5 OHVD - Steel Fixing for Hanger Wall	1d	28-Jan-17	29-Jan-17											C5 OHVD - Steel Fixing for Hanger Wall
	T3500	C5 OHVD - Erect Formwork for Hanger Wall	1d	29-Jan-17	30-Jan-17											C5 OHVD - Erect Formwork for Hanger Wall
	T3510	C5 Roof - Erect Falsework & Soffit Formwork	3d	30-Jan-17	02-Feb-17											C5 Roof - Erect Falsework & Soffit Formwork
	T3520	C5 Roof - Steel Fixing (Wall Steel Fixing Completed together with Roof)	3d	02-Feb-17	05-Feb-17											C5 Roof - Steel Fixing (Wall Steel Fixing Completed together with Roof)
	T3530	C5 Roof - Placing Concrete to Roof Slab & OHVD Hanger Wall	1d	05-Feb-17	06-Feb-17											C5 Roof - Placing Concrete to Roof Slab & OHVD Hanger Wall
	Removal of Falseworks & SL5		16d	06-Feb-17	22-Feb-17											
	T3330	C5 Roof - 10 Days Curing of Roof Prior to Removal of Falsework	10d	06-Feb-17	16-Feb-17											C5 Roof - 10 Days Curing of Roof Prior to Removal of Falsework
	T3340	C5 Roof - Remove Falsework	6d	16-Feb-17	22-Feb-17											C5 Roof - Remove Falsework
	Utility Trough		16d	22-Feb-17	10-Mar-17											
	Left Hand Side		8d	02-Mar-17	10-Mar-17											
	A4080	C5 - LHS Backing Concrete of Utility Trough	4d	02-Mar-17	06-Mar-17											C5 - LHS Backing Concrete of Utility Trough
	A4070	C5 - LHS Profile Barrier of Utility Trough	4d	06-Mar-17	10-Mar-17											C5 - LHS Profile Barrier of Utility Trough
	Right Hand Side		8d	22-Feb-17	02-Mar-17											
	A4090	C5 - RHS Backing Concrete of Utility Trough	4d	22-Feb-17	26-Feb-17											C5 - RHS Backing Concrete of Utility Trough
	A4100	C5 - RHS Profile Barrier of Utility Trough	4d	26-Feb-17	02-Mar-17											C5 - RHS Profile Barrier of Utility Trough
	Bay C6		70d	07-Jan-17	18-Mar-17											

Activity ID		Activity Name	Original Duration	Start	Finish	2016		2017																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
						Dec		Jan			Feb			Mar			Apr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
SR8 (Zone B) - Ch.385.000 to Ch.317.500 - (Inside Victoria Park to Tunnel Portal)	Structure		39d	07-Jan-17	15-Feb-17																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																

Activity ID	Activity Name	Original Duration	Start	Finish												
					2016			2017								
					Dec			Jan		Feb			Mar			Apr
	SR8_ZB_1480	Zone B - OHVD Bay 3 - Rebar Fixing for Slab of OHVD	3d	24-Jan-17	26-Jan-17					■	Zone B - OHVD Bay 3 - Rebar Fixing for Slab of OHVD					
	SR8_ZB_1490	Zone B - OHVD Bay 3 - Concrete of Slab of OHVD	1d	27-Jan-17	27-Jan-17					■	Zone B - OHVD Bay 3 - Concrete of Slab of OHVD					
	SR8_ZB_1530	Zone B - OHVD Bay 3 - Curing Period for OHVD Slab	10d	28-Jan-17	06-Feb-17					■	Zone B - OHVD Bay 3 - Curing Period for OHVD Slab					
	SR8_ZB_1500	Zone B - OHVD Bay 3 - Rebar Fixing to Hanger Wall	1d	01-Feb-17	01-Feb-17					■	Zone B - OHVD Bay 3 - Rebar Fixing to Hanger Wall					
	SR8_ZB_1510	Zone B - OHVD Bay 3 - Erect Hanger Wall Formwork for OHVD	2d	02-Feb-17	03-Feb-17					■	Zone B - OHVD Bay 3 - Erect Hanger Wall Formwork for OHVD					
	SR8_ZB_1520	Zone B - OHVD Bay 3 - Concrete Hanger Wall of OHVDV	1d	04-Feb-17	04-Feb-17					■	Zone B - OHVD Bay 3 - Concrete Hanger Wall of OHVDV					
	SR8_ZB_1540	Zone B - OHVD Bay 3 - Remove Soffit Formwork & Scaffolding	5d	07-Feb-17	11-Feb-17					■	Zone B - OHVD Bay 3 - Remove Soffit Formwork & Scaffolding					
	Utility Trough		28d	30-Dec-16	04-Feb-17											
	Left Hand Side		21d	09-Jan-17	04-Feb-17											
	SR8_ZB_1570	Zone B - U trough (LHS) Bay 3	7d	09-Jan-17	16-Jan-17			■	Zone B : U trough (LHS) Bay 3							
	SR8_ZB_1560	Zone B - U trough (LHS) Bay 2	7d	17-Jan-17	24-Jan-17			■	Zone B : U trough (LHS) Bay 2							
	SR8_ZB_1550	Zone B - U trough (LHS) Bay 1	7d	25-Jan-17	04-Feb-17				■	Zone B - U trough (LHS) Bay 1						
	Right Hand Side		21d	30-Dec-16	24-Jan-17											
	SR8_ZB_1600	Zone B - U trough (RHS) Bay 3	7d	30-Dec-16*	07-Jan-17		■	Zone B - U trough (RHS) Bay 3								
	SR8_ZB_1590	Zone B - U trough (RHS) Bay 2	7d	09-Jan-17	16-Jan-17			■	Zone B : U trough (RHS) Bay 2							
	SR8_ZB_1580	Zone B - U trough (RHS) Bay 1	7d	17-Jan-17	24-Jan-17				■	Zone B - U trough (RHS) Bay 1						
	Pump House		53d	30-Dec-16	20-Feb-17											
	Pressure Relief Manhole		14d	26-Jan-17	15-Feb-17											
	SR8_ZB_1800	PS- Manhole Internal Wall Formwork	4d	26-Jan-17	03-Feb-17					■	PS- Manhole Internal Wall Formwork					
	SR8_ZB_1810	PS- Erect Scaffolding + Roof Soffit Formwork	5d	03-Feb-17	09-Feb-17					■	PS- Erect Scaffolding + Roof Soffit Formwork					
	SR8_ZB_1820	PS- Rebar Fixing	4d	09-Feb-17	14-Feb-17					■	PS- Rebar Fixing					
	SR8_ZB_1830	PS- Place Concrete to Manhole Wall & Roof Slab	1d	14-Feb-17	15-Feb-17					■	PS- Place Concrete to Manhole Wall & Roof Slab					
	Floor Slabs & Partition Walls		14d	03-Feb-17	20-Feb-17											
	SR8_ZB_1860	PS-Internal Wall Inside Pump House	14d	03-Feb-17	20-Feb-17					■	PS-Internal Wall Inside Pump House					
	Remining Works inside Pump Sump E		52d	30-Dec-16	19-Feb-17											
	SR8_ZB_1890	Steel Works Installation inside Pump Sump E	45d	30-Dec-16	12-Feb-17					■	Steel Works Installation inside Pump Sump E					
	SR8_ZB_1900	Installation Manhole Covers for Pump Sump E	7d	13-Feb-17	19-Feb-17					■	Installation Manhole Covers for Pump Sump E					
	SR8 (Zone A) - Ch 317.500 to Ch 210.000 - U-Structure & Slab (Victoria Park)		37d	23-Dec-16 A	02-Feb-17											
	RC CCT & Backfill Ch317.5000 to Ch240.000		28d	23-Dec-16 A	02-Feb-17											
	Structure		28d	23-Dec-16 A	02-Feb-17											
	Utility Through		28d	23-Dec-16 A	02-Feb-17											
	SR8_ZA_1260	Zone A - Utility Trough for Zone A (CH240 to CH317)	28d	23-Dec-16 A	02-Feb-17		■	Zone A - Utility Trough for Zone A (CH240 to CH317)								
	SR8 Structural Slab Ch.240.000 to Ch.210.000		14d	30-Dec-16	12-Jan-17											
	SR8_2090B	Zone A - Wall - Bay 3	14d	30-Dec-16*	12-Jan-17			■	Zone A - Wall - Bay 3							
	Works in KD9 (Include Re-provisioning Works of KD4,KD5)		231d	10-Oct-16 A	05-Jul-17											
	External Works Under KD9		231d	14-Nov-16 A	05-Jul-17											
	Tsing Fung St - RW & Subway Extension & Toe Wall at Hing Fat St		115d	03-Dec-16 A	30-Mar-17											
	Retaining Wall + Toe Wall at Hing Fat Street		115d	03-Dec-16 A	30-Mar-17											
	Retaining Wall RW8D		115d	03-Dec-16 A	14-Mar-17											
	Bay 3(10m) to Bay 4(10m)		3d	30-Dec-16	01-Jan-17											
	RW8D_1220	RW8D (Bay 3 to Bay 4) - Sub-soil & Backfilling to Base Slab	3d	30-Dec-16	01-Jan-17				■	RW8D (Bay 3 to Bay 4) - Sub-soil & Backfilling to Base Slab						
	Bay 2(10m) to Bay 1(12.5m)		3d	30-Dec-16	01-Jan-17											
	RW8D_1230	RW8D(B2 to B1) - Sub-soil & Backfilling to Base	3d	30-Dec-16	01-Jan-17				■	RW8D(B2 to B1) - Sub-soil & Backfilling to Base						
	Re-open Hing Fat Street Footpath to Plubic (Request by VPMO)		111d	03-Dec-16 A	14-Mar-17											

Activity ID	Activity Name	Original Duration	Start	Finish												
					2016		2017									
					Dec		Jan		Feb		Mar			Apr		
A4590	Backfilling of Wall after Completion of RW8D Construction	9d	03-Dec-16 A	07-Dec-16 A	Wall after Completion of RW8D Construction											
A4600	Reinstatement of footpath for temp open to public	9d	07-Dec-16 A	14-Dec-16 A	Reinstatement of footpath for temp open to public											
A4610	Re-open Hing Fat Street Footpath for Plubic (From 5m CCTV footing to subway)	90d	15-Dec-16 A	14-Mar-17												
Works along RW8D During Reopen Hing Fat Street Footpath to Public		63d	03-Jan-17	07-Mar-17												
A4910	Cross Road Duct to Connect C19 Cable Draw Pit at Isalnd in Tsing Fung Street	45d	03-Jan-17*	28-Feb-17												
A4920	Demolition of Wall Head of Existing Retaining Wall at Tsing Fung Street	14d	19-Jan-17	08-Feb-17												
A4930	Install Steel Vechile Parapet on Wall Top from RW8D to RW8C	14d	07-Feb-17	21-Feb-17												
A4940	Minor Road Works above Demolished Wall Head	14d	08-Feb-17	24-Feb-17												
A4950	Realign & Provide the New Road Marking From Hing Fat Street to Tsing Fung Street	7d	25-Feb-17	07-Mar-17												
Retaining Walls RW8E, Sign Footings & Sewer Pipe (SK266G, SK539C, SK375B)		14d	15-Mar-17	30-Mar-17												
A4620	Excavate and lay blinding layer of RW8E	14d	15-Mar-17	30-Mar-17												
Foul Drain Pipe (VP Area, SK266G, SK265C & SK226L)		76d	14-Nov-16 A	21-Feb-17												
A4480	MH2-68B to MH2-69	14d	14-Nov-16 A	12-Dec-16 A	2-68B to MH2-69											
A4490	MH2-69 to MH2-70	14d	30-Dec-16	16-Jan-17												
A4440	MH2-63 to MH2-64 (under temp containers)	14d	16-Jan-17*	04-Feb-17												
A4460	MHA (beside pump sump E) to MH2-61	14d	04-Feb-17	21-Feb-17												
Storm Drain Pipe behind RW8C along Tsing Fung Street (SK547A)		60d	21-Nov-16 A	16-Jan-17												
A4510	MH TFS-03 to MH TFS-04 (with gully)	14d	21-Nov-16 A	14-Dec-16 A	MH TFS-03 to MH TFS-04 (with gully)											
A4520	MH TFS-04 to TFS-04a	11d	05-Dec-16 A	09-Dec-16 A	04 to TFS-04a											
A4530	TFS-04a to Extg MH A1	11d	10-Dec-16 A	15-Dec-16 A	TFS-04a to Extg MH A1											
A4540	MHTFS-05 to extg MH A3 (gully)	14d	30-Dec-16	16-Jan-17												
Sign Footings at Victoria Park		75d	30-Dec-16	31-Mar-17												
A4570	Construction of 5m CCTV, AID, OHVD, TSG, luminance meter at verge inside VP	60d	30-Dec-16	14-Mar-17												
A4580	All drawpits (ATC, E&M and lighting) and ductings at verge inside VP (SK375B)	60d	18-Jan-17	31-Mar-17												
Boundary Fence, Type 2 Railing Footings & Fence Wall From RW8C to Zone B		188d	23-Dec-16 A	05-Jul-17												
A4710	Modification of extg type 2 railing footing in front of RW8C (approx. 40m)	30d	23-Dec-16 A	14-Mar-17												
A4700	Construction of boundary fenceadjacent RW8C toe wall (approx. 40m)	30d	30-Dec-16*	07-Feb-17												
A4990	Abour Footings Construction	14d	11-Mar-17	25-Mar-17												
A4720	Construction of boundary fence (approx. 460m)	90d	15-Mar-17	05-Jul-17												
A5000	Shelter & Benches Installation	21d	25-Mar-17	15-Apr-17												
A4730	Fence wall between BGO and Zone A (60m)	30d	24-Nov-17 A	11-Mar-17												
Other Storm, Sewerage Pipe & Irrigation System in VP (SK336D, SK539C)		70d	04-Feb-17	04-May-17												
A4740	FMH-B03 to Extg 1-40 (8 MHS and 7 foul pipeline)	40d	04-Feb-17	23-Mar-17												
A4780	Complete Backfilling & Removal Top Two Layer of Strut at Bay 3 of Zone B	14d	01-Mar-17*	16-Mar-17												
A4760	MHB (beside pump sump E) to MH2-70 (300 dia. stormwater pipeline)	14d	17-Mar-17	01-Apr-17												
A4750	SHM-B01 to Extg. MH A3 (4 MHS and 4 storm pipeline)	30d	23-Mar-17	04-May-17												
Preparation Works before Implementation TTA at Central Median		64d	30-Dec-16	04-Mar-17												
A4790	Construction of drawpit, ducting and remedial work on top of RW8C etc on top of RW8C	30d	30-Dec-16	07-Feb-17												
A4800	Lay temp bituminous pavement for road diversion beside RW8C (Incl. Steel Vehicle Parapet on RW8C)	20d	08-Feb-17	02-Mar-17												
A4810	Implement TTA for Closing Central Median at Tsing Fung Street	1d	03-Mar-17	04-Mar-17												
Centre Median at Tsing Fung Street (SK375B, SK226L)		60d	04-Mar-17	19-May-17												
A4820	Construct VMS6, LCS footing, ATC drawpit and ducts , steel vehicle parapet	60d	04-Mar-17	19-May-17												
Works in Victoria Park (KD4, KD5, KD9)		153d	10-Oct-16 A	02-Jun-17												
Re-Provisioning Works		153d	10-Oct-16 A	02-Jun-17												

Activity ID	Activity Name	Original Duration	Start	Finish										
					2016		2017							
					Dec		Jan		Feb		Mar		Apr	
Nursery Compound														
Submission														
ABWF Submission														
Material														
VP_NC_1050	ABWF Materail - ER Review and Approval	28d	18-Oct-16 A	30-Dec-16										
VP_NC_1060	ABWF Issue P.O. / MAnufacturing / Fabrication	30d	30-Dec-16	07-Feb-17										
VP_NC_1070	ABWF Materail Delivery	30d	08-Feb-17	14-Mar-17										
Shop Drawing														
VP_NC_1080	ABWF Shop Drawing - Submission	21d	10-Oct-16 A	31-Dec-16										
VP_NC_1090	ABWF Shop Drawing - ER Review and Approval	60d	03-Jan-17	16-Mar-17										
E&M Submission														
Material														
VP_NC_1130	E&M Materail - ER Review and Approval	28d	21-Oct-16 A	06-Jan-17										
VP_NC_1140	E&M Issue P.O. / MAnufacturing / Fabrication	15d	07-Jan-17	24-Jan-17										
VP_NC_1150	E&M Materail Delivery	30d	25-Jan-17	03-Mar-17										
Shop Drawing														
VP_NC_1160	E&M Shop Drawing - Submission	21d	07-Jan-17	03-Feb-17										
VP_NC_1170	E&M Shop Drawing - ER Review and Approval	30d	04-Feb-17	10-Mar-17										
Nursery compound														
A4370	Backfill to ground slab and beams (including underground PE pipes installation work)	8d	24-Nov-16 A	03-Dec-16 A										
A4380	Construction of ground slab and beams	7d	09-Dec-16 A	30-Dec-16										
A4390	Fix rebar and erect walls, columns, falsework and fwk to roof slab and beams	12d	30-Dec-16	13-Jan-17										
A4400	Construction of roof slab and beams	7d	14-Jan-17	21-Jan-17										
A4410	Concreting of two concrete plinths, 150 thick curbs and 1450H parapet wall above roof slab	7d	23-Jan-17	02-Feb-17										
A4420	ABWF, Plumbing Works, waterproofing and E&M works	60d	17-Mar-17	02-Jun-17										
Sea Wall Reinstatement & Reverting Traffic for IEC,VP Rd & TF St (KD9)														
Reinstatement Existing Slopping & Vertical Sea Wall														
Major Reinstatement Works for Seawall Reinstatement														
Stage 1														
A5040	Diversion of Temporary Pedestrian Walkway on D-wall	7d	02-Mar-17	09-Mar-17										
TTA Revert Traffic Back to Original Alignment														
Preparation Works - Backfill of Zone C to Top of Tunnel Structure														
A5780	Curing to Roof Slab of Zone C	3d	15-Feb-17	18-Feb-17										
A5790	Waterproofing & Screeding to Roof	4d	18-Feb-17	22-Feb-17										
A5800	Load Transfer for King Post	6d	22-Feb-17	28-Feb-17										
A5810	Make Good Box-out Left by King Post	2d	28-Feb-17	02-Mar-17										
A5820	Backfill to Formation & Remove Struts SL1 to SL3 (Approx. 7m)	33d	02-Mar-17	04-Apr-17										
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks														
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)														
EW_1000	Establishment Works - for Landscape Softworks and transplanted trees in Portion XIV & XV	901d	23-Feb-15 A	14-Dec-17										
KD12 - Section 7B: Portion VI & VII (Reprov. Bowling Green Area)														
EW_1010	Establishment Works - for Landscape Softworks and transplanted trees in Portion VI & VII	177d	03-Dec-15 A	30-Dec-16										
KD10 - Preservation and Protection of Trees														
PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	30-Dec-16										

Activity ID	Activity Name	Original Duration	Start	Finish	2016				2017											
					Dec				Jan			Feb				Mar				Apr
	KD15 & KD8 - Mooring Components Upkeep (CBTS and ATS)	1423d	21-Mar-13 A	30-Dec-16																
MAR_2000	Mooring Upkeep at Portion XIX(19) & XX(20) - ATS (if instructed by Engineer)	1399d	21-Mar-13 A	30-Dec-16																
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	30-Dec-16																
	Works for Public Works Regional Laboratory (North Lantau) - KD1,KD16,KD17)	1301d	19-Jul-13 A	21-Nov-17																
	KD17 - Maintenance and Upkeep of New PWRL (Portion XVII)	1301d	19-Jul-13 A	21-Nov-17																
PWRL_1050	Maintenance/ Upkeep of New PWRL	1301d	19-Jul-13 A	21-Nov-17																

China State Construction Engineering (Hong Kong) Ltd.

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)

Activity Name	Start	Finish	2017		
			Apr	May	Jun
Hung Hing Road Resurfacing	1/6/2017	30/6/2017			
Defect works inside tunnel	1/4/2017	30/9/2017			

Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip
Road 8 Section) - 3 Months Rolling Programme

Date	Revision	Checked	Approved
20-Apr-17	DWP-07 (6) - 3 Months Rolling	FS	TL

Activity ID		Activity Name	Original Duration	Start	Finish	2017											
						Apr			May			Jun			Jul		
		Removal Bulkhead at CH525 (TS3W / SR8 Junction)	41d	06-Mar-17 A	13-Apr-17 A												
		A6080 Remove Bulkhead between TS3W & SR8	37d	06-Mar-17 A	13-Apr-17 A												
		A5180 Remove Scaffolding of SR1R Roof	4d	22-Mar-17 A	25-Mar-17 A												
		Works in KD8	129d	09-Mar-17 A	28-Jul-17												
		TS3W - Remove Temporary Reclamation	129d	09-Mar-17 A	28-Jul-17												
		Stage 1 - North West Comer (Bay Z4-25 to Bay 20)	56d	09-Mar-17 A	14-Apr-17 A												
		A2660 Remove filled material to -4.35mPD at Bay Z4-25 to Bay 19 (6,500m3)	8d	09-Mar-17 A	24-Mar-17 A												
		A2670 Remove filled material to -4.35mPD at Bay Z4-22 to Z4-24 (4,500m3)	5d	25-Mar-17 A	14-Apr-17 A												
		A2680 Remove seawall blocks at Bay Z4-25 to Bay 20 (426 nos.)	8d	27-Mar-17 A	10-Apr-17 A												
		A6260 Remove filled material to -7.0 mPD	4d	05-Apr-17 A	13-Apr-17 A												
		Stage 2 - North to East Side (Bay 19 to Bay 11 + Bay 26 to Bay 28)	14d	24-Mar-17 A	07-Apr-17 A												
		A2690 Break concrete slab at Bay 19 to Bay 11 + Bay 26 to Bay 28 (2,500m2)	7d	24-Mar-17 A	31-Mar-17 A												
		A2700 Remove filled material to +2.8mPD (2,500m3)	7d	01-Apr-17 A	07-Apr-17 A												
		Stage 3 - North to East Side (Bay 19 to bay 26)	49d	31-Mar-17 A	01-May-17												
		A2710 Completion of Recharging of Sea Water into TS3W Cofferdam	2d	31-Mar-17 A	04-Apr-17 A												
		North West D-wall Opening	22d	07-Apr-17 A	29-Apr-17 A												
		A2720 Core D-wall cut holes at Panel DW02 to NA6 (27 nos.)	6d	07-Apr-17 A	10-Apr-17 A												
		A2730 Vertical cut at Panel DW02 to NA6 (19 nos.)	8d	14-Apr-17 A	20-Apr-17 A												
		A2740 Horizontal cut at Panel DW02 to NA6 (25 nos.)	8d	21-Apr-17 A	29-Apr-17 A												
		North East & East	13d	13-Apr-17 A	01-May-17												
		A2750 Remove filled material to -4.35mPD (22,500m3)	9d	13-Apr-17 A	26-Apr-17												
		A2760 Remove seawall blocks at Bay 19 to 11 & Bay 26 to 28 (1,335 nos.)	13d	20-Apr-17 A	29-Apr-17												
		A2770 Remove filled material to -7.0mPD (North & East side)	10d	29-Apr-17 A	01-May-17												
		Stage 4 - West & South Side (Remove Seawall Block Bay Z4-23 & 24, Excavate to -4.35mPD)	47d	31-Mar-17 A	05-Jun-17												
		West Side	18d	31-Mar-17 A	07-May-17												
		A2790 Remove seawall blocks at Bay Bay Z4-23 to Z4-24 (249 nos.)	5d	31-Mar-17 A	02-May-17												
		A2800 Remove filled material to -7.0mPD (West)	5d	03-May-17	07-May-17												
		North East Side	32d	19-Apr-17 A	05-Jun-17												
		A2810 Core D-wall cut holes at Panel W1D1 to W1D32 (128 nos.) (North Side)	14d	19-Apr-17 A	26-Apr-17 A												
		A2820 Vertical cut at Panel W1D1 to W1D32 (96 nos.) (North Side)	16d	27-Apr-17 A	08-May-17												
		A2830 Horizontal cut at Panel W1D1 to W1D32 (128 nos.) (North Side)	20d	17-May-17	05-Jun-17												
		East Side	33d	20-Apr-17 A	03-Jun-17												
		A2840 Core D-wall cut holes at Panel TZ31 to TZ38 (32 nos.) (East Side)	10d	20-Apr-17 A	26-Apr-17 A												
		A2850 Vertical cut at Panel TZ31 to TZ38 (24 nos.) (East Side)	9d	16-May-17	24-May-17												
		A2860 Horizontal cut at Panel TZ31 to TZ38 (32 nos.) (East Side)	10d	25-May-17	03-Jun-17												
		South Side	30d	20-Apr-17	19-May-17												
		A2870 Remove filled material to -4.35mPD (41,300m3)	30d	20-Apr-17	19-May-17												
		Stage 5 - West & South side (Reove Seawwall Block Bay 24 7 25, Excavate to -7.0mPD)	30d	12-Apr-17 A	06-Jun-17												
		A2910 Core D-wall cut holes at Panel BWD2 to BWD9 (30 nos.) (West Side)	5d	12-Apr-17 A	17-Apr-17 A												
		A2920 Vertical cut at Panel BWD2 to BWD9 (22 nos.) (West Side)	8d	08-May-17	15-May-17												
		A2930 Horizontal cut at Panel BWD2 to BWD9 (29 nos.) (West Side)	8d	16-May-17	23-May-17												
		A2880 Remove seawall blocks at Bay 24, 25 (264 nos.) (South West)	6d	20-May-17	25-May-17												
		A2890 Remove seawall blocks at Bay 2 to 4 (550 nos.) (South East)	11d	20-May-17	30-May-17												
		A2900 Remove filled material to -7.0mPD (South)	7d	31-May-17	06-Jun-17												

中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Page 2 of 8
Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip Road 8 Section) - 3 Months Rolling Progamme

Date	Revision	Checked	Approved
20-Apr-17	DWP-07 (6) - 3 Months Rolling	FS	TL

Activity ID		Activity Name	Original Duration	Start	Finish	2017											
						Apr			May			Jun			Jul		
Stage 6 - West & South Side (Saw Cut D-wall + Shaft D)			48d	24-May-17	10-Jul-17												
A2940	Remove fill material to -7.0mPD around shaft D	5d	24-May-17	28-May-17													
A2950	Core D-wall cut holes at PanelW2D1 to W2D18 (72 nos.) (South West)	9d	07-Jun-17	15-Jun-17													
A2980	Core D-wall cut holes at Panel W2D23 to W2D34 (50 nos.) (South East)	10d	07-Jun-17	16-Jun-17													
A2990	Vertical cut at Panel W2D23 to W2D34 (38 nos.) (South East)	13d	11-Jun-17	23-Jun-17													
A2960	Vertical cut at Panel W2D1 to W2D18 (54 nos.) (South West)	18d	15-Jun-17	02-Jul-17													
A3000	Horizontal cut at Panel W2D23 to W2D34 (50 nos.) (South East)	13d	18-Jun-17	30-Jun-17													
A2970	Horizontal cut at Panel W2D1 to W2D18 (72 nos.) (South West)	18d	23-Jun-17	10-Jul-17													
Stage 7 - West & South Side (Saw Cut Shaft D, Excavate to -7.0mPD at SR8)			40d	29-May-17	07-Jul-17												
A3010	Vertical cut at Shaft D (14 nos.)	10d	29-May-17	07-Jun-17													
A3020	Horizontal cut at Shaft D (14 nos.)	5d	08-Jun-17	12-Jun-17													
A3030	Remove filled material to -7.0mPD at SR8	7d	01-Jul-17	07-Jul-17													
Stage 8 - South East & West Side (Remove Seawall Block Bay Z4-22 to Bay 23, Saw Cut D-wall at SR8)			46d	13-Jun-17	28-Jul-17												
South West Side			42d	13-Jun-17	24-Jul-17												
A3040	Remove seawall blocks at Bay Z4-22 to Bay 23 (741 nos.)	15d	13-Jun-17	27-Jun-17													
A3050	Remove filled material to -7.0mPD (South West)	8d	28-Jun-17	05-Jul-17													
A3060	Vertical cut at Panel BWD10 to SA7 (26 nos.) (South West)	9d	06-Jul-17	14-Jul-17													
A3070	Horizontal cut at Panel BWD10 to SA7 (37 nos.) (South West)	10d	15-Jul-17	24-Jul-17													
SR08 - West Wall			21d	08-Jul-17	28-Jul-17												
A3080	Vertical cut at Panel W4D1 to W4D11 (28 nos.) (SR8)	10d	08-Jul-17	17-Jul-17													
A3090	Horizontal cut at Panel W4D1 to W4D11 (39 nos.) (SR8)	11d	18-Jul-17	28-Jul-17													
SR08 - East Wall			19d	08-Jul-17	26-Jul-17												
A7010	Vertical cut at Panel W4D1 to W4D11 (26 nos.)	9d	08-Jul-17	16-Jul-17													
A7020	Horizontal cut at Panel W3D1 to W3D7 (36 nos.)	10d	17-Jul-17	26-Jul-17													
Works in KD6			136d	22-Jan-17 A	05-Jul-17												
Works in SR8 (Open Cut Method)			136d	22-Jan-17 A	05-Jul-17												
SR8 (Zone C) - Ch. 528 to Ch. 368			88d	14-Feb-17 A	16-May-17												
Zone C - Tunnel Structure			88d	14-Feb-17 A	16-May-17												
1.2m Thick Base Slab			2d	26-Feb-17 A	21-Apr-17												
Bay C6			2d	26-Feb-17 A	21-Apr-17												
A7540	C6 - Remove Strut SL5 & SL3	2d	26-Feb-17 A	21-Apr-17													
1.0m Thick Wall at Both Side			7d	22-Apr-17	28-Apr-17												
LHS Wall			7d	22-Apr-17	28-Apr-17												
A7340	5th Pour - CH500 to CH525	7d	22-Apr-17	28-Apr-17													
200mm Thick OHVD Slab & 400mm Thick Hanger Wall			9d	01-May-17	09-May-17												
Bay C6			9d	01-May-17	09-May-17												
A7570	C6 - Construct OHVD Slab & Hanger Wall	9d	01-May-17	09-May-17													
1.2m Thick Roof Slab			55d	14-Feb-17 A	08-May-17												
Bay C4			13d	14-Feb-17 A	24-Mar-17 A												
A7610	C4 - Roof Slab Construction	13d	14-Feb-17 A	24-Mar-17 A													
Bay C5			8d	16-Mar-17 A	25-Mar-17 A												
A7620	C5 - Roof Slab Construction	8d	16-Mar-17 A	25-Mar-17 A													
Bay C6			9d	23-Mar-17 A	08-May-17												
A7630	C6 - Partial Roof + Up Stand Wall Construction for Access Shaft	9d	23-Mar-17 A	08-May-17													



中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Date	Revision	Checked	Approved
20-Apr-17	DWP-07 (6) - 3 Months Rolling	FS	TL

Activity ID	Activity Name	Original Duration	Start	Finish	2017											
					Apr			May			Jun			Jul		
Egress Passage - EP01		31d	13-Mar-17 A	24-Apr-17 A												
Bay C1		31d	13-Mar-17 A	14-Apr-17 A												
A7690	C1 - EP01 Wall Construction	9d	13-Mar-17 A	30-Mar-17 A	Wall Construction											
A7700	C1 - EP01 Roof Construction	8d	13-Mar-17 A	30-Mar-17 A	Roof Construction											
A8010	C1 - Dismantle Scaffolding of EP01 Roof Slab - 10 days Curing	14d	31-Mar-17 A	14-Apr-17 A	C1 - Dismantle:Scaffolding of EP01 Roof Slab - 10 days Curing											
Bay C2		31d	13-Mar-17 A	14-Apr-17 A												
A7710	C2 - EP01 Wall Construction	9d	13-Mar-17 A	30-Mar-17 A	Wall Construction											
A7720	C2 - EP01 Roof Construction	8d	13-Mar-17 A	30-Mar-17 A	Roof Construction											
A8020	C2 - Dismantle Scaffolding of EP01 Roof Slab - 10 days Curing	14d	31-Mar-17 A	14-Apr-17 A	C2 - Dismantle:Scaffolding of EP01 Roof Slab - 10 days Curing											
Bay C3		31d	20-Mar-17 A	24-Apr-17 A												
A7730	C3 - EP01 Wall Construction	9d	20-Mar-17 A	05-Apr-17 A	C3 - EP01 Wall Construction											
A7740	C3 - EP01 Roof Construction	8d	20-Mar-17 A	05-Apr-17 A	C3 - EP01 Roof Construction											
A8030	C3 - Dismantle Scaffolding of EP01 Roof Slab - 10 days Curing	14d	06-Apr-17 A	24-Apr-17 A	C3 - Dismantle Scaffolding of EP01 Roof Slab - 10 days Curing											
Bay C4		31d	20-Mar-17 A	24-Apr-17 A												
A7750	C4 - EP01 Wall Construction	9d	20-Mar-17 A	05-Apr-17 A	C4 - EP01 Wall Construction											
A7760	C4 - EP01 Roof Construction	8d	20-Mar-17 A	05-Apr-17 A	C4 - EP01 Roof Construction											
A8040	C4 - Dismantle Scaffolding of EP01 Roof Slab - 10 days Curing	14d	06-Apr-17 A	24-Apr-17 A	C4 - Dismantle Scaffolding of EP01 Roof Slab - 10 days Curing											
Utility Trough		27d	20-Apr-17	16-May-17												
Bay C1		16d	20-Apr-17	05-May-17												
A7790	RHS / C1 - Backing Concrete	4d	20-Apr-17	23-Apr-17	RHS / C1 - Backing Concrete											
A7800	RHS / C1 - Profile Barrier	4d	24-Apr-17	27-Apr-17	RHS / C1 - Profile Barrier											
A7770	LHS / C1 - Backing Concrete	4d	28-Apr-17	01-May-17	LHS / C1 - Backing Concrete											
A7780	LHS / C1 - Profile Barrier	4d	02-May-17	05-May-17	LHS / C1 - Profile Barrier											
Bay C2		16d	20-Apr-17	05-May-17												
A7830	RHS / C2 - Backing Concrete	4d	20-Apr-17	23-Apr-17	RHS / C2 - Backing Concrete											
A7840	RHS / C2 - Profile Barrier	4d	24-Apr-17	27-Apr-17	RHS / C2 - Profile Barrier											
A7810	LHS / C2 - Backing Concrete	4d	28-Apr-17	01-May-17	LHS / C2 - Backing Concrete											
A7820	LHS / C2 - Profile Barrier	4d	02-May-17	05-May-17	LHS / C2 - Profile Barrier											
Bay C3		16d	20-Apr-17	05-May-17												
A7870	RHS / C3 - Backing Concrete	4d	20-Apr-17	23-Apr-17	RHS / C3 - Backing Concrete											
A7880	RHS / C3 - Profile Barrier	4d	24-Apr-17	27-Apr-17	RHS / C3 - Profile Barrier											
A7850	LHS / C3 - Backing Concrete	4d	28-Apr-17	01-May-17	LHS / C3 - Backing Concrete											
A7860	LHS / C3 - Profile Barrier	4d	02-May-17	05-May-17	LHS / C3 - Profile Barrier											
Bay C4		16d	20-Apr-17	05-May-17												
A7910	RHS / C4 - Backing Concrete	4d	20-Apr-17	23-Apr-17	RHS / C4 - Backing Concrete											
A7920	RHS / C4 - Profile Barrier	4d	24-Apr-17	27-Apr-17	RHS / C4 - Profile Barrier											
A7890	LHS / C4 - Backing Concrete	4d	28-Apr-17	01-May-17	LHS / C4 - Backing Concrete											
A7900	LHS / C4 - Profile Barrier	4d	02-May-17	05-May-17	LHS / C4 - Profile Barrier											
Bay C5		16d	01-May-17	16-May-17												
A7950	RHS / C5 - Backing Concrete	4d	01-May-17	04-May-17	RHS / C5 - Backing Concrete											
A7960	RHS / C5 - Profile Barrier	4d	05-May-17	08-May-17	RHS / C5 - Profile Barrier											
A7930	LHS / C5 - Backing Concrete	4d	09-May-17	12-May-17	LHS / C5 - Backing Concrete											
A7940	LHS / C5 - Profile Barrier	4d	13-May-17	16-May-17	LHS / C5 - Profile Barrier											
SR8 (Zone B) - Ch.385.000 to Ch.317.500 - (Inside Victoria Park to Tunnel Portal)		77d	20-Apr-17	05-Jul-17												



中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.


- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Page 4 of 8

Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip Road 8 Section) - 3 Months Rolling Progamme

Date	Revision	Checked	Approved
20-Apr-17	DWP-07 (6) - 3 Months Rolling	FS	TL

Activity ID		Activity Name		Original Duration	Start	Finish	2017											
							Apr			May			Jun			Jul		
		SR8 (Zone B) Tunnel - ELS / CCT / BF Works (7 Bays Ch. 385.000 to Ch.317.500)		77d	20-Apr-17	05-Jul-17												
		Portal Structure		77d	20-Apr-17	05-Jul-17												
		OHVD		43d	20-Apr-17	01-Jun-17												
		Bay B1 + B2 (CH338.625 to CH368)		43d	20-Apr-17	01-Jun-17												
	SR8_ZB_1390	Zone B - OHVD - Erect Scaffolding & Soffit Formwork		6d	20-Apr-17	25-Apr-17												
	SR8_ZB_1400	Zone B - Redrill & Install Rebar on Soffit of Roof Slab		10d	26-Apr-17	05-May-17												
	SR8_ZB_1420	Zone B - OHVD - Rebar Fixing for Slab & Hanger Wall of OHVD		4d	06-May-17	10-May-17												
	SR8_ZB_1430	Zone B - OHVD Erect Hanger Wall Formwork for OHVD		2d	11-May-17	12-May-17												
	SR8_ZB_1440	Zone B - OHVD Place Concrete to OHVD Slab & Wall		1d	13-May-17	13-May-17												
	SR8_ZB_1450	Zone B - OHVD Curing Period for OHVD Slab		10d	15-May-17	25-May-17												
	SR8_ZB_1460	Zone B - OHVD Remove Soffit Formwork & Scaffolding		5d	26-May-17	01-Jun-17												
		Utility Trough		28d	02-Jun-17	05-Jul-17												
		Left Hand Side		21d	10-Jun-17	05-Jul-17												
	SR8_ZB_1570	Zone B - U trough (LHS) Bay 3		7d	10-Jun-17	17-Jun-17												
	SR8_ZB_1560	Zone B - U trough (LHS) Bay 2		7d	19-Jun-17	26-Jun-17												
	SR8_ZB_1550	Zone B - U trough (LHS) Bay 1		7d	27-Jun-17	05-Jul-17												
		Right Hand Side		21d	02-Jun-17	26-Jun-17												
	SR8_ZB_1600	Zone B - U trough (RHS) Bay 3		7d	02-Jun-17	09-Jun-17												
	SR8_ZB_1590	Zone B - U trough (RHS) Bay 2		7d	10-Jun-17	17-Jun-17												
	SR8_ZB_1580	Zone B - U trough (RHS) Bay 1		7d	19-Jun-17	26-Jun-17												
		Pump House		52d	20-Apr-17	10-Jun-17												
		Remining Works inside Pump Sump E		52d	20-Apr-17	10-Jun-17												
	SR8_ZB_1890	Steel Works Installation inside Pump Sump E		45d	20-Apr-17	03-Jun-17												
	SR8_ZB_1900	Installation Manhole Covers for Pump Sump E		7d	04-Jun-17	10-Jun-17												
		SR8 (Zone A) - Ch 317.500 to Ch 210.000 - U-Structure & Slab (Victoria Park)		28d	22-Jan-17 A	26-May-17												
		RC CCT & Backfill Ch317.5000 to Ch240.000		28d	22-Jan-17 A	26-May-17												
		Structure		28d	22-Jan-17 A	26-May-17												
		Utility Through		28d	22-Jan-17 A	26-May-17												
	SR8_ZA_1260	Zone A - Utility Trough for Zone A (CH240 to CH317)		28d	22-Jan-17 A	26-May-17												
		Works in KD9 (Include Re-provisioning Works of KD4,KD5)		299d	12-Dec-16 A	11-Sep-17												
		External Works Under KD9		299d	12-Dec-16 A	11-Sep-17												
		Tsing Fung St - RW & Subway Extension & Toe Wall at Hing Fat St		191d	23-Jan-17 A	01-Aug-17												
		Retaining Wall + Toe Wall at Hing Fat Street		191d	23-Jan-17 A	01-Aug-17												
		Retaining Wall RW8D		100d	23-Jan-17 A	02-May-17												
		Bay 3(10m) to Bay 4(10m)		6d	23-Jan-17 A	23-Mar-17 A												
	RW8D_1220	RW8D (Bay 3 to Bay 4) - Sub-soil &Backfilling to Base Slab		6d	23-Jan-17 A	23-Mar-17 A												
		Works along RW8D During Reopen Hing Fat Street Footpath to Public		33d	01-Mar-17 A	02-May-17												
	A4910	Close slow lane of HFS to cut coping of RW8D and subway		20d	01-Mar-17 A	26-Apr-17 A												
	A4920	Lay temp bituminous pavement for road diversion (from RW8D to Subway)		3d	20-Apr-17	22-Apr-17												
	A4940	Install steel vehicle parapet on RW8C, subway and RW8D		10d	20-Apr-17	02-May-17												
		Retaining Walls RW8E, Sign Footings & Sewer Pipe (SK266G, SK539C, SK375B)		135d	20-Mar-17 A	01-Aug-17												
	A4615	Re-occupy Hing Fat Street Footpath as site Area		1d	20-Mar-17 A	20-Mar-17 A												
	A4620	Excavate and lay blinding layer of RW8E (Including ELS)		14d	19-Apr-17 A	08-May-17												
	A4880	DS16 - Sign Frame Installation		14d	20-Apr-17	03-May-17												

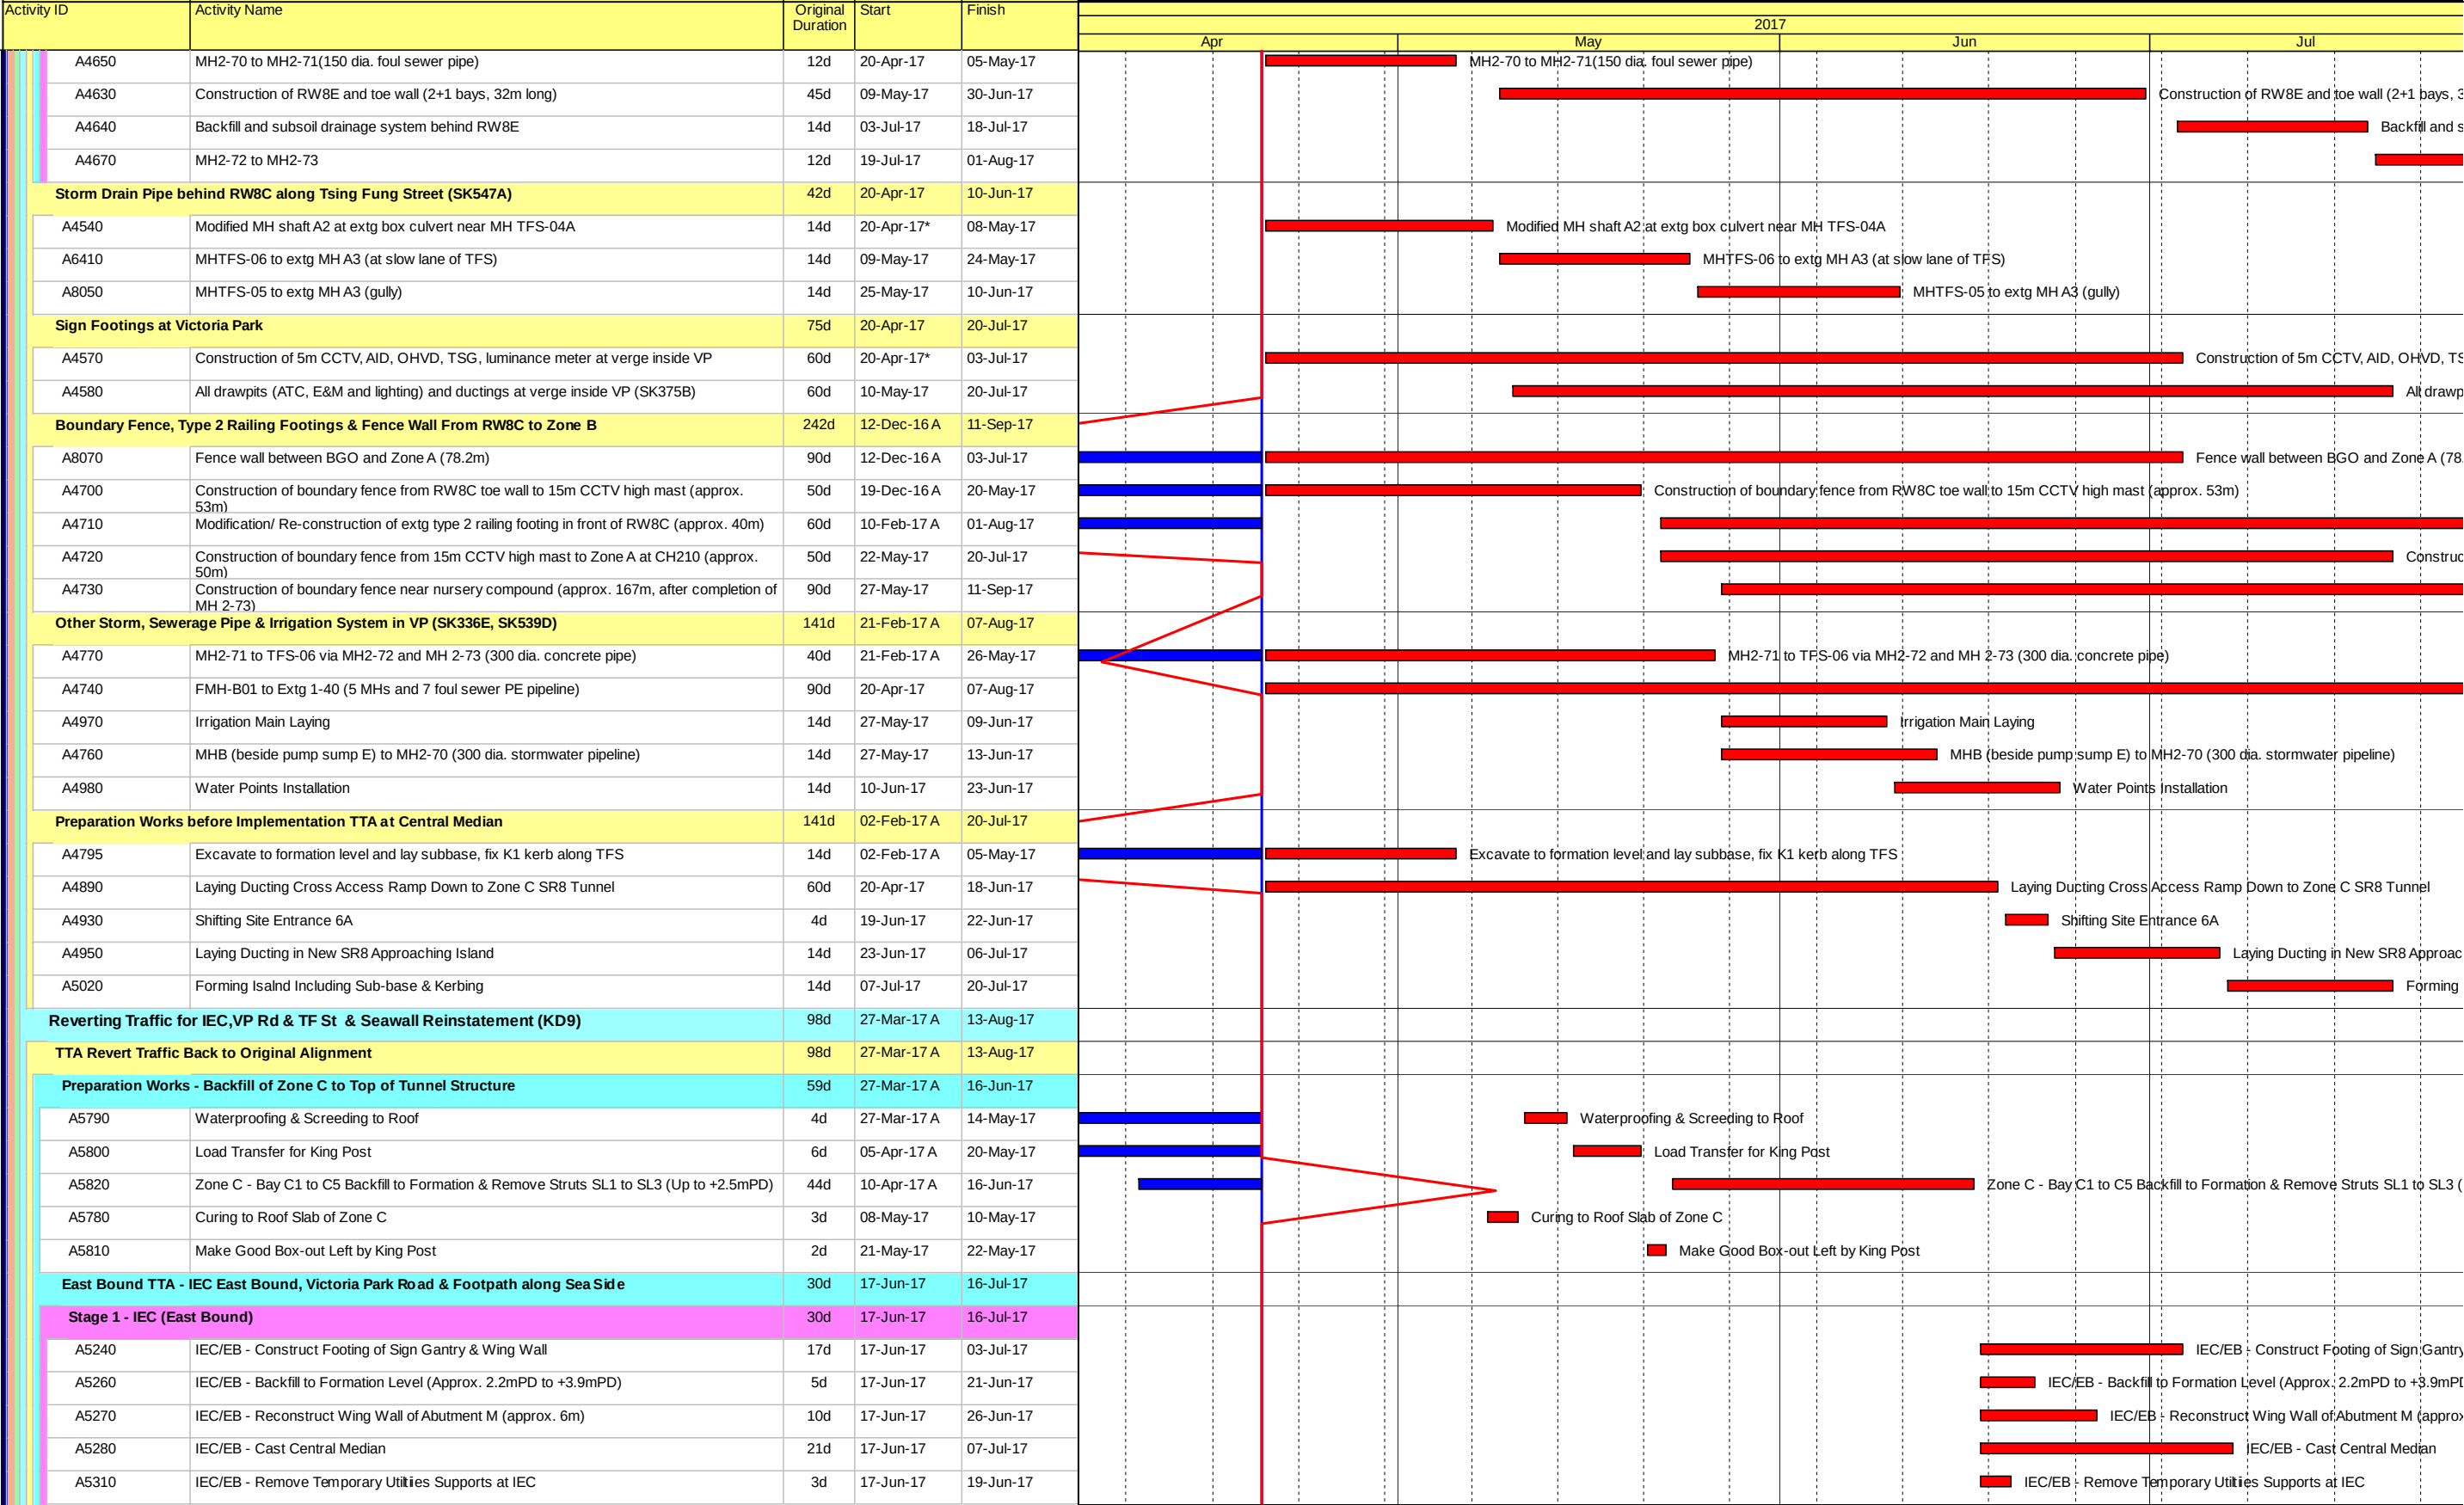

中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Date	Revision	Checked	Approved
20-Apr-17	DWP-07 (6) - 3 Months Rolling	FS	TL


Activity ID		Activity Name	Original Duration	Start	Finish	2017											
						Apr			May			Jun			Jul		
	A3285	IEC/EB - Cut and Remove Pipe Pile (2m Below Ground Level)	7d	17-Jun-17	23-Jun-17												
	A5320	IEC/EB - Reinstate Existing Drainage System	14d	20-Jun-17	03-Jul-17												
	A3286	IEC/EB - Cut and Remove Sheet Pile (2m Below Ground Level)	7d	24-Jun-17	30-Jun-17												
	A5290	IEC/EB - Street Lighting Cable Duct & Poles	3d	01-Jul-17	03-Jul-17												
	A5250	IEC/EB - Install A Frame of Sign Gantry	4d	04-Jul-17	07-Jul-17												
	A5300	IEC/EB - TOC of Street Lightings	2d	04-Jul-17	05-Jul-17												
	A5330	IEC/EB - Backfill Drainage Tranch Up to Formnation (+2.5mPd to +3.9mPD)	5d	04-Jul-17	08-Jul-17												
	A5340	IEC/EB - Laying Sub-base	2d	09-Jul-17	10-Jul-17												
	A5350	IEC/EB - Laying Asphlat Pavement	3d	11-Jul-17	13-Jul-17												
	A5360	IEC/EB - Road Mark & Traffic Signs	3d	14-Jul-17	16-Jul-17												
	West Bound - IEC West Bound & Tsing Fung Street		58d	17-Jun-17	13-Aug-17												
	Stage 1 - IEC (West Bound)		30d	17-Jun-17	16-Jul-17												
	A5690	IEC/WB - Cut pipe pile - 1 week	7d	17-Jun-17	23-Jun-17												
	A5710	IEC/WB - Removal of pedestrian decking	11d	17-Jun-17	27-Jun-17												
	A3785	IEC/WB - Reconstruct Wing Wall of Abutment M (approx. 6m)	10d	17-Jun-17	26-Jun-17												
	A5700	IEC/WB - Cut sheetpile - 1 week	7d	24-Jun-17	30-Jun-17												
	A5720	IEC/WB - Remove temporary utilities support 3 days	3d	28-Jun-17	30-Jun-17												
	A5730	IEC/WB - Backfill up to Formation under Asphalt (from +2.5mPD to +3.9mPD) 5 days	5d	01-Jul-17	05-Jul-17												
	A5740	IEC/WB - Subbase Laying 2 days	2d	06-Jul-17	07-Jul-17												
	A5750	IEC/WB - Asphalt (Road Base, Base Course, Wearing Course) 5 days	5d	08-Jul-17	12-Jul-17												
	A5760	IEC/WB - Road Marking/Traffic Sign 3 days	3d	13-Jul-17	15-Jul-17												
	A5840	IEC/WB - Implement TTM	1d	16-Jul-17	16-Jul-17												
	Stage 2 - Tsing Fung Street		28d	17-Jul-17	13-Aug-17												
	A5850	Decking /Footing Removal - 2 weeks	14d	17-Jul-17	30-Jul-17												
	A5880	Light Weight Conc. Ramp Rem. 4 weeks	28d	17-Jul-17	13-Aug-17												
	A5890	Trench Excavation for Towngas - 4 weeks	28d	17-Jul-17	13-Aug-17												
	Reinstatement Existing Slopping & Vertical Sea Wall		55d	17-Jun-17	10-Aug-17												
	Major Reinstatement Works for Seawall Reinstatement		55d	17-Jun-17	10-Aug-17												
	Stage 1 - Removal of Remaining Pipe Pile Wall, Sheet Pile Wall & D-wall		55d	17-Jun-17	10-Aug-17												
	A7030	Backfill upto +2.5mPD at all bay of SR8	1d	17-Jun-17	17-Jun-17												
	A7040	Cut pipe pile wall at A1 - A14	14d	18-Jun-17	01-Jul-17												
	A7050	Under water cut sheet pile wall (36 nos.)	40d	02-Jul-17	10-Aug-17												
Works in Victoria Park (KD4, KD5, KD9)			184d	20-Jan-17 A	06-Sep-17												
Re-Provisioning Works			184d	20-Jan-17 A	06-Sep-17												
Nursery Compound			184d	20-Jan-17 A	06-Sep-17												
Submission			124d	20-Jan-17 A	27-Jun-17												
ABWF Submission			99d	01-Feb-17 A	02-Jun-17												
Material			99d	01-Feb-17 A	12-May-17												
	VP_NC_1060	ABWF Issue P.O. / Manufacturing / Fabrication	14d	01-Feb-17 A	18-Apr-17 A												
	VP_NC_1070	ABWF Materail Delivery	21d	19-Apr-17 A	12-May-17												
Shop Drawing			14d	03-Feb-17 A	02-Jun-17												
	VP_NC_1090	ABWF Shop Drawing - ER Review and Approval	14d	03-Feb-17 A	02-Jun-17												
E&M Submission			124d	20-Jan-17 A	27-Jun-17												
Material			124d	20-Jan-17 A	27-Jun-17												

Activity ID	Activity Name	Original Duration	Start	Finish	2017											
					Apr			May			Jun			Jul		
VP_NC_1140	E&M Issue P.O. / Manufacturing / Fabrication	15d	20-Jan-17 A	22-May-17												
VP_NC_1150	E&M Materail Delivery	30d	23-May-17	27-Jun-17												
Shop Drawing		30d	20-Apr-17	26-May-17												
VP_NC_1170	E&M Shop Drawing - ER Review and Approval	30d	20-Apr-17	26-May-17												
Nursery compound		125d	09-Mar-17 A	06-Sep-17												
A4410	Concreting of two concrete plinths, 150 thick curbs and 1450H parapet wall above roof slab	7d	09-Mar-17 A	30-Mar-17 A												
A4420	ABWF, Plumbing Works, waterproofing and E&M works	60d	05-Apr-17 A	06-Sep-17												
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks		1087d	23-Feb-15 A	09-Feb-18												
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)		885d	23-Feb-15 A	09-Feb-18												
EW_1000	Establishment Works - for Landscape Softworks and transplanted trees in Portion XIV & XV	901d	23-Feb-15 A	09-Feb-18												
KD12 - Section 7B: Portion VI & VII (Reprov. Bowling Green Area)		177d	03-Dec-15 A	20-Apr-17												
EW_1010	Establishment Works - for Landscape Softworks and transplanted trees in Portion VI & VII	177d	03-Dec-15 A	20-Apr-17												
KD10 - Preservation and Protection of Trees		1088d	21-Mar-13 A	20-Apr-17												
PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	20-Apr-17												
KD15 & KD8 - Mooring Components Upkeep (CBTS and ATS)		980d	15-May-14 A	20-Apr-17												
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	20-Apr-17												
Works for Public Works Regional Laboratory (North Lantau) - KD1,KD16,KD17)		1301d	19-Jul-13 A	21-Nov-17												
KD17 - Maintenance and Upkeep of New PWRL (Portion XVII)		1301d	19-Jul-13 A	21-Nov-17												
PWRL_1050	Maintenance/ Upkeep of New PWRL	1301d	19-Jul-13 A	21-Nov-17												

Data Date: 20-Apr-17	CWB(CC) - Commissioning Contract TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.	
----------------------	---	--

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017											
						Apr			May			Jun			Jul		
Update 2017-04-20 CWB(CC) - Commissioning Contract (DWP R2d)																	
PRELIMINARIES AND GENERAL REQUIREMENTS																	
Salient Key Dates and Milestones																	
Contract Key Dates																	
KD003	KD3 - Achievement of Stage 3 (1178 days)	0		20-May-17*	0												
KD002	KD2 - Achievement of Stage 2 (1232 days)	0		13-Jul-17*	0												
Possession Dates and Vacation Dates																	
PO-IVa2_b	Possession of Portion IVa (Day 930) - SR1	203	30-Mar-17 A	18-Oct-17	-369												
PO-Vb2_b	Possession of Portion V (Day 607) - SCP3	182	20-Apr-17	18-Oct-17	-343												
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	30-Jun-17	18-Oct-17	-74												
Submissions and Approvals																	
Initial General Submission																	
1211	Submission of 1st Project video film	0		17-Apr-17 A													
9932	Submission of 1st Project video film Video1 / Video2 (Release II)	0		20-Apr-17*	-809												
DETAILED DESIGN OF WORKS																	
Permanent Works Design and Engineering																	
Metal Roof on MVB																	
2188	MVB Roof - Engineer review & approval	24	06-Mar-17 A	05-May-17	-259												
2190	MVB Roof - Prepare the Detailed Design submission	12	06-May-17	19-May-17	-259												
2192	MVB Roof - Finalise detailed design submission and ICE Checks & issue Check Certificate	12	20-May-17	03-Jun-17	-259												
12436	MVB Roof - Submit detailed design to the Engineer with ICE Certificate	0		03-Jun-17	-259												
2194	MVB Roof - Engineer review & Approval; Consent to Proceed Construction	24	05-Jun-17	03-Jul-17	-257												
Green Roof on EVB																	
2166	EVB Roof - Engineer review & Approval; Consent to Proceed Construction	24	18-Apr-16 A	05-May-17	-324												





Leighton Contractors (Asia) Limited
Programme Update 38 (April 2017)
THREE MONTH ROLLING

Project ID: H2613-U038
Baseline: DWP2d
Layout: Update Three Month Rolling
U038
Page 1 of 40

Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

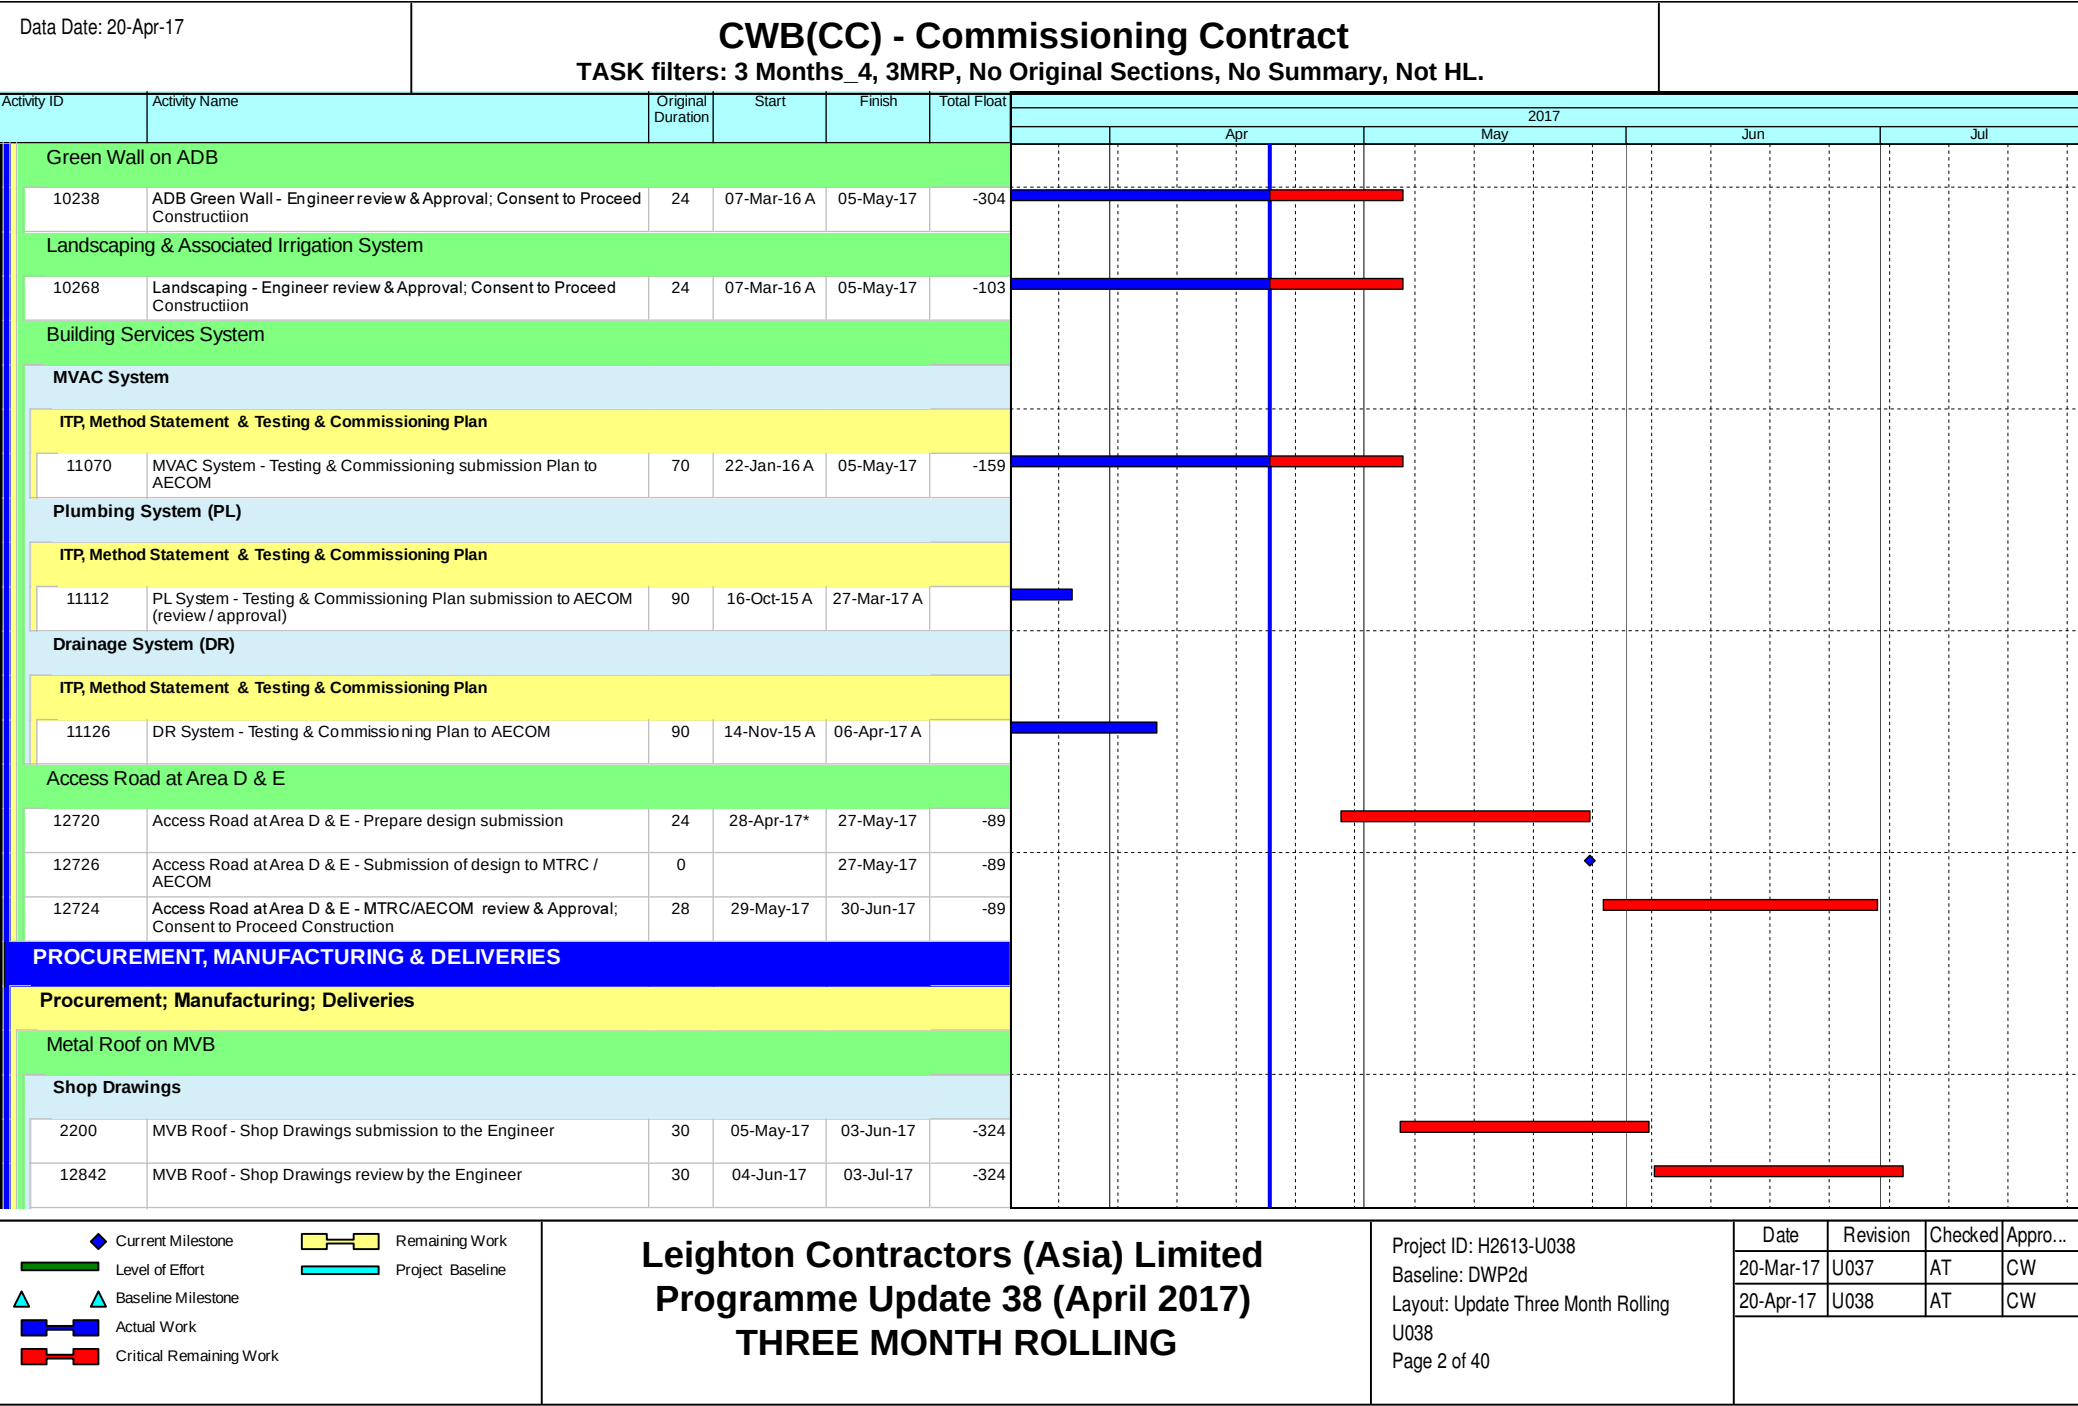

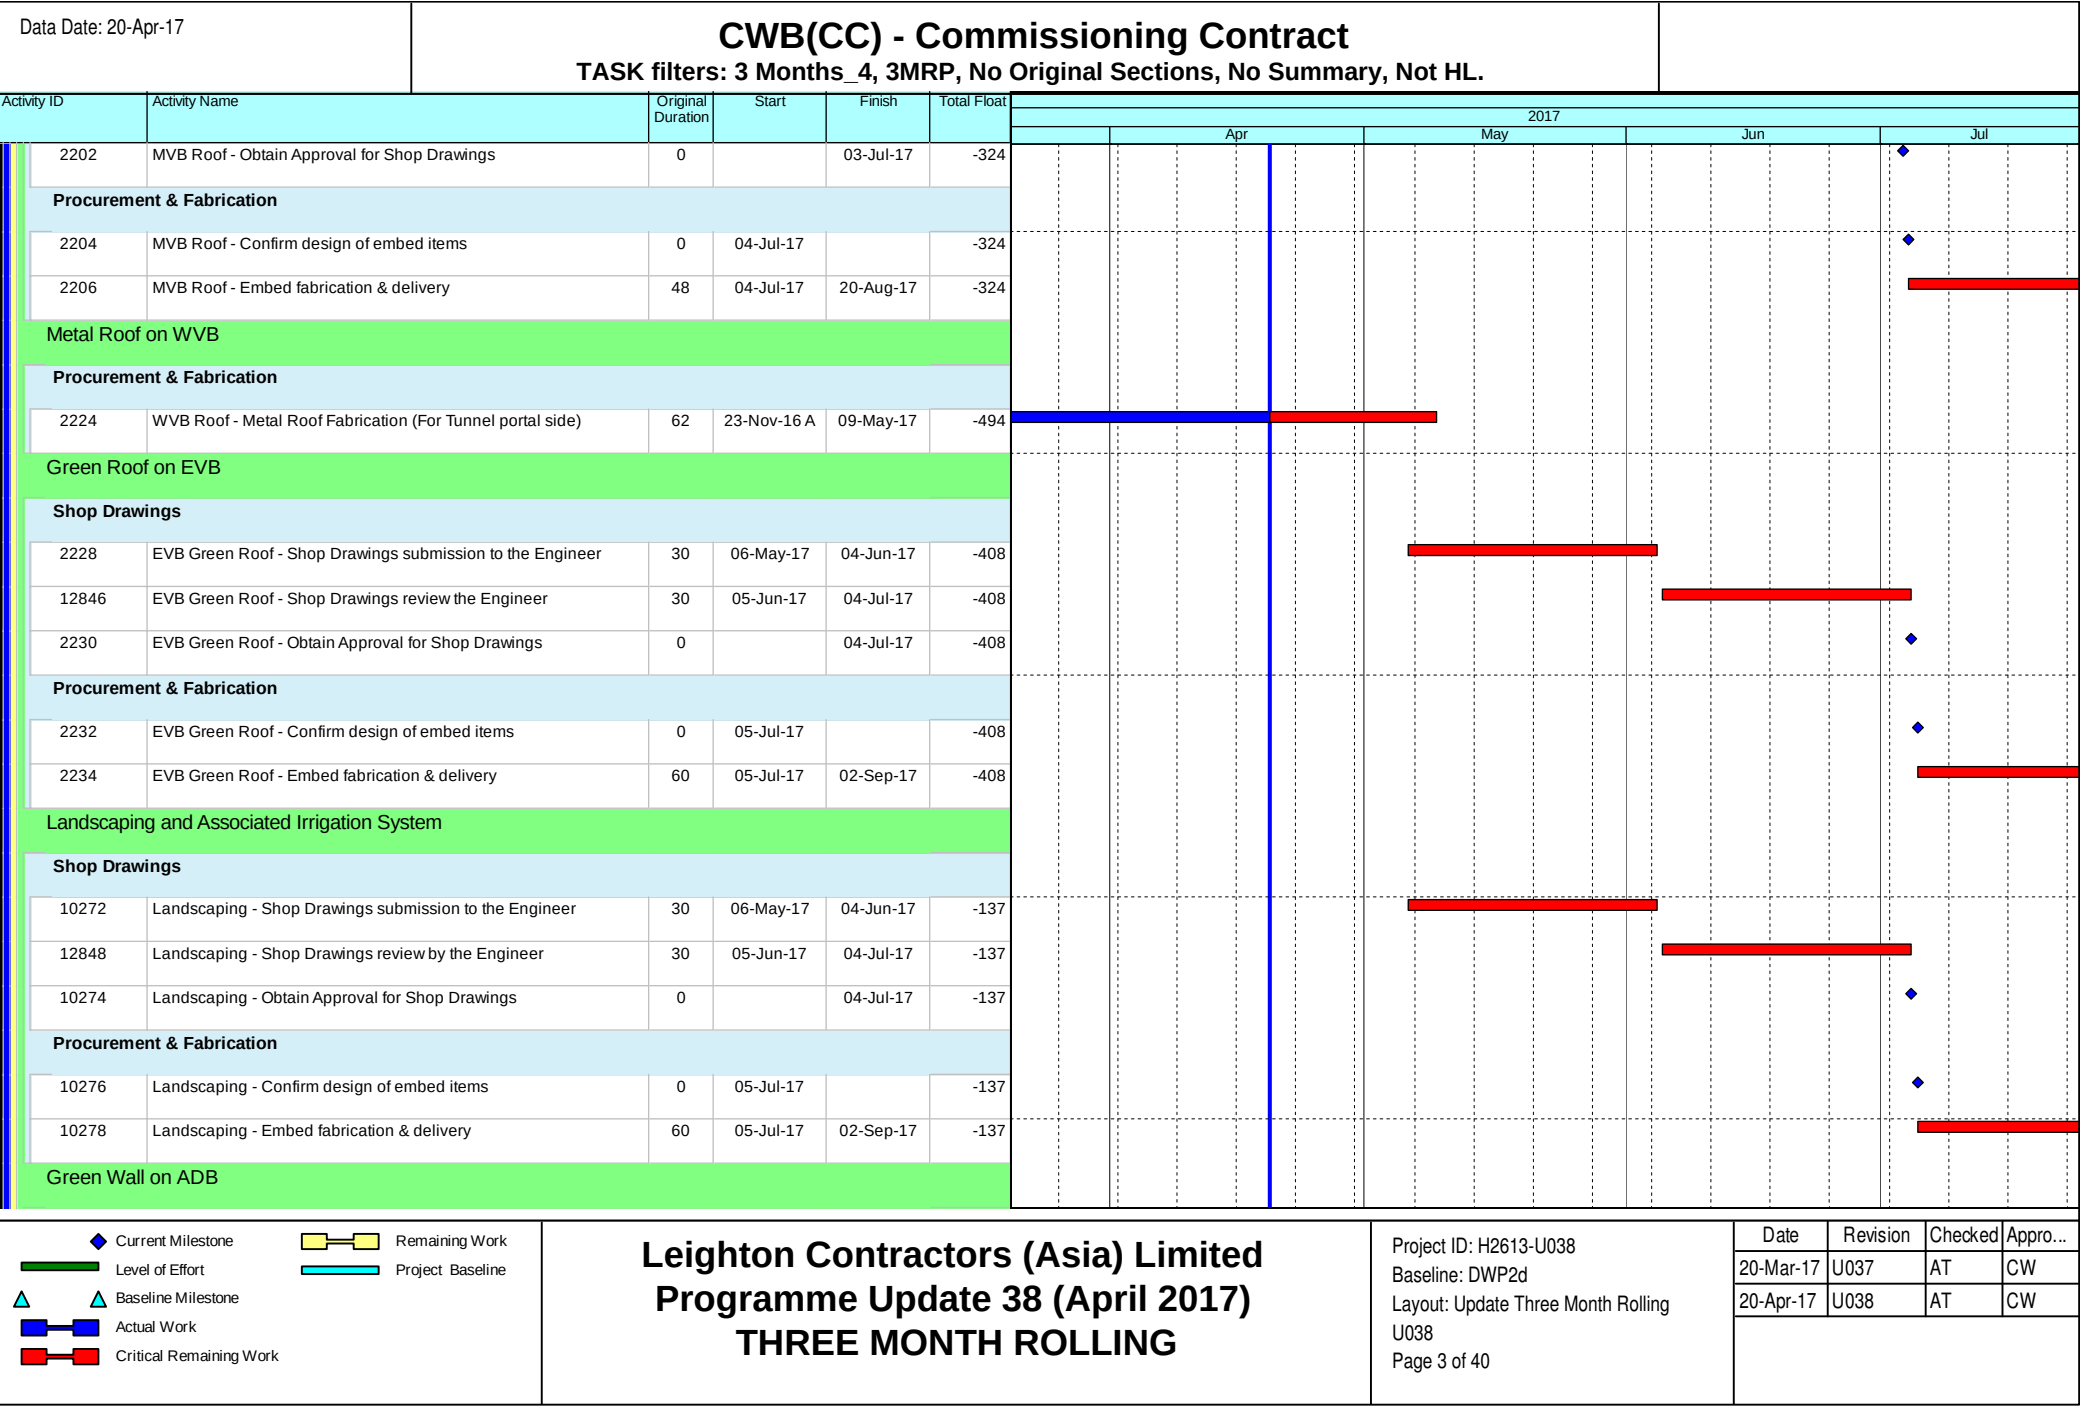

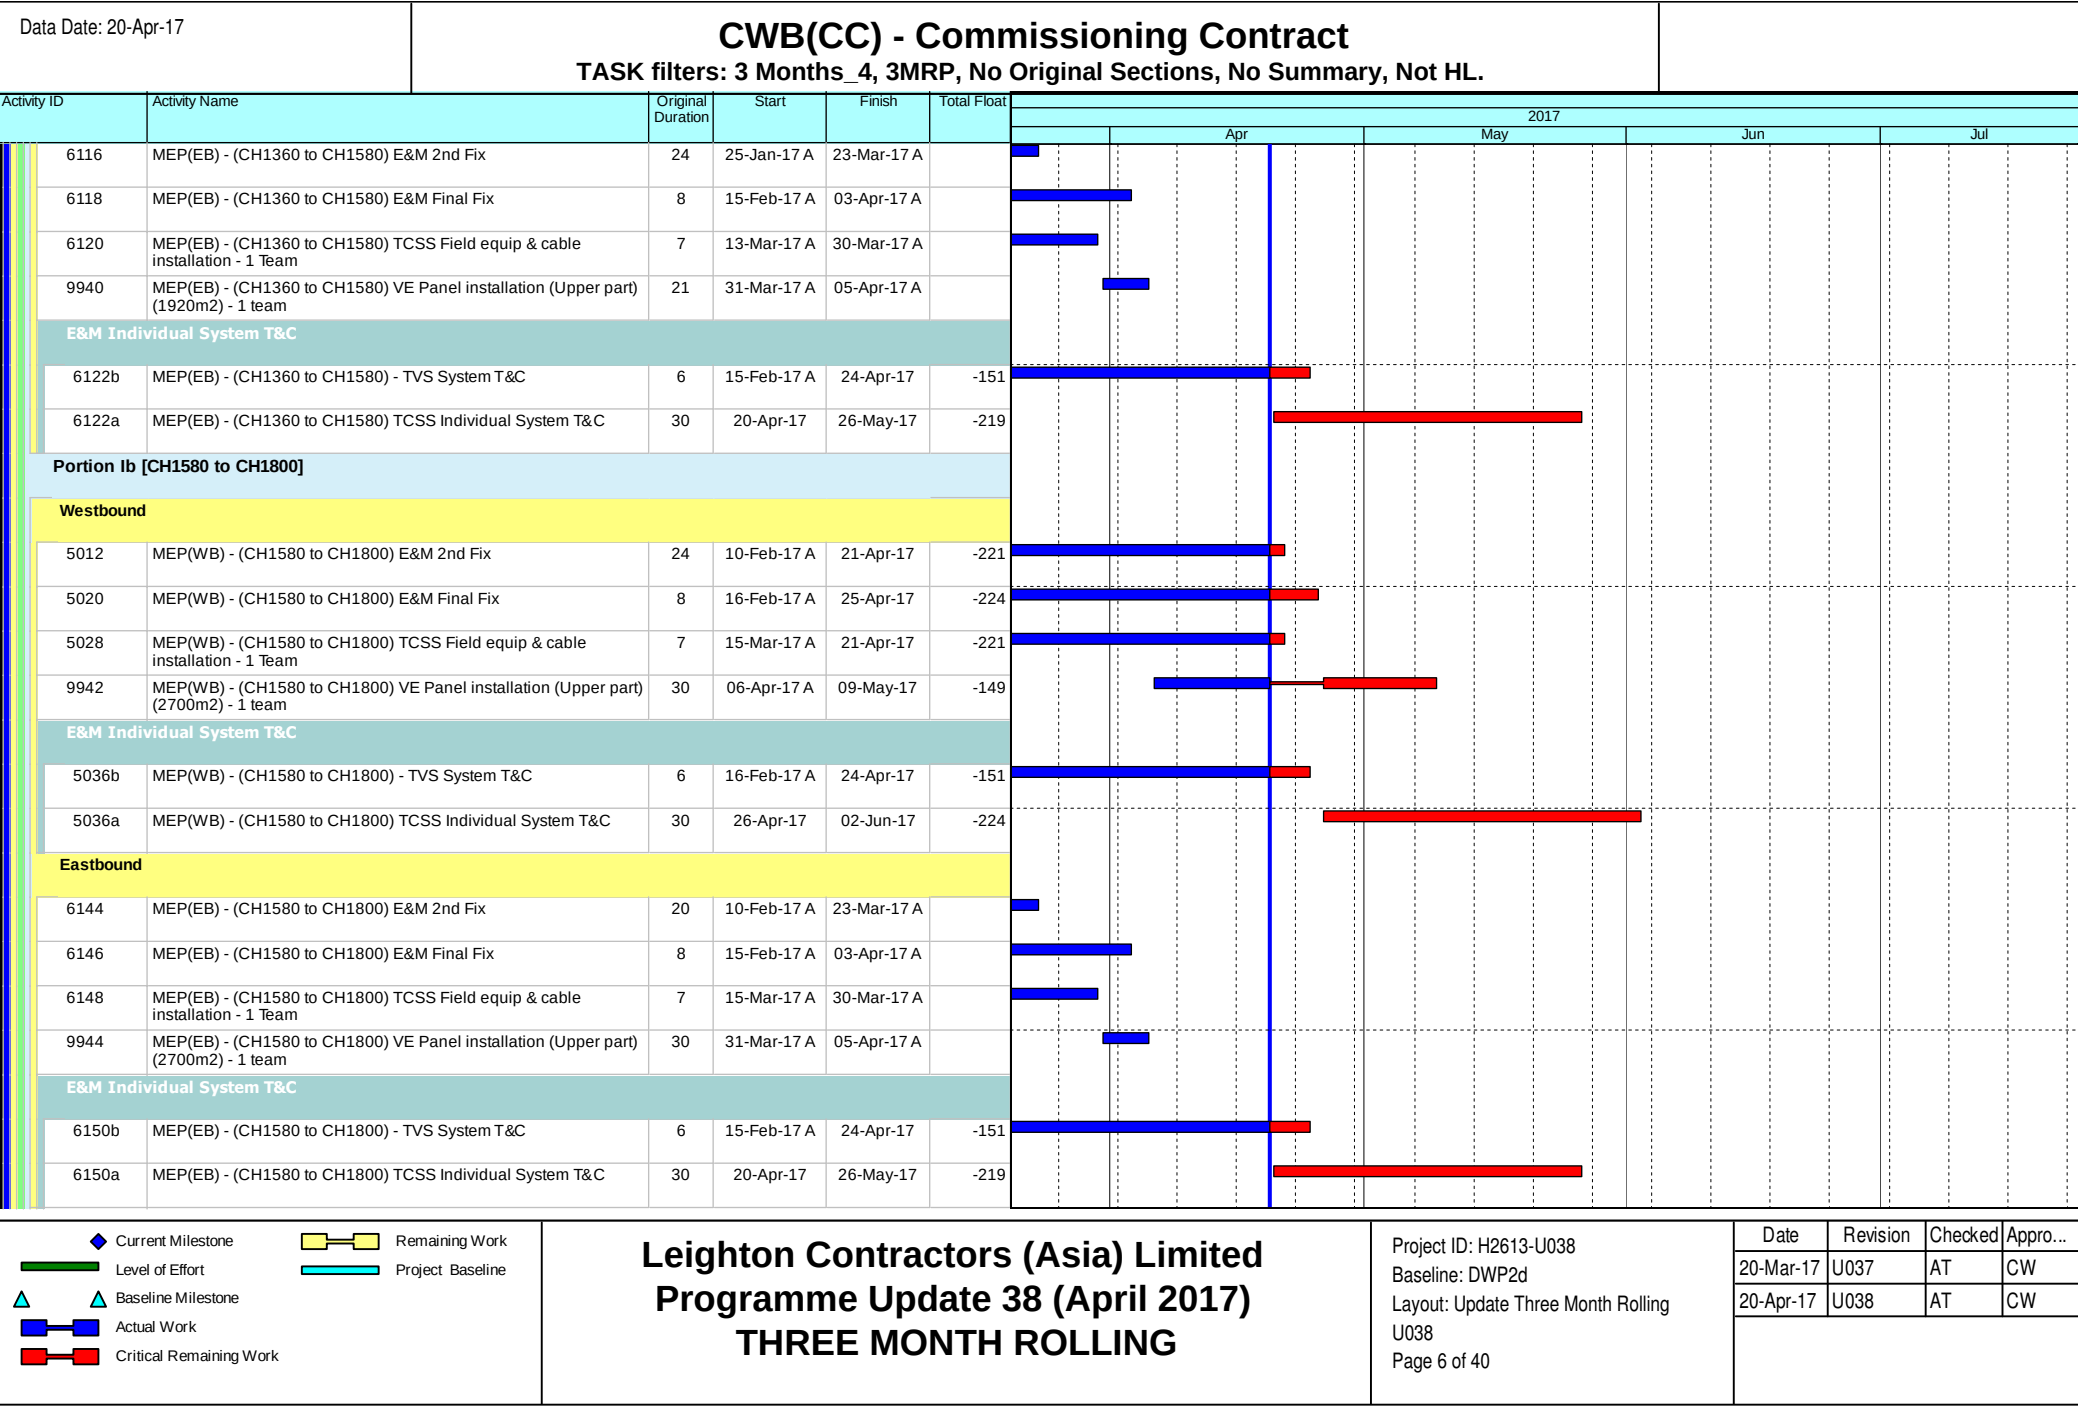


Data Date: 20-Apr-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017											
						Apr			May			Jun			Jul		
10442a2	WVB - Installation of steel roof structure (Eastern side extra steel trust issue)	42	15-Feb-17 A	31-Mar-17 A													
10442a4	WVB - Installation of extra roof fins support (M.J.East) (VO) (Tentative, duration subject to change)	42	20-Apr-17	10-Jun-17	-236												
10452a	WVB - Roof cladding / (East Boundary)	30	12-Jun-17	17-Jul-17	-236												
Metal Roof Western Side (M.J. West)																	
10442	WVB - Installation of temporary roof support at tunnel portal	18	22-Apr-17	15-May-17	-391												
10440	WVB - Erection of 1st steel structure at tunnel portal	6	16-May-17	22-May-17	-391												
10444	WVB - Installation of steel trust at tunnel portal (connecting to the 1st steel structure)	18	23-May-17	13-Jun-17	-391												
10446	WVB - Dismantle temporary roof support at tunnel portal	12	14-Jun-17	27-Jun-17	-391												
10450	WVB - Installation of steel roof structure (steel trusts) (Western side)	30	28-Jun-17	02-Aug-17	-391												
MEP & ABWF Works																	
3088	MEP(WVB) - TCSS Enabling Works	30	11-Jul-17	14-Aug-17	-269												
Basement																	
TV Plenum (B1-02)																	
12280	MEP(WVB) - Installation of electrical services	24	24-Jan-17 A	29-Mar-17 A													
10658	MEP(WVB) - ESP & De-NO2 filter	12	07-Feb-17 A	08-Apr-17 A													
10660	MEP(WVB) - E&M final fixing	24	02-Mar-17 A	26-Apr-17	-153												
Sump Pump Room (B1-03)																	
10668	MEP(WVB) - E&M final fixing	24	13-Feb-17 A	21-Apr-17	-149												
G/F																	
General Area & Corridor																	
10710	MEP(WVB) - E&M 2nd fixing	30	08-Aug-16 A	22-Apr-17	-150												
1/F																	
TVF Room (L1-03)																	
12338	MEP(WVB) - E&M 2nd fixing	24	03-Nov-16 A	21-Apr-17	-149												





Leighton Contractors (Asia) Limited Programme Update 38 (April 2017) THREE MONTH ROLLING


Project ID: H2613-U038
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U038
 Page 8 of 40


Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

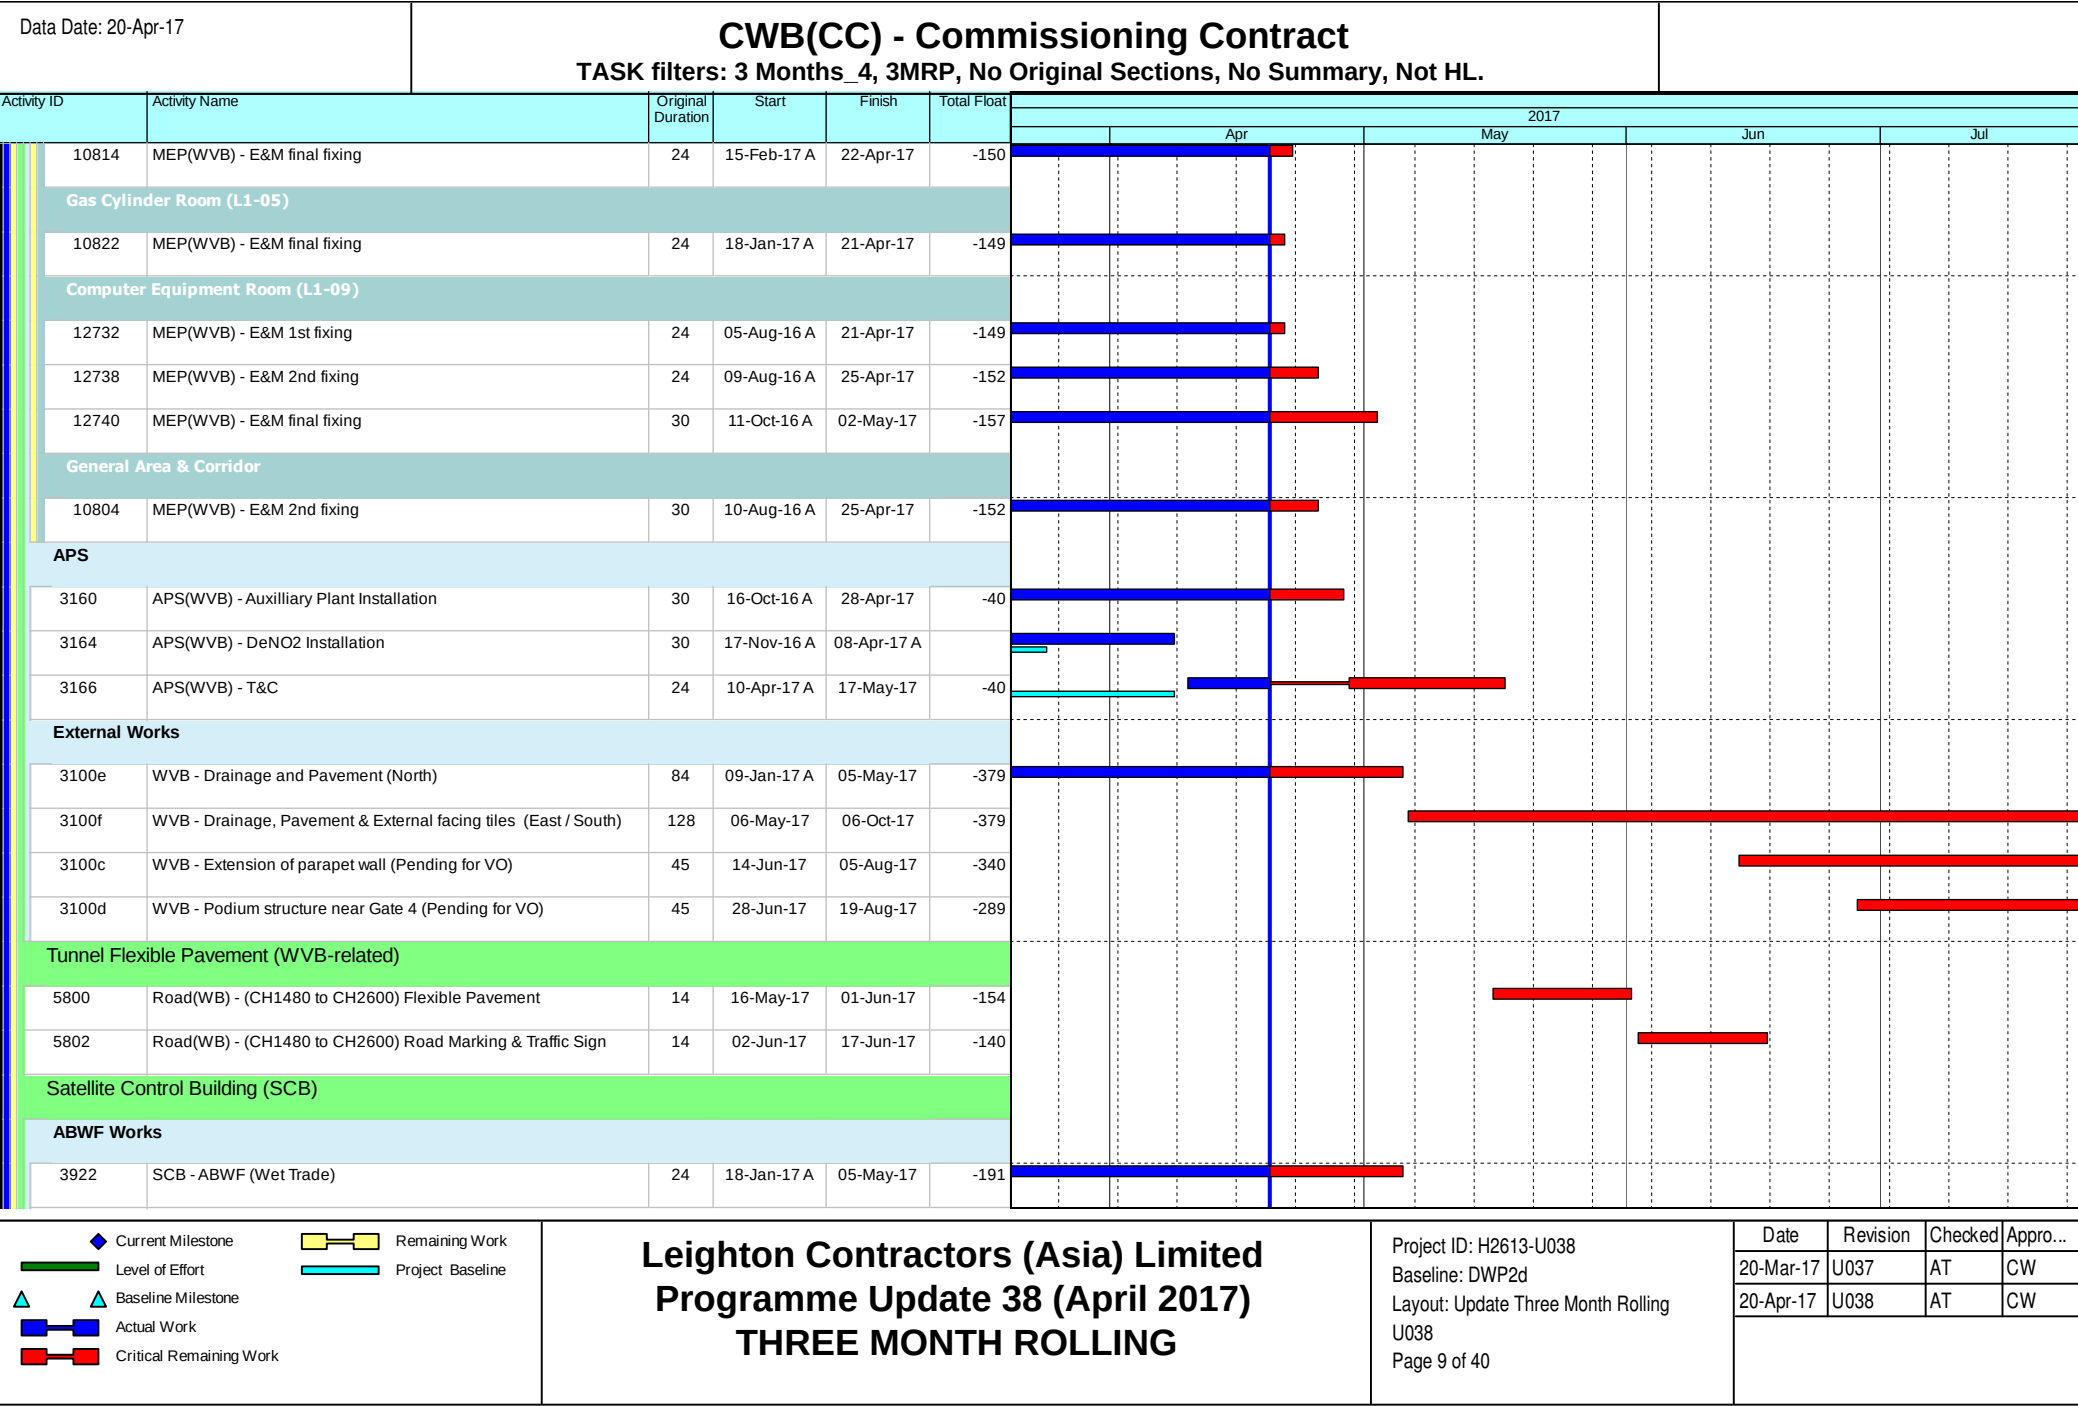


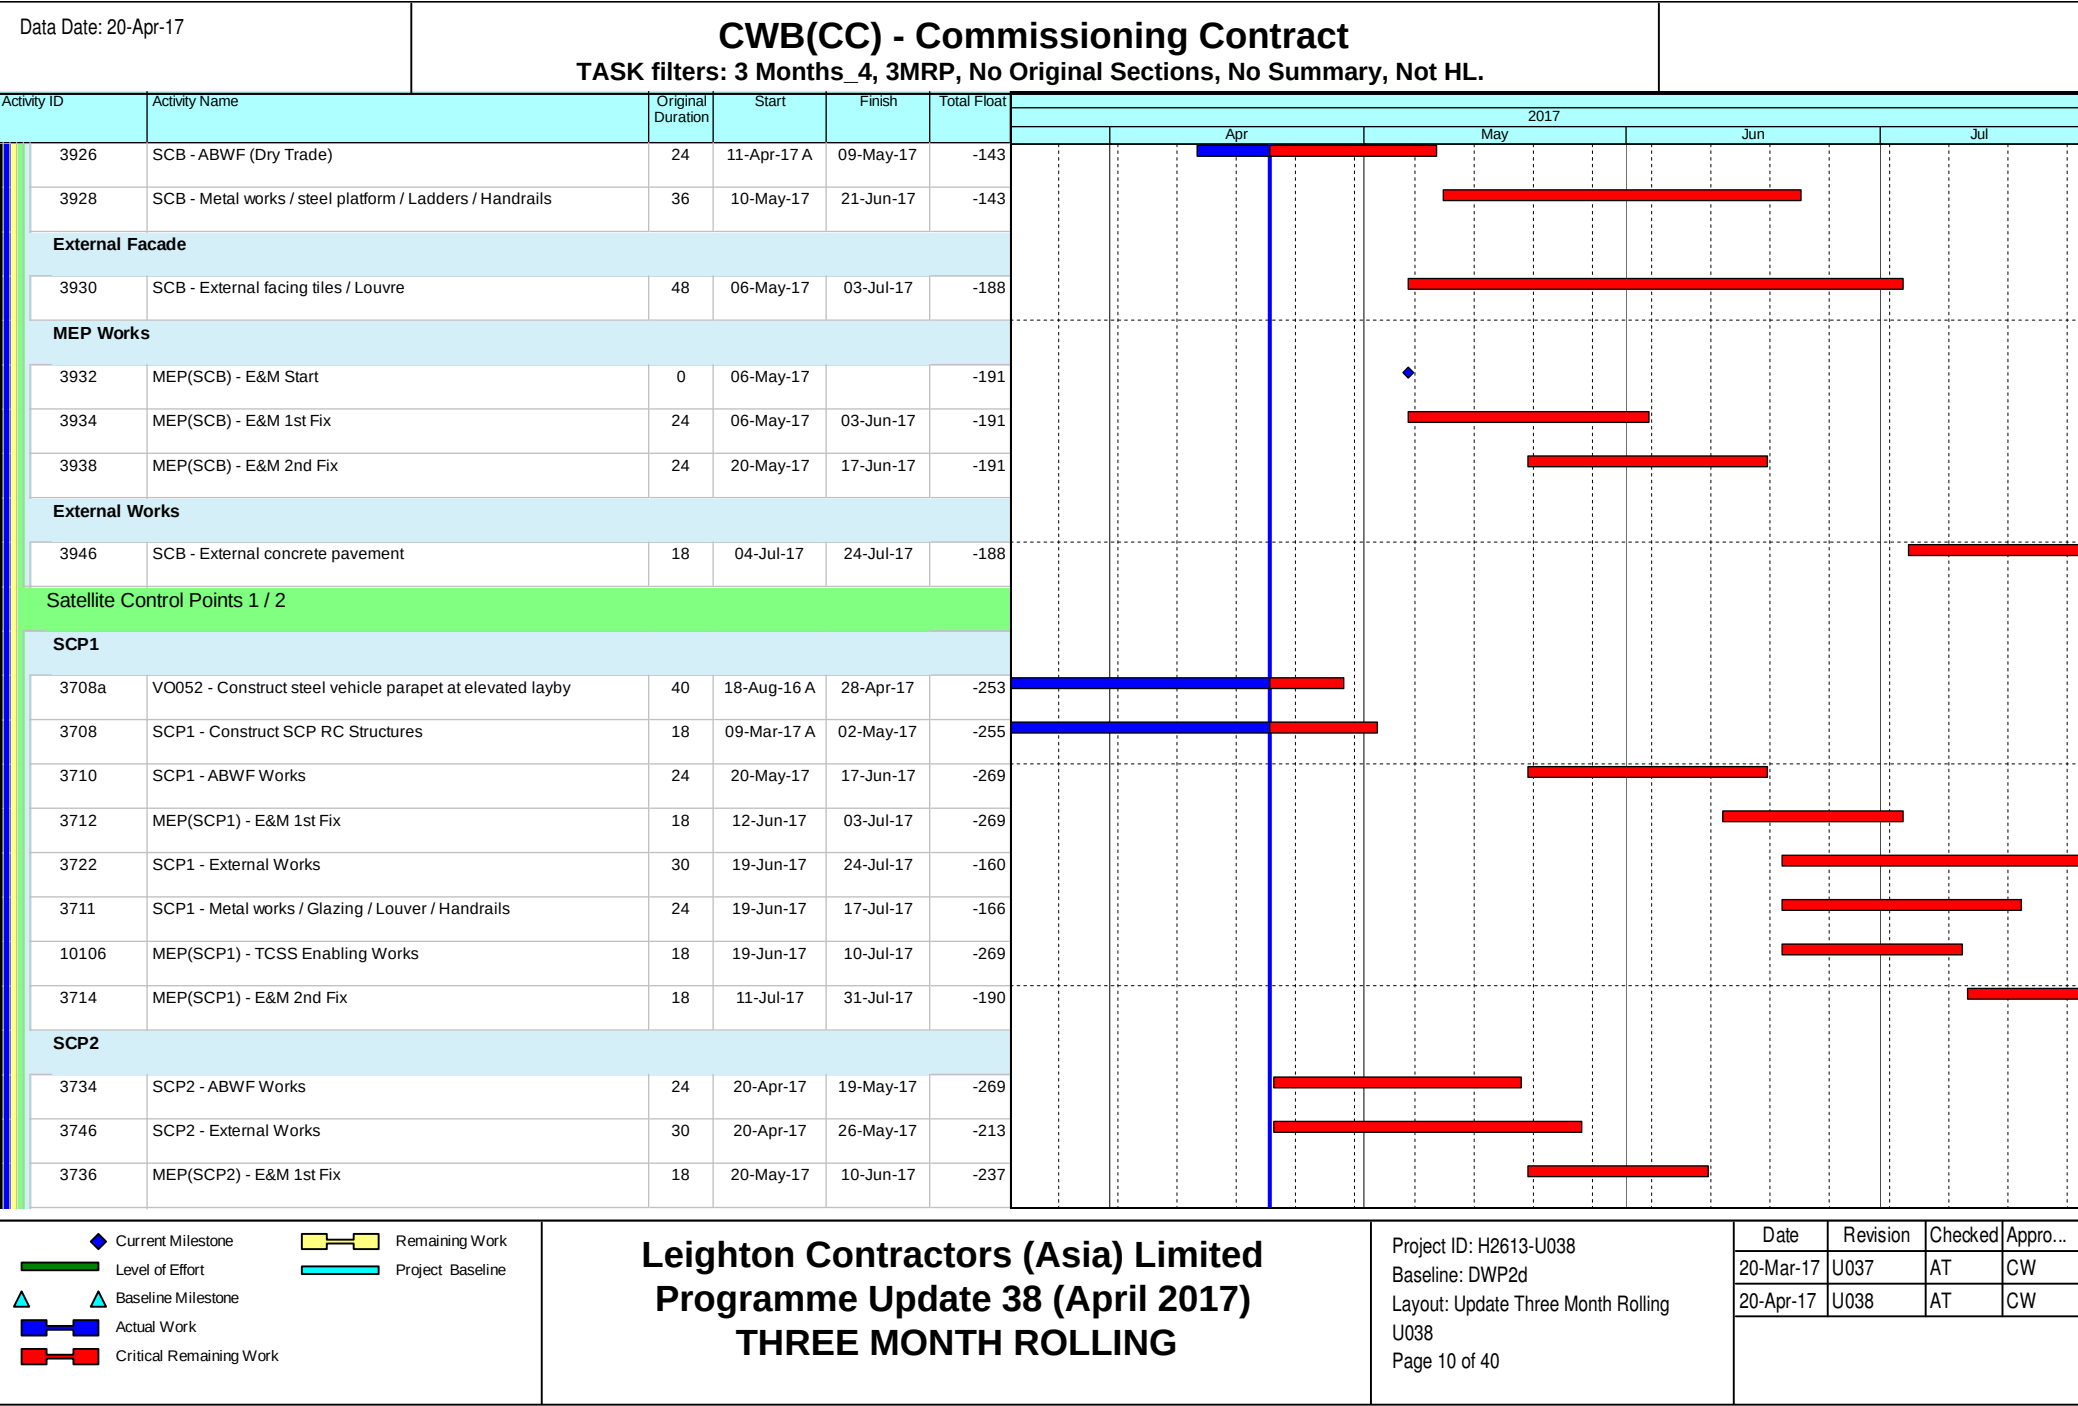

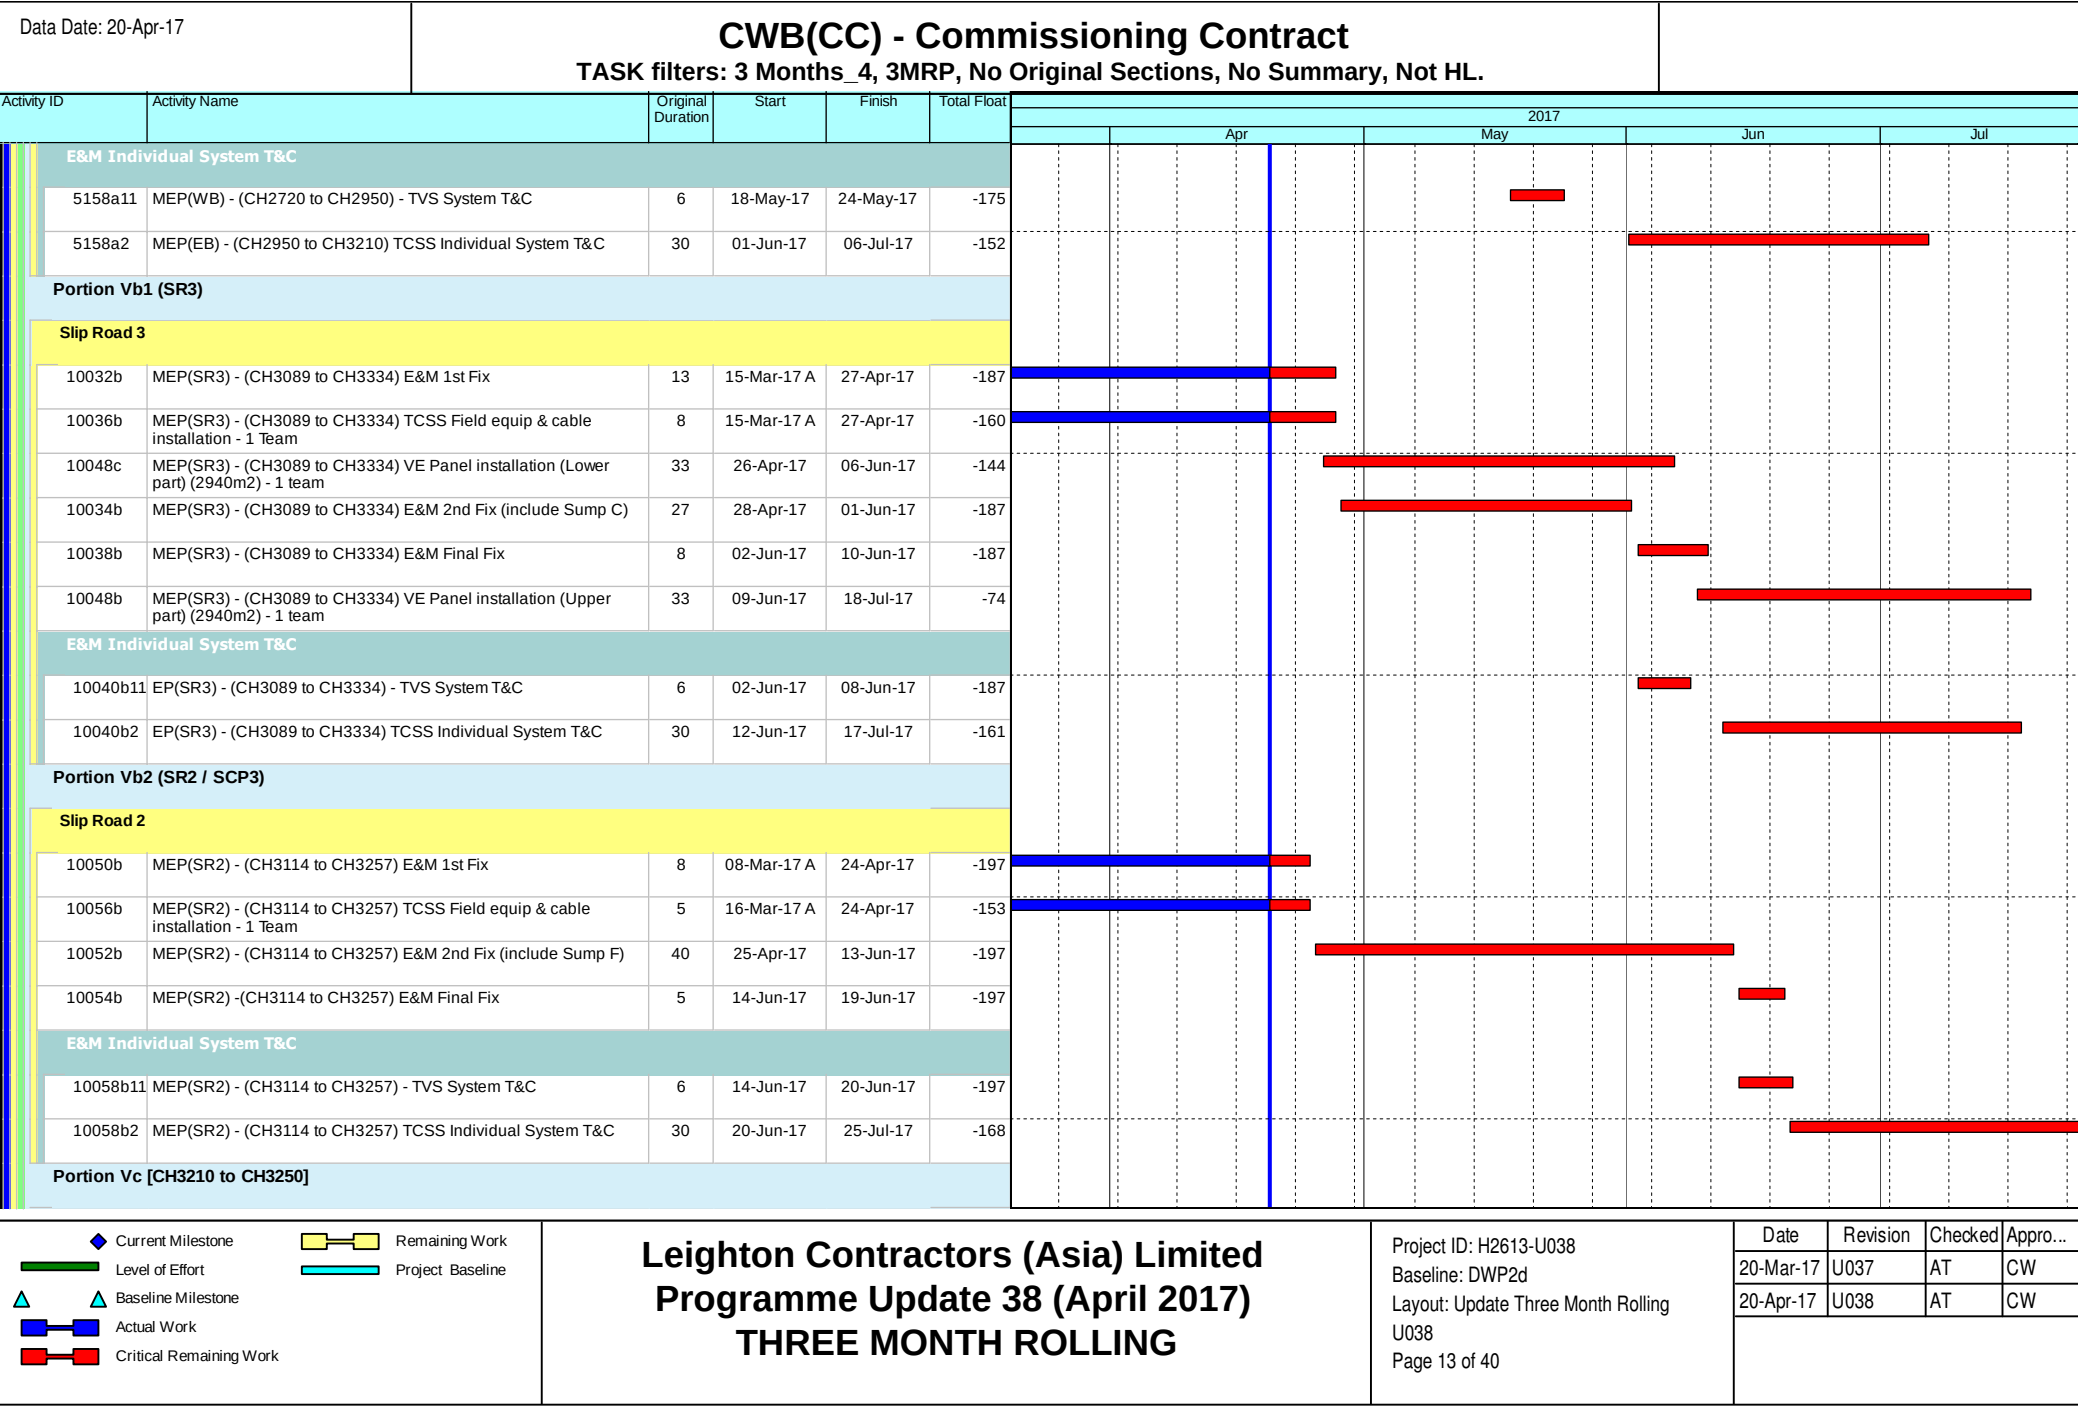

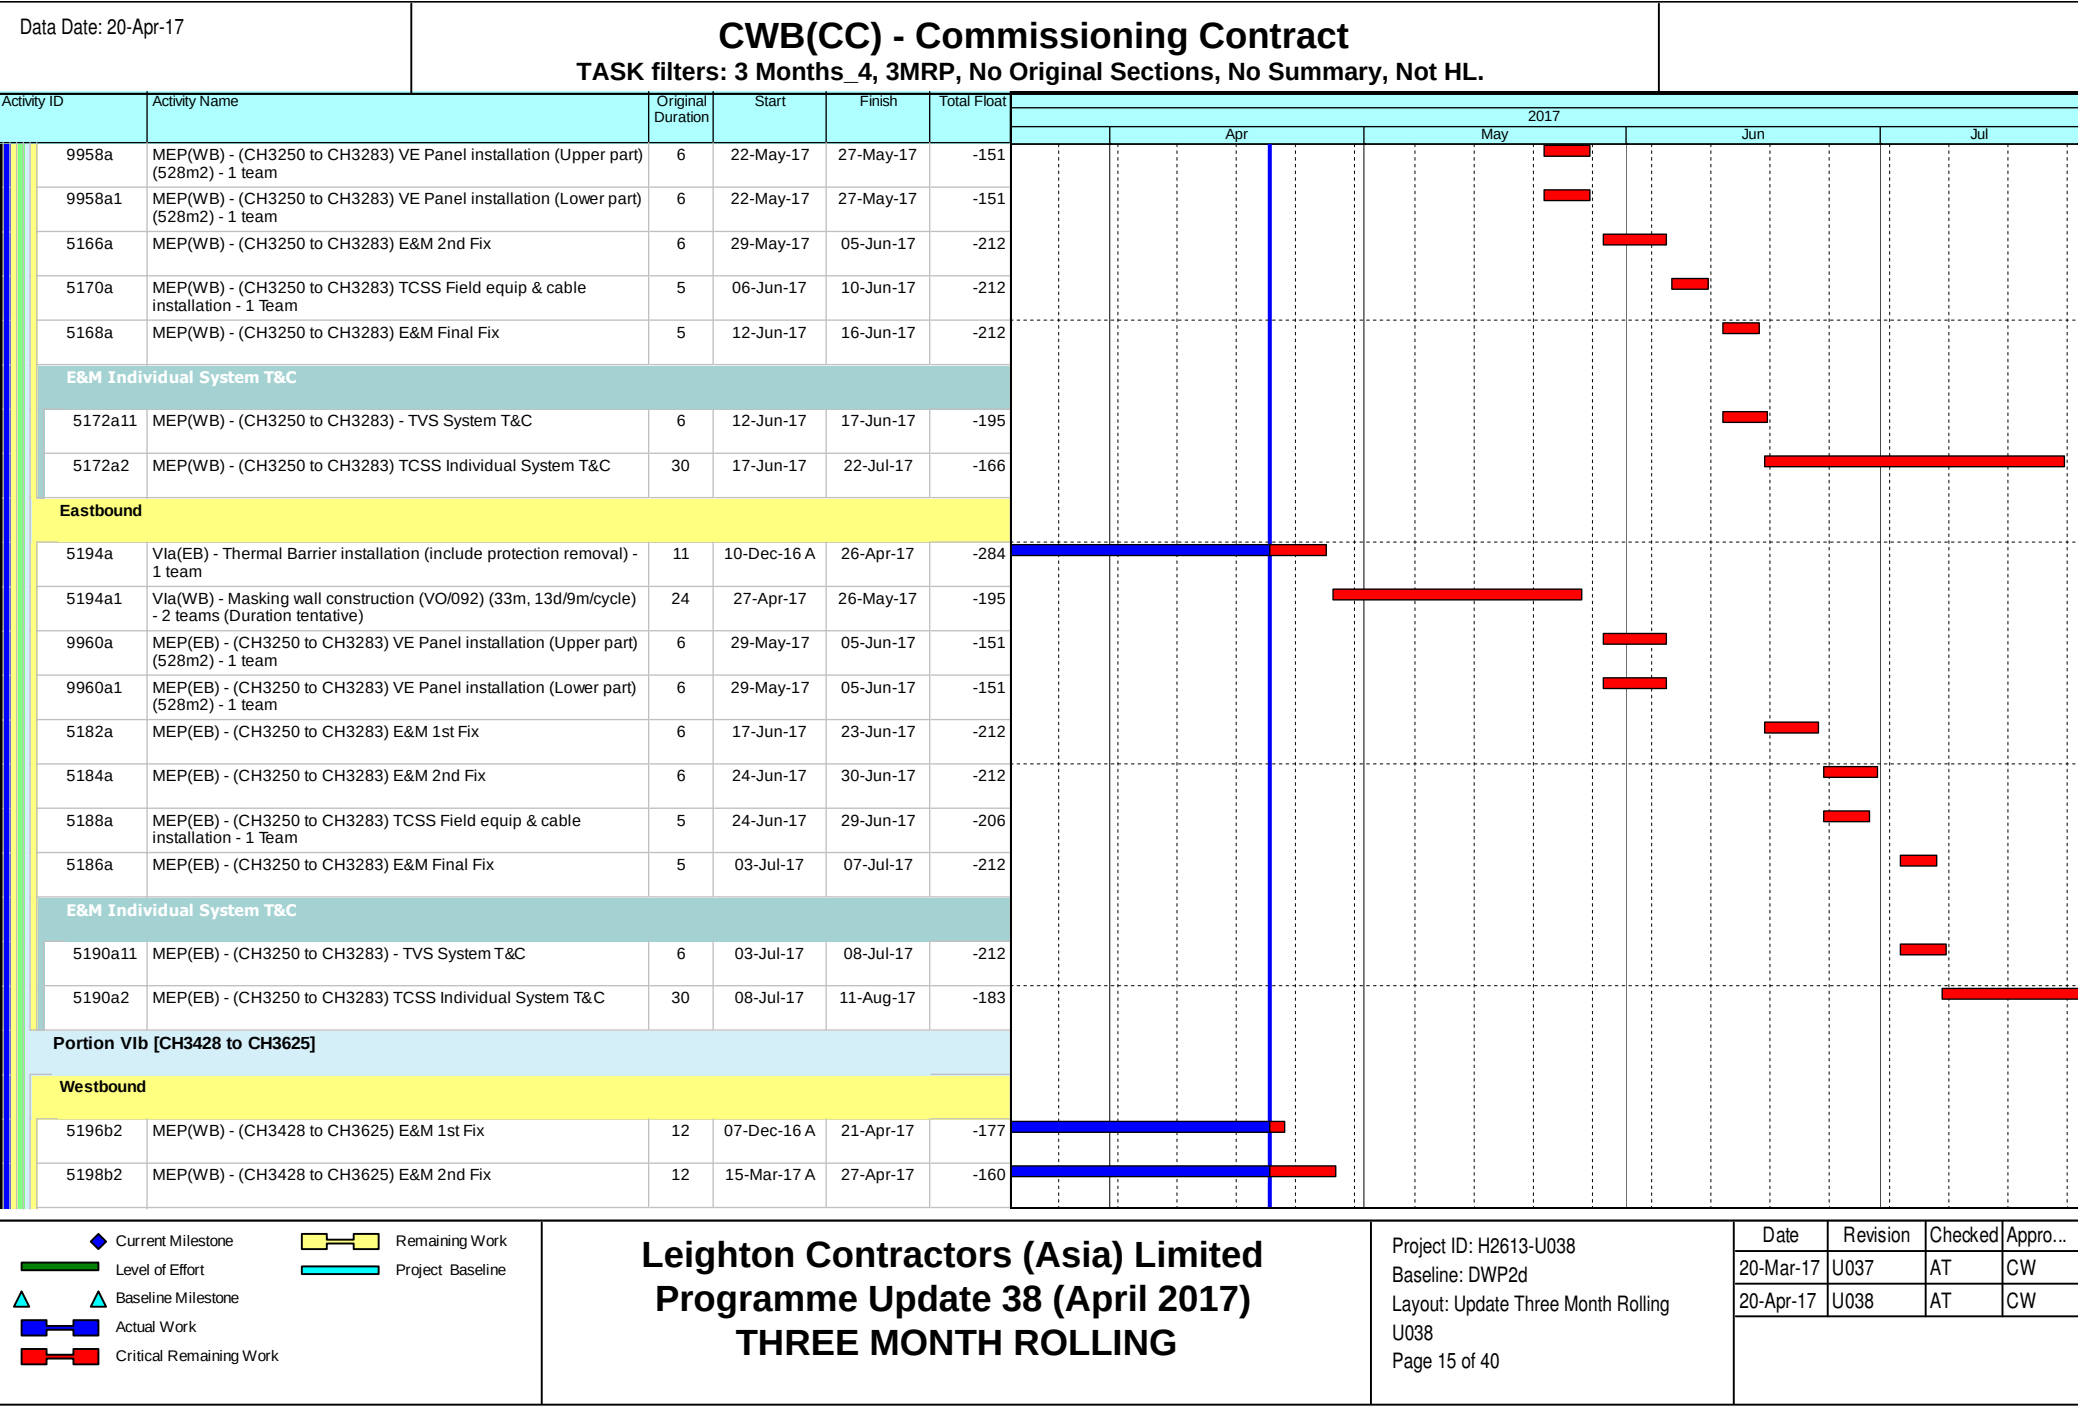

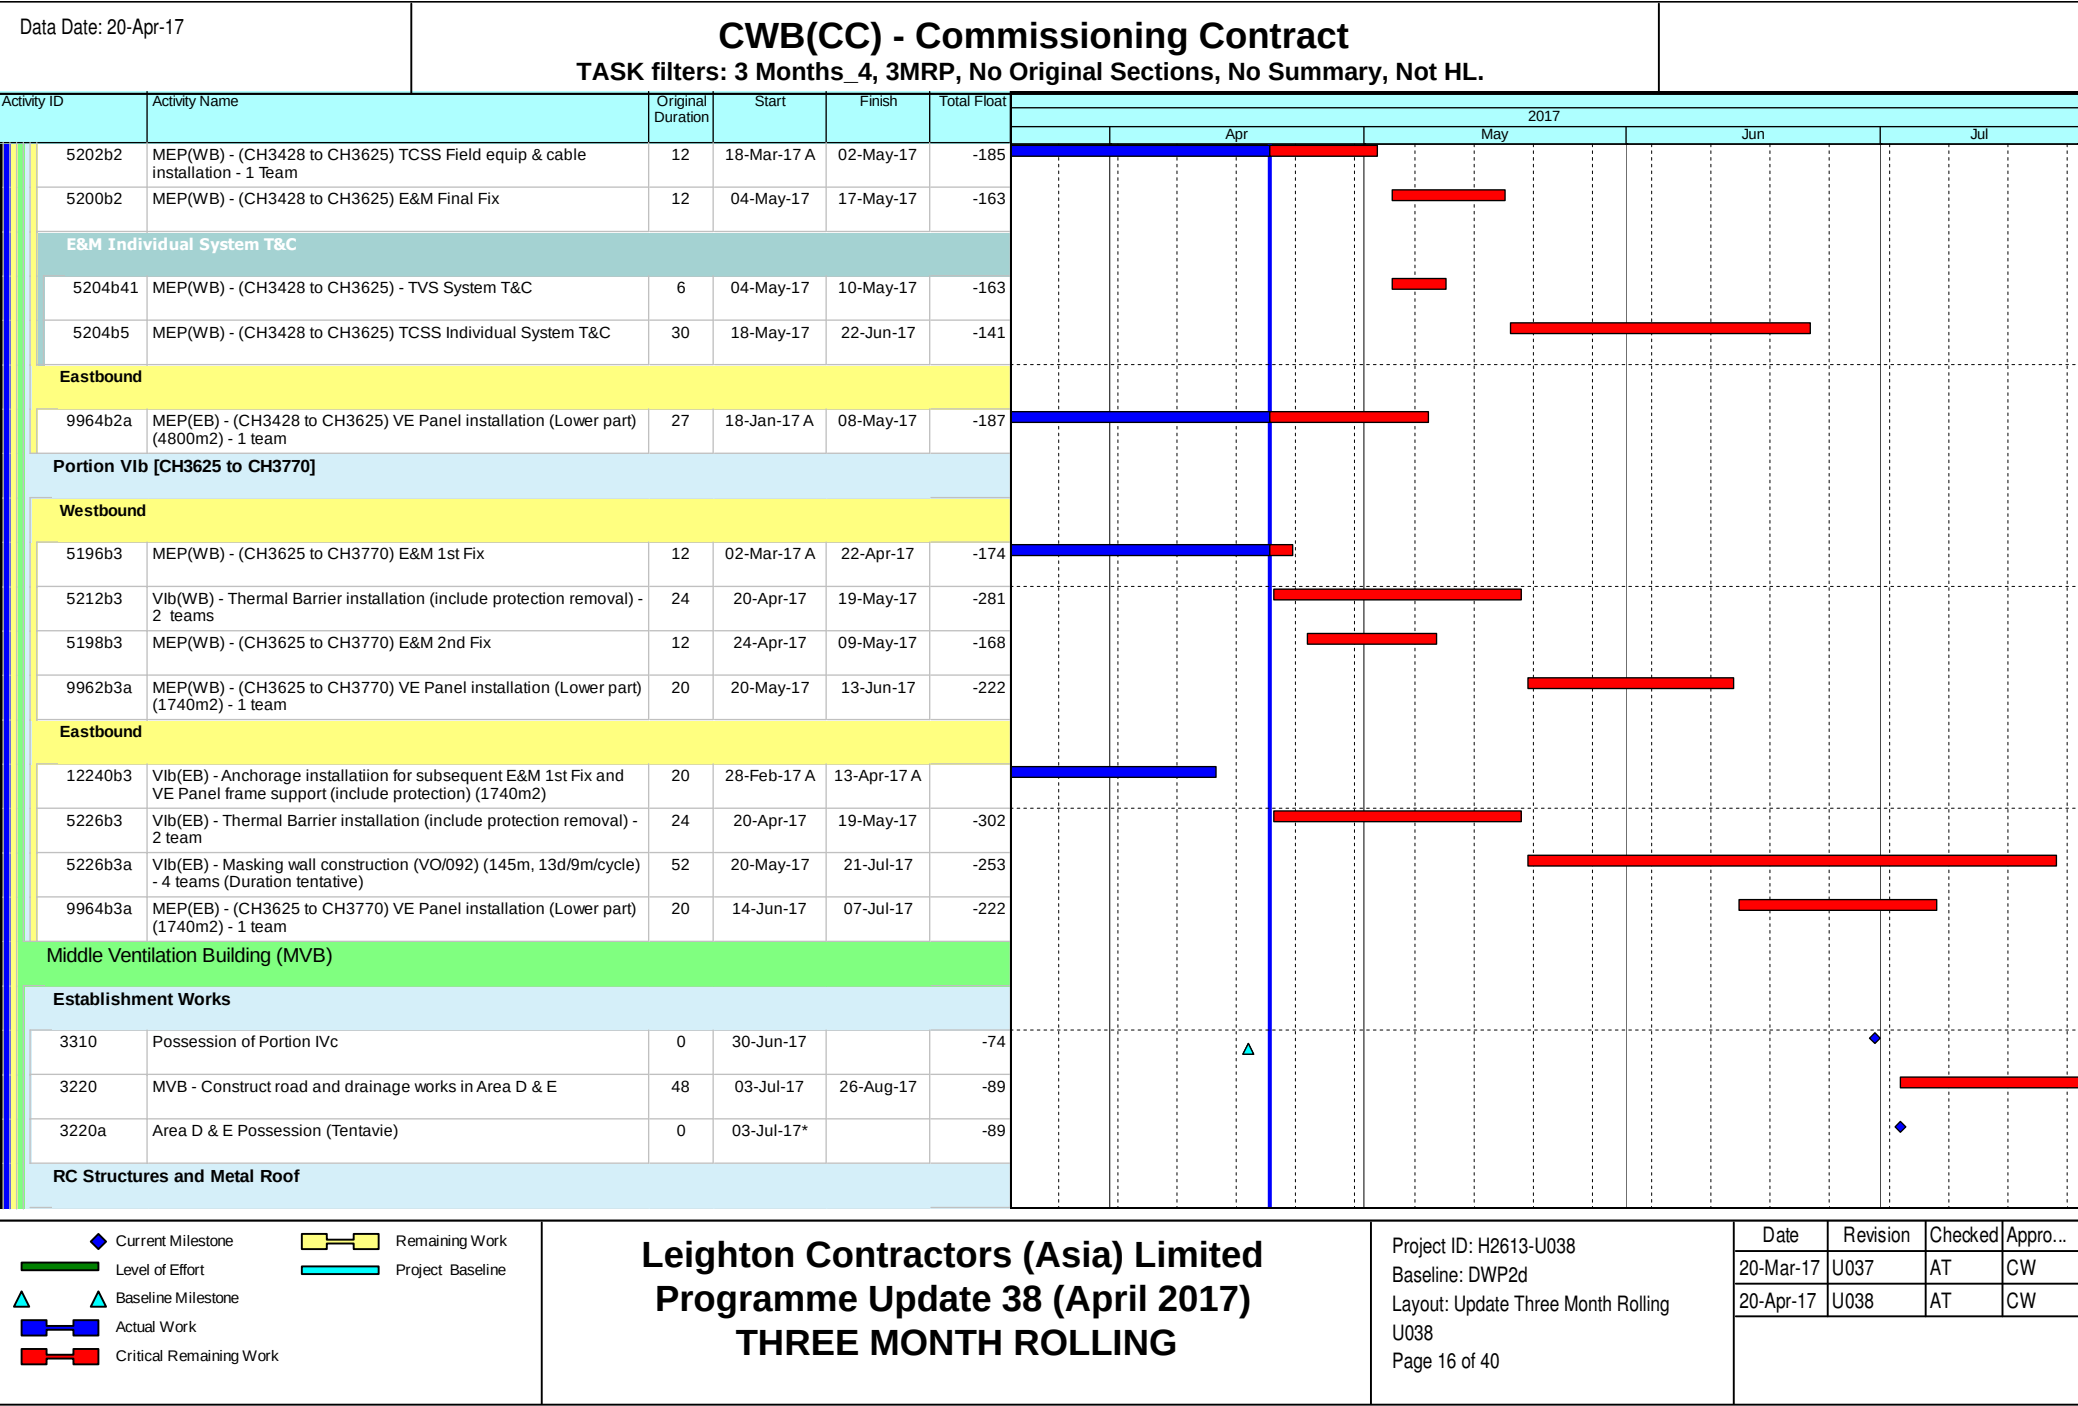

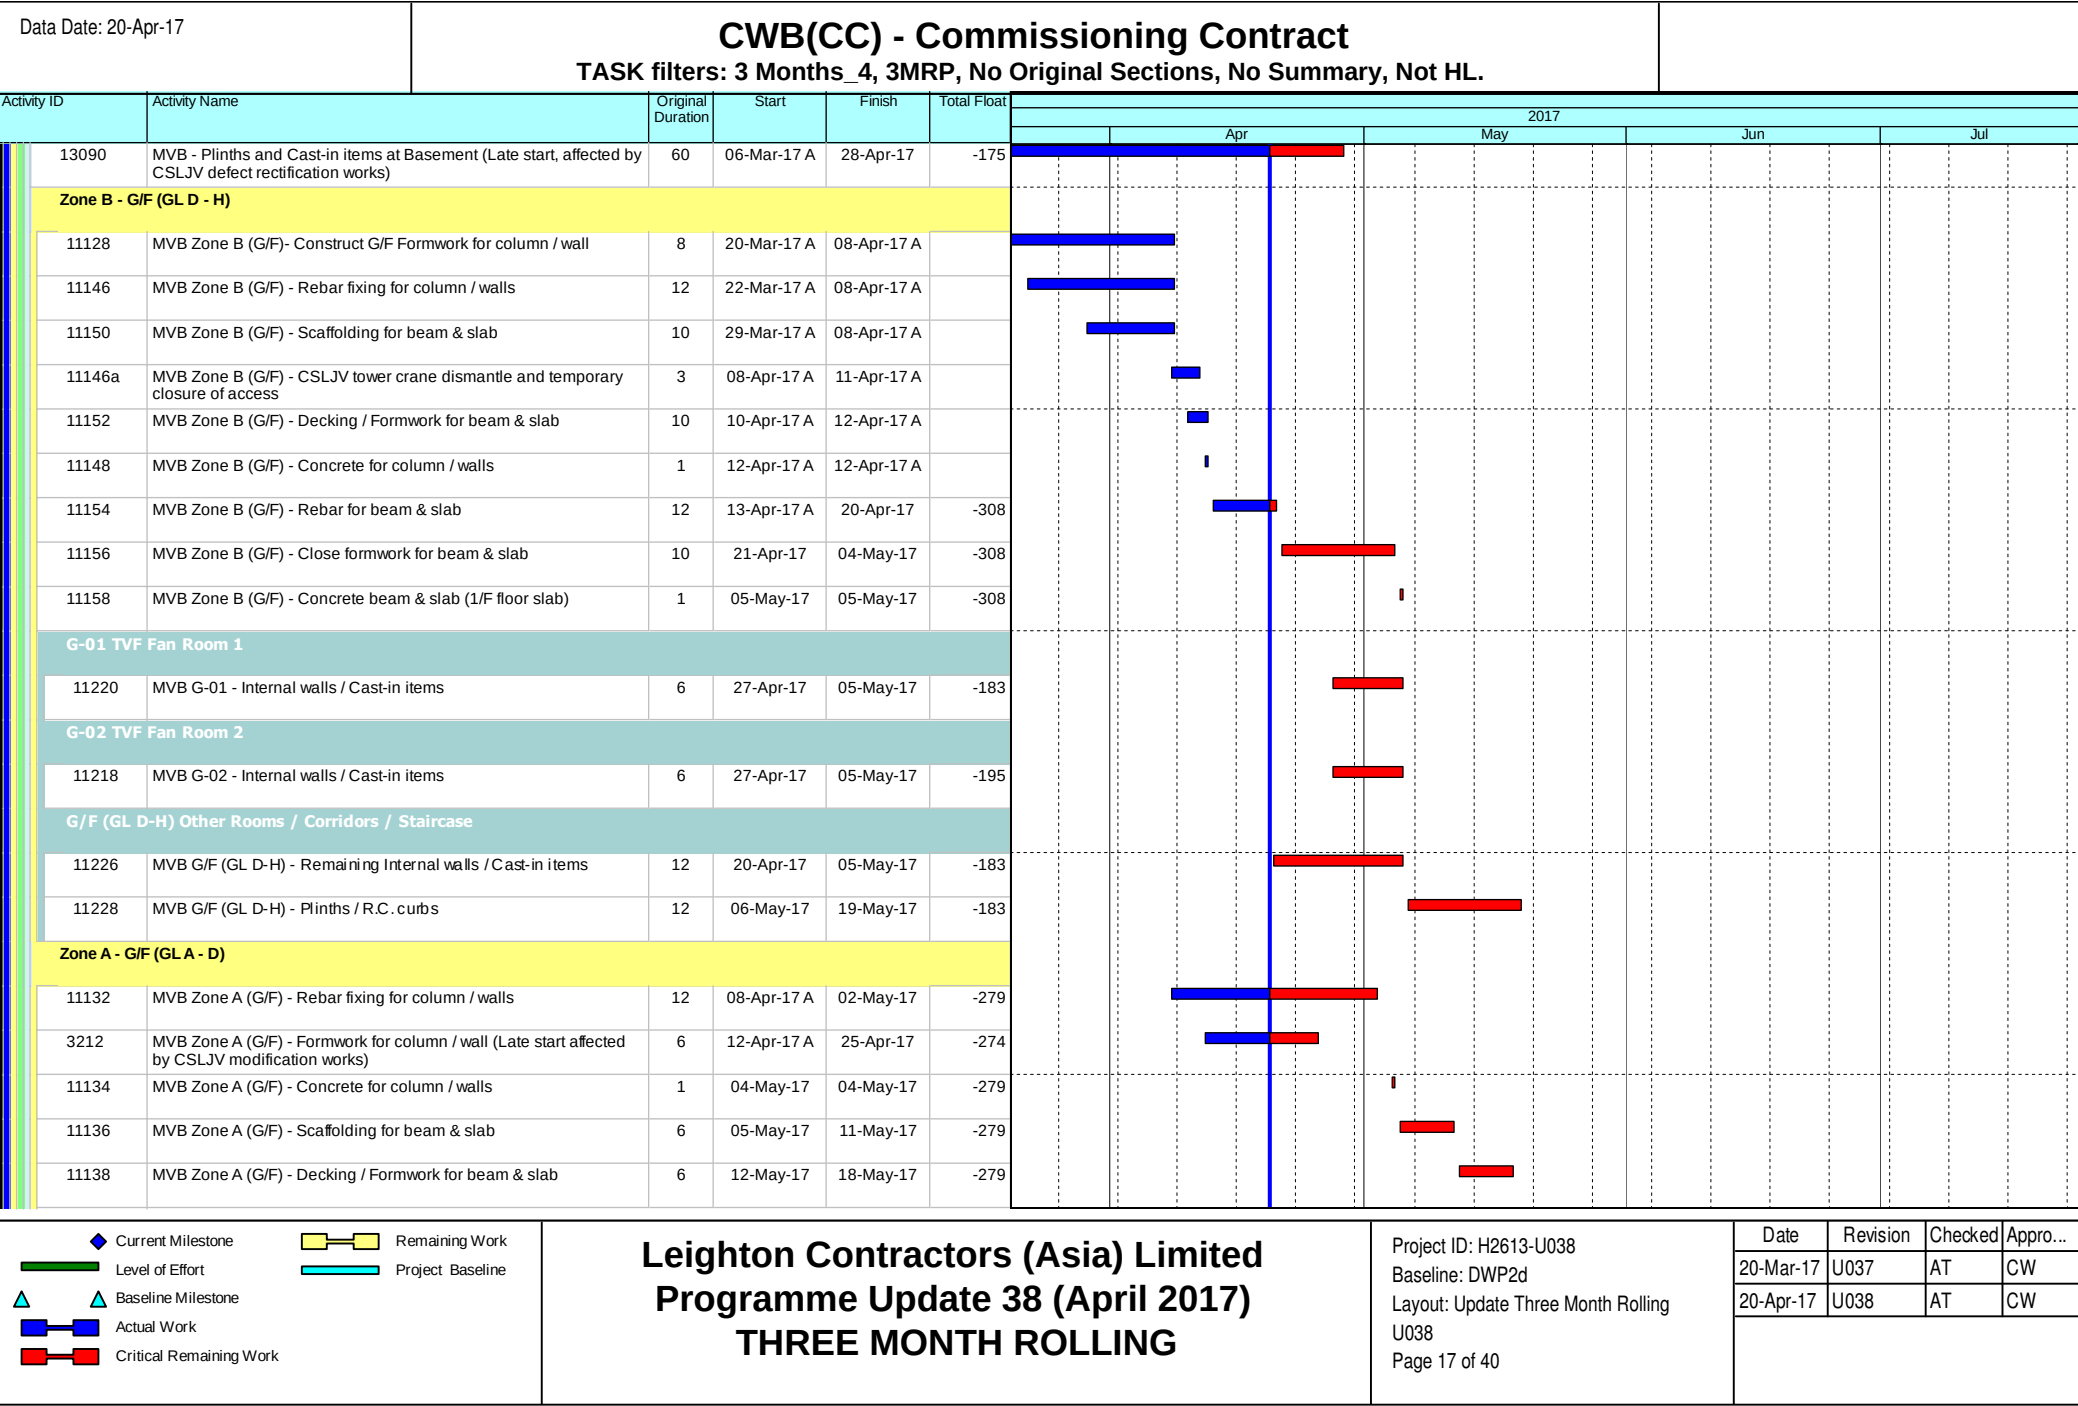

Data Date: 20-Apr-17		CWB(CC) - Commissioning Contract																
TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.																		
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017												
						Apr			May			Jun			Jul			
11140	MVB Zone A (G/F) - Rebar for beam & slab	10	19-May-17	31-May-17	-279													
11142	MVB Zone A (G/F) - Close formwork for beam & slab	6	01-Jun-17	07-Jun-17	-279													
11144	MVB Zone A (G/F) - Concrete beam & slab (1/F floor slab)	1	08-Jun-17	08-Jun-17	-279													
G-07 HKE/HV Switch Room 1																		
11210	MVB G-07 - Internal walls / Cast-in items	6	02-Jun-17	08-Jun-17	-231													
G-10 HKE/HV Switch Room 2																		
11208	MVB G-10 - Internal walls / Cast-in items	6	02-Jun-17	08-Jun-17	-219													
G-05 Transformer Room 1																		
11212	MVB G-05 - Internal walls / Cast-in items	6	02-Jun-17	08-Jun-17	-231													
G-08 Transformer Room 2																		
11214	MVB G-08 - Internal walls / Cast-in items	12	25-May-17	08-Jun-17	-213													
G-11 Fire Control Centre																		
11216	MVB G-11 - Internal walls / Cast-in items	12	25-May-17	08-Jun-17	-165													
G/F Other Rooms / Corridors / Staircase																		
11222	MVB G/F (GL A-D) - Remaining Internal walls / Cast-in items	24	11-May-17	08-Jun-17	-165													
11224	MVB G/F (GL A-D) - Plinths / R.C. curbs	12	09-Jun-17	22-Jun-17	-165													
Zone B - 1/F (GL D - H)																		
11176	MVB Zone B (1/F) - Formwork for column / wall	8	06-May-17	15-May-17	-308													
11178	MVB Zone B (1/F) - Rebar fixing for column / walls	12	16-May-17	29-May-17	-308													
11180	MVB Zone B (1/F) - Concrete for column / walls	1	31-May-17	31-May-17	-308													
11182	MVB Zone B (1/F) - Scaffolding for beam & slab	10	01-Jun-17	12-Jun-17	-308													
11184	MVB Zone B (1/F) - Decking / Formwork for beam & slab	10	13-Jun-17	23-Jun-17	-308													
11186	MVB Zone B (1/F) - Rebar for beam & slab	12	24-Jun-17	08-Jul-17	-308													
11188	MVB Zone B (1/F) - Close formwork for beam & slab	10	10-Jul-17	20-Jul-17	-308													

Current Milestone

Level of Effort

Baseline Milestone

Actual Work

Critical Remaining Work

Remaining Work

Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 38 (April 2017)

THREE MONTH ROLLING

Project ID: H2613-U038

Baseline: DWP2d

Layout: Update Three Month Rolling

U038

Page 18 of 40

Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

◆ Current Milestone

▬ Level of Effort

▲ Baseline Milestone

▬ Actual Work

▬ Critical Remaining Work

▬ Remaining Work

▬ Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 38 (April 2017)

THREE MONTH ROLLING

Project ID: H2613-U038

Baseline: DWP2d

Layout: Update Three Month Rolling

U038

Page 18 of 40

Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

Data Date: 20-Apr-17		CWB(CC) - Commissioning Contract																
TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.																		
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017												
						Apr			May			Jun			Jul			
19030	MEP(MVB) - E&M 1st fixing	30	31-May-17	05-Jul-17	-163													
19032	MEP(MVB) - E&M 2nd fixing	24	06-Jul-17	02-Aug-17	-163													
Basement 2M (GL D - H)																		
TV Plenum																		
19036	MEP(MVB) - ABWF Works	12	31-May-17	13-Jun-17	-175													
19038	MEP(MVB) - E&M 1st fixing	30	14-Jun-17	19-Jul-17	-175													
Basement 1 (GL D - H)																		
General Area & Corridor																		
11312	MEP(MVB) - ABWF Works	12	29-Apr-17	15-May-17	-151													
11314	MEP(MVB) - E&M 1st fixing	30	16-May-17	20-Jun-17	-151													
11316	MEP(MVB) - E&M 2nd fixing	24	21-Jun-17	19-Jul-17	-151													
Basement 1 (GLA - D)																		
MCC Room 1 (B1-04)																		
11280	MVB - ABWF works for MCC Room 1	12	01-Jun-17	14-Jun-17	-258													
11282	MEP(MVB) - E&M 1st fixing	12	15-Jun-17	28-Jun-17	-204													
12346	APS(MVB) - E&M 2nd fixing	12	29-Jun-17	13-Jul-17	-204													
11284	MEP(MVB) - MCC installation	12	14-Jul-17	27-Jul-17	-158													
UPS Room 1 (B1-11)																		
11288	MVB - ABWF works for UPS Room	12	15-Jun-17	28-Jun-17	-258													
11290	MEP(MVB) - E&M 1st fixing	12	29-Jun-17	13-Jul-17	-212													
12348	APS(MVB) - E&M 2nd fixing	12	14-Jul-17	27-Jul-17	-212													
MCC Room 2 (B1-07)																		
11304	MVB - ABWF works for MCC Room 2	12	29-Jun-17	13-Jul-17	-258													
11306	MEP(MVB) - E&M 1st fixing	12	14-Jul-17	27-Jul-17	-212													

Current Milestone

Level of Effort

Baseline Milestone

Actual Work

Critical Remaining Work

Remaining Work

Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 38 (April 2017)

THREE MONTH ROLLING

Project ID: H2613-U038

Baseline: DWP2d

Layout: Update Three Month Rolling

U038

Page 20 of 40

Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

◆ Current Milestone

▬ Level of Effort

▲ Baseline Milestone

▬ Actual Work

▬ Critical Remaining Work

▬ Remaining Work

▬ Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 38 (April 2017)

THREE MONTH ROLLING

Project ID: H2613-U038


Baseline: DWP2d


Layout: Update Three Month Rolling


U038


Page 20 of 40


Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

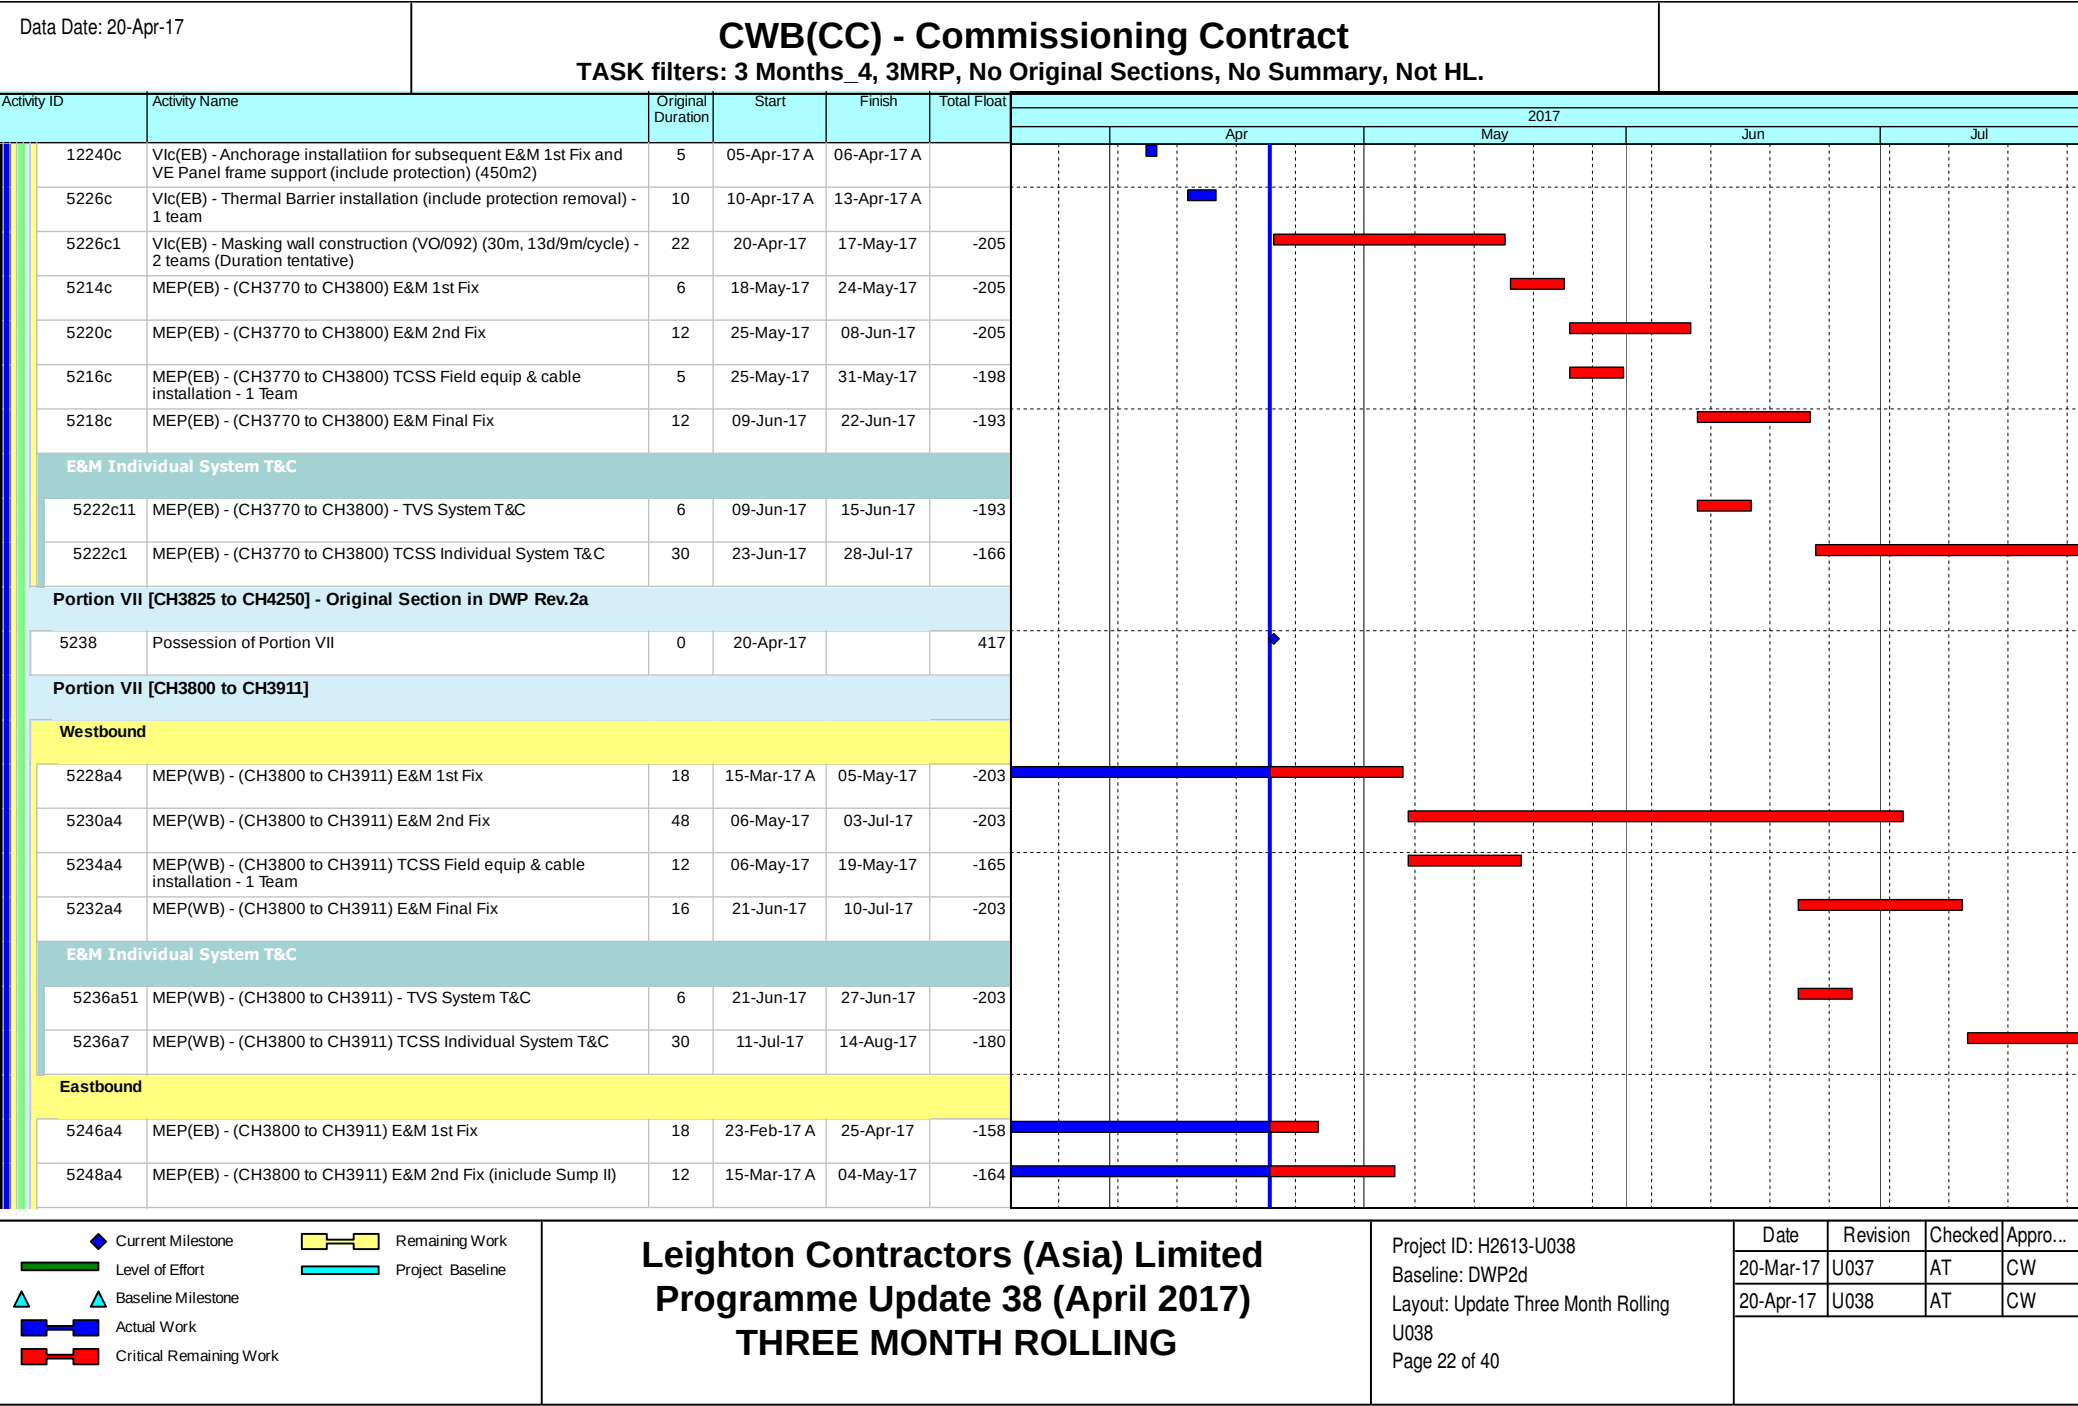


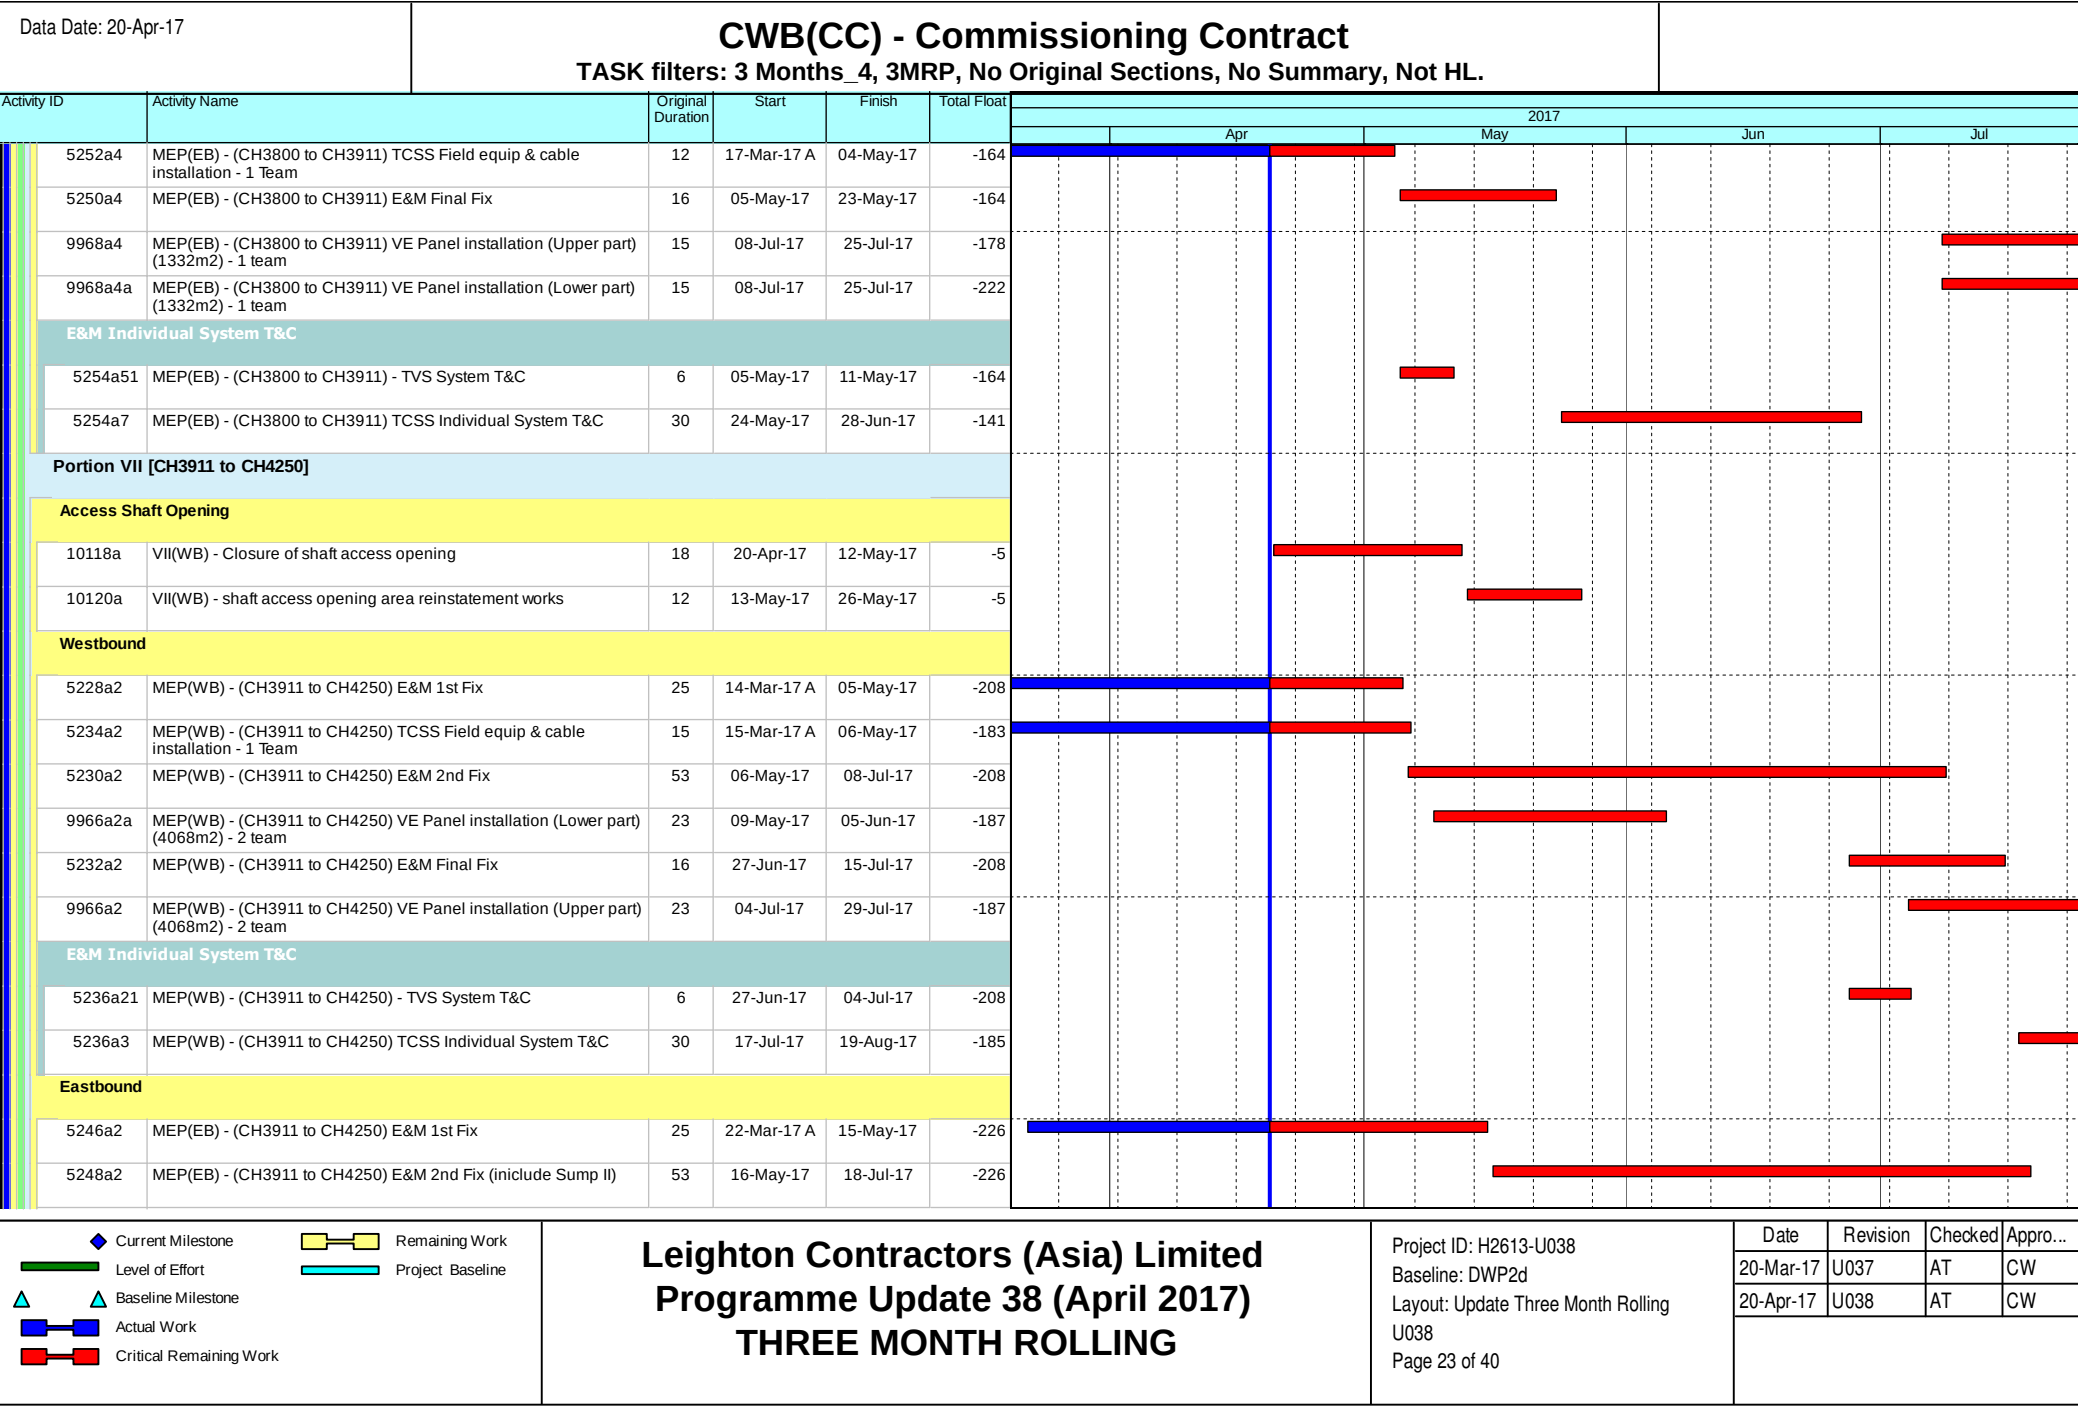


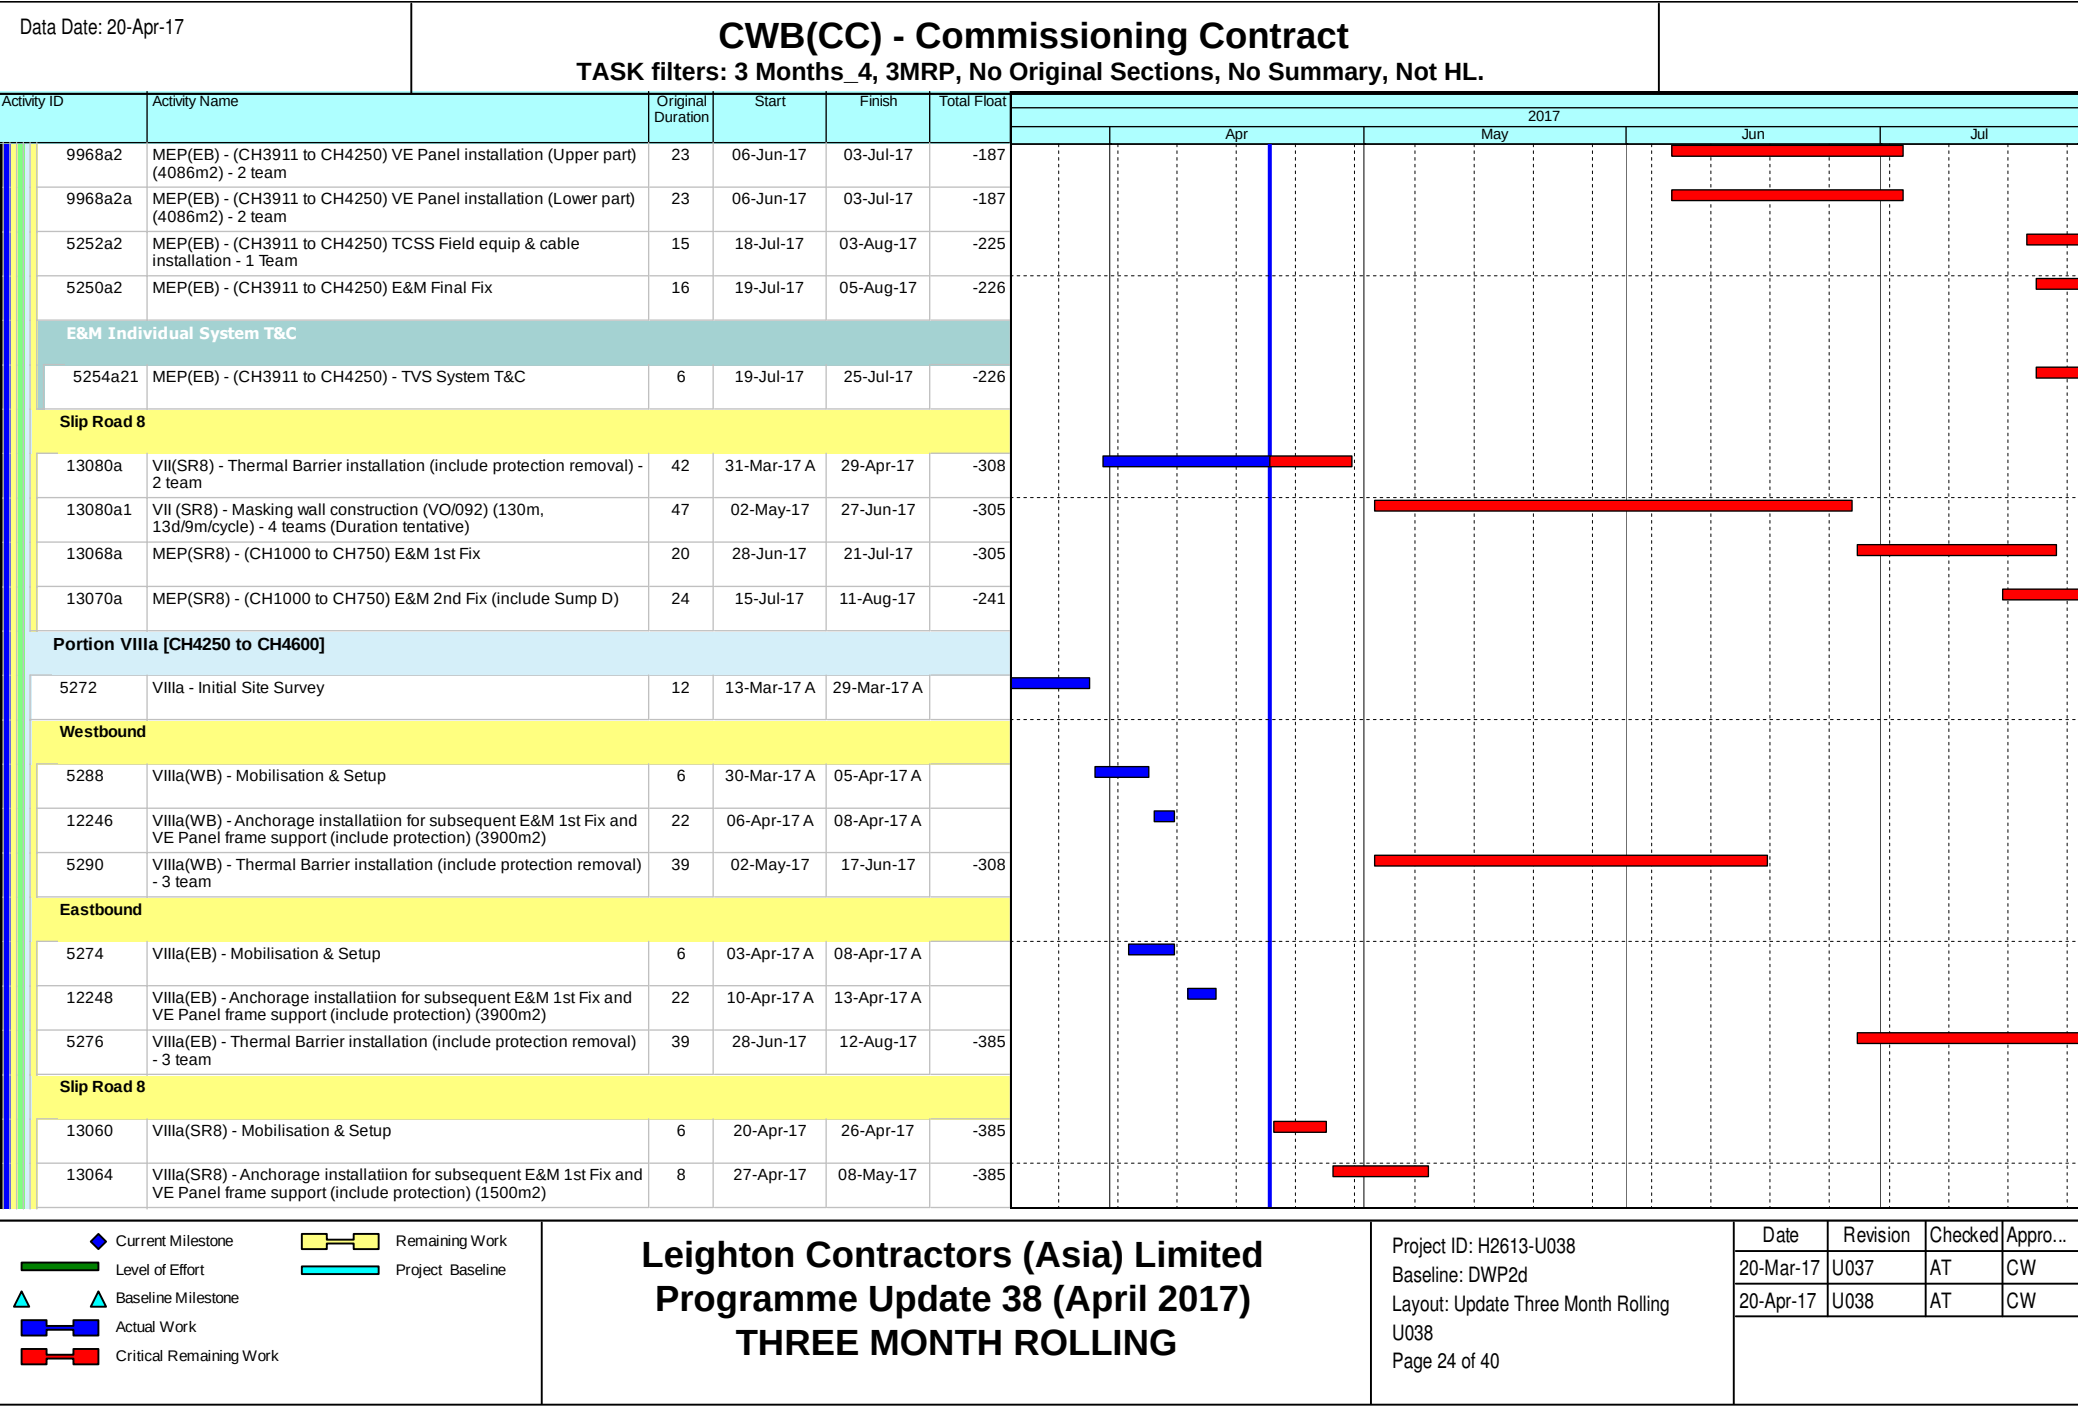

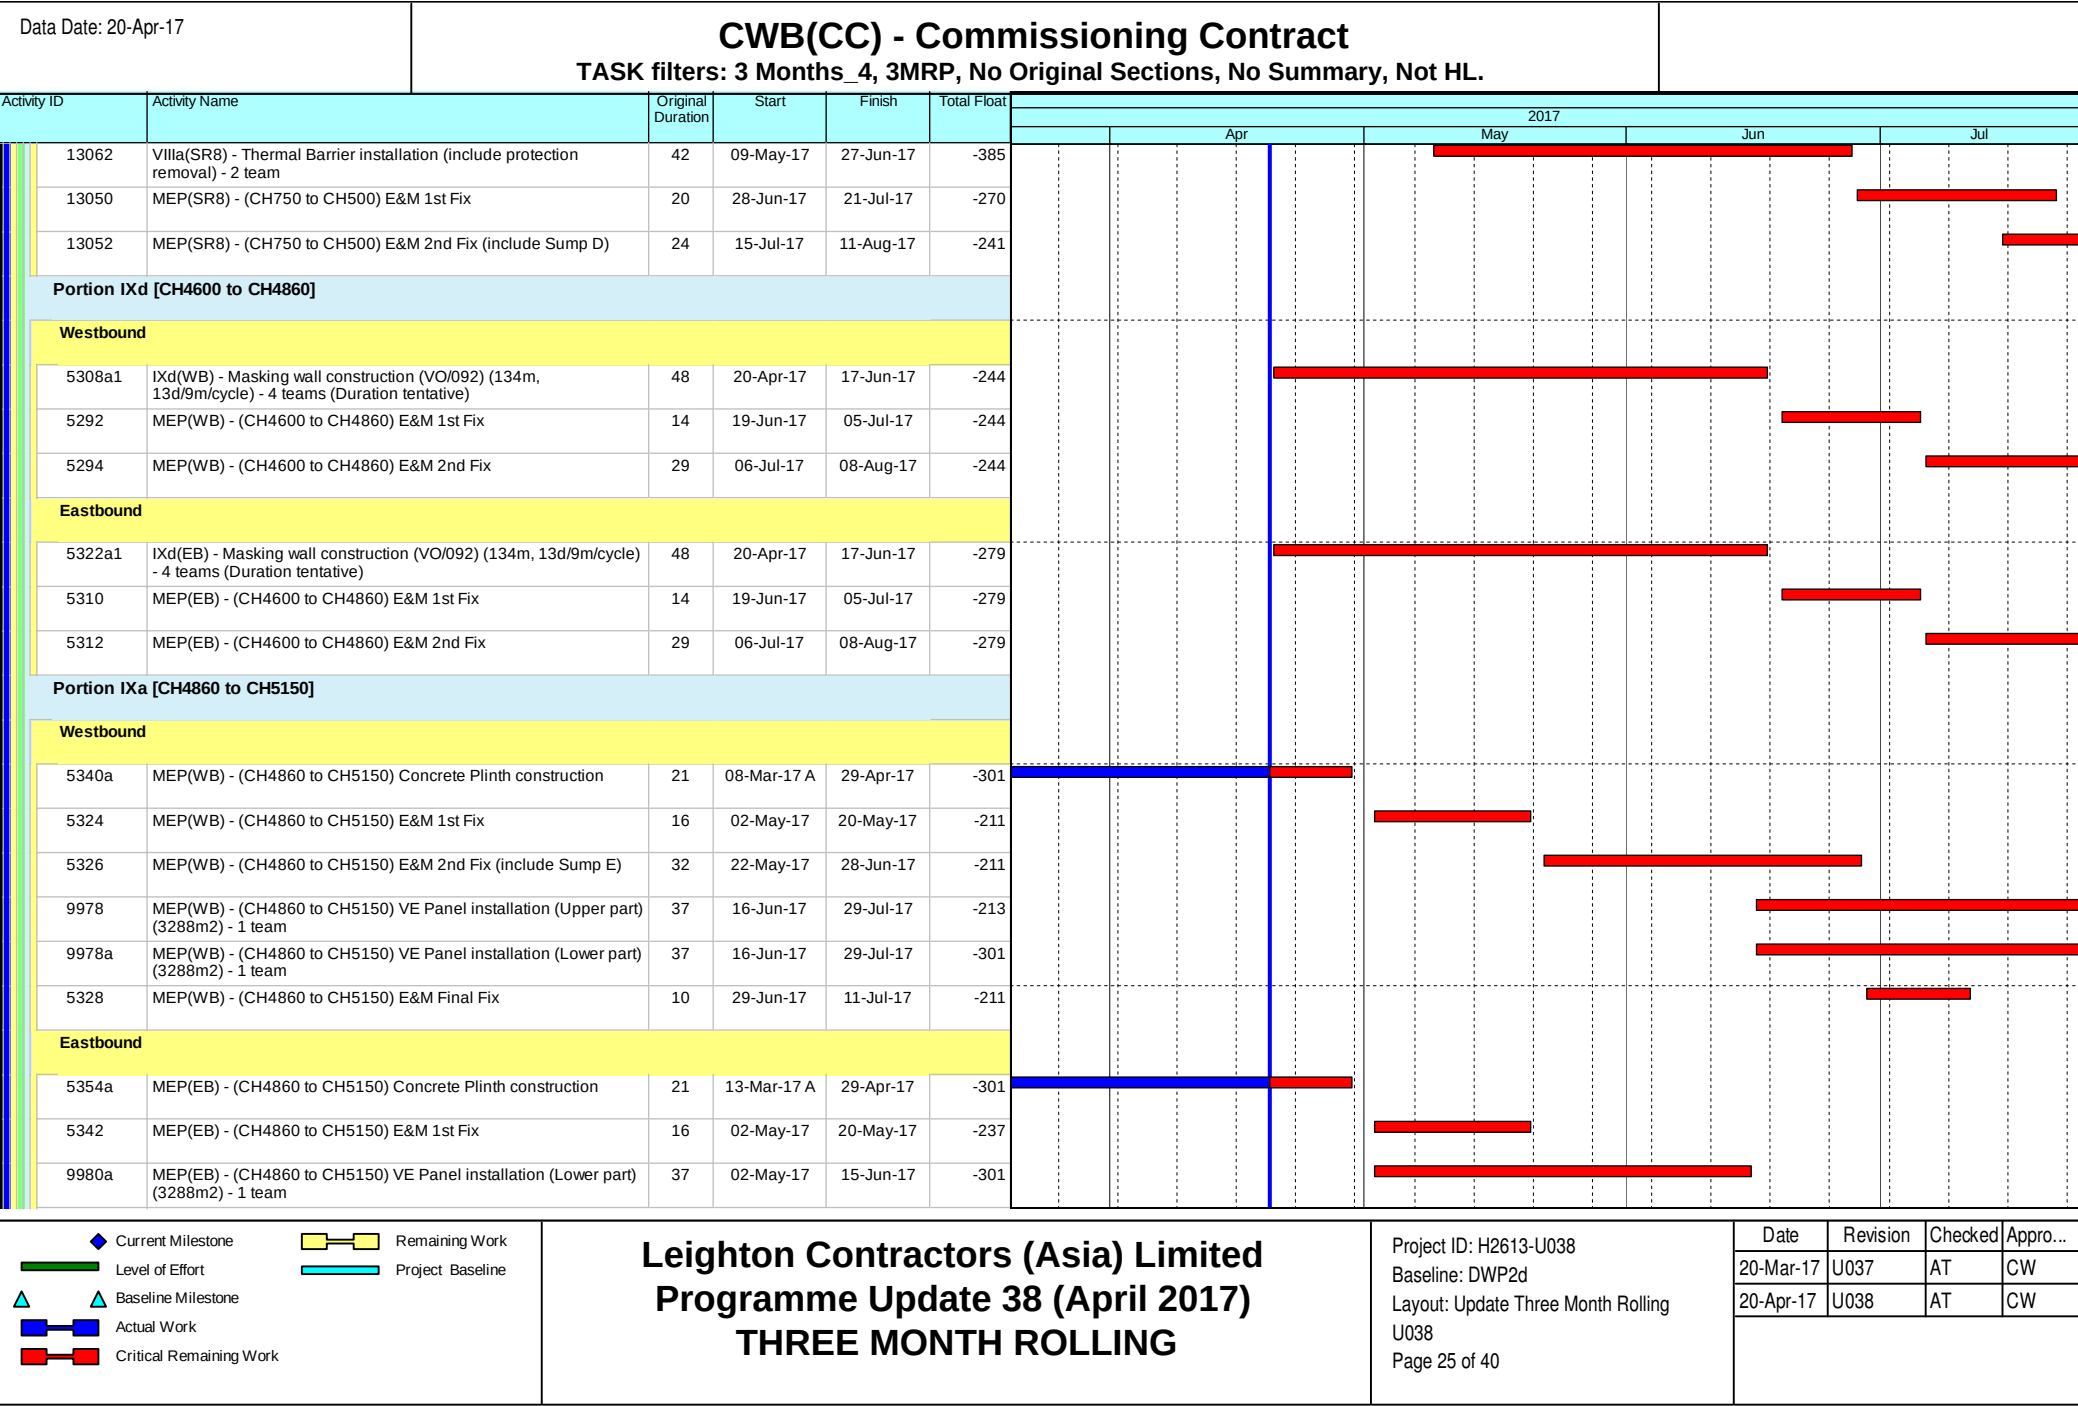

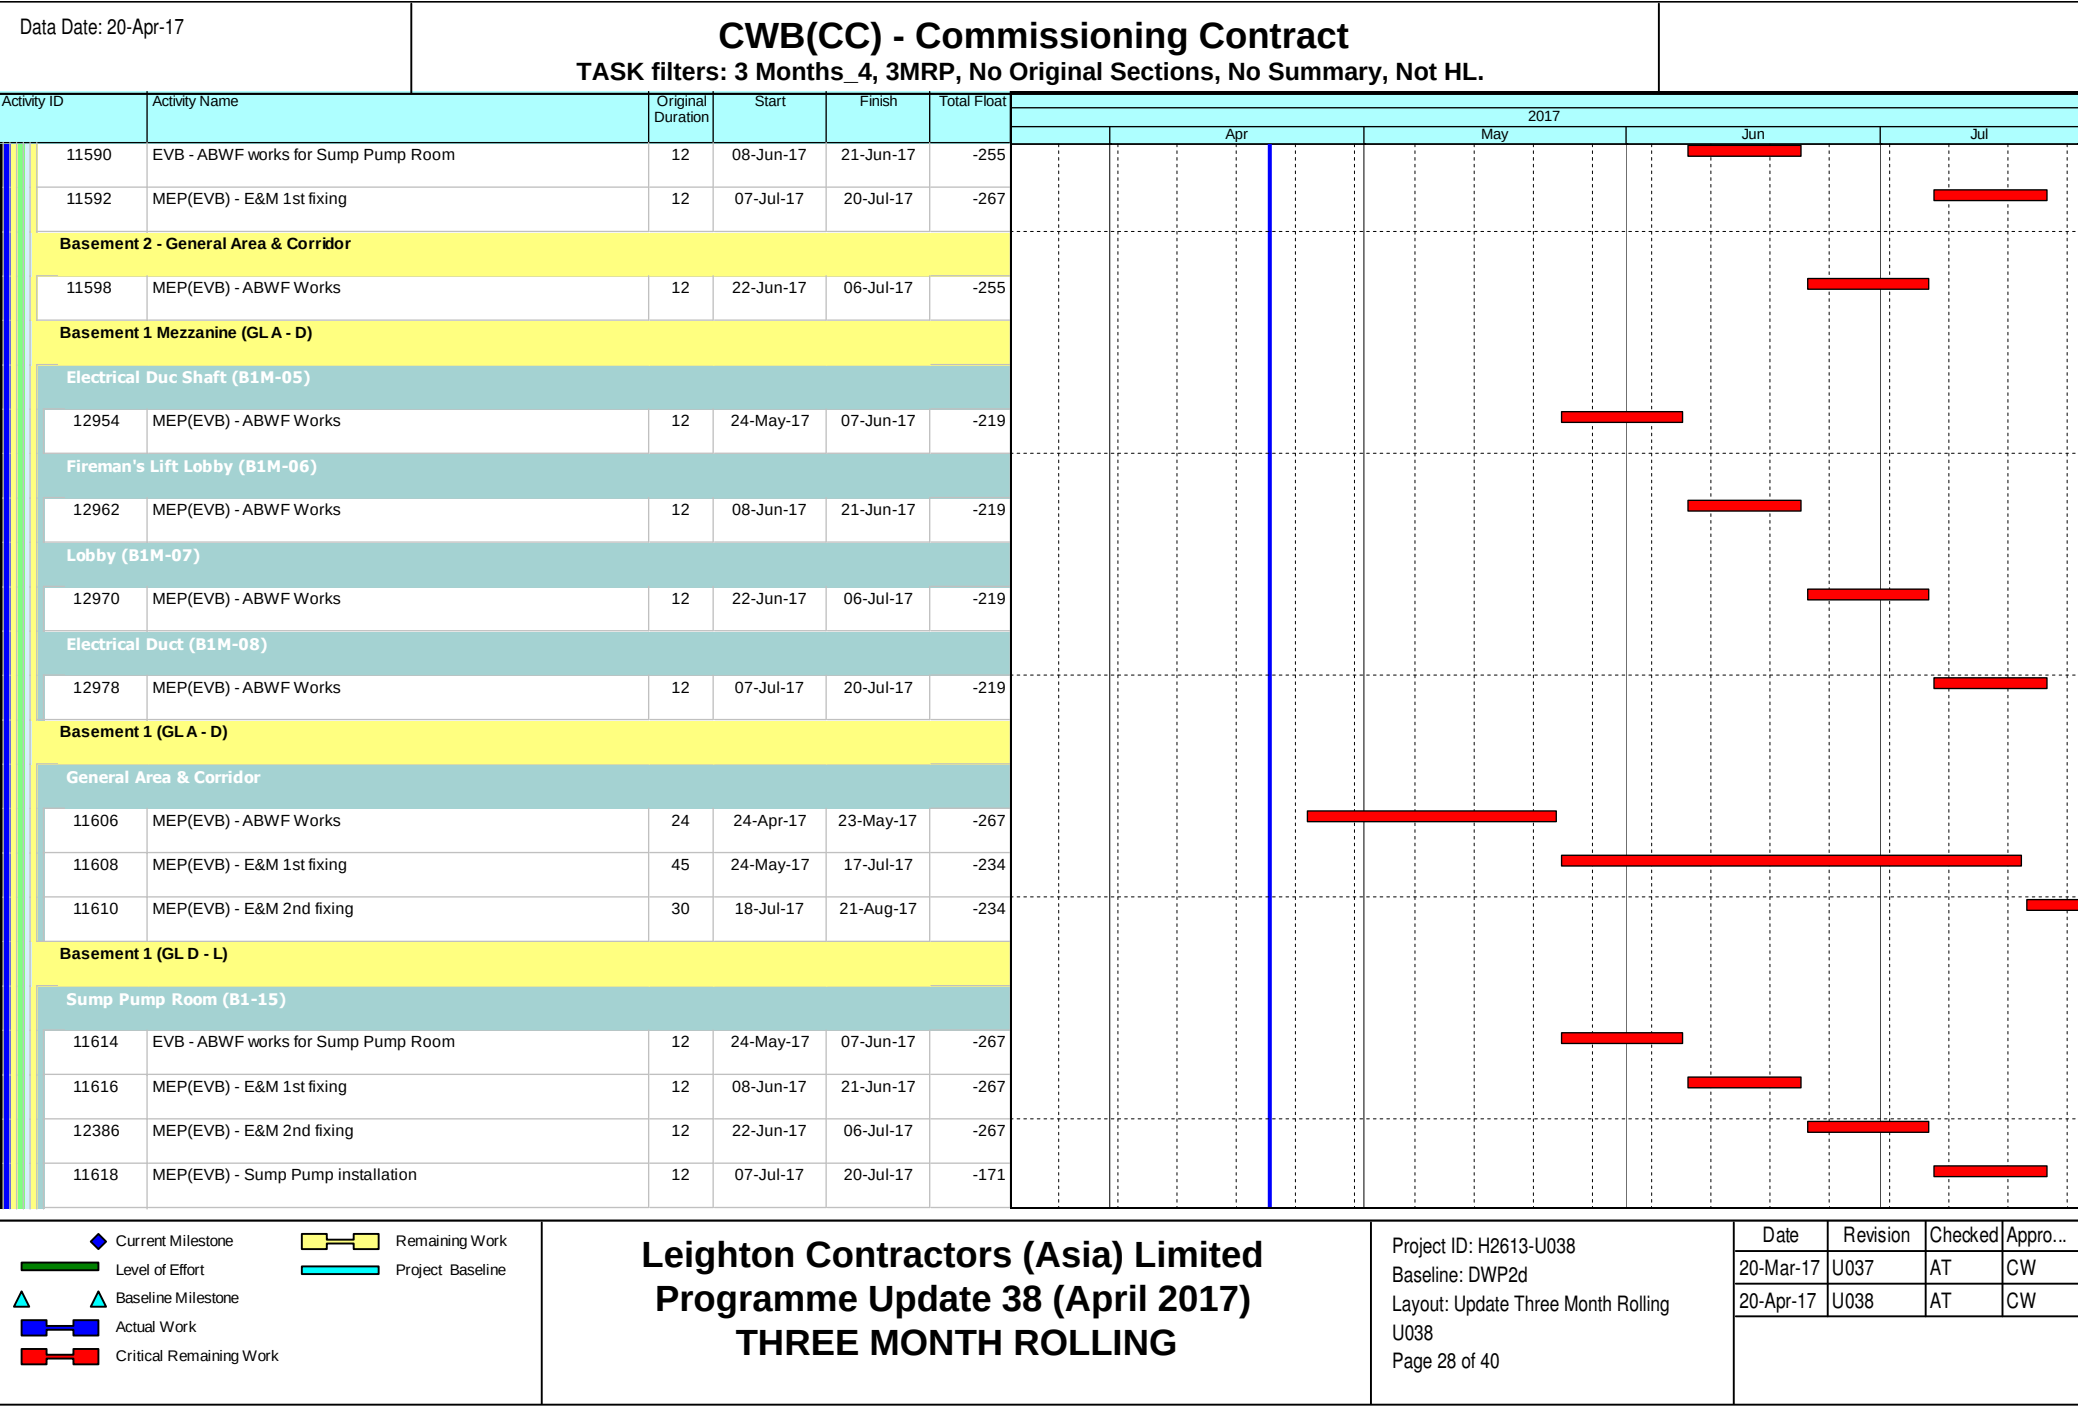

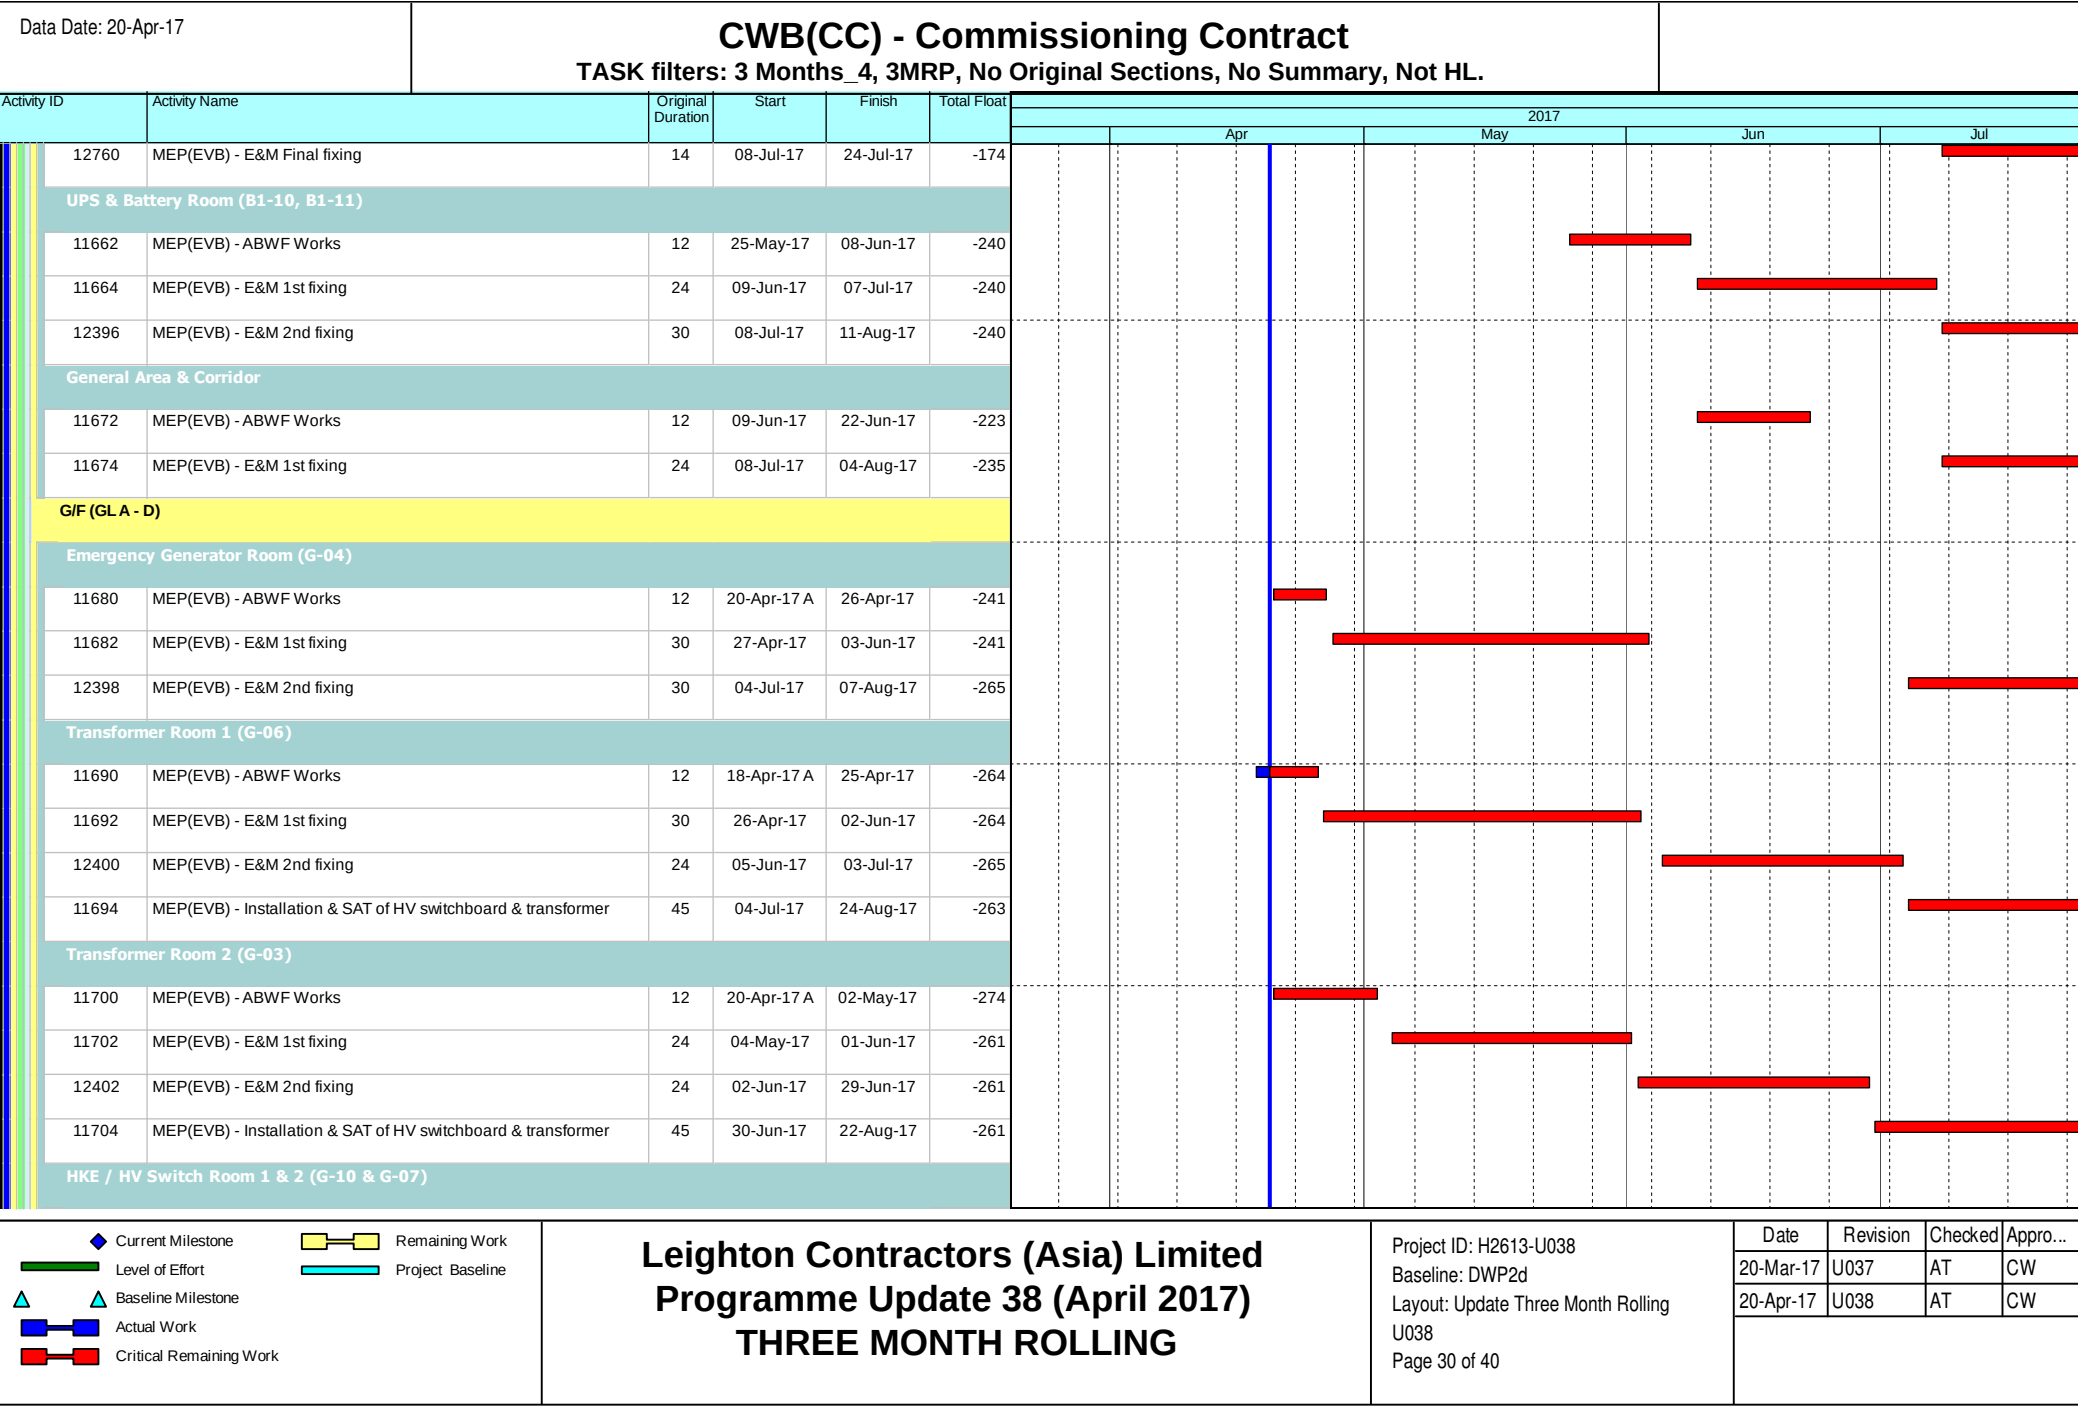

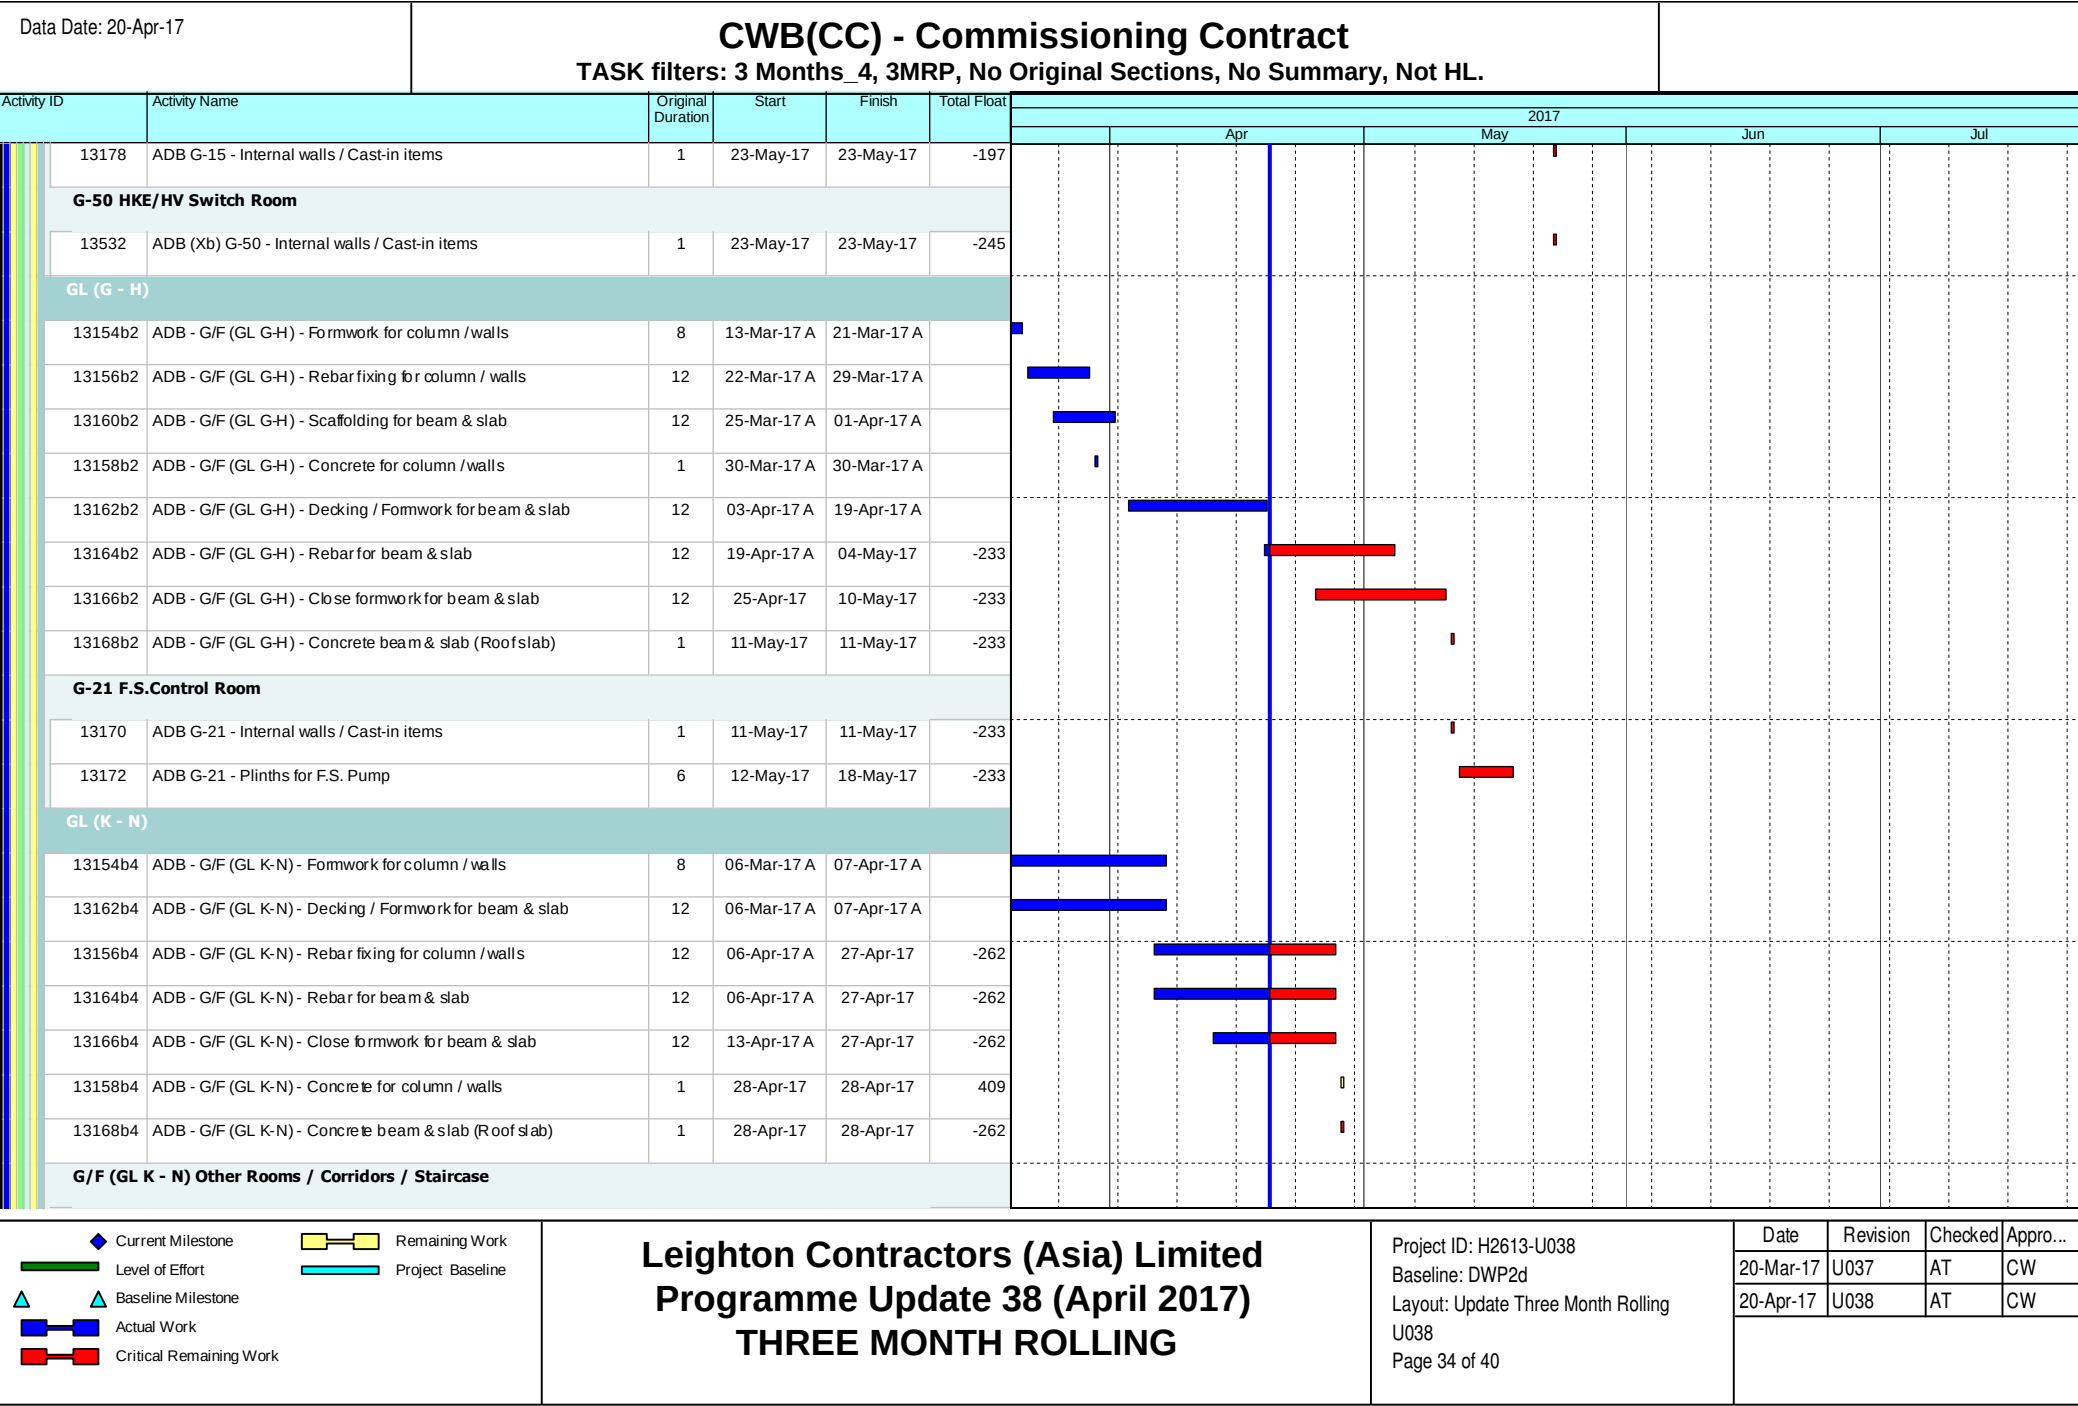

Data Date: 20-Apr-17			CWB(CC) - Commissioning Contract																
			TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.																
Activity ID	Activity Name		Original Duration	Start	Finish	Total Float	2017												
				Apr	May	Jun	Jul												
13308	MEP(ADB) - ABWF Works		12	16-May-17	29-May-17	-262													
G/F (GL D - N)																			
F.S. Control Room (G-21)																			
13346	MEP(ADB) - ABWF Works		12	16-Jun-17	29-Jun-17	-256													
13348	MEP(ADB) - E&M 1st fixing		8	07-Jul-17	15-Jul-17	-261													
Transformer Room 1 (G-14)																			
13370	MEP(ADB) - ABWF Works		12	24-May-17	07-Jun-17	-287													
Un-interrupted Power Supply (UPS) Room (G-13)																			
13394	MEP(ADB) - ABWF Works		12	08-Jun-17	21-Jun-17	-261													
13396	MEP(ADB) - E&M 1st fixing		12	22-Jun-17	06-Jul-17	-261													
13404	MEP(ADB) - E&M 2nd fixing		12	07-Jul-17	20-Jul-17	-221													
LV Switch Room (G-15)																			
13384	ADB - ABWF works for LV Switch Rooms		12	22-Jun-17	06-Jul-17	-221													
13388	MEP(ADB) - E&M 1st fixing		12	07-Jul-17	20-Jul-17	-221													
1/F (GL A - D)																			
Water Pump Room (L1-08)																			
13422	MEP(ADB) - ABWF Works		12	18-May-17	01-Jun-17	-256													
13424	MEP(ADB) - E&M 1st fixing		12	02-Jun-17	15-Jun-17	-216													
13430	MEP(ADB) - E&M 2nd fixing		12	16-Jun-17	29-Jun-17	-216													
13426	MEP(ADB) - Installation of FS Pump		24	30-Jun-17	28-Jul-17	-216													
General Area & Corridor																			
13414	MEP(ADB) - ABWF Works		12	02-Jun-17	15-Jun-17	-256													
13416	MEP(ADB) - E&M 1st fixing		24	16-Jun-17	14-Jul-17	-216													
E&M Testing &Commissioning / Statutory Inspection																			

Current Milestone

Level of Effort

Baseline Milestone

Actual Work

Critical Remaining Work

Remaining Work

Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 38 (April 2017)

THREE MONTH ROLLING

Project ID: H2613-U038

Baseline: DWP2d

Layout: Update Three Month Rolling

U038



Page 36 of 40

Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

Data Date: 20-Apr-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

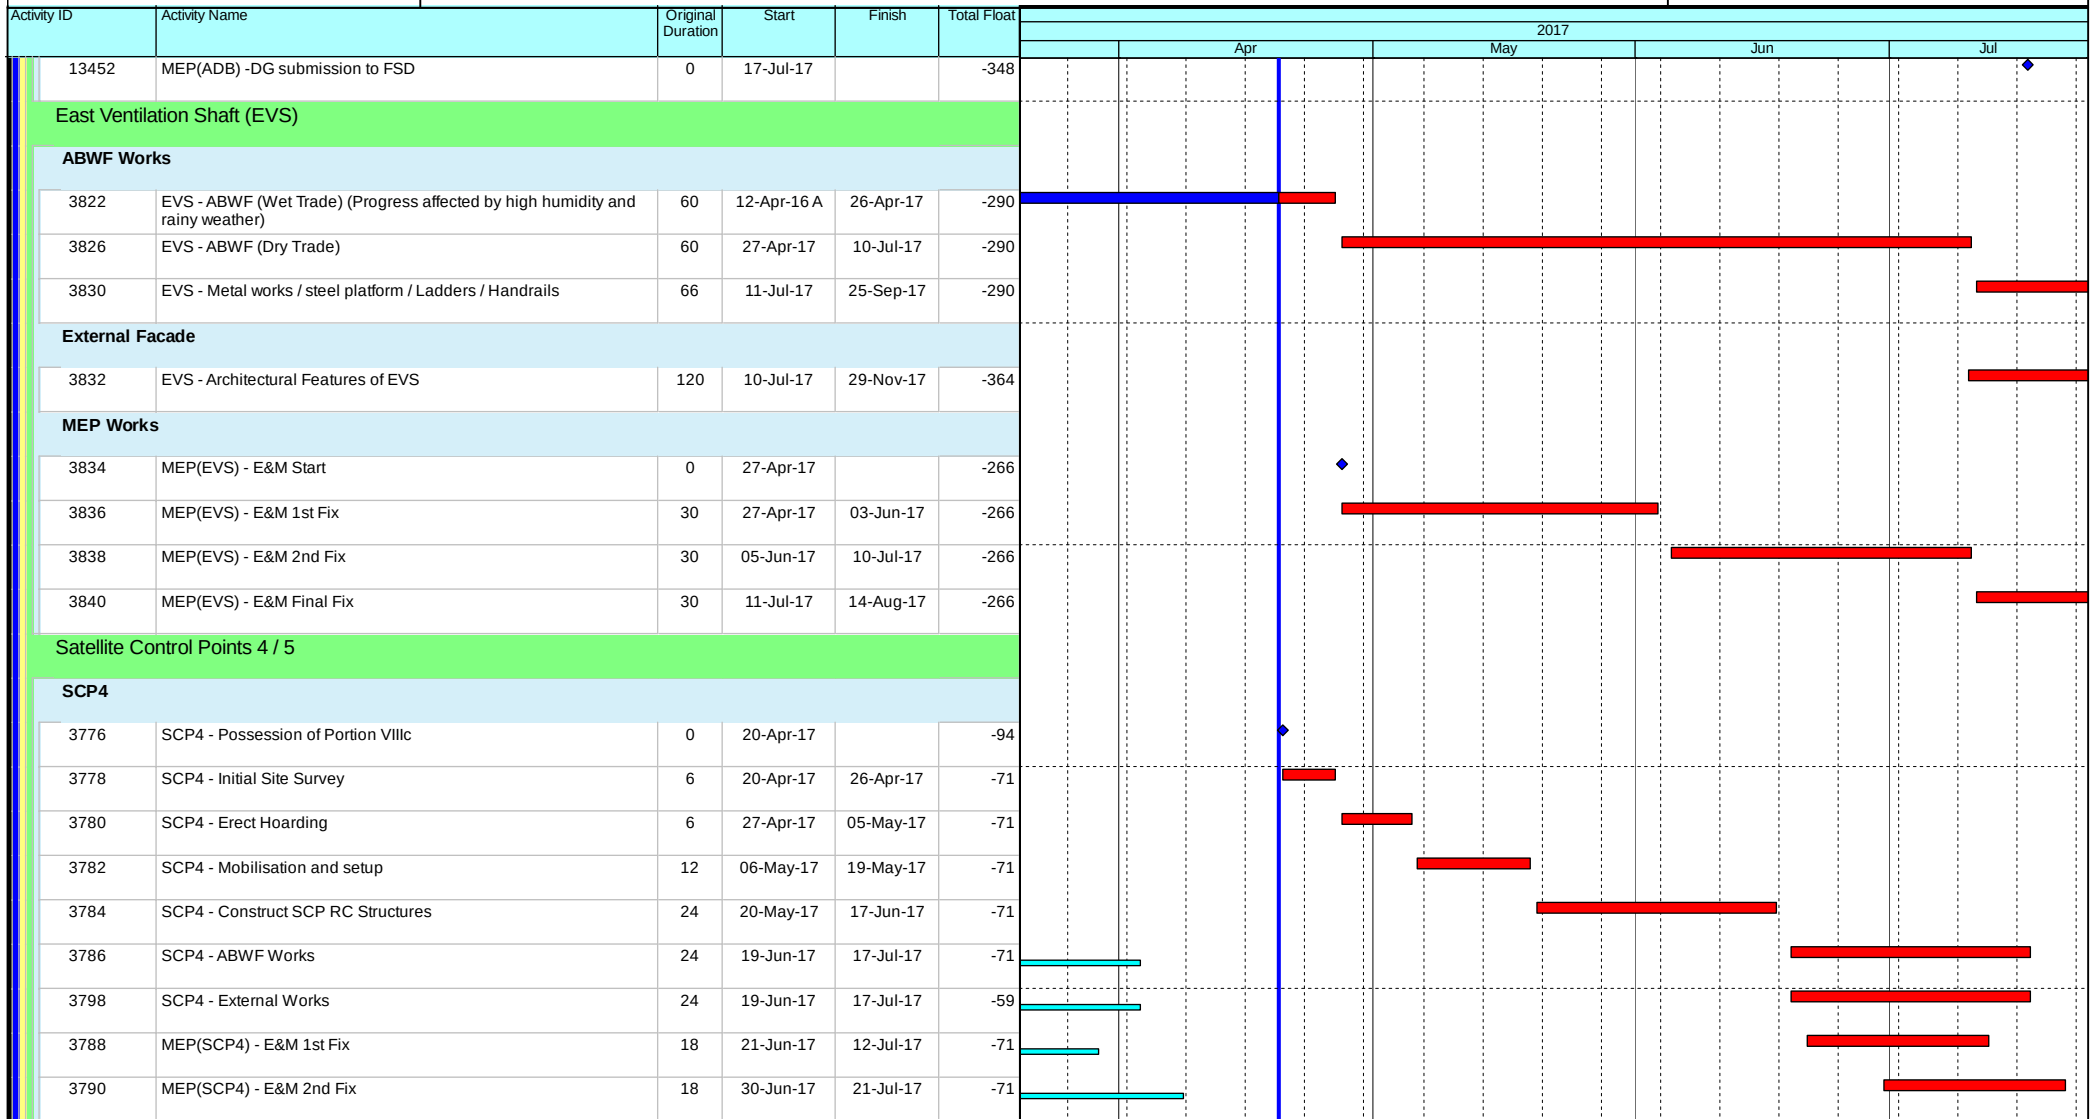

Leighton Contractors (Asia) Limited Programme Update 38 (April 2017) THREE MONTH ROLLING

Project ID: H2613-U038
Baseline: DWP2d
Layout: Update Three Month Rolling
U038
Page 37 of 40

Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

Data Date: 20-Apr-17

CWB(CC) - Commissioning Contract
TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

CWB(CC) - Commissioning Contract
TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
19014	Area B - TTA Approved	0	02-May-17*		-18
19016	Area B (Remaining need TTA) - Noise enclosure lighting brackets installation	53	02-May-17	05-Jul-17	-18
19018	Area B (Remaining need TTA) - Cable containment installation	29	06-Jul-17	08-Aug-17	-18

 Current Milestone
 Level of Effort
 Baseline Milestone
 Actual Work
 Critical Remaining Work

 Remaining Work
 Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 38 (April 2017)

THREE MONTH ROLLING


Project ID: H2613-U038


Baseline: DWP2d


Layout: Update Three Month Rolling U038

Page 40 of 40

Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

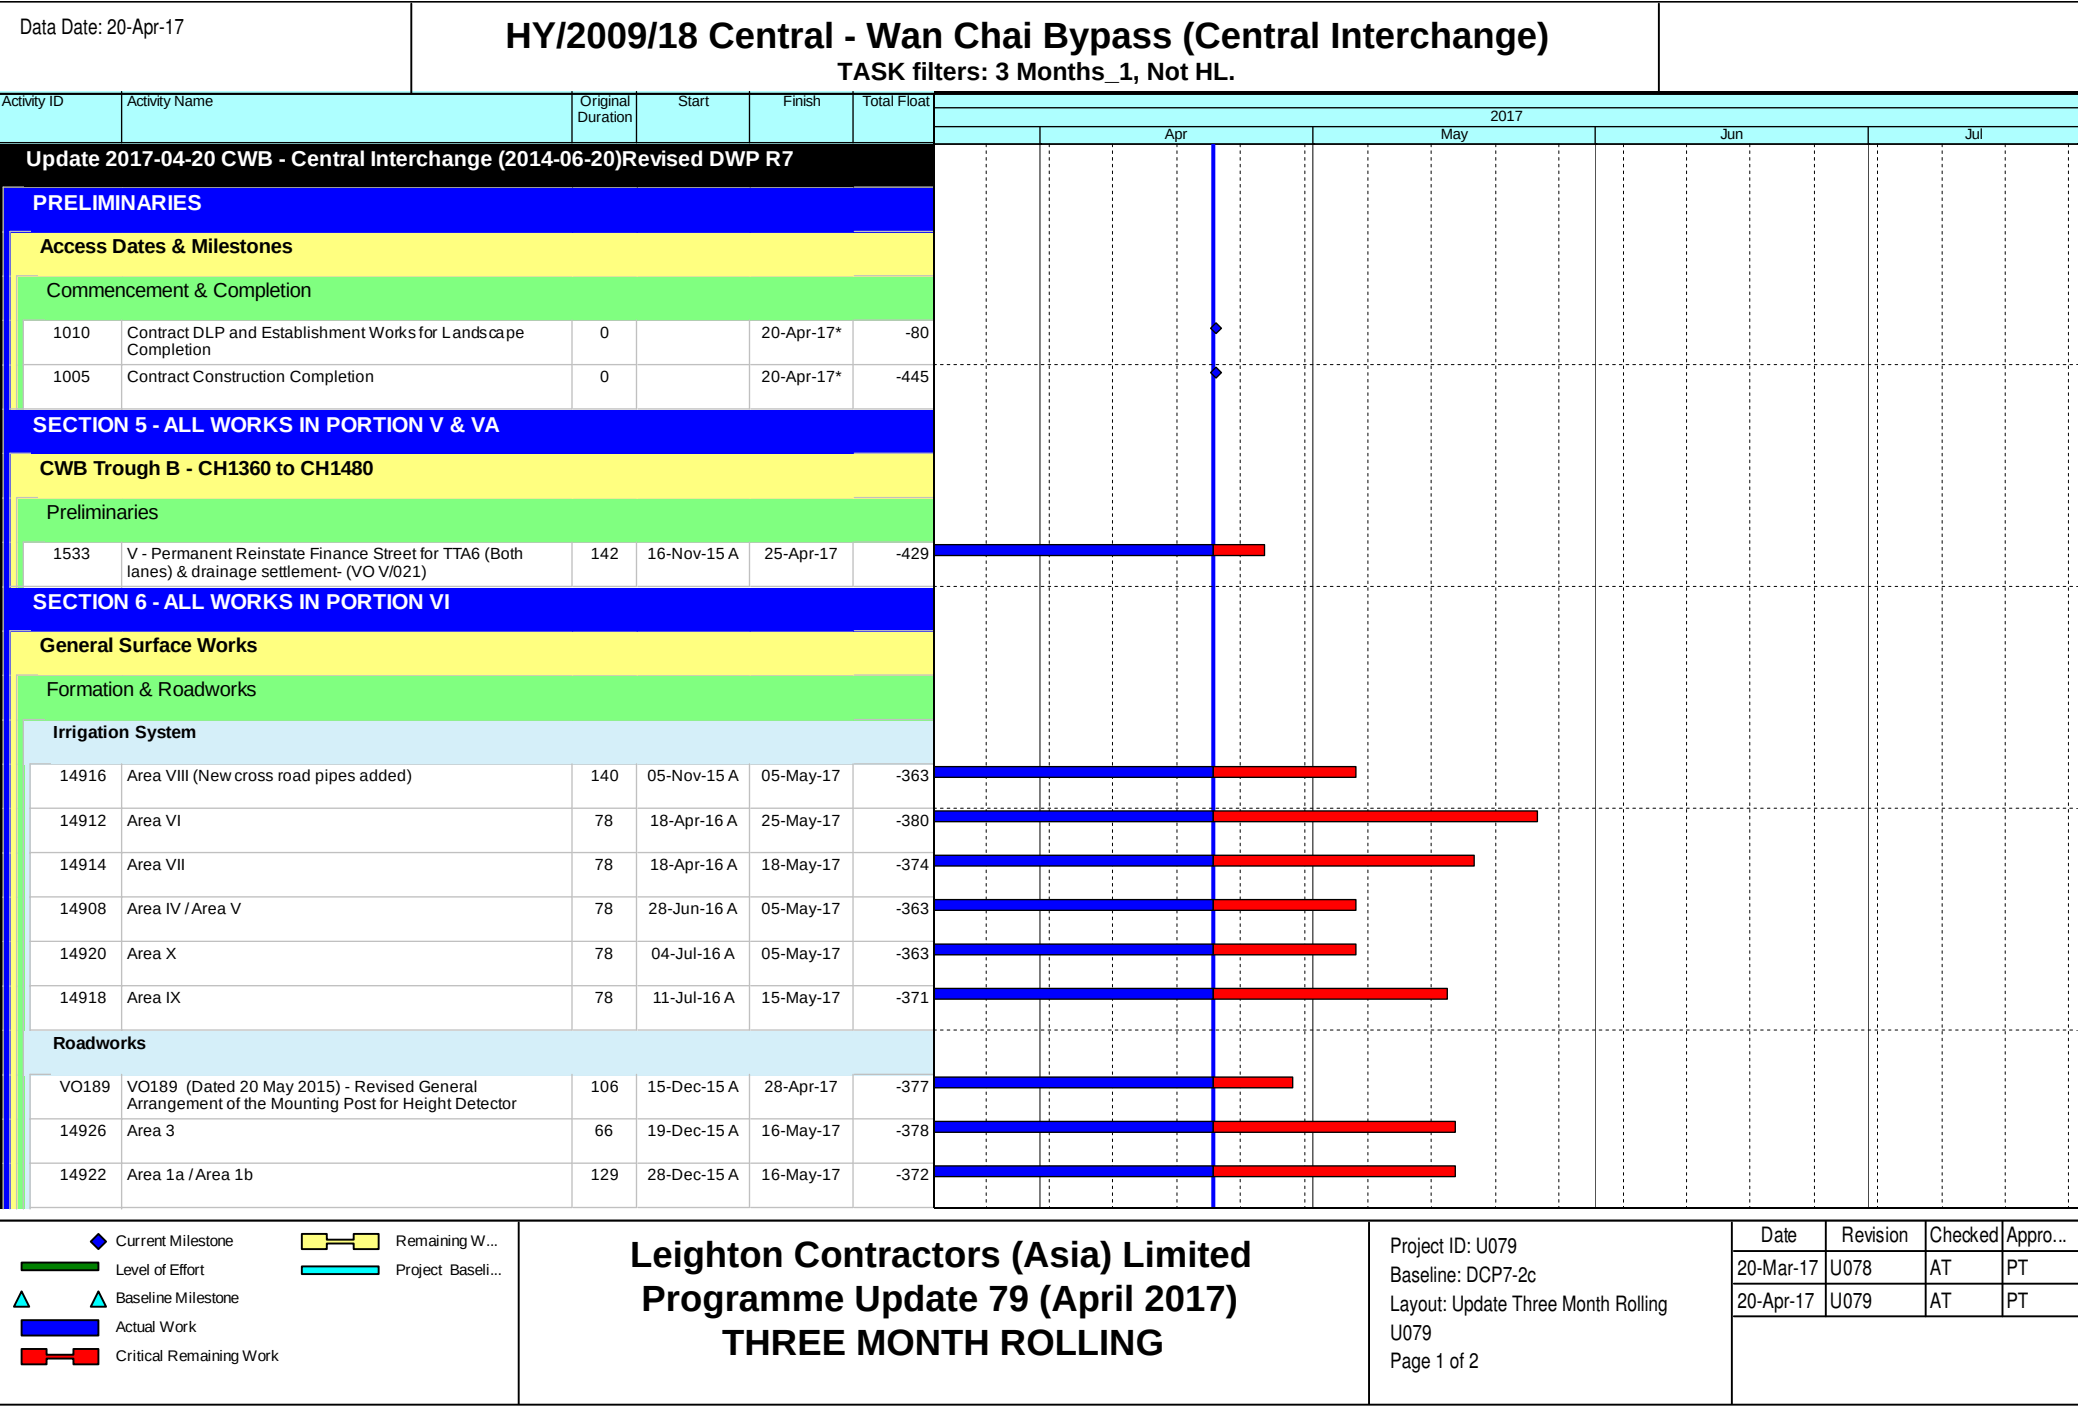

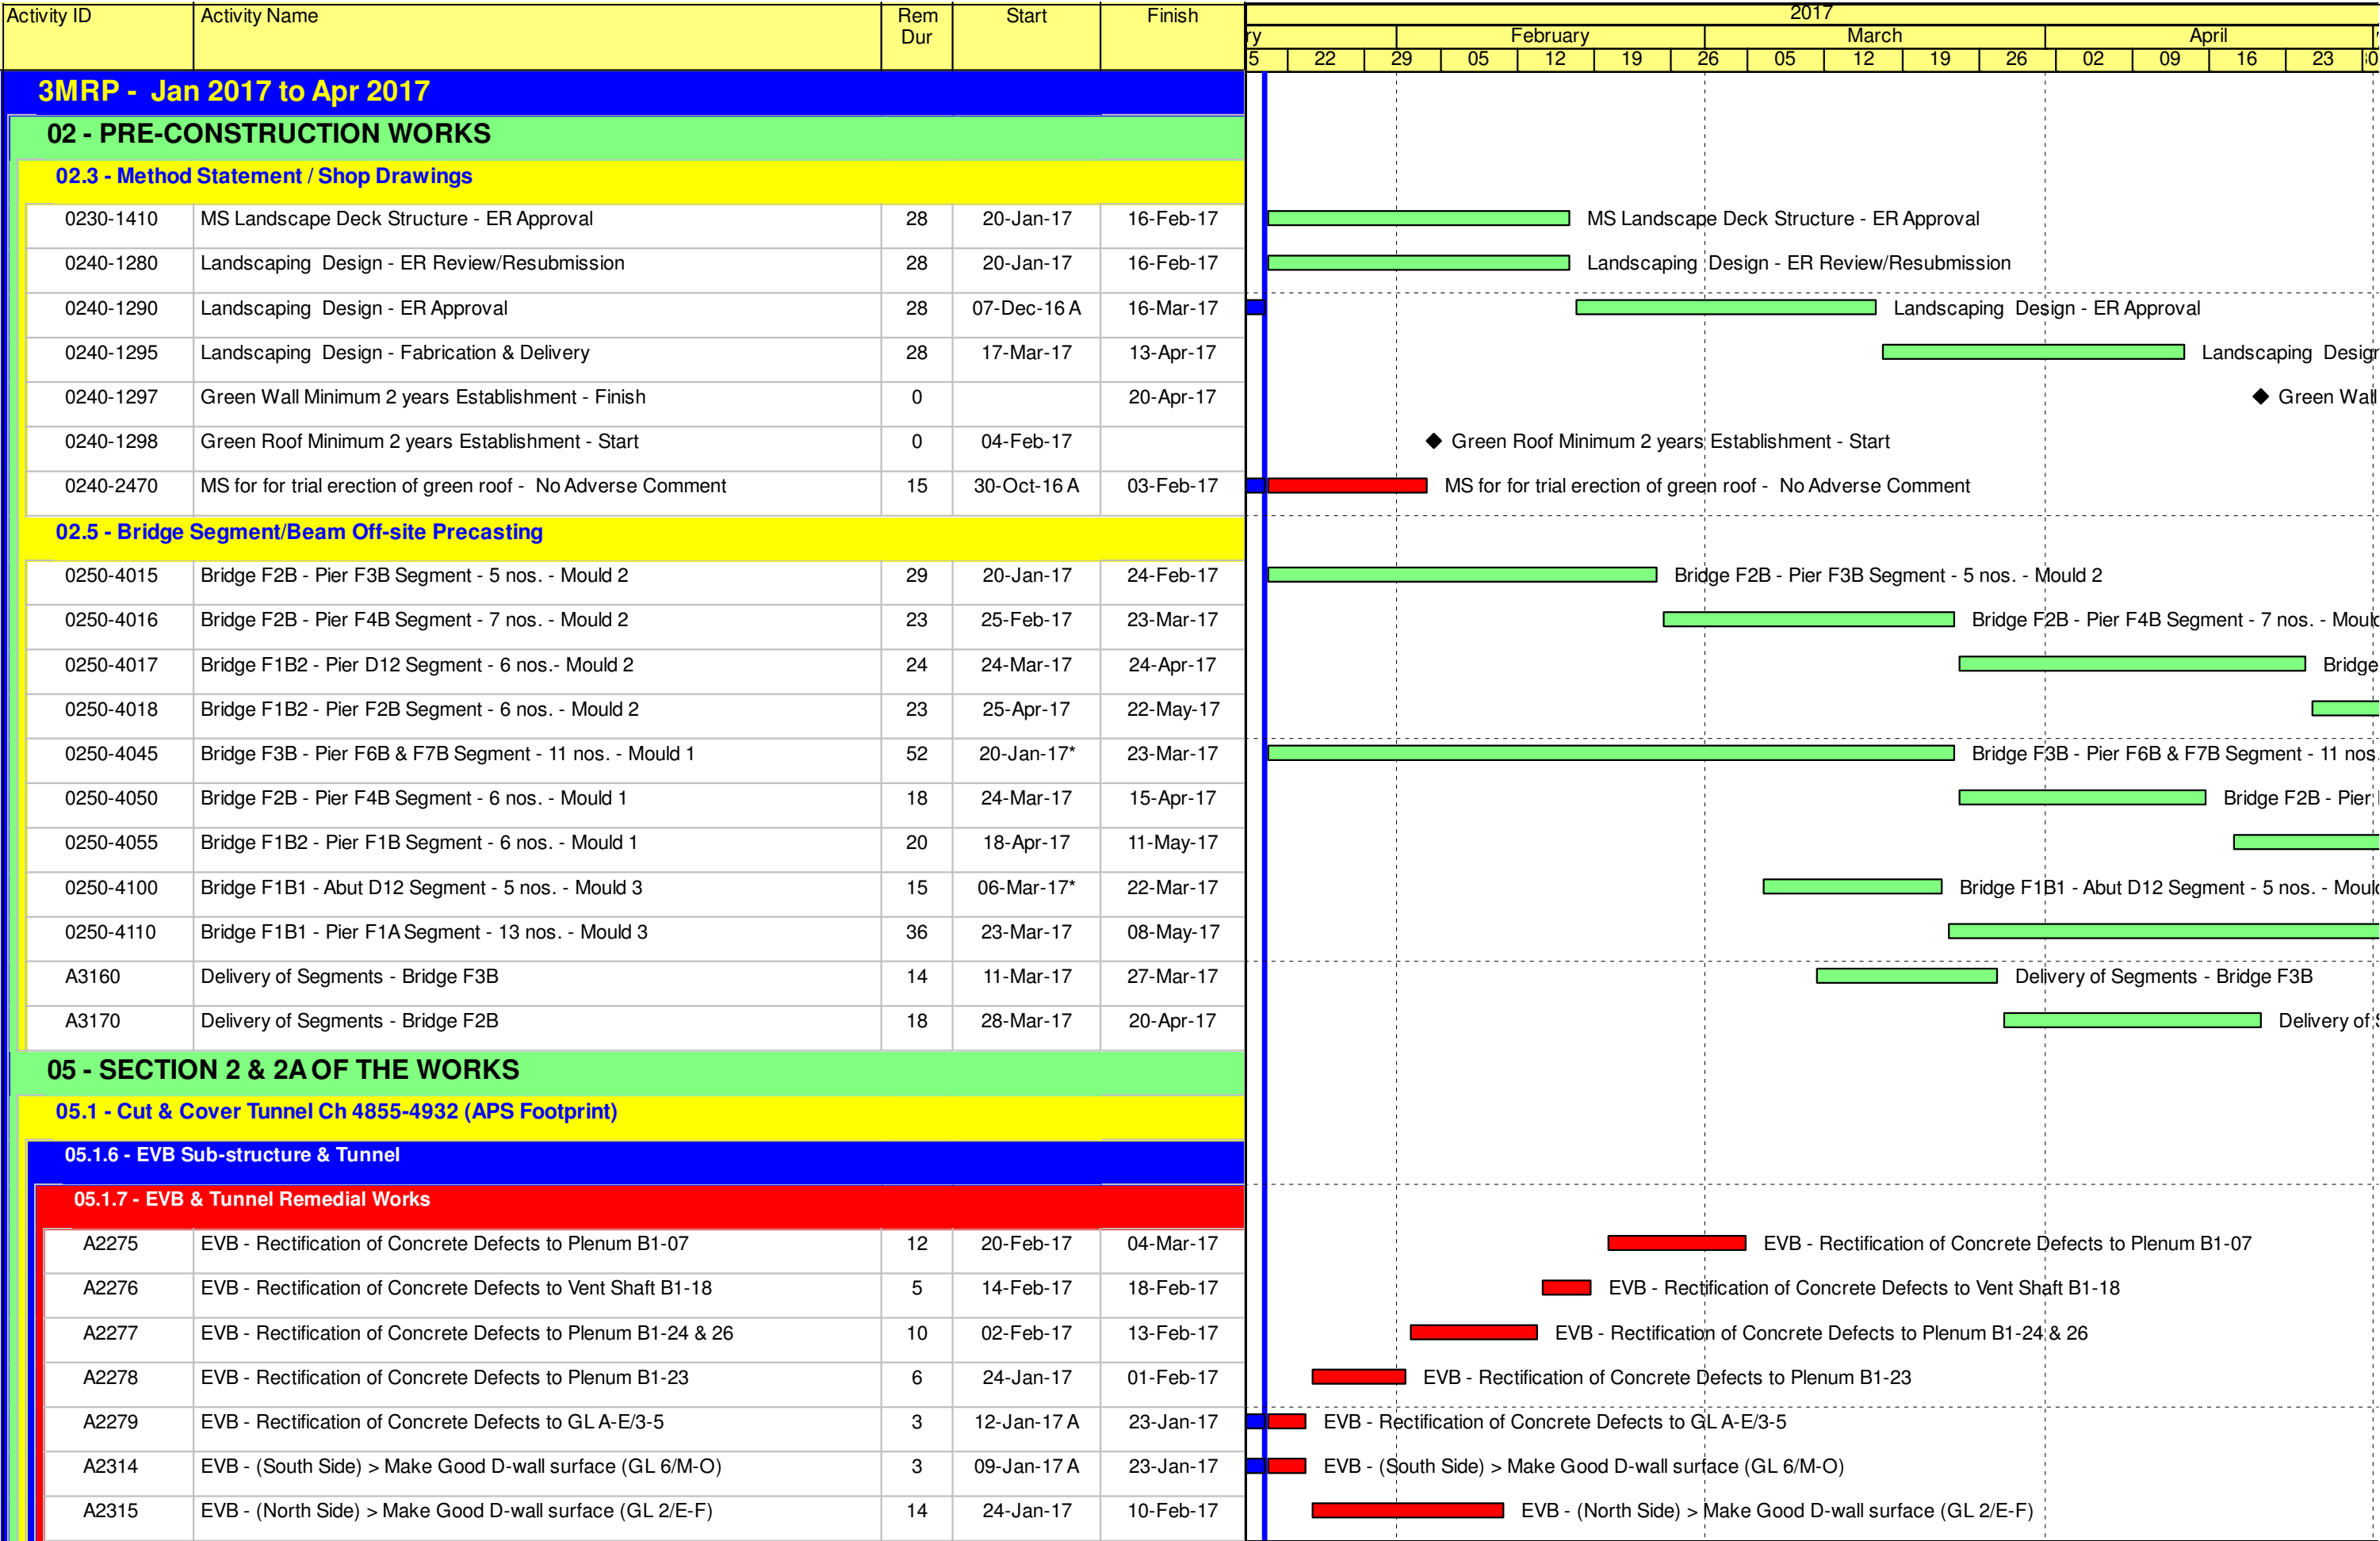

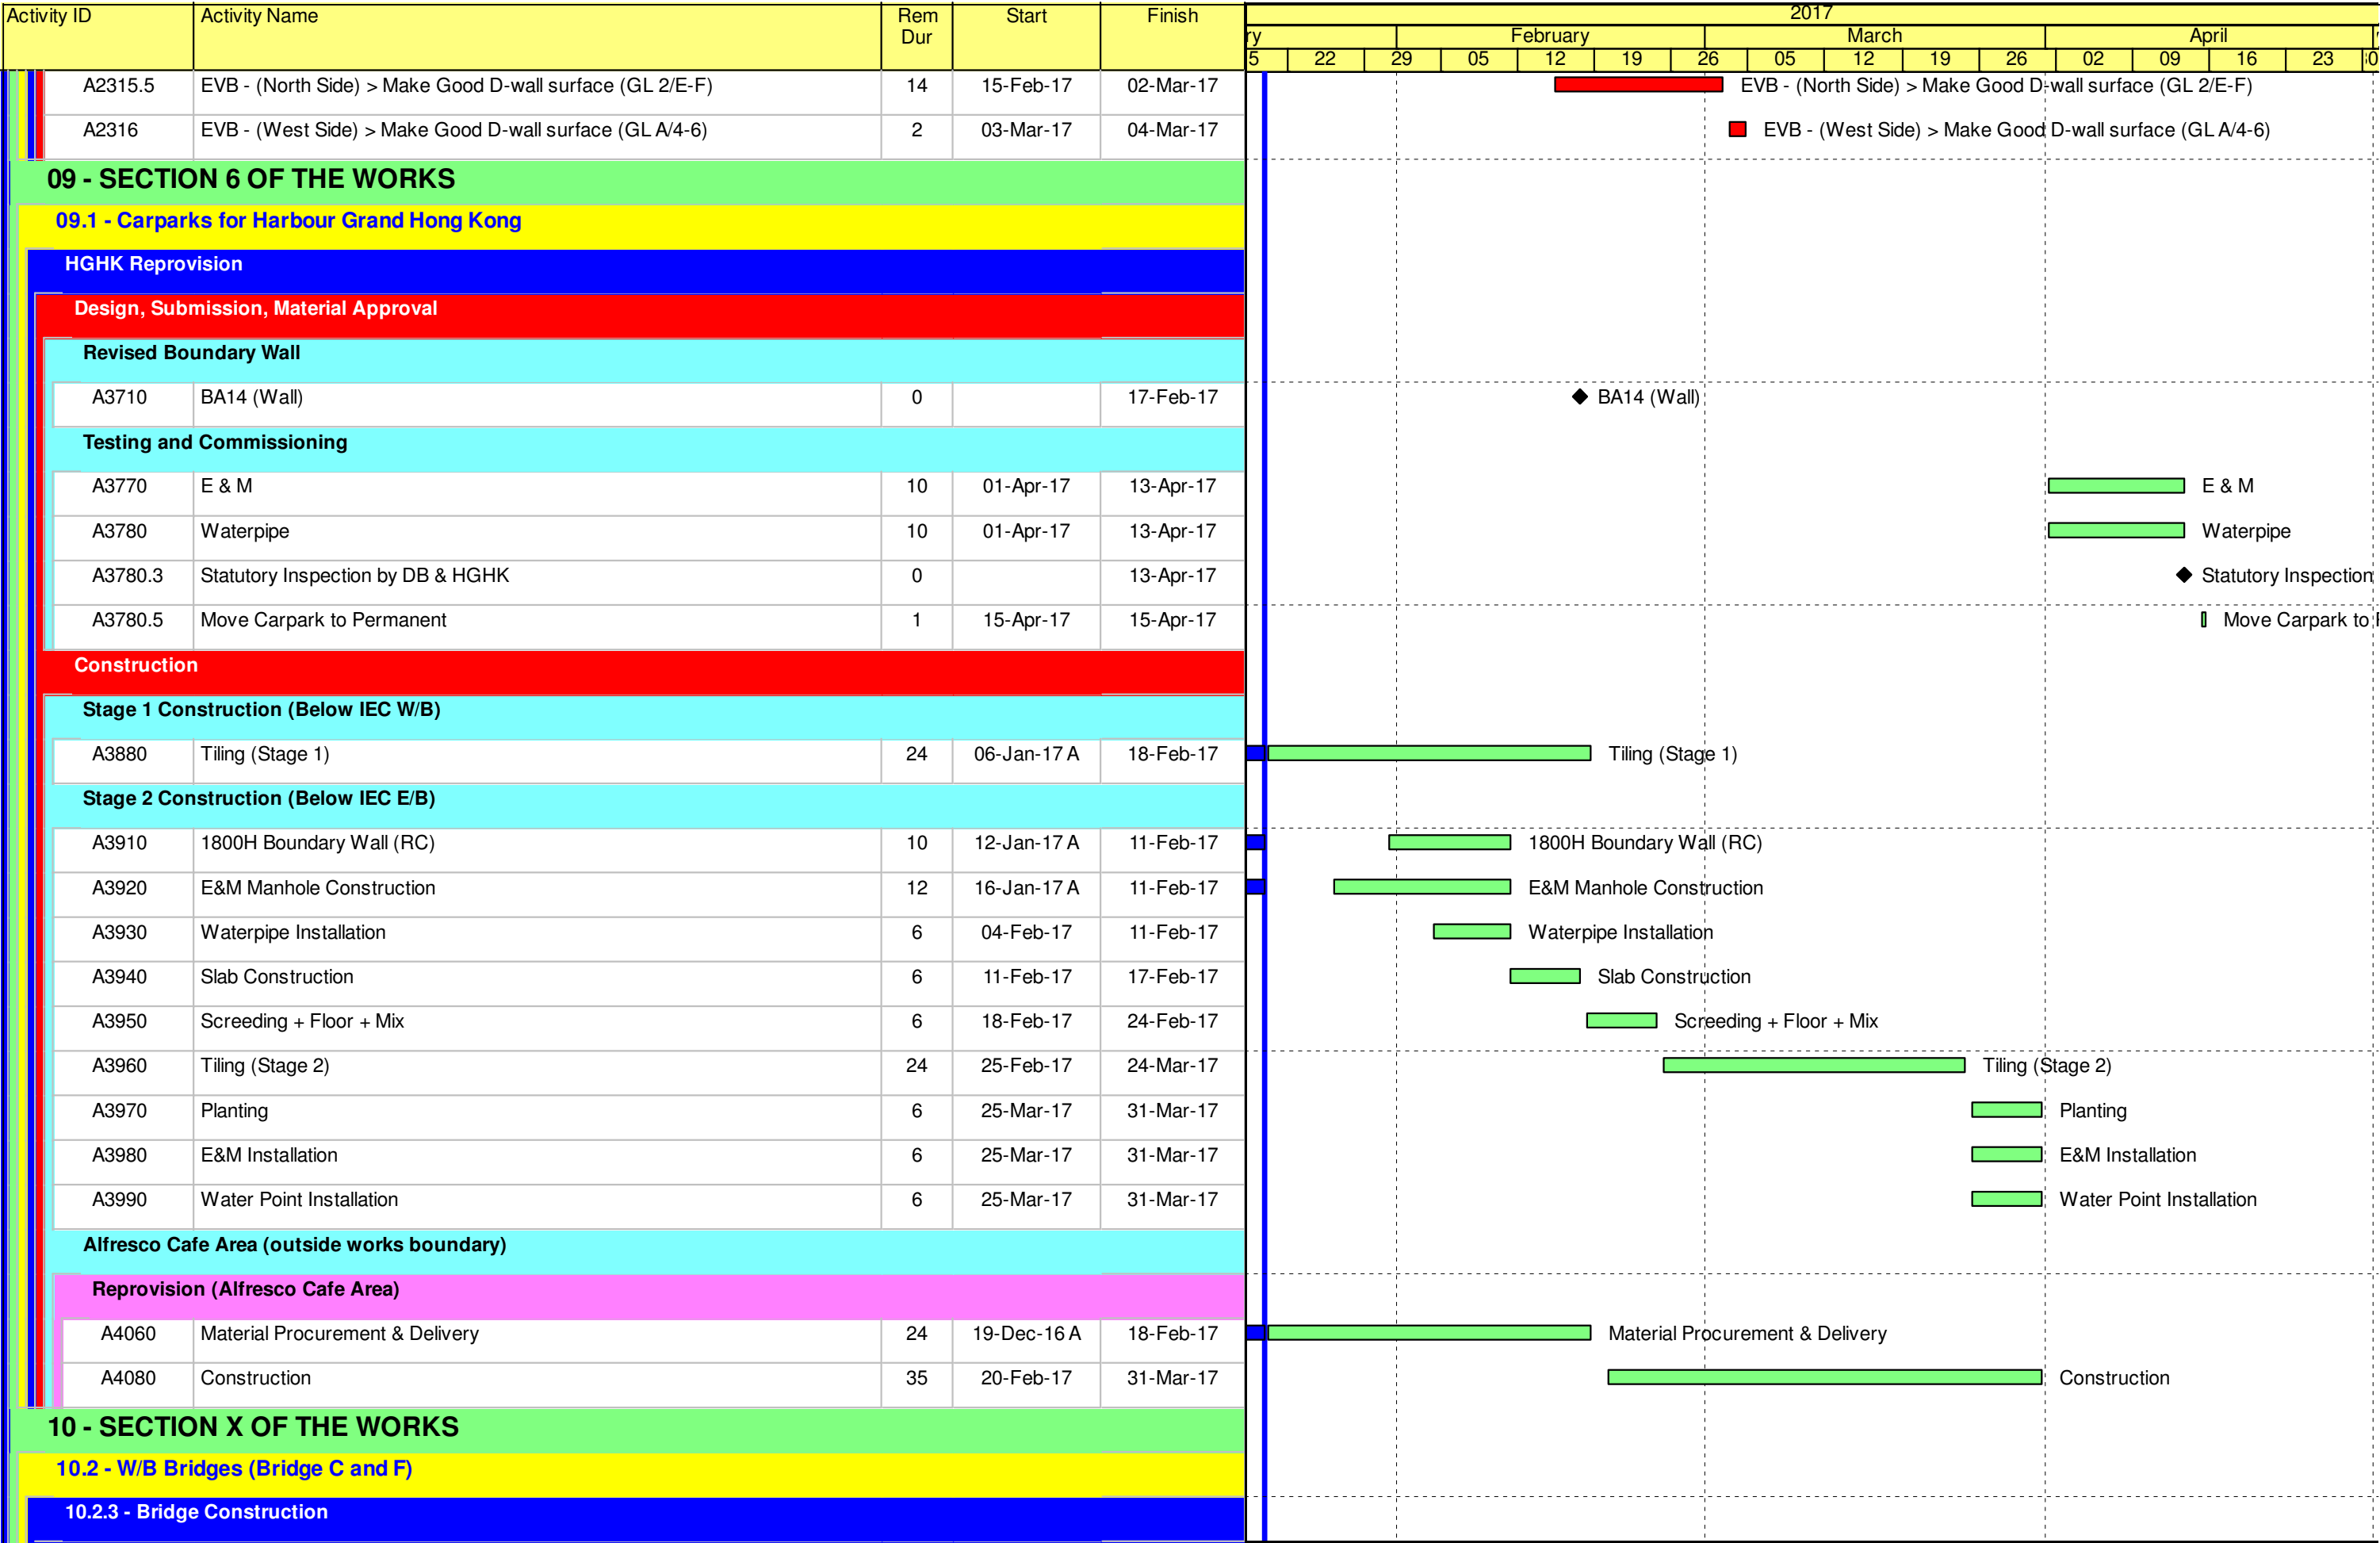

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Activity ID	Activity Name	Rem Dur	Start	Finish	2017																				
					January					February					March					April					
					5	12	19	26	31	5	12	19	26	31	5	12	19	26	31	5	12	19	26	31	
Bridge C1 Outstanding Works Between Bridge C1 & E	A4530	Pier 17 to 18 - Steel Mould Erection	2	20-Jan-17	21-Jan-17	Pier 17 to 18 - Steel Mould Erection																			
	A4550	Pier 17 to 18 - Concreting	1	23-Jan-17	23-Jan-17	Pier 17 to 18 - Concreting																			
	A4570	Pier 16 to 17 - Forwork Erection	2	20-Jan-17	21-Jan-17	Pier 16 to 17 - Forwork Erection																			
	A4590	Pier 16 to 17 - Rebar Bending	2	20-Jan-17	21-Jan-17	Pier 16 to 17 - Rebar Bending																			
	A4610	Pier 16 to 17 - Rebar Fixing	2	23-Jan-17	24-Jan-17	Pier 16 to 17 - Rebar Fixing																			
	A4630	Pier 16 to 17 - Steel Mould Erection	2	25-Jan-17	26-Jan-17	Pier 16 to 17 - Steel Mould Erection																			
	A4650	Pier 16 to 17 - Concreting	1	27-Jan-17	27-Jan-17	Pier 16 to 17 - Concreting																			
	A4670	Pier 15 to 16 - Forwork Erection	2	24-Jan-17	25-Jan-17	Pier 15 to 16 - Forwork Erection																			
	A4690	Pier 15 to 16 - Rebar Bending	2	24-Jan-17	25-Jan-17	Pier 15 to 16 - Rebar Bending																			
	A4710	Pier 15 to 16 - Rebar Fixing	2	26-Jan-17	27-Jan-17	Pier 15 to 16 - Rebar Fixing																			
	A4730	Pier 15 to 16 - Steel Mould Erection	2	31-Jan-17	01-Feb-17	Pier 15 to 16 - Steel Mould Erection																			
	A4750	Pier 15 to 16 - Concreting	1	02-Feb-17	02-Feb-17	Pier 15 to 16 - Concreting																			
	A4770	Temp Lighting (2 Nos)	2	07-Feb-17	08-Feb-17	Temp Lighting (2 Nos)																			
	A4790	Noise Barrier Const. Pier E1 to D1	12	20-Jan-17	04-Feb-17	Noise Barrier Const. Pier E1 to D1																			
	A4810	Noise Barrier Const. Pier 18 to 19	13	06-Feb-17	20-Feb-17	Noise Barrier Const. Pier 18 to 19																			
	A4830	Noise Barrier Const. Pier 17 to 18	12	21-Feb-17	06-Mar-17	Noise Barrier Const. Pier 17 to 18																			
	A4850	Paving & Road Marking	2	07-Mar-17	08-Mar-17	Paving & Road Marking																			
	10.3 - Middle Bridge (Bridge F)																								
10.3.1 - Pier Construction																									
Pier F1B2 to F4B																									
1031-1440	Existing P39/F4B Prepare C.J.	7	04-Apr-17	12-Apr-17											Existing P39/F4B Prepare C.J.										
1031-1460	Existing P39/F4B Construct Pier/Column	14	13-Apr-17	02-May-17																Existing P39/F4B Construct Pier/Column					
Pier F5B to F8B																									
1031-1520	Existing P40/F5B Prepare C.J.	6	21-Mar-17	27-Mar-17											Existing P40/F5B Prepare C.J.										
1031-1540	Existing P40/F5B Construct Pier/Column	14	28-Mar-17	13-Apr-17											Existing P40/F5B Construct Pier/Column										
1031-1600	Existing P41/F6B Prepare C.J.	6	07-Mar-17	13-Mar-17											Existing P41/F6B Prepare C.J.										
1031-1620	Existing P41/F6B Construct Pier/Column	14	14-Mar-17	29-Mar-17											Existing P41/F6B Construct Pier/Column										
1031-1640	Existing P41/F6B Construct Crosshead	18	30-Mar-17	22-Apr-17											Existing P41/F6B Construct Crosshead										
1031-1680	Existing P42/F7B Prepare C.J.	6	21-Feb-17	27-Feb-17						Existing P42/F7B Prepare C.J.															
1031-1700	Existing P42/F7B Construct Pier/Column	14	28-Feb-17	15-Mar-17						Existing P42/F7B Construct Pier/Column															
1031-1720	Existing P42/F7B Construct Crosshead	18	16-Mar-17	06-Apr-17											Existing P42/F7B Construct Crosshead										

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Activity ID		Activity Name	Rem Dur	Start	Finish
2017 JanuaryFebruaryMarchApril					
A3240	Demolish Four(4nos) Beams at Pier 42-41 - by LG-BM	2	08-Feb-17	09-Feb-17	Demolish Four(4nos) Beams at Pier 42-41 - by LG-BM
A3250	Demolish Pier + Steel Support at Pier 42	9	10-Feb-17	20-Feb-17	Demolish Pier + Steel Support at Pier 42
A3260	Launch LG-BM to next Bridge Span	1	21-Feb-17	21-Feb-17	Launch LG-BM to next Bridge Span
A3270	Demolish Four(4nos) Beams at Pier 41-40 - by LG-BM	2	22-Feb-17	23-Feb-17	Demolish Four(4nos) Beams at Pier 41-40 - by LG-BM
A3280	Demolish Pier + Steel Support at Pier 41	9	24-Feb-17	06-Mar-17	Demolish Pier + Steel Support at Pier 41
A3290	Launch LG-BM to next Bridge Span	1	07-Mar-17	07-Mar-17	Launch LG-BM to next Bridge Span
A3300	Demolish Four(4nos) Beams at Pier 40-39 - by LG-BM	2	08-Mar-17	09-Mar-17	Demolish Four(4nos) Beams at Pier 40-39 - by LG-BM
A3310	Demolish Pier + Steel Support at Pier 40	9	10-Mar-17	20-Mar-17	Demolish Pier + Steel Support at Pier 40
A3320	Launch LG-BM to next Bridge Span	1	21-Mar-17	21-Mar-17	Launch LG-BM to next Bridge Span
A3330	Demolish Four(4nos) Beams at Pier 39-38 - by LG-BM	2	22-Mar-17	23-Mar-17	Demolish Four(4nos) Beams at Pier 39-38 - by LG-BM
A3340	Demolish Pier + Steel Support at Pier 39	9	24-Mar-17	03-Apr-17	Demolish Pier + Steel Support at Pier 39
A3350	Launch LG-BM to next Bridge Span	1	04-Apr-17	04-Apr-17	Launch LG-BM to next Bridge Span
A3360	Demolish Four(4nos) Beams at Pier 38-37 - by LG-BM	2	06-Apr-17	07-Apr-17	Demolish Four(4nos) Beams at Pier 38-37 - by LG-BM
A3370	Demolish Pier + Steel Support at Pier 38	9	08-Apr-17	20-Apr-17	Demolish Pier + Steel Support at Pier 38
10.5 - Temporary Bridge					
10.5.2 - Temporary Bridge 'TB'					
1052-1260	TB > Demolition of Temporary Bridge "TB"	27	25-Mar-17	28-Apr-17	Demolition of Temporary Bridge "TB"
A4140	TTA Implementation prior to Demolition	14	09-Mar-17	24-Mar-17	TTA Implementation prior to Demolition
10.6 - Tunnel Approach Ramp					
10.6.1 - Approach Ramp (Excluding Portion IIB)					
Piling Works					
1061-3490	Moving Temp Car Park to Permanent Car Park Completed	0		18-Apr-17	Moving Temp Car Park to Permanent Car Park Completed
1061-3495	Modify Contractor's Temp Site Office	28	13-Mar-17	18-Apr-17	Modify Contractor's Temp Site Office
1061-3500	Pre Bored H-Pile > Pile Ramp - BM03 A	4	18-Apr-17	21-Apr-17	Pre Bored H-Pile > Pile Ramp - BM03 A
Excavation & ELS Works					
1061-4901.1	Sheet Piling Works (WF2>B1:46m@1.5m/d) (including Re-boring for remedial works)	27	10-Oct-16 A	22-Feb-17	Sheet Piling Works (WF2>B1:46m@1.5m/d) (including Re-boring for remedial works)
1061-4901.2	Sheet Piling Works (WF1>B3:19m@1.5m/d) (including Re-boring for remedial works)	41	12-Jul-16 A	10-Mar-17	Sheet Piling Works (WF1>B3:19m@1.5m/d) (including Re-boring for remedial works)
1061-4910	Advance Sheet Piling Works + Pre-drilling in Phase 2 - Cul de sac Area (30m)	14	11-Mar-17	27-Mar-17	Advance Sheet Piling Works + Pre-drilling in Phase 2 - Cul de sac Area (30m)
1061-4915	Tam Grouting	43	14-Sep-16 A	13-Mar-17	Tam Grouting
1061-5040	Recharge Well Installation (8Nos)	0	22-Dec-16 A	10-Jan-17 A	Recharge Well Installation (8Nos)
1061-5060	Dewatering Well Installation (14Nos)	18	11-Jan-17 A	11-Feb-17	Dewatering Well Installation (14Nos)
1061-5080	Observation Well Installation (10Nos)	15	13-Feb-17	01-Mar-17	Observation Well Installation (10Nos)

Activity ID	Activity Name	Rem Dur	Start	Finish	2017																
					January			February				March				April					
					5	22	29	05	12	19	26	05	12	19	26	02	09	16	23	30	
10.6 - Section 10.6 - Pumping Test	1061-5100	Pumping Test	9	14-Mar-17	23-Mar-17																
	1061-5120	Complete Pump Test	0		23-Mar-17																
	1061-5140	Ch 5285 - 5331 > Excav from Ex. Lvl down to 2.5mPD (Ch 5285 - 5331 w/ open cut)	18	15-Aug-16 A	11-Feb-17																
	1061-5160	Ch 5234 - 5285 > Excav from Ex. Lvl down to 2.5mPD	20	13-Feb-17	07-Mar-17																
	1061-5180	Ch 5234 - 5285 > Install 1st Layer of Strut & Waling	9	11-Mar-17	21-Mar-17																
	1061-5200	Ch 5234 - 5285 > Excav from 2.5mPD to 1m Below 2nd Layer of Struts	16	24-Mar-17	12-Apr-17																
	1061-5220	Ch 5234 - 5285 > Install 2nd Layer of Strut & Waling	9	13-Apr-17	25-Apr-17																
	1061-5240	Ch 5234 - 5285 > Excav to FEL	13	26-Apr-17	11-May-17																
Structure Works																					
1061-5260	Bay 1 - Ch 5322 - 5331 > Base Slab - Blinding Layer	1	13-Apr-17	13-Apr-17																	
1061-5280	Bay 1 - Ch 5322 - 5331 > Base Slab - Water Proofing Membrane	2	15-Apr-17	18-Apr-17																	
1061-5300	Bay 1 - Ch 5322 - 5331 > Base Slab - Rebar Fixing	5	19-Apr-17	24-Apr-17																	
10.7 - Section X - Miscellaneous Works																					
10.7.3 - Open Area																					
1073-1010	Open Area - Pedestrian Parapet -Ch570.40 to Ch540.00	14	17-Feb-17*	04-Mar-17																	
1073-1010.3	Open Area - Pedestrian Parapet - Ch540.00 to Ch520.00	14	06-Mar-17	21-Mar-17																	
1073-1010.5	Open Area - Pedestrian Parapet - Ch0.00 - Ch40.00	18	22-Mar-17	12-Apr-17																	
1073-1010.7	Open Area - Pedestrian Parapet - Ch40.00 - 80.00	18	13-Apr-17	06-May-17																	
11 - SECTION 11 OF THE WORKS																					
11.1 - Portion XIIA - Stage 1																					
11.1.1 - Along Watson Road - Waterwork & Roadworks (Portion XIIA)																					
1110-2820	Permanent Cul-de Sac - Constr. of drainage	25	06-Feb-17*	06-Mar-17																	
1110-2830	Permanent Cul-de Sac - Constr. of watermains	25	17-Feb-17	17-Mar-17																	
1110-2840	Permanent Cul-de Sac - Constr. of public lighting & telecom (conduits & drawpits)	25	01-Mar-17	29-Mar-17																	
1110-2850	Permanent Cul-de Sac - Constr. of (kerbs & pavements)	25	30-Mar-17	02-May-17																	
11.1.3 - Along Tsing Fung St. - TCSS cable ducting (Portion XIIA)																					
1110-2930	TCSS cable ducting along Tsing Fung St	36	06-Mar-17*	19-Apr-17																	

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Milestone

Activity ID	Activity Name	Rem Dur	Start	Finish	2017															
									May				June				July			
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23	
3MRP - Apr 2017 to Jul 2017																				
02 - PRE-CONSTRUCTION WORKS																				
02.3 - Method Statement / Shop Drawings																				
0230-1410	MS Landscape Deck Structure - ER Approval	28	20-Apr-17	17-May-17	MS Landscape Deck Structure - ER Approval															
0240-1280	Landscaping Design - ER Review/Resubmission	28	20-Apr-17	17-May-17	Landscaping Design - ER Review/Resubmission															
0240-1290	Landscaping Design - ER Approval	28	07-Dec-16 A	14-Jun-17	Landscaping Design - ER Approval															
0240-1295	Landscaping Design - Fabrication & Delivery	28	15-Jun-17	12-Jul-17	Landscaping Design -															
0240-1298	Green Roof Minimum 2 years Establishment - Start	0	05-May-17		◆ Green Roof Minimum 2 years Establishment - Start															
0240-2470	MS for for trial erection of green roof - No Adverse Comment	15	30-Oct-16 A	04-May-17	MS for for trial erection of green roof - No Adverse Comment															
02.5 - Bridge Segment/Beam Off-site Precasting																				
0250-4017	Bridge F1B2 - Pier D12 Segment - 6 nos.- Mould 2	4	24-Mar-17 A	24-Apr-17	Bridge F1B2 - Pier D12 Segment - 6 nos.- Mould 2															
0250-4018	Bridge F1B2 - Pier F2B Segment - 6 nos. - Mould 2	23	25-Apr-17	22-May-17	Bridge F1B2 - Pier F2B Segment - 6 nos. - Mould 2															
0250-4019	Bridge F1B2 - Pier F3B Segment - 5 nos. - Mould 2	14	23-May-17	08-Jun-17	Bridge F1B2 - Pier F3B Segment - 5 nos. - Mould 2															
0250-4055	Bridge F1B2 - Pier F1B Segment - 6 nos. - Mould 1	18	18-Apr-17 A	11-May-17	Bridge F1B2 - Pier F1B Segment - 6 nos. - Mould 1															
0250-4057	Bridge F1B2 - Abut D12 Segment - 6 nos. - Mould 1	18	12-May-17	02-Jun-17	Bridge F1B2 - Abut D12 Segment - 6 nos. - Mould 1															
0250-4059	Bridge F1B2 - Pier F2B Segment - 5 nos. - Mould 1	13	03-Jun-17	17-Jun-17	Bridge F1B2 - Pier F2B Segment - 5 nos. - Mould 1															
0250-4110	Bridge F1B1 - Pier F1A Segment - 13 nos. - Mould 3	15	23-Mar-17 A	08-May-17	Bridge F1B1 - Pier F1A Segment - 13 nos. - Mould 3															
0250-4115	Bridge F1B1 - Pier F2A Segment - 11nos. - Mould 3	32	09-May-17	15-Jun-17	Bridge F1B1 - Pier F2A Segment - 11nos. - Mould 3															
0250-4120	Bridge F1B1 - Pier F3A Segment - 6 nos. - Mould 3	17	16-Jun-17	06-Jul-17	Bridge F1B1 - Pier F3A Segment															
A3170	Delivery of Segments - Bridge F2B	3	28-Mar-17 A	22-Apr-17	Delivery of Segments - Bridge F2B															
A3180	Delivery of Segments - Bridge F1B2	18	01-Jun-17	21-Jun-17	Delivery of Segments - Bridge F1B2															
A3190	Delivery of Segments - Bridge F1B1	18	16-Jun-17	07-Jul-17	Delivery of Segments - Bridge															
03 - PRELIMINARY WORKS																				
03.3 - Interface Works																				
FEHD Permanent Depot																				
0330-1020	Breaking-up Slabs for Pole Installations (25Nos)	13	25-Apr-17	10-May-17	Breaking-up Slabs for Pole Installations (25Nos)															
0330-1023	Drilling & Base Plate Installation (M25 - 104Nos)	21	27-Apr-17	22-May-17	Drilling & Base Plate Installation (M25 - 104Nos)															
0330-1025	Installation of Pole (25Nos)	13	11-May-17	25-May-17	Installation of Pole (25Nos)															
0330-1027	Installtion of Beams (77Nos)	26	12-May-17	12-Jun-17	Installtion of Beams (77Nos)															
0330-1029	Installation of Bondek (Soffit Formworks)	12	05-Jun-17	17-Jun-17	Installation of Bondek (Soffit Formworks)															
0330-1031	Rebar Fixing	7	12-Jun-17	19-Jun-17	Rebar Fixing															
0330-1033	Edges Formworks	2	17-Jun-17	19-Jun-17	Edges Formworks															
0330-1035	Concreting of Deck	3	20-Jun-17	22-Jun-17	Concreting of Deck															
0330-1037	Breaking Slab for Brace Footing Construction (3Nos)	9	25-Apr-17	05-May-17	Breaking Slab for Brace Footing Construction (3Nos)															
0330-1039	Excavation for Brace Footing	3	06-May-17	09-May-17	Excavation for Brace Footing															

Activity ID	Activity Name	Rem Dur	Start	Finish	2017																
					May				June				July								
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23		
	0330-1043	Construction of Brace Footing	5	10-May-17	15-May-17	Construction of Brace Footing															
	0330-1047	Erection of Bracing Beam (3Nos)	3	16-May-17	18-May-17	Erection of Bracing Beam (3Nos)															
	0330-1049	Touch-up Painting	12	22-May-17	05-Jun-17	Touch-up Painting															
	0330-1051	Waterproofing & Slab Reinstatement	7	19-May-17	26-May-17	Waterproofing & Slab Reinstatement															
	0330-1053	Breaking Slab & Excavate for Lamp Pole Footing	7	11-May-17	18-May-17	Breaking Slab & Excavate for Lamp Pole Footing															
	0330-1055	Construction of Lamp Pole Footing (12Nos)	21	12-May-17	06-Jun-17	Construction of Lamp Pole Footing (12Nos)															
	0330-1057	Drilling for Lamp Pole at Existing Slab (8Nos Poles; M16-64Nos)	8	18-May-17	26-May-17	Drilling for Lamp Pole at Existing Slab (8Nos Poles; M16-64Nos)															
	0330-1059	Installation of Lamp Pole (total 20Nos)	14	23-May-17	08-Jun-17	Installation of Lamp Pole (total 20Nos)															
	0330-1061	Breaking Existing Slab for Cross Road Ducting (Approx 300m)	18	24-May-17	14-Jun-17	Breaking Existing Slab for Cross Road Ducting (Approx 300m)															
	0330-1063	Laying Duct	5	15-Jun-17	20-Jun-17	Laying Duct															
	0330-1065	Cabling Works	9	21-Jun-17	30-Jun-17	Cabling Works															
	0330-1067	Slab Reinstatement	8	03-Jul-17	11-Jul-17	Slab Reinstatement															
	0330-1069	Drilling for Post Anchor Bolts for Facility Area 5 & 10 (172Nos)	9	25-Apr-17	05-May-17	Drilling for Post Anchor Bolts for Facility Area 5 & 10 (172Nos)															
	0330-1071	Installation of Post (43Nos)	9	28-Apr-17	09-May-17	Installation of Post (43Nos)															
	0330-1073	Construction of Steel Roof	9	04-May-17	13-May-17	Construction of Steel Roof															
	0330-1075	Sprinkler System Installation	10	09-May-17	19-May-17	Sprinkler System Installation															
	0330-1077	T & C of Sprinkler System	6	20-May-17	26-May-17	T & C of Sprinkler System															
	0330-1079	Drilling for Post Anchor Bolts for Facility Area 6, 8 & 9 (292Nos)	15	08-May-17	24-May-17	Drilling for Post Anchor Bolts for Facility Area 6, 8 & 9 (292Nos)															
	0330-1081	Installation of Post (73Nos)	15	12-May-17	29-May-17	Installation of Post (73Nos)															
	0330-1083	Breaking Slab & Connection to Existing Draw Pits	14	11-May-17	26-May-17	Breaking Slab & Connection to Existing Draw Pits															
0330-1085	Breaking Slab & Excavate for Draw Pits (17Nos)	15	27-May-17	14-Jun-17	Breaking Slab & Excavate for Draw Pits (17Nos)																
0330-1087	Construction of Draw Pits (3 Gang @ 6d/Pit)	36	02-Jun-17	14-Jul-17	Construction of Draw Pits (3 Gang @ 6d/Pit)																
0330-1089	BackFilling Works around Draw Pits	7	15-Jul-17	22-Jul-17	BackFilling Works around Draw Pits																
0330-1093	Construction of U-Channels	33	02-Jun-17	11-Jul-17	Construction of U-Channels																
05 - SECTION 2 & 2A OF THE WORKS																					
05.1 - Cut & Cover Tunnel Ch 4855-4932 (APS Footprint)																					
05.1.6 - EVB Sub-structure & Tunnel																					
05.1.7 - EVB & Tunnel Remedial Works																					
A2273	EVB - Rectification of Concrete Defects at Stairs 01 & 6	6	20-Dec-16 A	26-Apr-17	EVB - Rectification of Concrete Defects at Stairs 01 & 6																
A4870	APS - B2M Southern Wall	6	11-Mar-17 A	26-Apr-17	APS - B2M Southern Wall																
09 - SECTION 6 OF THE WORKS																					
09.1 - Carparks for Harbour Grand Hong Kong																					
HG HK Reprovision																					
Design, Submission, Material Approval																					
Testing and Commissioning																					

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work


Critical Remaining Work

Milestone

Contract HY/2009/19

Three Months Rolling Programme (20 April 2017 to 19 July 2017)

Page 2 of 9

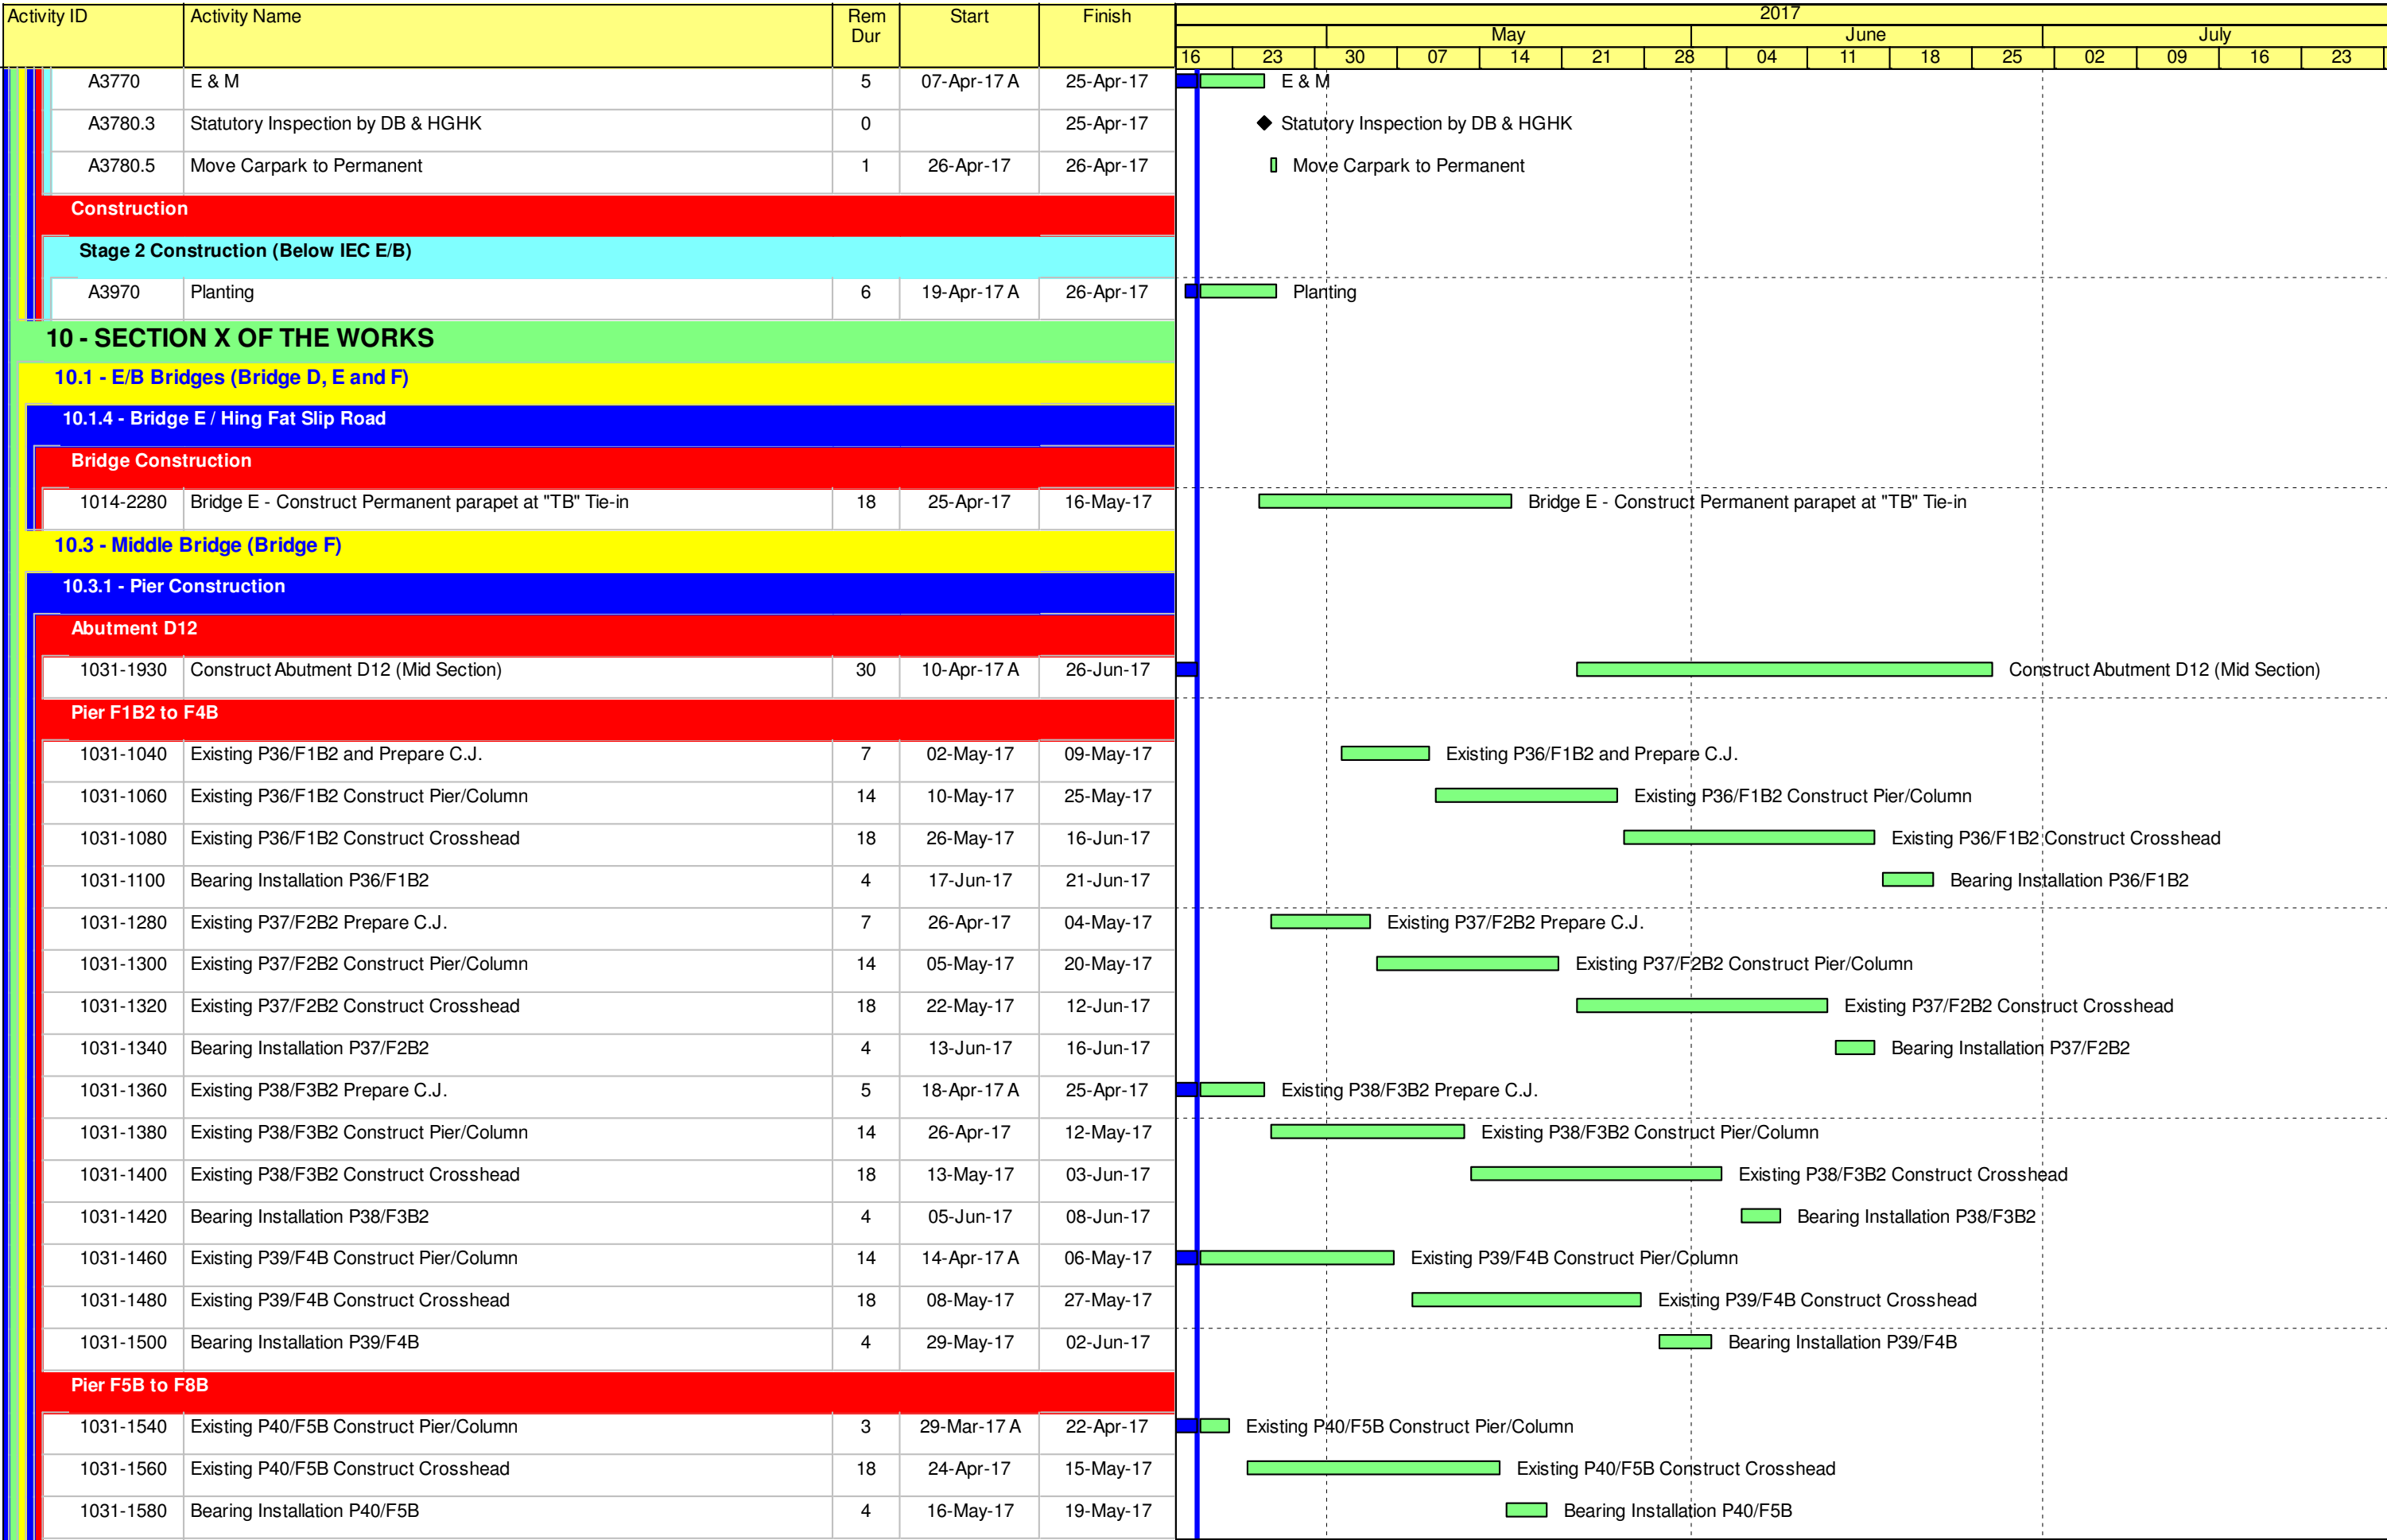

█

 Remaining Level of Effort

█

 Remaining Work

█

 Actual Level of Effort

█

 Critical Remaining Work

█

 Actual Work

◆

 Milestone

◆

 Milestone

Contract HY/2009/19

Three Months Rolling Programme (20 April 2017 to 19 July 2017)

Activity ID	Activity Name	Rem Dur	Start	Finish	2017															
					May						June				July					
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23	
1031-1640	Existing P41/F6B Construct Crosshead	13	10-Apr-17 A	05-May-17	Existing P41/F6B Construct Crosshead															
1031-1660	Bearing Installation P41/F6B	4	06-May-17	10-May-17	Bearing Installation P41/F6B															
1031-1720	Existing P42/F7B Construct Crosshead	8	24-Mar-17 A	28-Apr-17	Existing P42/F7B Construct Crosshead															
1031-1740	Bearing Installation P42/F7B	4	29-Apr-17	04-May-17	Bearing Installation P42/F7B															
1031-1800	Existing P43/F8B Construct Crosshead	3	17-Mar-17 A	22-Apr-17	Existing P43/F8B Construct Crosshead															
1031-1820	Upstand Wall + Bearing Installation P43/F8B	11	24-Apr-17	06-May-17	Upstand Wall + Bearing Installation P43/F8B															
10.3.2 - Bridge Construction																				
Bridge F3B																				
1032-1840	LG-A Launching - Engage FL at F7B/Pier42	2	08-May-17	09-May-17	LG-A Launching - Engage FL at F7B/Pier42															
1032-1860	P42/F7B - Install Pier Segment - Place Pier Segment	1	10-May-17	10-May-17	P42/F7B - Install Pier Segment - Place Pier Segment															
1032-1880	P42/F7B - Install Pier Segment - Adjust Segment Level and Location	2	11-May-17	12-May-17	P42/F7B - Install Pier Segment - Adjust Segment Level and Location															
1032-1900	P42/F7B - Install Pier Segment - Grouting the Bearing Upper Plinth	2	13-May-17	15-May-17	P42/F7B - Install Pier Segment - Grouting the Bearing Upper Plinth															
1032-1920	P42/F7B - Install Pier Segment - Stressing Nailing	2	16-May-17	17-May-17	P42/F7B - Install Pier Segment - Stressing Nailing															
1032-1940	LG-A Launching - Install MS at P42/F7B	1	18-May-17	18-May-17	LG-A Launching - Install MS at P42/F7B															
1032-1960	LG-A Launching - Deactivate the MS at F9B/Pier44 and Engage FL at P41/F6B	2	19-May-17	20-May-17	LG-A Launching - Deactivate the MS at F9B/Pier44 and Engage FL at P41/F6B															
1032-1980	P41/F6B - Install Pier Segment - Place Pier Segment	1	22-May-17	22-May-17	P41/F6B - Install Pier Segment - Place Pier Segment															
1032-2000	P41/F6B - Install Pier Segment - Adjust Segment Level and Location	2	23-May-17	24-May-17	P41/F6B - Install Pier Segment - Adjust Segment Level and Location															
1032-2020	P41/F6B - Install Pier Segment - Grouting the Bearing Upper Plinth	2	25-May-17	26-May-17	P41/F6B - Install Pier Segment - Grouting the Bearing Upper Plinth															
1032-2040	P41/F6B - Install Pier Segment - Stressing Nailing	2	27-May-17	29-May-17	P41/F6B - Install Pier Segment - Stressing Nailing															
1032-2060	P41/F6B - Install Pier Segment - Install MS at F6B/Pier41	1	31-May-17	31-May-17	P41/F6B - Install Pier Segment - Install MS at F6B/Pier41															
1032-2080	P42/F7B - T Span Erection (5 pairs)	4	01-Jun-17	05-Jun-17	P42/F7B - T Span Erection (5 pairs)															
1032-2100	P43/F8B(MJ Left) - End Span Erection - Hanging Segments	3	06-Jun-17	08-Jun-17	P43/F8B(MJ Left) - End Span Erection - Hanging Segments															
1032-2120	P43/F8B(MJ Left) - End Span Erection - Erect Segments	1	09-Jun-17	09-Jun-17	P43/F8B(MJ Left) - End Span Erection - Erect Segments															
1032-2140	P43/F8B(MJ Left) - End Span Erection - Stitching	2	10-Jun-17	12-Jun-17	P43/F8B(MJ Left) - End Span Erection - Stitching															
1032-2160	P43/F8B(MJ Left) - End Span Erection - Formwork Fixing for and Grouting for Bearing	2	10-Jun-17	12-Jun-17	P43/F8B(MJ Left) - End Span Erection - Formwork Fixing for and Grouting for Bearing															
1032-2180	P43/F8B(MJ Left) - End Span Erection - Prestress Span Tendons	2	13-Jun-17	14-Jun-17	P43/F8B(MJ Left) - End Span Erection - Prestress Span Tendons															
1032-2200	P43/F8B(MJ Left) - End Span Erection - Remove Hanger Bar & Hanger Beam & Stitching Formwork	1	15-Jun-17	15-Jun-17	P43/F8B(MJ Left) - End Span Erection - Remove Hanger Bar & Hanger Beam & Stitching Formwork															
1032-2220	LG-A Launching - Deactivate the MS at F8B/Pier43 and Engage FL at P40/F5B	2	16-Jun-17	17-Jun-17	LG-A Launching - Deactivate the MS at F8B/Pier43 and Engage FL at P40/F5B															
1032-2240	P41/F6B - T Span Erection (6 pairs)	4	19-Jun-17	22-Jun-17	P41/F6B - T Span Erection (6 pairs)															
1032-2260	P40/F5B - Install Pier Segment - Place Pier Segment (2nos.)	2	19-Jun-17	20-Jun-17	P40/F5B - Install Pier Segment - Place Pier Segment (2nos.)															
1032-2280	P40/F5B - Install Pier Segment - Adjust Segment Level and Location	3	21-Jun-17	23-Jun-17	P40/F5B - Install Pier Segment - Adjust Segment Level and Location															
1032-2300	P40/F5B - Install Pier Segment - Install the Tie & Packing System	2	24-Jun-17	26-Jun-17	P40/F5B - Install Pier Segment - Install the Tie & Packing System															
1032-2320	P40/F5B - Install Pier Segment - Install MS at P40/F5B (Right) and Engage FL at P39/F4B	2	27-Jun-17	28-Jun-17	P40/F5B - Install Pier Segment - Install MS at P40/F5B (Right) and Engage FL at P39/F4B															
1032-2340	P40/F5B(MJ Right) - End Span Erection - Hanging Segments	2	29-Jun-17	30-Jun-17	P40/F5B(MJ Right) - End Span Erection - Hanging Segments															
1032-2360	P40/F5B(MJ Right) - End Span Erection - Erect Segments	1	03-Jul-17	03-Jul-17	P40/F5B(MJ Right) - End Span Erection - Erect Segments															

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Contract HY/2009/19

Three Months Rolling Programme (20 April 2017 to 19 July 2017)

Page 4 of 9

Activity ID	Activity Name	Rem Dur	Start	Finish	2017															
									May				June				July			
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23	
1032-2380	P40/F5B(MJ Right) - End Span Erection - Stitching	2	04-Jul-17	05-Jul-17													P40/F5B(MJ Right) - End Span Erection - Stitching			
1032-2400	P40/F5B(MJ Right) - End Span Erection - Formwork Fixing for and Grouting for Bearing	2	04-Jul-17	05-Jul-17													P40/F5B(MJ Right) - End Span Erection - Formwork Fixing for and Grouting for Bearing			
1032-2420	P40/F5B(MJ Right) - End Span Erection - Prestress Span Tendons	2	06-Jul-17	07-Jul-17													P40/F5B(MJ Right) - End Span Erection - Prestress Span Tendons			
1032-2440	P40/F5B(MJ Right) - End Span Erection - Remove Hanger Bar & Hanger Beam & Stitching Formwork	1	08-Jul-17	08-Jul-17													P40/F5B(MJ Right) - End Span Erection - Remove Hanger Bar & Hanger Beam & Stitching Formwork			
1032-2460	Prestress Extenral Tendon Bridge F3B	10	10-Jul-17	20-Jul-17													Prestress Extenral Tendon Bridge F3B			
Bridge F2B																				
1032-2580	P39/F4B - Install Pier Segment - Place Pier Segment	1	04-Jul-17	04-Jul-17													P39/F4B - Install Pier Segment - Place Pier Segment			
1032-2600	P39/F4B - Install Pier Segment - Adjust Segment Level and Location	2	05-Jul-17	06-Jul-17													P39/F4B - Install Pier Segment - Adjust Segment Level and Location			
1032-2620	P39/F4B - Install Pier Segment - Grouting the Bearing Upper Plinth	2	07-Jul-17	08-Jul-17													P39/F4B - Install Pier Segment - Grouting the Bearing Upper Plinth			
1032-2640	P39/F4B - Install Pier Segment - Stressing Nailing	2	10-Jul-17	11-Jul-17													P39/F4B - Install Pier Segment - Stressing Nailing			
1032-2660	P39/F4B - Install MS at P39/F4B	2	12-Jul-17	13-Jul-17													P39/F4B - Install MS at P39/F4B			
1032-2680	P39/F4B - Install Pier Segment - Relocate MS at P40/F5B to left and Engage FL at P39/F3B	2	14-Jul-17	15-Jul-17													P39/F4B - Install Pier Segment - Relocate MS at P40/F5B to left and Engage FL at P39/F3B			
1032-2700	P39/F4B - T Span Erection (6 pairs)	4	17-Jul-17	20-Jul-17													P39/F4B - T Span Erection (6 pairs)			
All Middle Bridge F (Common)																				
1032-4350	TCSS/LV Ducts at Pier 50-51	14	27-Apr-17	13-May-17													TCSS/LV Ducts at Pier 50-51			
1032-4353	TCSS/LV Ducts at Pier 51-52	14	15-May-17	31-May-17													TCSS/LV Ducts at Pier 51-52			
1032-4354	TCSS/LV Ducts at Pier 52-53	14	01-Jun-17	16-Jun-17													TCSS/LV Ducts at Pier 52-53			
1032-4355	TCSS/LV Ducts at Pier 53-54	14	17-Jun-17	04-Jul-17													TCSS/LV Ducts at Pier 53-54			
1032-4356	TCSS/LV Ducts at Pier 55-56	14	05-Jul-17	20-Jul-17													TCSS/LV Ducts at Pier 55-56			
10.4 - Bridge Deck Demolition																				
10.4.3 - Existing E/B Bridge																				
10412-1650	Demolish Dolphin + Tie Beam & Reconstruct Tie Beam Pier 34	20	19-Jun-17	12-Jul-17													Demolish Dolphin + Tie Beam & Reconstruct Tie Beam Pier 34			
10412-1670	Demolish Temp. E/B Bridge - Crosshead & Pier > Pier 34 & 35 by Crane	9	08-Jun-17	17-Jun-17													Demolish Temp. E/B Bridge - Crosshead & Pier > Pier 34 & 35 by Crane			
10412-1700	Demolish Dolphin+Pile Cap & Reconstruct Pier 33 Pile Cap	20	19-Jun-17	12-Jul-17													Demolish Dolphin+Pile Cap & Reconstruct Pier 33 Pile Cap			
10412-1710	Demolish Temp. E/B Bridge - Crosshead & Pier > Pier 33	9	27-May-17	07-Jun-17													Demolish Temp. E/B Bridge - Crosshead & Pier > Pier 33			
10412-1720	Demolish Temp. E/B Bridge - Deck > Pier 33 to 34 (6 beams)	5	22-May-17	26-May-17													Demolish Temp. E/B Bridge - Deck > Pier 33 to 34 (6 beams)			
10412-1730	Demolish Dolphin+Pile Cap & Reconstruct Pier 32 Pile Cap	20	08-Jun-17	30-Jun-17													Demolish Dolphin+Pile Cap & Reconstruct Pier 32 Pile Cap			
10412-1760	Demolish Dolphin+Pile Cap & Reconstruct Pier 31 Pile Cap	20	08-Mar-17 A	13-May-17													Demolish Dolphin+Pile Cap & Reconstruct Pier 31 Pile Cap			
10412-1790	Demolish Dolphin+Pile Cap & Reconstruct Pier 30 Pile Cap	20	02-Mar-17 A	13-May-17													Demolish Dolphin+Pile Cap & Reconstruct Pier 30 Pile Cap			
A3430	Demolish Pier + Steel Support at Pier 36	9	20-Apr-17 A	29-Apr-17													Demolish Pier + Steel Support at Pier 36			
A3440	Launch LG-BM to next Bridge Span	1	02-May-17	02-May-17													Launch LG-BM to next Bridge Span			
A3450	Demolish Four(4nos) Beams at Pier 35-34 - by LG-BM	2	03-May-17	04-May-17													Demolish Four(4nos) Beams at Pier 35-34 - by LG-BM			
A3460	Dismantle LGB	14	05-May-17	20-May-17													Dismantle LGB			
10.5 - Temporary Bridge																				
10.5.2 - Temporary Bridge 'TB'																				

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Contract HY/2009/19

Three Months Rolling Programme (20 April 2017 to 19 July 2017)

Page 5 of 9

Activity ID	Activity Name	Rem Dur	Start	Finish	2017															
					May						June				July					
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23	
1052-1260	TB > Demolition of Temporary Bridge "TB"	4	03-Apr-17 A	24-Apr-17	TB > Demolition of Temporary Bridge "TB"															
10.6 - Tunnel Approach Ramp																				
10.6.1 - Approach Ramp (Excluding Portion IIB)																				
Piling Works																				
1061-3490	Moving Temp Car Park to Permanent Car Park Completed	0		27-Apr-17	◆ Moving Temp Car Park to Permanent Car Park Completed															
1061-3500	Pre Bored H-Pile > Pile Ramp - BM03 A	4	27-Apr-17	02-May-17	Pre Bored H-Pile > Pile Ramp - BM03 A															
1061-3520	Pre Bored H-Pile > Pile Ramp - BM03 A - (H-Pile + Grouting)	1	03-May-17	03-May-17	Pre Bored H-Pile > Pile Ramp - BM03 A - (H-Pile + Grouting)															
1061-3540	Pre Bored H-Pile > Pile Ramp - BM03 B	4	03-May-17	06-May-17	Pre Bored H-Pile > Pile Ramp - BM03 B															
1061-3560	Pre Bored H-Pile > Pile Ramp - BM03 B - (H-Pile + Grouting)	1	08-May-17	08-May-17	Pre Bored H-Pile > Pile Ramp - BM03 B - (H-Pile + Grouting)															
1061-3820	Pre Bored H-Pile > Pile Ramp - BN11 A(Low Head Rm)	8	08-May-17	16-May-17	Pre Bored H-Pile > Pile Ramp - BN11 A(Low Head Rm)															
1061-3840	Pre Bored H-Pile > Pile Ramp - BN11 A - (H-Pile + Grouting)	1	17-May-17	17-May-17	Pre Bored H-Pile > Pile Ramp - BN11 A - (H-Pile + Grouting)															
1061-3860	Pre Bored H-Pile > Pile Ramp - BN11 B (LHR)	8	08-May-17	16-May-17	Pre Bored H-Pile > Pile Ramp - BN11 B (LHR)															
1061-3880	Pre Bored H-Pile > Pile Ramp - BN11 B - (H-Pile + Grouting)	1	17-May-17	17-May-17	Pre Bored H-Pile > Pile Ramp - BN11 B - (H-Pile + Grouting)															
1061-3900	Pre Bored H-Pile > Pile Ramp - BN12 A (LHR)	8	17-May-17	25-May-17	Pre Bored H-Pile > Pile Ramp - BN12 A (LHR)															
1061-3920	Pre Bored H-Pile > Pile Ramp - BN12 A - (H-Pile + Grouting)	1	26-May-17	26-May-17	Pre Bored H-Pile > Pile Ramp - BN12 A - (H-Pile + Grouting)															
1061-3940	Pre Bored H-Pile > Pile Ramp - BN12 B (LHR)	8	17-May-17	25-May-17	Pre Bored H-Pile > Pile Ramp - BN12 B (LHR)															
1061-3960	Pre Bored H-Pile > Pile Ramp - BN12 B - (H-Pile + Grouting)	1	26-May-17	26-May-17	Pre Bored H-Pile > Pile Ramp - BN12 B - (H-Pile + Grouting)															
1061-3980	Pre Bored H-Pile > Pile Ramp - BN13 A (LHR)	8	26-May-17	05-Jun-17	Pre Bored H-Pile > Pile Ramp - BN13 A (LHR)															
1061-4000	Pre Bored H-Pile > Pile Ramp - BN13 A - (H-Pile + Grouting)	1	06-Jun-17	06-Jun-17	Pre Bored H-Pile > Pile Ramp - BN13 A - (H-Pile + Grouting)															
1061-4020	Pre Bored H-Pile > Pile Ramp - BN13 B (LHR)	8	26-May-17	05-Jun-17	Pre Bored H-Pile > Pile Ramp - BN13 B (LHR)															
1061-4040	Pre Bored H-Pile > Pile Ramp - BN13 B - (H-Pile + Grouting)	1	06-Jun-17	06-Jun-17	Pre Bored H-Pile > Pile Ramp - BN13 B - (H-Pile + Grouting)															
1061-4060	Pre Bored H-Pile > Pile Ramp - BN01 A (LHR)	8	06-Jun-17	14-Jun-17	Pre Bored H-Pile > Pile Ramp - BN01 A (LHR)															
1061-4080	Pre Bored H-Pile > Pile Ramp - BN01 A - (H-Pile + Grouting)	1	15-Jun-17	15-Jun-17	Pre Bored H-Pile > Pile Ramp - BN01 A - (H-Pile + Grouting)															
1061-4100	Pre Bored H-Pile > Pile Ramp - BN01 B (LHR)	8	06-Jun-17	14-Jun-17	Pre Bored H-Pile > Pile Ramp - BN01 B (LHR)															
1061-4120	Pre Bored H-Pile > Pile Ramp - BN01 B - (H-Pile + Grouting)	1	15-Jun-17	15-Jun-17	Pre Bored H-Pile > Pile Ramp - BN01 B - (H-Pile + Grouting)															
1061-4140	Pre Bored H-Pile > Pile Ramp - BN05 A (LHR)	8	15-Jun-17	23-Jun-17	Pre Bored H-Pile > Pile Ramp - BN05 A (LHR)															
1061-4160	Pre Bored H-Pile > Pile Ramp - BN05 A - (H-Pile + Grouting)	1	24-Jun-17	24-Jun-17	Pre Bored H-Pile > Pile Ramp - BN05 A - (H-Pile + Grouting)															
1061-4180	Pre Bored H-Pile > Pile Ramp - BN05 B (LHR)	8	15-Jun-17	23-Jun-17	Pre Bored H-Pile > Pile Ramp - BN05 B (LHR)															
1061-4200	Pre Bored H-Pile > Pile Ramp - BN05 B - (H-Pile + Grouting)	1	24-Jun-17	24-Jun-17	Pre Bored H-Pile > Pile Ramp - BN05 B - (H-Pile + Grouting)															
1061-4220	Pre Bored H-Pile > Pile Ramp - BN06 A (LHR)	8	24-Jun-17	04-Jul-17	Pre Bored H-Pile > Pile Ramp - BN06 A (LHR)															
1061-4240	Pre Bored H-Pile > Pile Ramp - BN06 A - (H-Pile + Grouting)	1	05-Jul-17	05-Jul-17	Pre Bored H-Pile > Pile Ramp - BN06 A - (H-Pile + Grouting)															
1061-4260	Pre Bored H-Pile > Pile Ramp - BN06 B (LHR)	8	24-Jun-17	04-Jul-17	Pre Bored H-Pile > Pile Ramp - BN06 B (LHR)															
1061-4280	Pre Bored H-Pile > Pile Ramp - BN06 B - (H-Pile + Grouting)	1	05-Jul-17	05-Jul-17	Pre Bored H-Pile > Pile Ramp - BN06 B - (H-Pile + Grouting)															
1061-4300	Remaining Bored Piles & Pre-Bored H-Pile Testing	30	31-May-17	05-Jul-17	Remaining Bored Piles & Pre-Bored H-Pile Testing															
Excavation & ELS Works																				

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Contract HY/2009/19

Three Months Rolling Programme (20 April 2017 to 19 July 2017)

Page 6 of 9

Activity ID	Activity Name	Rem Dur	Start	Finish	2017																
							May				June				July						
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23		
1061-4901.2	Sheet Piling Works (WF1>B3:19m@1.5m/d) (incl Re-boring & Welding Remedial Works)	9	12-Jul-16 A	29-Apr-17			Sheet Piling Works (WF1>B3:19m@1.5m/d) (incl Re-boring & Welding Remedial Works)														
1061-4910	Advance Sheet Piling Works + Pre-drilling in Phase 2 - Cul de sac Area (30m)	14	04-Apr-17 A	17-May-17				Advance Sheet Piling Works + Pre-drilling in Phase 2 - Cul de sac Area (30m)													
1061-4915	Tam Grouting	12	14-Sep-16 A	04-May-17			Tam Grouting														
1061-5060	Dewatering Well Installation (14Nos)	9	11-Jan-17 A	29-Apr-17			Dewatering Well Installation (14Nos)														
1061-5080	Observation Well Installation (10Nos)	9	13-Feb-17 A	29-Apr-17			Observation Well Installation (10Nos)														
1061-5100	Pumping Test	9	05-May-17	15-May-17				Pumping Test													
1061-5120	Complete Pump Test	0		15-May-17				◆ Complete Pump Test													
1061-5140	Ch 5285 - 5331 > Excav from Ex. Lvl down to 2.5mPD (Ch 5285 - 5331 w/ open cut)	7	15-Aug-16 A	27-Apr-17			Ch 5285 - 5331 > Excav from Ex. Lvl down to 2.5mPD (Ch 5285 - 5331 w/ open cut)														
1061-5160	Ch 5234 - 5285 > Excav from Ex. Lvl down to 2.5mPD	9	30-Mar-17 A	09-May-17				Ch 5234 - 5285 > Excav from Ex. Lvl down to 2.5mPD													
1061-5180	Ch 5234 - 5285 > Install 1st Layer of Strut & Waling	9	10-May-17	19-May-17				Ch 5234 - 5285> Install 1st Layer of Strut & Waling													
1061-5200	Ch 5234 - 5285 > Excav from 2.5mPD to 1m Below 2nd Layer of Struts	16	20-May-17	08-Jun-17				Ch 5234 - 5285 > Excav from 2.5mPD to 1m Below 2nd Layer of Struts													
1061-5220	Ch 5234 - 5285 > Install 2nd Layer of Strut & Waling	9	09-Jun-17	19-Jun-17					Ch 5234 - 5285 > Install 2nd Layer of Strut & Waling												
1061-5240	Ch 5234 - 5285 > Excav to FEL	13	20-Jun-17	05-Jul-17					Ch 5234 - 5285 > Excav to FEL												
Structure Works																					
1061-5260	Bay 1 - Ch 5322 - 5331 > Base Slab - Blinding Layer	1	09-Jun-17	09-Jun-17									Bay 1 - Ch 5322 - 5331 > Base Slab - Blinding Layer								
1061-5280	Bay 1 - Ch 5322 - 5331 > Base Slab - Water Proofing Membrane	2	10-Jun-17	12-Jun-17									Bay 1 - Ch 5322 - 5331 > Base Slab - Water Proofing Membrane								
1061-5300	Bay 1 - Ch 5322 - 5331 > Base Slab - Rebar Fixing	5	13-Jun-17	17-Jun-17									Bay 1 - Ch 5322 - 5331 > Base Slab - Rebar Fixing								
1061-5320	Bay 1 - Ch 5322 - 5331 > Base Slab - Erect Formworks	4	19-Jun-17	22-Jun-17									Bay 1 - Ch 5322 - 5331 > Base Slab - Erect Formwork								
1061-5340	Bay 1 - Ch 5322 - 5331 > Base Slab - Concreting	1	23-Jun-17	23-Jun-17									Bay 1 - Ch 5322 - 5331 > Base Slab - Concreting								
1061-5360	Bay 2 - Ch 5313 - 5322 > Base Slab - Blinding Layer	1	24-Jun-17	24-Jun-17									Bay 2 - Ch 5313 - 5322 > Base Slab - Blinding Layer								
1061-5380	Bay 2 - Ch 5313 - 5322 > Base Slab - Water Proofing Membrane	2	26-Jun-17	27-Jun-17									Bay 2 - Ch 5313 - 5322 > Base Slab - Water Proofing Membrane								
1061-5400	Bay 2 - Ch 5313 - 5322 > Base Slab - Rebar Fixing	5	28-Jun-17	04-Jul-17									Bay 2 - Ch 5313 - 5322 > Base Slab - Rebar Fixing								
1061-5420	Bay 2 - Ch 5313 - 5322 > Base Slab - Erect Formworks	4	05-Jul-17	08-Jul-17									Bay 2 - Ch 5313 - 5322 > Base Slab - Erect Formwork								
1061-5440	Bay 2 - Ch 5313 - 5322 > Base Slab - Concreting	1	10-Jul-17	10-Jul-17									Bay 2 - Ch 5313 - 5322 > Base Slab - Concreting								
1061-5460	Bay 3 - Ch 5303 - 5313 > Base Slab - Blinding Layer	1	11-Jul-17	11-Jul-17									Bay 3 - Ch 5303 - 5313 > Base Slab - Blinding Layer								
1061-5480	Bay 3 - Ch 5303 - 5313 > Base Slab - Water Proofing Membrane	2	12-Jul-17	13-Jul-17									Bay 3 - Ch 5303 - 5313 > Base Slab - Water Proofing Membrane								
1061-5500	Bay 3 - Ch 5303 - 5313 > Base Slab - Rebar Fixing	5	14-Jul-17	19-Jul-17									Bay 3 - Ch 5303 - 5313 > Base Slab - Rebar Fixing								
1061-5560	Bay 6 - Ch 5262 - 5277 > Base Slab - Blinding Layer	1	06-Jul-17	06-Jul-17									Bay 6 - Ch 5262 - 5277 > Base Slab - Blinding Layer								
1061-5580	Bay 6 - Ch 5262 - 5277 > Base Slab - Water Proofing Membrane	2	07-Jul-17	08-Jul-17									Bay 6 - Ch 5262 - 5277 > Base Slab - Water Proofing Membrane								
1061-5600	Bay 6 - Ch 5262 - 5277 > Base Slab - Rebar Fixing	6	10-Jul-17	15-Jul-17									Bay 6 - Ch 5262 - 5277 > Base Slab - Rebar Fixing								
Retaining Walls & Trough Structure B,C & D																					
1061-6860	Construct Retaining Wall E Pile Cap (7 nos)	24	06-Mar-17 A	18-May-17			Construct Retaining Wall E Pile Cap (7 nos)														
1061-6880	Construct Retaining Wall E1 (Ch 5332 - 5371)	18	19-May-17	09-Jun-17					Construct Retaining Wall E1 (Ch 5332 - 5371)												
1061-6900	Construct Retaining Wall E3 (Ch 5371 - 5398)	18	10-Jun-17	30-Jun-17						Construct Retaining Wall E3 (Ch 5371 - 5398)											
1061-6920	Construct Retaining Wall E3 (Ch 5398 - 5419)	18	19-May-17	09-Jun-17					Construct Retaining Wall E3 (Ch 5398 - 5419)												
Remaining Level of Effort Actual Level of Effort Actual Work		Remaining Work Critical Remaining Work Milestone		Contract HY/2009/19 Three Months Rolling Programme (20 April 2017 to 19 July 2017)												Page 7 of 9					

Activity ID	Activity Name	Rem Dur	Start	Finish	2017															
							May				June				July					
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23	
10.6.2 - Approach Ramp (Within Portion IIB)																				
Pre-Bored H-Piles																				
1062-1020	Predrilling for ramp within Portion IIB (14no - 3set)	18	28-Apr-17	19-May-17	Predrilling for ramp within Portion IIB (14no - 3set)															
1062-1040	Approach Ramp Portion IIB Piles Final Report / Founding Level	18	08-May-17	27-May-17	Approach Ramp Portion IIB Piles Final Report / Founding Level															
1062-1400	Pre Bored H-Pile > Pile Ramp - BS01 A	14	15-May-17	31-May-17	Pre Bored H-Pile > Pile Ramp - BS01 A															
1062-1420	Pre Bored H-Pile > Pile Ramp - BS01 B	14	20-May-17	06-Jun-17	Pre Bored H-Pile > Pile Ramp - BS01 B															
1062-1440	Pre Bored H-Pile > Pile Ramp - BS02 A	14	26-May-17	12-Jun-17	Pre Bored H-Pile > Pile Ramp - BS02 A															
1062-1460	Pre Bored H-Pile > Pile Ramp - BS02 B	14	02-Jun-17	17-Jun-17	Pre Bored H-Pile > Pile Ramp - BS02 B															
1062-1480	Pre Bored H-Pile > Pile Ramp - BS03 A	14	08-Jun-17	23-Jun-17	Pre Bored H-Pile > Pile Ramp - BS03 A															
1062-1500	Pre Bored H-Pile > Pile Ramp - BS03 B	14	14-Jun-17	29-Jun-17	Pre Bored H-Pile > Pile Ramp - BS03 B															
1062-1520	Pre Bored H-Pile > Pile Ramp - BS04 A	14	20-Jun-17	06-Jul-17	Pre Bored H-Pile > Pile Ramp - BS04 A															
1062-1540	Pre Bored H-Pile > Pile Ramp - BS04 B	14	26-Jun-17	12-Jul-17	Pre Bored H-Pile > Pile Ramp - BS04 B															
1062-1560	Pre Bored H-Pile > Pile Ramp - BS05 A	14	15-May-17	31-May-17	Pre Bored H-Pile > Pile Ramp - BS05 A															
1062-1580	Pre Bored H-Pile > Pile Ramp - BS05 B	14	20-May-17	06-Jun-17	Pre Bored H-Pile > Pile Ramp - BS05 B															
1062-1600	Pre Bored H-Pile > Pile Ramp - BS06 A	14	26-May-17	12-Jun-17	Pre Bored H-Pile > Pile Ramp - BS06 A															
1062-1620	Pre Bored H-Pile > Pile Ramp - BS06 B	14	02-Jun-17	17-Jun-17	Pre Bored H-Pile > Pile Ramp - BS06 B															
1062-1640	Pre Bored H-Pile > Pile Ramp - BS07 A	14	08-Jun-17	23-Jun-17	Pre Bored H-Pile > Pile Ramp - BS07 A															
1062-1660	Pre Bored H-Pile > Pile Ramp - BS07 B	14	14-Jun-17	29-Jun-17	Pre Bored H-Pile > Pile Ramp - BS07 B															
1062-1680	Pre Bored H-Pile > Pile Ramp - BS08 A	14	20-Jun-17	06-Jul-17	Pre Bored H-Pile > Pile Ramp - BS08 A															
1062-1700	Pre Bored H-Pile > Pile Ramp - BS08 B	14	26-Jun-17	12-Jul-17	Pre Bored H-Pile > Pile Ramp - BS08 B															
1062-1720	Pre Bored H-Pile > Pile Ramp - BS09 A	14	20-May-17	06-Jun-17	Pre Bored H-Pile > Pile Ramp - BS09 A															
1062-1740	Pre Bored H-Pile > Pile Ramp - BS09 B	14	26-May-17	12-Jun-17	Pre Bored H-Pile > Pile Ramp - BS09 B															
1062-1760	Pre Bored H-Pile > Pile Ramp - BS10 A	14	02-Jun-17	17-Jun-17	Pre Bored H-Pile > Pile Ramp - BS10 A															
1062-1780	Pre Bored H-Pile > Pile Ramp - BS10 B	14	08-Jun-17	23-Jun-17	Pre Bored H-Pile > Pile Ramp - BS10 B															
1062-1800	Pre Bored H-Pile > Pile Ramp - BS11 A	14	14-Jun-17	29-Jun-17	Pre Bored H-Pile > Pile Ramp - BS11 A															
1062-1820	Pre Bored H-Pile > Pile Ramp - BS11 B	14	20-Jun-17	06-Jul-17	Pre Bored H-Pile > Pile Ramp - BS11 B															
1062-1840	Pre Bored H-Pile > Pile Ramp - BS12 A	14	26-Jun-17	12-Jul-17	Pre Bored H-Pile > Pile Ramp - BS12 A															
1062-1860	Pre Bored H-Pile > Pile Ramp - BS12 B	14	20-May-17	06-Jun-17	Pre Bored H-Pile > Pile Ramp - BS12 B															
1062-1880	Pre Bored H-Pile > Pile Ramp - BS13 A	14	26-May-17	12-Jun-17	Pre Bored H-Pile > Pile Ramp - BS13 A															
1062-1900	Pre Bored H-Pile > Pile Ramp - BS13 B	14	02-Jun-17	17-Jun-17	Pre Bored H-Pile > Pile Ramp - BS13 B															
1062-1920	Pre Bored H-Pile >Pile Ramp - BM01 A	14	08-Jun-17	23-Jun-17	Pre Bored H-Pile >Pile Ramp - BM01 A															
1062-1940	Pre Bored H-Pile > Pile Ramp - BM01 B	14	14-Jun-17	29-Jun-17	Pre Bored H-Pile > Pile Ramp - BM01 B															
1062-1960	Pre Bored H-Pile > Pile Ramp - BM02 A	14	20-Jun-17	06-Jul-17	Pre Bored H-Pile > Pile Ramp - BM02 A															
1062-1980	Pre Bored H-Pile > Pile Ramp - BM02 B	14	26-Jun-17	12-Jul-17	Pre Bored H-Pile > Pile Ramp - BM02 B															
ELS																				

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

◆

 Milestone

Activity ID	Activity Name	Rem Dur	Start	Finish	2017																
									May				June				July				
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23		
	A1000	Sheet Pile and Preboring Works	61	09-May-17	20-Jul-17	Sheet Pile and Preboring Works															
	A1010	Dewatering System and Instrumentation installation	38	31-May-17	14-Jul-17	Dewatering System and Instrumentation installation															
10.7 - Section X - Miscellaneous Works																					
10.7.2 - Oil Street/Watson Road (Portion III)																					
	1072-1000	Remaining Fresh Water Main 200DI - F02 Portion VIIB (Watson/VB)	120	27-Apr-17	16-Sep-17	Remaining Fresh Water Main 200DI - F02 Portion VIIB (Watson/VB)															
	1072-1020	Remaining Storm Water Drain Portion VII (Watson/VB)	120	27-Apr-17	16-Sep-17	Remaining Storm Water Drain Portion VII (Watson/VB)															
	1072-1040	Fresh Water Main 100DI - F03 Portion III (Oil Street/Admin Bldg)	50	27-Apr-17	26-Jun-17	Fresh Water Main 100DI - F03 Portion III (Oil Street/Admin Bldg)															
	1072-1060	Salt Water Main 100DI - S03 Portion III (Oil Street/Admin Bldg)	50	27-Apr-17	26-Jun-17	Salt Water Main 100DI - S03 Portion III (Oil Street/Admin Bldg)															
	1072-1065	Salt Water Main 100DI - S02 (Watson rd - Previously at Portion XIIB)	50	27-Apr-17	26-Jun-17	Salt Water Main 100DI - S02 (Watson rd - Previously at Portion XIIB)															
	1072-1080	Foul Sewer Dia. 225 Portion III (Oil Street/Admin Bldg)	50	27-Apr-17	26-Jun-17	Foul Sewer Dia. 225 Portion III (Oil Street/Admin Bldg)															
10.7.3 - Open Area																					
	1073-1010	Open Area - Pedestrian Parapet -Ch570.40 to Ch540.00	14	22-May-17*	07-Jun-17	Open Area - Pedestrian Parapet -Ch570.40 to Ch540.00															
	1073-1010.3	Open Area - Pedestrian Parapet - Ch540.00 to Ch520.00	14	08-Jun-17	23-Jun-17	Open Area - Pedestrian Parapet - Ch540.00 to Ch520.00															
	1073-1010.5	Open Area - Pedestrian Parapet - Ch0.00 - Ch40.00	14	24-Jun-17	11-Jul-17	Open Area - Pedestrian Parapet - Ch0.00 - Ch40.00															
	1073-1010.7	Open Area - Pedestrian Parapet - Ch40.00 - 80.00	14	12-Jul-17	27-Jul-17	Open Area - Pedestrian Parapet - Ch40.00 - 80.00															
11 - SECTION 11 OF THE WORKS																					
11.1 - Portion XIIA - Stage 1																					
11.1.1 - Along Watson Road - Waterwork & Roadworks (Portion XIIA)																					
	1110-2820	Permanent Cul-de Sac - Constr. of drainage	25	20-Apr-17*	19-May-17	Permanent Cul-de Sac - Constr. of drainage															
	1110-2830	Permanent Cul-de Sac - Constr. of watermains	25	03-May-17	01-Jun-17	Permanent Cul-de Sac - Constr. of watermains															
	1110-2840	Permanent Cul-de Sac - Constr. of public lighting & telecom (conduits & drawpits)	25	15-May-17	13-Jun-17	Permanent Cul-de Sac - Constr. of public lighting & telecom (conduits & drawpits)															
	1110-2850	Permanent Cul-de Sac - Constr. of (kerbs & pavements)	25	14-Jun-17	13-Jul-17	Permanent Cul-de Sac - Constr. of (kerbs & pavements)															
11.1.3 - Along Tsing Fung St. - TCSS cable ducting (Portion XIIA)																					
	1110-2930	TCSS cable ducting along Tsing Fung St	36	08-May-17*	19-Jun-17	TCSS cable ducting along Tsing Fung St															
11.1.4 - Along Gordon House - Cross road ducting at Hing Fat St adjacent to (Portion XIIA)																					
	1110-2940	Trench 1 (E&M, PL) - (Night Work)	16	19-Sep-16 A	09-May-17	Trench 1 (E&M, PL) - (Night Work)															
	1110-2950	Trench 2 (ATC) - (Night Work)	38	10-May-17	23-Jun-17	Trench 2 (ATC) - (Night Work)															
11.1.5 - Footing and frame/pole for directional sign FVMSH2, ADS16 and OHVD (Portion XIIA)																					
	1110-2960	ADS16	26	14-Sep-16 A	20-May-17	ADS16															
	1110-2970	OHVD	12	22-May-17	05-Jun-17	OHVD															
	1110-2980	FVMSH2	18	06-Jun-17	26-Jun-17	FVMSH2															

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone
