

Remaining Works Programme

Legend

Original Programme Period
as in version date 11/12/18
Extended Programme Period
as in this version date 21/1/19

Create Date : 21/1/2019
Revised Date : 25/1/2019
28/1/2019
30/1/2019
1/2/2019


項目	工序	Jan-19																																											
		Week 54					Week 55					Week 56					Week 01					Week 02					Week 03																		
		1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13
1	Removal of Temporary Storage of Backfill material at Portion 5	Portion 5 運泥回填 WCR1 停止運泥因為Close P5 Exit													Portion 5 運泥回填 WCR1																														
2	Seawall海床	夾泥至原海床													鋪設 G400 石面及拋斜水(800m3)																														
3	地面墊仔& 100mm Subbase														做墊仔																														
4	舊直升機場, 海墜及梯台														舊直升機場Landing 清場 入機 打 pipe																														
5	打D-Wall	打D區D-Wall至+1.5 (48M) 回填													掘泥 打B區remaining D-Wall至+1.5 (15M) 回填																														
6	U Channel & 沙井	打culvert頂石屎													北面東段4個catchpit和300U渠 (103m) DN8.1 DN8.2 清場 北面西段1個catchpit和300, 375U渠(56m) DN1.1 北面中段300U渠 Formation Drainage Works adjacent to Area 7(2個catchpit和300/450U渠) C1.3 DN1.2 BACKFILL																														
7	渠網 & 沙井														沙井 7356 and 7349 225呎由DN8.6至7349 225呎由7356和7349至BC0 CCTV 7352, 7340, 7328, 7327 試氣 7353, 7339, C1.3																														
8	IRRIGATION PIPE	WWW542 (21/12/18)													subsoil drainage WSD approval of design WWW046報開工																														
9	Fresh Water Main	TTA approved in TMLG Meeting 5/12/18																																											
10	HHR 馬路	AREA ABCD remove PMSMA Relay Area ABCD PMSMA AREA E remove and relay BC+PMSMA REMEDIAL TO CONCRETE LAYBY													FOOTPATH ALONG HHR waiting core test result survey remedial to concrete layby																														
10.1	HHR FLYOVER REMAINING WORK	V0258 MODIFICATION WORK AT ABUTMENT ROOM V0253 PROVIDE STAINLESS STEEL LADDER AT ABUTMENT ROOM													place order and delivery																														
11	還原運盛街 Stage 0.5	EVA																																											
12	博覽道東, WCR1 & WCR3 未完成工作	* Portion 2 Zone 1 * Zone 2a upto end of EVA													清石屎 打路面石屎 升井蓋 打石屎 * Portion 2 Zone 2b REMEDIAL TO EXPO DRIVE COVERED WALKWAY WCR3 填 Sub Base (100mm thk 7000m²) Caisson seawall defects 海龍明珠如下COPING (COMMENCEMENT DATE TO BE CONFIRMED) WCR1&3 MAKE GOOD ARMOUR SLOPE PROFILE																														

Wan Chai Development Phase II - East
Central - Wan Chai Bypass at Wan Chai
Contract: HK/2009/02
Remaining Works Programme

項目	工序	June																																		
		Week 18					Week 19					Week 20					Week 21					Week 22														
		27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30
1	Removal of Temporary Storage of Backfill material at Portion 5																																			
2	Seawall海床																																			
3	地面墊仔& 100mm Subbase																																			
4	舊直升機場, 海墾及梯台																																			
5	打D-Wall																																			
6	U Channel & 沙井																																			
7	渠網& 沙井																																			
8	IRRIGATION PIPE																																			
9	Fresh Water Main																																			
10	HHR 馬路																																			
10.1	HHR FLYOVER REMAINING WORK																																			
11	還原運盛街 Stage 0.5																																			
12	博覽道東, WCR1 & WCR3 未完成工作																																			

CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019					
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
Promenade Seawall Parapet Construction & EVA																							
SVII12000	Sec VII - Precast parapet	67	18-Nov-17 A	14-May-18	0%																		
SVII12010	Sec VII - Zone CRIII - seawall parapet: Backfilling	14	20-Feb-18	07-Mar-18	0%																		
SVII12120	Sec VII - Zone CRIII - seawall parapet: Construct mass concrete coping	30	08-Mar-18	16-Apr-18	0%																		
SVII12122	Sec VII - Zone CRIII - seawall parapet: reinforced concret coping	17	17-Apr-18	07-May-18	0%																		
SVII12140	Sec VII - Zone CRIII - seawall parapet: construct seawall parapet	30	08-May-18	12-Jun-18	0%																		
SVII12160	Sec VII - CRIII - EVA: watermain	14	13-Jun-18	29-Jun-18	0%																		
SVII12180	Sec VII - CRIII - EVA: U-channel	14	30-Jun-18	17-Jul-18	0%																		
SVII12200	Sec VII - CRIII - EVA: bituminous layer	5	18-Jul-18	23-Jul-18	0%																		
SVII12220	Sec VII - CRIII - EVA: paving block	30	24-Jul-18	27-Aug-18	0%																		
SVII13120	Sec VII - Zone A1, A2 & B - seawall parapet: Construct mass concrete coping	14	28-Dec-17 A	07-Mar-18	68.18%																		
SVII13122	Sec VII - Zone A1, A2 & B - seawall parapet: reinforced concrete coping	18	08-Mar-18	28-Mar-18	0%																		
SVII13140	Sec VII - Zone A1, A2 & B - seawall parapet: Construct seawall parapet	30	09-Apr-18	14-May-18	0%																		
SVII13160	Sec VII - Zone A1, A2 & B - EVA: watermain	14	15-May-18	31-May-18	0%																		
SVII13180	Sec VII - Zone A1, A2 & B - EVA: U-channel	14	01-Jun-18	16-Jun-18	0%																		
SVII13182	Sec VII - Zone A1, A2 & B - EVA: bituminous layer	5	19-Jun-18	23-Jun-18	0%																		
SVII13184	Sec VII - Zone A1, A2 & B - EVA: paving block	30	25-Jun-18	30-Jul-18	0%																		
SVII13200	Sec VII - Zone D - seawall parapet: Remove temporary seawall block	21	07-Mar-18	03-Apr-18	0%																		
SVII13220	Sec VII - Zone D - seawall parapet: Construct mass concrete	30	04-Apr-18	10-May-18	0%																		
SVII13222	Sec VII - Zone D - seawall parapet: reinforced concrete coping	18	11-May-18	01-Jun-18	0%																		
SVII13240	Sec VII - Zone D - seawall parapet: Construct seawall parapet	25	02-Jun-18	03-Jul-18	0%																		
SVII13260	Sec VII - Zone D - EVA : watermain	14	04-Jul-18	19-Jul-18	0%																		
SVII13280	Sec VII - Zone D - EVA : U-channel	14	20-Jul-18	04-Aug-18	0%																		
SVII13300	Sec VII - Zone D - EVA : bituminous layer	5	06-Aug-18	10-Aug-18	0%																		
SVII13320	Sec VII - Zone D - EVA : paving block	30	11-Aug-18	14-Sep-18	0%																		
Promenade Footpath																							
Section 1																							
SVII10440	Sec VII - section 1 footpath - drainage works : connection pipe & U -channel	10	24-May-18	04-Jun-18	0%																		
SVII10445	Sec VII - section 1 footpath - watermain	7	05-Jun-18	12-Jun-18	0%																		
SVII10460	Sec VII - section 1 footpath - lighting	7	13-Jun-18	21-Jun-18	0%																		
SVII10500	Sec VII - section 1 footpath - paving block	21	22-Jun-18	17-Jul-18	0%																		
Section 2																							
SVII12610	Sec VII - section 2 footpath - drainage works : L2202 - L2203A	20	20-Feb-18	14-Mar-18	0%																		
SVII12615	Sec VII - section 2 footpath - watermain	7	15-Mar-18	22-Mar-18	0%																		
SVII12630	Sec VII - section 2 footpath - utilities: TCSS	21	23-Mar-18	20-Apr-18	0%																		
SVII12670	Sec VII - section 2 footpath - paving block	30	21-Apr-18	28-May-18	0%																		
Section 3																							
SVII12850	Sec VII - section 3 footpath - watermain	17	20-Feb-18	10-Mar-18	0%																		
SVII12870	Sec VII - section 3 footpath - utilities (HEC, TCSS, HGC, PCCW)	40	12-Mar-18	02-May-18	0%																		
SVII12875	Sec VII - 3 footpath - drainage works :U chanel	14	03-May-18	18-May-18	0%																		

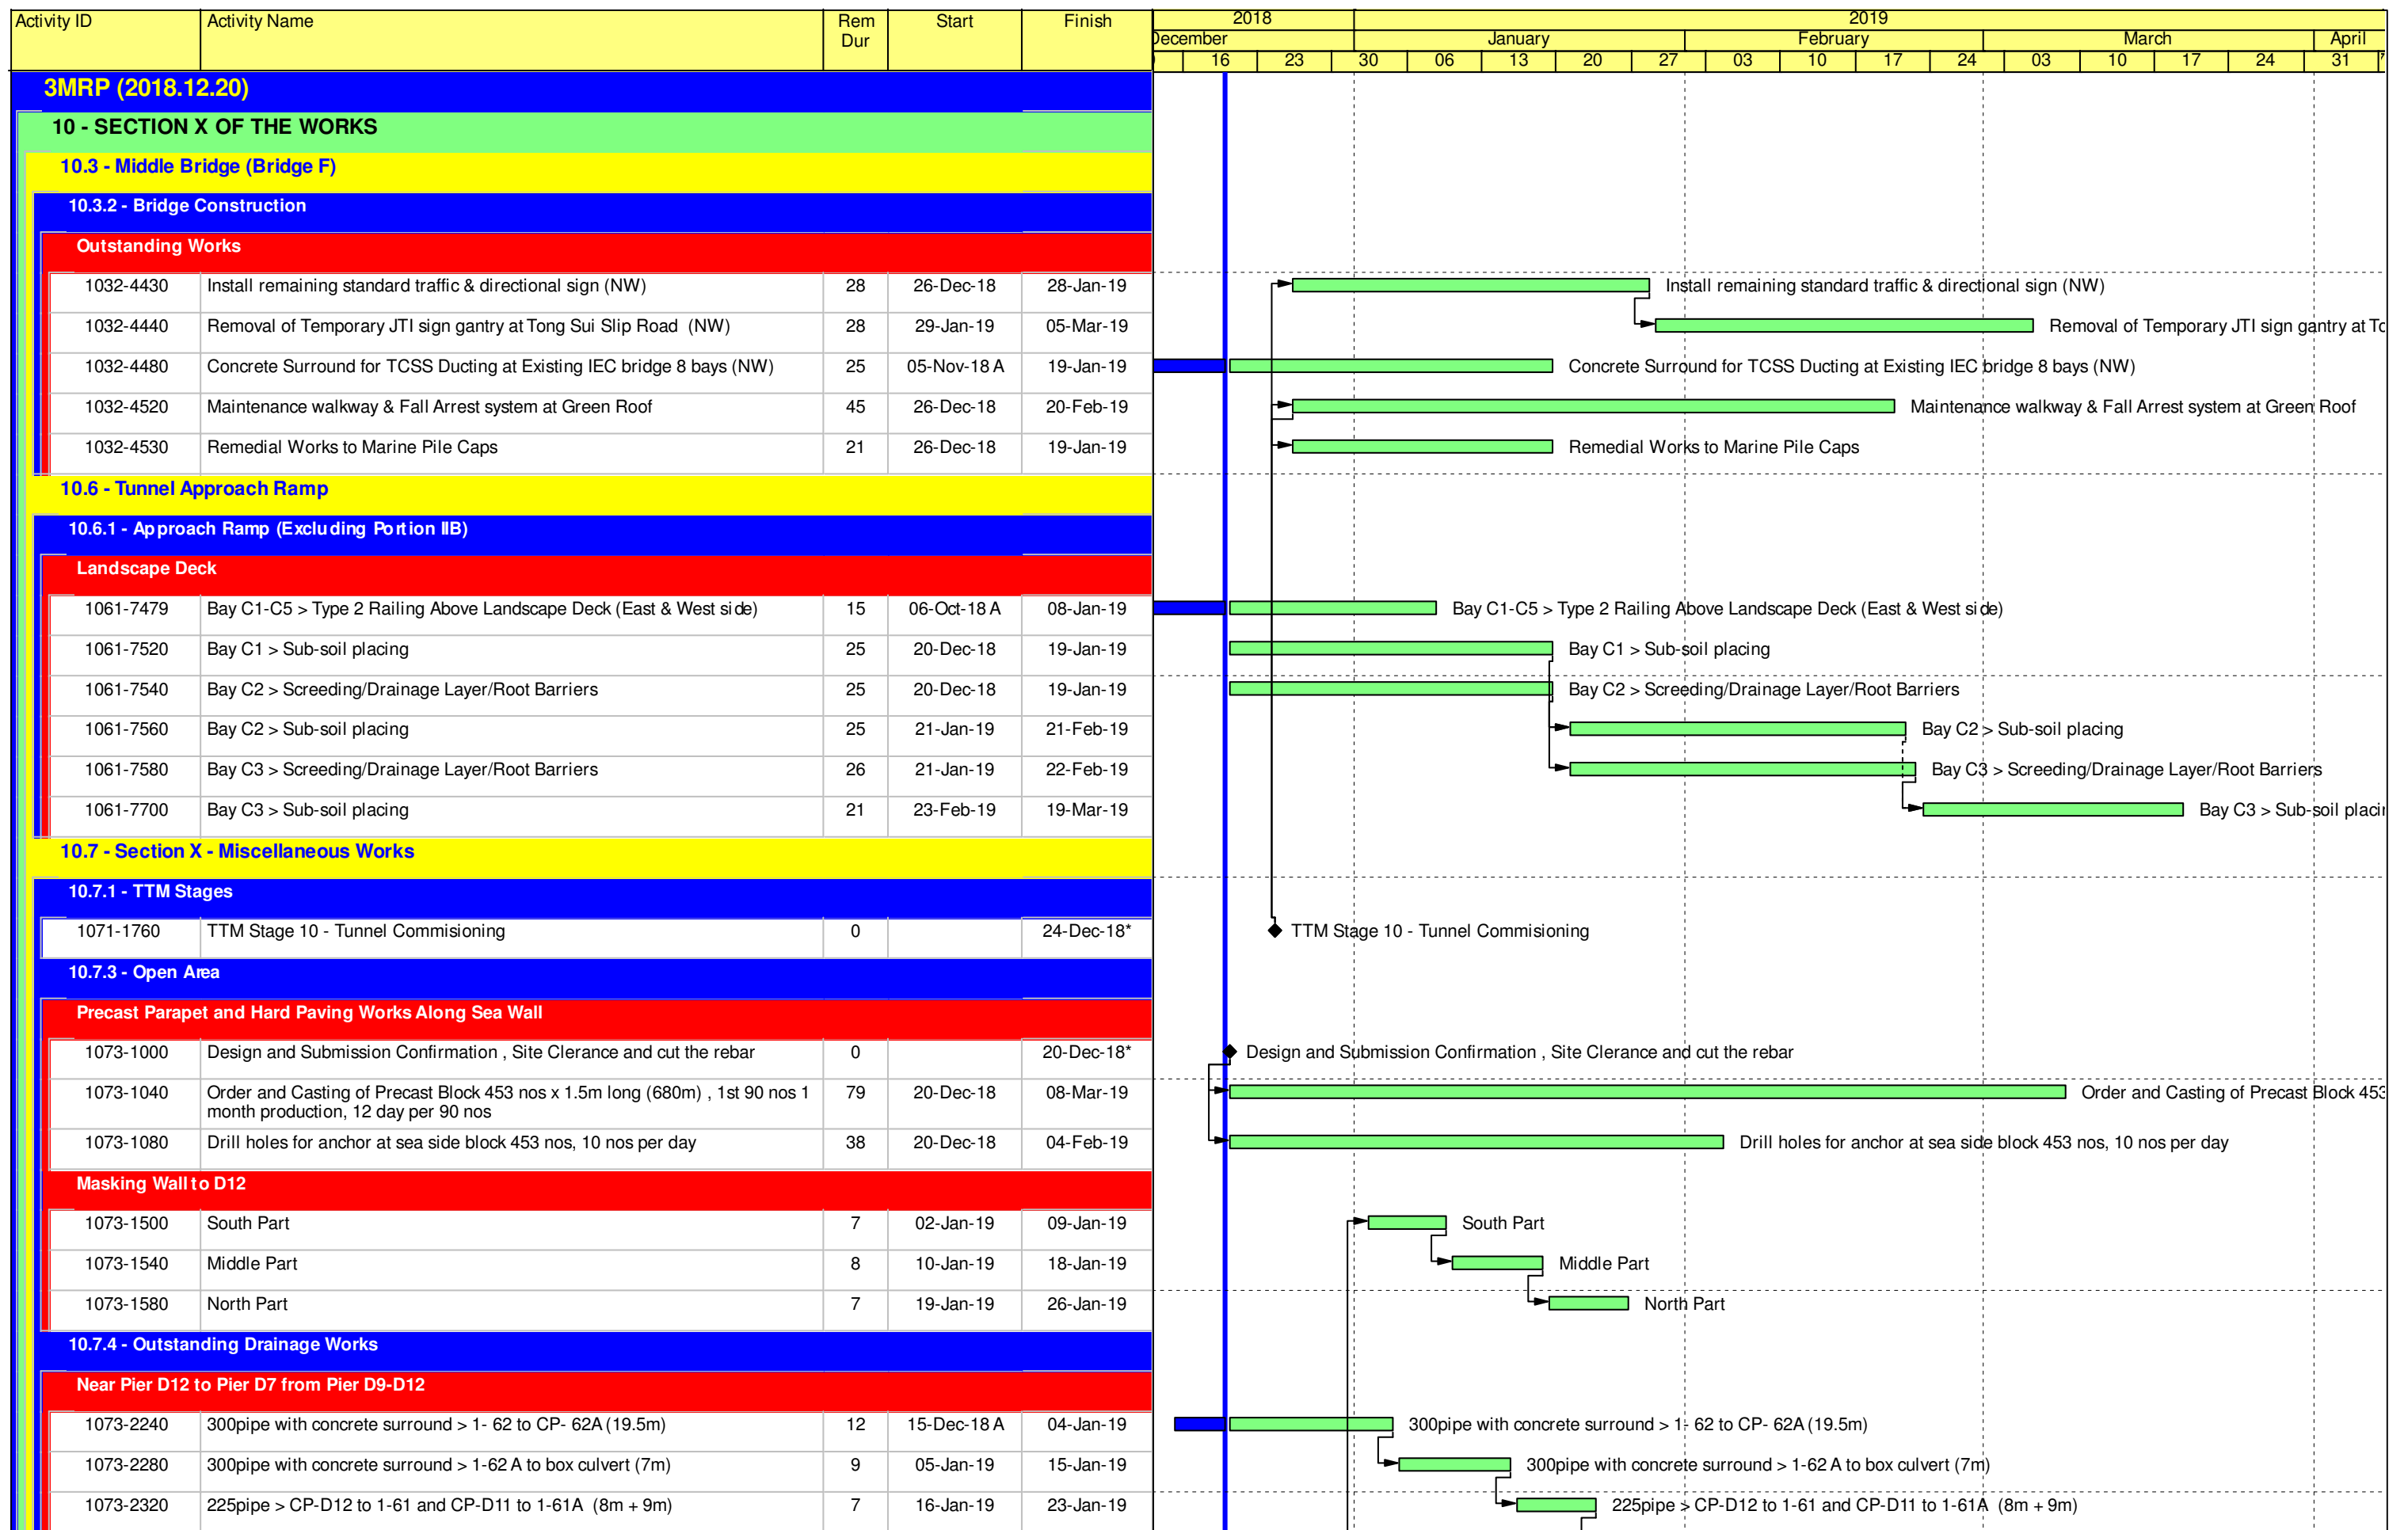

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Dec.2018 to 20.Mar.2019)

Activity ID	Activity Name	Rem Dur	Start	Finish	2018					2019											
					December			January			February				March				April		
					16	23	30	06	13	20	27	03	10	17	24	03	10	17	24	31	
1073-2360	450pipe > 1-67 to 1 -68 (30.5m)	13	24-Jan-19	11-Feb-19	[Gantt bar: 20 Jan to 11 Feb]																
1073-2400	450pipe > 1-68 to Box Culvert @ +0.88mPD (8m)	8	12-Feb-19	20-Feb-19	[Gantt bar: 12 Feb to 20 Feb]																
Bet Pier D19-D26 - West of SR13 to Box Culvert (to commence after removal of girder)																					
1073-2760	225 U Channel (4days/20m) (110m)	24	02-Jan-19*	29-Jan-19	[Gantt bar: 02 Jan to 29 Jan]																
1073-2800	Drain pit to Sand Trap with 225 pipe (10m)	5	30-Jan-19	04-Feb-19	[Gantt bar: 30 Jan to 04 Feb]																
1073-2840	Sand Trap to Box ,225 pipe (6m)	6	08-Feb-19	14-Feb-19	[Gantt bar: 08 Feb to 14 Feb]																
Bet Pier P20-P26 - Under Westbound Bridge (to commence after removal of site office)																					
1073-2880	225 U Channel at site office and West bound SR13(4days/20m) (124m)	34	30-Jan-19*	13-Mar-19	[Gantt bar: 30 Jan to 13 Mar]																
1073-2920	225 pipe > Pier 22 Catch Pit to Ex. MH (15m)	5	30-Jan-19	04-Feb-19	[Gantt bar: 30 Jan to 04 Feb]																
1073-2960	300pipe > 1-40C to Ex. MH, 1-40C to 225U Channel (21+6.5m)	10	08-Feb-19	19-Feb-19	[Gantt bar: 08 Feb to 19 Feb]																
Bet Pier P28-P35 - ADB area (to commence after LJV works - 1/12/2019)																					
1073-3200	150 U Channel at ADB (83m)	20	03-Jan-19*	25-Jan-19	[Gantt bar: 03 Jan to 25 Jan]																
1073-3240	Paving Block at ADB (140m2)	9	26-Jan-19	08-Feb-19	[Gantt bar: 26 Jan to 08 Feb]																
1073-3280	225 pipe > 1-52A to DP1-52A (13m)	8	02-Jan-19*	10-Jan-19	[Gantt bar: 02 Jan to 10 Jan]																
1073-3320	225 U Channel, narrow condition, 6days / 20m (65m)	20	11-Jan-19	02-Feb-19	[Gantt bar: 11 Jan to 02 Feb]																
1073-3360	300 pipe > 1-47D to 1-48B (19m)	7	02-Jan-19	09-Jan-19	[Gantt bar: 02 Jan to 09 Jan]																
1073-3400	375 pipe > 1-48B to 1-50 and 1-50 to 1-51 (10+5m)	7	11-Jan-19	18-Jan-19	[Gantt bar: 11 Jan to 18 Jan]																
1073-3440	2 Catch pit to 1-47D (5+6m)	5	10-Jan-19	15-Jan-19	[Gantt bar: 10 Jan to 15 Jan]																
1073-3480	300 UC 6days/20m (103m)	32	09-Feb-19	18-Mar-19	[Gantt bar: 09 Feb to 18 Mar]																

11 - SECTION 11 OF THE WORKS

11.4- Hing Fat Street

Time for Trial Run & RC preparation period

1140-1010	RC Preparation Period	2	20-Nov-18 A	21-Dec-18	[Gantt bar: 20 Nov to 21 Dec]	
-----------	-----------------------	---	-------------	-----------	-------------------------------	--

Tsing Fung Street (Left side) Kerblin underneath flyover (CWBIEL/058 - 111)

1140-1020	Construct new kerb and relocate gully	46	22-Dec-18	19-Feb-19	[Gantt bar: 22 Dec to 19 Feb]	
-----------	---------------------------------------	----	-----------	-----------	-------------------------------	--

Triangular Island at Tsing Fung Street and Hing Fat Street Junction (North side) (CWBIEL/058 - 100)

1140-1040	Construct new kerb, relocate gully, dwarf wall, beam barrier, irrigation pipe	46	22-Dec-18	19-Feb-19	[Gantt bar: 22 Dec to 19 Feb]	
-----------	---	----	-----------	-----------	-------------------------------	--

Stage 1a & 1b (CWBIEL/058 - 111)


Hing Fat Street (S/B) Slow Lane


1140-1260	Breaking existing pavement and excavation	6	22-Dec-18	29-Dec-18	[Gantt bar: 22 Dec to 29 Dec]	
1140-1280	Laying underground ducting & backfilling	6	31-Dec-18	07-Jan-19	[Gantt bar: 31 Dec to 07 Jan]	
1140-1300	Reconstruction pavement & road marking	6	08-Jan-19	14-Jan-19	[Gantt bar: 08 Jan to 14 Jan]	

Wing Hing Street Footpath


1140-1320	Breaking existing footpath and excavation	6	22-Dec-18	29-Dec-18	[Gantt bar: 22 Dec to 29 Dec]	
1140-1340	Laying underground ducting and backfilling	6	31-Dec-18	07-Jan-19	[Gantt bar: 31 Dec to 07 Jan]	
1140-1360	Reconstruction footpath	6	08-Jan-19	14-Jan-19	[Gantt bar: 08 Jan to 14 Jan]	

Triangular Island at Victoria Park Road (East side)

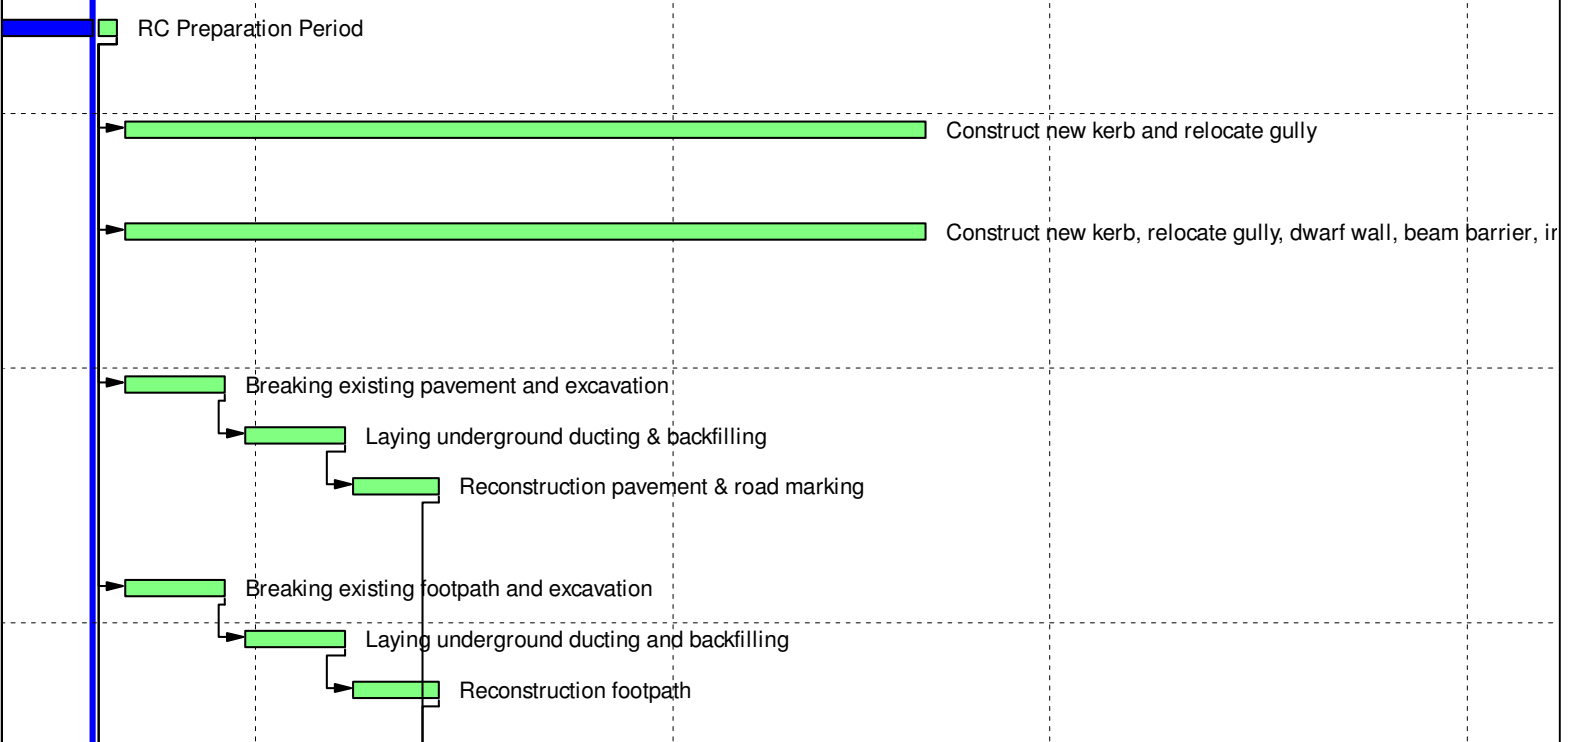

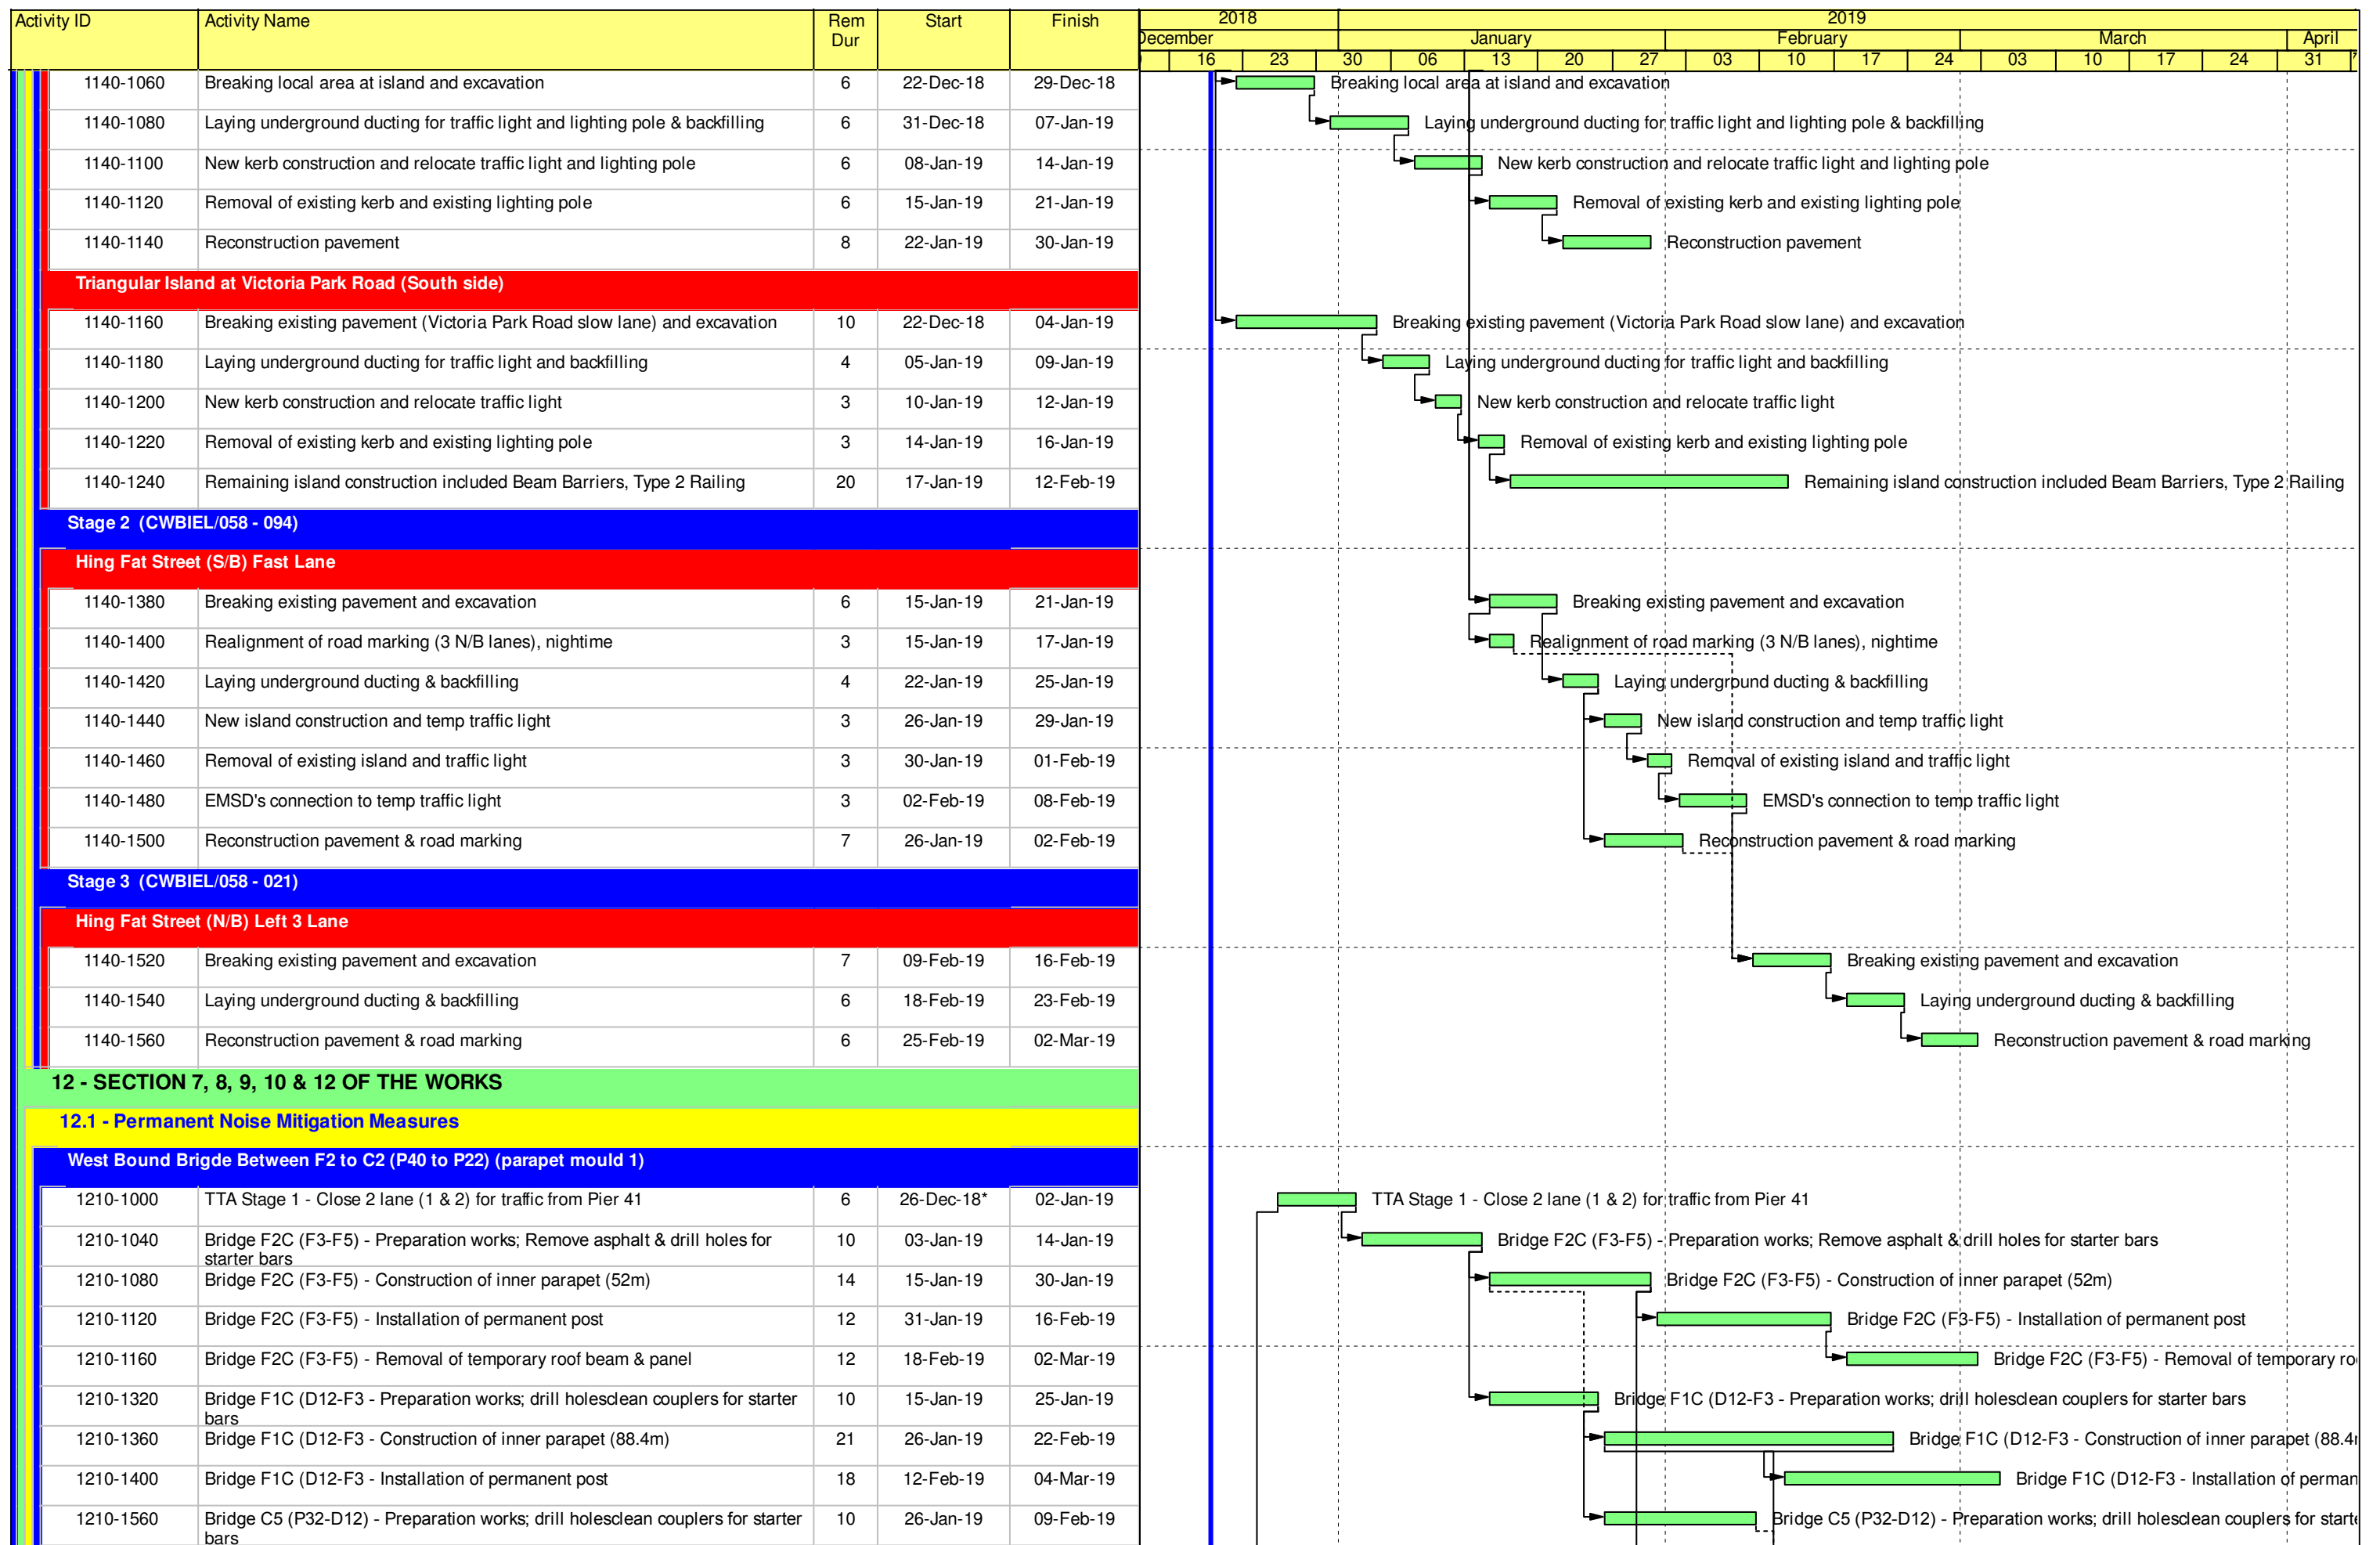

Contract HY/2009/19
Three Months Rolling Programme (20.Dec.2018 to 20.Mar.2019)

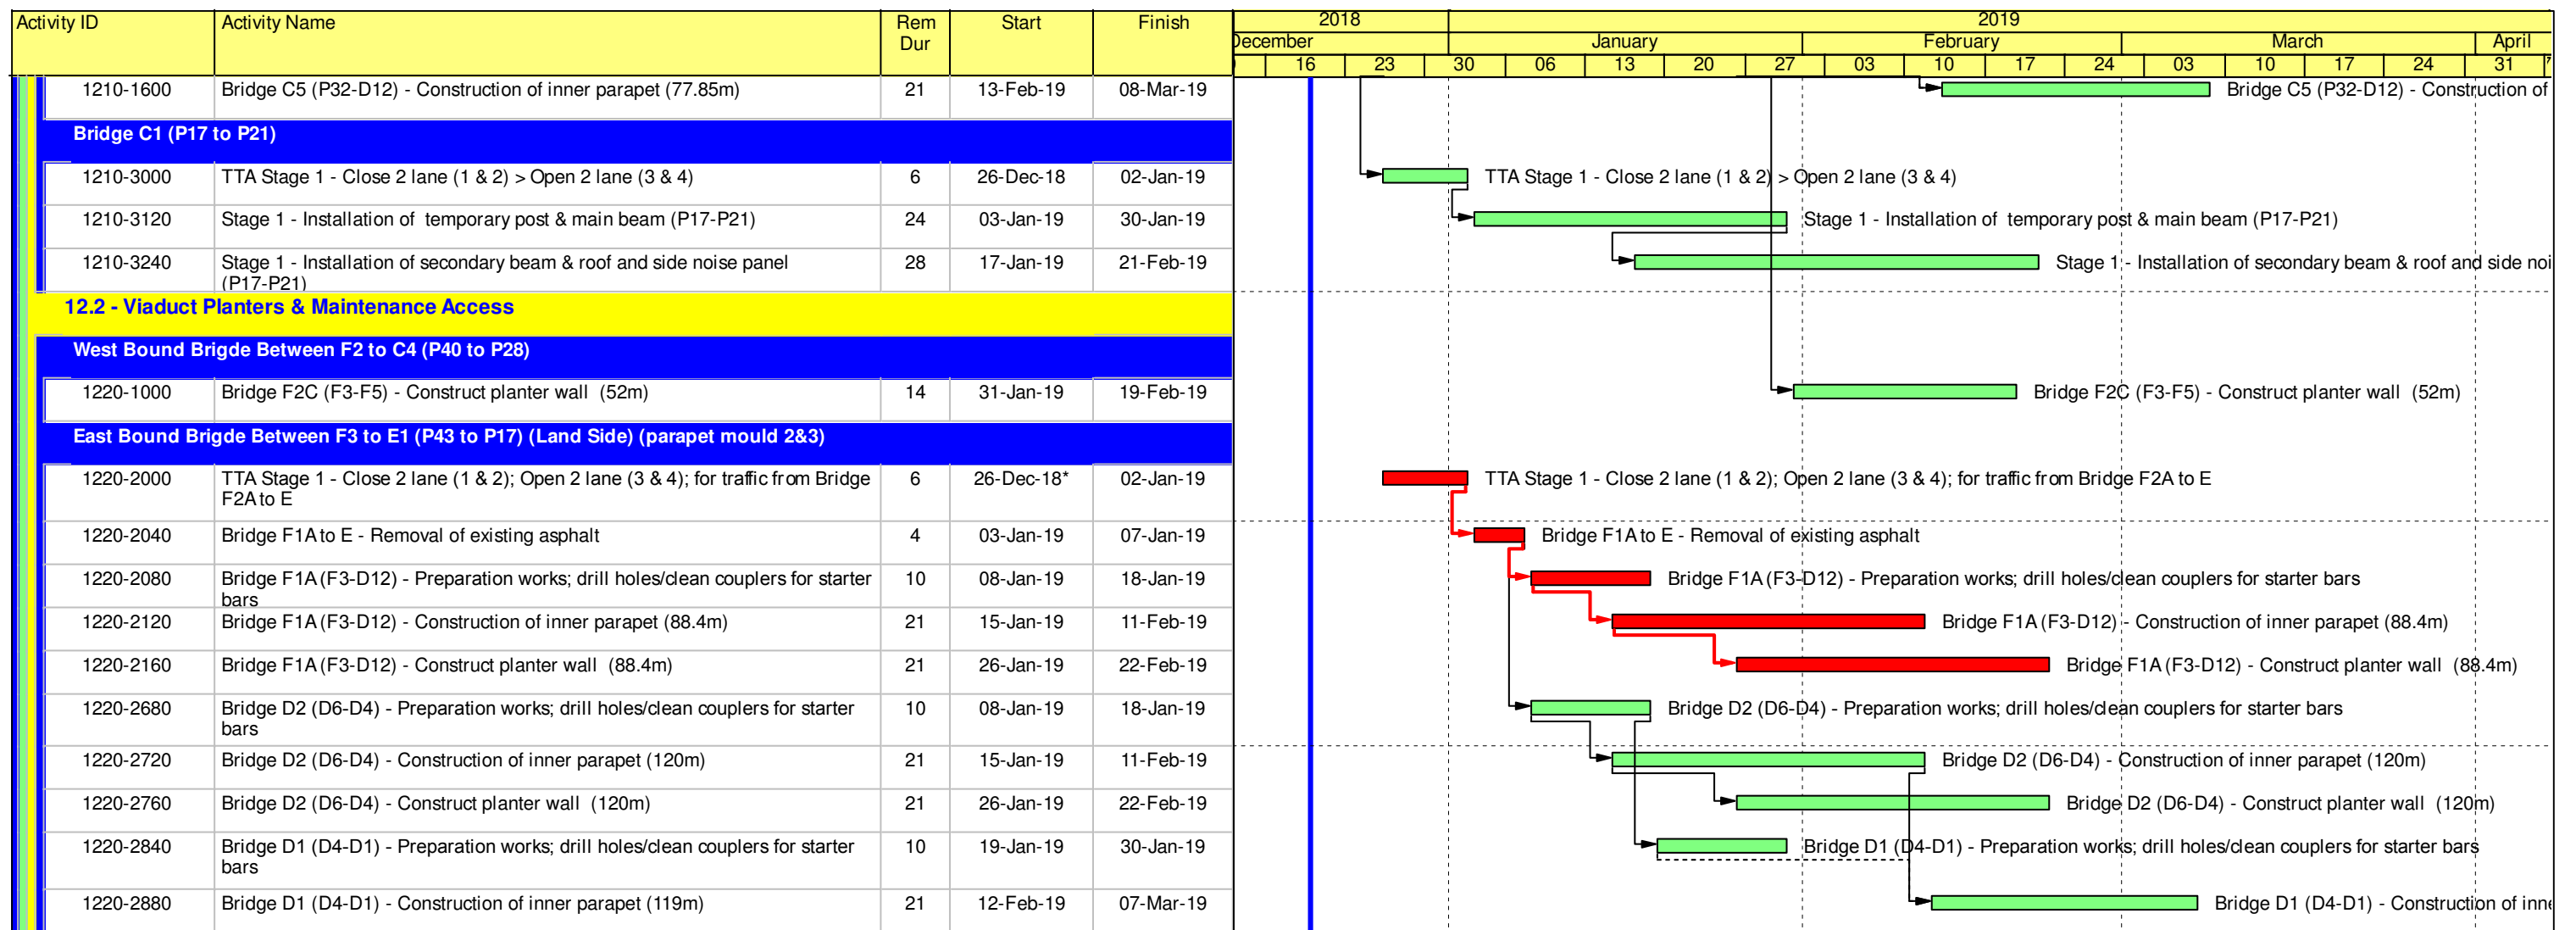

Contract HY/2009/19
Three Months Rolling Programme (20.Dec.2018 to 20.Mar.2019)

Activity ID	Activity Name	Original Duration	Start	Finish	2018				2019											
					Dec	Jan	Feb	Mar	Jan	Feb	Mar	Apr								
Total		2504	21-Mar-13 A	27-Jan-20																
DWP-08 - (2) - Update Progress As of 20 Dec 18		2504	21-Mar-13 A	27-Jan-20																
Works in KD9 (Include Re-provisioning Works of KD4,KD5)		341	30-Jan-18 A	27-Jan-19																
External Works Under KD9		201	30-Jan-18 A	17-Jan-19																
Zone 4 up to Elderly Facilities		201	30-Jan-18 A	17-Jan-19																
Elderly Facilities V/039 Received on 22 Jun 2017		201	30-Jan-18 A	17-Jan-19																
EXW_2270	Facilities fabrication	90	30-Jan-18 A	15-Jan-19																
EXW_2280	Ground levelling, drainage works and safety met installation	30	16-Nov-18 A	17-Jan-19																
Additional Walkway & Arbour V/040 Received on 22 Aug 2017		30	03-May-18 A	27-Nov-18 A																
EXW_2320	Arbour installation and walkway construction	30	03-May-18 A	27-Nov-18 A																
Reverting Traffic for IEC,VP Rd & TF St & Seawall Reinstatement (KD9)		341	13-Apr-18 A	27-Jan-19																
TTA Revert Traffic Back to Original Alignment		251	13-Apr-18 A	25-Dec-18																
East Bound TTA - IEC East Bound, Victoria Park Road & footpath along Sea Side		146	20-Jun-18 A	07-Dec-18 A																
TTM Stage 1 - IEC (East Bound)		6	01-Dec-18 A	07-Dec-18 A																
Reinstatement Existing Structure		6	01-Dec-18 A	07-Dec-18 A																
EB_1020	Install metal parapet on parapet wall (30m)	6	01-Dec-18 A	07-Dec-18 A																
TTM Stage 2 - Revert Traffic back to Original Victoria Road		4	01-Dec-18 A	07-Dec-18 A																
Existing Bridge Parapet Reinstatement		4	01-Dec-18 A	07-Dec-18 A																
EB_1180	Install metal parapet on parapet wall (40m)	4	01-Dec-18 A	07-Dec-18 A																
TTM Stage 3 - Reinstatement of Footpath along Seafront		15	20-Jun-18 A	04-Aug-18 A																
Reinstatement of Existing Utilities at Existing Footpath		2	20-Jun-18 A	20-Jun-18 A																
EB_1580	Water main Connection by WSD	2	20-Jun-18 A	20-Jun-18 A																
Reinstatement of Permanent Footpath at Seafront		1	04-Aug-18 A	04-Aug-18 A																
EB_1650	Pedestrian diversion on Permanent Footpath	1	04-Aug-18 A	04-Aug-18 A																
West Bound - IEC West Bound & Tsing fung Street		251	13-Apr-18 A	25-Dec-18																
TTM Stage 2 - Revert Traffic back to Original Tsing Fung Street		5	29-Dec-18 A	25-Dec-18																
Existing Bridge Parapet Reinstatement		5	29-Dec-18 A	25-Dec-18																
IECW_1140	Install metal parapet on parapet wall (60m)	5	29-Dec-18 A	25-Dec-18																
TTM Stage 3 - Reinstatement of Victoria Park		21	13-Apr-18 A	01-Dec-18 A																
Reinstatement Works inside Victoria Park		21	13-Apr-18 A	01-Dec-18 A																
IECW_1470	Slope Reinstatement of Victoria Park	21	13-Apr-18 A	01-Dec-18 A																
Completion of Minor Outstanding / Remaining Works for KD9		230	03-May-18 A	27-Jan-19																
East Bound - Minor Outstanding Works in Footpath after Substantial Completion of KD9		137	27-Jun-18 A	20-Dec-18 A																
Minor Reinstatement Works for Existing Sign Gantry		63	19-Jul-18 A	19-Sep-18 A																
EB_1780	Erect Sign Gantry Steel Supports and Sign Gantry Beam across VPR and IEC E/B	4	19-Jul-18 A	05-Aug-18 A																
EB_1760	Connection of Public Lighting by HyD (Lighting)	2	14-Sep-18 A	18-Sep-18 A																
EB_1790	Installation of E & M at Sign Gantry (night work)	1	19-Sep-18 A	19-Sep-18 A																
Minor Reinstatement Works for Central Median of IEC & Footbridge		6	05-Dec-18 A	20-Dec-18 A																
EB_1810	Dismantlement of temp directional sign mounted on extg footbridge	1	05-Dec-18 A	05-Dec-18 A																
EB_1800	Reconstruction of central divider (6m long, night work)	6	17-Dec-18 A	20-Dec-18 A																
Minor Reinstatement Works for Footpath		9	27-Sep-18 A	15-Nov-18 A																
EB_1840	Re-provision of Tree	8	27-Sep-18 A	15-Nov-18 A																
EB_1830	Reinstatement of District Council Welcome Sign and opening plaque at Planter area	1	03-Oct-18 A	03-Oct-18 A																

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Page 1 of 2
Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel (Slip Road 8 Section) - 3 Months Rolling Programme

Date	Revision	Checked	Approved
20-Dec-18	DWP-08 (2) - 3 Months Rolling	TL	TL



Activity ID	Activity Name	Original Duration	Start	Finish	2018												2019											
					Dec				Jan				Feb				Mar				Apr				May			
					1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4
Minor Reinstatement Works for Bus Stop																												
EB_1870	Relocation of Bus Stop	1	27-Jun-18 A	27-Jun-18 A																								
EB_1880	Reinstate Planter(Previous Temporary Bus Stop)	5	20-Jul-18 A	05-Oct-18 A																								
Minor Reinstatement Works for Loop Detector																												
EB_1900	Construction of concrete plinth and fix counter housing for Loop Detector (ILDS)	3	14-Jul-18 A	14-Jul-18 A																								
EB_1890	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)	1	23-Aug-18 A	24-Aug-18 A																								
West Bound - Completion of Minor Outstanding / Remaining Works for KD9																												
Minor Reinstatement Works for Victoria Park																												
IECW_1500	Re-provision of Tree	32	03-May-18 A	27-Jan-19	Re-provision of Tree																							
IECW_1510	Laying Irrigation Main	10	27-Sep-18 A	30-Dec-18	Laying Irrigation Main																							
IECW_1520	Construct Landscape Footpath and Lightings	7	05-Nov-18 A	27-Dec-18	Construct Landscape Footpath and Lightings																							
Minor Reinstatement Works in IEC West Bound																												
IECW_1640	Erection of new precast concrete panels (12 nos.) at abutment M facing to VPR	2	13-Jul-18 A	17-Jul-18 A																								
IECW_1620	Repairing of concrete defects on extg concrete deck and abutment M	30	15-Oct-18 A	24-Nov-18 A	Repairing of concrete defects on extg concrete deck and abutment M																							
IECW_1610	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)	57	24-Nov-18 A	24-Dec-18 A	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)																							
IECW_1660	Replacement of new rubber seal on extg MJ at IEC W/B and E/B (night work)	4	26-Nov-18 A	31-Dec-18 A	Replacement of new rubber seal on extg MJ at IEC W/B and E/B (night work)																							
IECW_1600	Replacement of new movement joint at IEC W/B (Sun midnight only)	8	27-Dec-18 A	30-Dec-18 A	Replacement of new movement joint at IEC W/B (Sun midnight only)																							
Works in Victoria Park (KD4, KD5, KD9)																												
Re-Provisioning Works																												
Nursery Compound																												
Nursery compound																												
Fire Services																												
VP_NC_2030	FS inspection	14	20-Aug-18 A	27-Sep-18 A																								
Plumbing and Flushing Water Supplies																												
VP_NC_2100	WSD Inspection	14	19-Aug-18 A	19-Aug-18 A																								
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks																												
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)																												
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365	28-Jan-19	27-Jan-20																								
KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH>500mm)																												
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365	28-Jan-19	27-Jan-20																								
KD18 - Section 11: Transplanted Trees DBH>500mm in Portion VA and XII																												
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365	28-Jan-19	27-Jan-20																								
KD10 - Preservation and Protection of Trees																												
PPT_0000	Preservation and Protection of Existing Trees	1088	21-Mar-13 A	28-Jan-19	Preservation and Protection of Existing Trees																							
KD15 & KD8 - Mooring Components Upkeep (CBTS and ATS)																												
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979	15-May-14 A	21-Dec-18	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS																							



- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Date	Revision	Checked	Approved
20-Dec-18	DWP-08 (2) - 3 Months Rolling	TL	TL
