

Legend

Original Programme Period  
 as in version date 11/12/18  
 Extended Programme Period  
 as in this version date 21/1/19

Create Date: 21/12/19  
 Revised Date: 25/12/19  
 28/12/19  
 30/12/19  
 1/2/2019

Remaining Works Programme

項目	工序	Jan-19													Wc																																													
		Week 54			Week 55			Week 56			Week 01			Week 02																																														
		1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13															
1	Removal of Temporary Storage of Backfill material at Portion 5	Portion 5 運泥回填 WCR1 停止運泥因為Close P5 Exit						Portion 5 運泥回填 WCR1																																																				
2	Seawall 海床							受泥區原海床						填 400 萬石渣土換新水 (400m <sup>3</sup> )																																														
3	地面墊仔 & 100mm Subbase																																					做墊仔																						
4	舊直升機場, 海墘及梯台																			舊直升機場 Landing	清場	入機																																						
5	打 D-Wall																																					打 D-Wall 至 +1.5 (-45M) 回填	填泥 打 8 條 remaining D-Wall 至 +1.5 (15M) 回填																					
6	U Channel & 沙井																																					鋪設 1 條 300 沙井	北面東段 4 個 catchpit + 3000 渠 (108m) DN8, 1, DN8, 2						北面東段 3 個 catchpit + 3000 渠 DN8, 6						北面東段 DN8, 3									
																																						北面西段 1 個 catchpit + 300, 3750 渠 (56m) DN1, 1	北面中段 3000 渠						北面中段 3750 渠						北面中段 3750 渠									
																																						Area T (2 個 catchpit + 300/450 渠)						BACKFILL																
7	渠網 & 沙井																																					沙井 7350 and 7349						225 呎由 DN8, 5 至 7349						225 呎由 DN8, 5 至 7349										
																																						225 呎由 7350 和 7349 至 BCO						CCTV 7352, 7340, 7328, 7327 試表 7353, 7338, C1, 3						CCTV 7338 試表 7338										
8	IRRIGATION PIPE																																					subsoil drainage						approval of design						VVV046 核稿										
9	Fresh Water Main																																					VVV542 (21/12/18)						TTA approved in TMLG Meeting 5/12/18																
10	HRR 馬路																																					AREA ABCD remove PMSMA						Relay Area ABCD PMSMA						AREA E remove and relay BC+PMSMA						AREA F remove and relay BC+PMSMA				
																																						REMEDIAL TO CONCRETE LAYBY						REMEDIAL TO CONCRETE LAYBY																
10.1	HRR FLYOVER REMAINING WORK																																					VO258 MODIFICATION WORK AT ABUTMENT ROOM						VO253 PROVIDE STAINLESS STEEL LADDER AT ABUTMENT ROOM																
11	還原運泥街 Stage 0.5																																					EYA																						
12	博覽道東, WCR1 & WCR3 未完成工作																																					* Portion 2 Zone 1 清石渠 打石渠 填formation						* Zone 2a upto end of EYA 打石渠 填formation						* Zone 2a remaining area 打石渠										
																																						* Portion 2 Zone 2b 打石渠 填formation						REMEDIAL TO EXPO DRIVE COVERED WALKWAY						WCR3 填 Sub Base (100mm thk, 7000m <sup>2</sup> )										
																																						Caisson seawall defects						Caisson seawall defects						Caisson seawall defects										
																																						海墘圍欄如下 COPING (COMMENCEMENT DATE TO BE CONFIRMED)						WCR1&3 MAKE GOOD ARMOUR SLOPE PROFILE																



**Wan Chai Development Phase II - East Central - Wan Chai Bypass at Wan Chai**  
 Contract: HK/2009/02  
 Remaining Works Programme

項目	工序	Feb-10	Week 04							Week 05							19-Mar							Week 06							Week 07							Week 08							Week 09							Week						
		14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4							
1	Removal of Temporary Storage of Backfill material at Portion 5																																																									
2	Seawall海床	[Activities related to seawall construction]														[Activities related to seawall construction]																																										
3	地面墊仔& 100mm Subbase	[Activities related to subbase construction]																																																								
4	垂直升降機, 海墜及梯台	[Activities related to lift and platform construction]																																																								
5	打D-Wall																																																									
6	U Channel & 沙井	[Activities related to U channel and manholes]																																																								
7	渠網 & 沙井	[Activities related to sewerage network]																																																								
8	IRRIGATION PIPE	[Activities related to irrigation pipes]																																																								
9	Fresh Water Main	[Activities related to fresh water main]																																																								
10	HHR 馬路	[Activities related to HHR road]																																																								
10.1	HHR FLYOVER REMAINING WORK	[Activities related to HHR flyover]																																																								
11	通車理處街 Stage 0.5	[Activities related to Stage 0.5 road opening]																																																								
12	博覽道東, WCR1 & WCR3 未完成工作	[Activities related to WCR1 and WCR3]																																																								



Wan Chai Development Phase II - East  
Central - Wan Chai Bypass at Wan Chai

Contract: HK/2009/02

Remaining Works Programme

項目	工序	June																																				
		Week 18					Week 19					Week 20					Week 21					Week 22																
		27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30		
1	Removal of Temporary Storage of Backfill material at Portion 5																																					
2	Seawall 海床																																					
3	地面墊仔及 100mm Subbase																																					
4	舊直升機場, 海墜及梯台																																					
5	打 D-Wall																																					
6	U Channel & 沙井																																					
7	渠網及沙井																																					
8	IRRIGATION PIPE																																					
9	Fresh Water Main																																					
10	HHR 馬路																																					
10.1	HHR FLYOVER REMAINING WORK																																					
11	還原運盛街 Stage 0.5																																					
12	博覽道東, WCR1 & WCR3 未完成工作																																					



**CEDD Contract No. HK/2012/08  
Wan Chai Development Phase II  
Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019							
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
<b>HK/2012/08 Revised Works Programme Rev.12.0(DD 20 November 2017)</b>																									
<b>Key Dates and Milestone Dates</b>																									
<b>Sections of Works Completion (Included Not Granted EOT Entitlement of The Contractor)</b>																									
KD10840	Completion of Section IIIA	0		08-Sep-18*	0%																				
KD10860	Completion of Section IV	0		30-Aug-18*	0%																				
KD10880	Completion of Section V	0		26-Sep-18*	0%																				
KD11010	Completion of Section VII	0		14-Sep-18*	0%																				
KD11020	Completion of Section VIII	0		21-Sep-18*	0%																				
KD11040	Completion of Section IX	0		21-Sep-19*	0%																				
KD11060	Completion of Section X	0		21-Sep-18*	0%																				
<b>Planned Sections of Works Completion</b>																									
KD10080	Planned Section IIIA Completion - Road A2,A4, A5	0		08-Sep-18	0%																				
KD10100	Planned Section IV Completion - Slip Road 3	0		30-Aug-18	0%																				
KD10140	Planned Section V Completion - Remaining At-Grade Road	0		26-Sep-18	0%																				
KD10280	Planned Section VII Completion - Remainder Works	0		14-Sep-18	0%																				
KD10300	Planned Section VIII Completion - Landscape Softwork	0		21-Sep-18	0%																				
KD10320	Planned Section IX Completion - Establishment Works	0		21-Sep-19	0%																				
KD10340	Planned Section X Completion - Tree Protection & Preservation	0		21-Sep-18	0%																				
<b>Dredging and Reclamation</b>																									
<b>Marine Work Construction</b>																									
<b>Zone CRIII</b>																									
<b>Seawall Construction - Zone CRIII</b>																									
<b>Zone CRIII Seawall- 2nd Stage</b>																									
<b>Seawall 2 &amp; 12</b>																									
MAR21371	Zone CRIII - seawall 2 & 12 - Backfilling remaining portion (type A, geotextile and filter)	0	19-Jan-18 A	27-Jan-18 A	100%	■																			
<b>Zone D</b>																									
<b>Seawall Construction - Zone D</b>																									
<b>Seawall 10 &amp; 11</b>																									
MAR20630	Zone D - Seawall 10 & 11: Install remaining seawall block	14	20-Feb-18*	05-Mar-18	0%		■																		
MAR20650	Zone D - Seawall 10 & 11: Backfill Type A	7	06-Mar-18	12-Mar-18	0%			■																	
MAR20670	Zone D - Seawall 10 & 11: Lay geotextile and filter	7	13-Mar-18	19-Mar-18	0%			■																	
<b>Works for Section Completion</b>																									
<b>Construction</b>																									
<b>Section III A - Road A2, A4 &amp; A5</b>																									
<b>Roadwork &amp; Utilities - Section 1 (L1806 - L1801)</b>																									

Data Date: 20-Feb-18

- ◆ Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Remaining Level of Effort

**Updated Works Programme Rev.12  
(Ref. to Rev.12 as of 20 Feburary 2018)**

Date	Revision	Checked	Approved
20-Feb-18	12		




















**CEDD Contract No. HK/2012/08**  
**Wan Chai Development Phase II**  
**Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019					
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
<b>Promenade Seawall Parapet Construction &amp; EVA</b>																							
SVII12000	Sec VII - Precast parapet	67	18-Nov-17 A	14-May-18	0%																		
SVII12010	Sec VII - Zone CRIII - seawall parapet: Backfilling	14	20-Feb-18	07-Mar-18	0%																		
SVII12120	Sec VII - Zone CRIII - seawall parapet: Construct mass concrete coping	30	08-Mar-18	16-Apr-18	0%																		
SVII12122	Sec VII - Zone CRIII - seawall parapet: reinforced concret coping	17	17-Apr-18	07-May-18	0%																		
SVII12140	Sec VII - Zone CRIII - seawall parapet: construct seawall parapet	30	08-May-18	12-Jun-18	0%																		
SVII12160	Sec VII - CRIII - EVA: watermain	14	13-Jun-18	29-Jun-18	0%																		
SVII12180	Sec VII - CRIII - EVA: U-channel	14	30-Jun-18	17-Jul-18	0%																		
SVII12200	Sec VII - CRIII - EVA: bituminous layer	5	18-Jul-18	23-Jul-18	0%																		
SVII12220	Sec VII - CRIII - EVA: paving block	30	24-Jul-18	27-Aug-18	0%																		
SVII13120	Sec VII - Zone A1, A2 & B - seawall parapet: Construct mass concrete coping	14	28-Dec-17 A	07-Mar-18	68.18%																		
SVII13122	Sec VII - Zone A1, A2 & B - seawall parapet: reinforced concrete coping	18	08-Mar-18	28-Mar-18	0%																		
SVII13140	Sec VII - Zone A1, A2 & B - seawall parapet: Construct seawall parapet	30	09-Apr-18	14-May-18	0%																		
SVII13160	Sec VII - Zone A1, A2 & B - EVA: watermain	14	15-May-18	31-May-18	0%																		
SVII13180	Sec VII - Zone A1, A2 & B - EVA: U-channel	14	01-Jun-18	16-Jun-18	0%																		
SVII13182	Sec VII - Zone A1, A2 & B - EVA: bituminous layer	5	19-Jun-18	23-Jun-18	0%																		
SVII13184	Sec VII - Zone A1, A2 & B - EVA: paving block	30	25-Jun-18	30-Jul-18	0%																		
SVII13200	Sec VII - Zone D - seawall parapet: Remove temporary seawall block	21	07-Mar-18	03-Apr-18	0%																		
SVII13220	Sec VII - Zone D - seawall parapet: Construct mass concrete	30	04-Apr-18	10-May-18	0%																		
SVII13222	Sec VII - Zone D - seawall parapet: reinforced concrete coping	18	11-May-18	01-Jun-18	0%																		
SVII13240	Sec VII - Zone D - seawall parapet: Construct seawall parapet	25	02-Jun-18	03-Jul-18	0%																		
SVII13260	Sec VII - Zone D - EVA : watermain	14	04-Jul-18	19-Jul-18	0%																		
SVII13280	Sec VII - Zone D - EVA : U-channel	14	20-Jul-18	04-Aug-18	0%																		
SVII13300	Sec VII - Zone D - EVA : bituminous layer	5	06-Aug-18	10-Aug-18	0%																		
SVII13320	Sec VII - Zone D - EVA : paving block	30	11-Aug-18	14-Sep-18	0%																		
<b>Promenade Footpath</b>																							
<b>Section 1</b>																							
SVII10440	Sec VII - section 1 footpath - drainage works : connection pipe & U -channel	10	24-May-18	04-Jun-18	0%																		
SVII10445	Sec VII - section 1 footpath - watermain	7	05-Jun-18	12-Jun-18	0%																		
SVII10460	Sec VII - section 1 footpath - lighting	7	13-Jun-18	21-Jun-18	0%																		
SVII10500	Sec VII - section 1 footpath - paving block	21	22-Jun-18	17-Jul-18	0%																		
<b>Section 2</b>																							
SVII12610	Sec VII - section 2 footpath - drainage works : L2202 - L2203A	20	20-Feb-18	14-Mar-18	0%																		
SVII12615	Sec VII - section 2 footpath - watermain	7	15-Mar-18	22-Mar-18	0%																		
SVII12630	Sec VII - section 2 footpath - utilities: TCSS	21	23-Mar-18	20-Apr-18	0%																		
SVII12670	Sec VII - section 2 footpath - paving block	30	21-Apr-18	28-May-18	0%																		
<b>Section 3</b>																							
SVII12850	Sec VII - section 3 footpath - watermain	17	20-Feb-18	10-Mar-18	0%																		
SVII12870	Sec VII - section 3 footpath - utilities (HEC, TCSS, HGC, PCCW)	40	12-Mar-18	02-May-18	0%																		
SVII12875	Sec VII - 3 footpath - drainage works :U chanel	14	03-May-18	18-May-18	0%																		







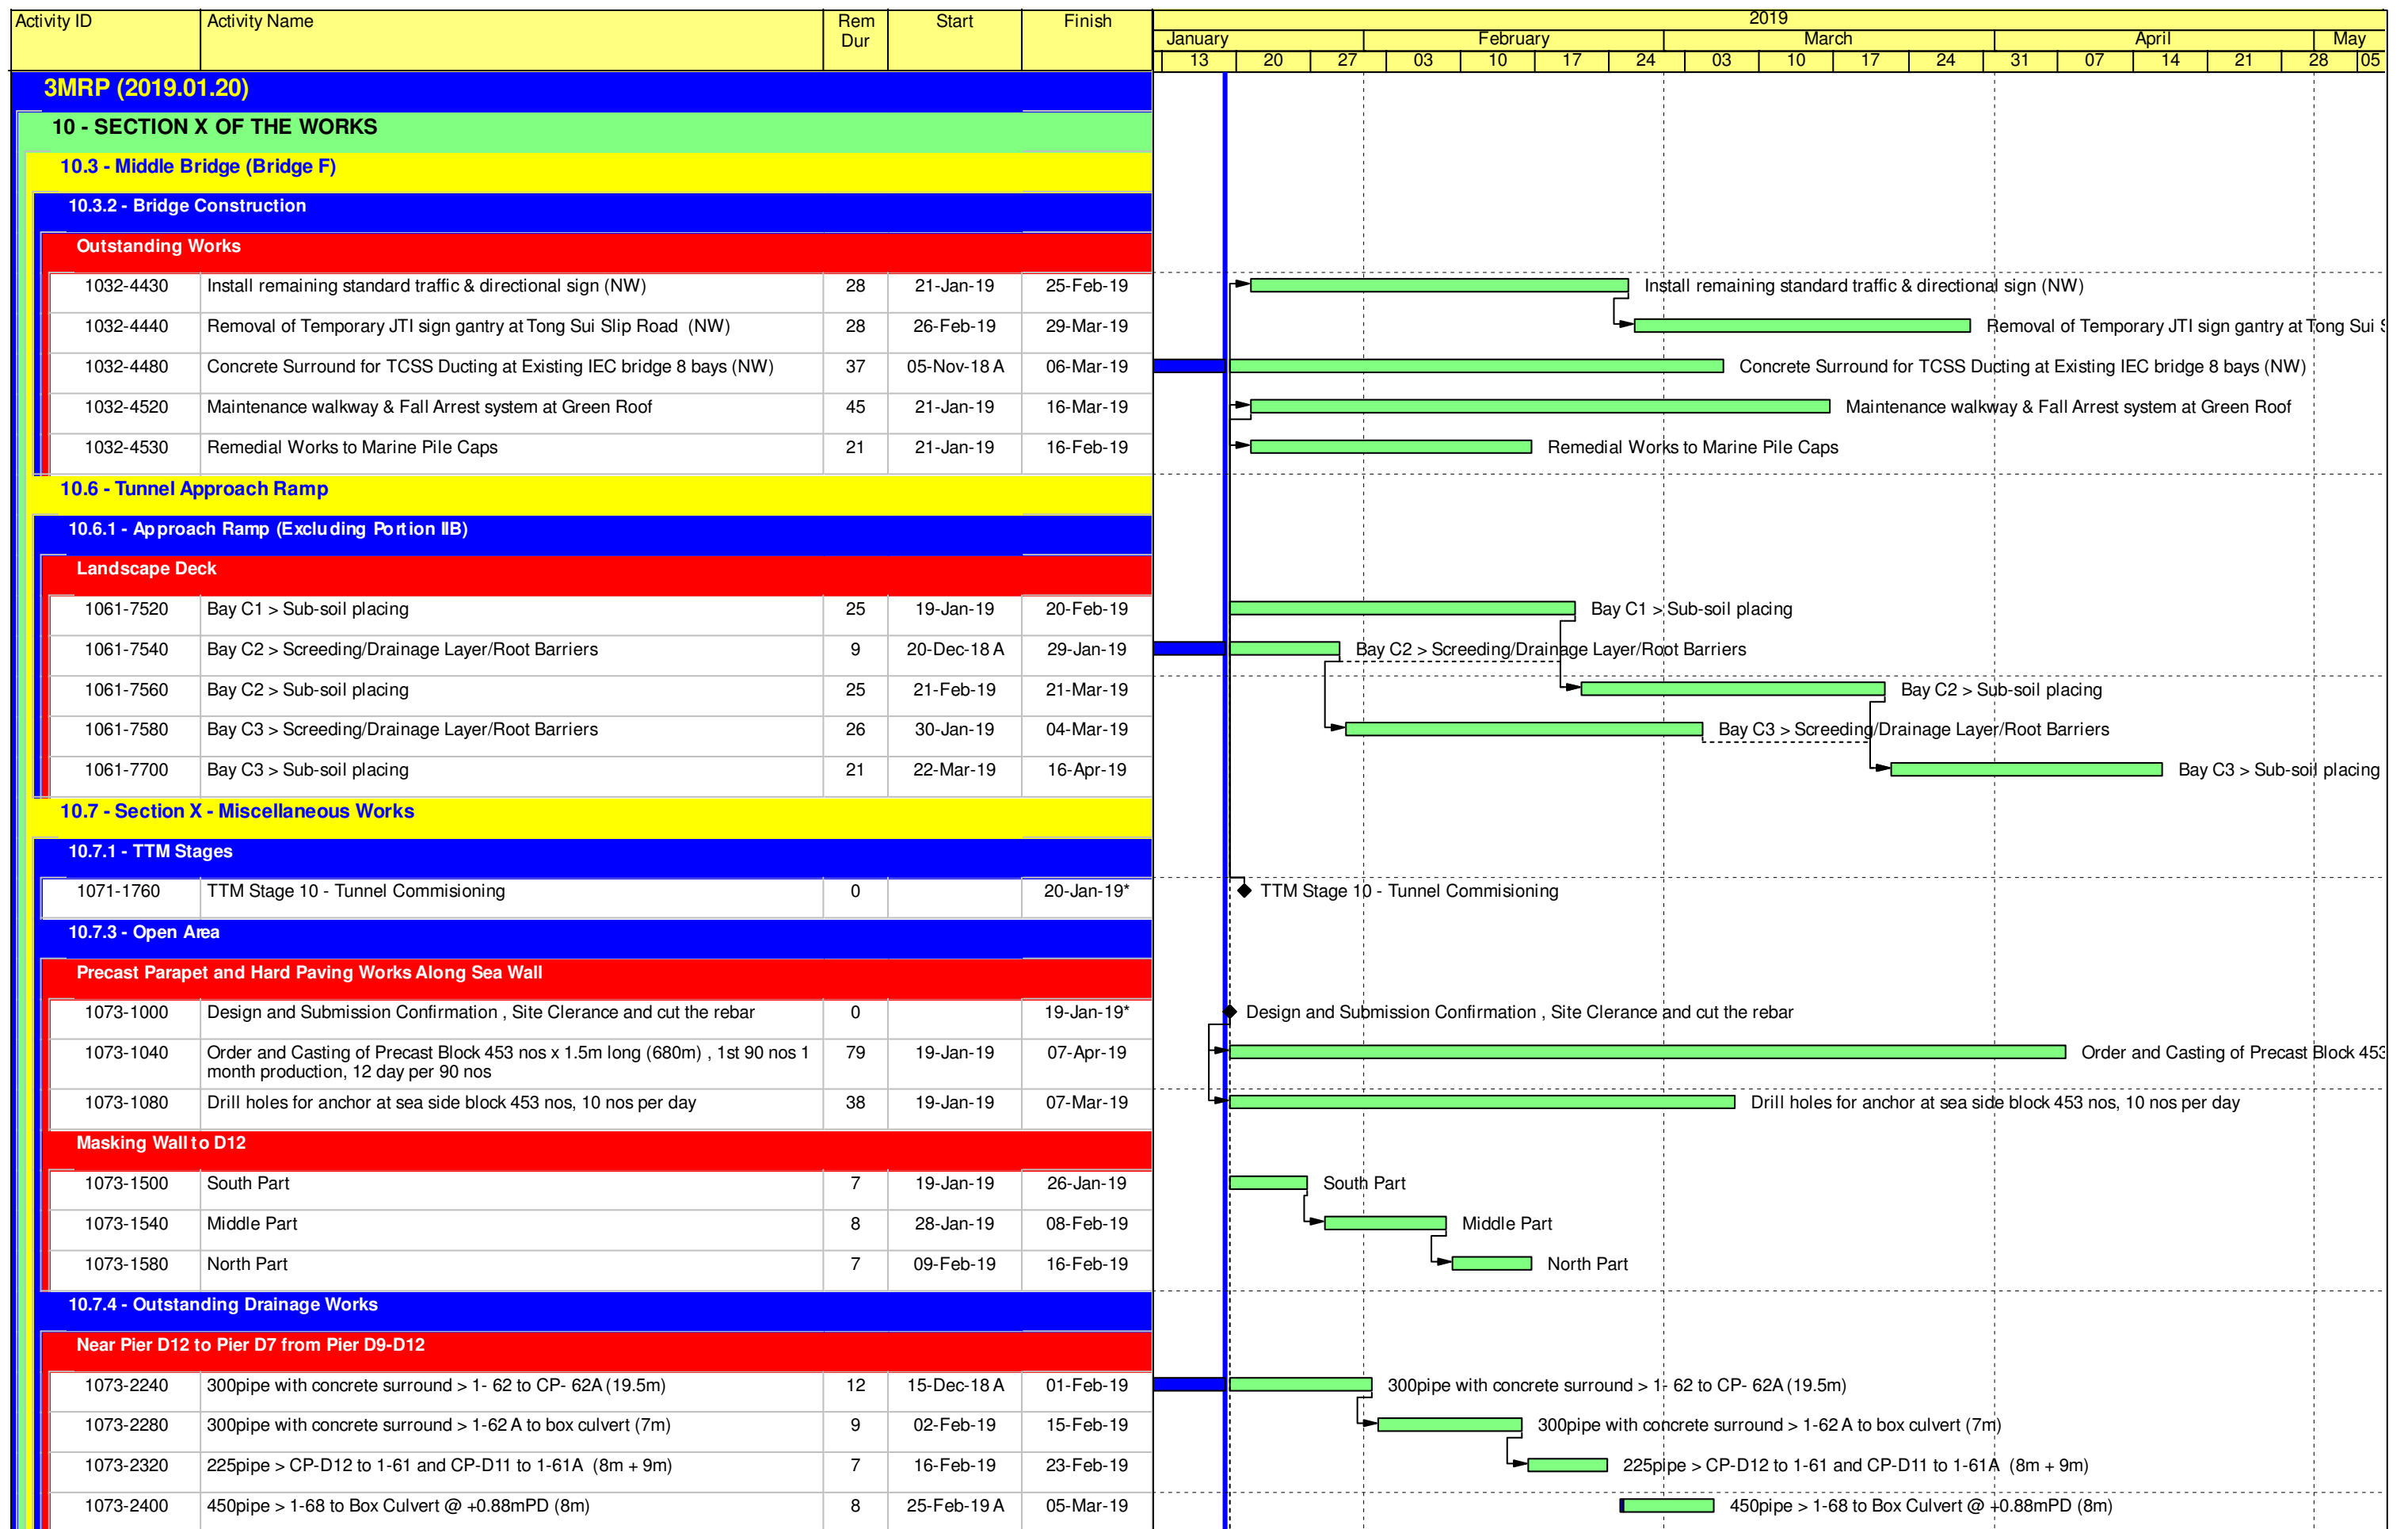

█ Remaining Level of Effort    █ Remaining Work  
█ Actual Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Jan.2019 to 20.Apr.2019)**





**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Jan.2019 to 20.Apr.2019)**







Activity ID	Activity Name	Rem Dur	Start	Finish	2019																
					January			February				March				April				May	
					13	20	27	03	10	17	24	03	10	17	24	31	07	14	21	28	05
1220-2120	Bridge F1A (F3-D12) - Construction of inner parapet (88.4m)	21	13-Feb-19	08-Mar-19																	
1220-2160	Bridge F1A (F3-D12) - Construct planter wall (88.4m)	21	25-Feb-19	20-Mar-19																	
1220-2680	Bridge D2 (D6-D4) - Preparation works; drill holes/clean couplers for starter bars	10	02-Feb-19	16-Feb-19																	
1220-2720	Bridge D2 (D6-D4) - Construction of inner parapet (120m)	21	13-Feb-19	08-Mar-19																	
1220-2760	Bridge D2 (D6-D4) - Construct planter wall (120m)	21	25-Feb-19	20-Mar-19																	
1220-2840	Bridge D1 (D4-D1) - Preparation works; drill holes/clean couplers for starter bars	10	18-Feb-19	28-Feb-19																	
1220-2880	Bridge D1 (D4-D1) - Construction of inner parapet (119m)	21	09-Mar-19	02-Apr-19																	
<b>12.3 - Waterworks</b>																					
1230-1000	Irrigation System - Landscape Deck	121	21-Jan-19	19-Jun-19																	
<b>12.4 - Soft Landscape</b>																					
1240-1000	Top soil & Footpath at Landscape Deck & green roof	97	23-Mar-19	20-Jul-19																	
<b>15 - SECTION 13A OF THE WORKS</b>																					
<b>15.1 - Soft Landscape</b>																					
1510-1000	Establishment Works at Portion XIII	365	14-May-19	12-May-20																	

Remaining Level of Effort    Remaining Work  
 Actual Level of Effort    Critical Remaining Work  
 Actual Work    Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Jan.2019 to 20.Apr.2019)**



Activity ID	Activity Name	Original Duration	Start	Finish	2018				2019											
					Dec	Jan	Feb	Mar	Dec	Jan	Feb	Mar								
<b>Total</b>		2504	21-Mar-13 A	27-Jan-20																
<b>DWP-08 - (2) - Update Progress As of 20 Dec 18</b>		2504	21-Mar-13 A	27-Jan-20																
<b>Works in KD9 (Include Re-provisioning Works of KD4,KD5)</b>		341	30-Jan-18 A	27-Jan-19																
<b>External Works Under KD9</b>		201	30-Jan-18 A	17-Jan-19																
<b>Zone 4 up to Elderly Facilities</b>		201	30-Jan-18 A	17-Jan-19																
<b>Elderly Facilities V/039 Received on 22 Jun 2017</b>		201	30-Jan-18 A	17-Jan-19																
EXW_2270	Facilities fabrication	90	30-Jan-18 A	15-Jan-19																
EXW_2280	Ground levelling, drainage works and safety met installation	30	16-Nov-18 A	17-Jan-19																
<b>Additional Walkway &amp; Arbour V/040 Received on 22 Aug 2017</b>		30	03-May-18 A	27-Nov-18 A																
EXW_2320	Arbour installation and walkway construction	30	03-May-18 A	27-Nov-18 A																
<b>Reverting Traffic for IEC,VP Rd &amp; TF St &amp; Seawall Reinstatement (KD9)</b>		341	13-Apr-18 A	27-Jan-19																
<b>TTA Revert Traffic Back to Original Alignment</b>		251	13-Apr-18 A	25-Dec-18																
<b>East Bound TTA - IEC East Bound, Victoria Park Road &amp; footpath along Sea Side</b>		146	20-Jun-18 A	07-Dec-18 A																
<b>TTM Stage 1 - IEC (East Bound)</b>		6	01-Dec-18 A	07-Dec-18 A																
<b>Reinstatement Existing Structure</b>		6	01-Dec-18 A	07-Dec-18 A																
EB_1020	Install metal parapet on parapet wall (30m)	6	01-Dec-18 A	07-Dec-18 A																
<b>TTM Stage 2 - Revert Traffic back to Original Victoria Road</b>		4	01-Dec-18 A	07-Dec-18 A																
<b>Existing Bridge Parapet Reinstatement</b>		4	01-Dec-18 A	07-Dec-18 A																
EB_1180	Install metal parapet on parapet wall (40m)	4	01-Dec-18 A	07-Dec-18 A																
<b>TTM Stage 3 - Reinstatement of Footpath along Seafront</b>		15	20-Jun-18 A	04-Aug-18 A																
<b>Reinstatement of Existing Utilities at Existing Footpath</b>		2	20-Jun-18 A	20-Jun-18 A																
EB_1580	Water main Connection by WSD	2	20-Jun-18 A	20-Jun-18 A																
<b>Reinstatement of Permanent Footpath at Seafront</b>		1	04-Aug-18 A	04-Aug-18 A																
EB_1650	Pedestrian diversion on Permanent Footpath	1	04-Aug-18 A	04-Aug-18 A																
<b>West Bound - IEC West Bound &amp; Tsing fung Street</b>		251	13-Apr-18 A	25-Dec-18																
<b>TTM Stage 2 - Revert Traffic back to Original Tsing Fung Street</b>		5	29-Dec-18 A	25-Dec-18																
<b>Existing Bridge Parapet Reinstatement</b>		5	29-Dec-18 A	25-Dec-18																
IECW_1140	Install metal parapet on parapet wall (60m)	5	29-Dec-18 A	25-Dec-18																
<b>TTM Stage 3 - Reinstatement of Victoria Park</b>		21	13-Apr-18 A	01-Dec-18 A																
<b>Reinstatement Works inside Victoria Park</b>		21	13-Apr-18 A	01-Dec-18 A																
IECW_1470	Slope Reinstatement of Victoria Park	21	13-Apr-18 A	01-Dec-18 A																
<b>Completion of Minor Outstanding / Remaining Works for KD9</b>		230	03-May-18 A	27-Jan-19																
<b>East Bound - Minor Outstanding Works in Footpath after Substantial Completion of KD9</b>		137	27-Jun-18 A	20-Dec-18 A																
<b>Minor Reinstatement Works for Existing Sign Gantry</b>		63	19-Jul-18 A	19-Sep-18 A																
EB_1780	Erect Sign Gantry Steel Supports and Sign Gantry Beam across VPR and IEC E/B	4	19-Jul-18 A	05-Aug-18 A																
EB_1760	Connection of Public Lighting by HyD (Lighting)	2	14-Sep-18 A	18-Sep-18 A																
EB_1790	Installation of E & M at Sign Gantry (night work)	1	19-Sep-18 A	19-Sep-18 A																
<b>Minor Reinstatement Works for Central Median of IEC &amp; Footbridge</b>		6	05-Dec-18 A	20-Dec-18 A																
EB_1810	Dismantlement of temp directional sign mounted on extg footbridge	1	05-Dec-18 A	05-Dec-18 A																
EB_1800	Reconstruction of central divider (6m long, night work)	6	17-Dec-18 A	20-Dec-18 A																
<b>Minor Reinstatement Works for Footpath</b>		9	27-Sep-18 A	15-Nov-18 A																
EB_1840	Re-provision of Tree	8	27-Sep-18 A	15-Nov-18 A																
EB_1830	Reinstatement of District Council Welcome Sign and opening plaque at Planter area	1	03-Oct-18 A	03-Oct-18 A																

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Page 1 of 2  
**Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel (Slip Road 8 Section) - 3 Months Rolling Programme**

Date	Revision	Checked	Approved
20-Dec-18	DWP-08 (2) - 3 Months Rolling	TL	TL



Activity ID	Activity Name	Original Duration	Start	Finish	2018				2019			
					Dec	Jan	Feb	Mar	Dec	Jan	Feb	Mar
<b>Minor Reinstatement Works for Bus Stop</b>												
EB_1870	Relocation of Bus Stop	1	27-Jun-18 A	27-Jun-18 A								
EB_1880	Reinstate Planter(Previous Temporary Bus Stop)	5	20-Jul-18 A	05-Oct-18 A								
<b>Minor Reinstatement Works for Loop Detector</b>												
EB_1900	Construction of concrete plinth and fix counter housing for Loop Detector (ILDS)	3	14-Jul-18 A	14-Jul-18 A								
EB_1890	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)	1	23-Aug-18 A	24-Aug-18 A								
<b>West Bound - Completion of Minor Outstanding / Remaining Works for KD9</b>												
<b>Minor Reinstatement Works for Victoria Park</b>												
IECW_1500	Re-provision of Tree	32	03-May-18 A	27-Jan-19	Re-provision of Tree							
IECW_1510	Laying Irrigation Main	10	27-Sep-18 A	30-Dec-18	Laying Irrigation Main							
IECW_1520	Construct Landscape Footpath and Lightings	7	05-Nov-18 A	27-Dec-18	Construct Landscape Footpath and Lightings							
<b>Minor Reinstatement Works in IEC West Bound</b>												
IECW_1640	Erection of new precast concrete panels (12 nos.) at abutment M facing to VPR	2	13-Jul-18 A	17-Jul-18 A								
IECW_1620	Repairing of concrete defects on extg concrete deck and abutment M	30	15-Oct-18 A	24-Nov-18 A	Repairing of concrete defects on extg concrete deck and abutment M							
IECW_1610	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)	57	24-Nov-18 A	24-Dec-18 A	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)							
IECW_1660	Replacement of new rubber seal on extg MJ at IEC W/B and E/B (night work)	4	26-Nov-18 A	31-Dec-18 A	Replacement of new rubber seal on extg MJ at IEC W/B and E/B (night work)							
IECW_1600	Replacement of new movement joint at IEC W/B (Sun midnight only)	8	27-Dec-18 A	30-Dec-18 A	Replacement of new movement joint at IEC W/B (Sun midnight only)							
<b>Works in Victoria Park (KD4, KD5, KD9)</b>												
<b>Re-Provisioning Works</b>												
<b>Nursery Compound</b>												
<b>Nursery compound</b>												
<b>Fire Services</b>												
VP_NC_2030	FS inspection	14	20-Aug-18 A	27-Sep-18 A								
<b>Plumbing and Flushing Water Supplies</b>												
VP_NC_2100	WSD Inspection	14	19-Aug-18 A	19-Aug-18 A								
<b>KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks</b>												
<b>KD11 - Section 7A: Portion XIV &amp; XV (Victoria Park Open Space)</b>												
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365	28-Jan-19	27-Jan-20								
<b>KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH&gt;500mm)</b>												
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365	28-Jan-19	27-Jan-20								
<b>KD18 - Section 11: Transplanted Trees DBH&gt;500mm in Portion VA and XII</b>												
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365	28-Jan-19	27-Jan-20								
<b>KD10 - Preservation and Protection of Trees</b>												
PPT_0000	Preservation and Protection of Existing Trees	1088	21-Mar-13 A	28-Jan-19	Preservation and Protection of Existing Trees							
<b>KD15 &amp; KD8 - Mooring Components Upkeep (CBTS and ATS)</b>												
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979	15-May-14 A	21-Dec-18	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS							



- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Date	Revision	Checked	Approved
20-Dec-18	DWP-08 (2) - 3 Months Rolling	TL	TL
