

Wan Chai Development Phase II - East
 Central - Wan Chai Bypass at Wan Chai
 Contract: HK/2009/02

Remaining Works Programme

項目	工序	Jan-19																																											
		Week 54							Week 55							Week 56							Week 01							Week 02						Wc									
		1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3		4	5	6	7	8	9	10	11	12
1	Removal of Temporary Storage of Backfill material at Portion 5	Portion 5 運泥回填 WCR1 停止運泥因為Close P5 Exit							Portion 5 運泥回填 WCR1																																				
2	Seawall海床	填600石面及鋪碎石(800m)																																											
3	地面墊層及100mm Subbase	做墊層																																											
4	舊直升機場、海墘及梯台	舊直升機場Landing 清場 入機																																											
5	打D-Wall	打D-Wall 至+1.5 (-48) 回填 鋪泥 打3區 remaining D-Wall 至+1.5 (15M) 回填																																											
6	U Channel & 沙井	Inculvert 埋石渠 北面東段4個catchpit+3000渠 (108m) DN8, 1 DN8, 2 北面西段1個catchpit+300, 3750渠 (56m) DN1, 1 北面中段3000渠 北面中段3個catchpit+3000渠 DN8, 6 北面中段3750 to 北面中段3個catchpit+300/450渠 BACKFILL																																											
7	渠網及沙井	沙井 7350 and 7349 225呎由DN8, 5至7349 225呎由7350和7349至BCO CCTV 7352, 7348, 7328, 7327 試表 7353, 7338, C1, 3 CCTV 7348 試表 7348																																											
8	IRRIGATION PIPE	subsoil drain approval of designs VVV046 埋管土																																											
9	Fresh Water Main	TTA approved in TMLG Meeting 5/12/18																																											
10	HRR 馬路	FOOTPATH ALONG HRR FOOTPATH AREA ABCD remove PMSMA Relay Area ABCD PMSMA waiting cone test result AREA E remove and relay BC+PMSMA waiting cone test result AREA F remove and relay BC+PMSMA survey REMEDIAL TO CONCRETE LAYBY remedial to concrete layby																																											
10.1	HRR FLYOVER REMAINING WORK	V0258 MODIFICATION WORK AT ABUTMENT ROOM place order and delivery V0253 PROVIDE STAINLESS STEEL LADDER AT ABUTMENT ROOM delivery																																											
11	還原運泥街 Stage 0.5																																												
12	博覽道東, WCR1 & WCR3 未完成工作	EVA * Portion 2 Zone 1 清石渠 打石渠 軟formation * Zone 2a upto end of EYA 打石渠 打石渠 軟formation * Zone 2a remaining area 打石渠 * Portion 2 Zone 2b 打石渠 軟formation REMEDIAL TO EXPO DRIVE COVERED WALKWAY 做磚 WCR3 填 Sub Base (100mm thk 7000m ²) subbase Caisson seawall defects 拆泥岩池 resumption of a monitoring point WCR1-1 海墘圍填如下COPING (COMMENCEMENT DATE TO BE CONFIRMED) WCR1&3 MAKE GOOD ARMOUR SLOPE PROFILE																																											

項目	工序	Feb-10				Week 04				Week 05				Week 06				19-Mar				Week 08	Week 09				Week																						
		14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2
1	Removal of Temporary Storage of Backfill material at Portion 5																																																
2	Seawall海床	<div style="display: flex; justify-content: space-between;"> 製Armour 製Precast Unit 失制物泥度原海床 </div>																																															
3	地面墊仔& 100mm Subbase	<div style="display: flex; justify-content: space-between;"> 碎石碎(100mm) (Whole Portion 3&4) </div>																																															
4	蓄直升機場, 海墜及梯台	<div style="display: flex; justify-content: space-between;"> Rockfill Level 第二度加塊磚 第三度第三度第五度磚 </div>																																															
5	打D-Wall																																																
6	U Channel & 沙井	<div style="display: flex; justify-content: space-between;"> 1個entchpit#3000渠(103m) DNS. 4 3個entchpit#3000渠(120m) DNS. 5 DNS. 7 3000渠(60m) ONL. 2 (60m) </div>																																															
7	渠網& 沙井	<div style="display: flex; justify-content: space-between;"> NR. 3 & 7350 (24m) 回流 19, 7356 </div>																																															
8	IRRIGATION PIPE	<div style="display: flex; justify-content: space-between;"> 灑花水3個WATER POINT & PLANTER#150U WATER METER BOX M01 WWW046 WSD approval </div>																																															
9	Fresh Water Main	<div style="display: flex; justify-content: space-between;"> STAGE 1 TTA (HRR) + HYS AECOM OFFICE STAGE 2 TTA (HRR) </div>																																															
10	HRR 馬路	<div style="display: flex; justify-content: space-between;"> Installation of precast end block concreting of footing Installation of barrier </div>																																															
10.1	HRR FLYOVER REMAINING WORK	<div style="display: flex; justify-content: space-between;"> carry out work install ladder </div>																																															
11	遵原理盛街 Stage 0.5	<div style="display: flex; justify-content: space-between;"> 遵原理盛街 Stage 0.5 PHASE 1 </div>																																															
12	博覽道東, WCR1 & WCR3 未完成工作	<div style="display: flex; justify-content: space-between;"> WCR3 圍鐵欄 (150M) (TBC (Alignment)) WANDOVER OF EYA (notional, to be confirmed) </div>																																															

Wan Chai Development Phase II - East
 Central - Wan Chai Bypass at Wan Chai
 Contract: HK/2009/02

Remaining Works Programme


項目	工序	15-Apr							Week 11							Week 12							Week 13							Week 14							Week 15							May							
		5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24
1	Removal of Temporary Storage of Backfill material at Portion 5																																																		
2	Seawall海床																																																		
3	地面壓仔& 100mm Subbase																																																		
4	舊直升機塔、海墘及梯台	<p> 拆 Precast 樓梯 落石原 2nd Coving 樓梯對 聚鐵 安裝Fender cut pipe pile 回填至+2.8 運海石海地台 鋪泥布及填膠 filter 鋼骨 Steel Beam </p>																																																	
5	打D-Wall																																																		
6	U Channel & 沙井																																																		
7	渠網及沙井																																																		
8	IRRIGATION PIPE																																																		
9	Fresh Water Main																																																		
10	HHR 馬路																																																		
10.1	HHR FLYOVER REMAINING WORK																																																		
11	還原運廢物 Stage 0.5	PHASE 2															PHASE 3																																		
12	博覽道東, WCR1 & WCR3 未完成工作																																																		

Wan Chai Development Phase II - East
Central - Wan Chai Bypass at Wan Chai
Contract: HK/2009/02
Remaining Works Programme

項目	工序	June																																			
		Week 18					Week 19					Week 20					Week 21					Week 22															
		27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
1	Removal of Temporary Storage of Backfill material at Portion 5																																				
2	Seawall 海床																																				
3	地面墊仔 100mm Subbase																																				
4	舊直升機場, 海墜及梯台																																				
5	打D-Wall																																				
6	U Channel & 沙井																																				
7	渠網 & 沙井																																				
8	IRRIGATION PIPE																																				
9	Fresh Water Main																																				
10	HHR 馬路																																				
10.1	HHR FLYOVER REMAINING WORK																																				
11	還原運盛街 Stage 0.5																																				
12	博覽道東, WCR1 & WCR3 未完成工作																																				

Programme for Outstanding and Defective Works

ID	Task Name	Duration	Start	Finish	2019																															
					July 2019							August 2019							September 2019							October 2019										
					14	17	20	23	26	29	1	4	7	10	13	16	19	22	25	28	31	3	6	9	12	15	18	21	24	27	30	3	6	9	12	15
1	15. Reinstatement of Hung Hing Road and Wan Shing Street in Accordance to Hung Hing Road Traffic Diversion Reinstatement Stage 0.5 Scheme Under VO No. 257 on Hung Hing Road	248 days	Fri 1/3/19	Sun 3/11/19																																
2	Phase 1 (Completed)	41 days	Fri 1/3/19	Wed 10/4/19																																
55	Phase 2 (Completed)	41 days	Tue 2/4/19	Sun 12/5/19																																
169	Yacht Club (40m Long)	43 days	Fri 15/3/19	Fri 26/4/19																																
182	Triangle Island (40m Long)	28 days	Fri 31/5/19	Thu 27/6/19																																
194	Phase 3	144 days	Thu 13/6/19	Sun 3/11/19																																
195	Advacne Work	35 days	Thu 13/6/19	Wed 17/7/19																																
200	Construction of Road Kerb and Pavement (Portion 5)	23 days	Thu 18/7/19	Fri 9/8/19																																
201	TTA Implementation	1 day	Thu 18/7/19	Thu 18/7/19																																
202	Demolition of Concrete and Asphalt Pavement	4 days	Fri 19/7/19	Mon 22/7/19																																
203	Removal of Steel Plate	4 days	Tue 23/7/19	Fri 26/7/19																																
204	Installation of Kerb	2 days	Sat 27/7/19	Sun 28/7/19																																
205	Subbase Levelling	1 day	Mon 29/7/19	Mon 29/7/19																																
206	SRT for Sub-base	5 days	Tue 30/7/19	Sat 3/8/19																																
207	Concrete Laying	1 day	Sun 4/8/19	Sun 4/8/19																																
208	Concrete Curing	3 days	Mon 5/8/19	Wed 7/8/19																																
209	Existing Asphalt Patch Up Work at Water Ponding Area (Photo 3, 4 & 5, Figure 211) (Concurrent with ID 669)	2 days	Thu 8/8/19	Fri 9/8/19																																
210	Demolition of water ponding area	1 day	Thu 8/8/19	Thu 8/8/19																																
211	Patching Up with Asphalt layer	1 day	Fri 9/8/19	Fri 9/8/19																																
212	Construction of Road Kerb and Pavement (Portion 4)	30 days	Fri 2/8/19	Sat 31/8/19																																
213	TTA Implementation	1 day	Sat 10/8/19	Sat 10/8/19																																
214	Demolition of Concrete and Asphalt Pavement	4 days	Sun 11/8/19	Wed 14/8/19																																
215	Removal of Steel Plate	4 days	Thu 15/8/19	Sun 18/8/19																																
216	Installation of Kerb	1 day	Mon 19/8/19	Mon 19/8/19																																
217	Subbase Levelling	1 day	Tue 20/8/19	Tue 20/8/19																																
218	SRT for Sub-base	5 days	Wed 21/8/19	Sun 25/8/19																																
219	Concrete Laying	1 day	Mon 26/8/19	Mon 26/8/19																																
220	Concrete Curing	3 days	Tue 27/8/19	Thu 29/8/19																																
221	Existing Asphalt Patch Up Work at Water Ponding Area (Photo 1, Figure 212)	2 days	Fri 30/8/19	Sat 31/8/19																																
224	Repaving Works at Yacht Club (Photo 2, Figure 216-1), Same as	30 days	Fri 2/8/19	Sat 31/8/19																																
231	Construction of Trial Pit and Installation of decking (Portion 3)	21 days	Mon 2/9/19	Sun 22/9/19																																
232	TTA Implementation	1 day	Mon 2/9/19	Mon 2/9/19																																
233	Demolition of Concrete and Asphalt Pavement	4 days	Tue 3/9/19	Fri 6/9/19																																
234	Removal of Steel Plate and installation of ELS for waterpipe	4 days	Sat 7/9/19	Tue 10/9/19																																
235	Kerb Installation and installation of decking	2 days	Wed 11/9/19	Thu 12/9/19																																
236	Subbase Levelling	1 day	Fri 13/9/19	Fri 13/9/19																																
237	SRT for Sub-base	5 days	Sat 14/9/19	Wed 18/9/19																																
238	Concrete Laying	1 day	Thu 19/9/19	Thu 19/9/19																																
239	Concrete Curing	3 days	Fri 20/9/19	Sun 22/9/19																																
240	Construction of Road Kerb and Pavement (Portion 2)	21 days	Mon 23/9/19	Sun 13/10/19																																
249	Construction of Road Kerb and Pavement (Portion 1)	21 days	Mon 14/10/19	Sun 3/11/19																																
258	Phase 3.5 (Remaining Works for HHR0.5 Scheme & Cable Duct Laying)	69 days	Tue 14/5/19	Sun 21/7/19																																
259	Construction of Footpath at HHR (Up Birdge)	11 days	Fri 31/5/19	Mon 10/6/19																																

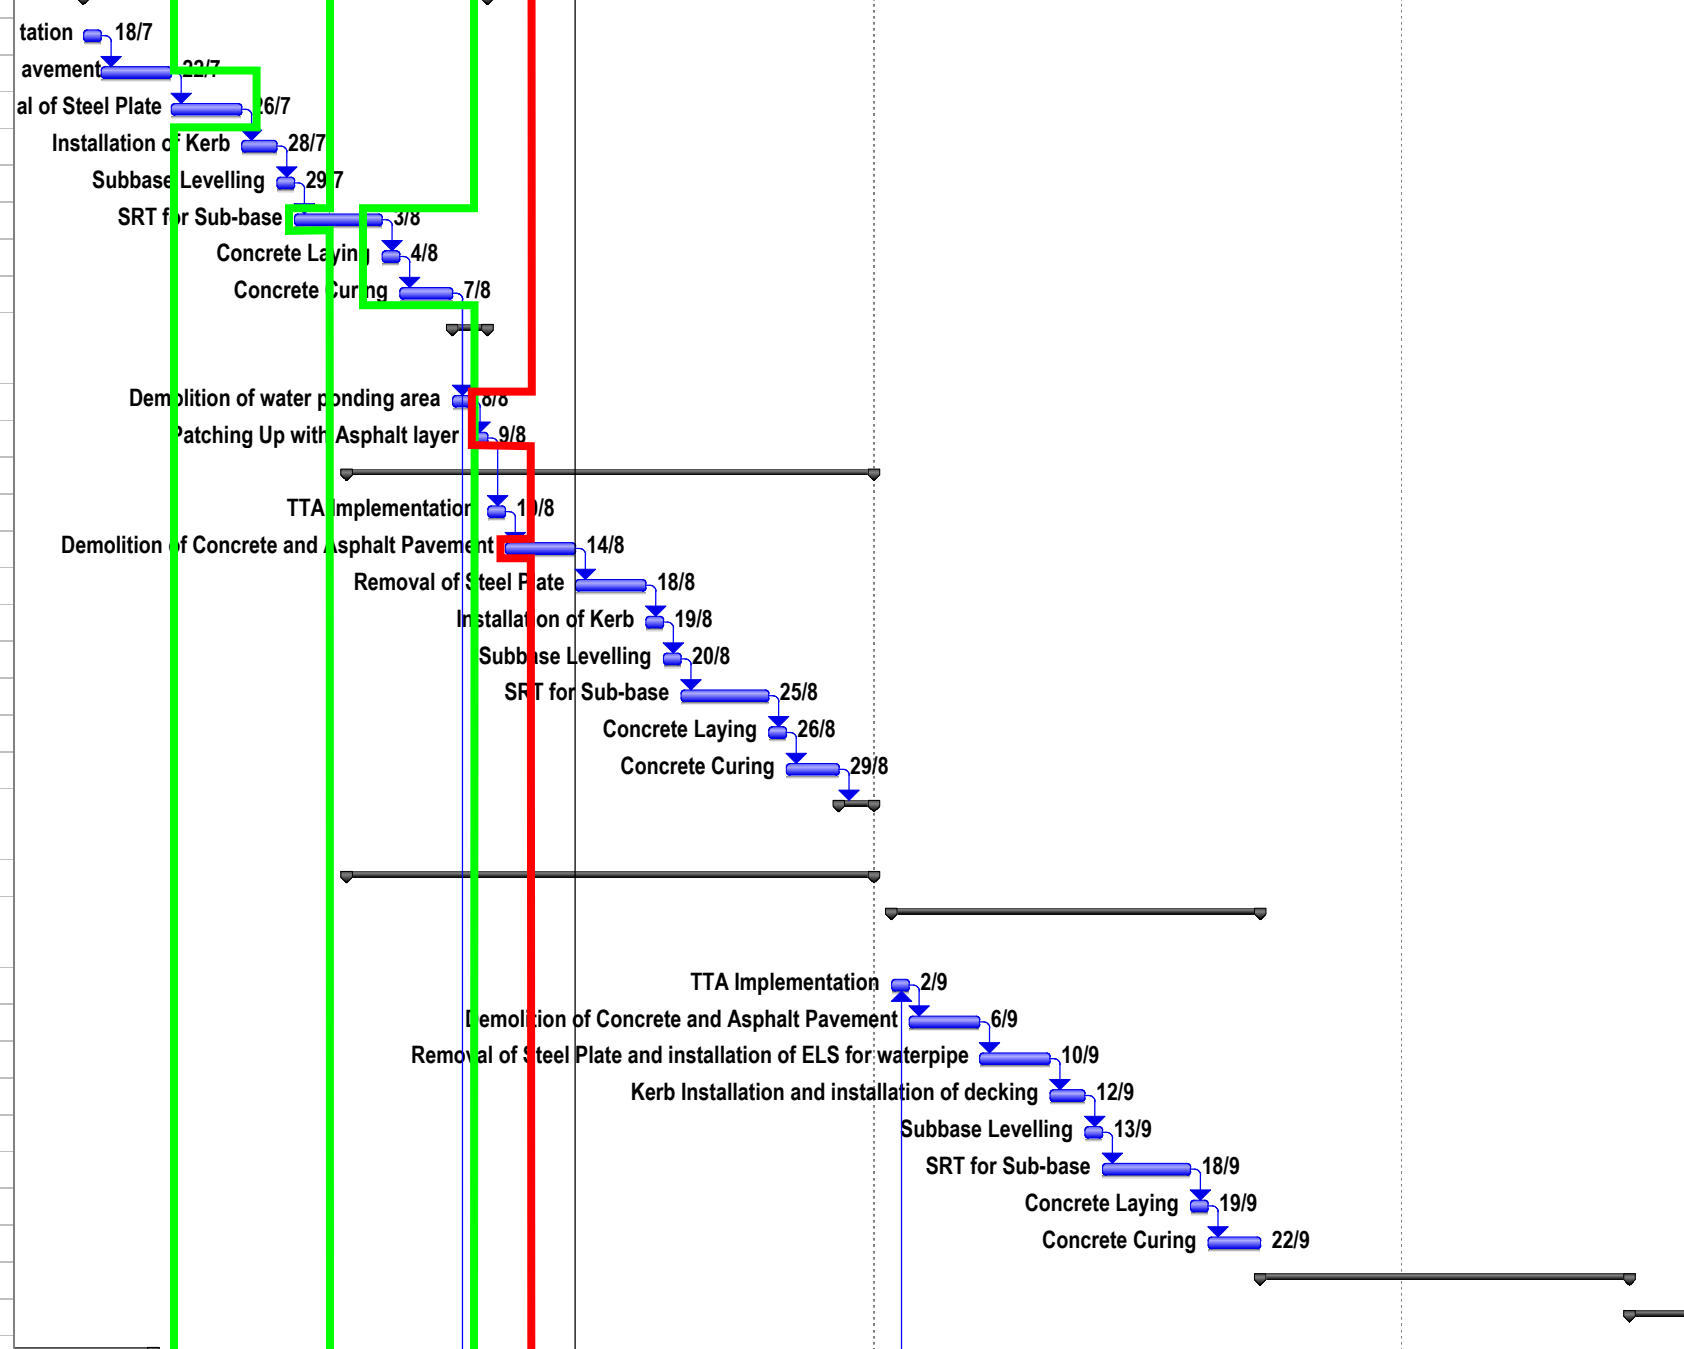

Task Milestone Rolled Up Task Rolled Up Progress External Tasks Group By Summary
Progress Summary Rolled Up Milestone Split Project Summary Deadline

Programme for Outstanding and Defective Works

ID	Task Name	Duration	Start	Finish	Qtr 3, 2019																														
					July 2019							August 2019							September 2019							October 2019									
387	Backfilling of Subbase Level and SRT	8 days	Tue 30/7/19	Tue 6/8/19	g of Subbase Level and SRT																														
388	RB Laying	1 day	Wed 7/8/19	Wed 7/8/19	RB Laying																														
389	BC Laying	1 day	Thu 8/8/19	Thu 8/8/19	BC Laying																														
390	WC Laying	1 day	Fri 9/8/19	Fri 9/8/19	WC Laying																														
391	Construction of Cross road duct (Opposite to SPCA)	85 days	Fri 17/5/19	Fri 9/8/19																															
392	Endorsement of TTA Drawing (Notional)	57 days	Fri 17/5/19	Fri 12/7/19	2/7																														
393	Application Road Work Advise	7 days	Sat 13/7/19	Fri 19/7/19	19/7																														
394	TTA Implementation	1 day	Sat 20/7/19	Sat 20/7/19	20/7																														
395	Demolition and Removal of Asphalt and Concrete Surface	5 days	Sun 21/7/19	Thu 25/7/19	25/7																														
396	Excavation for PVC duct laying	3 days	Fri 26/7/19	Sun 28/7/19	28/7																														
397	Duct Laying	2 days	Mon 29/7/19	Tue 30/7/19	30/7																														
398	Backfilling to Formaiton Level	1 day	Wed 31/7/19	Wed 31/7/19	31/7																														
399	Backfilling of Subbase Level and SRT	7 days	Thu 1/8/19	Wed 7/8/19	7/8																														
400	RB Laying	1 day	Thu 8/8/19	Thu 8/8/19	8/8																														
401	BC Laying	1 day	Fri 9/8/19	Fri 9/8/19	9/8																														
402	Construction of cross road duct (Bus Lane)	73 days	Fri 31/5/19	Sun 11/8/19																															
403	Endorsement of TTA Drawing	22 days	Fri 31/5/19	Fri 21/6/19																															
404	Application Road Work Advise	7 days	Sat 22/6/19	Fri 28/6/19																															
405	Cross road duct at Bus Lane (Northern Portion)	19 days	Fri 5/7/19	Tue 23/7/19																															
406	TTA Implementation	1 day	Fri 5/7/19	Fri 5/7/19																															
407	Demolition and Removal of Asphalt Surface	2 days	Sat 6/7/19	Sun 7/7/19																															
408	Excavation for PVC duct laying	3 days	Mon 8/7/19	Wed 10/7/19																															
409	Duct Laying	1 day	Thu 11/7/19	Thu 11/7/19																															
410	Backfilling to Formaiton Level	1 day	Fri 12/7/19	Fri 12/7/19																															
411	Backfilling of Subbase Level and SRT	8 days	Sat 13/7/19	Sat 20/7/19	20/7																														
412	RB Laying	1 day	Sun 21/7/19	Sun 21/7/19	21/7																														
413	BC Laying	1 day	Mon 22/7/19	Mon 22/7/19	22/7																														
414	WC Laying	1 day	Tue 23/7/19	Tue 23/7/19	23/7																														
415	Cross road duct at Bus Lane (Southern Portion)	19 days	Wed 24/7/19	Sun 11/8/19																															
416	TTA Implementation	1 day	Wed 24/7/19	Wed 24/7/19	24/7																														
417	Demolition and Removal of Asphalt Surface	2 days	Thu 25/7/19	Fri 26/7/19	26/7																														
418	Excavation for PVC duct laying	3 days	Sat 27/7/19	Mon 29/7/19	29/7																														
419	Duct Laying	1 day	Tue 30/7/19	Tue 30/7/19	30/7																														
420	Backfilling to Formaiton Level	1 day	Wed 31/7/19	Wed 31/7/19	31/7																														
421	Backfilling of Subbase Level and SRT	8 days	Thu 1/8/19	Thu 8/8/19	8/8																														
422	Road Base Laying	1 day	Fri 9/8/19	Fri 9/8/19	9/8																														
423	BC Laying	1 day	Sat 10/8/19	Sat 10/8/19	10/8																														
424	WC Laying	1 day	Sun 11/8/19	Sun 11/8/19	11/8																														
425	Construction of Cross road duct (EVA Access)	115 days	Fri 17/5/19	Sun 8/9/19																															
426	Endorsement of TTA Drawing	22 days	Fri 17/5/19	Fri 7/6/19																															
427	Application Road Work Advise	7 days	Sat 8/6/19	Fri 14/6/19																															
428	Seeking Permission from FSD for Enclosure of EVA access	27 days	Sat 8/6/19	Thu 4/7/19																															
429	Run-in at EVA (Eastern Portion)	16 days	Thu 8/8/19	Fri 23/8/19																															
430	TTA Implementation	1 day	Thu 8/8/19	Thu 8/8/19	8/8																														
431	Demolition and Removal of Asphalt Surface	1 day	Fri 9/8/19	Fri 9/8/19	9/8																														
432	Excavation for PVC duct laying	1 day	Sat 10/8/19	Sat 10/8/19	10/8																														
433	Duct Laying	1 day	Sun 11/8/19	Sun 11/8/19	11/8																														
434	Backfilling to Formaiton Level	1 day	Mon 12/8/19	Mon 12/8/19	12/8																														

Task Milestone Rolled Up Task Rolled Up Progress External Tasks Group By Summary

Progress Summary Rolled Up Milestone Split Project Summary Deadline

Programme for Outstanding and Defective Works

ID	Task Name	Duration	Start	Finish	Qtr 3, 2019																																
					July 2019							August 2019							September 2019							October 2											
435	Backfilling of Subbase Level and SRT	8 days	Tue 13/8/19	Tue 20/8/19	14	17	20	23	26	29	1	4	7	10	13	16	19	22	25	28	31	3	6	9	12	15	18	21	24	27	30	3	6	9	12	15	
436	RB Laying	1 day	Wed 21/8/19	Wed 21/8/19																																	
437	BC Laying	1 day	Thu 22/8/19	Thu 22/8/19																																	
438	WC Laying	1 day	Fri 23/8/19	Fri 23/8/19																																	
439	Run-in at EVA (Western Portion)	16 days	Sat 24/8/19	Sun 8/9/19																																	
440	TTA Implementation	1 day	Sat 24/8/19	Sat 24/8/19																																	
441	Demolition and Removal of Asphalt Surface	1 day	Sun 25/8/19	Sun 25/8/19																																	
442	Excavation for PVC duct laying	1 day	Mon 26/8/19	Mon 26/8/19																																	
443	Duct Laying	1 day	Tue 27/8/19	Tue 27/8/19																																	
444	Backfilling to Formaiton Level	1 day	Wed 28/8/19	Wed 28/8/19																																	
445	Backfilling of Subbase Level and SRT	8 days	Thu 29/8/19	Thu 5/9/19																																	
446	RB Laying	1 day	Fri 6/9/19	Fri 6/9/19																																	
447	BC Laying	1 day	Sat 7/9/19	Sat 7/9/19																																	
448	WC Laying	1 day	Sun 8/9/19	Sun 8/9/19																																	
449	Construction of Lighting Cable Duct (Yacht Club)	10 days	Mon 4/11/19	Wed 13/11/19																																	
450	TTA Implementation	1 day	Mon 4/11/19	Mon 4/11/19																																	
451	Demolition of Concrete Pavement	2 days	Tue 5/11/19	Wed 6/11/19																																	
452	PVC Duct Laying	1 day	Thu 7/11/19	Thu 7/11/19																																	
453	Backfilling of Trench	1 day	Fri 8/11/19	Fri 8/11/19																																	
454	Subbase Laying and SRT	4 days	Sat 9/11/19	Tue 12/11/19																																	
455	Concrete Laying	1 day	Wed 13/11/19	Wed 13/11/19																																	
456	Installation of Lamp Post (West of Triangular Island) (8 nos.)	26 days	Sat 10/8/19	Wed 4/9/19																																	
457	Inspection of laid cable duct by Hyd	7 days	Sat 10/8/19	Fri 16/8/19																																	
458	Preparation work by Hyd Lighting Division for instllation of Lamp Post (8 nos.)	14 days	Sat 17/8/19	Fri 30/8/19																																	
459	Installation of Lamp Post (2 nos./day)	5 days	Sat 31/8/19	Wed 4/9/19																																	
460	Installation of Lamp Post (East of Triangular Island to Yacht Club) (6 nos.)	26 days	Thu 14/11/19	Mon 9/12/19																																	
461	Inspection of laid cable duct Hyd	7 days	Thu 14/11/19	Wed 20/11/19																																	
462	Preparation work by HyD Lighting Division for instllation of Lamp Post (6 nos.)	14 days	Thu 21/11/19	Wed 4/12/19																																	
463	Installation of Lamp Post (2 nos./day)	5 days	Thu 5/12/19	Mon 9/12/19																																	
464	Construction Directional Sign at Triangle Island	213 days	Tue 14/5/19	Thu 12/12/19																																	
465	Advance Work	211 days	Tue 14/5/19	Tue 10/12/19																																	
466	Submit shop drawing of traffic sign and frame to AECOM	0 days	Tue 14/5/19	Tue 14/5/19																																	
467	Approval of shop drawing of traffic sign and frame by AECOM	14 days	Tue 14/5/19	Mon 27/5/19																																	
468	Procurement of traffic sign and frame	30 days	Tue 28/5/19	Wed 26/6/19																																	
469	Delivery of traffic sign and frame	0 days	Wed 26/6/19	Wed 26/6/19																																	
470	Design of footing	7 days	Thu 6/6/19	Thu 13/6/19																																	
471	Obtain ICE certificate for footing	1 day	Thu 13/6/19	Fri 14/6/19																																	
472	Submission to AECOM	0 days	Fri 14/6/19	Fri 14/6/19																																	
473	Approval of footing design	180 days	Fri 14/6/19	Tue 10/12/19																																	
474	Site Work	168 days	Fri 28/6/19	Thu 12/12/19																																	

Task Milestone Rolling Up Task Rolling Up Progress External Tasks Group By Summary

Progress Summary Rolling Up Milestone Split Project Summary Deadline

**CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019							
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
HK/2012/08 Revised Works Programme Rev.12.0(DD 20 November 2017)																									
Key Dates and Milestone Dates																									
Sections of Works Completion (Included Not Granted EOT Entitlement of The Contractor)																									
KD10840	Completion of Section IIIA	0		08-Sep-18*	0%																				
KD10860	Completion of Section IV	0		30-Aug-18*	0%																				
KD10880	Completion of Section V	0		26-Sep-18*	0%																				
KD11010	Completion of Section VII	0		14-Sep-18*	0%																				
KD11020	Completion of Section VIII	0		21-Sep-18*	0%																				
KD11040	Completion of Section IX	0		21-Sep-19*	0%																				
KD11060	Completion of Section X	0		21-Sep-18*	0%																				
Planned Sections of Works Completion																									
KD10080	Planned Section IIIA Completion - Road A2,A4, A5	0		08-Sep-18	0%																				
KD10100	Planned Section IV Completion - Slip Road 3	0		30-Aug-18	0%																				
KD10140	Planned Section V Completion - Remaining At-Grade Road	0		26-Sep-18	0%																				
KD10280	Planned Section VII Completion - Remainder Works	0		14-Sep-18	0%																				
KD10300	Planned Section VIII Completion - Landscape Softwork	0		21-Sep-18	0%																				
KD10320	Planned Section IX Completion - Establishment Works	0		21-Sep-19	0%																				
KD10340	Planned Section X Completion - Tree Protection & Preservation	0		21-Sep-18	0%																				
Dredging and Reclamation																									
Marine Work Construction																									
Zone CRIII																									
Seawall Construction - Zone CRIII																									
Zone CRIII Seawall- 2nd Stage																									
Seawall 2 & 12																									
MAR21371	Zone CRIII - seawall 2 & 12 - Backfilling remaining portion (type A, geotextile and filter)	0	19-Jan-18 A	27-Jan-18 A	100%	■																			
Zone D																									
Seawall Construction - Zone D																									
Seawall 10 & 11																									
MAR20630	Zone D - Seawall 10 & 11: Install remaining seawall block	14	20-Feb-18*	05-Mar-18	0%		■																		
MAR20650	Zone D - Seawall 10 & 11: Backfill Type A	7	06-Mar-18	12-Mar-18	0%			■																	
MAR20670	Zone D - Seawall 10 & 11: Lay geotextile and filter	7	13-Mar-18	19-Mar-18	0%			■																	
Works for Section Completion																									
Construction																									
Section III A - Road A2, A4 & A5																									
Roadwork & Utilities - Section 1 (L1806 - L1801)																									

Data Date: 20-Feb-18

- ◆ Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Remaining Level of Effort

**Updated Works Programme Rev.12
(Ref. to Rev.12 as of 20 February 2018)**

Date	Revision	Checked	Approved
20-Feb-18	12		

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019											
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
SIIIA10279C	Sec III A - section 1 carriageway - sewerage pipe from M/H 8C to F8B (night time): construct sewerage pipe	0	02-Jan-18 A	03-Feb-18 A	100%																								
SIIIA10293	Sec III A - section 1 carriageway - sewerage pipe from M/H F8B - F8A (night time)	6	05-Feb-18 A	26-Feb-18	0%																								
SIIIA10294	Sec III A - section 1 carriageway - sewerage pipe from M/H F8A - F8	8	17-Jan-18 A	28-Feb-18	27.27%																								
SIIIA10295	Sec III A - carriageway - works prior TTA stage 5: excavation and duct laying of TCSS and public lighting	7	18-Jan-18 A	27-Feb-18	0%																								
SIIIA10298	Sec III A - section 1 carriageway - works prior TTA stage 5: road kerb	5	28-Feb-18	05-Mar-18	0%																								
SIIIA10301	Sec III A - section 1 carriageway - works prior TTA stage 5: road formation	2	06-Mar-18	07-Mar-18	0%																								
SIIIA10302	Sec III A - section 1 carriageway - works prior TTA stage 5: laying asphalt	5	08-Mar-18	13-Mar-18	0%																								
SIIIA10303	Sec III A - section 1 carriageway - works prior TTA stage 5: road marking & preparation works	3	14-Mar-18	16-Mar-18	0%																								
SIIIA10310	Sec III A - section 1 carriageway - TTA stage 5: Implementation of TTA Stage 5	1	17-Mar-18	17-Mar-18	0%																								
SIIIA10310a	Sec III A - section 1 carriageway - TTA stage 5: remaining sewerage pipe for M/H F8A - M/H F8	12	19-Mar-18	04-Apr-18	0%																								
SIIIA10310b	Sec III A - section 1 carriageway - TTA stage 5: remaining sewerage pipe for M/H F8A - M/H F8B	18	06-Apr-18	26-Apr-18	0%																								
SIIIA10310c	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - remove sheetpile at U-trough west	5	19-Mar-18	23-Mar-18	0%																								
SIIIA10310d	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - remove temp. road access bay 5 of SR1	21	24-Mar-18	21-Apr-18	0%																								
SIIIA10310e	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - construct upstand wall above Dwall	25	23-Apr-18	23-May-18	0%																								
SIIIA10310f	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - roadside barrier	14	24-May-18	08-Jun-18	0%																								
SIIIA10310g	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - road formation	7	09-Jun-18	16-Jun-18	0%																								
SIIIA10310h	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - laying asphalt with transition slab	14	19-Jun-18	05-Jul-18	0%																								
SIIIA10312	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L2202 - L2201)	15	19-Mar-18	09-Apr-18	0%																								
SIIIA10312a	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L1805 - L1801)	15	10-Apr-18	26-Apr-18	0%																								
SIIIA10312b	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L1805-1807)	12	27-Apr-18	11-May-18	0%																								
SIIIA10313	Sec III A - roadwork and utilities section 1 carriageway - gully pipe (L1807 - L1801)	14	07-May-18	23-May-18	0%																								
SIIIA10320	Sec III A - roadwork and utilities section 1 carriageway - fresh watermain	7	24-May-18	31-May-18	0%																								
SIIIA10340	Sec III A - roadwork and utilities section 1 carriageway - utilities: HEC (80m) along carriageway	14	01-Jun-18	16-Jun-18	0%																								
SIIIA10360	Sec III A - roadwork and utilities section 1 carriageway - road kerb & formation	14	19-Jun-18	05-Jul-18	0%																								
SIIIA10400	Sec III A - roadwork and utilities section 1 carriageway - black top	7	06-Jul-18	13-Jul-18	0%																								
SIIIA10420	Sec III A - Implementation of TTA Stage 7P (Closure of U-turn at Expo Drive)	1	14-Jul-18	14-Jul-18	0%																								
SIIIA10440	Sec III A - roadwork and utilities section 1 carriageway : breaking existing asphalt	10	16-Jul-18	26-Jul-18	0%																								
SIIIA10460	Sec III A - roadwork and utilities section 1 carriageway: road kerb and formation	14	27-Jul-18	11-Aug-18	0%																								
SIIIA10480	Sec III A - roadwork and utilities section 1 carriageway : black top	10	13-Aug-18	23-Aug-18	0%																								
SIIIA10500	Sec III A - roadwork and utilities section 1 carriageway : roadmarking and road furniture	14	24-Aug-18	08-Sep-18	0%																								
Roadwork & Utilities - Section 2 (L1810 - L1807)																													
SIIIA12590	Sec III A - roadwork and utilities section 2 carriageway - black top	0	20-Jan-18 A	27-Jan-18 A	100%																								
Roadwork & Utilities - Section 3 (L1808 - L1102)																													
SIIIA12770	Sec III A - roadwork and utilities section 3 carriageway - utilities: HEC ducting (60m) & crossroad duct (PCCW & HGC)	0	20-Jan-18 A	07-Feb-18 A	100%																								
SIIIA12790	Sec III A - roadwork and utilities section 3 carriageway - road kerb & formation	17	08-Feb-18 A	10-Mar-18	0%																								
SIIIA12810	Sec III A - roadwork and utilities section 3 carriageway - black top	7	12-Mar-18	19-Mar-18	0%																								
Roadwork & Utilities - Section 6 (L1102 - L1411)																													
SIIIA13399	Sec III A - roadwork and utilities section 6 carriageway - gully pipe (L1101 - L1102)	0	12-Jan-18 A	26-Jan-18 A	100%																								
SIIIA13444	Sec III A - roadwork and utilities section 6 carriageway - watermain (road crossing)	0	27-Jan-18 A	03-Feb-18 A	100%																								
SIIIA13445	Sec III A - roadwork and utilities section 6 carriageway - utilities: crossed duct (HEC, HGC, PCCW)	13	05-Feb-18 A	06-Mar-18	0%																								

CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019					
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
Promenade Seawall Parapet Construction & EVA																							
SVII12000	Sec VII - Precast parapet	67	18-Nov-17 A	14-May-18	0%																		
SVII12010	Sec VII - Zone CRIII - seawall parapet: Backfilling	14	20-Feb-18	07-Mar-18	0%																		
SVII12120	Sec VII - Zone CRIII - seawall parapet: Construct mass concrete coping	30	08-Mar-18	16-Apr-18	0%																		
SVII12122	Sec VII - Zone CRIII - seawall parapet: reinforced concret coping	17	17-Apr-18	07-May-18	0%																		
SVII12140	Sec VII - Zone CRIII - seawall parapet: construct seawall parapet	30	08-May-18	12-Jun-18	0%																		
SVII12160	Sec VII - CRIII - EVA: watermain	14	13-Jun-18	29-Jun-18	0%																		
SVII12180	Sec VII - CRIII - EVA: U-channel	14	30-Jun-18	17-Jul-18	0%																		
SVII12200	Sec VII - CRIII - EVA: bituminous layer	5	18-Jul-18	23-Jul-18	0%																		
SVII12220	Sec VII - CRIII - EVA: paving block	30	24-Jul-18	27-Aug-18	0%																		
SVII13120	Sec VII - Zone A1, A2 & B - seawall parapet: Construct mass concrete coping	14	28-Dec-17 A	07-Mar-18	68.18%																		
SVII13122	Sec VII - Zone A1, A2 & B - seawall parapet: reinforced concrete coping	18	08-Mar-18	28-Mar-18	0%																		
SVII13140	Sec VII - Zone A1, A2 & B - seawall parapet: Construct seawall parapet	30	09-Apr-18	14-May-18	0%																		
SVII13160	Sec VII - Zone A1, A2 & B - EVA: watermain	14	15-May-18	31-May-18	0%																		
SVII13180	Sec VII - Zone A1, A2 & B - EVA: U-channel	14	01-Jun-18	16-Jun-18	0%																		
SVII13182	Sec VII - Zone A1, A2 & B - EVA: bituminous layer	5	19-Jun-18	23-Jun-18	0%																		
SVII13184	Sec VII - Zone A1, A2 & B - EVA: paving block	30	25-Jun-18	30-Jul-18	0%																		
SVII13200	Sec VII - Zone D - seawall parapet: Remove temporary seawall block	21	07-Mar-18	03-Apr-18	0%																		
SVII13220	Sec VII - Zone D - seawall parapet: Construct mass concrete	30	04-Apr-18	10-May-18	0%																		
SVII13222	Sec VII - Zone D - seawall parapet: reinforced concrete coping	18	11-May-18	01-Jun-18	0%																		
SVII13240	Sec VII - Zone D - seawall parapet: Construct seawall parapet	25	02-Jun-18	03-Jul-18	0%																		
SVII13260	Sec VII - Zone D - EVA : watermain	14	04-Jul-18	19-Jul-18	0%																		
SVII13280	Sec VII - Zone D - EVA : U-channel	14	20-Jul-18	04-Aug-18	0%																		
SVII13300	Sec VII - Zone D - EVA : bituminous layer	5	06-Aug-18	10-Aug-18	0%																		
SVII13320	Sec VII - Zone D - EVA : paving block	30	11-Aug-18	14-Sep-18	0%																		
Promenade Footpath																							
Section 1																							
SVII10440	Sec VII - section 1 footpath - drainage works : connection pipe & U -channel	10	24-May-18	04-Jun-18	0%																		
SVII10445	Sec VII - section 1 footpath - watermain	7	05-Jun-18	12-Jun-18	0%																		
SVII10460	Sec VII - section 1 footpath - lighting	7	13-Jun-18	21-Jun-18	0%																		
SVII10500	Sec VII - section 1 footpath - paving block	21	22-Jun-18	17-Jul-18	0%																		
Section 2																							
SVII12610	Sec VII - section 2 footpath - drainage works : L2202 - L2203A	20	20-Feb-18	14-Mar-18	0%																		
SVII12615	Sec VII - section 2 footpath - watermain	7	15-Mar-18	22-Mar-18	0%																		
SVII12630	Sec VII - section 2 footpath - utilities: TCSS	21	23-Mar-18	20-Apr-18	0%																		
SVII12670	Sec VII - section 2 footpath - paving block	30	21-Apr-18	28-May-18	0%																		
Section 3																							
SVII12850	Sec VII - section 3 footpath - watermain	17	20-Feb-18	10-Mar-18	0%																		
SVII12870	Sec VII - section 3 footpath - utilities (HEC, TCSS, HGC, PCCW)	40	12-Mar-18	02-May-18	0%																		
SVII12875	Sec VII - 3 footpath - drainage works :U chanel	14	03-May-18	18-May-18	0%																		

Activity ID	Activity Name	Original Duration	Start	Finish	2019			
					May	Jun	Jul	Aug
Total		2586.0d	21-Mar-13 08:00 A	21-Mar-20 18:00				
DWP-08 - (2) - Update Progress As of 20 May 19		2586.0d	21-Mar-13 08:00 A	21-Mar-20 18:00				
Works in KD9 (Include Re-provisioning Works of KD4,KD5)		57.0d	24-Nov-18 08:00 A	31-Dec-18 18:00 A				
Reverting Traffic for IEC,VP Rd & TF St & Seawall Reinstatement (KD9)		57.0d	24-Nov-18 08:00 A	31-Dec-18 18:00 A				
TTA Revert Traffic Back to Original Alignment		19.0d	01-Dec-18 08:00 A	31-Dec-18 18:00 A				
East Bound TTA - IEC East Bound, Victoria Park Road & footpath along Sea Side		10.0d	01-Dec-18 08:00 A	07-Dec-18 18:00 A				
TTM Stage 1 - IEC (East Bound)		6.0d	01-Dec-18 08:00 A	07-Dec-18 18:00 A				
Reinstatement Existing Structure		6.0d	01-Dec-18 08:00 A	07-Dec-18 18:00 A				
EB_1020 Install metal parapet on parapet wall (30m)		6.0d	01-Dec-18 08:00 A	07-Dec-18 18:00 A				
TTM Stage 2 - Revert Traffic back to Original Victoria Road		4.0d	01-Dec-18 08:00 A	07-Dec-18 18:00 A				
Existing Bridge Parapet Reinstatement		4.0d	01-Dec-18 08:00 A	07-Dec-18 18:00 A				
EB_1180 Install metal parapet on parapet wall (40m)		4.0d	01-Dec-18 08:00 A	07-Dec-18 18:00 A				
West Bound - IEC West Bound & Tsing fung Street		5.0d	29-Dec-18 08:00 A	31-Dec-18 18:00 A				
TTM Stage 2 - Revert Traffic back to Original Tsing Fung Street		5.0d	29-Dec-18 08:00 A	31-Dec-18 18:00 A				
Existing Bridge Parapet Reinstatement		5.0d	29-Dec-18 08:00 A	31-Dec-18 18:00 A				
IECW_1140 Install metal parapet on parapet wall (60m)		5.0d	29-Dec-18 08:00 A	31-Dec-18 18:00 A				
Completion of Minor Outstanding / Remaining Works for KD9		57.0d	24-Nov-18 08:00 A	31-Dec-18 08:00 A				
East Bound - Minor Outstanding Works in Footpath after Substantial Completion of KD9		6.0d	05-Dec-18 08:00 A	20-Dec-18 18:00 A				
Minor Reinstatement Works for Central Median of IEC & Footbridge		6.0d	05-Dec-18 08:00 A	20-Dec-18 18:00 A				
EB_1810 Dismantlement of temp directional sign mounted on extg footbridge		1.0d	05-Dec-18 08:00 A	05-Dec-18 18:00 A				
EB_1800 Reconstruction of central divider (6m long, night work)		6.0d	17-Dec-18 08:00 A	20-Dec-18 18:00 A				
West Bound - Completion of Minor Outstanding / Remaining Works for KD9		57.0d	24-Nov-18 08:00 A	31-Dec-18 08:00 A				
Minor Reinstatement Works in IEC West Bound		57.0d	24-Nov-18 08:00 A	31-Dec-18 08:00 A				
IECW_1610 Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)		57.0d	24-Nov-18 08:00 A	24-Dec-18 18:00 A				
IECW_1660 Replacement of new rubber seal on extg MJ at IEC W/B and E/B (night work)		4.0d	26-Nov-18 08:00 A	31-Dec-18 08:00 A				
IECW_1600 Replacement of new movement joint at IEC W/B (Sun midnight only)		8.0d	27-Dec-18 08:00 A	30-Dec-18 18:00 A				
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks		385.0d	21-Mar-19 08:00 A	21-Mar-20 18:00				
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)		365.0d	21-Mar-19 08:00 A	21-Mar-20 18:00				
EW_1012 Establishment Works - for Landscape Softworks and transplanted trees in Portion XV		365.0d	21-Mar-19 08:00 A	21-Mar-20 18:00				
KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH>500mm)		365.0d	21-Mar-19 08:00 A	21-Mar-20 18:00				
EW_1040 Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm		365.0d	21-Mar-19 08:00 A	21-Mar-20 18:00				
KD18 - Section 11: Transplanted Trees DBH>500mm in Portion VA and XII		365.0d	21-Mar-19 08:00 A	21-Mar-20 18:00				
EW_1050 Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII		365.0d	21-Mar-19 08:00 A	21-Mar-20 18:00				
KD10 - Preservation and Protection of Trees		1088.0d	21-Mar-13 08:00 A	21-May-19 18:00				
PPT_0000 Preservation and Protection of Existing Trees		1088.0d	21-Mar-13 08:00 A	21-May-19 18:00				
KD15 & KD8 - Mooring Components Upkeep (CBTS and ATS)		979.0d	15-May-14 08:00 A	19-Jun-19 18:00				
MAR_3020 Mooring Upkeep at Portion X(10) & XVI(16) - CBTS		979.0d	15-May-14 08:00 A	19-Jun-19 18:00				

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Date	Revision	Checked	Approved
20-May-19 1...	DWP-08 (2) - 3 Months Rolling	TL	TL
