

Project: MAN KWONG ST., JO MAN YIU ST., BUS TERMINUS RELOCATION  
Date: 2010/5/25  
H= HIGHWAYS, A=AECOM, C=CHIUI HING

任務  
任務進度  
里程碑任務  
要徑任務  
要徑任務進度  
里程碑

上層型任務  
上層型里程碑  
要徑任務  
要徑型里程碑

上層型進度  
分割  
外部任務

專案摘要  
摘要群組  
期限





Contract no. HY/2009/17

Contract Title : Central - Wan Chai Bypass - FEHD Whitfield Depot Re-provisioning Works

Works Schedule for the Advance Piling Works

ACTIVITY	Duration	START	FINISH	2010							2011
				July	August	September	October	November	December	January	
<u>Submissions before Commencement of Piling Works</u>											
Notification of Commencement Date of Construction	1	16/7/2010	16/7/2010	◆							
Organization Chart of Environmental Management Team	1	16/7/2010	16/7/2010	◆							
Works Schedule	1	16/7/2010	16/7/2010	◆							
Location and Layout Plan	1	31/8/2010	31/8/2010			◆					
Construction Noise Management Plan	1	31/8/2010	31/8/2010			◆					
<u>Installation of Piles</u>											
Plants Set-up	7	24/9/2010	30/9/2010				■				
Installation of pipes E3b	70	2/10/2010	10/12/2010				■				
Installation of pipes E3a	60	2/10/2010	30/11/2010				■				
Installation of pipes E2a	60	12/10/2010	10/12/2010				■				
Installation of pipes E2b	70	14/10/2010	22/12/2010				■				
Testing	14	23/12/2010	6/1/2011							■	

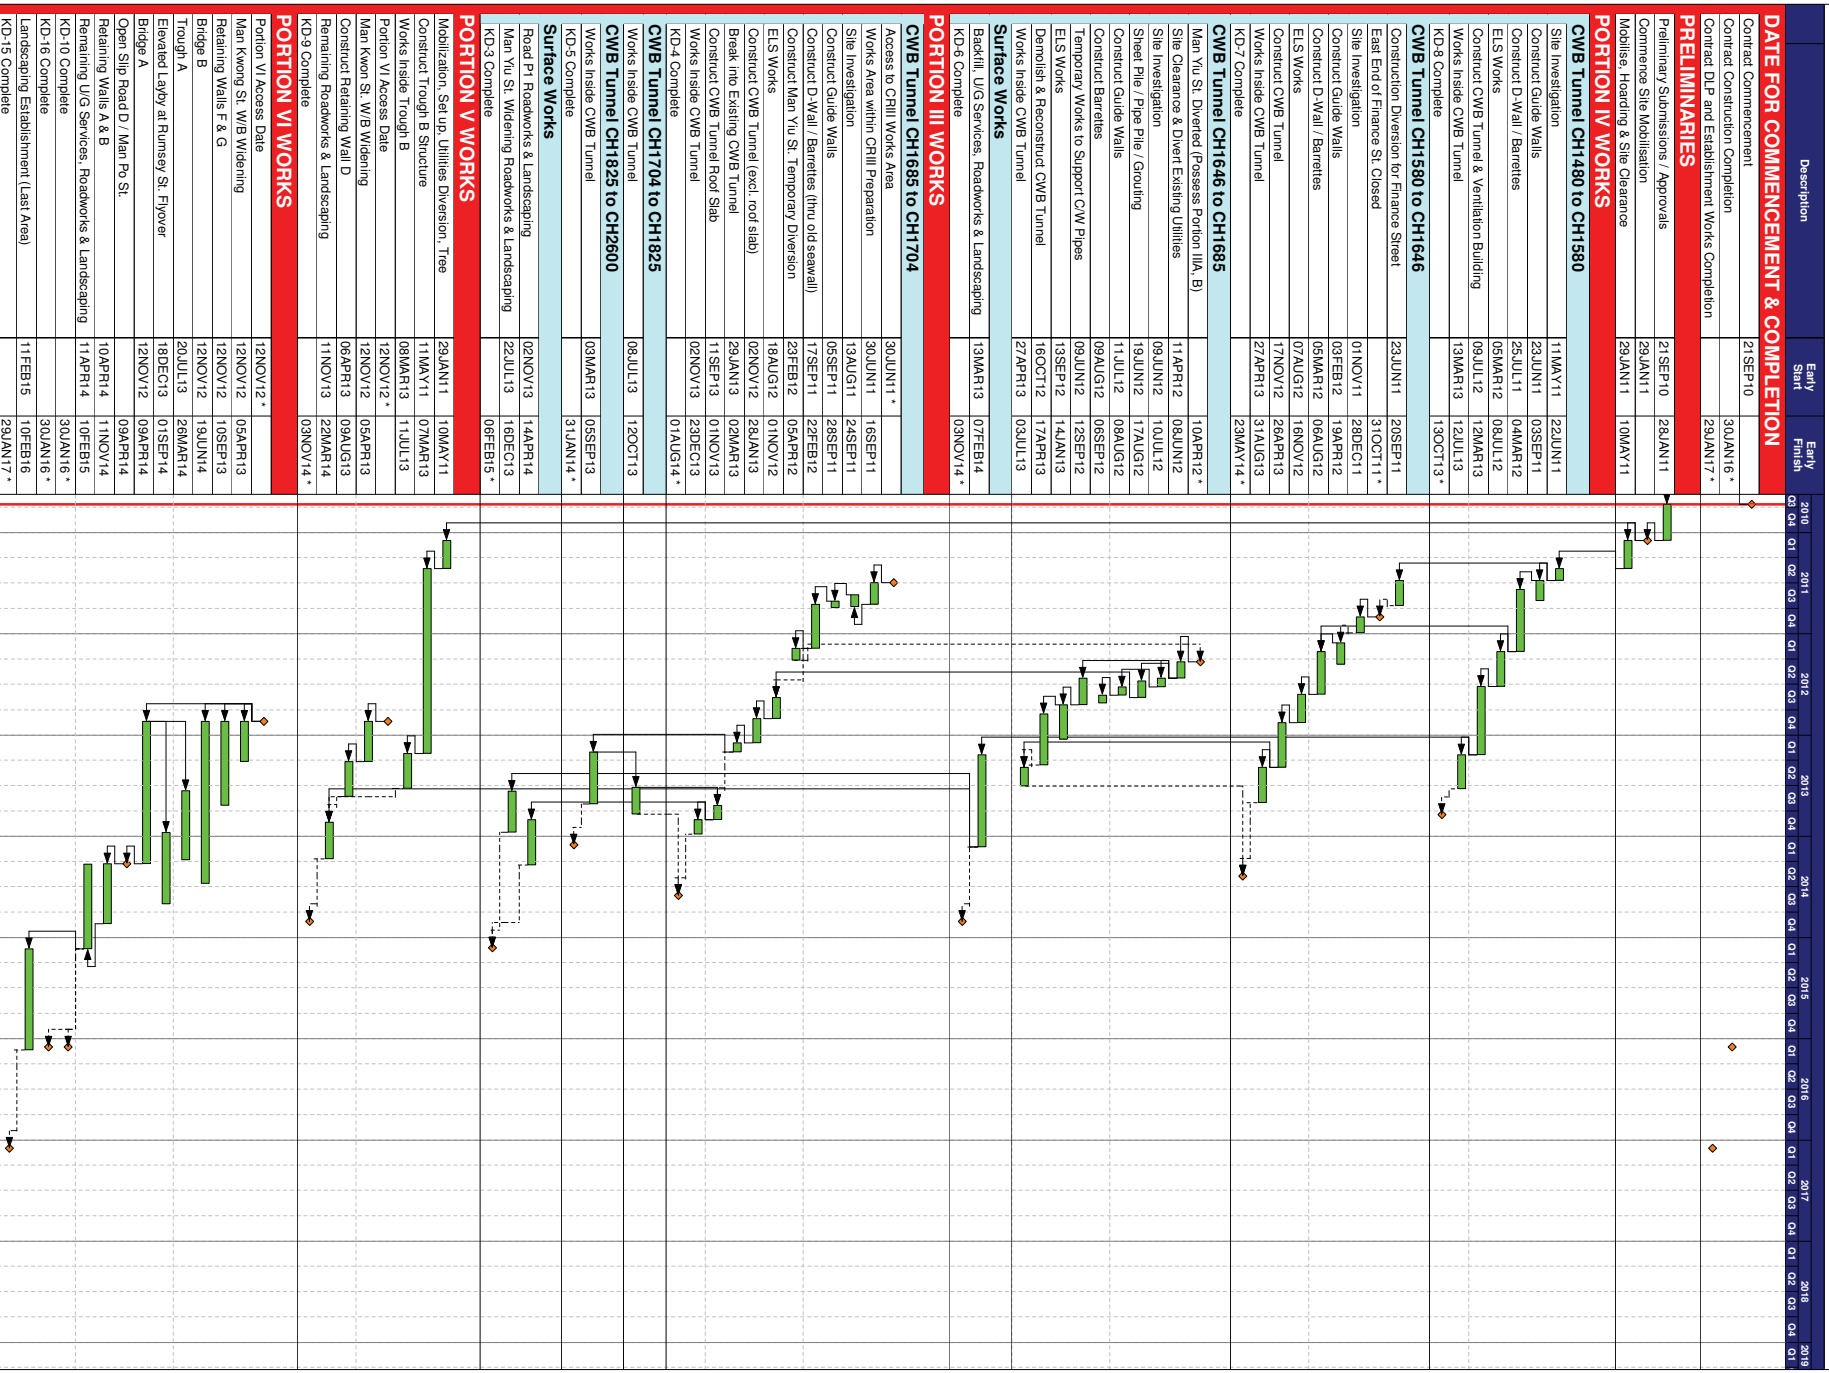

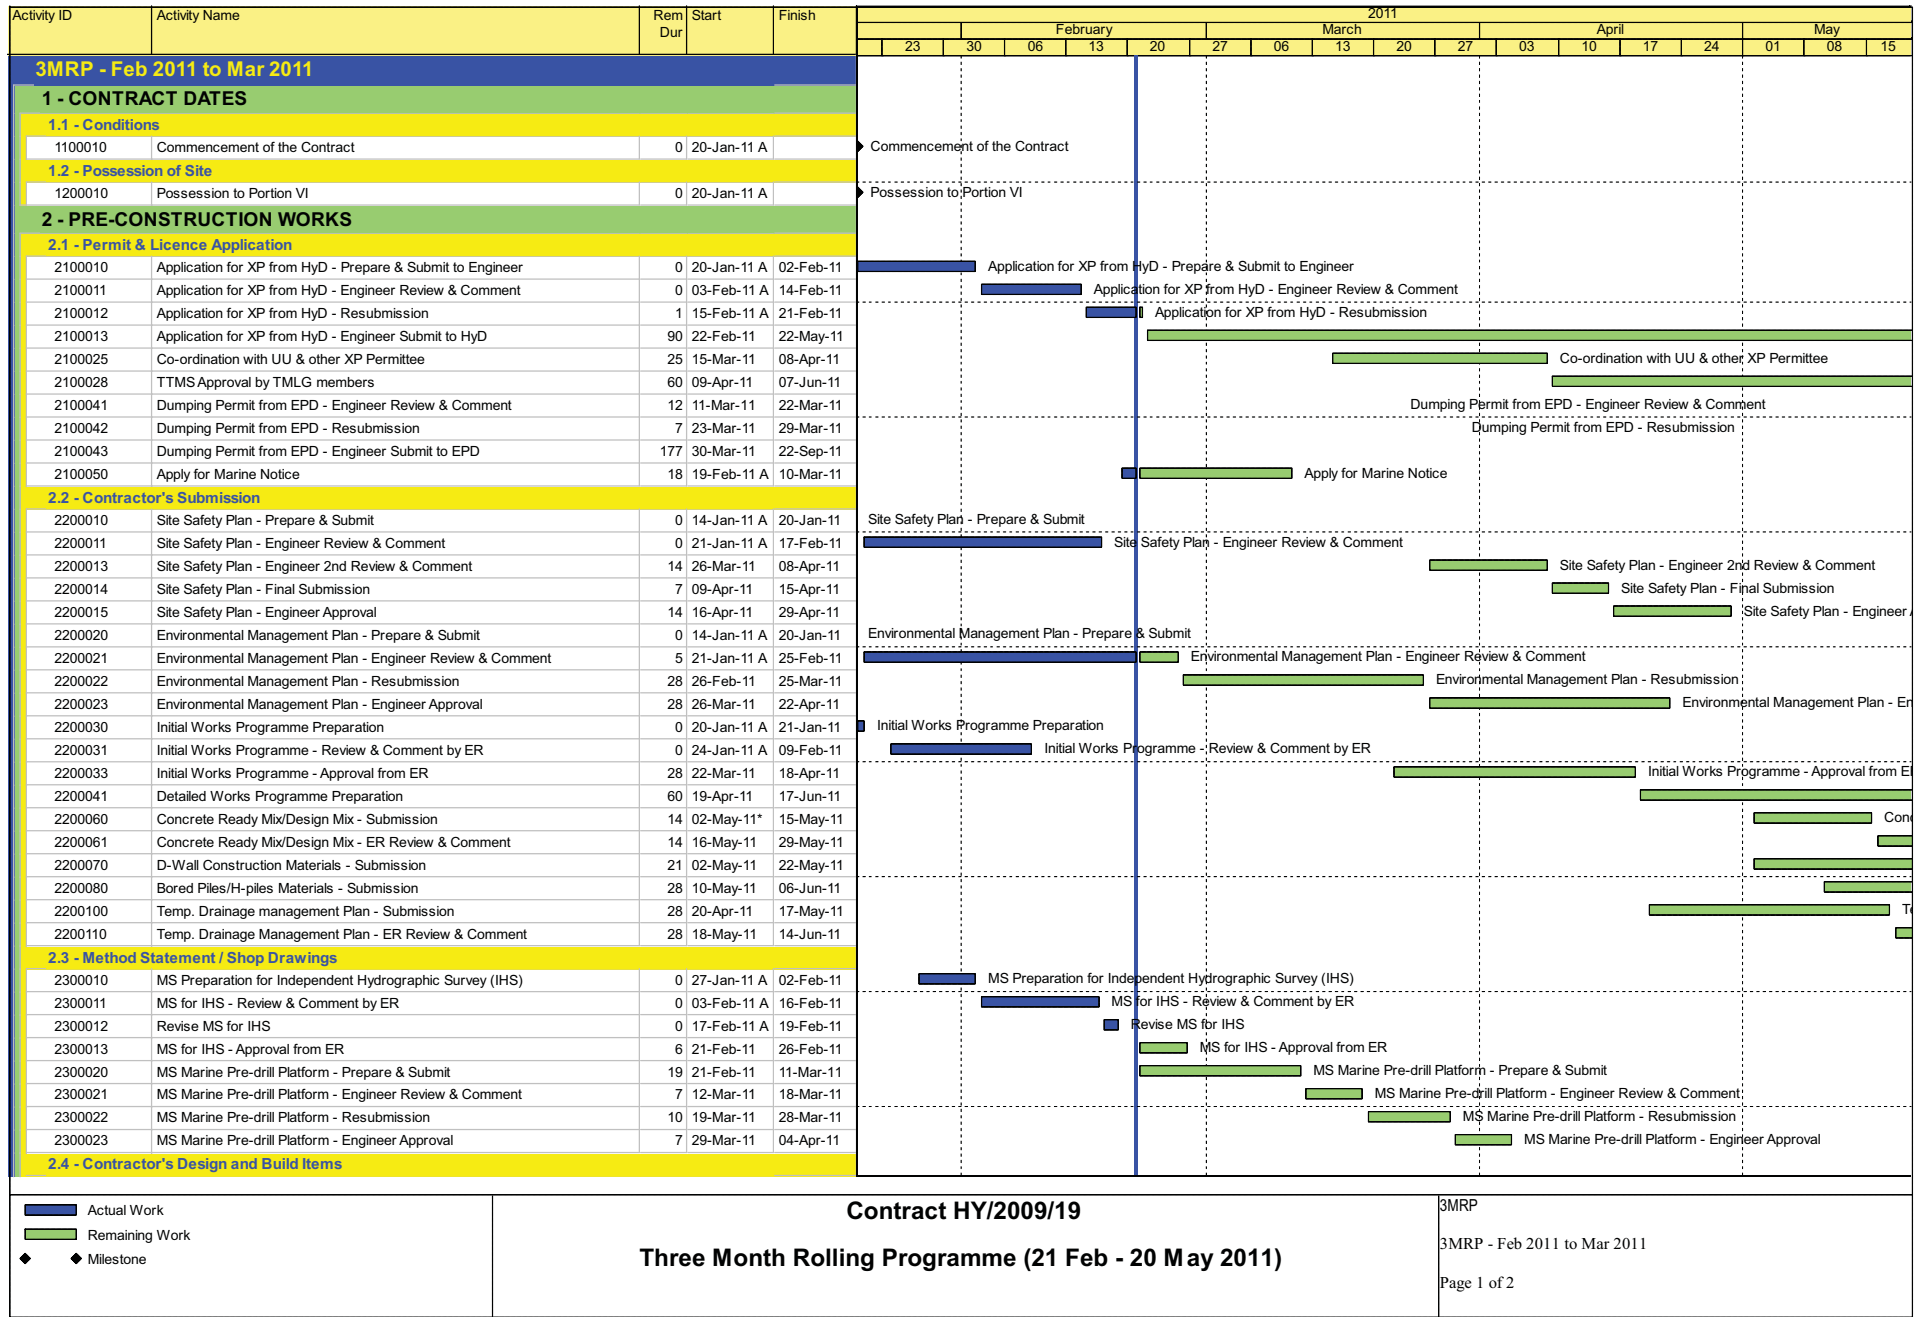

Activity ID	Activity Name	Rem Dur	Start	Finish	2011																
					February					March					April					May	
					23	30	06	13	20	27	06	13	20	27	03	10	17	24	01	08	15
2400010	Marine Pre-drilling Platform Design - Prep & Submit	36	21-Feb-11	28-Mar-11	Marine Pre-drilling Platform Design - Prep & Submit																
2400011	Marine Pre-drilling Platform Design - ER review & comment	7	29-Mar-11	04-Apr-11	Marine Pre-drilling Platform Design - ER review & comment																
2400012	Marine Pre-drilling Platform Design - Resubmission	7	02-Apr-11	08-Apr-11	Marine Pre-drilling Platform Design - Resubmission																
2400013	Marine Pre-drilling Platform Design - ER Approval	9	09-Apr-11	17-Apr-11	Marine Pre-drilling Platform Design - ER App																
<b>3 - CONSTRUCTION WORKS</b>																					
<b>3.1 - Site Set-up</b>																					
<b>3.1.1 - General</b>																					
3010010	Site mobilization - Contractor's Temporary Office	25	20-Jan-11 A	21-Mar-11	Site mobilization - Contractor's Temporary Office																
3010015	Site mobilization - Initial Surveys & Photographs	0	20-Jan-11 A	20-Feb-11	Site mobilization - Initial Surveys & Photographs																
3010020	Site mobilization - Engineer's Equipment & Services	25	20-Jan-11 A	21-Mar-11	Site mobilization - Engineer's Equipment & Services																
3010025	Site mobilization - Contractor's Staff & Equipments	25	20-Jan-11 A	21-Mar-11	Site mobilization - Contractor's Staff & Equipments																
3010120	Independent hydrographic survey	12	21-Feb-11	05-Mar-11	Independent hydrographic survey																
<b>3.9 - Section X Works</b>																					
<b>3.9.1 - Bridge - Eastbound - Pier F3-F15</b>																					
3910010	Mobilization of Crane Barge & Self Propelled Derick	3	24-Mar-11	26-Mar-11	Mobilization of Crane Barge & Self Propelled Derick																
3910011	Pre-drilling Platform Material Delivery	3	28-Mar-11	30-Mar-11	Pre-drilling Platform Material Delivery																
3910020	Marine pre-drilling platform - Type 3 Deck Fabrication (2 nos.)	12	31-Mar-11	14-Apr-11	Marine pre-drilling platform - Type 3 Deck Fabrica																
3910022	Marine pre-drilling platform - Type 2 Deck Fabrication	9	15-Apr-11	27-Apr-11	Marine pre-drilling platform - T																
3910024	Marine pre-drilling platform - Type 1 Deck Fabrication	9	28-Apr-11	07-May-11	Marine pre-drillin																
3910026	Marine pre-drilling platform - Drive H-pile for F6 & F3 Caps	12	15-Apr-11	30-Apr-11	Marine pre-drilling platform																
3910030	Marine pre-drilling platform - Install Type 3 Deck at F9	12	15-Apr-11	30-Apr-11	Marine pre-drilling platform																
3910035	Marine pre-drilling platform - Install Type 3 Deck at F12	9	02-May-11	11-May-11	Marine pre																
3910040	Marine pre-drilling platform - Install Type 2 Deck at F6	9	12-May-11	21-May-11																	
3910055	Mobilise & Set-up for Marine Pre-drilling	5	12-May-11	17-May-11	M																
3910060	Marine bored pile - Predrilling at F9 Cap (2 of 2)	12	18-May-11	31-May-11																	
3910070	Marine bored pile - Predrilling at F9 Dolphin (2 of 6)	12	18-May-11	31-May-11																	

- Actual Work
- Remaining Work
- Milestone

Contract HY/2009/19

Three Month Rolling Programme (21 Feb - 20 May 2011)

3MRP

3MRP - Feb 2011 to Mar 2011

Page 2 of 2
