

編號	Task Name	工期	開始時間	完成時間	前置任務	資源名稱	Gantt Chart (5/05 to 2/11)																											
1	Planning & Approval	33 days	2010/5/18	2010/6/24			[Gantt bars for tasks 1-58]																											
2	Planning of new bus terminus scheme	28 days	2010/5/18	2010/6/24		H,A,C	[Gantt bar for task 2]																											
3	Approval of scheme	0 days	2010/6/24	2010/6/24	2	TD	[Gantt bar for task 3]																											
4	Setting out data of final scheme	7 days	2010/5/18	2010/5/26		HA	[Gantt bar for task 4]																											
5	Construction Works - Stage 1	114 days	2010/5/21	2010/9/30			[Gantt bar for task 5]																											
6	Issue WO#1	0 days	2010/5/21	2010/5/21		HA	[Gantt bar for task 6]																											
7	Handling over of extg depot	0 days	2010/5/21	2010/5/21	6	HA	[Gantt bar for task 7]																											
8	Demolish existing Depot (superstructure)	14 days	2010/5/21	2010/6/9		C	[Gantt bar for task 8]																											
9	Demolish existing Depot (substructure)	14 days	2010/6/10	2010/6/29		C	[Gantt bar for task 9]																											
10	Convert the site depot area into C/W & Xconstruct F/P for Bay 4 (part 1)	60 days	2010/6/30	2010/9/21		C	[Gantt bar for task 10]																											
11	Fence Off new RCP location	14 days	2010/5/31	2010/6/17		C	[Gantt bar for task 11]																											
12	Relocation of existing RCP	11 days	2010/6/18	2010/7/2		C	[Gantt bar for task 12]																											
13	XP (SSW) for trial trench	2 days	2010/5/31	2010/6/1		HA	[Gantt bar for task 13]																											
14	Issue WO#2	0 days	2010/5/25	2010/5/25	15SS-7 days	HA	[Gantt bar for task 14]																											
15	Trial trench to confirm UU (MK,MY)	3 days	2010/6/2	2010/6/4		C	[Gantt bar for task 15]																											
16	TTA approval of task 17 to 25	14 days	2010/6/25	2010/7/14	13,3	C	[Gantt bar for task 16]																											
17	UU meeting & diversion	14 days	2010/7/15	2010/8/3		H,A,C	[Gantt bar for task 17]																											
18	Transplant/fell extg trees	8 days	2010/7/15	2010/7/26		C	[Gantt bar for task 18]																											
19	Relocate Kiosk of Bus operator	3 days	2010/7/30	2010/8/3	17FF	other	[Gantt bar for task 19]																											
20	Convert extg F/P to C/W along Man Kwong St & Yiu St (stage 1B)	35 days	2010/8/4	2010/9/21	17,18	C	[Gantt bar for task 20]																											
21	Construct New Entrance for Bus Terminus	21 days	2010/8/4	2010/9/1		C	[Gantt bar for task 21]																											
22	Transplant/fell extg trees at Bay A	7 days	2010/7/15	2010/7/23		C	[Gantt bar for task 22]																											
23	Removal of Bus Shelter A	14 days	2010/7/15	2010/8/3		other	[Gantt bar for task 23]																											
24	Relocate gullies	7 days	2010/8/4	2010/8/12	23	C	[Gantt bar for task 24]																											
25	Convert Extg bus bay A into C/W	21 days	2010/8/13	2010/9/10	24	C	[Gantt bar for task 25]																											
26	Allowable flow	8 days	2010/9/22	2010/9/30	25,10,20		[Gantt bar for task 26]																											
27	Central Reserve of man Kwong St (stage 1C)	123 days	2010/5/24	2010/10/13			[Gantt bar for task 27]																											
28	Issue W.O.	3 days	2010/5/24	2010/5/26		HA	[Gantt bar for task 28]																											
29	XP (SSW) for trial trench	2 days	2010/6/1	2010/6/2	28	HA	[Gantt bar for task 29]																											
30	Trial trench to confirm UU	2 days	2010/6/3	2010/6/4	29	C	[Gantt bar for task 30]																											
31	UU meeting & diversion	16 days	2010/6/7	2010/6/28	30	H,A,C	[Gantt bar for task 31]																											
32	Tree Transplantation / Removal	74 days	2010/6/3	2010/9/14	29	C	[Gantt bar for task 32]																											
33	Convert verge into C/W	21 days	2010/9/15	2010/10/13	32	C	[Gantt bar for task 33]																											
34	Cable duct & traffic aids	16 days	2010/9/22	2010/10/13	33FF	C	[Gantt bar for task 34]																											
35	Stage 2 - New Bus bay 1-3, 4a	119 days	2010/6/25	2010/11/10			[Gantt bar for task 35]																											
36	Approval of TTA for Stage 2	14 days	2010/6/25	2010/7/14	3	TDRMO	[Gantt bar for task 36]																											
37	Implement TTA	1 day	2010/7/15	2010/7/15	36	C	[Gantt bar for task 37]																											
38	Relocate St lighting (Bay B-H)	14 days	2010/7/16	2010/8/4	37	other	[Gantt bar for task 38]																											
39	Removal of Bus Shelter (B-H)	14 days	2010/7/16	2010/8/4	37	other	[Gantt bar for task 39]																											
40	Tree Transplantation / Removal	7 days	2010/7/16	2010/7/26	37	C	[Gantt bar for task 40]																											
41	Relocate extg gully pits	21 days	2010/7/16	2010/8/13	37	C	[Gantt bar for task 41]																											
42	Convert Bus Bay (B-H) into C/W	50 days	2010/8/5	2010/10/13	38,39	C	[Gantt bar for task 42]																											
43	Construct New Bus Terminal (Bay 1-3,4a)	56 days	2010/8/16	2010/11/1	41	C	[Gantt bar for task 43]																											
44	Construct Bus Shelter (1-3, 4a)	45 days	2010/9/8	2010/11/9	43FF+7 days	other	[Gantt bar for task 44]																											
45	Traffic aids & road marking	7 days	2010/11/2	2010/11/10	43	C	[Gantt bar for task 45]																											
46	Stage 3 - New Bus bay 4b	44 days	2010/10/25	2010/12/14			[Gantt bar for task 46]																											
47	Approval of TTA for Stage 3	14 days	2010/10/26	2010/11/12	45FS-14 days	TDRMO	[Gantt bar for task 47]																											
48	Implement TTA & relocate Bus stop	1 day	2010/11/15	2010/11/15	47	C	[Gantt bar for task 48]																											
49	Relocate extg gully pits	9 days	2010/11/16	2010/11/26	48	C	[Gantt bar for task 49]																											
50	Construct New Bus Terminal (Bay 4b)	14 days	2010/11/16	2010/12/3	48	C	[Gantt bar for task 50]																											
51	Construct Bus Shelter 4b	14 days	2010/11/16	2010/12/3	50FF	other	[Gantt bar for task 51]																											
52	Cable ducts/pits for signalised Junction	30 days	2010/10/25	2010/12/3	50FF	C	[Gantt bar for task 52]																											
53	Traffic aids & road marking	7 days	2010/12/6	2010/12/14	50	C	[Gantt bar for task 53]																											
54	Stage 4 - New F/P & delineate new site area	48 days	2010/12/7	2011/1/31			[Gantt bar for task 54]																											
55	Approval of TTA for Stage 4	7 days	2010/12/7	2010/12/15	53FS-7 days	TDRMO	[Gantt bar for task 55]																											
56	Implement TTA & relocate Bus stop	1 day	2010/12/16	2010/12/16	55	C	[Gantt bar for task 56]																											
57	Construction of new F/P	21 days	2010/12/17	2011/1/14	56	C	[Gantt bar for task 57]																											
58	Allowable Flow	14 days	2011/1/15	2011/1/31	57		[Gantt bar for task 58]																											

Project: MAN KWONG ST. JO MAN YIU ST. BUS TERMINUS RELOCATION
 Date: 2010/5/25
 H= HIGHWAYS, A=AECOM, C=CHIUI HING


任務 任務進度 任務里程碑 要徑任務進度 要徑任務里程碑 上層型任務 上層型里程碑 上層型任務進度 上層型任務里程碑 外部任務 專案摘要 摘要群組 期限

Contract no. HY/2009/17

Contract Title : Central - Wan Chai Bypass - FEHD Whitfield Depot Re-provisioning Works

Works Schedule for the Advance Piling Works

ACTIVITY	Duration	START	FINISH	2010							2011
				July	August	September	October	November	December	January	
<u>Submissions before Commencement of Piling Works</u>											
Notification of Commencement Date of Construction	1	16/7/2010	16/7/2010	◆							
Organization Chart of Environmental Management Team	1	16/7/2010	16/7/2010	◆							
Works Schedule	1	16/7/2010	16/7/2010	◆							
Location and Layout Plan	1	31/8/2010	31/8/2010			◆					
Construction Noise Management Plan	1	31/8/2010	31/8/2010			◆					
<u>Installation of Piles</u>											
Plants Set-up	7	24/9/2010	30/9/2010				■				
Installation of pipes E3b	70	2/10/2010	10/12/2010				■				
Installation of pipes E3a	60	2/10/2010	30/11/2010				■				
Installation of pipes E2a	60	12/10/2010	10/12/2010				■				
Installation of pipes E2b	70	14/10/2010	22/12/2010				■				
Testing	14	23/12/2010	6/1/2011							■	

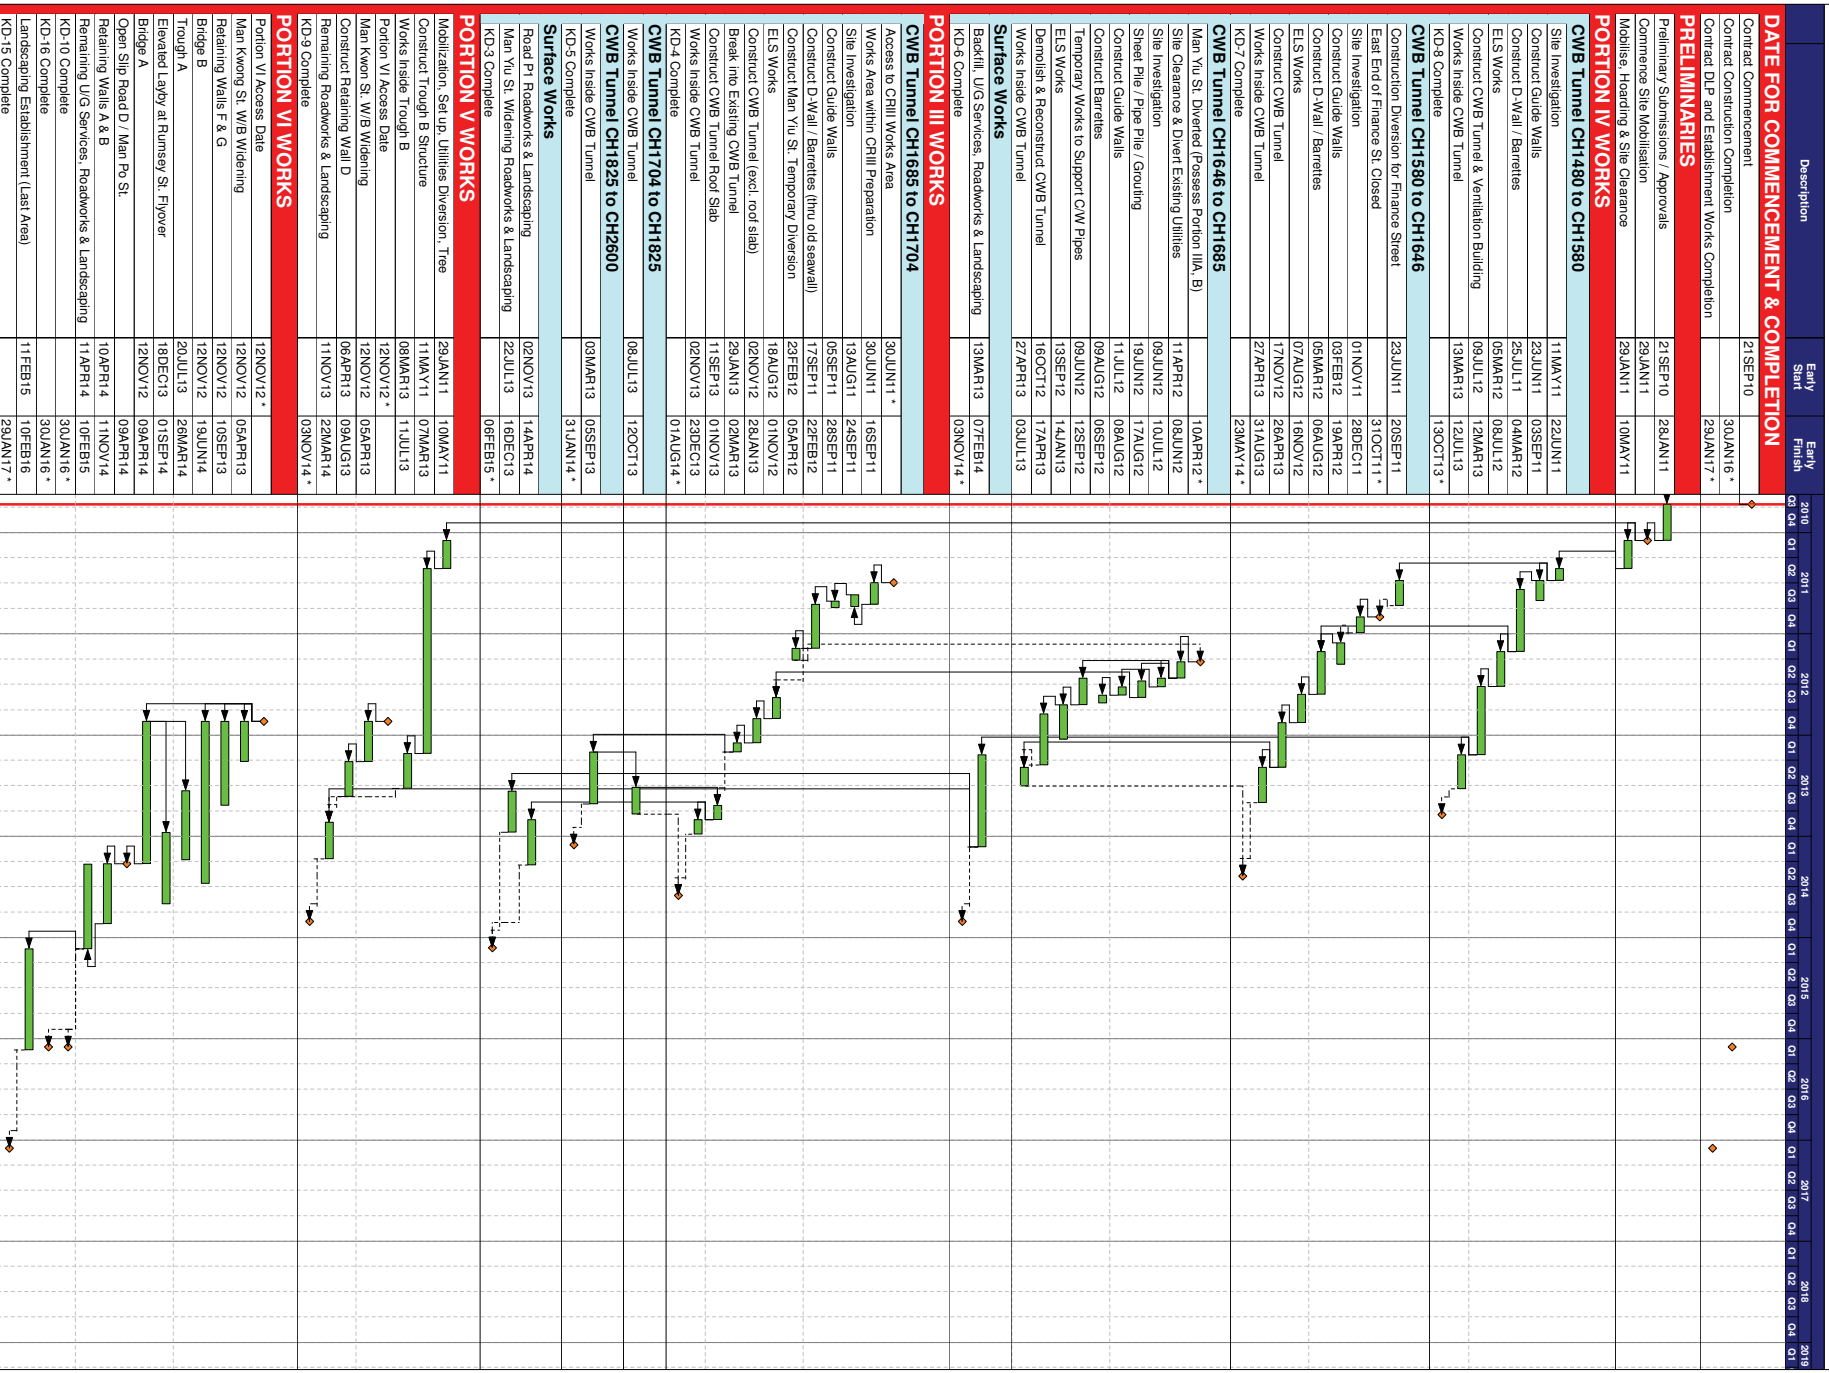

Leighton Contractors (Asia) Limited
 High Level Programme
 (Initial Works Programme IWPO)

Activity ID	Activity Name	Rem Dur	Start	Finish	2011																	
					February					March					April				May			
					23	30	06	13	20	27	06	13	20	27	03	10	17	24	01	08	15	
3MRP - Feb 2011 to Mar 2011																						
1 - CONTRACT DATES																						
1.1 - Conditions																						
1100010	Commencement of the Contract	0	20-Jan-11 A																			
1.2 - Possession of Site																						
1200010	Possession to Portion VI	0	20-Jan-11 A																			
2 - PRE-CONSTRUCTION WORKS																						
2.1 - Permit & Licence Application																						
2100010	Application for XP from HyD - Prepare & Submit to Engineer	0	20-Jan-11 A	02-Feb-11																		
2100011	Application for XP from HyD - Engineer Review & Comment	0	03-Feb-11 A	14-Feb-11																		
2100012	Application for XP from HyD - Resubmission	1	15-Feb-11 A	21-Feb-11																		
2100013	Application for XP from HyD - Engineer Submit to HyD	90	22-Feb-11	22-May-11																		
2100025	Co-ordination with UU & other XP Permittee	25	15-Mar-11	08-Apr-11																		
2100028	TTMS Approval by TMLG members	60	09-Apr-11	07-Jun-11																		
2100041	Dumping Permit from EPD - Engineer Review & Comment	12	11-Mar-11	22-Mar-11																		
2100042	Dumping Permit from EPD - Resubmission	7	23-Mar-11	29-Mar-11																		
2100043	Dumping Permit from EPD - Engineer Submit to EPD	177	30-Mar-11	22-Sep-11																		
2100050	Apply for Marine Notice	18	19-Feb-11 A	10-Mar-11																		
2.2 - Contractor's Submission																						
2200010	Site Safety Plan - Prepare & Submit	0	14-Jan-11 A	20-Jan-11																		
2200011	Site Safety Plan - Engineer Review & Comment	0	21-Jan-11 A	17-Feb-11																		
2200013	Site Safety Plan - Engineer 2nd Review & Comment	14	26-Mar-11	08-Apr-11																		
2200014	Site Safety Plan - Final Submission	7	09-Apr-11	15-Apr-11																		
2200015	Site Safety Plan - Engineer Approval	14	16-Apr-11	29-Apr-11																		
2200020	Environmental Management Plan - Prepare & Submit	0	14-Jan-11 A	20-Jan-11																		
2200021	Environmental Management Plan - Engineer Review & Comment	5	21-Jan-11 A	25-Feb-11																		
2200022	Environmental Management Plan - Resubmission	28	26-Feb-11	25-Mar-11																		
2200023	Environmental Management Plan - Engineer Approval	28	26-Mar-11	22-Apr-11																		
2200030	Initial Works Programme Preparation	0	20-Jan-11 A	21-Jan-11																		
2200031	Initial Works Programme - Review & Comment by ER	0	24-Jan-11 A	09-Feb-11																		
2200033	Initial Works Programme - Approval from ER	28	22-Mar-11	18-Apr-11																		
2200041	Detailed Works Programme Preparation	60	19-Apr-11	17-Jun-11																		
2200060	Concrete Ready Mix/Design Mix - Submission	14	02-May-11*	15-May-11																		
2200061	Concrete Ready Mix/Design Mix - ER Review & Comment	14	16-May-11	29-May-11																		
2200070	D-Wall Construction Materials - Submission	21	02-May-11	22-May-11																		
2200080	Bored Piles/H-piles Materials - Submission	28	10-May-11	06-Jun-11																		
2200100	Temp. Drainage management Plan - Submission	28	20-Apr-11	17-May-11																		
2200110	Temp. Drainage management Plan - ER Review & Comment	28	18-May-11	14-Jun-11																		
2.3 - Method Statement / Shop Drawings																						
2300010	MS Preparation for Independent Hydrographic Survey (IHS)	0	27-Jan-11 A	02-Feb-11																		
2300011	MS for IHS - Review & Comment by ER	0	03-Feb-11 A	16-Feb-11																		
2300012	Revise MS for IHS	0	17-Feb-11 A	19-Feb-11																		
2300013	MS for IHS - Approval from ER	6	21-Feb-11	26-Feb-11																		
2300020	MS Marine Pre-drill Platform - Prepare & Submit	19	21-Feb-11	11-Mar-11																		
2300021	MS Marine Pre-drill Platform - Engineer Review & Comment	7	12-Mar-11	18-Mar-11																		
2300022	MS Marine Pre-drill Platform - Resubmission	10	19-Mar-11	28-Mar-11																		
2300023	MS Marine Pre-drill Platform - Engineer Approval	7	29-Mar-11	04-Apr-11																		
2.4 - Contractor's Design and Build Items																						

- Actual Work
- Remaining Work
- Milestone

Contract HY/2009/19

Three Month Rolling Programme (21 Feb - 20 May 2011)

3MRP

3MRP - Feb 2011 to Mar 2011

Page 1 of 2

Activity ID	Activity Name	Rem Dur	Start	Finish	2011																
					February					March				April				May			
					23	30	06	13	20	27	06	13	20	27	03	10	17	24	01	08	15
2400010	Marine Pre-drilling Platform Design - Prep & Submit	36	21-Feb-11	28-Mar-11	Marine Pre-drilling Platform Design - Prep & Submit																
2400011	Marine Pre-drilling Platform Design - ER review & comment	7	29-Mar-11	04-Apr-11	Marine Pre-drilling Platform Design - ER review & comment																
2400012	Marine Pre-drilling Platform Design - Resubmission	7	02-Apr-11	08-Apr-11	Marine Pre-drilling Platform Design - Resubmission																
2400013	Marine Pre-drilling Platform Design - ER Approval	9	09-Apr-11	17-Apr-11	Marine Pre-drilling Platform Design - ER Approval																
3 - CONSTRUCTION WORKS																					
3.1 - Site Set-up																					
3.1.1 - General																					
3010010	Site mobilization - Contractor's Temporary Office	25	20-Jan-11 A	21-Mar-11	Site mobilization - Contractor's Temporary Office																
3010015	Site mobilization - Initial Surveys & Photographs	0	20-Jan-11 A	20-Feb-11	Site mobilization - Initial Surveys & Photographs																
3010020	Site mobilization - Engineer's Equipment & Services	25	20-Jan-11 A	21-Mar-11	Site mobilization - Engineer's Equipment & Services																
3010025	Site mobilization - Contractor's Staff & Equipments	25	20-Jan-11 A	21-Mar-11	Site mobilization - Contractor's Staff & Equipments																
3010120	Independent hydrographic survey	12	21-Feb-11	05-Mar-11	Independent hydrographic survey																
3.9 - Section X Works																					
3.9.1 - Bridge - Eastbound - Pier F3-F15																					
3910010	Mobilization of Crane Barge & Self Propelled Derick	3	24-Mar-11	26-Mar-11	Mobilization of Crane Barge & Self Propelled Derick																
3910011	Pre-drilling Platform Material Delivery	3	28-Mar-11	30-Mar-11	Pre-drilling Platform Material Delivery																
3910020	Marine pre-drilling platform - Type 3 Deck Fabrication (2 nos.)	12	31-Mar-11	14-Apr-11	Marine pre-drilling platform - Type 3 Deck Fabrication																
3910022	Marine pre-drilling platform - Type 2 Deck Fabrication	9	15-Apr-11	27-Apr-11	Marine pre-drilling platform - Type 2 Deck Fabrication																
3910024	Marine pre-drilling platform - Type 1 Deck Fabrication	9	28-Apr-11	07-May-11	Marine pre-drilling platform - Type 1 Deck Fabrication																
3910026	Marine pre-drilling platform - Drive H-pile for F6 & F3 Caps	12	15-Apr-11	30-Apr-11	Marine pre-drilling platform - Drive H-pile for F6 & F3 Caps																
3910030	Marine pre-drilling platform - Install Type 3 Deck at F9	12	15-Apr-11	30-Apr-11	Marine pre-drilling platform - Install Type 3 Deck at F9																
3910035	Marine pre-drilling platform - Install Type 3 Deck at F12	9	02-May-11	11-May-11	Marine pre-drilling platform - Install Type 3 Deck at F12																
3910040	Marine pre-drilling platform - Install Type 2 Deck at F6	9	12-May-11	21-May-11	Marine pre-drilling platform - Install Type 2 Deck at F6																
3910055	Mobilise & Set-up for Marine Pre-drilling	5	12-May-11	17-May-11	Mobilise & Set-up for Marine Pre-drilling																
3910060	Marine bored pile - Predrilling at F9 Cap (2 of 2)	12	18-May-11	31-May-11	Marine bored pile - Predrilling at F9 Cap (2 of 2)																
3910070	Marine bored pile - Predrilling at F9 Dolphin (2 of 6)	12	18-May-11	31-May-11	Marine bored pile - Predrilling at F9 Dolphin (2 of 6)																

- Actual Work
- Remaining Work
- Milestone

Contract HY/2009/19

Three Month Rolling Programme (21 Feb - 20 May 2011)

3MRP

3MRP - Feb 2011 to Mar 2011

Page 2 of 2

Wan Chai Development Phase II - Central - Wan Chai Bypass at Wan Chai East CONTRACT HK/2009/02

CHUN WO - CRGL JV

Activity ID	Activity Name	OD	Start	Finish	% complete	2011												2012			2013			2014			2015			2016					
						J	A	J	J	A	J	J	A	J	J	A	J	J	A	J	J	A	J	J	A	J	J	A	J	J	A	J	J	A	J
Wan Chai Development Phase II - Central - Wan Chai Bypass at Wan Chai East																																			
Expanded and More Detailed Initial Works Programme																																			
Section IX B Works - Central - Wan Chai Bypass Tunnel Structure from chainage 3400 to eastern tunnel																																			
Tunnel Portion 1																																			
S9B-T1-0005	Tunnel portion 1 Predrill & guide wall	10	18-Feb-11	13-Apr-11	40%	Tunnel portion 1 Predrill & guide wall																													
S9B-T1-0007	Tunnel Portion 1 Bored Piling works	105	09-Feb-11	08-Aug-11	0%	Tunnel Portion 1 Bored Piling works																													
S9B-T1-0010	Tunnel portion 1 diaphragm wall works	105	25-Apr-11	27-Aug-11	0%	Tunnel portion 1 diaphragm wall works																													
S9B-T1-0015	Tunnel portion 1 Pump Test and demobilization of Silos equipments	35	20-Aug-11	30-Sep-11	0%	Tunnel portion 1 Pump Test and demobilization of Silos equipments																													
S9B-T1-0020	Tunnel portion 1 ELSW excavation	130	03-Oct-11	07-Mar-12	0%	Tunnel portion 1 ELSW excavation																													
S9B-T1-0030	Tunnel portion 1 structure construction	100	08-Mar-12	09-Jul-12	0%	Tunnel portion 1 structure construction																													
S9B-T1-0040	Tunnel portion 1 backfilling and ELSW removal	54	10-Jul-12	10-Sep-12	0%	Tunnel portion 1 backfilling and ELSW removal																													
Tunnel Portion 2																																			
S9B-T1-0105	Tunnel portion 2 Predrill & guide wall	10	02-Aug-12	13-Aug-12	0%	Tunnel portion 2 Predrill & guide wall																													
S9B-T2-0010	Tunnel portion 2 diaphragm wall and bored pile works	100	14-Aug-12	10-Dec-12	0%	Tunnel portion 2 diaphragm wall and bored pile works																													
S9B-T2-0015	Tunnel portion 2 Pump Test	14	03-Dec-12	18-Dec-12	0%	Tunnel portion 2 Pump Test																													
S9B-T2-0020	Tunnel portion 2 ELSW excavation	80	11-Dec-12	19-Mar-13	0%	Tunnel portion 2 ELSW excavation																													
S9B-T2-0030	Tunnel portion 2 structure construction	100	20-Mar-13	22-Jul-13	0%	Tunnel portion 2 structure construction																													
S9B-T2-0040	Tunnel portion 2 backfilling and ELSW removal	80	23-Jul-13	25-Oct-13	0%	Tunnel portion 2 backfilling and ELSW removal																													
Tunnel Portion 3																																			
S9B-T3-0005	HEC 132kv diversion at Wan Shing Street Completed	0	01-Apr-12*		0%	HEC 132kv diversion at Wan Shing Street Completed																													
S9B-T3-0008	Tunnel portion 3 Predrill & guide wall	20	02-Oct-12	25-Oct-12	0%	Tunnel portion 3 Predrill & guide wall																													
S9B-T3-0010	Remaining diaphragm wall, bored piles and temporary pipe pile wall at tunnel portion 3	50	26-Oct-12	22-Dec-12	0%	Remaining diaphragm wall, bored piles and temporary pipe pile wall at tunnel portion 3																													
S9B-T3-0015	Tunnel portion 3 Pump Test	30	15-Dec-12	22-Jan-13	0%	Tunnel portion 3 Pump Test																													
S9B-T3-0020	Tunnel portion 3 ELSW excavation	30	15-Jan-13	20-Feb-13	0%	Tunnel portion 3 ELSW excavation																													
S9B-T3-0030	Tunnel portion 3 structure construction	60	21-Feb-13	06-May-13	0%	Tunnel portion 3 structure construction																													
S9B-T3-0040	Tunnel portion 3 backfilling and ELSW removal	30	07-May-13	11-Jun-13	0%	Tunnel portion 3 backfilling and ELSW removal																													
Tunnel Portion 4																																			
S9B-T4-0005	Tunnel portion 4 Predrill & guide wall for section not at approach ramp	21	30-Aug-12	22-Sep-12	0%	Tunnel portion 4 Predrill & guide wall for section not at approach ramp																													
S9B-T4-0010	Diaphragm wall and bored pile for steel bridge no.1 above tunnel portion 4	40	24-Sep-12	10-Nov-12	0%	Diaphragm wall and bored pile for steel bridge no.1 above tunnel portion 4																													
S9B-T4-0020	Diaphragm wall & bored pile works at tunnel portion 4 (section not at approach ramp)	420	11-Sep-12	06-Feb-14	0%	Diaphragm wall & bored pile works at tunnel portion 4 (section not at approach ramp)																													
S9B-T4-0025	Tunnel portion 4 Predrill & guide wall (for section at approach ramp)	5	23-Dec-13	30-Dec-13	0%	Tunnel portion 4 Predrill & guide wall (for section at approach ramp)																													
S9B-T4-0030	Diaphragm wall works for remaining area of tunnel portion 4 (for section at approach ramp)	30	31-Dec-13	06-Feb-14	0%	Diaphragm wall works for remaining area of tunnel portion 4 (for section at approach ramp)																													
S9B-T4-0035	Tunnel portion 4 Pump Test	14	28-Jan-14	14-Feb-14	0%	Tunnel portion 4 Pump Test																													
S9B-T4-0040	Tunnel portion 4 ELSW excavation	60	07-Feb-14	19-Apr-14	0%	Tunnel portion 4 ELSW excavation																													
S9B-T4-0050	Tunnel portion 4 structure construction	110	22-Apr-14	01-Sep-14	0%	Tunnel portion 4 structure construction																													
S9B-T4-0060	Tunnel portion 4 backfilling and ELSW removal	60	02-Sep-14	13-Nov-14	0%	Tunnel portion 4 backfilling and ELSW removal																													
Section X Works - Central - Wan Chai Bypass Tunnel Structure from western tunnel to chainage 3400																																			
Tunnel Portion 5																																			
S10-T5-0005	Tunnel portion 5 Predrill & guide	21	23-Dec-14	19-Jan-15	0%	Tunnel portion 5 Predrill & guide																													
S10-T5-0010	Tunnel portion 5 diaphragm wall & bored pile works	110	20-Jan-15	04-Jun-15	0%	Tunnel portion 5 diaphragm wall & bored pile works																													
S10-T5-0015	Tunnel portion 5 pump test	14	13-Jun-15	30-Jun-15	0%	Tunnel portion 5 pump test																													
S10-T5-0020	Tunnel portion 5 tunnel ELSW excavation	45	04-Jul-15	25-Aug-15	0%	Tunnel portion 5 tunnel ELSW excavation																													
S10-T5-0030	Tunnel portion 5 tunnel structure construction	90	26-Aug-15	11-Dec-15	0%	Tunnel portion 5 tunnel structure construction																													
Tunnel Portion 6																																			
S10-T6-0040	Tunnel portion 6 Predrill & guide	12	24-Apr-15	08-May-15	0%	Tunnel portion 6 Predrill & guide																													
S10-T6-0050	Tunnel portion 6 diaphragm wall & bored pile works at Area 10	45	09-May-15	03-Jul-15	0%	Tunnel portion 6 diaphragm wall & bored pile works at Area 10																													
S10-T6-0055	Tunnel portion 6 pump test	14	25-Jun-15	11-Jul-15	0%	Tunnel portion 6 pump test																													
S10-T6-0060	Tunnel portion 6 tunnel ELSW excavation at Area 10	45	04-Jul-15	25-Aug-15	0%	Tunnel portion 6 tunnel ELSW excavation at Area 10																													
S10-T6-0070	Tunnel portion 6 tunnel structure construction at Area 10	58	26-Aug-15	04-Nov-15	0%	Tunnel portion 6 tunnel structure construction at Area 10																													

俊和 - 中國中鐵聯營
CHUN WO - CRGL JOINT VENTURE

Remaining Level of Effort (Green bar)

Actual Level of Effort (Blue bar)

Actual Work (Dark Blue bar)

Remaining Work (Light Green bar)

Critical Remaining Work (Red bar)

Milestone (Diamond symbol)

Summary (Arrow symbol)

CEDD CONTRACT NO. HK/2009/02

Wan Chai Development Phase II - Central Wan Chai Bypass at Wan Chai East (Contract 2)

Revised Programme dated 7 April 2011

Date	Revision	Checked	Approved
07-Apr-11		KT	KY

Page 1 of 1
