



Contract no. HY/2009/17


Contract Title : Central - Wan Chai Bypass - FEHD Whitfield Depot Re-provisioning Works

Works Schedule for the Advance Piling Works

ACTIVITY	Duration	START	FINISH	2010							2011
				July	August	September	October	November	December	January	
<u>Submissions before Commencement of Piling Works</u>											
Notification of Commencement Date of Construction	1	16/7/2010	16/7/2010	◆							
Organization Chart of Environmental Management Team	1	16/7/2010	16/7/2010	◆							
Works Schedule	1	16/7/2010	16/7/2010	◆							
Location and Layout Plan	1	31/8/2010	31/8/2010			◆					
Construction Noise Management Plan	1	31/8/2010	31/8/2010			◆					
<u>Installation of Piles</u>											
Plants Set-up	7	24/9/2010	30/9/2010				■				
Installation of pipes E3b	70	2/10/2010	10/12/2010				■				
Installation of pipes E3a	60	2/10/2010	30/11/2010				■				
Installation of pipes E2a	60	12/10/2010	10/12/2010				■				
Installation of pipes E2b	70	14/10/2010	22/12/2010				■				
Testing	14	23/12/2010	6/1/2011							■	

Central - Wan Chai Bypass (Central Interchange)

HY/2009/18

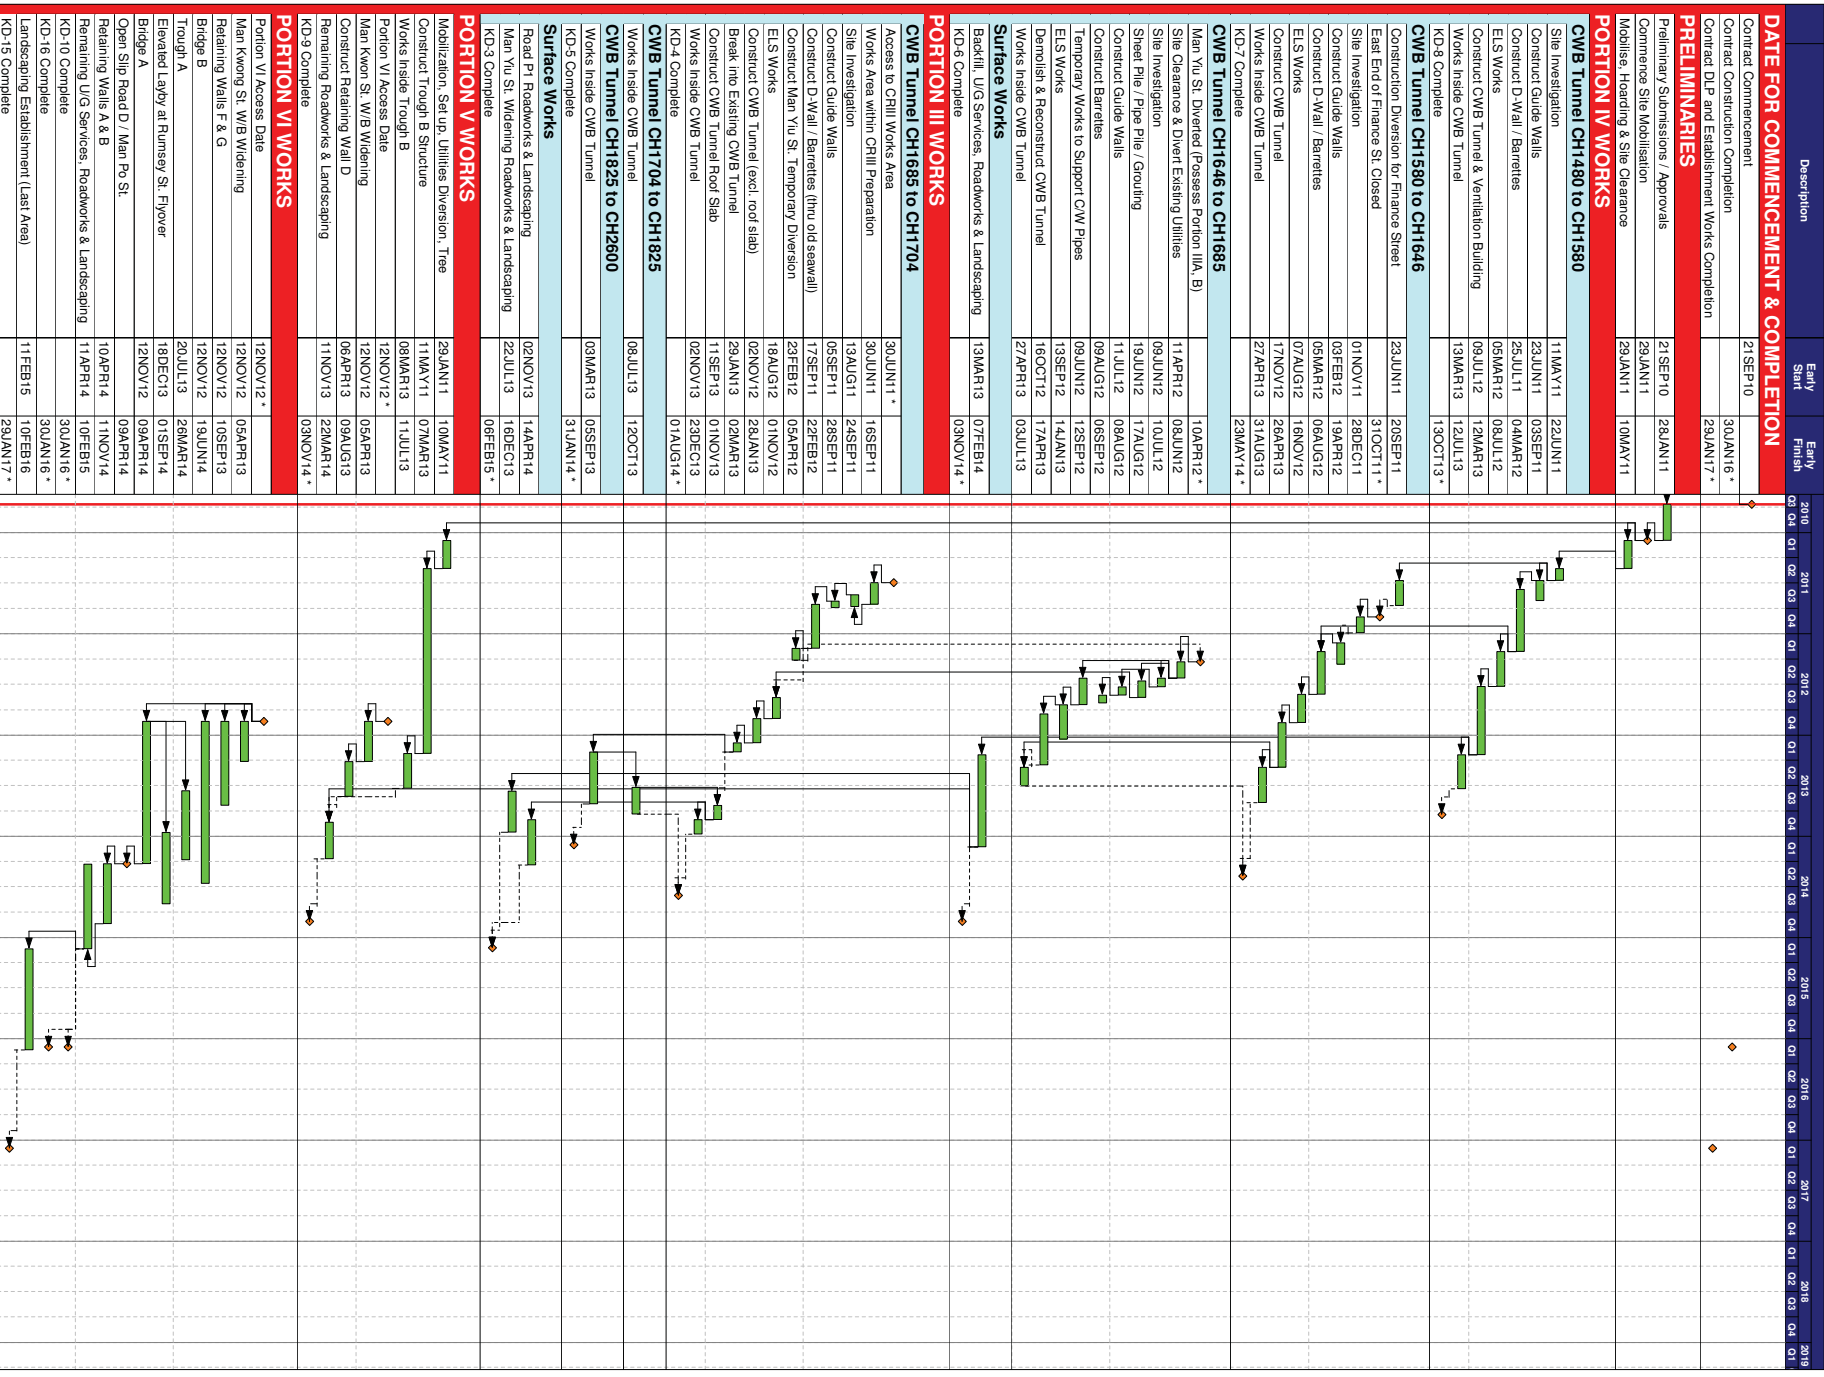

Leighton Contractors (Asia) Limited  
 High Level Programme  
 (Initial Works Programme IWPO)

Activity ID	Activity Name	Rem Dur	Start	Finish	2011																
					July					August				September				October			
					0	27	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10
<b>3MRP - Jul 2011 to Oct 2011</b>																					
<b>1 - CONTRACT DATES</b>																					
<b>1.1 - Conditions</b>																					
G01_POS_00280	PMI for Section 1 of the Works	0		04-Oct-11															◆ PMI for Section 1 of		
<b>1.2 - Possession of Site</b>																					
G01_POS_00020	Possession to Portion VIIA	0	04-Aug-11*																◆ Possession to Portion VIIA		
G01_POS_00030	Possession to Portion VIIB	0	04-Aug-11*																◆ Possession to Portion VIIB		
G01_POS_00040	Possession to Portion VIIC	0	04-Aug-11*																◆ Possession to Portion VIIC		
G01_POS_00050	Possession to Portion VIID	0	04-Aug-11*																◆ Possession to Portion VIID		
G01_POS_00060	Possession to Portion XI	0	05-Oct-11*																◆ Possession to Port		
<b>1.5 - Period of Site Possession for each Portion</b>																					
G04_POS_00010	Portion VI	2164	20-Jan-11 A	22-Jun-17																	
G04_POS_00020	Portion VIIA	2122	04-Aug-11	25-May-17																	
G04_POS_00030	Portion VIIB	930	04-Aug-11	18-Feb-14																	
G04_POS_00040	Portion VIIC	1309	04-Aug-11	04-Mar-15																	
G04_POS_00050	Portion VIID	930	04-Aug-11	18-Feb-14																	
G04_POS_00060	Portion XI	703	05-Oct-11	06-Sep-13																	
<b>2 - PRE-CONSTRUCTION WORKS</b>																					
<b>2.1 - Permit &amp; Licence Application</b>																					
P01_PLA_000040	Apply for XP from HyD	8	20-Jan-11 A	28-Jul-11															Apply for XP from HyD		
P01_PLA_000050	XP issued by HyD	0		28-Jul-11															◆ XP issued by HyD		
P01_PLA_000200	Dumping Permit from CEDD	128	10-Mar-11 A	25-Nov-11																	
<b>2.2 - Contractor's Submission</b>																					
P02_SUB_000360	Detailed Works Programme - Review & Comment by ER	0	08-Jun-11 A	07-Jul-11 A															Detailed Works Programme - Review & Comment by ER		
P02_SUB_000370	Revise Detailed Works Programme	9	08-Jul-11 A	29-Jul-11															Revise Detailed Works Programme		
P02_SUB_000380	Detailed Works Programme - Approval from ER	28	30-Jul-11	26-Aug-11															Detailed Works Programme - Approval from ER		
P02_SUB_000430	Temp. Drainage Management Plan Preparation	14	21-Jul-11	03-Aug-11															Temp. Drainage Management Plan Preparation		
P02_SUB_000440	Temp. Drainage Management Plan - Review & Comment by ER	28	04-Aug-11	31-Aug-11															Temp. Drainage Management Plan - Review & Comment by ER		
P02_SUB_000450	Revise temp. drainage management plan	14	01-Sep-11	14-Sep-11															Revise temp. drainage management plan		
P02_SUB_000460	Temp. Drainage Management Plan - Approval from ER	28	15-Sep-11	12-Oct-11															Temp. D		
P02_SUB_000470	Concrete Ready Mix/Design Mix - Submission	0	21-May-11 A	24-Jun-11 A															Concrete Ready Mix/Design Mix - Submission		
P02_SUB_000480	Concrete Ready Mix/Design Mix - ER Review & Comment	0	25-Jun-11 A	02-Jul-11 A															Concrete Ready Mix/Design Mix - ER Review & Comment		
P02_SUB_000490	Concrete Ready Mix/Design Mix - Resubmission	3	04-Jul-11 A	23-Jul-11															Concrete Ready Mix/Design Mix - Resubmission		
P02_SUB_000500	Concrete Ready Mix/Design Mix - ER Approval	21	24-Jul-11	13-Aug-11															Concrete Ready Mix/Design Mix - ER Approval		
P02_SUB_000510	Concrete Ready Mix/Design Mix - Concrete Plant Trials & Approval	45	14-Aug-11	27-Sep-11															Concrete Ready Mix/Design M		
P02_SUB_000700	D-Wall Construction Materials - Submission	9	14-Jun-11 A	29-Jul-11															D-Wall Construction Materials - Submission		
P02_SUB_000710	D-Wall Construction Materials - ER Review/Comment	28	30-Jul-11	26-Aug-11															D-Wall Construction Materials - ER Review/Comment		
P02_SUB_000720	D-Wall Construction Materials - Resubmission	7	27-Aug-11	02-Sep-11															D-Wall Construction Materials - Resubmission		
P02_SUB_000730	D-Wall Construction Materials - ER Approval	21	03-Sep-11	23-Sep-11															D-Wall Construction Materials - ER		
P02_SUB_000740	D-Wall Construction Materials - Procurement & Delivery	12	24-Sep-11	05-Oct-11															D-Wall Construction		
P02_SUB_000920	Bored Piles/H-piles Materials - Resubmission	3	21-Jun-11 A	23-Jul-11															Bored Piles/H-piles Materials - Resubmission		
P02_SUB_000930	Bored Piles/H-piles Materials - ER Approval	21	24-Jul-11	13-Aug-11															Bored Piles/H-piles Materials - ER Approval		
P02_SUB_000940	Bored Piles/H-piles Materials - Procurement & Delivery	45	14-Aug-11	27-Sep-11															Bored Piles/H-piles Materials		
P02_SUB_001010	Bridge Bearing - Submission	60	17-Sep-11	15-Nov-11																	

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone


**Contract HY/2009/19**

**Three Month Rolling Programme (21 July to 20 October 2011)**

3MRP

3MRP - Jul 2011 to Oct 2011

Page 1 of 4

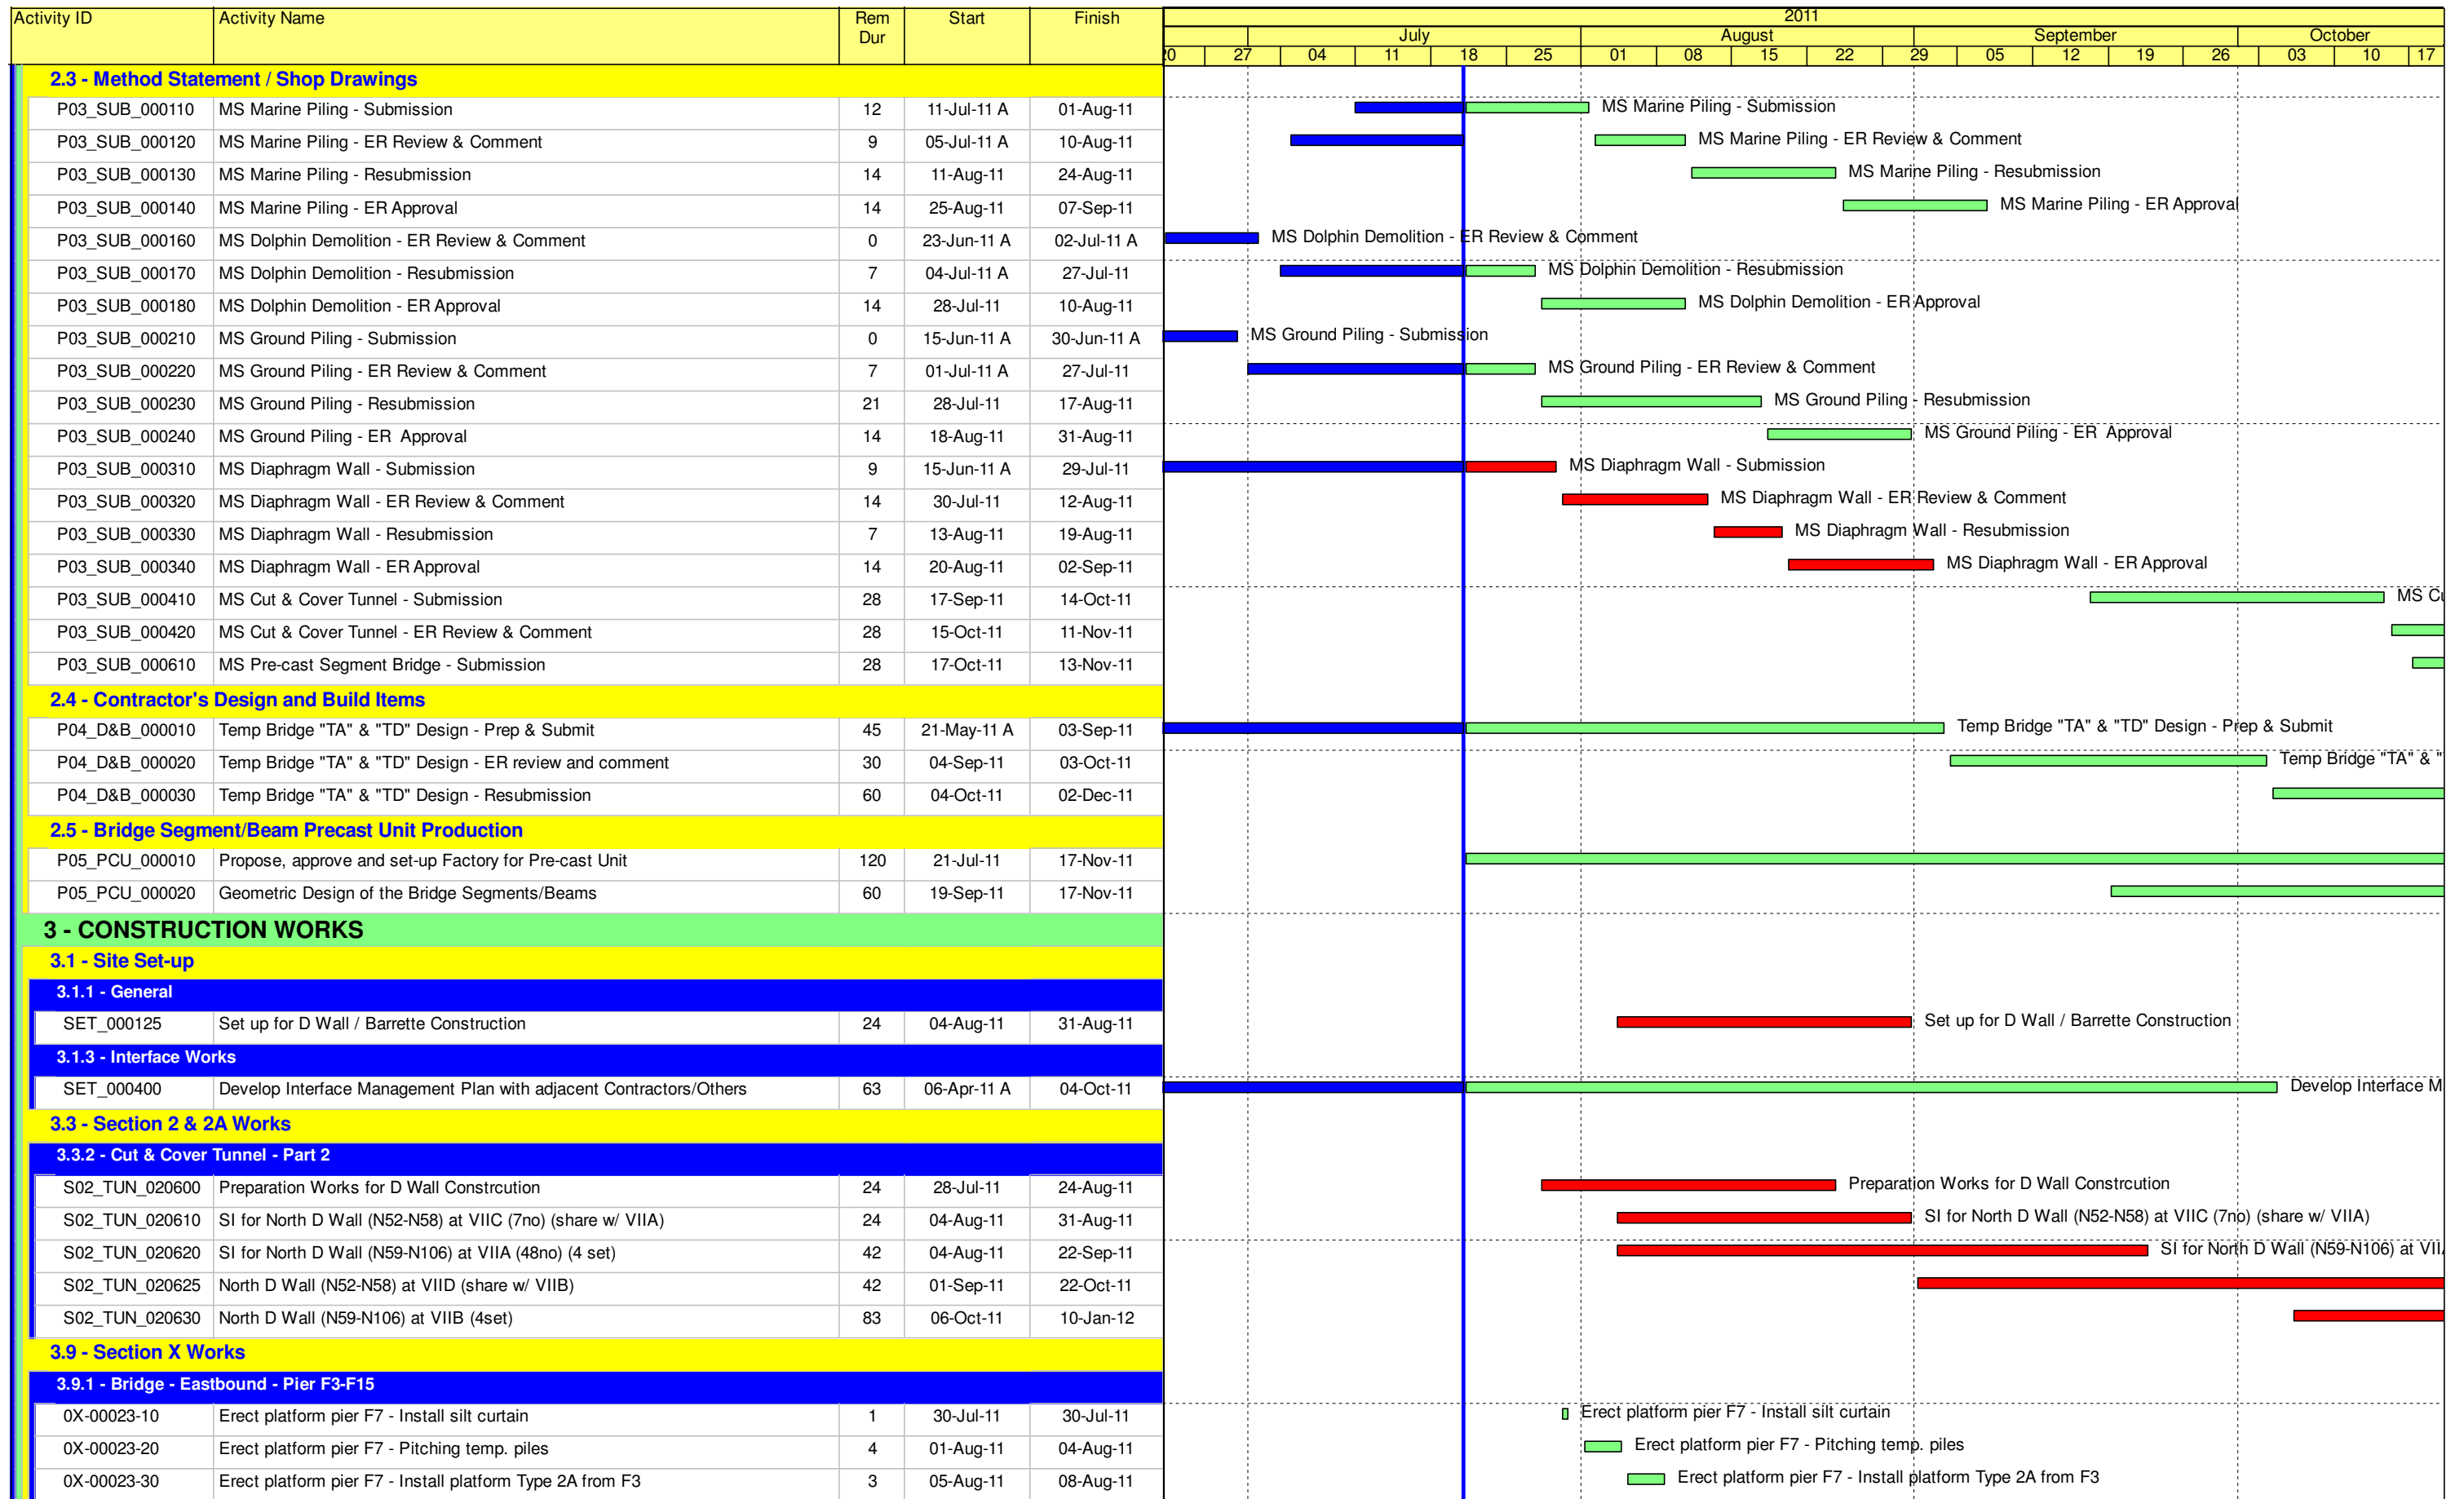


- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

**Contract HY/2009/19**

**Three Month Rolling Programme (21 July to 20 October 2011)**

3MRP

3MRP - Jul 2011 to Oct 2011

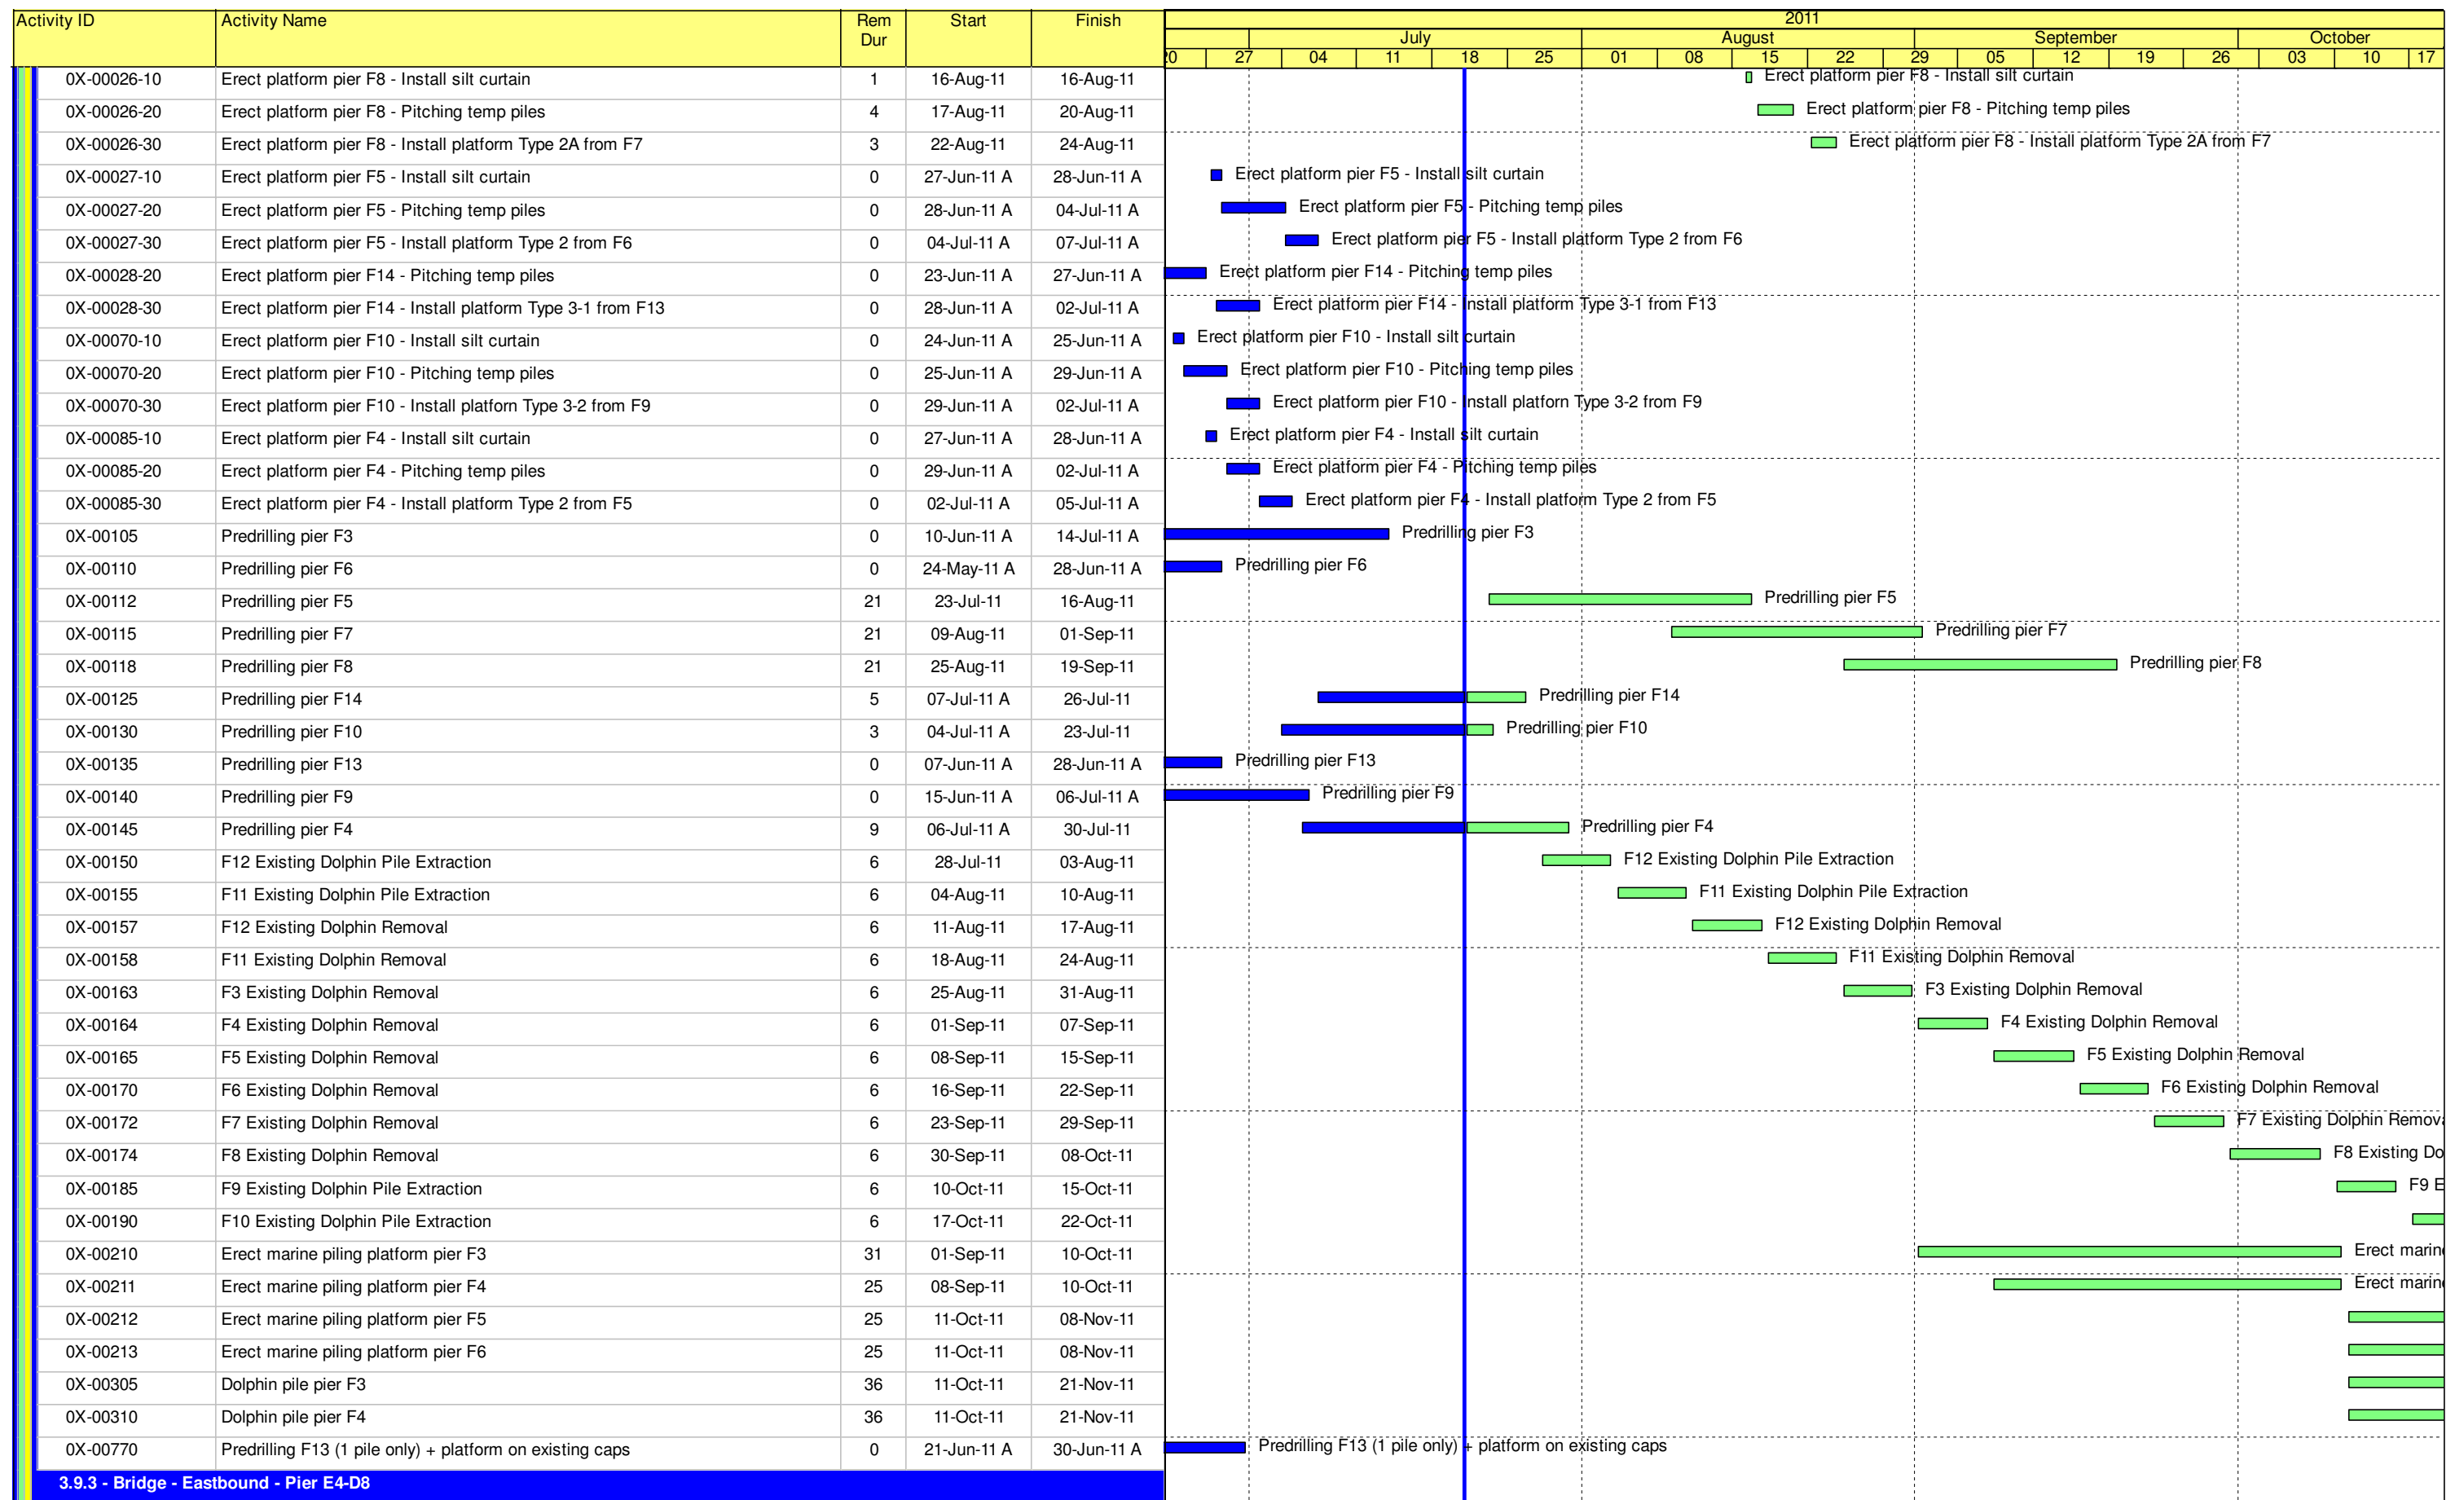

**3.9.3 - Bridge - Eastbound - Pier E4-D8**

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone







**Contract HY/2009/19**

**Three Month Rolling Programme (21 July to 20 October 2011)**

3MRP

3MRP - Jul 2011 to Oct 2011

Activity ID	Activity Name	Rem Dur	Start	Finish	2011																													
					July							August							September							October								
					0	27	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17												
S02_BRE_020010	Set-up for Piling Works on Ground at VIIB (possession VIIB on 03Aug11)	6	04-Aug-11	10-Aug-11																														
S02_BRE_020015	Pre-drilling for 18 nos Piling at VIIB ( 2set)	33	01-Sep-11	12-Oct-11																														
S02_BRE_020020	Bored Piles at E1, D5 to D7 (18 nos) at VIIB (2 set)	162	13-Oct-11	25-Apr-12																														
<b>3.12 - Section 14 Works</b>																																		
<b>3.12.1 - Soft Landscape</b>																																		
S11_LAN_110010	Transplant. of ex. Trees to Nursery & upkeep	1860	04-Aug-11*	12-Oct-17																														
<b>VO No. 1</b>																																		
V001-020	Prepare Sampling and Testing Plan	0	17-May-11 A	23-Jun-11 A																														
V001-030	EPD Approve Sampling and Testing Plan	9	24-Jun-11 A	30-Jul-11																														
V001-040	Excavate Trial Pit/Ground Investigation	48	01-Aug-11	26-Sep-11																														
V001-050	Testing of Soil Samples	48	27-Sep-11	23-Nov-11																														

-  Remaining Level of Effort
-  Actual Level of Effort
-  Actual Work
-  Remaining Work
-  Critical Remaining Work
-  Milestone


**Contract HY/2009/19**

**Three Month Rolling Programme (21 July to 20 October 2011)**

3MRP  
 3MRP - Jul 2011 to Oct 2011  
 Page 4 of 4

Wan Chai Development Phase II - Central - Wan Chai Bypass at Wan Chai East CONTRACT HK/2009/02

CHUN WO - CRGL JV

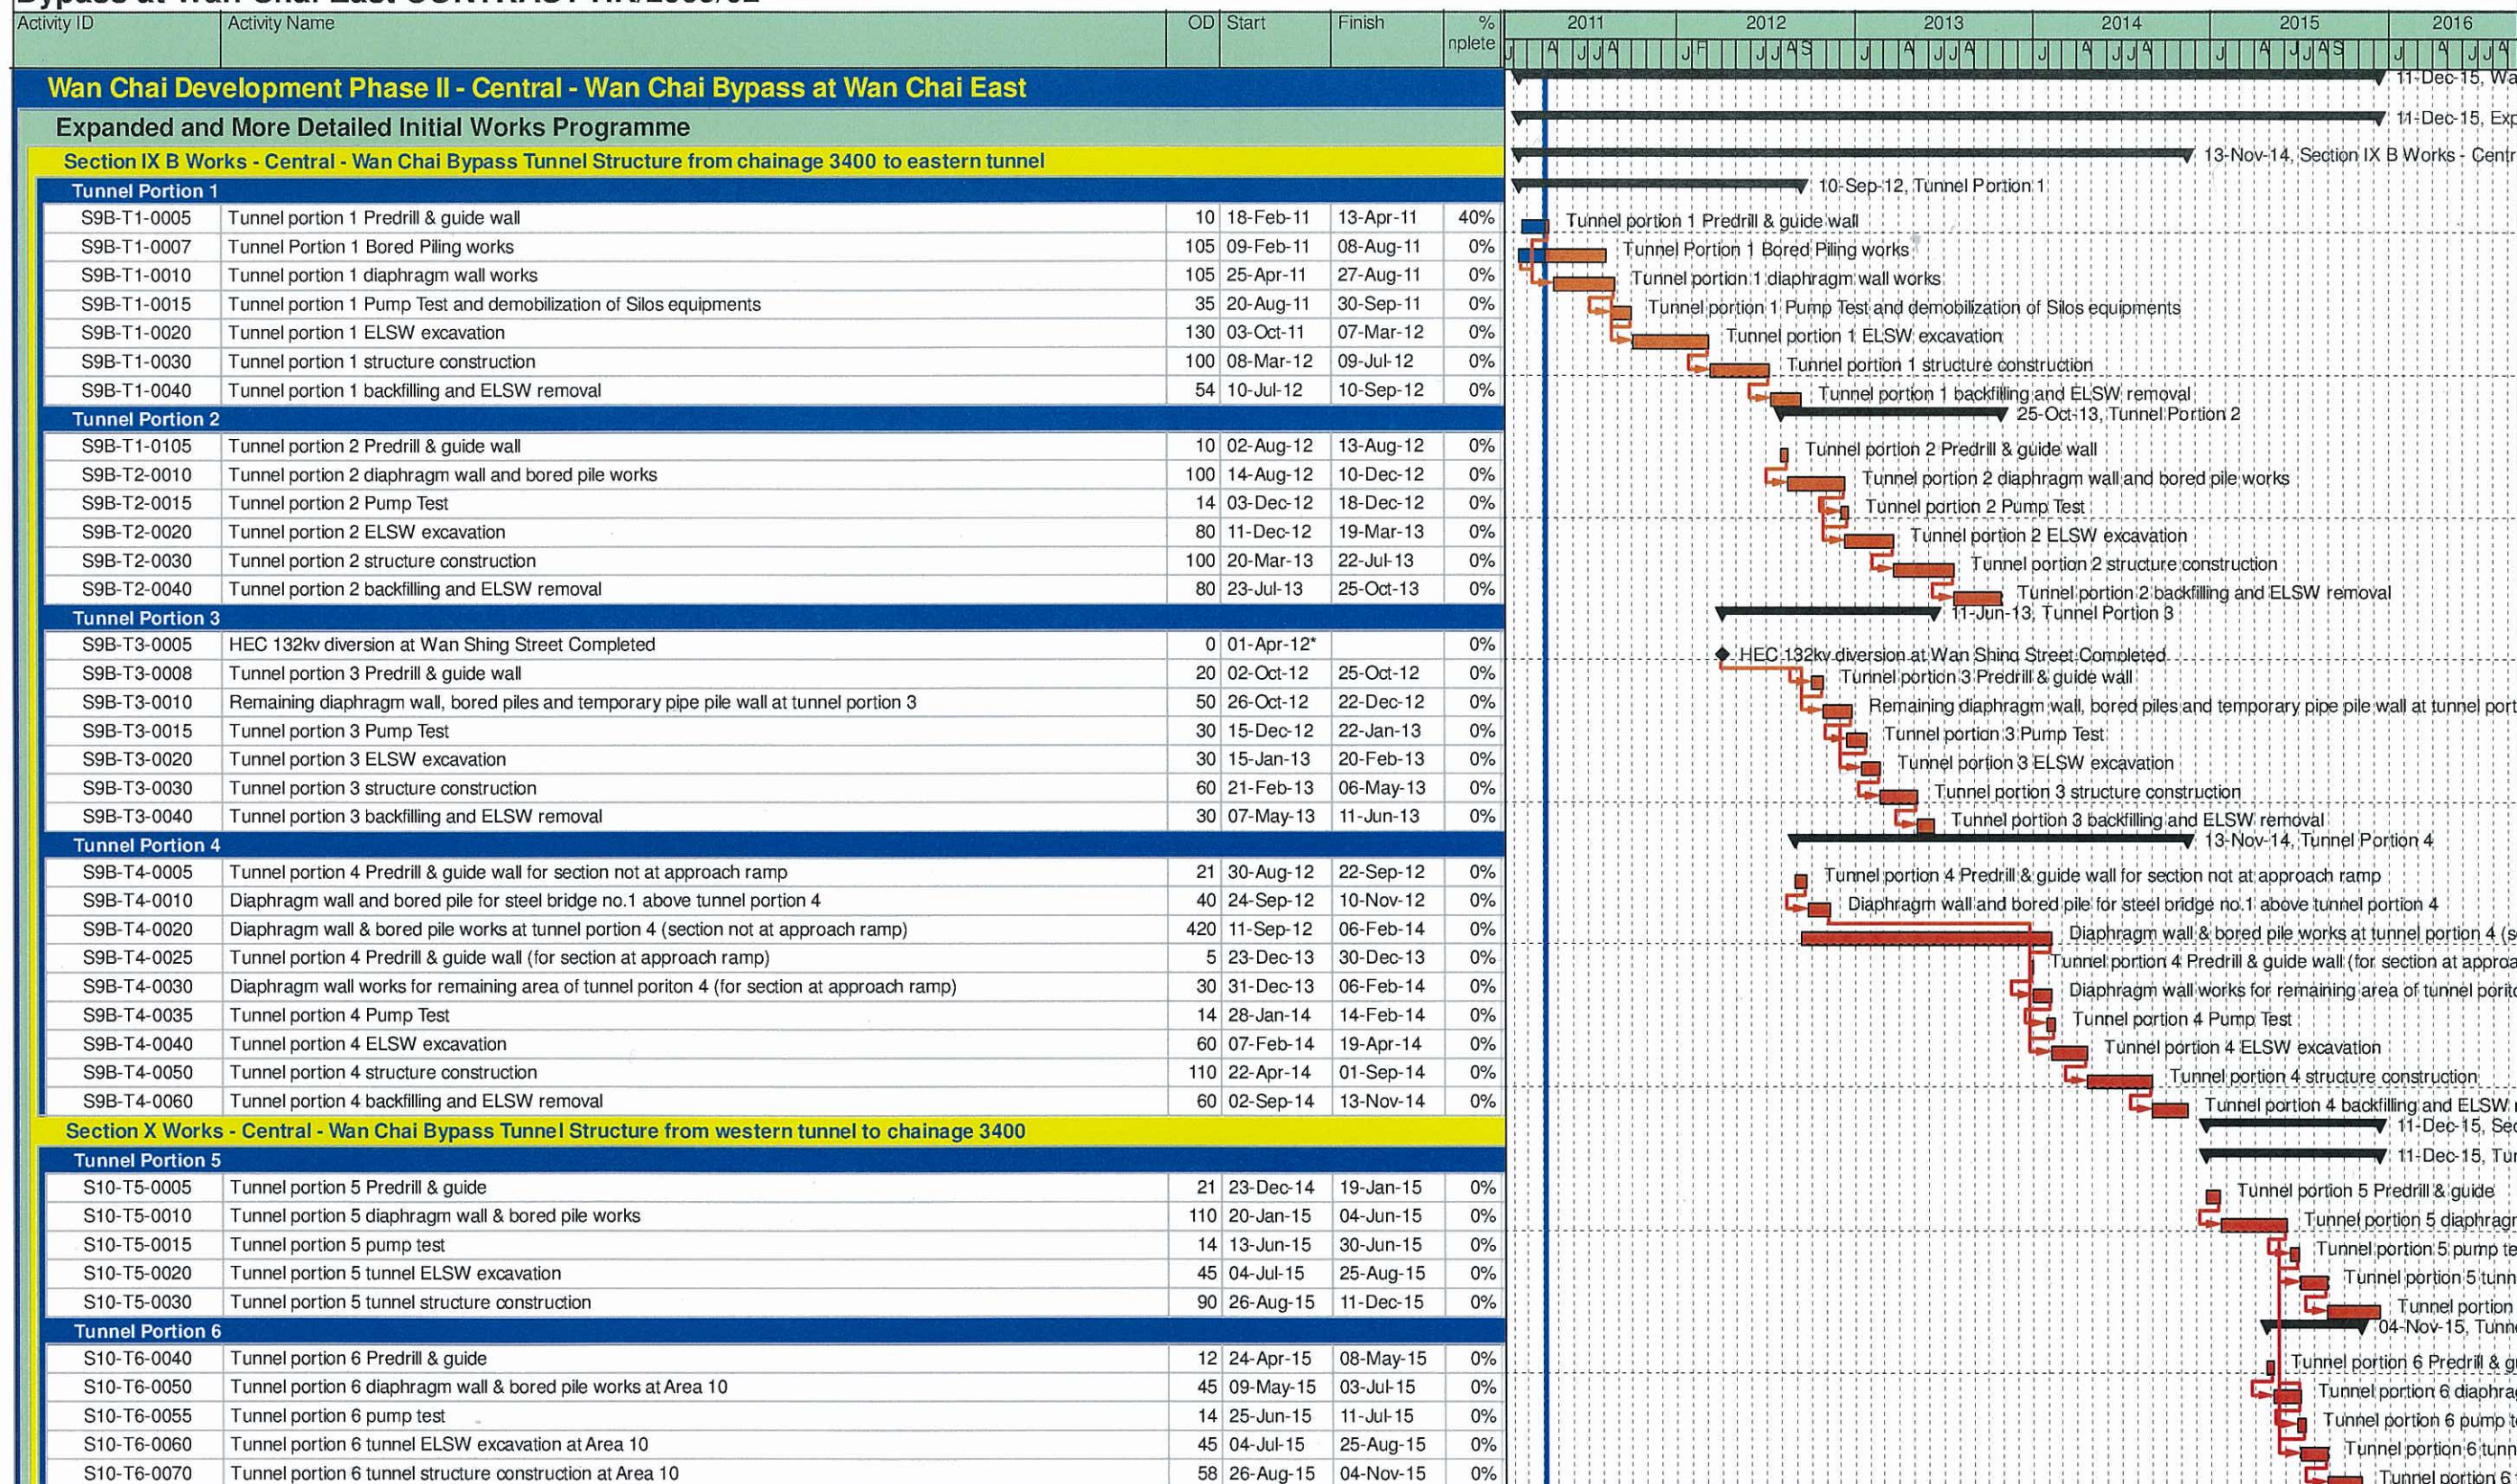

█ Remaining Level of Effort    ◆ Milestone  
█ Actual Level of Effort    ◀ Summary  
█ Actual Work  
█ Remaining Work  
█ Critical Remaining Work

CEDD CONTRACT NO. HK/2009/02  
**Wan Chai Development Phase II - Central Wan Chai Bypass at Wan Chai East (Contract 2)**  
 Revised Programme dated 7 April 2011

Date	Revision	Checked	Approved
07-Apr-11		KT	KY
