

Activity Name	Original Duration	Planned Start	Planned Finish	2011				2012				2013				2014				2015				2016	
				Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
<b>HY/2009/15 - CWB TUNNEL (CBTS SECTION)</b>																									
<b>SUBMISSIONS COMPLYING WITH EPs</b>																									
EM&A Manual ( rely on the Master EP's submission EP-364/2009/A Condition 2.9)																									
Baseline Monitoring Report (rely on the Master EP's submission EP-364/2009 Condition 3.3)																									
Monthly EM&A (rely on the masters EP's Submission, EP-364/2009/A Condition 3.4)																									
A dedicated website (rely on the master EP's submission, EP-364/2009/A Condition 4.2)																									
Management organization of main construction companies (FEP Condition 2.6)	1d	02-Oct-10	02-Oct-10																						
Work Schedule (FEP Condition 2.7)	1d	27-Oct-10	27-Oct-10																						
Location Plan (FEP Condition 2.8)	1d	27-Oct-10	27-Oct-10																						
Noise Management plan (FEP Condition 2.9)	1d	27-Oct-10	27-Oct-10																						
Landscape plan (FEP condition 2.10)	1d	31-Jan-11	31-Jan-11																						
<b>EAST VENTILATION ADIT</b>																									
CCT @ Portion 1, 2, 4, 6, 22	1315d	27-Sep-10	03-May-14																						
EV Adit @ Portion 4-Advance Works	526d	27-Sep-10	05-Mar-12																						
EV Adit Portion 1, 2, 6, 22	26d	22-Dec-11	16-Jan-12																						
EV Adit-based on Conforming Design	323d	15-Feb-12	02-Jan-13																						
<b>TCBR1E (TS1 Area)</b>																									
Diaphragm Wall Construction (incl. SI, & tests after completion)	107d	26-Apr-11	10-Aug-11																						
Excavation & Lateral Support, ELS	99d	16-Jul-11	22-Oct-11																						
Cut & Cover Tunnel Construction (incl. backfill)	78d	22-Oct-11	07-Jan-12																						
OHVD and Cable Trough (access from Portion 22)	76d	18-Dec-13	03-Mar-14																						
<b>TCBR2 + TCBR3 (TS2 Area)</b>																									
Diaphragm Wall Construction	118d	06-Jul-12	31-Oct-12																						
Excavation & Lateral Support, ELS	248d	06-Jul-12	10-Mar-13																						
Cut & Cover Tunnel Construction	164d	11-Mar-13	21-Aug-13																						
OHVD Cable Trough (Access from Portion 22)	150d	05-Aug-13	01-Jan-14																						
<b>TCBR1W (TS4 Area)</b>																									
Diaphragm Wall Construction	148d	28-Jun-11	22-Nov-11																						
Excavation & Lateral Support, ELS	319d	26-Jun-11	11-May-12																						
Landing Steps - Demolition/Reconstruct as footpath	40d	28-Jun-11	23-Aug-11																						

- ◆ Milestone
- ◆ Milestone
- ▨ Remaining Work
- ▨ Critical Remaining Work
- ▨ Actual Work

1 of 2

**China State Construction Engineering (Hong Kong) Ltd.**

**Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel**

**( CBTS Section)**

Prepared by William Caluza			
Date	Revision	Checked	Approved
14-Mar-11	Revision C	ST	KL
	File: GC01a		
	(Layout:HY/2009/15: CWB - Summary)		

**中國建築工程(香港)有限公司**

CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD

Activity Name	Original Duration	Planned Start	Planned Finish	2011					2012				2013				2014				2015				2016	
				Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1
Rock Excavation	235d	25-Apr-12	15-Dec-12																							
ME4-Diaphragm Wall	114d	10-May-12	19-Oct-12																							
AS Logistics Area for Mined Tunneling Works	174d	01-Jun-12	07-Feb-13																							
ME4-ELS Works	212d	01-Jun-12	02-Apr-13																							
SCL Entrusted Works	291d	18-Jul-12	08-Sep-13																							
Cut & Cover Tunnel Construction (w/o TS4 +)	111d	17-Dec-12	06-Apr-13																							
ME4-RC Structure	146d	28-Jan-13	21-Aug-13																							
OHVD and Cable Trough (Access from TZ5/TPCWAE/TPCWAW)	180d	17-Jun-13	13-Dec-13																							
<b>MINED TUNNEL</b>																										
CHT Protection Works @ location A, B, C	342d	27-Sep-10	01-Feb-12																							
Tunnel works from West Portal (access from TPCWAE& TZ5)	418d	12-Mar-12	30-Oct-13																							
Tunnel Works from East Portal (Access from TS4 Area)	214d	30-Mar-12	01-Feb-13																							
Tunnel OHVD & Cable Trough	384d	02-Dec-13	22-May-15																							
<b>TPCWAE</b>																										
Drainage Diversion works along Hung Hing Road (Portion 19)	176d	15-Oct-10	24-Jun-11																							
Diaphragm Wall Construction	147d	20-May-11	13-Oct-11																							
Excavation & Lateral Support, ELS	421d	20-May-11	13-Jul-12																							
Rock Excavation	206d	12-Mar-12	03-Oct-12																							
AS Logistics Area for Mined Tunneling works	342d	12-May-12	18-Apr-13																							
Cut & Cover Tunnel Construction	130d	28-Jan-13	06-Jun-13																							
OHVD and Cable Trough (Access from TZ5/TPCWAW)	182d	18-Feb-15	18-Aug-15																							
<b>TPCWAW &amp; PORTION 11</b>																										
Diaphragm Wall Construction + Portion 11	222d	25-Oct-13	03-Jun-14																							
Excavation & Lateral Support, ELS	478d	25-Oct-13	14-Feb-15																							
Cut & Cover Tunnel Construction	143d	30-Dec-14	21-May-15																							
OHVD and Cable Trough Installation (Access from Portion 11)	235d	22-May-15	11-Jan-16																							

- ◆ Milestone
- ◆ Milestone
- ▨ Remaining Work
- ▨ Critical Remaining Work
- ▨ Actual Work


2 of 2

**China State Construction Engineering (Hong Kong) Ltd.**

**Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel**

**( CBTS Section )**

Prepared by William Caluza			
Date	Revision	Checked	Approved
14-Mar-11	Revision C	ST	KL
	File: 0001a		
	(Layout: HY/2009/15: CWB - Summary)		














Wan Chai Development Phase II - Central - Wan Chai  
Bypass at Wan Chai East CONTRACT HK/2009/02

CHUN WO - CRGL JV

Activity ID	Activity Name	OD	Start	Finish	% Planned	2011	2012	2013	2014	2015	2016
<b>Wan Chai Development Phase II - Central - Wan Chai Bypass at Wan Chai East</b>											
<b>Expanded and More Detailed Initial Works Programme</b>											
Section IX B Works - Central - Wan Chai Bypass Tunnel Structure from chainage 3400 to eastern tunnel											
<b>Tunnel Portion 1</b>											
S9B-T1-0005	Tunnel portion 1 Predrill & guide wall	10	18-Feb-11	13-Apr-11	40%						
S9B-T1-0007	Tunnel Portion 1 Bored Piling works	105	09-Feb-11	08-Aug-11	0%						
S9B-T1-0010	Tunnel portion 1 diaphragm wall works	105	26-Apr-11	27-Aug-11	0%						
S9B-T1-0015	Tunnel portion 1 Pump Test and demobilization of Slos equipments	35	20-Aug-11	30-Sep-11	0%						
S9B-T1-0020	Tunnel portion 1 ELSW excavation	130	03-Oct-11	07-Mar-12	0%						
S9B-T1-0030	Tunnel portion 1 structure construction	100	09-Mar-12	09-Jul-12	0%						
S9B-T1-0040	Tunnel portion 1 backfilling and ELSW removal	54	10-Jul-12	10-Sep-12	0%						
<b>Tunnel Portion 2</b>											
S9B-T2-0105	Tunnel portion 2 Predrill & guide wall	10	02-Aug-12	13-Aug-12	0%						
S9B-T2-0010	Tunnel portion 2 diaphragm wall and bored pile works	100	14-Aug-12	10-Dec-12	0%						
S9B-T2-0015	Tunnel portion 2 Pump Test	14	03-Dec-12	18-Dec-12	0%						
S9B-T2-0020	Tunnel portion 2 ELSW excavation	80	11-Dec-12	19-Mar-13	0%						
S9B-T2-0030	Tunnel portion 2 structure construction	100	20-Mar-13	22-Jul-13	0%						
S9B-T2-0040	Tunnel portion 2 backfilling and ELSW removal	80	23-Jul-13	25-Oct-13	0%						
<b>Tunnel Portion 3</b>											
S9B-T3-0005	HEC 132kv diversion at Wan Shing Street Completed	0	01-Apr-12*		0%						
S9B-T3-0008	Tunnel portion 3 Predrill & guide wall	20	02-Oct-12	25-Oct-12	0%						
S9B-T3-0010	Remaining diaphragm wall, bored piles and temporary pipe pile wall at tunnel portion 3	50	25-Oct-12	22-Dec-12	0%						
S9B-T3-0015	Tunnel portion 3 Pump Test	30	15-Dec-12	22-Jan-13	0%						
S9B-T3-0020	Tunnel portion 3 ELSW excavation	30	15-Jan-13	20-Feb-13	0%						
S9B-T3-0030	Tunnel portion 3 structure construction	80	21-Feb-13	06-May-13	0%						
S9B-T3-0040	Tunnel portion 3 backfilling and ELSW removal	30	07-May-13	11-Jun-13	0%						
<b>Tunnel Portion 4</b>											
S9B-T4-0005	Tunnel portion 4 Predrill & guide wall for section not at approach ramp	21	30-Aug-12	22-Sep-12	0%						
S9B-T4-0010	Diaphragm wall and bored pile for steel bridge no.1 above tunnel portion 4	40	24-Sep-12	10-Nov-12	0%						
S9B-T4-0020	Diaphragm wall & bored pile works at tunnel portion 4 (section not at approach ramp)	420	11-Sep-12	05-Feb-14	0%						
S9B-T4-0025	Tunnel portion 4 Predrill & guide wall (for section at approach ramp)	5	23-Dec-13	30-Dec-13	0%						
S9B-T4-0030	Diaphragm wall works for remaining area of tunnel portion 4 (for section at approach ramp)	30	31-Dec-13	06-Feb-14	0%						
S9B-T4-0035	Tunnel portion 4 Pump Test	14	28-Jan-14	14-Feb-14	0%						
S9B-T4-0040	Tunnel portion 4 ELSW excavation	60	07-Feb-14	19-Apr-14	0%						
S9B-T4-0050	Tunnel portion 4 structure construction	110	22-Apr-14	01-Sep-14	0%						
S9B-T4-0060	Tunnel portion 4 backfilling and ELSW removal	60	02-Sep-14	13-Nov-14	0%						
Section X Works - Central - Wan Chai Bypass Tunnel Structure from western tunnel to chainage 3400											
<b>Tunnel Portion 5</b>											
S10-T5-0005	Tunnel portion 5 Predrill & guide	21	23-Dec-14	19-Jan-15	0%						
S10-T5-0010	Tunnel portion 5 diaphragm wall & bored pile works	110	20-Jan-15	04-Jun-15	0%						
S10-T5-0015	Tunnel portion 5 pump test	14	13-Jun-15	30-Jun-15	0%						
S10-T5-0020	Tunnel portion 5 tunnel ELSW excavation	45	04-Jul-15	25-Aug-15	0%						
S10-T5-0030	Tunnel portion 5 tunnel structure construction	90	26-Aug-15	11-Dec-15	0%						
<b>Tunnel Portion 6</b>											
S10-T6-0040	Tunnel portion 6 Predrill & guide	12	24-Apr-15	08-May-15	0%						
S10-T6-0050	Tunnel portion 6 diaphragm wall & bored pile works at Area 10	45	09-May-15	09-Jul-15	0%						
S10-T6-0055	Tunnel portion 6 pump test	14	25-Jun-15	11-Jul-15	0%						
S10-T6-0060	Tunnel portion 6 tunnel ELSW excavation at Area 10	45	04-Jul-15	26-Aug-15	0%						
S10-T6-0070	Tunnel portion 6 tunnel structure construction at Area 10	58	26-Aug-15	04-Nov-15	0%						

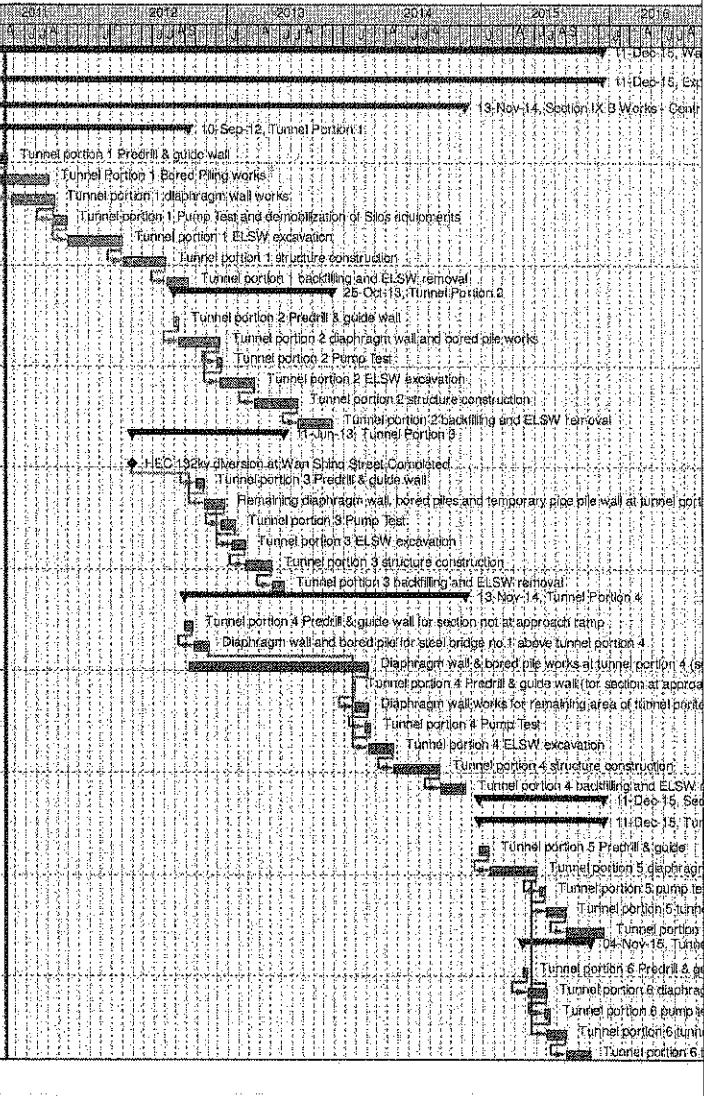

CEDD CONTRACT NO. HK/2009/02  
**Wan Chai Development Phase II - Central Wan Chai Bypass at Wan Chai East (Contract 2)**  
 Revised Programme dated 7 April 2011

Date	Revision	Checked	Approved
07-Apr-11		KT	KY

Page 10 of 11

Activity ID	Activity Name	Rem Dur	Start	Finish	2011							2012						
					December				January			February			March			
					21	28	05	12	19	26	02	09	16	23	30	06	13	20
<b>3MRP - Dec 2011 to Mar 2012</b>																		
<b>01 - CONTRACT DATES</b>																		
<b>01.1 - Conditions</b>																		
0110-1100	PMI for Section 1 of the Works	0		21-Dec-11														
<b>01.2 - Possession of Site</b>																		
0120-2000	Possession to Portion X	0	21-Dec-11*															
0120-2100	Possession to Portion III	0	31-Dec-11*															
0120-2200	Possession to Portion VA	0	31-Dec-11*															
0120-2300	Possession to Portion VB	0	31-Dec-11*															
0120-2400	Possession to Portion VC	0	31-Dec-11*															
0120-2500	Possession to Portion VD	0	31-Dec-11*															
<b>01.5 - Period of Site Possession for each Portion</b>																		
0150-1000	Site possession Period Portion VI	2062	20-Jan-11 A	12-Aug-17														
0150-1100	Site Possession Period Portion VIIA	2062	04-Aug-11 A	12-Aug-17														
0150-1200	Site Possession Period Portion VIIB	821	04-Aug-11 A	20-Mar-14														
0150-1300	Site Possession Period Portion VIIIC	1196	04-Aug-11 A	30-Mar-15														
0150-1400	Site Possession Period Portion VIID	821	04-Aug-11 A	20-Mar-14														
0150-1500	Site Possession Period Portion XI	626	05-Oct-11 A	06-Sep-13														
0150-1700	Site Possession Period Portion IB	821	10-Nov-11 A	20-Mar-14														
0150-1800	Site Possession Period Portion IC	1196	10-Nov-11 A	30-Mar-15														
0150-1900	Site Possession Period Portion ID	821	10-Nov-11 A	20-Mar-14														
0150-2000	Site Possession Period Portion X	2062	21-Dec-11	12-Aug-17														
0150-2100	Site Possession Period Portion III	2052	31-Dec-11	12-Aug-17														
0150-2200	Site Possession Period Portion VA	2052	31-Dec-11	12-Aug-17														
0150-2300	Site Possession Period Portion VB	994	31-Dec-11	19-Sep-14														
0150-2400	Site Possession Period Portion VC	2052	31-Dec-11	12-Aug-17														
0150-2500	Site Possession Period Portion VD	1314	31-Dec-11	05-Aug-15														
<b>02 - PRE-CONSTRUCTION WORKS</b>																		
<b>02.2 - Contractor's Submission</b>																		
0220-1200	Temp. Drainage Management Plan - Approval from ER	14	10-Sep-11 A	03-Jan-12														
0220-1250	Concrete Ready Mix/Design Mix - Concrete Plant Trials & Approval	15	04-Aug-11 A	04-Jan-12														
0220-1260	Drainage Pipes & Materials - Submission	14	15-Sep-11 A	03-Jan-12														
0220-1270	Drainage Pipes & Materials - ER Review/Comment	14	04-Jan-12	17-Jan-12														
0220-1280	Drainage Pipes & Materials - Resubmission	7	18-Jan-12	24-Jan-12														
0220-1290	Drainage Pipes & Materials - ER Approval	14	25-Jan-12	07-Feb-12														
0220-1300	Drainage Pipes & Materials - Procurement & Delivery	14	01-Feb-12	14-Feb-12														
0220-1350	D-Wall Construction Materials - Procurement & Delivery	0	15-Oct-11 A	28-Nov-11 A														
0220-1460	Bridge Bearing - Submission	15	10-Oct-11 A	04-Jan-12														
0220-1470	Bridge Bearing - ER Review/Comment	28	05-Jan-12	01-Feb-12														
0220-1480	Bridge Bearing - Resubmission	14	02-Feb-12	15-Feb-12														
0220-1490	Bridge Bearing - ER Approval	28	16-Feb-12	14-Mar-12														
<b>02.3 - Method Statement / Shop Drawings</b>																		
0230-1131	MS Marine Piling - Submission (low headroom)	28	27-Jan-12	23-Feb-12														
0230-1132	MS Marine Piling - ER Review & Comment (low headroom)	28	24-Feb-12	22-Mar-12														

**Contract HY/2009/19**  
**Three Month Rolling Programme (21 DEC 2011 - 20 MAR 2012)**



Activity ID	Activity Name	Rem Dur	Start	Finish	2011							2012						
					December				January			February			March			
					21	28	05	12	19	26	02	09	16	23	30	06	13	20
0230-1260	MS Cut & Cover Tunnel - Submission	28	15-Jan-12	11-Feb-12														
0230-1270	MS Cut & Cover Tunnel - ER Revlew & Comment	28	12-Feb-12	10-Mar-12														
0230-1280	MS Cut & Cover Tunnel - Resubmission	28	11-Mar-12	07-Apr-12														
0230-1460	MS Stressing/Destressing Tendons - Submission	28	01-Mar-12	28-Mar-12														
0230-1540	MS Precasting of Bridge Segment & Beam - Submission	55	14-Dec-11 A	13-Feb-12														
0230-1550	MS Precasting of Bridge Segment & Beam - ER Review & Comment	28	14-Feb-12	12-Mar-12														
0230-1560	MS Precasting of Bridge Segment & Beam - Resubmission	36	13-Mar-12	17-Apr-12														
<b>02.4 - Contractor's Design and Build Items</b>																		
0240-1010	Temp Bridge "TA" Design - Prep & Submit	118	16-Dec-11 A	16-Apr-12														
0240-1090	Int. Noise Enclosure Design - Public Consultation	144	29-Jul-11 A	12-May-12														
0240-1085	Int. Noise Enclosure Design - ACABAS/ER Consultation/Submission	86	16-Dec-11 A	15-Mar-12														
0240-1120	Noise Barrier Design - Public Consultation	144	29-Jul-11 A	12-May-12														
0240-1122	Noise Barrier Design - ACABAS/ER Consultation/Submission	86	16-Dec-11 A	15-Mar-12														
0240-1130	Perm. Noise Enclosure Design - Public Consultation	180	14-Feb-12	11-Aug-12														
0240-1360	Marine Bored Piling Platform Design - Resubmission (F3 to F8)	0	22-Aug-11 A	25-Nov-11 A														
0240-1370	Marine Bored Piling Platform Design - ER Approval (F3 to F8)	0	23-Sep-11 A	01-Dec-11 A														
0240-1371	Marine Bored Piling Platform Design (F9 to F14) - Submission	7	07-Nov-11 A	27-Dec-11														
0240-1372	Marine Bored Piling Platform Design (F9 to F14) - ER Review/Comment	14	28-Dec-11	10-Jan-12														
0240-1373	Marine Bored Piling Platform Design (F9 to F14) - Resubmission	14	11-Jan-12	24-Jan-12														
0240-1374	Marine Bored Piling Platform Design (F9 to F14) - ER Approval	14	25-Jan-12	07-Feb-12														
<b>02.5 - Bridge Segment/Beam Off-site Precasting</b>																		
0250-1000	Propose, approve and set-up Factory for Pre-cast Unit	147	14-Dec-11 A	15-May-12														
0250-1100	Geometric Design of the Bridge Segments/Beams	75	14-Dec-11 A	04-Mar-12														
0250-1200	Bridge Segment/Beam Mould Preparation	24	05-Mar-12	28-Mar-12														
<b>03 - PRELIMINARY WORKS</b>																		
<b>03.1 - Site Establishment</b>																		
0310-1290	Fabrication of Special Hoarding	26	24-Oct-11 A	19-Jan-12														
0310-1300	Hoarding at Portion VA & VB	40	20-Jan-12	09-Mar-12														
0310-1400	Move In Surcharge to Portion III & VD	6	10-Mar-12	16-Mar-12														
<b>03.2 - Geotechnical Instrumentation &amp; Monitoring Works</b>																		
0320-1050	Geotechnical Instrumentation Portion IB, ID	21	14-Nov-11 A	13-Jan-12														
0320-1100	Geotechnical Instrumentation Portion X	60	14-Jan-12	27-Mar-12														
<b>03.3 - Interface Works</b>																		
0330-1100	Works at FEHD Permanent Depot (Stage 1)	36	21-Dec-11	03-Feb-12														
0330-1110	Submit to FEHD/ER Relocation Sequence & Programme	6	21-Dec-11	27-Dec-11														
0330-1120	Relocate FEHD to Permanent Depot at Portions IA & X	12	04-Feb-12	17-Feb-12														
<b>04 - SECTION 1 OF THE WORKS (Subject to Excision)</b>																		
<b>04.1 - Drainage &amp; Sewerage</b>																		
0410-0980	Ground investigation + CAR & RAP approval	6	19-Jul-11 A	27-Dec-11														
0410-0990	Engineer Instruction to excision of the works	0		27-Dec-11														
0410-1010	Confirmatory Investigation/Sample/Tests/Decontamination	60	28-Dec-11	09-Mar-12														
0410-1020	Utility Coordination and Liaison	48	28-Dec-11	24-Feb-12														
0410-1030	Setting Out and Utility Detection & Protection at Portion XI	18	10-Mar-12	30-Mar-12														
<b>05 - SECTION 2 &amp; 2A OF THE WORKS</b>																		

- ▬ Remaining Level of Effort
- ▬ Actual Level of Effort
- ▬ Actual Work
- ▬ Remaining Work
- ▬ Critical Remaining Work
- ◆ Milestone

**Contract HY/2009/19**  
**Three Month Rolling Programme (21 DEC 2011 - 20 MAR 2012)**






3MRP  
3MRP - Dec 2011 to Mar 2012  
Page 2 of 7

Activity ID	Activity Name	Rem Dur	Start	Finish	2011												2012					
					December						January						February			March		
					21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	05	12	19
<b>05.2 - Cut &amp; Cover Tunnel Ch 4932-5149</b>																						
<b>05.2.1 - D-Wall Construction</b>																						
0521-1710.05	D-wall Panel N106 (6m - 441cu.m)	12	07-Mar-12	20-Mar-12																		
0521-1710.10	D-wall Panel N105 (4.8m - 354cu.m)	10	17-Feb-12	28-Feb-12															D-wall Panel N105 (4.8m - 354cu.m)			
0521-1710.15	D-wall Panel N104 (3.4m - 257cu.m)	9	09-Jan-12	18-Jan-12															D-wall Panel N104 (3.4m - 257cu.m)			
0521-1710.20	D-wall Panel N103 (3.4m - 256cu.m)	9	30-Jan-12	08-Feb-12															D-wall Panel N103 (3.4m - 256cu.m)			
0521-1710.25	D-wall Panel N101 (6m - 453cu.m)	0	17-Nov-11 A	14-Dec-11 A															D-wall Panel N101 (6m - 453cu.m)			
0521-1710.30	D-wall Panel N102 (6m - 452cu.m)	12	21-Dec-11	03-Jan-12															D-wall Panel N102 (6m - 452cu.m)			
0521-1710.35	D-wall Panel N100 (6m - 456cu.m)	12	29-Feb-12	13-Mar-12															D-wall Panel N100 (6m - 456cu.m)			
0521-1710.40	D-wall Panel N99 (6m - 459cu.m)	12	11-Feb-12	24-Feb-12															D-wall Panel N99 (6m - 459cu.m)			
0521-1710.45	D-wall Panel N98 (6m - 462cu.m)	3	03-Dec-11 A	23-Dec-11															D-wall Panel N98 (6m - 462cu.m)			
0521-1710.50	D-wall Panel N97 (3.29m - 265cu.m)	0	14-Nov-11 A	01-Dec-11 A															D-wall Panel N97 (3.29m - 265cu.m)			
0521-1710.55	D-wall Panel N96 (6m - 488cu.m)	12	14-Jan-12	31-Jan-12															D-wall Panel N96 (6m - 488cu.m)			
0521-1710.60	D-wall Panel N95 (6m - 492cu.m)	12	03-Jan-12	16-Jan-12															D-wall Panel N95 (6m - 492cu.m)			
0521-1750.05	D-wall Panel N94 (6m - 497cu.m)	12	20-Jan-12	06-Feb-12															D-wall Panel N94 (6m - 497cu.m)			
0521-1750.10	D-wall Panel N93 (6m - 501cu.m)	12	06-Feb-12	18-Feb-12															D-wall Panel N93 (6m - 501cu.m)			
0521-1750.15	D-wall Panel N92 (6m - 503cu.m)	12	23-Feb-12	07-Mar-12															D-wall Panel N92 (6m - 503cu.m)			
0521-1750.20	D-wall Panel N91 (6m - 472cu.m)	12	28-Dec-11	10-Jan-12															D-wall Panel N91 (6m - 472cu.m)			
0521-1750.25	D-wall Panel N90 (4.16m - 349cu.m)	0	01-Dec-11 A	19-Dec-11 A															D-wall Panel N90 (4.16m - 349cu.m)			
0521-1750.30	D-wall Panel N89 (4.16m - 349cu.m)	0	03-Nov-11 A	29-Nov-11 A															D-wall Panel N89 (4.16m - 349cu.m)			
0521-1750.35	D-wall Panel N88 (6m - 505cu.m)	8	19-Dec-11 A	29-Dec-11															D-wall Panel N88 (6m - 505cu.m)			
0521-1750.40	D-wall Panel N87 (6m - 506cu.m)	12	05-Jan-12	18-Jan-12															D-wall Panel N87 (6m - 506cu.m)			
0521-1750.45	D-wall Panel N86 (6m - 507cu.m)	12	24-Feb-12	08-Mar-12															D-wall Panel N86 (6m - 507cu.m)			
0521-1750.50	D-wall Panel N85 (6m - 507cu.m)	12	13-Feb-12	25-Feb-12															D-wall Panel N85 (6m - 507cu.m)			
0521-1750.55	D-wall Panel N84 (6m - 511cu.m)	12	26-Jan-12	08-Feb-12															D-wall Panel N84 (6m - 511cu.m)			
0521-1750.60	D-wall Panel N83 (6m - 517cu.m)	12	11-Jan-12	27-Jan-12															D-wall Panel N83 (6m - 517cu.m)			
0521-1790.10	D-wall Panel N74 (6m - 582cu.m)	12	01-Mar-12	14-Mar-12															D-wall Panel N74 (6m - 582cu.m)			
0521-1790.15	D-wall Panel N75 (6m - 554cu.m)	12	07-Feb-12	20-Feb-12															D-wall Panel N75 (6m - 554cu.m)			
0521-1790.20	D-wall Panel N76 (6m - 585cu.m)	12	17-Jan-12	02-Feb-12															D-wall Panel N76 (6m - 585cu.m)			
0521-1795.10	D-wall Panel N77 (6m - 570cu.m)	12	01-Feb-12	14-Feb-12															D-wall Panel N77 (6m - 570cu.m)			
0521-1795.15	D-wall Panel N78 (6m - 554cu.m)	12	30-Dec-11	12-Jan-12															D-wall Panel N78 (6m - 554cu.m)			
0521-1795.20	D-wall Panel N79 (6m - 545cu.m)	0	30-Nov-11 A	17-Dec-11 A															D-wall Panel N79 (6m - 545cu.m)			
0521-1795.25	D-wall Panel N80 (6m - 537cu.m)	12	18-Feb-12	02-Mar-12															D-wall Panel N80 (6m - 537cu.m)			
0521-1795.30	D-wall Panel N81 (6m - 530cu.m)	12	24-Dec-11	06-Jan-12															D-wall Panel N81 (6m - 530cu.m)			
0521-1795.35	D-wall Panel N82 (6m - 524cu.m)	0	10-Nov-11 A	09-Dec-11 A															D-wall Panel N82 (6m - 524cu.m)			
0521-1800	D-wall N59-N70 Pre-drilling (6 nos. remaining - 1 rig@6d/hole)	36	19-Sep-11 A	15-Feb-12															D-wall N59-N70 Pre-drilling (6 nos. remaining - 1 rig@6d/hole)			
0521-1810	D-wall N59-N70 Grouting for Existing Seawall Rubble Mound	21	16-Feb-12	10-Mar-12															D-wall N59-N70 Grouting for Existing Seawall Rubble Mound			
0521-1820	D-wall N59-N70 Guide Wall	12	12-Mar-12	24-Mar-12															D-wall N59-N70 Guide Wall			
0521-1830.10	D-wall Panel N70 (6m - 621cu.m)	12	06-Mar-12	19-Mar-12															D-wall Panel N70 (6m - 621cu.m)			
0521-1830.20	D-wall Panel N68 (3.95m - 409cu.m)	10	10-Mar-12	21-Mar-12															D-wall Panel N68 (3.95m - 409cu.m)			
0521-1840	D-wall N52-N58 Pre-drilling (7 nos@3d - 2 rig)	21	16-Feb-12	10-Mar-12															D-wall N52-N58 Pre-drilling (7 nos@3d - 2 rig)			
0521-1850	D-wall N52-N58 Grouting for Existing Seawall Rubble Mound	21	12-Mar-12	05-Apr-12															D-wall N52-N58 Grouting for Existing Seawall Rubble Mound			
0521-1910	D-wall Temp End-wall Pre-drilling (7 nos@3d - 1 rig)	18	12-Mar-12	31-Mar-12															D-wall Temp End-wall Pre-drilling (7 nos@3d - 1 rig)			
0521-1945.15	Slurry-wall TEW2 (Set 2)	4	13-Mar-12	16-Mar-12															Slurry-wall TEW2 (Set 2)			

Remaining Level of Effort  
 Actual Level of Effort  
 Actual Work  
 Remaining Work  
 Critical Remaining Work  
 Milestone

**Contract HY/2009/19**  
**Three Month Rolling Programme (21 DEC 2011 - 20 MAR 2012)**

Activity ID	Activity Name	Rem Dur	Start	Finish	2011												2012											
					December						January						February						March					
					21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	05	12	19						
0521-1960.10	Site Establishment - Haul Road / Access Road	0	15-Nov-11 A	27-Dec-11 A	Site Establishment - Haul Road / Access Road																							
0521-1960.20	Site Establishment - Additional Bentonite Plant	15	31-Dec-11	17-Jan-12	Site Establishment - Additional Bentonite Plant																							
0521-1970	D-wall S102-S113 Pre-drilling	0	10-Nov-11 A	03-Dec-11 A	D-wall S102-S113 Pre-drilling																							
0521-1980	D-wall S102-S113 Guide Wall	15	21-Dec-11	06-Jan-12	D-wall S102-S113 Guide Wall																							
0521-1990.10	D-wall Panel S113 (3.28m - 244cu.m)	10	18-Feb-12	29-Feb-12	D-wall Panel S113 (3.28m - 244cu.m)																							
0521-1990.20	D-wall Panel S111 (7.65m - 575cu.m)	12	18-Jan-12	03-Feb-12	D-wall Panel S111 (7.65m - 575cu.m)																							
0521-1990.25	D-wall Panel S110 (5.4m - 409cu.m)	10	25-Feb-12	07-Mar-12	D-wall Panel S110 (5.4m - 409cu.m)																							
0521-1990.35	D-wall Panel S108 (7.65m - 581cu.m)	12	28-Jan-12	10-Feb-12	D-wall Panel S108 (7.65m - 581cu.m)																							
0521-1990.40	D-wall Panel S107 (5.2m - 395cu.m)	10	03-Mar-12	14-Mar-12	D-wall Panel S107 (5.2m - 395cu.m)																							
0521-1990.50	D-wall Panel S105 (6m - 458cu.m)	12	04-Feb-12	17-Feb-12	D-wall Panel S105 (6m - 458cu.m)																							
0521-1990.55	D-wall Panel S104 (6m - 481cu.m)	12	10-Mar-12	23-Mar-12	D-wall Panel S104 (6m - 481cu.m)																							
0521-1990.65	D-wall Panel S102 (5.96m - 483 cu.m)	12	11-Feb-12	24-Feb-12	D-wall Panel S102 (5.96m - 483 cu.m)																							
0521-2000	D-wall S90-S101 Pre-drilling	0	14-Nov-11 A	15-Dec-11 A	D-wall S90-S101 Pre-drilling																							
0521-2010	D-wall S90-S101 Guide Wall	15	31-Dec-11	17-Jan-12	D-wall S90-S101 Guide Wall																							
0521-2030	D-wall S78-S89 Pre-drilling	12	10-Nov-11 A	03-Jan-12	D-wall S78-S89 Pre-drilling																							
0521-2040	D-wall S81-S89 Guide Wall	15	07-Jan-12	27-Jan-12	D-wall S81-S89 Guide Wall																							
0521-2050.10	D-wall Panel S81 (2.8m - 262cu.m)	9	11-Feb-12	21-Feb-12	D-wall Panel S81 (2.8m - 262cu.m)																							
0521-2050.15	D-wall Panel S82 (2.8m - 248cu.m)	9	28-Jan-12	07-Feb-12	D-wall Panel S82 (2.8m - 248cu.m)																							
0521-2050.20	D-wall Panel S83 (6m - 517cu.m)	12	18-Feb-12	02-Mar-12	D-wall Panel S83 (6m - 517cu.m)																							
0521-2050.25	D-wall Panel S84 (6m - 511cu.m)	12	04-Feb-12	17-Feb-12	D-wall Panel S84 (6m - 511cu.m)																							
0521-2055.10	D-wall Panel S85 (6m - 507cu.m)	12	25-Feb-12	09-Mar-12	D-wall Panel S85 (6m - 507cu.m)																							
0521-2055.20	D-wall Panel S87 (6m - 506cu.m)	12	03-Mar-12	16-Mar-12	D-wall Panel S87 (6m - 506cu.m)																							
0521-2055.30	D-wall Panel S89 (4.16m - 349cu.m)	10	10-Mar-12	21-Mar-12	D-wall Panel S89 (4.16m - 349cu.m)																							
0521-2060	D-wall S66-S77 Pre-drilling	25	04-Jan-12	04-Feb-12	D-wall S66-S77 Pre-drilling																							
0521-2070	D-wall S66-S77 Guide Wall	15	06-Feb-12	22-Feb-12	D-wall S66-S77 Guide Wall																							
0521-2090	D-wall S60-S65 Pre-drilling	25	18-Jan-12	18-Feb-12	D-wall S60-S65 Pre-drilling																							
0521-2100	D-wall S60-S65 Guide Wall	15	20-Feb-12	07-Mar-12	D-wall S60-S65 Guide Wall																							
0521-2120	D-wall S56-S59 Pre-drilling	25	04-Feb-12	03-Mar-12	D-wall S56-S59 Pre-drilling																							
0521-2130	D-wall S56-S59 Guide Wall	15	05-Mar-12	21-Mar-12	D-wall S56-S59 Guide Wall																							
0521-2150	D-wall N52-N108 G.I. Preliminary Report / Founding Level	37	25-Feb-12	11-Apr-12	D-wall N52-N108 G.I. Preliminary Report / Founding Level																							
0521-2155	D-wall S52-S113 G.I. Preliminary Report / Founding Level	30	06-Feb-12	10-Mar-12	D-wall S52-S113 G.I. Preliminary Report / Founding Level																							
<b>05.2.2 - Barrette Construction</b>																												
0522-2180	Barrette BC53-BC56 Pre-drilling	18	28-Jan-12	17-Feb-12	Barrette BC53-BC56 Pre-drilling																							
0522-2190	Barrette BC54-BC56 Grouting for Existing Seawall Rubble Mound	12	18-Feb-12	02-Mar-12	Barrette BC54-BC56 Grouting for Existing Seawall Rubble Mound																							
0522-2200	Barrette BC54-BC56 Guide Wall	12	03-Mar-12	16-Mar-12	Barrette BC54-BC56 Guide Wall																							
0522-2220	Barrette BC57-BC68 Pre-drilling	30	14-Nov-11 A	27-Jan-12	Barrette BC57-BC68 Pre-drilling																							
0522-2230	Barrette BC57-BC68 Grouting for Existing Seawall Rubble Mound	30	28-Jan-12	02-Mar-12	Barrette BC57-BC68 Grouting for Existing Seawall Rubble Mound																							
0522-2240	Barrette BC57-BC68 Guide Wall	24	18-Feb-12	16-Mar-12	Barrette BC57-BC68 Guide Wall																							
0522-2270	Barrette BC43-BC52 Pre-drilling	25	08-Feb-12	07-Mar-12	Barrette BC43-BC52 Pre-drilling																							
0522-2280	Barrette BC43-BC52 Grouting for Existing Seawall Rubble Mound	12	29-Feb-12	13-Mar-12	Barrette BC43-BC52 Grouting for Existing Seawall Rubble Mound																							
0522-2320	Barrette BC40-BC42 Pre-drilling	25	18-Feb-12	17-Mar-12	Barrette BC40-BC42 Pre-drilling																							
0522-2360	Bulkhead BW1-BW7 Pre-drilling	25	03-Mar-12	31-Mar-12	Bulkhead BW1-BW7 Pre-drilling																							
0522-2392	Barrette BC40-BC68 & BW1-7 G.I. Prelim Report / Founding Lev	48	18-Feb-12	17-Apr-12	Barrette BC40-BC68 & BW1-7 G.I. Prelim Report / Founding Lev																							
<b>05.2.3 - ELS</b>																												

-  Remaining Level of Effort
-  Actual Level of Effort
-  Actual Work
-  Remaining Work
-  Critical Remaining Work
-  Milestone

**Contract HY/2009/19**  
**Three Month Rolling Programme (21 DEC 2011 - 20 MAR 2012)**

3MRP  
3MRP - Dec 2011 to Mar 2012  
Page 4 of 7

Activity ID	Activity Name	Rem Dur	Start	Finish	2011												2012											
					December					January							February					March						
					21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	05	12	19						
0523-2398	Prepare & Submit Documents as per ETWB TCW No. 15/2005	30	21-Dec-11	27-Jan-12	Prepare & Submit Documents as per ETWB TCW No. 15/2005																							
<b>05.3 - Box Culvert T1</b>																												
0530-2990	Bay 4-5 Trench excavation	13	14-Nov-11 A	04-Jan-12	Bay 4-5 Trench excavation																							
0530-3000	Bay 4-5 Box Culvert Construction	42	05-Jan-12	25-Feb-12	Bay 4-5 Box Culvert Construction																							
0530-3010	Bay 4-5 Road Reinstatement	7	27-Feb-12	05-Mar-12	Bay 4-5 Road Reinst																							
0530-3015	Watson Road TTM Satge 2 - TMLG Approval/Endorsement	0	05-Aug-11 A	07-Dec-11 A	Watson Road TTM Satge 2 - TMLG Approval/Endorsement																							
0530-3020	Implement Watson Road TTM Stage 2	3	18-Feb-12	21-Feb-12	Implement Watson Road TTM Stage 2																							
0530-3030	Bay 1-3 Site Clearance/Formation	3	22-Feb-12	24-Feb-12	Bay 1-3 Site Clearance/Formation																							
0530-3040	Bay 1-3 Trench excavation	36	25-Feb-12	10-Apr-12																								
0530-3070	Bay 6A Trench excavation	9	03-Mar-12	13-Mar-12	Bay 6A T																							
0530-3111	Bay 9 - Sheet Piling Works	12	15-Oct-11 A	11-Feb-12	Bay 9 - Sheet Piling Works																							
0530-3113	Bay 9 - Excavation	12	13-Feb-12	25-Feb-12	Bay 9 - Excavation																							
0530-3114	Bay 9 - Box Culvert/Outfall Construction	48	27-Feb-12	25-Apr-12																								
0530-3200	Storm Drainage 1500 Dia. Within Portion X (FEHD)	60	18-Feb-12	02-May-12																								







**10 - SECTION X OF THE WORKS**

**10.1 - E/B Bridges (Bridge D, E and F)**

**10.1.1 - Marine Pier Construction**

**Pier F03 to F15**

1011-1420	Extract Existing Dolphin Front Pile pier F9	1	26-Dec-11*	26-Dec-11	Extract Existing Dolphin Front Pile pier F9																							
1011-1425	Remove Existing Dolphin pier F9	2	27-Dec-11	28-Dec-11	Remove Existing Dolphin pier F9																							
1011-1430	Extract Existing Dolphin Front Pile pier F10	1	29-Dec-11	29-Dec-11	Extract Existing Dolphin Front Pile pier F10																							
1011-1435	Remove Existing Dolphin pier F10	2	30-Dec-11	31-Dec-11	Remove Existing Dolphin pier F10																							
1011-1530.30	F3 piling platform - ICE	0	03-Nov-11 A	23-Nov-11 A	F3 piling platform - ICE																							
1011-1550.10	F5 piling platform - temporary piles 1 to 4	0	17-Oct-11 A	22-Nov-11 A	F5 piling platform - temporary piles 1 to 4																							
1011-1550.20	F5 piling platform - erect steel platform modules 1 & 2	0	21-Nov-11 A	25-Nov-11 A	F5 piling platform - erect steel platform modules 1 & 2																							
1011-1550.30	F5 piling platform - temporary piles 5 & 6	0	25-Nov-11 A	30-Nov-11 A	F5 piling platform - temporary piles 5 & 6																							
1011-1550.40	F5 piling platform - erect steel platform modules 3 & 4	0	30-Nov-11 A	03-Dec-11 A	F5 piling platform - erect steel platform modules 3 & 4																							
1011-1550.50	F5 piling platform - ICE	0	05-Dec-11 A	08-Dec-11 A	F5 piling platform - ICE																							
1011-1560.20	F6 piling platform - erect steel platform modules 1 & 2	0	21-Nov-11 A	25-Nov-11 A	F6 piling platform - erect steel platform modules 1 & 2																							
1011-1560.30	F6 piling platform - temporary piles 5 & 6	0	25-Nov-11 A	30-Nov-11 A	F6 piling platform - temporary piles 5 & 6																							
1011-1560.40	F6 piling platform - erect steel platform modules 3 & 4	0	01-Dec-11 A	09-Dec-11 A	F6 piling platform - erect steel platform modules 3 & 4																							
1011-1560.50	F6 piling platform - ICE	0	10-Dec-11 A	13-Dec-11 A	F6 piling platform - ICE																							
1011-1570.10	F7 piling platform - temporary piles 1 to 4	0	15-Oct-11 A	30-Nov-11 A	F7 piling platform - temporary piles 1 to 4																							
1011-1570.20	F7 piling platform - erect steel platform modules 1 & 2	0	01-Dec-11 A	15-Dec-11 A	F7 piling platform - erect steel platform modules 1 & 2																							
1011-1570.30	F7 piling platform - temporary piles 5 & 6	5	16-Dec-11 A	26-Dec-11	F7 piling platform - temporary piles 5 & 6																							
1011-1570.40	F7 piling platform - erect steel platform modules 3 & 4	7	27-Dec-11	03-Jan-12	F7 piling platform - erect steel platform modules 3 & 4																							
1011-1570.50	F7 piling platform - ICE	6	04-Jan-12	10-Jan-12	F7 piling platform - ICE																							
1011-1580.10	F8 piling platform - temporary piles 1 to 4	0	18-Oct-11 A	15-Dec-11 A	F8 piling platform - temporary piles 1 to 4																							
1011-1580.20	F8 piling platform - erect steel platform modules 1 & 2	5	16-Nov-11 A	26-Dec-11	F8 piling platform - erect steel platform modules 1 & 2																							
1011-1580.30	F8 piling platform - temporary piles 5 & 6	7	27-Dec-11	03-Jan-12	F8 piling platform - temporary piles 5 & 6																							
1011-1580.40	F8 piling platform - erect steel platform modules 3 & 4	7	04-Jan-12	11-Jan-12	F8 piling platform - erect steel platform modules 3 & 4																							
1011-1580.50	F8 piling platform - ICE	6	12-Jan-12	18-Jan-12	F8 piling platform - ICE																							
1011-1610	Erect marine piling platform pier F11	36	26-Jan-12	07-Mar-12	Erect marine piling platform pier F11																							
1011-1620	Erect marine piling platform pier F12	36	12-Jan-12	25-Feb-12	Erect marine piling platform pier F12																							

-  Remaining Level of Effort
-  Actual Level of Effort
-  Actual Work
-  Remaining Work
-  Critical Remaining Work
-  Milestone

Contract HY/2009/19

Three Month Rolling Programme (21 DEC 2011 - 20 MAR 2012)

3MRP

3MRP - Dec 2011 to Mar 2012

Page 5 of 7

Activity ID	Activity Name	Rem Dur	Start	Finish	2011												2012											
					December						January						February						March					
					21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	05	12	19						
1011-1650	Pre-drill F5 raking dolphin piles (2 nos.)	0	09-Dec-11 A	20-Dec-11 A	Pre-drill F5 raking dolphin piles (2 nos.)																							
1011-1660	Pre-drill F6 raking dolphin piles (2 nos.)	2	13-Dec-11 A	22-Dec-11	Pre-drill F6 raking dolphin piles (2 nos.)																							
1011-1670	Pre-drill F7 raking dolphin piles (2 nos.)	10	11-Jan-12	21-Jan-12	Pre-drill F7 raking dolphin piles (2 nos.)																							
1011-1680	Pre-drill F8 raking dolphin piles (2 nos.)	10	26-Jan-12	06-Feb-12	Pre-drill F8 raking dolphin piles (2 nos.)																							
1011-1710	Pre-drill F11 raking dolphin piles (2 nos.)	10	08-Mar-12	19-Mar-12	Pre-drill F11 raking dolphin piles (2 nos.)																							
1011-1760.10	Pier F3 Marine Bore Pile - F3-8	1	23-Nov-11 A	21-Dec-11	Pier F3 Marine Bore Pile - F3-8																							
1011-1760.20	Pier F3 Marine Bore Pile - F3-4	12	22-Dec-11	04-Jan-12	Pier F3 Marine Bore Pile - F3-4																							
1011-1760.30	Pier F3 Marine Bore Pile - F3-7	12	05-Jan-12	18-Jan-12	Pier F3 Marine Bore Pile - F3-7																							
1011-1760.40	Pier F3 Marine Bore Pile - F3-3	12	19-Jan-12	04-Feb-12	Pier F3 Marine Bore Pile - F3-3																							
1011-1760.50	Pier F3 Marine Bore Pile - F3-6	12	06-Feb-12	18-Feb-12	Pier F3 Marine Bore Pile - F3-6																							
1011-1760.60	Pier F3 Marine Bore Pile - F3-2	12	20-Feb-12	03-Mar-12	Pier F3 Marine Bore Pile - F3-2																							
1011-1800.10	Pier F6 Marine Bore Pile - F6-2	10	15-Dec-11 A	31-Dec-11	Pier F6 Marine Bore Pile - F6-2																							
1011-1800.20	Pier F6 Marine Bore Pile - F6-4	12	02-Jan-12	14-Jan-12	Pier F6 Marine Bore Pile - F6-4																							
1011-1800.30	Pier F6 Marine Bore Pile - F6-1	12	16-Jan-12	01-Feb-12	Pier F6 Marine Bore Pile - F6-1																							
1011-1800.40	Pier F6 Marine Bore Pile - F6-3	12	02-Feb-12	15-Feb-12	Pier F6 Marine Bore Pile - F6-3																							
1011-1820.10	Pier F5 Marine Bore Pile - F5-4	8	09-Dec-11 A	29-Dec-11	Pier F5 Marine Bore Pile - F5-4																							
1011-1820.20	Pier F5 Marine Bore Pile - F5-2	12	30-Dec-11	12-Jan-12	Pier F5 Marine Bore Pile - F5-2																							
1011-1820.30	Pier F5 Marine Bore Pile - F5-1	12	19-Jan-12	30-Jan-12	Pier F5 Marine Bore Pile - F5-1																							
1011-1820.40	Pier F5 Marine Bore Pile - F5-3	12	31-Jan-12	13-Feb-12	Pier F5 Marine Bore Pile - F5-3																							
1011-1860.10	Pier F4 Marine Bore Pile - F4-3	0	14-Nov-11 A	16-Dec-11 A	Pier F4 Marine Bore Pile - F4-3																							
1011-1860.20	Pier F4 Marine Bore Pile - F4-6	11	19-Dec-11 A	02-Jan-12	Pier F4 Marine Bore Pile - F4-6																							
1011-1860.30	Pier F4 Marine Bore Pile - F4-5	12	03-Jan-12	16-Jan-12	Pier F4 Marine Bore Pile - F4-5																							
1011-1860.40	Pier F4 Marine Bore Pile - F4-2	12	17-Jan-12	02-Feb-12	Pier F4 Marine Bore Pile - F4-2																							
1011-1860.50	Pier F4 Marine Bore Pile - F4-4	12	03-Feb-12	16-Feb-12	Pier F4 Marine Bore Pile - F4-4																							
1011-1860.60	Pier F4 Marine Bore Pile - F4-1	12	17-Feb-12	01-Mar-12	Pier F4 Marine Bore Pile - F4-1																							
1011-1910	Pier F7 Dolphin Pile (team 5)	72	26-Jan-12	21-Apr-12	Pier F7 Dolphin Pile (team 5)																							
<b>Risk F01 to F02</b>																												
1011-2540	Possession to Portion III	0	31-Dec-11*		◆ Possession to Portion III																							
1011-2550	Marine piling preparation works, portion III	6	31-Dec-11	06-Jan-12	Marine piling preparation works, portion III																							
1011-2560	Erect Pre-drilling Platform pier F2B	8	02-Jan-12	10-Jan-12	Erect Pre-drilling Platform pier F2B																							
1011-2570	Erect Pre-drilling Platform pier F2A	8	11-Jan-12	19-Jan-12	Erect Pre-drilling Platform pier F2A																							
1011-2580	Erect Pre-drilling Platform pier F1B	8	20-Jan-12	01-Feb-12	Erect Pre-drilling Platform pier F1B																							
1011-2590	Erect Pre-drilling Platform pier F1A	8	02-Feb-12	10-Feb-12	Erect Pre-drilling Platform pier F1A																							
1011-2600	Pre-drilling pier F2B	10	11-Jan-12	21-Jan-12	Pre-drilling pier F2B																							
1011-2610	Pre-drilling pier F2A	20	20-Jan-12	15-Feb-12	Pre-drilling pier F2A																							
1011-2620	Pre-drilling pier F1B	10	02-Feb-12	13-Feb-12	Pre-drilling pier F1B																							
1011-2630	Pre-drilling pier F1A	20	11-Feb-12	05-Mar-12	Pre-drilling pier F1A																							
1011-2635	Portion III Marine Pile G.I. Final Report / Founding Level	30	06-Mar-12	12-Apr-12																								
1011-2640	Dismantle Pre-drilling Platform Pier F2B	5	26-Jan-12	31-Jan-12	Dismantle Pre-drilling Platform Pier F2B																							
1011-2650	Dismantle Pre-drilling Platform Pier F2A	5	16-Feb-12	21-Feb-12	Dismantle Pre-drilling Platform Pier F2A																							
1011-2660	Dismantle Pre-drilling Platform Pier F1B	5	22-Feb-12	27-Feb-12	Dismantle Pre-drilling Platform Pier F1B																							
1011-2670	Dismantle Pre-drilling Platform Pier F1A	5	06-Mar-12	10-Mar-12	Dismantle Pre-drilling Platform Pier F1A																							
1011-2680	Remove existing dolphin pier F2	6	22-Feb-12	28-Feb-12	Remove existing dolphin pier F2																							
1011-2690	Remove existing dolphin pier F1	6	12-Mar-12	17-Mar-12	Remove existing dolphin pier F1																							

Remaining Level of Effort  
 Actual Level of Effort  
 Actual Work  
 Remaining Work  
 Critical Remaining Work  
 Milestone

**Contract HY/2009/19**  
**Three Month Rolling Programme (21 DEC 2011 - 20 MAR 2012)**

3MRP  
 3MRP - Dec 2011 to Mar 2012  
 Page 6 of 7

Activity ID	Activity Name	Rem Dur	Start	Finish	2011					2012														
					December					January					February					March				
					21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	05	12	19		
<b>10.1.2 - Land Pier Construction</b>																								
<b>Pier D08 to D11</b>																								
1012-1010	Site Survey and Setting Out at Portion III	6	31-Dec-11	06-Jan-12	Site Survey and Setting Out at Portion III																			
1012-1015	Pre-drilling for Piling (D08 to D12) at III (28 no.) (4set)	27	07-Jan-12	10-Feb-12	Pre-drilling for Piling (D08 to D12) at III (28 no.) (4set)																			
1012-1020	Portion III Land Pile G.I. Prelim Report / Founding Level	6	11-Feb-12	17-Feb-12	Portion III Land Pile G.I. Prelim Report / Founding Level																			
1012-1025	Portion III Land Pile G.I. Final Report / Founding Level	24	18-Feb-12	16-Mar-12	Portion III Land Pile G.I. Final Report / Founding Level																			
1012-1030	Pier D08 Bored Piles (6 piles)	72	11-Feb-12	09-May-12	Pier D08 Bored Piles (6 piles)																			
1012-1040	Pier D09 Bored Piles (6 piles)	72	11-Feb-12	09-May-12	Pier D09 Bored Piles (6 piles)																			
1012-1050	Pier D10 Bored Piles (6 piles)	72	11-Feb-12	09-May-12	Pier D10 Bored Piles (6 piles)																			
1012-1060	Pier D11 Bored Piles (6 piles)	72	11-Feb-12	09-May-12	Pier D11 Bored Piles (6 piles)																			
<b>Pier D05 to D07</b>																								
1012-1260	Pre-drilling for 18 nos Piling at VIIB ( 2set)	30	08-Aug-11 A	27-Jan-12	Pre-drilling for 18 nos Piling at VIIB ( 2set)																			
1012-1265	Portion VIIB Land Pile G.I. Final Report / Founding Level	18	03-Oct-11 A	17-Feb-12	Portion VIIB Land Pile G.I. Final Report / Founding Level																			
1012-1280.30	Pier D06 Bored Pile D06-5	0	19-Nov-11 A	05-Dec-11 A	Pier D06 Bored Pile D06-5																			
1012-1280.40	Pier D06 Bored Pile D06-2	0	07-Dec-11 A	20-Dec-11 A	Pier D06 Bored Pile D06-2																			
1012-1280.50	Pier D06 Bored Pile D06-4	15	21-Dec-11	06-Jan-12	Pier D06 Bored Pile D06-4																			
1012-1280.60	Pier D06 Bored Pile D06-3	15	07-Jan-12	27-Jan-12	Pier D06 Bored Pile D06-3																			
1012-1290.10	Pier D05 Bored Pile D05-2	0	10-Nov-11 A	30-Nov-11 A	Pier D05 Bored Pile D05-2																			
1012-1290.20	Pier D05 Bored Pile D05-1	0	02-Dec-11 A	15-Dec-11 A	Pier D05 Bored Pile D05-1																			
<b>10.1.3 - E/B Bridge Construction</b>																								
<b>Bridge DS</b>																								
1013-1000	Design & Procurement of Launching Girder	75	20-Jan-12	23-Apr-12	Design & Procurement of Launching Girder																			
<b>14 - SECTION 14 OF THE WORKS</b>																								
<b>14.1 - Soft Landscape</b>																								
1410-1000	Transplant. of ex. Trees to Nursery & upkeep	1515	31-Dec-11	17-Jan-17	Transplant. of ex. Trees to Nursery & upkeep																			

- ▬ Remaining Level of Effort
- ▬ Actual Level of Effort
- ▬ Actual Work
- ▬ Remaining Work
- ▬ Critical Remaining Work
- ◆ Milestone

**Contract HY/2009/19**  
**Three Month Rolling Programme (21 DEC 2011 - 20 MAR 2012)**

3MRP  
3MRP - Dec 2011 to Mar 2012  
Page 7 of 7
