





Contract No. HK/2009/01

Wan Chai Development Phase II – Central -Wan Chai Bypass at
Hong Kong Convention and Exhibition Centre

Construction Activities for Three Months Rolling

Construction Activities	August 2017	September 2017	October 2017
Reinstatement of Amenity Area			
Road and Drain Works			



Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2017				2018	
					Oct	Nov	Dec	Jan		
HK/2012/08 Revised Works Programme Rev.11.1(DD 30 Jun 2017)										
Dredging and Reclamation										
Marine Work Construction										
Zone D										
Seawall Construction - Zone D										
Seawall 10 & 11										
MAR20630	Zone D - Seawall 10 & 11: Install remaining seawall block	15	14-Oct-17	28-Oct-17						
MAR20650	Zone D - Seawall 10 & 11: Backfill Type A	16	29-Oct-17	13-Nov-17						
MAR20670	Zone D - Seawall 10 & 11: Lay geotextile and filter	19	14-Nov-17	02-Dec-17						
Works for Section Completion										
Construction										
CWB Tunnel & Slip Road Structures and Facilities										
CWB D - Slip Road 1 - Trough / Retaining Wall										
CWB D - Slip Road 1 - Trough/Retaining Wall Structure										
SIIA13742	Sec II A - CWB SR1 Trough & RW: Trough Structure bay 1a & 1b: Construct box-out area & backfilling	25	07-Oct-17	31-Oct-17						
Section III A - Road A2, A4 & A5										
Roadwork & Utilities - Section 1 (L1806 - L1801)										
SIIA10301	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L1806 -L1801)	20	01-Nov-17	23-Nov-17						
SIIA10300	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L2202-L2201)	21	03-Oct-17	26-Oct-17						
SIIA10340	Sec III A - roadwork and utilities section 1 carriageway - utilities: HEC along carriageway	21	23-Dec-17	19-Jan-18						
SIIA10302	Sec III A - roadwork and utilities section 1 carriageway - gully pipe	18	24-Nov-17	14-Dec-17						
SIIA10320	Sec III A - roadwork and utilities section 1 carriageway - watermain	7	15-Dec-17	22-Dec-17						
SIIA10290	Sec III A - roadwork and utilities section 1 carriageway - Implementation of TTA Stage 5	1	30-Sep-17	30-Sep-17						
Roadwork & Utilities - Section 2 (L1810 - L1806)										
SIIA12530	Sec III A - roadwork and utilities section 2 carriageway - watermain	10	14-Nov-17	24-Nov-17						
SIIA12550	Sec III A - roadwork and utilities section 2 carriageway - Utilities: HEC along carriageway & Crossroad duct (HEC & HGC)	28	25-Nov-17	29-Dec-17						
SIIA12510	Sec III A - roadwork and utilities section 2 carriageway - gully pipe (L1801 - L1806)	25	14-Oct-17	13-Nov-17						
Roadwork & Utilities - Section 3 (L1808 - L1102)										
SIIA12810	Sec III A - roadwork and utilities section 3 carriageway - black top	7	23-Dec-17	03-Jan-18						
SIIA12770	Sec III A - roadwork and utilities section 3 carriageway - utilities: HEC & crossroad duct (PCCW & HGC)	41	13-Oct-17	30-Nov-17						
SIIA12790	Sec III A - roadwork and utilities section 3 carriageway - road kerb & formation	19	01-Dec-17	22-Dec-17						
Roadwork & Utilities - Section 4 (L1406 - L1401)										
SIIA13010	Sec III A - roadwork and utilities section 4 carriageway - road formation: crossroad duct (HEC), road kerb & formation	24	20-Oct-17	17-Nov-17						
SIIA13030	Sec III A - roadwork and utilities section 4 carriageway - black top	7	18-Nov-17	25-Nov-17						
SIIA12990	Sec III A - roadwork and utilities section 4 carriageway - watermain	10	09-Oct-17	19-Oct-17						

Data Date:
30-Jun-17

- Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Remaining Level of Effort

3 Months Rolling Programme for Non-CR III Area (Oct 2017 - Dec 2017)
(Ref. to Works Programme Rev.11.1)

Date	Revision	Checked	Approved
03-Oct-17	11.1		



Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2017			2018
					Oct	Nov	Dec	Jan
Roadwork & Utilities - Section 6 (L1102 - L1411)								
SIIIA13389	Sec III A - roadwork and utilities section 6 carriageway - Backfilling above tunnel roof slab	5	05-Oct-17	10-Oct-17	█			
SIIIA13399	Sec III A - roadwork and utilities section 6 carriageway - gully pipe (L1101 -L1102)	8	21-Oct-17	31-Oct-17		█		
SIIIA13470	Sec III A - roadwork and utilities section 6 carriageway - black top	7	22-Nov-17	29-Nov-17			█	
SIIIA13450	Sec III A - roadwork and utilities section 6 carriageway - road kerb & formation	18	01-Nov-17	21-Nov-17		█		
SIIIA13395	Sec III A - roadwork and utilities section 6 carriageway - Drainage works (L1101-L1102)	9	11-Oct-17	20-Oct-17	█			
Section V - Remaining At-Grade Road; Remove 2nd Stage ITA								
Roadwork & Utilities								
Section 1 (L1504 - L1900)								
SV12460	Sec V - Roadwork & Utilities Section 1 Carriageway - Utilities (TCS crossroad duct)	21	11-Oct-17	04-Nov-17	█			
SV12570	Sec V - Roadwork & Utilities Section 1 footpath - utilities:TCS	30	22-Nov-17	28-Dec-17			█	
SV12540	Sec V - Roadwork & Utilities Section 1 footpath - Watermain	14	06-Nov-17	21-Nov-17		█		
SV12580	Sec V - Roadwork & Utilities Section 1 footpath - paving block	30	29-Dec-17	02-Feb-18				█
SV12490	Sec V - Roadwork & Utilities Section 1 Carriageway - Road kerb & formation	24	06-Nov-17	02-Dec-17		█		
SV12520	Sec V - Roadwork & Utilities Section 1 Carriageway - Black top	20	04-Dec-17	28-Dec-17			█	
Section 2 (L1510 - L1504)								
SV12604	Sec V - Roadwork & Utilities Section 2 Carriageway : formation for access diversion	6	30-Sep-17	07-Oct-17	█			
SV12606	Sec V - Roadwork & Utilities Section 2 Carriageway: Divert access cross Zone B	0	09-Oct-17					
SV12630	Sec V - Roadwork & Utilities Section 2 Carriageway - Drainage Works L1406A - L1406B	21	15-Nov-17	08-Dec-17		█		
SV12690	Sec V - Roadwork & Utilities Section 2 footpath - Drainage Works (L2104 - L2105)	25	09-Dec-17	10-Jan-18			█	
SV12610	Sec V - Roadwork & Utilities Section 2 Carriageway - Drainage Works L1507-L1504)	31	09-Oct-17	14-Nov-17	█			
SV12665	Sec V - Roadwork & Utilities Section 2 Carriageway - Gully pipe (L1507-L1504, L1406A)	25	09-Dec-17	10-Jan-18			█	
Section 3 (Culvert L - L1510)								
SIV12844	Sec V - Roadwork & Utilities Section 3 footpath - U channel	21	15-Nov-17	08-Dec-17		█		
SIV12840	Sec V - Roadwork & Utilities footpath - Drainage works (Culvert L - L2105)	25	16-Oct-17	14-Nov-17	█			
SIV12860	Sec V - Roadwork & Utilities Section 3 footpath - Utilities: TCS, HGC, PCCW)	39	09-Dec-17	26-Jan-18			█	
SIV12820	Sec V - Roadwork & Utilities Section 3 Carriageway - Black top	20	19-Dec-17	13-Jan-18			█	
SIV12810	Sec V - Roadwork & Utilities Section 3 Carriageway - Gully pipe (Culvert L - L1611)	30	16-Oct-17	20-Nov-17	█			
SIV12850	Sec V - Roadwork & Utilities footpath - Watermain	21	15-Nov-17	08-Dec-17		█		
SIV12815	Sec V - Roadwork & Utilities Section 3 Carriageway - Road kerb & formation	24	21-Nov-17	18-Dec-17			█	
Section IV - Slip Road 3								
Roadwork & Utilities								
Section 1 (L16608 - L1601)								
SIV11762	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Drainage Works (L2103-L2101)	21	03-Nov-17	27-Nov-17		█		
SIV11780	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Watermain	18	29-Dec-17	19-Jan-18			█	
SIV11764	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Gully pipe (L1607-L1601, L2004-L2005)	25	28-Nov-17	28-Dec-17			█	
SIV11860	Sec IV - Roadwork & Utilities at SR3 Section 1 footpath - Drainage Works: future connection pipes	7	29-Dec-17	06-Jan-18			█	
Section 2 (L2301 - L2103)								
SIV11941	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Drainage Works (L608-L1609)	30	19-Oct-17	23-Nov-17	█			
SIV11960	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Watermain	10	20-Dec-17	03-Jan-18			█	



Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2017				2018
					Oct	Nov	Dec	Jan	
SIV11942	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Gully pipe (L2301-L2013, L1608-L1609)	22	24-Nov-17	19-Dec-17					
SIV12010	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Road kerb & formation	24	20-Dec-17	19-Jan-18					
Section 3 (M/H1.6 - L2301)									
SIV12103	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - M1.7-M1.6: ELS	10	18-Oct-17	30-Oct-17					
SIV12104	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - M1.7-M1.6: Construct manhole & pipes	36	31-Oct-17	11-Dec-17					
SIV12105	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - M1.7-M1.6: backfilling & divert EVA	12	12-Dec-17	27-Dec-17					
SIV12120	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Drainage Works (M1.6-C1.1-C1.2): Construct MH and pipes	28	28-Dec-17	30-Jan-18					
SIV12100	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Drainage Works (M/H1.7 - L2301)	31	19-Oct-17	24-Nov-17					
SIV12140	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Gully pipe (M/H 1.7 - L2301)	30	25-Nov-17	02-Jan-18					
SIV12180	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - U channel	14	24-Oct-17	09-Nov-17					
SIV12220	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - Paving block	45	10-Nov-17	04-Jan-18					
Section VII - Remainder Works									
Road & Drainage Works (Culvert L - M/H1.7, Adjacent to SR3)									
SVII11600	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - Drainage Works (Culvert L -MH1.7)	40	12-Dec-17	30-Jan-18					
Retaining Wall RW5 Construction									
SVII10860	Sec VII - Retaining wall RW5 - curing, removal formwork	15	07-Nov-17	23-Nov-17					
SVII10680	Sec VII - Retaining wall RW5 (bay 2) - construct base slab and wall	20	13-Oct-17	06-Nov-17					
SVII10820	Sec VII - Retaining wall RW5 (bay 4) - construct base slab and wall	20	13-Oct-17	06-Nov-17					
Landing Steps Construction									
Landing Steps BSW13									
SVII10920	Sec VII - Landing steps (BSW13) - install s.s. handrail / tactile / sign board / bollard	25	20-Nov-17	18-Dec-17					
SVII10900	Sec VII - Landing steps (BSW13) - install vertical fender / step fender	15	02-Nov-17	18-Nov-17					
Landing Steps BSW4									
SVII10980	Sec VII - Landing steps (BSW4) - install vertical fender / step fender	15	19-Dec-17	08-Jan-18					
Promenade Seawall Parapet Construction									
SVII13220	Sec VII - Zone D: Construct seawall block mass concrete coping	40	04-Dec-17	22-Jan-18					
SVII13140	Sec VII - Zone A1, A2 & B: Construct seawall parapet	35	02-Nov-17	12-Dec-17					
Promenade Footpath and EVA Construction									
Section 2									
SVII12610	Sec VII - section 2 footpath - drainage works (L2203 - L2202A) & U-channel	49	14-Nov-17	12-Jan-18					
Section 3									
SVII12850	Sec VII - section 3 footpath - watermain	18	13-Oct-17	03-Nov-17					
SVII12870	Sec VII - section 3 footpath - utilities (HEC, TCSS, HGC, PCCW)	44	04-Nov-17	27-Dec-17					
SVII12875	Sec VII - 3 footpath - drainage works :U chanel	14	28-Dec-17	13-Jan-18					
Section 4									
SVII13054	Sec VII - section 4 footpath - U channel	14	09-Dec-17	27-Dec-17					
SVII13052	Sec VII - section 4 footpath - watermain	21	15-Nov-17	08-Dec-17					
SVII13050	Sec VII - section 4 footpath - drainage works (L2203 -L2203A)	21	20-Oct-17	14-Nov-17					
SVII13055	Sec VII - section 4 footpath - utilities: HEC, TCSS, HEC & PCCW	56	09-Dec-17	15-Feb-18					
Section 5									



Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2017				2018
					Oct	Nov	Dec	Jan	
SVII13275	Sec VII - section 5 footpath - watermain	21	26-Oct-17	20-Nov-17					
SVII13310	Sec VII - section 5 footpath - utilities: HEC, TCSS, HGC, PCCW	59	21-Nov-17	31-Jan-18					
Section 6									
SVII13514	Sec VII - section 6 footpath - U channel	20	14-Dec-17	09-Jan-18					
SVII13510	Sec VII - section 6 footpath - watermain	20	21-Nov-17	13-Dec-17					
SVII13490	Sec VII - section 6 footpath - drainage works(Culvert L - L2204)	25	21-Oct-17	20-Nov-17					
SVII13530	Sec VII - section 6 footpath - utilities: HEC, TCSS, HGC, PCCW	62	14-Dec-17	02-Mar-18					

China State Construction Engineering (Hong Kong) Ltd.

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay)



Activity Name	Start	Finish	2017		
			Jul	Aug	Sep
Hung Hing Road Resurfacing	1/6/2017	30/9/2017			
Defect works inside tunnel	1/4/2017	30/9/2017			

Data Date: 20-Oct-17

HY/2009/18 Central - Wan Chai Bypass (Central Interchange)

TASK filters: 3 Months_1, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017				2018
						Oct	Nov	Dec	Jan	
Update 2017-10-20 CWB - Central Interchange (2014-06-20) Revised DWP R7										
PRELIMINARIES										
Access Dates & Milestones										
Commencement & Completion										
1010	Contract DLP and Establishment Works for Landscape Completion	0		20-Oct-17*	-263					
1005	Contract Construction Completion	0		20-Oct-17*	-628					
SECTION 6 - ALL WORKS IN PORTION VI										
General Surface Works										
Formation & Roadworks										
Roadworks										
VO150	VO150 (Dated 03 Jul 2015) - Replacement of Damaged Lattice	18	02-Oct-17 A	19-Oct-17 A						
Finishes & Landscaping										
14948	Area 4	12	09-Nov-16 A	18-Oct-17 A						
SECTION 7, 7A, 7B & 7C - LANDSCAPE ESTABLISHMENT										
4040	EST - Portion VI Landscape Establishment	365	19-Oct-17 A	18-Oct-18	-627					
SECTION 8 - PRESERVATION & PROTECTION OF TREES										
4100	Tree - Preservation & Protection of Existing Trees	1759	14-Dec-10 A	20-Oct-17	-628					
Key Dates for Completion of Sections										
Anticipated Completion										
1094	KD12 - Anticipated Completion	0		20-Oct-17*	-716					
1114	KD10 - Anticipated Completion	0		20-Oct-17*	-628					
1124	KD11 - Anticipated Completion	0		20-Oct-17*	-621					
1139	KD16 - Anticipated Completion	0		20-Oct-17*	-628					
1104	KD14 - Anticipated Completion	0		11-Jan-18*	-800					

-  Current Milestone
-  Level of Effort
-  Baseline Milestone
-  Actual Work
-  Critical Remaining Work
-  Remaining W...
-  Project Baseli...

Leighton Contractors (Asia) Limited Programme Update 85 (October 2017) THREE MONTH ROLLING

Project ID: U085
Baseline: DCP7-2c
Layout: Update Three Month Rolling
U085
Page 1 of 2








Date	Revision	Checked	Appro...
20-Sep-17	U084	AT	PT
20-Oct-17	U085	AT	PT

Data Date: 20-Oct-17

HY/2009/18 Central - Wan Chai Bypass (Central Interchange)

TASK filters: 3 Months_1, Not HL.


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017												2018	
						Oct				Nov				Dec				Jan	
Portion Handover Dates																			
Anticipated Handover																			
2960a	Portion IIIA Handover - Remaining (KD3 + 28 days) - (EOT 26.5 days added)	0		20-Oct-17*	-931														

-  Current Milestone
-  Level of Effort
-  Baseline Milestone
-  Actual Work
-  Critical Remaining Work
-  Remaining W...
-  Project Baseli...

Leighton Contractors (Asia) Limited Programme Update 85 (October 2017) THREE MONTH ROLLING

Project ID: U085
 Baseline: DCP7-2c
 Layout: Update Three Month Rolling
 U085
 Page 2 of 2

Date	Revision	Checked	Appro...
20-Sep-17	U084	AT	PT
20-Oct-17	U085	AT	PT

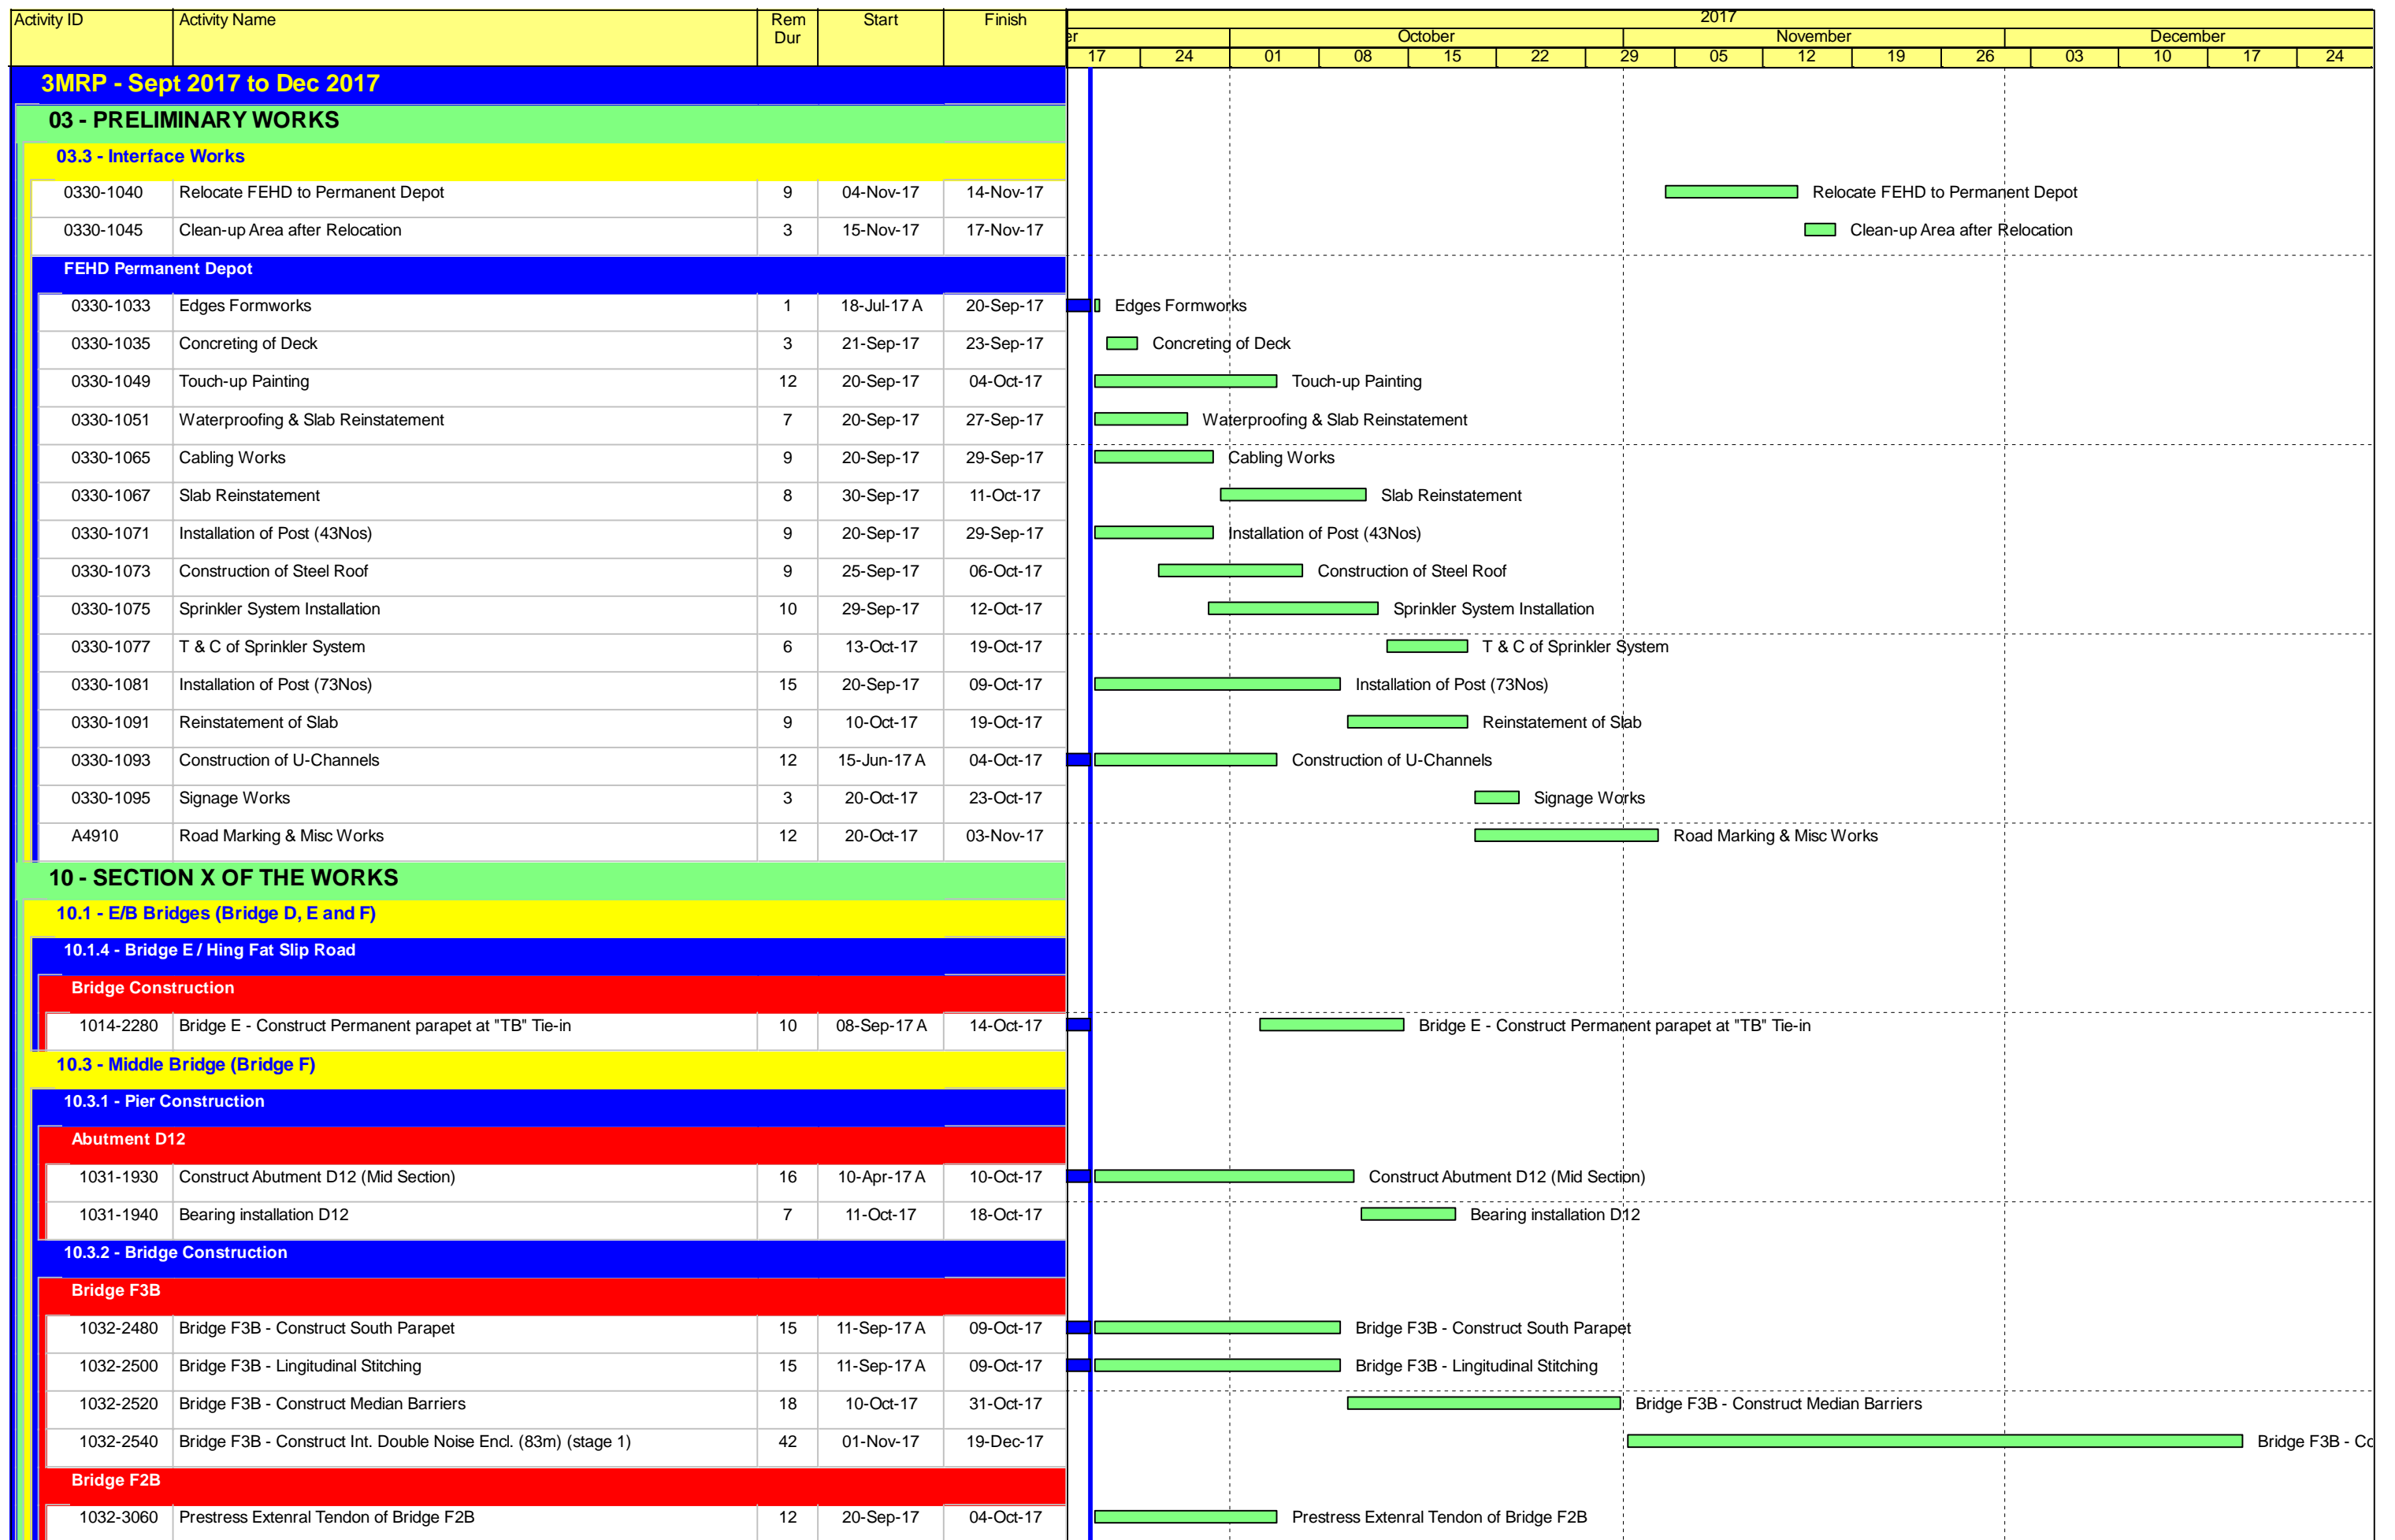

Remaining Level of Effort Remaining Work
 Actual Level of Effort Critical Remaining Work
 Actual Work Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Sept.2017 to 19.Dec.2017)

Activity ID	Activity Name	Rem Dur	Start	Finish	2017													
					October					November				December				
					17	24	01	08	15	22	29	05	12	19	26	03	10	17
1032-3080	Bridge F2B - Longitudinal Stitching	12	06-Oct-17	19-Oct-17	Bridge F2B - Longitudinal Stitching													
1032-3100	Bridge F2B - Construct Median Barriers	18	20-Oct-17	10-Nov-17	Bridge F2B - Construct Median Barriers													
1032-3120	Bridge F2B - Construct Int. Double Noise Encl.	36	11-Nov-17	22-Dec-17	Bridge F2B - Construct Int. Double Noise Encl.													
Bridge F1B2																		
1032-1000	Relignment LG - A for Launching at Bridge F1B2	4	20-Sep-17	23-Sep-17	Relignment LG - A for Launching at Bridge F1B2													
1032-3160	P38/F4B - Install Pier Segment - Place Pier Segment	1	25-Sep-17	25-Sep-17	P38/F4B - Install Pier Segment - Place Pier Segment													
1032-3180	P38/F4B - Install Pier Segment - Adjust Segment Level and Location	2	26-Sep-17	27-Sep-17	P38/F4B - Install Pier Segment - Adjust Segment Level and Location													
1032-3200	P38/F4B - Install Pier Segment - Grouting the Bearing Upper Plinth	3	28-Sep-17	30-Sep-17	P38/F4B - Install Pier Segment - Grouting the Bearing Upper Plinth													
1032-3220	P38/F4B - Install Pier Segment - Stressing Nailing	2	03-Oct-17	04-Oct-17	P38/F4B - Install Pier Segment - Stressing Nailing													
1032-3240	P38/F4B - Install MS at Pier 38 and Engage FL at P37/F2B	2	06-Oct-17	07-Oct-17	P38/F4B - Install MS at Pier 38 and Engage FL at P37/F2B													
1032-3260	P37/F2B - Install Pier Segment - Place Pier Segment	1	09-Oct-17	09-Oct-17	P37/F2B - Install Pier Segment - Place Pier Segment													
1032-3280	P37/F2B - Install Pier Segment - Adjust Segment Level and Location	2	10-Oct-17	11-Oct-17	P37/F2B - Install Pier Segment - Adjust Segment Level and Location													
1032-3300	P37/F2B - Install Pier Segment - Grouting the Bearing Upper Plinth	3	12-Oct-17	14-Oct-17	P37/F2B - Install Pier Segment - Grouting the Bearing Upper Plinth													
1032-3320	P37/F2B - Install Pier Segment - Stressing Nailing	2	16-Oct-17	17-Oct-17	P37/F2B - Install Pier Segment - Stressing Nailing													
1032-3340	P37/F2B - Install MS at F1B2/Pier37 and Engage FL at F1B/Pier36	2	18-Oct-17	19-Oct-17	P37/F2B - Install MS at F1B2/Pier37 and Engage FL at F1B/Pier36													
1032-3360	P37/F2B - T Span Erection (5 pairs)	4	20-Oct-17	24-Oct-17	P37/F2B - T Span Erection (5 pairs)													
1032-3380	P38/F4B(MJ Left) - End Span Erection - Hanging Segments	3	25-Oct-17	27-Oct-17	P38/F4B(MJ Left) - End Span Erection - Hanging Segments													
1032-3400	P38/F4B(MJ Left) - End Span Erection - Erect Segments	1	30-Oct-17	30-Oct-17	P38/F4B(MJ Left) - End Span Erection - Erect Segments													
1032-3420	P38/F4B(MJ Left) - End Span Erection - Stitching	2	31-Oct-17	01-Nov-17	P38/F4B(MJ Left) - End Span Erection - Stitching													
1032-3440	P38/F4B(MJ Left) - End Span Erection - Formwork Fixing for and Grouting for Bearing	2	31-Oct-17	01-Nov-17	P38/F4B(MJ Left) - End Span Erection - Formwork Fixing for and Grouting for Bearing													
1032-3460	P38/F4B(MJ Left) - End Span Erection - Prestress Span Tendons	2	02-Nov-17	03-Nov-17	P38/F4B(MJ Left) - End Span Erection - Prestress Span Tendons													
1032-3480	P38/F4B(MJ Left) - End Span Erection - Remove Hanger Bar & Hanger Beam & Stitching Formwork	1	04-Nov-17	04-Nov-17	P38/F4B(MJ Left) - End Span Erection - Remove Hanger Bar & Hanger Beam & Stitching Formwork													
1032-3500	P36/F1B - Install Pier Segment - Place Pier Segment	1	23-Oct-17	23-Oct-17	P36/F1B - Install Pier Segment - Place Pier Segment													
1032-3520	P36/F1B - Install Pier Segment - Adjust Segment Level and Location	2	24-Oct-17	25-Oct-17	P36/F1B - Install Pier Segment - Adjust Segment Level and Location													
1032-3540	P36/F1B - Install Pier Segment - Grouting the Bearing Upper Plinth	3	26-Oct-17	30-Oct-17	P36/F1B - Install Pier Segment - Grouting the Bearing Upper Plinth													
1032-3560	P36/F1B - Install Pier Segment - Stressing Nailing	2	31-Oct-17	01-Nov-17	P36/F1B - Install Pier Segment - Stressing Nailing													
1032-3580	P36/F1B - Install MS at F1B/Pier36 and Engage FL at D12	2	02-Nov-17	03-Nov-17	P36/F1B - Install MS at F1B/Pier36 and Engage FL at D12													
1032-3600	P36/F1B - T Span Erection (6 pairs)	4	06-Nov-17	09-Nov-17	P36/F1B - T Span Erection (6 pairs)													
1032-3620	Abut. D12 - Install Pier Segment - Place Pier Segment	2	10-Nov-17	11-Nov-17	Abut. D12 - Install Pier Segment - Place Pier Segment													
1032-3640	Abut. D12 - Install Pier Segment - Adjust Segment Level and Location	3	13-Nov-17	15-Nov-17	Abut. D12 - Install Pier Segment - Adjust Segment Level and Location													
1032-3660	Abut. D12 - Install Pier Segment - Install the Tie & Packing System	2	16-Nov-17	17-Nov-17	Abut. D12 - Install Pier Segment - Install the Tie & Packing System													
1032-3680	Abut. D12 - Install MS at D12	1	18-Nov-17	18-Nov-17	Abut. D12 - Install MS at D12													
1032-3700	Abut. D12 (MJ Right) - End Span Erection - Hanging Segments	3	20-Nov-17	22-Nov-17	Abut. D12 (MJ Right) - End Span Erection - Hanging Segments													
1032-3720	Abut. D12 (MJ Right) - End Span Erection - Erect Segments	1	23-Nov-17	23-Nov-17	Abut. D12 (MJ Right) - End Span Erection - Erect Segments													
1032-3740	Abut. D12 (MJ Right) - End Span Erection - Stitching	2	24-Nov-17	25-Nov-17	Abut. D12 (MJ Right) - End Span Erection - Stitching													
1032-3760	Abut. D12 (MJ Right) - End Span Erection - Formwork Fixing for and Grouting for Bearing	2	24-Nov-17	25-Nov-17	Abut. D12 (MJ Right) - End Span Erection - Formwork Fixing for and Grouting for Bearing													
1032-3780	Abut. D12 (MJ Right) - End Span Erection - Prestress Span Tendons	2	27-Nov-17	28-Nov-17	Abut. D12 (MJ Right) - End Span Erection - Prestress Span Tendons													
1032-3800	Abut. D12 (MJ Right) - End Span Erection - Remove Hanger Bar & Hanger Beam & Stitching Formwork	1	29-Nov-17	29-Nov-17	Abut. D12 (MJ Right) - End Span Erection - Remove Hanger Bar & Hanger Beam & Stitching Formwork													
1032-3820	Prestress External Tendon of Bridge F1B2	13	30-Nov-17	14-Dec-17	Prestress External Tendon of Bridge F1B2													

Remaining Level of Effort Remaining Work
 Actual Level of Effort Critical Remaining Work
 Actual Work Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Sept.2017 to 19.Dec.2017)

Activity ID	Activity Name	Rem Dur	Start	Finish	2017															
					October						November				December					
					17	24	01	08	15	22	29	05	12	19	26	03	10	17	24	
Bridge F1B1																				
1032-1400	P37/F2A - Install Pier Segment - Grouting the Bearing Upper Plinth	1	20-Sep-17	20-Sep-17	P37/F2A - Install Pier Segment - Grouting the Bearing Upper Plinth															
1032-1420	P37/F2A - Install Pier Segment - Stressing Nailing	2	21-Sep-17	22-Sep-17	P37/F2A - Install Pier Segment - Stressing Nailing															
1032-1440	P37/F2A - Install MS at F1B2/Pier37 and Engage RL at F1B/Pier36	1	23-Sep-17	23-Sep-17	P37/F2A - Install MS at F1B2/Pier37 and Engage RL at F1B/Pier36															
1032-1460	P37/F2A - T Span Erection (5 pairs)	3	25-Sep-17	27-Sep-17	P37/F2A - T Span Erection (5 pairs)															
1032-1480	P37/F2A-P36/F1A - Mid-span Stitching	2	28-Sep-17	29-Sep-17	P37/F2A-P36/F1A - Mid-span Stitching															
1032-1500	P37/F2A-P36/F1A - Prestress Span Tendons	3	30-Sep-17	04-Oct-17	P37/F2A-P36/F1A - Prestress Span Tendons															
1032-1520	P38/F3A - Install Pier Segment - Place Pier Segment	1	06-Nov-17	06-Nov-17	P38/F3A - Install Pier Segment - Place Pier Segment															
1032-1540	P38/F3A - Install Pier Segment - Adjust Segment Level and Location	2	07-Nov-17	08-Nov-17	P38/F3A - Install Pier Segment - Adjust Segment Level and Location															
1032-1560	P38/F3A - Install Pier Segment - Grouting the Bearing Upper Plinth	2	09-Nov-17	10-Nov-17	P38/F3A - Install Pier Segment - Grouting the Bearing Upper Plinth															
1032-1580	P38/F3A - Install Pier Segment - Stressing Nailing	1	11-Nov-17	11-Nov-17	P38/F3A - Install Pier Segment - Stressing Nailing															
1032-1600	P38/F3A - Install MS at Pier 38 and Engage FL at P37/F2A	2	13-Nov-17	14-Nov-17	P38/F3A - Install MS at Pier 38 and Engage FL at P37/F2A															
1032-1620	P38/F3A(MJ Left) - End Span Erection - Hanging Segments	1	15-Nov-17	15-Nov-17	P38/F3A(MJ Left) - End Span Erection - Hanging Segments															
1032-1640	P38/F3A(MJ Left) - End Span Erection - Erect Segments	2	15-Nov-17	16-Nov-17	P38/F3A(MJ Left) - End Span Erection - Erect Segments															
1032-1660	P38/F3A(MJ Left) - End Span Erection - Stitching	1	17-Nov-17	17-Nov-17	P38/F3A(MJ Left) - End Span Erection - Stitching															
1032-1680	P38/F3A(MJ Left) - End Span Erection - Formwork Fixing for and Grouting for Bearing	1	18-Nov-17	18-Nov-17	P38/F3A(MJ Left) - End Span Erection - Formwork Fixing for and Grouting for Bearing															
1032-1683	P38/F3A(MJ Left) - End Span Erection - Prestress Span Tendons	2	20-Nov-17	21-Nov-17	P38/F3A(MJ Left) - End Span Erection - Prestress Span Tendons															
1032-1685	P38/F3A(MJ Left) - End Span Erection - Remove Hanger Bar & Hanger Beam & Stitching Formwork	1	22-Nov-17	22-Nov-17	P38/F3A(MJ Left) - End Span Erection - Remove Hanger Bar & Hanger Beam & Stitching Formwork															
1032-1700	Dismantle LG1 and Cart away	14	23-Nov-17	08-Dec-17	Dismantle LG1 and Cart away															
1032-1720	Prestress External Tendon of Bridge F1B2	12	02-Dec-17	15-Dec-17	Prestress External Tendon of Bridge F1B2															
Bridge F5																				
1032-3960	Bridge F5 Median Barriers	26	23-Aug-17 A	21-Oct-17	Bridge F5 Median Barriers															
All Middle Bridge F (Common)																				
1032-4350	TCSS/LV Ducts at Pier 50-51	14	20-Sep-17	07-Oct-17	TCSS/LV Ducts at Pier 50-51															
1032-4353	TCSS/LV Ducts at Pier 51-52	14	09-Oct-17	24-Oct-17	TCSS/LV Ducts at Pier 51-52															
1032-4354	TCSS/LV Ducts at Pier 52-53	14	25-Oct-17	10-Nov-17	TCSS/LV Ducts at Pier 52-53															
1032-4355	TCSS/LV Ducts at Pier 53-54	14	11-Nov-17	27-Nov-17	TCSS/LV Ducts at Pier 53-54															
1032-4356	TCSS/LV Ducts at Pier 55-56	14	28-Nov-17	13-Dec-17	TCSS/LV Ducts at Pier 55-56															
10.4 - Bridge Deck Demolition																				
10.4.3 - Existing E/B Bridge																				
10412-1730	Demolish Dolphin+Pile Cap & Reconstruct Pier 32 Pile Cap	18	12-Jul-17 A	12-Oct-17	Demolish Dolphin+Pile Cap & Reconstruct Pier 32 Pile Cap															
10.6 - Tunnel Approach Ramp																				
10.6.1 - Approach Ramp (Excluding Portion IIB)																				
Piling Works																				
1061-3840	Pre Bored H-Pile > Pile Ramp - BN11 A - (H-Pile + Grouting)	1	20-Sep-17	20-Sep-17	Pre Bored H-Pile > Pile Ramp - BN11 A - (H-Pile + Grouting)															
1061-3860	Pre Bored H-Pile > Pile Ramp - BN11 B (LHR)	7	20-Sep-17	27-Sep-17	Pre Bored H-Pile > Pile Ramp - BN11 B (LHR)															
1061-3880	Pre Bored H-Pile > Pile Ramp - BN11 B - (H-Pile + Grouting)	1	28-Sep-17	28-Sep-17	Pre Bored H-Pile > Pile Ramp - BN11 B - (H-Pile + Grouting)															
1061-3900	Pre Bored H-Pile > Pile Ramp - BN12 A (LHR)	5	17-Aug-17 A	04-Oct-17	Pre Bored H-Pile > Pile Ramp - BN12 A (LHR)															
1061-3920	Pre Bored H-Pile > Pile Ramp - BN12 A - (H-Pile + Grouting)	1	06-Oct-17	06-Oct-17	Pre Bored H-Pile > Pile Ramp - BN12 A - (H-Pile + Grouting)															

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Sept.2017 to 19.Dec.2017)

Activity ID	Activity Name	Rem Dur	Start	Finish	2017																
					September					October					November					December	
					17	24	01	08	15	22	29	05	12	19	26	03	10	17	24		
1061-3960	Pre Bored H-Pile > Pile Ramp - BN12 B - (H-Pile + Grouting)	1	06-Oct-17	06-Oct-17				█													
1061-4000	Pre Bored H-Pile > Pile Ramp - BN13 A - (H-Pile + Grouting)	1	06-Oct-17	06-Oct-17				█													
1061-4120	Pre Bored H-Pile > Pile Ramp - BN01 B - (H-Pile + Grouting)	1	20-Sep-17	20-Sep-17				█													
1061-4240	Pre Bored H-Pile > Pile Ramp - BN06 A - (H-Pile + Grouting)	1	20-Sep-17	20-Sep-17				█													
Excavation & ELS Works																					
1061-5220	Ch 5234 - 5285 > Install 2nd Layer of Strut & Waling	1	17-Aug-17 A	20-Sep-17				█													
1061-5240	Ch 5234 - 5285 > Excav to FEL	9	11-Sep-17 A	30-Sep-17				█													
Structure Works																					
1061-5560	Bay 6 - Ch 5262 - 5277 > Base Slab - Blinding Layer	1	03-Oct-17	03-Oct-17				█													
1061-5580	Bay 6 - Ch 5262 - 5277 > Base Slab - Water Proofing Membrane	2	04-Oct-17	06-Oct-17				█													
1061-5600	Bay 6 - Ch 5262 - 5277 > Base Slab - Rebar Fixing	6	07-Oct-17	13-Oct-17				█													
1061-5620	Bay 6 - Ch 5262 - 5277 > Base Slab - Erect Formworks	4	14-Oct-17	18-Oct-17				█													
1061-5640	Bay 6 - Ch 5262 - 5277 > Base Slab - Concreting	1	19-Oct-17	19-Oct-17				█													
1061-5860	Bay 7 - Ch 5247 - 5262 > Base Slab - Blinding Layer (WF2)	1	20-Oct-17	20-Oct-17				█													
1061-5880	Bay 7 - Ch 5247 - 5262 > Base Slab - Base Slab - Water Proofing Membrane	3	21-Oct-17	24-Oct-17				█													
1061-5900	Bay 7 - Ch 5247 - 5262 > Base Slab - Rebar Fixing (WF2)	6	25-Oct-17	01-Nov-17				█													
1061-5920	Bay 7 - Ch 5247 - 5262 > Base Slab - Erect Formworks (WF2)	3	02-Nov-17	04-Nov-17				█													
1061-5940	Bay 7 - Ch 5247 - 5262 > Base Slab - Concreting (WF2)	1	06-Nov-17	06-Nov-17				█													
1061-5960	Bay 8- Ch 5232 - 5247 > Base Slab - Blinding Layer (WF2)	1	07-Nov-17	07-Nov-17				█													
1061-5980	Bay 8- Ch 5232 - 5247 > Base Slab - Base Slab - Water Proofing Membrane	3	08-Nov-17	10-Nov-17				█													
1061-6000	Bay 8- Ch 5232 - 5247 > Base Slab - Rebar Fixing (WF2)	5	11-Nov-17	16-Nov-17				█													
1061-6020	Bay 8- Ch 5232 - 5247 > Base Slab - Erect Formworks (WF2)	3	17-Nov-17	20-Nov-17				█													
1061-6040	Bay 8- Ch 5232 - 5247 > Base Slab - Concreting (WF2)	1	21-Nov-17	21-Nov-17				█													
1061-6060	Bay 5 & 6 > Side Wall - Lower Portion - Install Waterproofing Membrane	1	20-Oct-17	20-Oct-17				█													
1061-6080	Bay 5 & 6 > Side Wall - Lower Portion - Rebar Fixing	2	21-Oct-17	23-Oct-17				█													
1061-6100	Bay 5 & 6 > Side Wall - Lower Portion - Erect Formworks	2	24-Oct-17	25-Oct-17				█													
1061-6120	Bay 5 & 6 > Side Wall - Lower Portion - Concreting	1	26-Oct-17	26-Oct-17				█													
1061-6140	Bay 5 & 6 > Side Wall - Lower Portion - Backfill Behind Side Wall	3	27-Oct-17	31-Oct-17				█													
1061-6160	Bay 5 & 6 > Side Wall - Lower Portion - Cast Temp Concrete Slab (3days curing)	4	01-Nov-17	04-Nov-17				█													
1061-6180	Bay 5 & 6 > Side Wall - Lower Portion - Remove 1st & 2nd Struts & Waling	6	06-Nov-17	11-Nov-17				█													
1061-6200	Bay 5 & 6 > Side Wall - Upper Portion - Erect Scaffolding & Working Platform	4	13-Nov-17	16-Nov-17				█													
1061-6220	Bay 5 & 6 > Side Wall - Upper Portion - Erect Formwork (one side)	6	17-Nov-17	23-Nov-17				█													
1061-6240	Bay 5 & 6 > Side Wall - Upper Portion - Install Waterproofing Membrane	3	24-Nov-17	27-Nov-17				█													
1061-6260	Bay 5 & 6 > Side Wall - Upper Portion - Rebar Fixing	5	28-Nov-17	02-Dec-17				█													
1061-6280	Bay 5 & 6 > Side Wall - Upper Portion - Complete Formworks	4	04-Dec-17	07-Dec-17				█													
1061-6300	Bay 5 & 6 > Side Wall - Upper Portion - Concreting	1	08-Dec-17	08-Dec-17				█													
1061-6320	Bay 4 > Side Wall - Full Height - Erect Scaffolding & Working Platform	3	10-Oct-17	12-Oct-17				█													
1061-6340	Bay 4 > Side Wall - Full Height - Erect Formwork (one side)	3	13-Oct-17	16-Oct-17				█													
1061-6360	Bay 4 > Side Wall - Full Height - Install Waterproofing Membrane	2	17-Oct-17	18-Oct-17				█													

Remaining Level of Effort Remaining Work
 Actual Level of Effort Critical Remaining Work
 Actual Work ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Sept.2017 to 19.Dec.2017)

Activity ID	Activity Name	Original Duration	Start	Finish	2017												2018
					Oct			Nov			Dec			Jan			
Total		306d	15-May-17 A	16-Mar-18													
3 Months Rolling Programme - 2017-09 (DWP-08, 1st submission)		306d	15-May-17 A	16-Mar-18													
Removal of TS3 South side		306d	15-May-17 A	16-Mar-18													
South West (Zone A)		78d	17-May-17 A	16-Sep-17 A													
1	South West (Zone A)	66d	17-May-17 A	16-Sep-17 A	South West (Zone A)												
2	Remove filled material to -4.35mPD (13,000m3)	13d	17-May-17 A	01-Jun-17 A													
3	Remove seawall blocks at Bay Z4- 22 - 22 (400 nos.)	6d	19-May-17 A	26-May-17 A													
5	Core D-wall cut holes at Panel W2D5 to W2D8	6d	27-Jun-17 A	02-Jul-17 A													
6	Remove filled material to -7.0mPD up to Panel W2D8	7d	03-Jul-17 A	14-Jul-17 A													
4	Remove seawall blocks at Bay 23 & 24 (120 nos.)	2d	11-Aug-17 A	15-Aug-17 A													
54	Remove Outfall Q Sheet Piles Wall	14d	18-Aug-17 A	16-Sep-17 A	Remove Outfall Q Sheet Piles Wall												
Portion SW1		15d	12-Jun-17 A	14-Jul-17 A													
7	Vertical cut at Panel BWD14 to SA7 (25 nos./1.5m)	8d	12-Jun-17 A	30-Jun-17 A													
8	Horizontal cut at Panel BWD14 to SA7 (34 nos./1.5m)	9d	29-Jun-17 A	14-Jul-17 A													
Portion SW2		18d	19-Jul-17 A	04-Aug-17 A													
59	Vertical cut at Panel W2D1 to W2D9 (24 nos./1.5m)	9d	19-Jul-17 A	27-Jul-17 A													
69	Horizontal cut at Panel W2D1 to W2D9 (32 nos./1.5m)	9d	28-Jul-17 A	04-Aug-17 A													
South West (Zone B)		34d	22-Jun-17 A	25-Jul-17 A													
10	Excavation to Expose Existing Landing Steps	6d	22-Jun-17 A	27-Jun-17 A													
11	Excavation to Expose Existing Intake of Windsor House	5d	28-Jun-17 A	02-Jul-17 A													
12	Clear Up for Inspection of Existing Intake of Windsor House	7d	03-Jul-17 A	09-Jul-17 A													
13	Remove Filled Material to -4.35mPD (11,000m3)	18d	03-Jul-17 A	20-Jul-17 A													
14	Remove Filled Material to -7.0mPD	6d	18-Jul-17 A	23-Jul-17 A													
15	Core D-wall Cut Holes at Panel W2D10 to W4D3 (82 nos.)	2d	24-Jul-17 A	25-Jul-17 A													
South East (Zone C)		126d	24-May-17 A	24-Oct-17	South East (Zone C)												
16	South East (Zone C)	105d	24-May-17 A	24-Oct-17	South East (Zone C)												
17	Break concrete slab	2d	24-May-17 A	25-May-17 A													
18	Remove filled material to -4.35mPD (7,000m3)	8d	26-May-17 A	12-Jun-17 A													
19	Remove seawall blocks at Bay 2 - Bay 4 (454 nos.)	7d	13-Jun-17 A	19-Jun-17 A													
Portion SE1		35d	24-Jun-17 A	28-Jul-17 A													
20	Remove filled material to -7.0mPD	7d	24-Jun-17 A	30-Jun-17 A													
21	Clean and Install String for Vertical Cutting	1d	01-Jul-17 A	01-Jul-17 A													
22	Vertical cut at Panel W2D32 to W2D35 (18 nos./1.5m)	7d	02-Jul-17 A	14-Jul-17 A													
23	Horizontal cut at Panel W2D32 to W2D35 (24 nos./1.5m)	12d	17-Jul-17 A	28-Jul-17 A													
Portion SE2		34d	15-Aug-17 A	06-Sep-17 A													
82	Vertical cut at Panel W2D24 to W2D31 (18 nos./1.5m)	10d	15-Aug-17 A	26-Aug-17 A	(18 nos./1.5m)												
83	Horizontal cut at Panel W2D24 to W2D31 (24 nos./1.5m)	8d	03-Sep-17 A	06-Sep-17 A	Panel W2D24 to W2D31 (24 nos./1.5m)												
SR8 (E&W)		75d	11-Aug-17 A	24-Oct-17													
A61270	Vertical cut at W4D7 to W4D11 + W3D5 to W3D7 (24 nos.)	12d	11-Aug-17 A	09-Oct-17	Vertical cut at W4D7 to W4D11 + W3D5 to W3D7 (24 nos.)												
A61230	Vertical cut at W3D2 to W3D4 (9 nos.)	3d	28-Aug-17 A	05-Sep-17 A	to W3D4 (9 nos.)												
A61250	Horizontal cut at W3D2 to W3D4 (12 nos.)	3d	06-Sep-17 A	09-Sep-17 A	at W3D2 to W3D4 (12 nos.)												
A61280	Horizontal cut at W4D7 to W4D11 + W3D5 to W3D7 (32 nos.)	15d	10-Oct-17	24-Oct-17	Horizontal cut at W4D7 to W4D11 + W3D5 to W3D7 (32 nos.)												
SR8 (West Side)		306d	15-May-17 A	16-Mar-18													

 中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

█ Actual Work
█ Remaining Work
█ Critical Remaining Work
◆ Milestone

Page 1 of 4
 Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip Road 8 Section) - 3 Months Rolling Programme

Date	Revision	Checked	Approved
02-Oct-17 08...	DWP-08 (1) - 3 Months Rolling	TL	TL

Activity ID	Activity Name	Original Duration	Start	Finish	2017				2018
					Oct	Nov	Dec	Jan	
C6 Stitching Structure Construction									
120	SR8 - C6 Stitching Structure Construction	188d	15-May-17 A	09-Nov-17	SR8 - C6 Stitching Structure Construction				
Roof slab construction									
C61000	ICE design cert submission for Engineer's consent	9d	15-May-17 A	24-May-17 A					
C61010	Erection of falsework (Revised due to rainstorm and typhoon)	22d	26-May-17 A	20-Jun-17 A					
C61020	Formwork erection and diaphragm wall C.J. and couplers preparation (coring if required)	5d	21-Jun-17 A	25-Jun-17 A					
C61030	Steel fixing for roof slab	8d	26-Jun-17 A	05-Jul-17 A					
C61040	Final cleaning and concreting	1d	06-Jul-17 A	06-Jul-17 A					
C61050	Falsework and formwork removal	6d	17-Jul-17 A	19-Jul-17 A					
OHVD construction									
C61100	Falsework modification	8d	20-Jul-17 A	27-Jul-17 A					
C61110	OHVD slab construction (box out will be formed in R.J. location)	8d	28-Jul-17 A	04-Aug-17 A					
C61120	OHVD kicker wall construction	8d	05-Aug-17 A	11-Aug-17 A					
Base slab construction									
200	Base slab construction	27d	28-Aug-17 A	17-Sep-17 A	Base slab construction				
C61060	Shuffle the vehicular access	5d	28-Aug-17 A	01-Sep-17 A					
C61070	Construction of 1st portion base slab	7d	02-Sep-17 A	08-Sep-17 A	1st portion base slab				
C61080	Shuffle the vehicular access	5d	09-Sep-17 A	13-Sep-17 A	Shuffle the vehicular access				
C61090	Construction of 2nd portion base slab	7d	14-Sep-17 A	17-Sep-17 A	Construction of 2nd portion base slab				
SR8 - Rotational Joint Installation									
Omega Seal Installation									
A62190	1st part	5d	02-Oct-17	06-Oct-17	1st part				
A62200	2nd part	5d	07-Oct-17	11-Oct-17	2nd part				
A62210	3rd part	5d	12-Oct-17	16-Oct-17	3rd part				
Proprietary Cantilever Teeth Expansion Joint Installation for Base Slab									
A62220	Procurement (5 months)	150d	22-Jun-17 A	26-Oct-17	Procurement (5 months)				
A62230	Installation	14d	27-Oct-17	09-Nov-17	Installation				
Phase I - Reinstatement of Section of Sloping Seawall above Zone C Bay C6									
Backfill Rubble Mount, Installation of Granite Stone Facing by Land Team									
Section of Sloping Seawall above Bay C6 Reinstatement									
A61050	Dismantle Reprop Wall Partially (Above Slope Sea Wall)	5d	24-Jul-17 A	07-Oct-17	Dismantle Reprop Wall Partially (Above Slope Sea Wall)				
A61040	Backfilling of Rubble Mound (Grade 200 Rock)	7d	27-Sep-17 A	28-Sep-17 A	Backfilling of Rubble Mound (Grade 200 Rock)				
A61060	Cast Kerbing Concrete	3d	08-Oct-17	10-Oct-17	Cast Kerbing Concrete				
A61070	Make good rubble mound and shotcreting	5d	11-Oct-17	15-Oct-17	Make good rubble mound and shotcreting				
A61080	Installation of Granite Stone Facing	7d	16-Oct-17	22-Oct-17	Installation of Granite Stone Facing				
Removal of Remaining Pipe Pile Wall, Sheet Pile Wall & D-wall by Marine Team									
260	Removal of Remaining Pipe Pile Wall, Sheet Pile Wall & D-wall	145d	22-Oct-17	16-Mar-18	Removal of Remaining Pipe Pile Wall, Sheet Pile Wall & D-wall				
A61100	Cut pipe pile wall at A1 - A14 (After A61090 & 25A)	15d	09-Dec-17	23-Dec-17	Cut pipe pile wall at A1 - A14				
A61110	Under water cut sheet pile wall (5 nos.)	6d	24-Dec-17	29-Dec-17	Under water cut				
A61130	Remove filled material to -4.35mPD (6,000m3)	10d	30-Dec-17	08-Jan-18					
A61140	Remove seawall blocks at Bay 1 & 2 (356nos.)	8d	09-Jan-18	16-Jan-18					
A61150	Remove filled material below cut off level 1m	5d	17-Jan-18	21-Jan-18					
A61200	Vertical cut at Panel W4D12, 15, 16 & 17 (12nos./1.5m)	4d	22-Jan-18	25-Jan-18					
A61210	Horizontal cut at W4D12, 15, 16 & 17 (16 nos./1.5m)	5d	26-Jan-18	30-Jan-18					

Activity ID	Activity Name	Original Duration	Start	Finish	2017			2018
					Oct	Nov	Dec	
A61160	Vertical cut at W3D8 to W3D10 (9 nos.)	3d	26-Jan-18	28-Jan-18				
A61170	Horizontal cut at W3D8 to W3D10 (12 nos.)	9d	31-Jan-18	08-Feb-18				
Phase II Seawall Reinstatement		38d	30-Nov-17	07-Jan-18				
36	Phase II Seawall Reinstatement	31d	30-Nov-17	07-Jan-18				
Along existing vertical seawall		12d	30-Nov-17	12-Dec-17				
37	Along existing vertical seawall	10d	30-Nov-17	12-Dec-17				
38	Vertical cut at Panel W4D13 to 14 (8 nos./1.5m)	8d	01-Dec-17	08-Dec-17				
39	Horizontal cut at W4D13 to 14 (8 nos./1.5m)	4d	09-Dec-17	12-Dec-17				
Reinstatement of Vertical Seawall		26d	13-Dec-17	07-Jan-18				
40	Reinstatement of Vertical Seawall	21d	13-Dec-17	07-Jan-18				
41	Drill hole and install dowel bar at existing vertical seawall	7d	13-Dec-17	19-Dec-17				
42	Erect steel plate for external formwork of seawall (diver works)	7d	20-Dec-17	26-Dec-17				
43	Pour tremie concrete for reinstatement of existing seawall (diver works)	2d	27-Dec-17	28-Dec-17				
44	Remove steel formworks (diver works)	2d	29-Dec-17	30-Dec-17				
45	Reinstatement granitic facing stone at vertical seawall	4d	31-Dec-17	03-Jan-18				
46	Erect formwork for seawall coping	2d	04-Jan-18	05-Jan-18				
47	Pour concrete for seawall coping	1d	06-Jan-18	06-Jan-18				
48	Remove formwork at seawall coping	1d	07-Jan-18	07-Jan-18				
TTA Revert Traffic Back to Original Alignment		177d	11-Jul-17 A	03-Jan-18				
East Bound TTA - IEC East Bound, Victoria Park Road & footpath along Sea Side		175d	11-Jul-17 A	01-Jan-18				
Stage 1 - IEC (East Bound)		89d	11-Jul-17 A	07-Oct-17				
Reinstatement Existing Structure		89d	11-Jul-17 A	07-Oct-17				
A10790	Reinstatement of Type 2 Wing Wall (20m) and Type 3 Parapet (10m)	21d	11-Jul-17 A	08-Sep-17 A				
A10800	Install metal parapet on parapet wall (30m)	6d	02-Oct-17	07-Oct-17				
Stage 2 - Victoria Park Road		69d	01-Sep-17 A	19-Nov-17				
A10930	Break flexible pavement and concrete slab above EB traffic deck	2d	01-Sep-17 A	06-Sep-17 A				
A10900	Remove flexible pavement and then break temp light weight concrete ramp (60m)	14d	08-Sep-17 A	28-Oct-17				
A10910	Construct parapet wall Type R3 (15m) and Type R2 (25m) on extg bridge	23d	09-Sep-17 A	21-Oct-17				
A10940	Dismantle traffic deck (360m2) and cut king posts (4 nos.)	5d	15-Sep-17 A	20-Sep-17 A				
A10970	Backfill Type B Material up to 2m below F.F.L.(Ave.2.6m High, 13 Layer@0.2m each layer)	6d	21-Sep-17 A	23-Sep-17 A				
A10950	Break two concrete footings for temp traffic deck	6d	26-Sep-17 A	01-Oct-17 A				
A10960	Break pipe piles (28 nos.) and cut sheet pile (60 piece)	14d	26-Sep-17 A	09-Oct-17				
A10980	Backfill General Fill Material up to Formation Level (Ave. 1.5m High, 5 Layer@ 0.3m each Layer)	9d	28-Sep-17 A	11-Oct-17				
A10990	Construct 450/300 stormwater pipe (20m/35m) with 2 Manholes and 1 gully	8d	12-Oct-17	19-Oct-17				
A11000	Remove the temp uPVC divided pipe (45m) and two Manholes	3d	20-Oct-17	22-Oct-17				
A10920	Install metal parapet on parapet wall (40m)	6d	22-Oct-17	27-Oct-17				
A11010	Reinstate the road kerb along VPR (100m)	5d	23-Oct-17	27-Oct-17				
A11020	Well compact formation level and subbase for SRT	8d	28-Oct-17	04-Nov-17				
A11030	Lay flexible road pavement (RB, BC)	3d	05-Nov-17	07-Nov-17				
A11040	Expose and Install Manhole Covers	2d	08-Nov-17	09-Nov-17				
A11050	Lay flexible road pavement (WC)	2d	10-Nov-17	11-Nov-17				
A11060	Lay road marking and erect permanent traffic signs	2d	12-Nov-17	13-Nov-17				
A11070	Implement next TTM stage 3 (VPR footpath, EB)	1d	19-Nov-17	19-Nov-17				
Stage 3 - Reinstatement of Footpath along Sea Side		43d	20-Nov-17	01-Jan-18				

Activity ID	Activity Name	Original Duration	Start	Finish	2017				2018
					Oct	Nov	Dec	Jan	
Phase 1									
A11240	Temporary Pedestrian Diversion	4d	20-Nov-17	23-Nov-17					
A11250	Break flexible pavement and concrete slab above EB traffic deck (Partially)	3d	24-Nov-17	26-Nov-17					
A11310	Temporay Relocate telecom ducts	7d	24-Nov-17	30-Nov-17					
A11260	Dismantle traffic deck (Partially) and Cut king posts	5d	27-Nov-17	01-Dec-17					
A11270	Break two concrete footings	7d	02-Dec-17	08-Dec-17					
A11280	Cut pipe piles and sheet pile	10d	02-Dec-17	11-Dec-17					
A11290	Backfill Type B Material up to 2m below F.F.L (Compaction by proof rolling method of 0.2m each layer)	6d	12-Dec-17	17-Dec-17					
A11300	Backfill General Fill Material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)	10d	18-Dec-17	27-Dec-17					
Phase 2 - Sloping Seawall Reinstatement									
A11320	Backfill and make good rubble mound profile	7d	01-Dec-17	07-Dec-17					
A11330	Install hand pack rubble	6d	08-Dec-17	13-Dec-17					
A11340	Erect formwork for toe berm	3d	14-Dec-17	16-Dec-17					
A11350	Concreting for toe berm	2d	17-Dec-17	18-Dec-17					
A11360	Trim the rubble mound profile	4d	19-Dec-17	22-Dec-17					
A11370	Shotcreting on the rubble mound	2d	23-Dec-17	24-Dec-17					
A11380	Erect formwork for intermediate berms	7d	25-Dec-17	31-Dec-17					
A11390	Concreting for intermediate berms	1d	01-Jan-18	01-Jan-18					
West Bound - IEC West Bound & Tsing fung Street									
Stage 2 - Tsing Fung Street									
A11140	Remove flexible pavement and then break temp light weight concrete ramp (60m)	10d	07-Aug-17 A	09-Oct-17					
A11150	Construct parapet wall Type R2 (18m) and Type R1 (42m) on existing bridge	42d	11-Sep-17 A	20-Nov-17					
A11090	Dismantle traffic deck (300m2) and cut king posts (4 nos.)	5d	20-Sep-17 A	26-Sep-17 A					
A11100	Backfill Type B Material up to 2m below F.F.L (Ave. 2.6m High, 13 Layer @ 0.2m each Layer)	6d	27-Sep-17 A	28-Sep-17 A					
A11110	Backfill General Fill Material up to Formation Level (Ave. 1.5m High, 5 Layer @ 0.3m each Layer)	15d	29-Sep-17 A	04-Oct-17					
A11120	Break pipe piles (28 nos.) and cut sheet pile (60 piece)	10d	29-Sep-17 A	30-Sep-17 A					
A11130	Break two concrete footings for temp traffic deck	6d	01-Oct-17 A	06-Oct-17					
A11170	Relay new 400 diameter PE pipe under slow lane of TFS by HKCG (4+21)	25d	07-Oct-17	31-Oct-17					
A11180	Lay cross road duct for permanent lighting	3d	01-Nov-17	03-Nov-17					
A11190	Reinstate the Road Kerb along TFS (100m)	6d	04-Nov-17	09-Nov-17					
A11200	Well compact formation level and subbase for SRT	8d	10-Nov-17	17-Nov-17					
A11210	Lay flexible road pavement (RB, BC, WC)	7d	18-Nov-17	24-Nov-17					
A11160	Install metal parapet on parapet wall (60m)	6d	21-Nov-17	26-Nov-17					
A11220	Lay road marking and erect permanent traffic signs	2d	25-Nov-17	26-Nov-17					
A11230	Final cleaning for implement next TTM stage 3 (Victoria Park, WB)	1d	03-Dec-17	03-Dec-17					
Stage 3A - Removal of Temporary Traffic Deck on Diverted Tsing Fung Street & Reinstatement Works									
A11690	Break flexible pavement and concrete slab above traffic deck	3d	04-Dec-17	06-Dec-17					
A11700	Dismantle traffic deck and Cut king posts	5d	07-Dec-17	11-Dec-17					
A11710	Break two concrete footings	7d	12-Dec-17	18-Dec-17					
A11720	Cut pipe piles and sheet pile	7d	12-Dec-17	18-Dec-17					
A11730	Backfill Type B Material up to 2m below F.F.L (Compaction by proof rolling method of 0.2m each layer)	6d	19-Dec-17	24-Dec-17					
A11740	Backfill General Fill Material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)	10d	25-Dec-17	03-Jan-18					

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017				2018	
						Oct	Nov	Dec	Jan		
Update 2017-10-20 CWB(CC) - Commissioning Contract (DRM)											
PRELIMINARIES AND GENERAL REQUIREMENTS											
Salient Key Dates and Milestones											
Contract Key Dates											
KD003a	KD3 - Achievement of Stage 3 (1318 days) - include EOT (140 days)	0		07-Oct-17 A		▲					
KD004	KD4 - Achievement of Stage 4 (1377 days) - include EOT (81 days)	0		05-Dec-17*	0			▲			
KD005	KD5 - Achievement of Stage 5 (1377 days) - include EOT (81 days)	0		05-Dec-17*	0			▲			
KD006	KD6 - Completion of Section 1 of the Works (1377 days) - include EOT (81 days)	0		05-Dec-17*	0			▲			
KD011	KD11 - Completion of Section 6 of the Works (1377 days) - include EOT (81 days)	0		05-Dec-17*	0			▲			
Possession Dates and Vacation Dates											
PO-IIa	Possession of Portion IIa (Day 1) - WVb below +6.5mPD	1329	28-Feb-14 A	18-Dec-17	-244	[Gantt bar: blue, red, yellow]					
PO-III	Possession of Portion III (Day 120) - CH1805-2600	1209	28-Jun-14 A	18-Dec-17	-314	[Gantt bar: blue, red, yellow]					
PO-Ib	Possession of Portion Ib (Day 242) - CH1580-1805	1087	28-Oct-14 A	18-Dec-17	-248	[Gantt bar: blue, red, yellow]					
PO-IXd	Possession of Portion IXd (Day 266) - CH4600-4860	1063	21-Nov-14 A	18-Dec-17	-306	[Gantt bar: blue, red, yellow]					
PO-XI	Possession of Portion XI (Day 296) - EVS	1033	21-Dec-14 A	18-Dec-17	272	[Gantt bar: blue, red, yellow]					
PO-IIc	Possession of Portion IIc (Day 336) - CH1360-1580	993	30-Jan-15 A	18-Dec-17	-244	[Gantt bar: blue, red, yellow]					
PO-IIb	Possession of Portion IIb (Day 336) - WVb above +6.5mPD	669	30-Jan-15 A	18-Dec-17	-244	[Gantt bar: blue, red, yellow]					
PO-IXa	Possession of Portion IXa (Day 392) - CH4860-5150	937	27-Mar-15 A	18-Dec-17	-314	[Gantt bar: blue, red, yellow]					
PO-Va	Possession of Portion V (Day 607) - CH2950-3210	722	28-Oct-15 A	18-Dec-17	-268	[Gantt bar: blue, red, yellow]					
PO-VII_a1	Possession of Portion VII (Day 762) - CH3911-4250 (below -6.0mPD)	659	30-Dec-15 A	18-Dec-17	-226	[Gantt bar: blue, red, yellow]					
PO-Vc	Possession of Portion V (Day 607) - CH3210-3250	658	15-Jan-16 A	18-Dec-17	-252	[Gantt bar: blue, red, yellow]					
PO-VIb_b1	Possession of Portion VIb (Day 761) - CH3428-3625 (E/B)	619	18-Feb-16 A	18-Dec-17	-269	[Gantt bar: blue, red, yellow]					
PO-VIb_b2	Possession of Portion VIb (Day 761) - CH3428-3625 (W/B)	568	29-Feb-16 A	18-Dec-17	-248	[Gantt bar: blue, red, yellow]					
PO-Xa_1	Possession of Portion Xa (Day 650) - ADB Southern Portion (AECOM letter ref: 2015007890T)	589	07-Mar-16 A	18-Dec-17	-304	[Gantt bar: blue, red, yellow]					

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING

Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 1 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017				2018
						Oct	Nov	Dec	Jan	
PO-Xb_1	Possession of Portion Xb (Day 804) - ADB Northern Portion	589	07-Mar-16 A	18-Dec-17	-304					
PO-Vb1	Possession of Portion V (Day 607) - SR3	587	11-Mar-16 A	18-Dec-17	272					
PO-Ia	Possession of Portion Ia (Day 789) - SCB / SCP1 / SCP2 / Rumsey Street Flyover	600	28-Mar-16 A	18-Dec-17	-268					
PO-VII_a2	Possession of Portion VII (Day 762) - CH3800-3911 (below -6.0mPD)	567	31-Mar-16 A	18-Dec-17	-184					
PO-IXc_1	Possession of Portion IXc (Day 712) - EVB above 3.6mPD - Relinquished on 12 Apr 2016	445	29-Jul-16 A	18-Dec-17	-302					
PO-IXb_1	Possession of Portion IXb (Day 712) - EVB (below +3.6mPD to tunnel top slab) - Relinquished on 12 Apr 2016	445	05-Aug-16 A	18-Dec-17	-302					
PO-VIa_a	Possession of Portion VIa (Day 823) - CH3250-3283	425	15-Aug-16 A	18-Dec-17	-267					
PO-Vb2_a	Possession of Portion V (Day 607) - SR2	456	15-Aug-16 A	18-Dec-17	-304					
PO-VIc_a	Possession of Portion VIc (Day 761) - CH3770-3800 (Access Shaft Opening)	391	23-Sep-16 A	18-Dec-17	-233					
PO-VIb_c	Possession of Portion VIb (Day 761) - CH3625-3770	391	23-Sep-16 A	18-Dec-17	-252					
PO-IVa1	Possession of Portion IVa (Day 930) - CH2600-2720	323	30-Nov-16 A	18-Dec-17	-268					
PO-IVb2	Possession of Portion IVb (Day 930) - MVB (GL D-H)	233	28-Feb-17 A	18-Dec-17	-295					
PO-VIIIa_a	Possession of Portion VIIIa (Day 929) - CH4530-4591 W/B	233	28-Feb-17 A	18-Dec-17	-226					
PO-VIIIa	Possession of Portion VIIIa (Day 929) - CH4250-4600 (Remaining)	241	12-Mar-17 A	18-Dec-17	-226					
PO-VIIIb	Possession of Portion VIIIb (Day 929) - SR8 (CH700-350)	233	12-Mar-17 A	18-Dec-17	-134					
PO-VIIIc	Possession of Portion VIIIc (Day 1039) - SR8 (CH350-310) / SCP4	233	12-Mar-17 A	18-Dec-17	-151					
PO-IVa2_a	Possession of Portion IVa (Day 930) - CH2720-2950	241	12-Mar-17 A	18-Dec-17	-268					
PO-IVb1	Possession of Portion IVb (Day 930) - MVB (GL A-C)	239	14-Mar-17 A	18-Dec-17	-295					
PO-IVa2_b	Possession of Portion IVa (Day 930) - SR1	203	30-Mar-17 A	18-Dec-17	-268					
PO-Vb2_b	Possession of Portion V (Day 607) - SCP3	182	03-Jul-17 A	18-Dec-17	-304					
PO-VIb_a	Possession of Portion VIb (Day 761) - CH3400-3428	80	31-Jul-17 A	18-Dec-17	-244					
PO-VIa_b	Possession of Portion VIa (Day 823) - CH3283-3400	80	31-Jul-17 A	18-Dec-17	-288					
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-Oct-17	07-Feb-18	-176					

DETAILED DESIGN OF WORKS

- Current Milestone
- Remaining Work
- Level of Effort
- Project Baseline
- Baseline Milestone
- Actual Work
- Critical Remaining Work

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 2 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

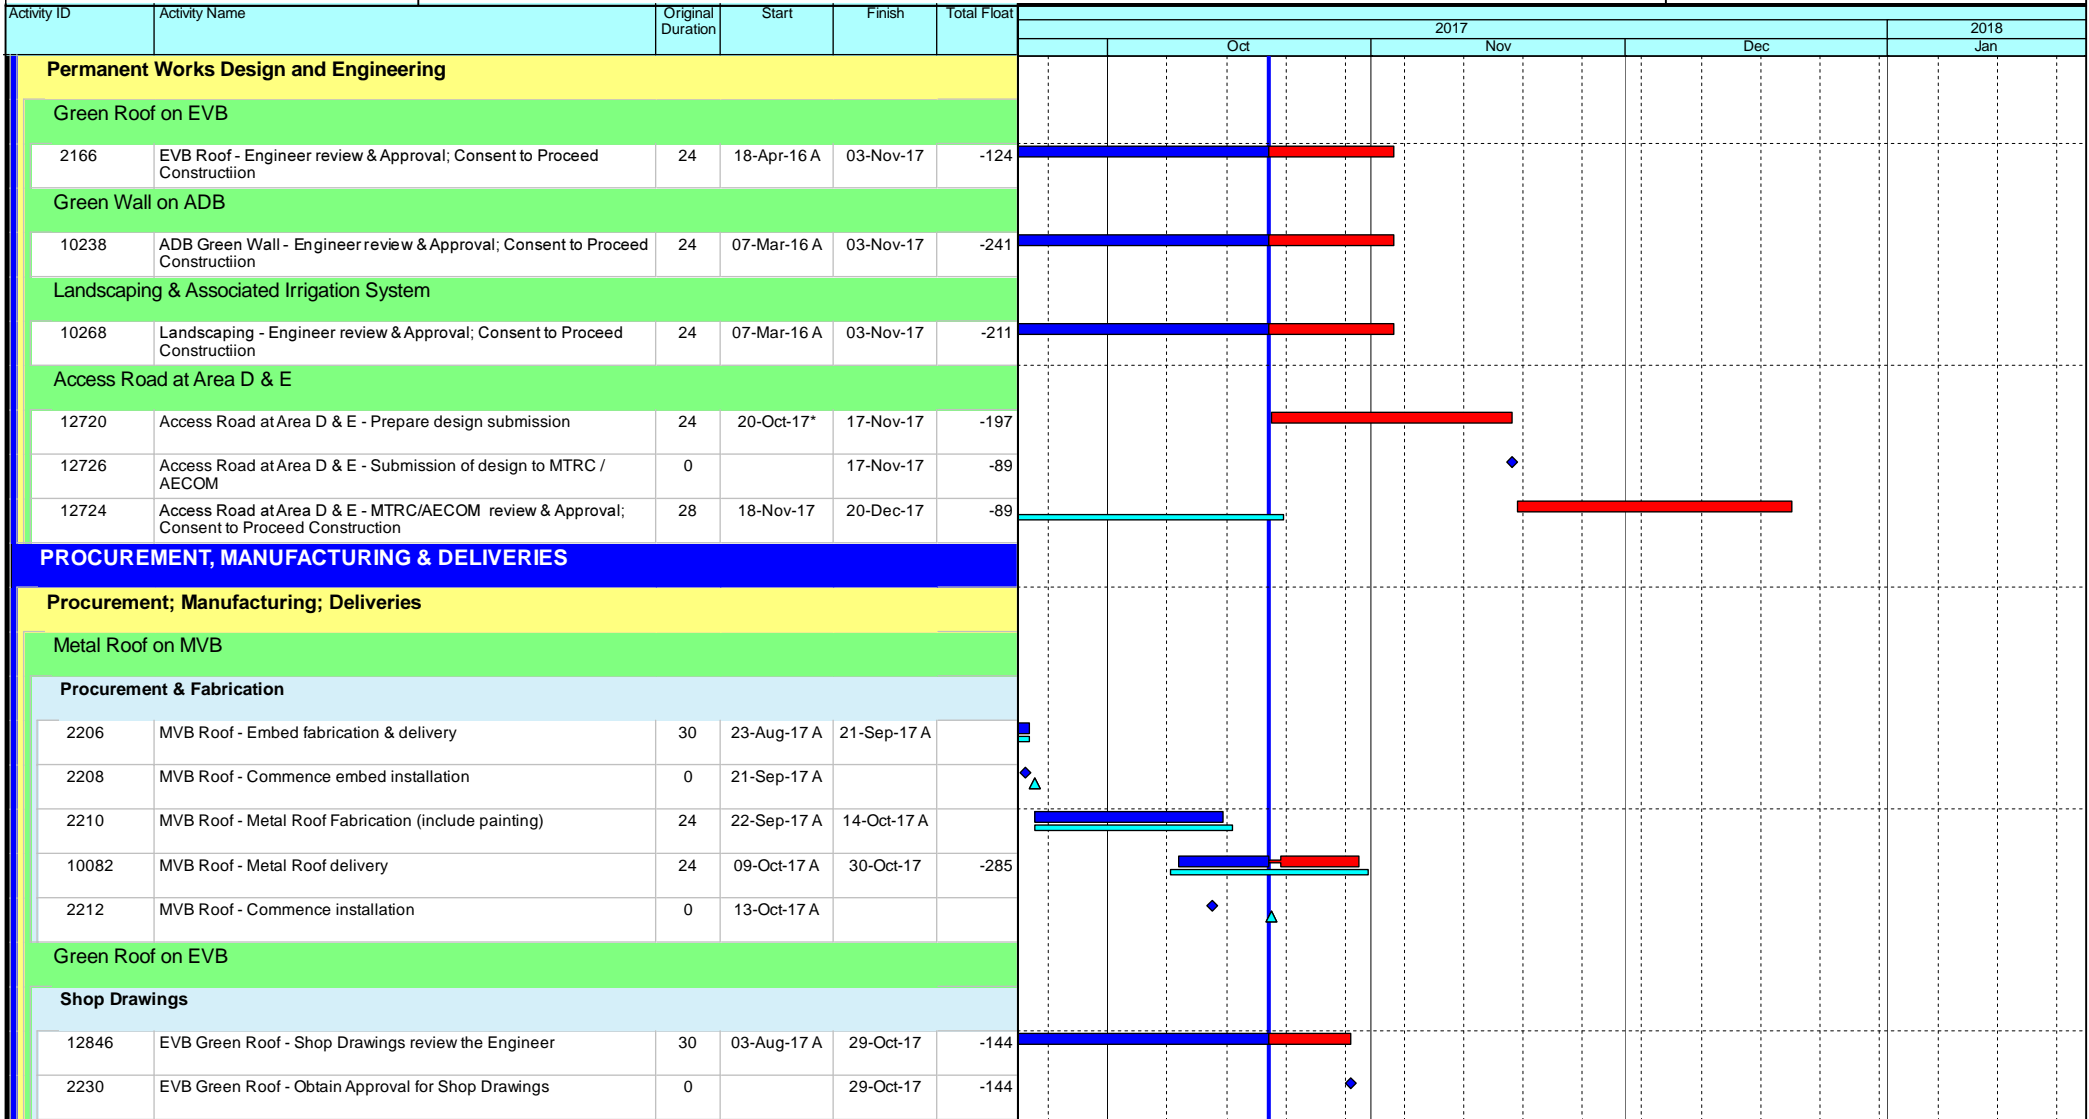

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 3 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

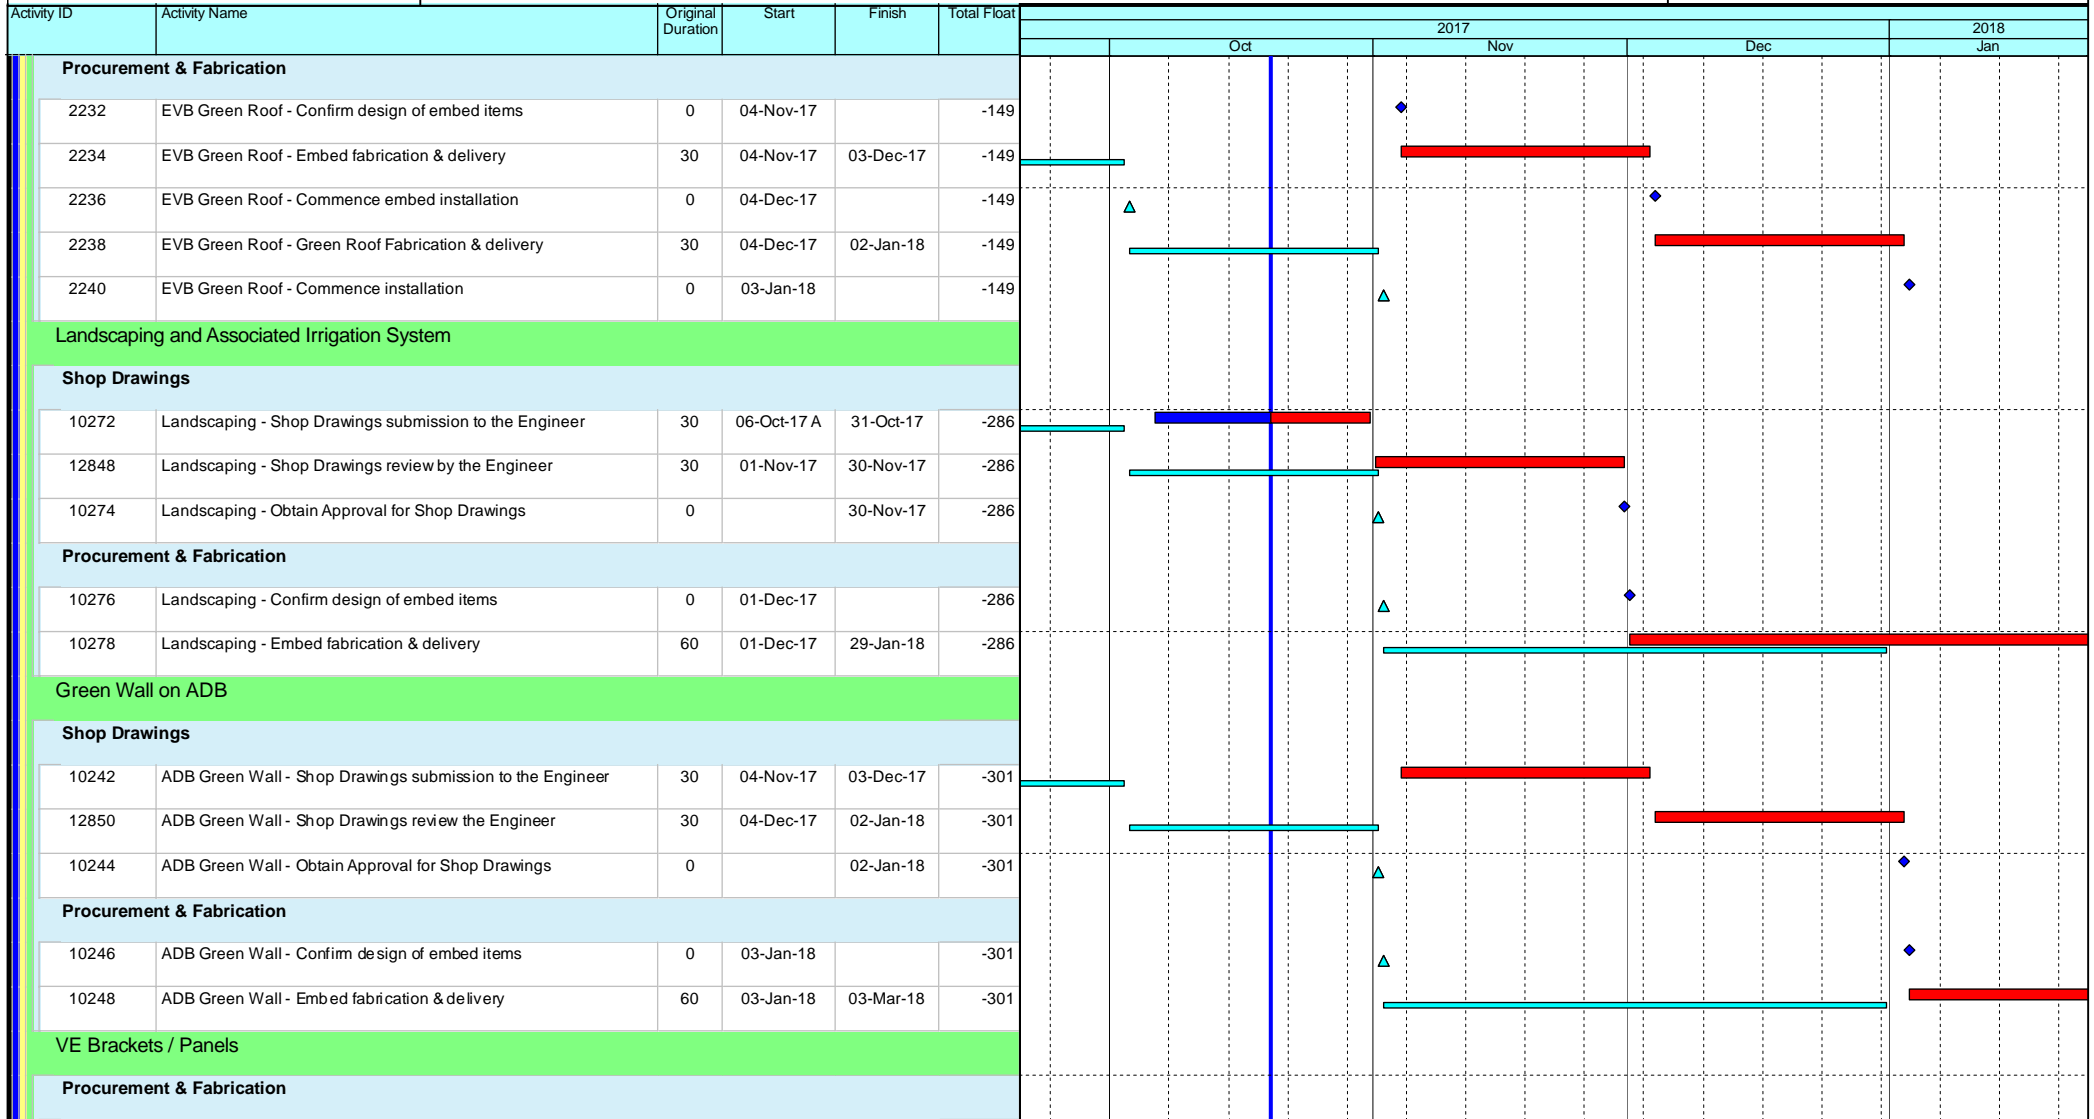

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 4 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

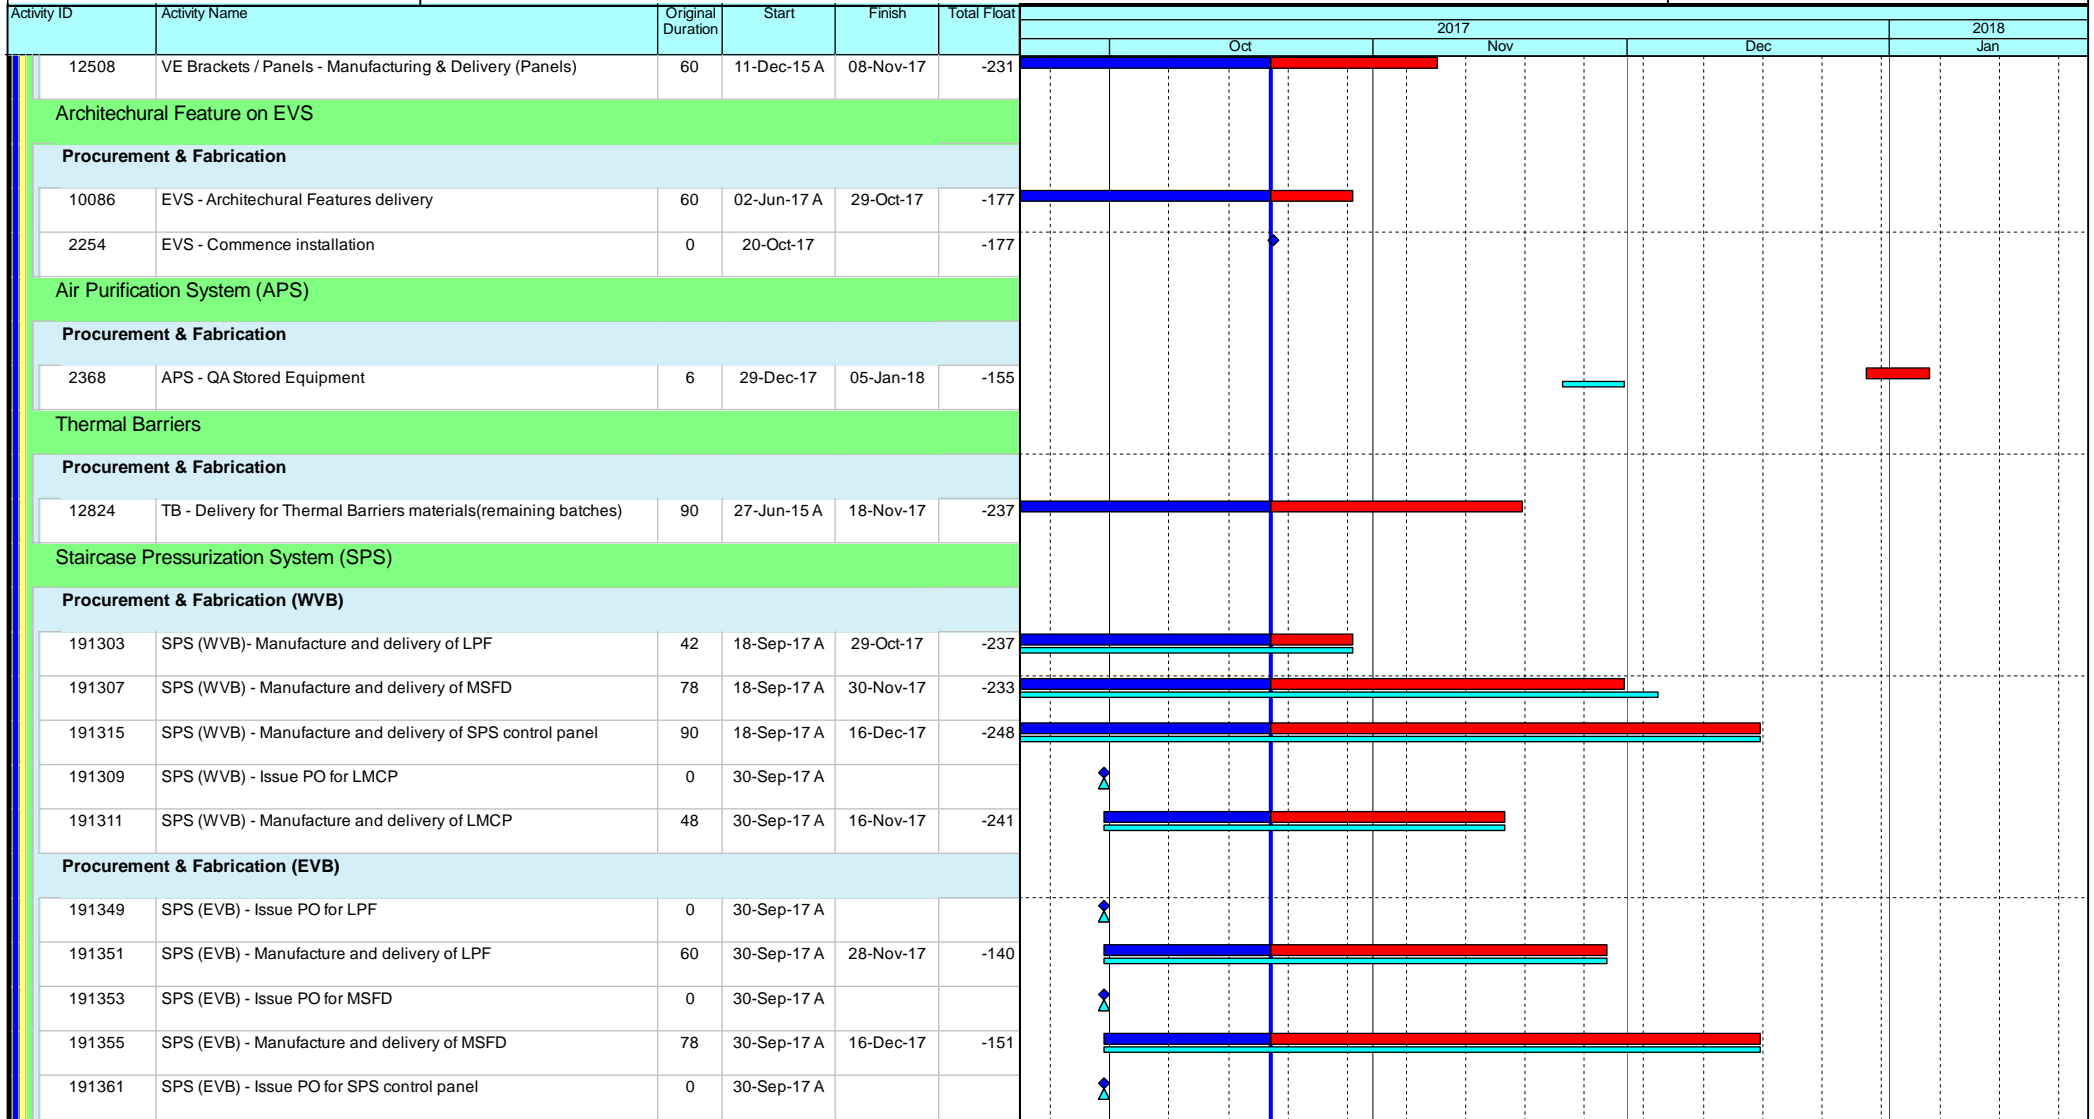

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING

Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 5 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017				2018
						Oct	Nov	Dec	Jan	
191363	SPS (EVB) - Manufacture and delivery of SPS control panel	90	30-Sep-17 A	28-Dec-17	-122					
191357	SPS (EVB) - Issue PO for LMCP	0	16-Oct-17 A							
191359	SPS (EVB) - Manufacture and delivery of LMCP	42	16-Oct-17 A	26-Nov-17	-117					
CONSTRUCTION										
West Ventilation Building (WVB - related)										
Tunnel Section (WVB-related)										
Portion Ia, IIc [CH840 to CH1360]										
13086a	Request for VO / instruction for TCSS equipment installation and cabling (Ganty FADS01) (Ref: H27613-LJV-ME-LE-4022)	24	04-Oct-16 A	03-Nov-17	-105					
13086	TCSS cabling and sign face installation (FADS01) - Start date is tentative and need to be confirmed at a later stage	40	04-Nov-17	20-Dec-17	-58					
Westbound										
5000	MEP(WB) - (CH840 to CH1360) E&M 1st Fix	29	05-Jun-17 A	26-Oct-17	-195					
5008	MEP(WB) - (CH840 to CH1360) E&M 2nd Fix (include Sump A)	58	12-Jun-17 A	03-Nov-17	-201					
5016	MEP(WB) - (CH840 to CH1360) E&M Final Fix	18	04-Nov-17	24-Nov-17	-201					
5024	MEP(WB) - (CH840 to CH1360) TCSS Field equip & cable installation	16	07-Nov-17	24-Nov-17	-201					
Eastbound										
6100	MEP(EB) - (CH840 to CH1360) E&M 1st Fix	29	01-Mar-17 A	26-Oct-17	-198					
6102	MEP(EB) - (CH840 to CH1360) E&M 2nd Fix (include Sump A)	58	22-May-17 A	03-Nov-17	-204					
6104	MEP(EB) - (CH840 to CH1360) E&M Final Fix	18	04-Nov-17	24-Nov-17	-204					
6106	MEP(EB) - (CH840 to CH1360) TCSS Field equip & cable installation	16	07-Nov-17	24-Nov-17	-204					
Portion IIa [CH1360 to CH1580]										
Westbound										
5010	MEP(WB) - (CH1360 to CH1580) E&M 2nd Fix	24	25-Jan-17 A	21-Sep-17 A						
5018	MEP(WB) - (CH1360 to CH1580) E&M Final Fix	8	08-Feb-17 A	23-Sep-17 A						
5026	MEP(WB) - (CH1360 to CH1580) TCSS Field equip & cable installation	7	13-Mar-17 A	23-Sep-17 A						

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 6 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

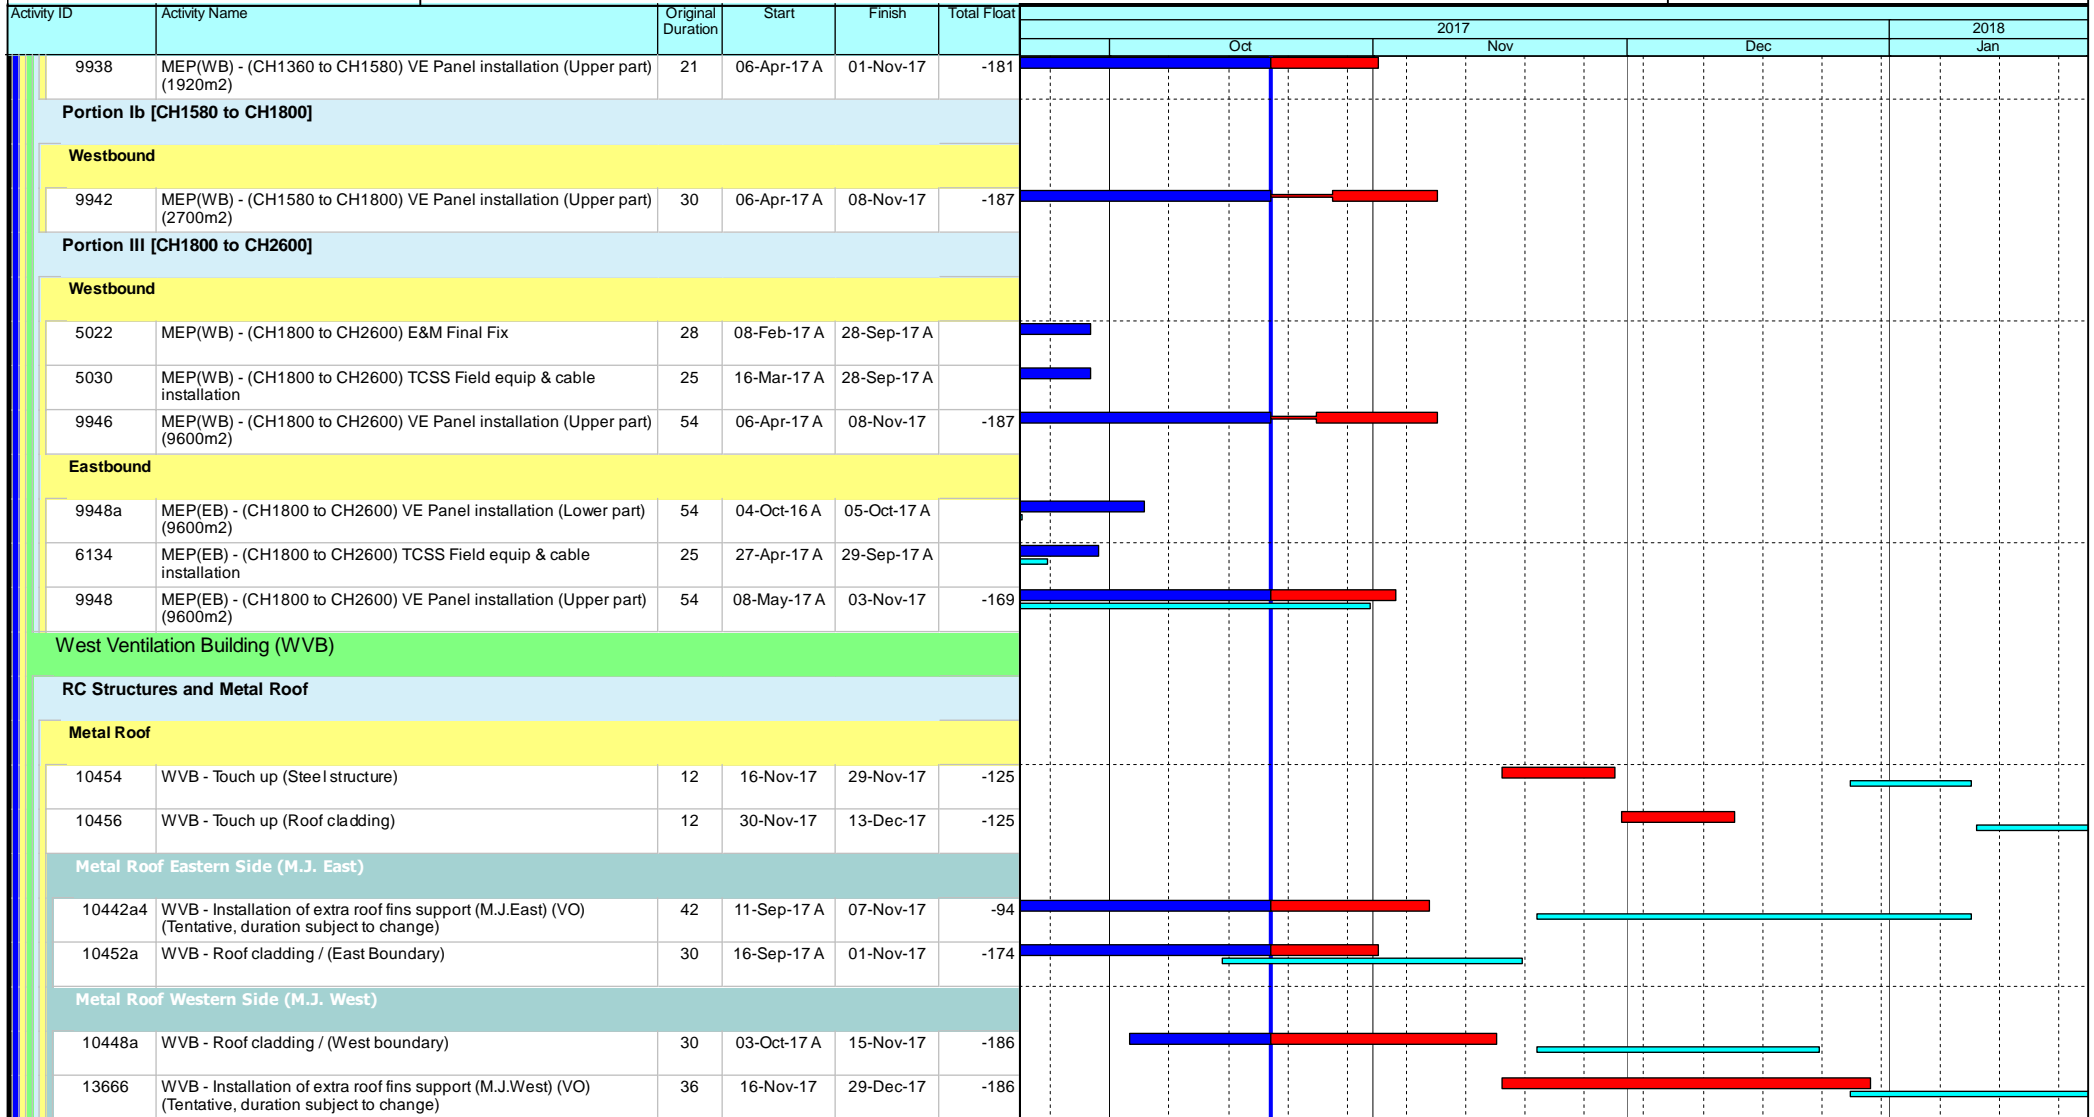

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
Baseline: DWP2d
Layout: Update Three Month Rolling
U044
Page 7 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

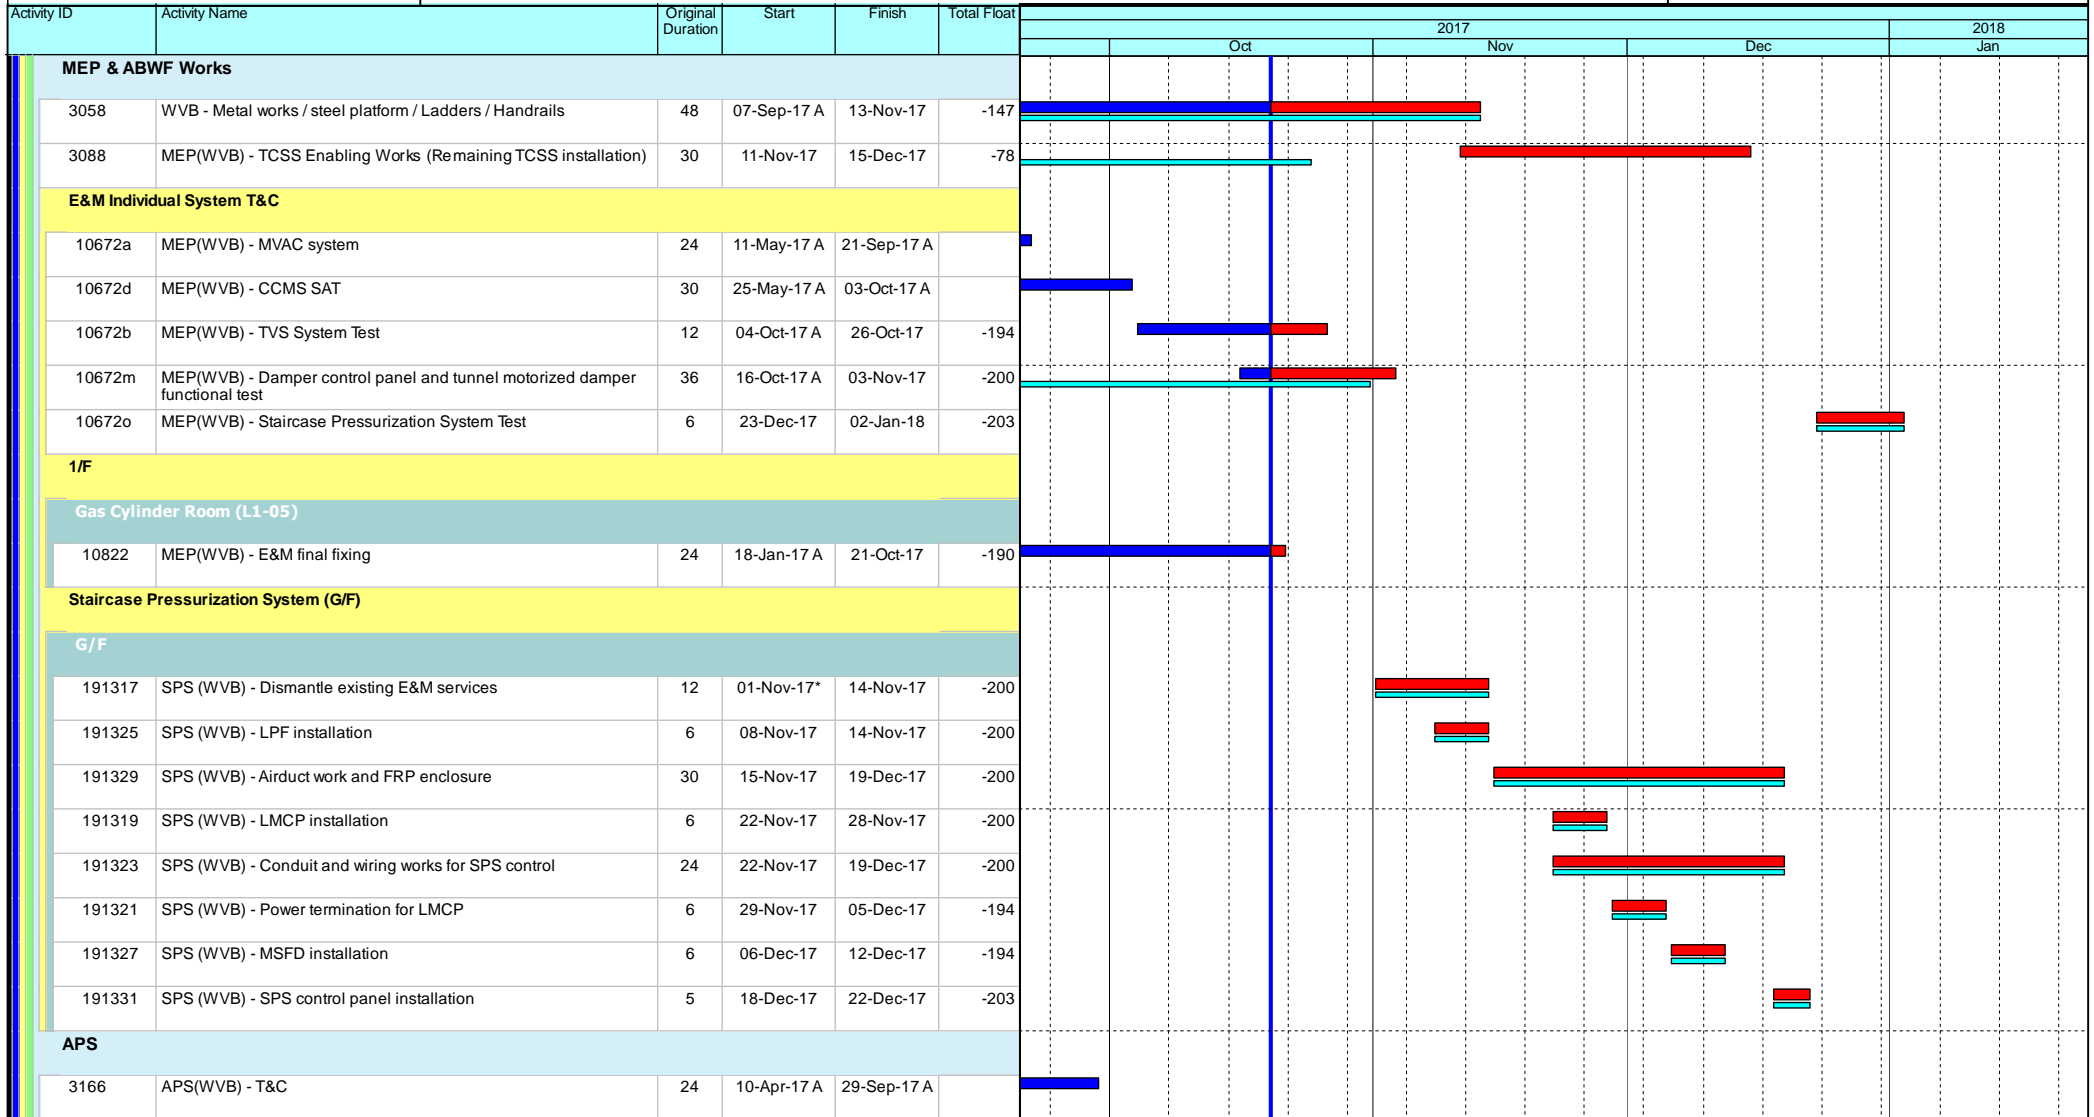

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 8 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

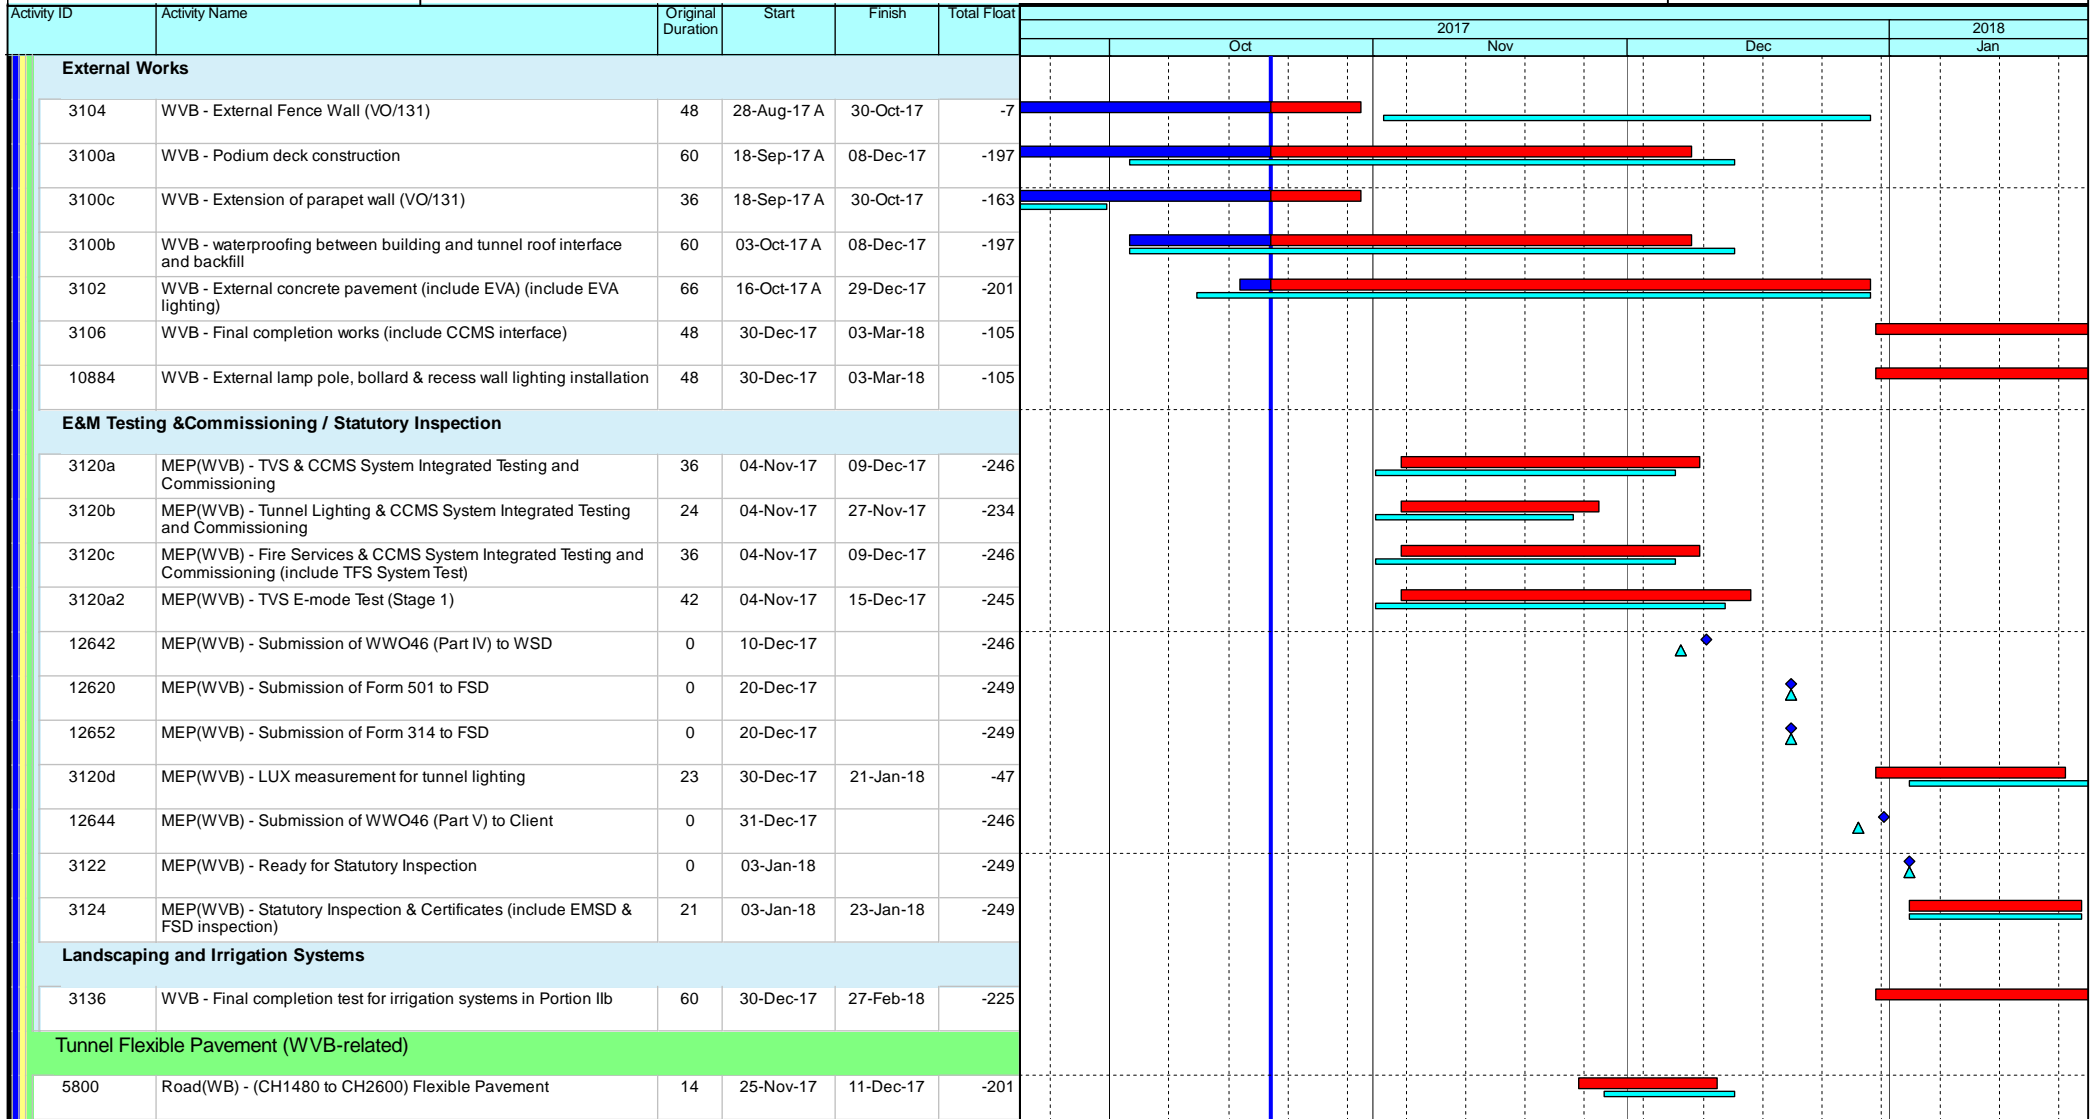

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 9 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

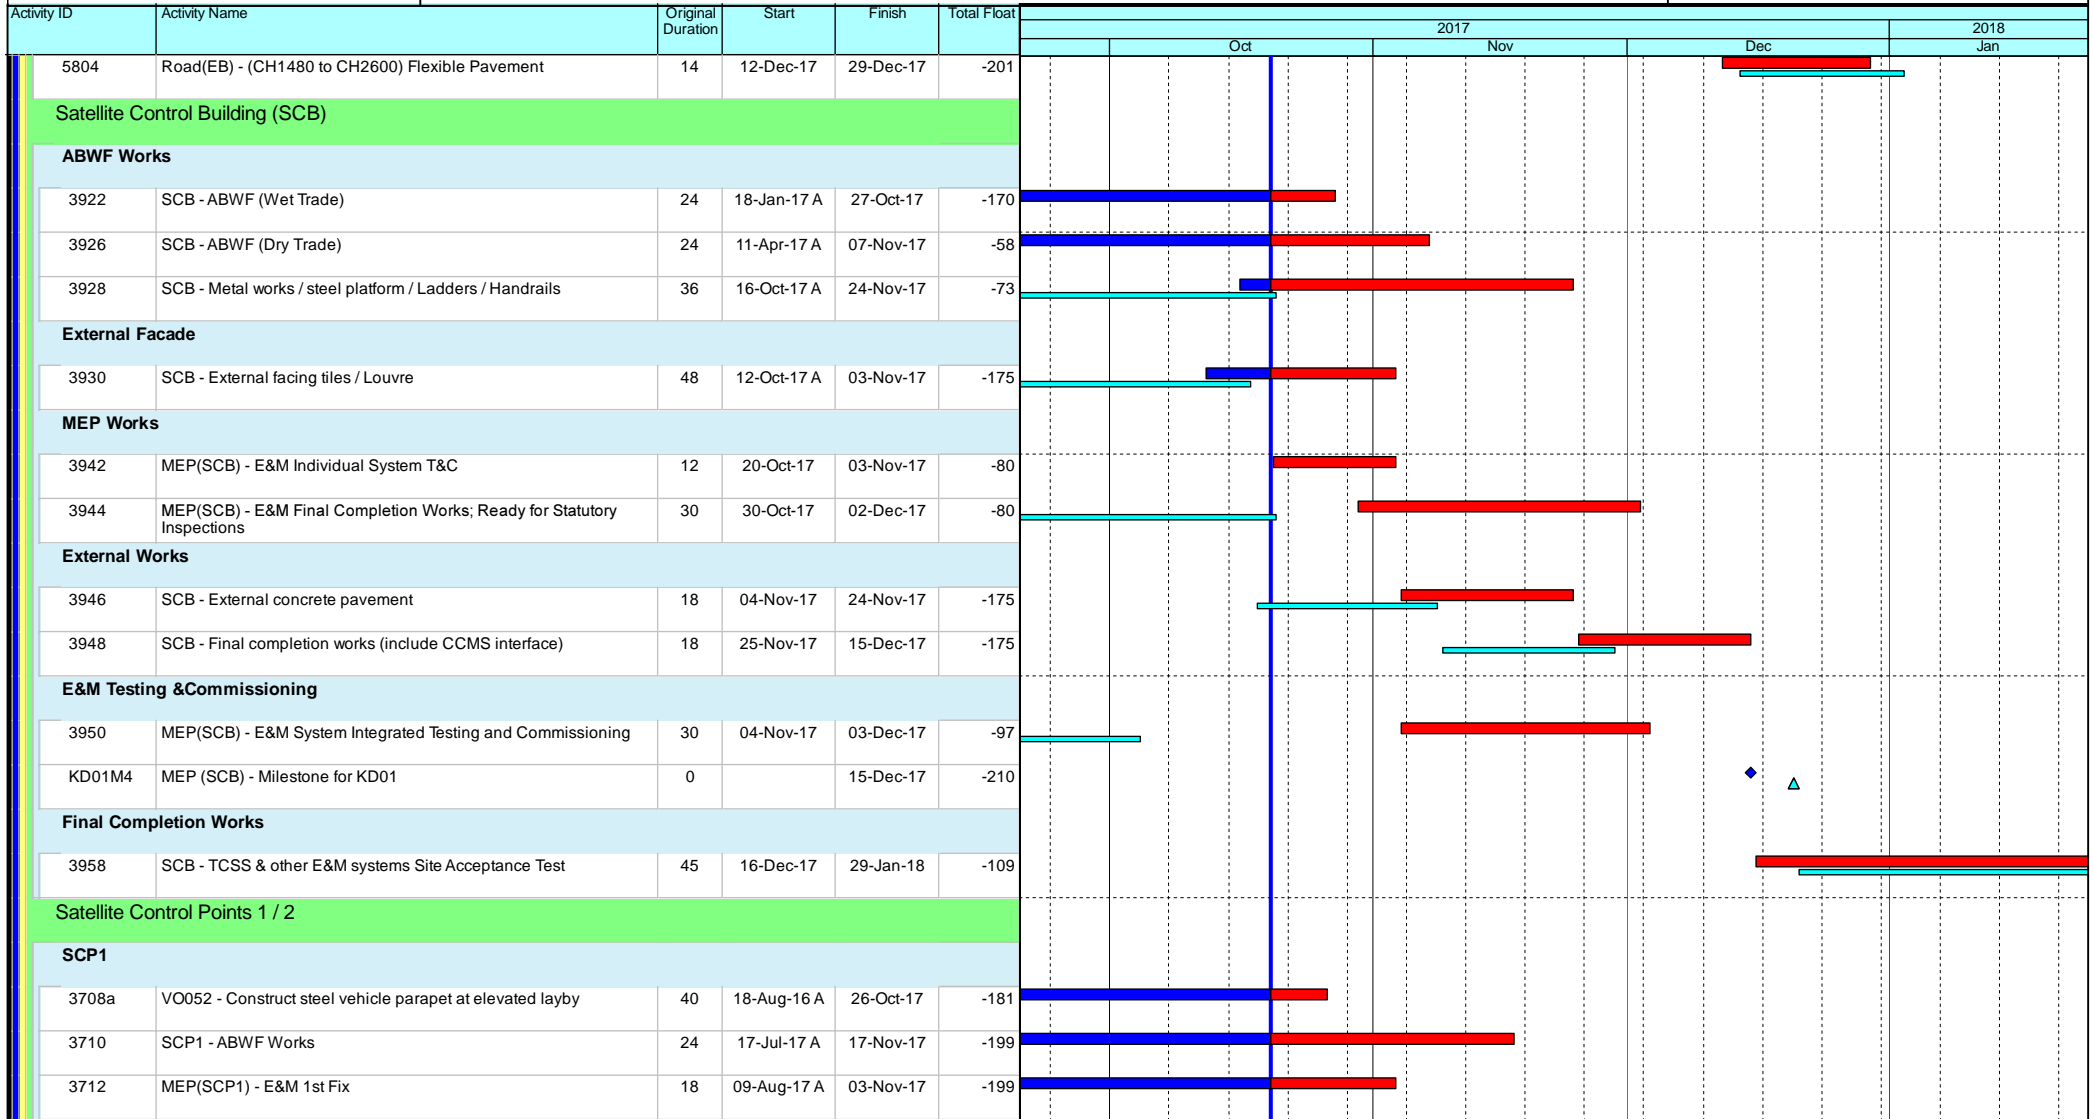


Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING

Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 10 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

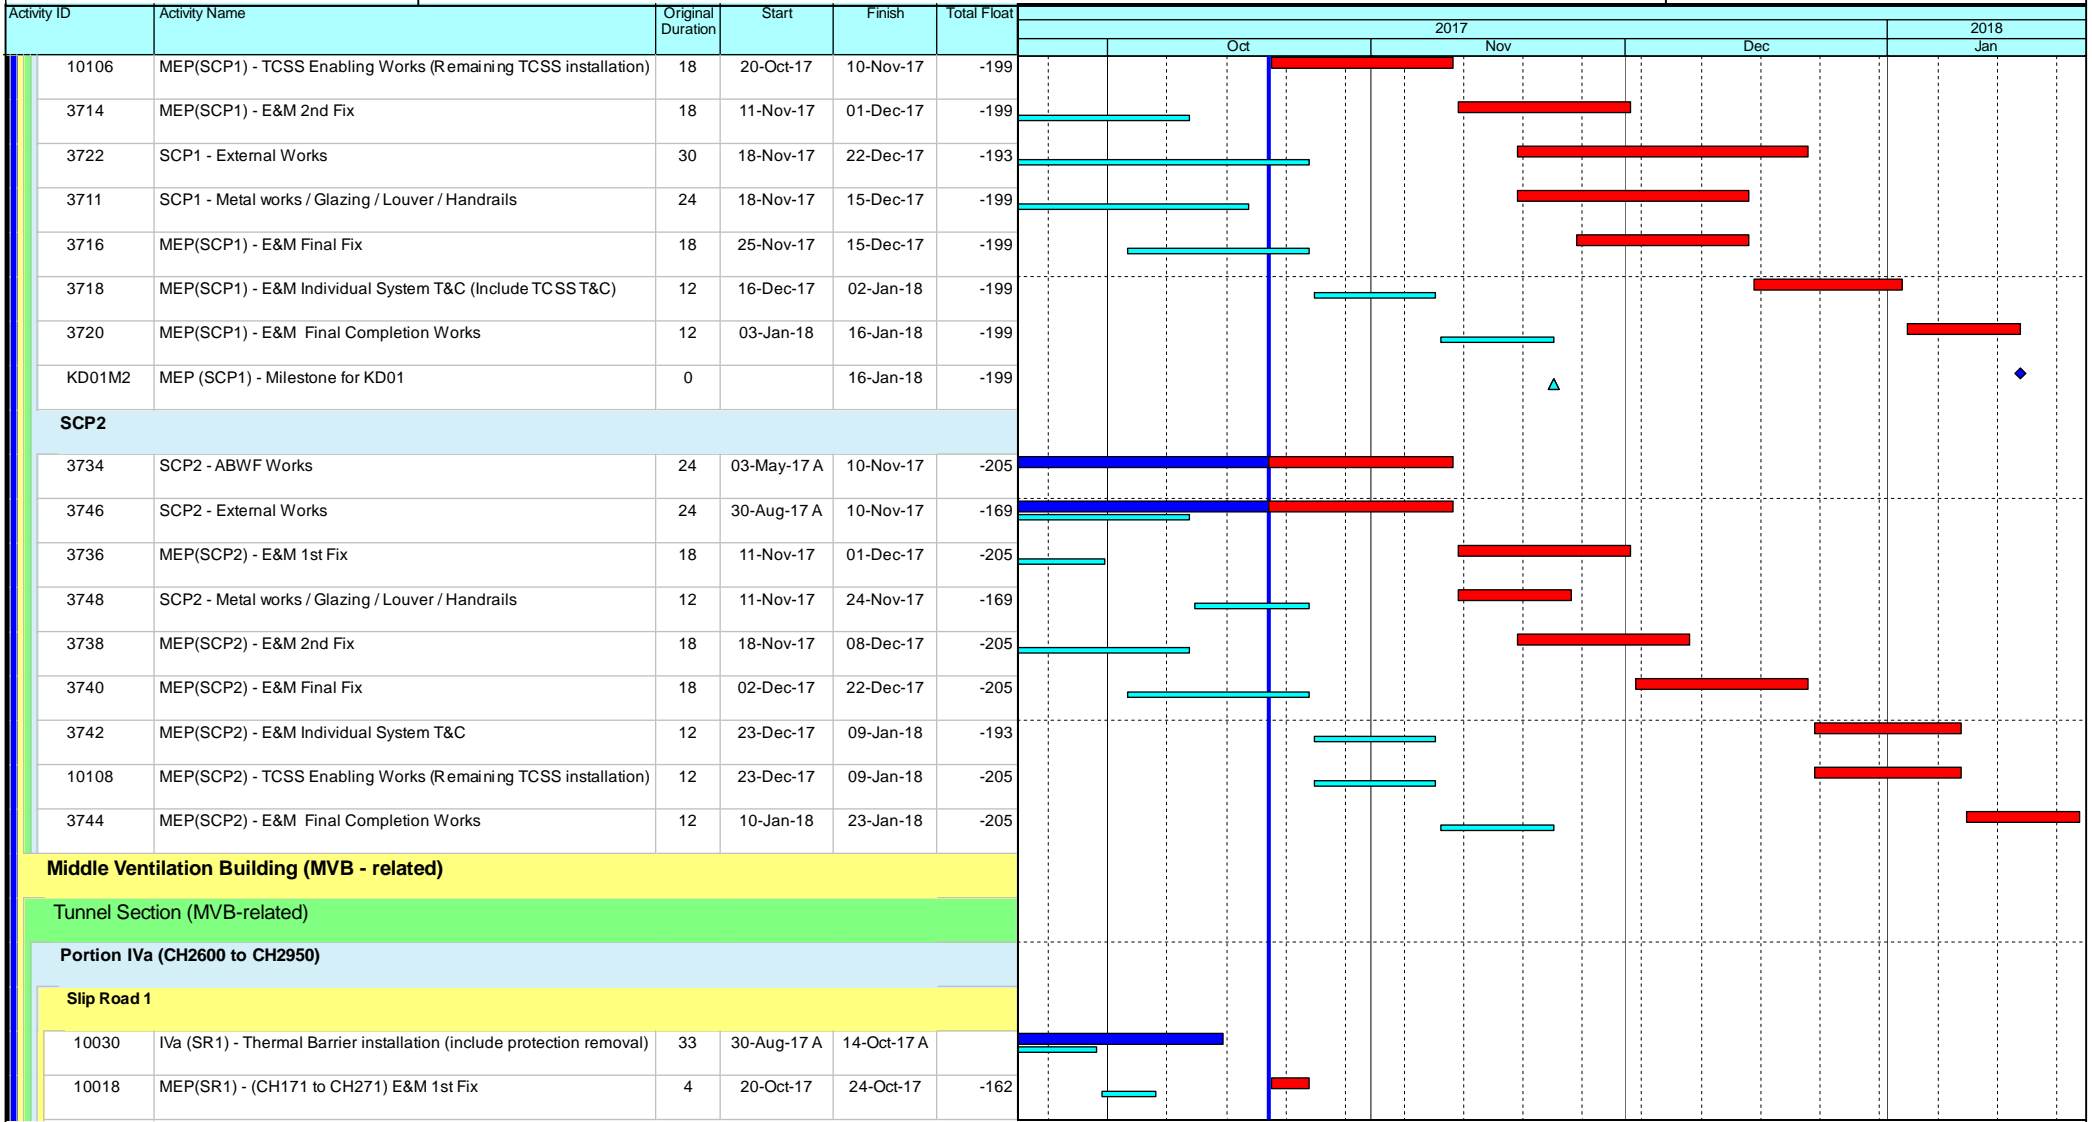

- ◆ Current Milestone
- ▬ Level of Effort
- △ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 44 (October 2017)

THREE MONTH ROLLING

Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 11 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017												2018		
						Oct			Nov			Dec			Jan			Jan		
						1	2	3	1	2	3	1	2	3	1	2	3	1		
10022a	MEP(SR1) - (CH171 to CH271) Niche installation	7	16-Nov-17	23-Nov-17	-156															
10020	MEP(SR1) - (CH171 to CH271) E&M 2nd Fix (include Sump B)	30	04-Dec-17	10-Jan-18	-195															
10030a	IVa (SR1) - Masking wall construction (VO) (56m)	14	08-Dec-17	23-Dec-17	-195															
10022	MEP(SR1) - (CH171 to CH271) E&M Final Fix	4	11-Jan-18	15-Jan-18	-195															
10046	MEP(SR1) - (CH171 to CH271) VE Panel installation (Upper part) (1200m2)	13	16-Jan-18	30-Jan-18	-195															
10046a	MEP(SR1) - (CH171 to CH271) VE Panel installation (Lower part) (1200m2)	13	16-Jan-18	30-Jan-18	-195															
Westbound (CH2600 to CH2720)																				
5100a	MEP(WB) - (CH2600 to CH2720) E&M 1st Fix	12	14-Apr-17 A	01-Nov-17	-168															
9950a1	MEP(WB) - (CH2600 to CH2720) VE Panel installation (Lower part) (1400m2)	9	02-Aug-17 A	21-Oct-17	-137															
5102a	MEP(WB) - (CH2600 to CH2720) E&M 2nd Fix	12	02-Nov-17	15-Nov-17	-168															
5104a2	MEP(WB) - (CH2600 to CH2720) Niche installation	4	03-Nov-17	07-Nov-17	-152															
9950a3	MEP(WB) - (CH2600 to CH2720) VE Panel installation (Upper part) (1750m2)	11	12-Jan-18	24-Jan-18	-214															
5104a	MEP(WB) - (CH2600 to CH2720) E&M Final Fix	6	18-Jan-18	24-Jan-18	-55															
5106a	MEP(WB) - (CH2600 to CH2720) TCSS Field equip & cable installation	6	18-Jan-18	24-Jan-18	-214															
Eastbound (CH2600 to CH2720)																				
5122a2	MEP(EB) - (CH2600 to CH2720) Niche installation	4	31-Oct-17	03-Nov-17	-166															
5130a1	IVa(EB) - Masking wall construction (VO) (23m)	12	02-Dec-17	15-Dec-17	-214															
9952a1	MEP(EB) - (CH2600 to CH2720) VE Panel installation (Lower part) (1400m2)	9	16-Dec-17	28-Dec-17	-181															
5120a	MEP(EB) - (CH2600 to CH2720) E&M 2nd Fix	7	03-Jan-18	10-Jan-18	-214															
5122a	MEP(EB) - (CH2600 to CH2720) E&M Final Fix	6	11-Jan-18	17-Jan-18	-208															
5124a	MEP(EB) - (CH2600 to CH2720) TCSS Field equip & cable installation	6	11-Jan-18	17-Jan-18	-214															
Westbound (CH2720 to CH2950)																				
5116b1	IVa(WB) - Masking wall construction (VO) (16m)	8	09-Oct-17 A	14-Oct-17 A																
5104b2	MEP(WB) - (CH2720 to CH2950) Niche installation	4	08-Nov-17	11-Nov-17	3															

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline
- ▲ Baseline Milestone

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 12 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

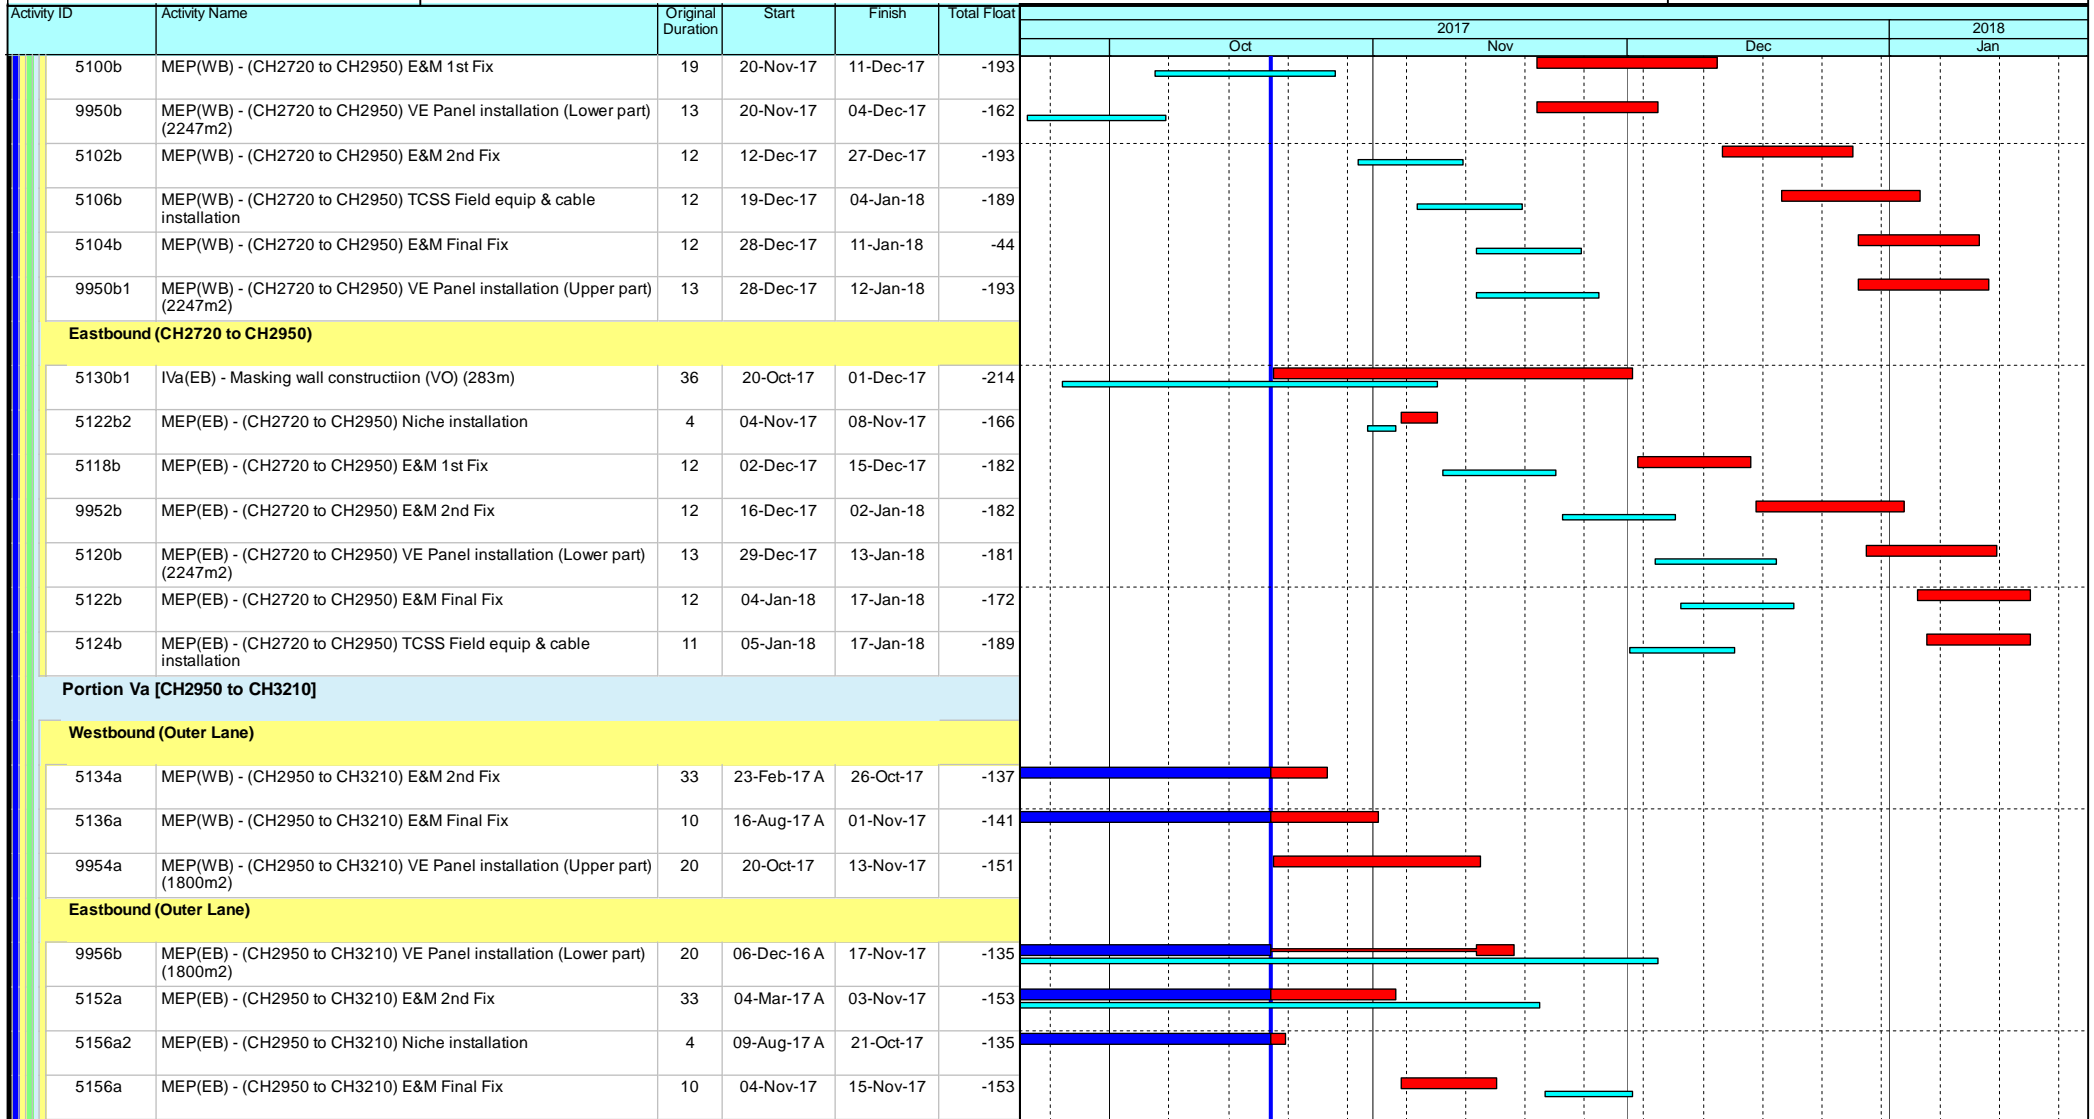

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING

Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 13 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017				2018
						Oct	Nov	Dec	Jan	
9956a	MEP(EB) - (CH2950 to CH3210) VE Panel installation (Upper part) (1800m2)	20	16-Nov-17	08-Dec-17	-153					
Portion Vb1 (SR3)										
Slip Road 3										
10032b	MEP(SR3) - (CH3089 to CH3334) E&M 1st Fix	13	15-Mar-17 A	27-Oct-17	-191					
10036b	MEP(SR3) - (CH3089 to CH3334) TCSS Field equip & cable installation	8	15-Mar-17 A	27-Oct-17	-164					
10034b	MEP(SR3) - (CH3089 to CH3334) E&M 2nd Fix (include Sump C)	27	30-Oct-17	29-Nov-17	-191					
10038b2	MEP(SR3) - (CH3089 to CH3334) Niche installation	2	23-Nov-17	24-Nov-17	-181					
10038b	MEP(SR3) - (CH3089 to CH3334) E&M Final Fix	8	30-Nov-17	08-Dec-17	-191					
10048b	MEP(SR3) - (CH3089 to CH3334) VE Panel installation (Upper part) (2940m2)	33	12-Jan-18	26-Feb-18	-250					
10048c	MEP(SR3) - (CH3089 to CH3334) VE Panel installation (Lower part) (2940m2)	33	12-Jan-18	26-Feb-18	-250					
Portion Vb2 (SR2 / SCP3)										
Slip Road 2										
10050b	MEP(SR2) - (CH3114 to CH3257) E&M 1st Fix	8	08-Mar-17 A	24-Oct-17	-161					
10056b	MEP(SR2) - (CH3114 to CH3257) TCSS Field equip & cable installation	5	16-Mar-17 A	24-Oct-17	-158					
10052b	MEP(SR2) - (CH3114 to CH3257) E&M 2nd Fix (include Sump F)	40	15-Jun-17 A	18-Nov-17	-182					
10054b2	MEP(SR2) -(CH3114 to CH3257) Niche installation	3	20-Nov-17*	22-Nov-17	-182					
10054b	MEP(SR2) -(CH3114 to CH3257) E&M Final Fix	5	23-Nov-17	28-Nov-17	-182					
10064c	MEP(SR2) - (CH3114 to CH3257) VE Panel installation (Lower part) (1716m2)	18	12-Dec-17	04-Jan-18	-250					
10064b2	MEP(SR2) - Road lighting installation (Portal)	18	08-Jan-18	27-Jan-18	-211					
Portion Vc [CH3210 to CH3250]										
Westbound (Outer Lane)										
5134c	MEP(WB) - (CH3210 to CH3250) E&M 2nd Fix	18	23-Feb-17 A	31-Oct-17	-130					
5136c	MEP(WB) - (CH3210 to CH3250) E&M Final Fix	10	01-Nov-17	11-Nov-17	-130					
9954c	MEP(WB) - (CH3210 to CH3250) VE Panel installation (Upper part) (1800m2)	20	14-Nov-17	06-Dec-17	-151					

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline
- ▲ Baseline Milestone

Leighton Contractors (Asia) Limited

Programme Update 44 (October 2017)

THREE MONTH ROLLING


Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 14 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

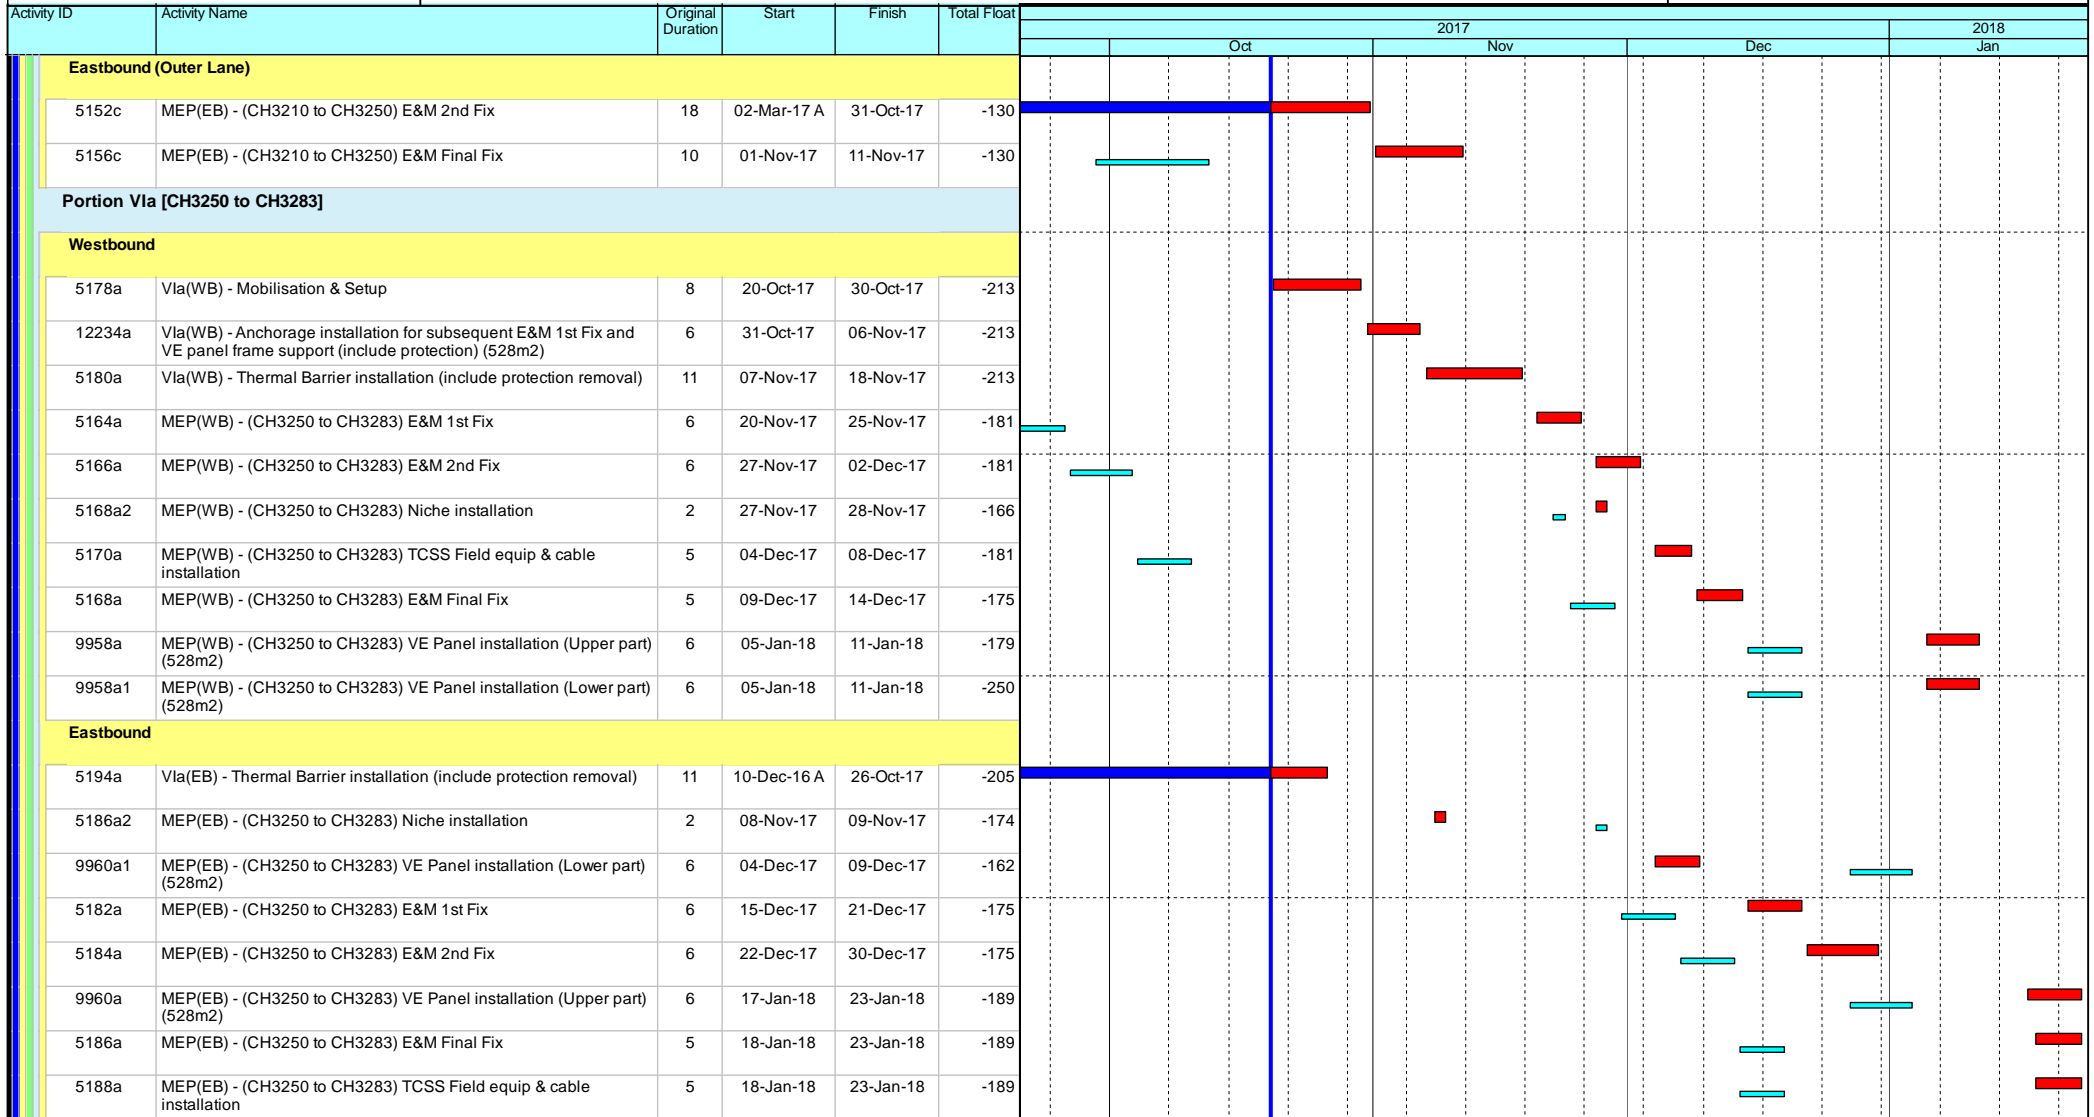

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 15 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

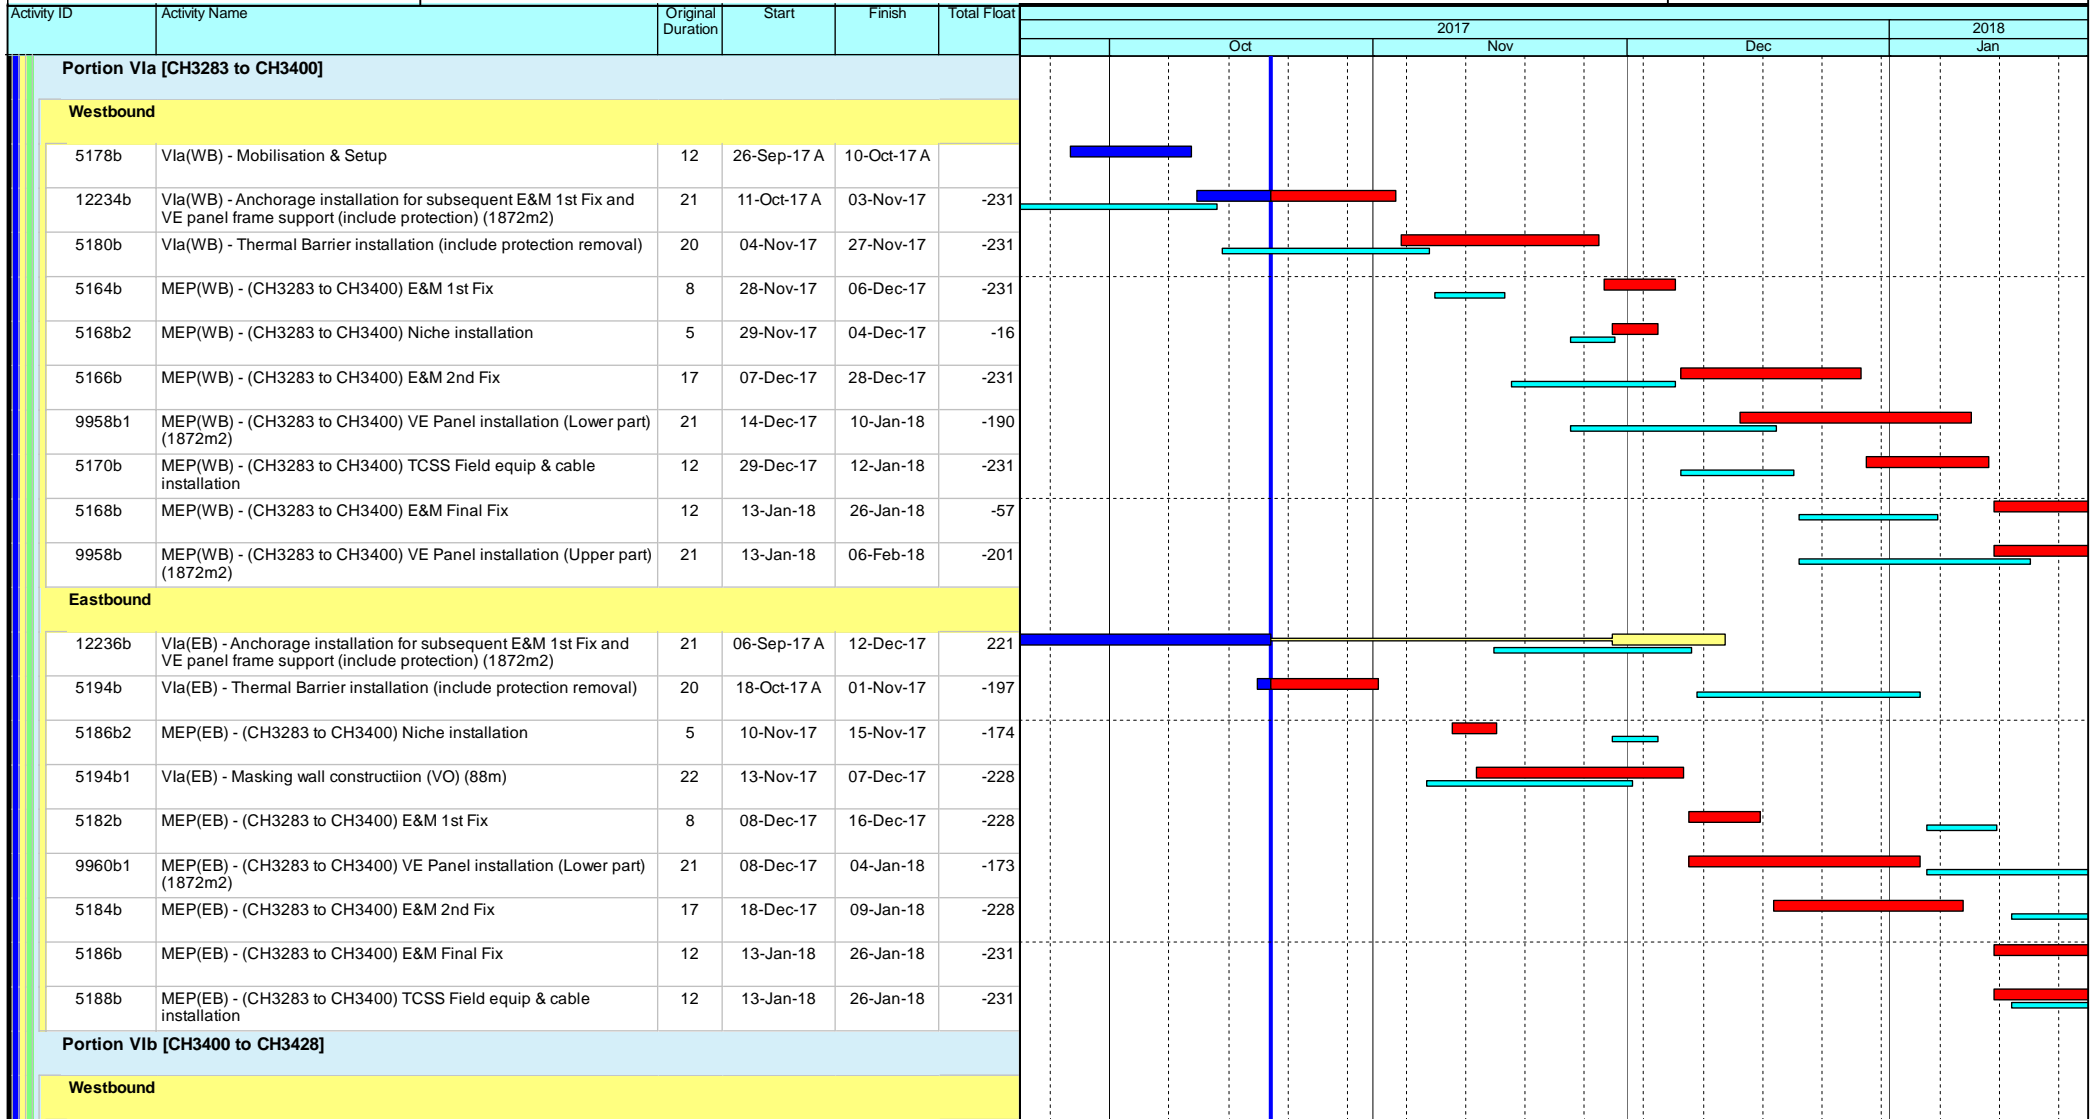

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING

Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 16 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017				2018
						Oct	Nov	Dec	Jan	
5200b9	MEP(WB) - (CH3400 to CH3428) Niche installation	2	18-Sep-17 A	20-Sep-17 A						
12238b1	Vib(WB) - Anchorage installation for subsequent E&M 1st Fix and VE Panel frame support (include protection) (336m2)	4	20-Oct-17	24-Oct-17	-199					
5212b1	Vib(WB) - Thermal Barrier installation (include protection removal)	10	25-Oct-17	06-Nov-17	-199					
5196b1	MEP(WB) - (CH3400 to CH3428) E&M 1st Fix	6	07-Nov-17	13-Nov-17	-199					
5198b1	MEP(WB) - (CH3400 to CH3428) E&M 2nd Fix	6	14-Nov-17	20-Nov-17	-153					
5202b1	MEP(WB) - (CH3400 to CH3428) TCSS Field equip & cable installation	6	08-Dec-17	14-Dec-17	-220					
9962b1a	MEP(WB) - (CH3400 to CH3428) VE Panel installation (Lower part) (336m2)	4	11-Dec-17	14-Dec-17	-162					
5200b1	MEP(WB) - (CH3400 to CH3428) E&M Final Fix	12	15-Dec-17	30-Dec-17	-174					
9962b1	MEP(WB) - (CH3400 to CH3428) VE Panel installation (Upper part) (336m2)	4	02-Jan-18	05-Jan-18	-174					
Eastbound										
5218b9	MEP(EB) - (CH3400 to CH3428) Niche installation	2	18-Sep-17 A	20-Sep-17 A						
5226b1a	Vib(EB) - Masking wall construction (VO) (28m)	14	26-Oct-17	11-Nov-17	-228					
5226b1	Vib(EB) - Thermal Barrier installation (include protection removal)	10	04-Nov-17	15-Nov-17	-137					
5214b1	MEP(EB) - (CH3400 to CH3428) E&M 1st Fix	6	16-Nov-17	22-Nov-17	-22					
5216b1	MEP(EB) - (CH3400 to CH3428) E&M 2nd Fix	6	23-Nov-17	29-Nov-17	-22					
9964b1	MEP(EB) - (CH3400 to CH3428) VE Panel installation (Upper part) (4800m2)	4	15-Dec-17	19-Dec-17	-162					
9964b1a	MEP(EB) - (CH3400 to CH3428) VE Panel installation (Lower part) (4800m2)	4	15-Dec-17	19-Dec-17	-162					
5218b1	MEP(EB) - (CH3400 to CH3428) E&M Final Fix	12	12-Jan-18	25-Jan-18	-56					
5220b1	MEP(EB) - (CH3400 to CH3428) TCSS Field equip & cable installation	6	19-Jan-18	25-Jan-18	-56					
Portion Vib [CH3428 to CH3625]										
Westbound										
5196b2	MEP(WB) - (CH3428 to CH3625) E&M 1st Fix	12	07-Dec-16 A	09-Nov-17	-220					
5198b2	MEP(WB) - (CH3428 to CH3625) E&M 2nd Fix	12	15-Mar-17 A	09-Nov-17	-220					
5202b2	MEP(WB) - (CH3428 to CH3625) TCSS Field equip & cable installation	12	18-Mar-17 A	09-Nov-17	-214					

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 17 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

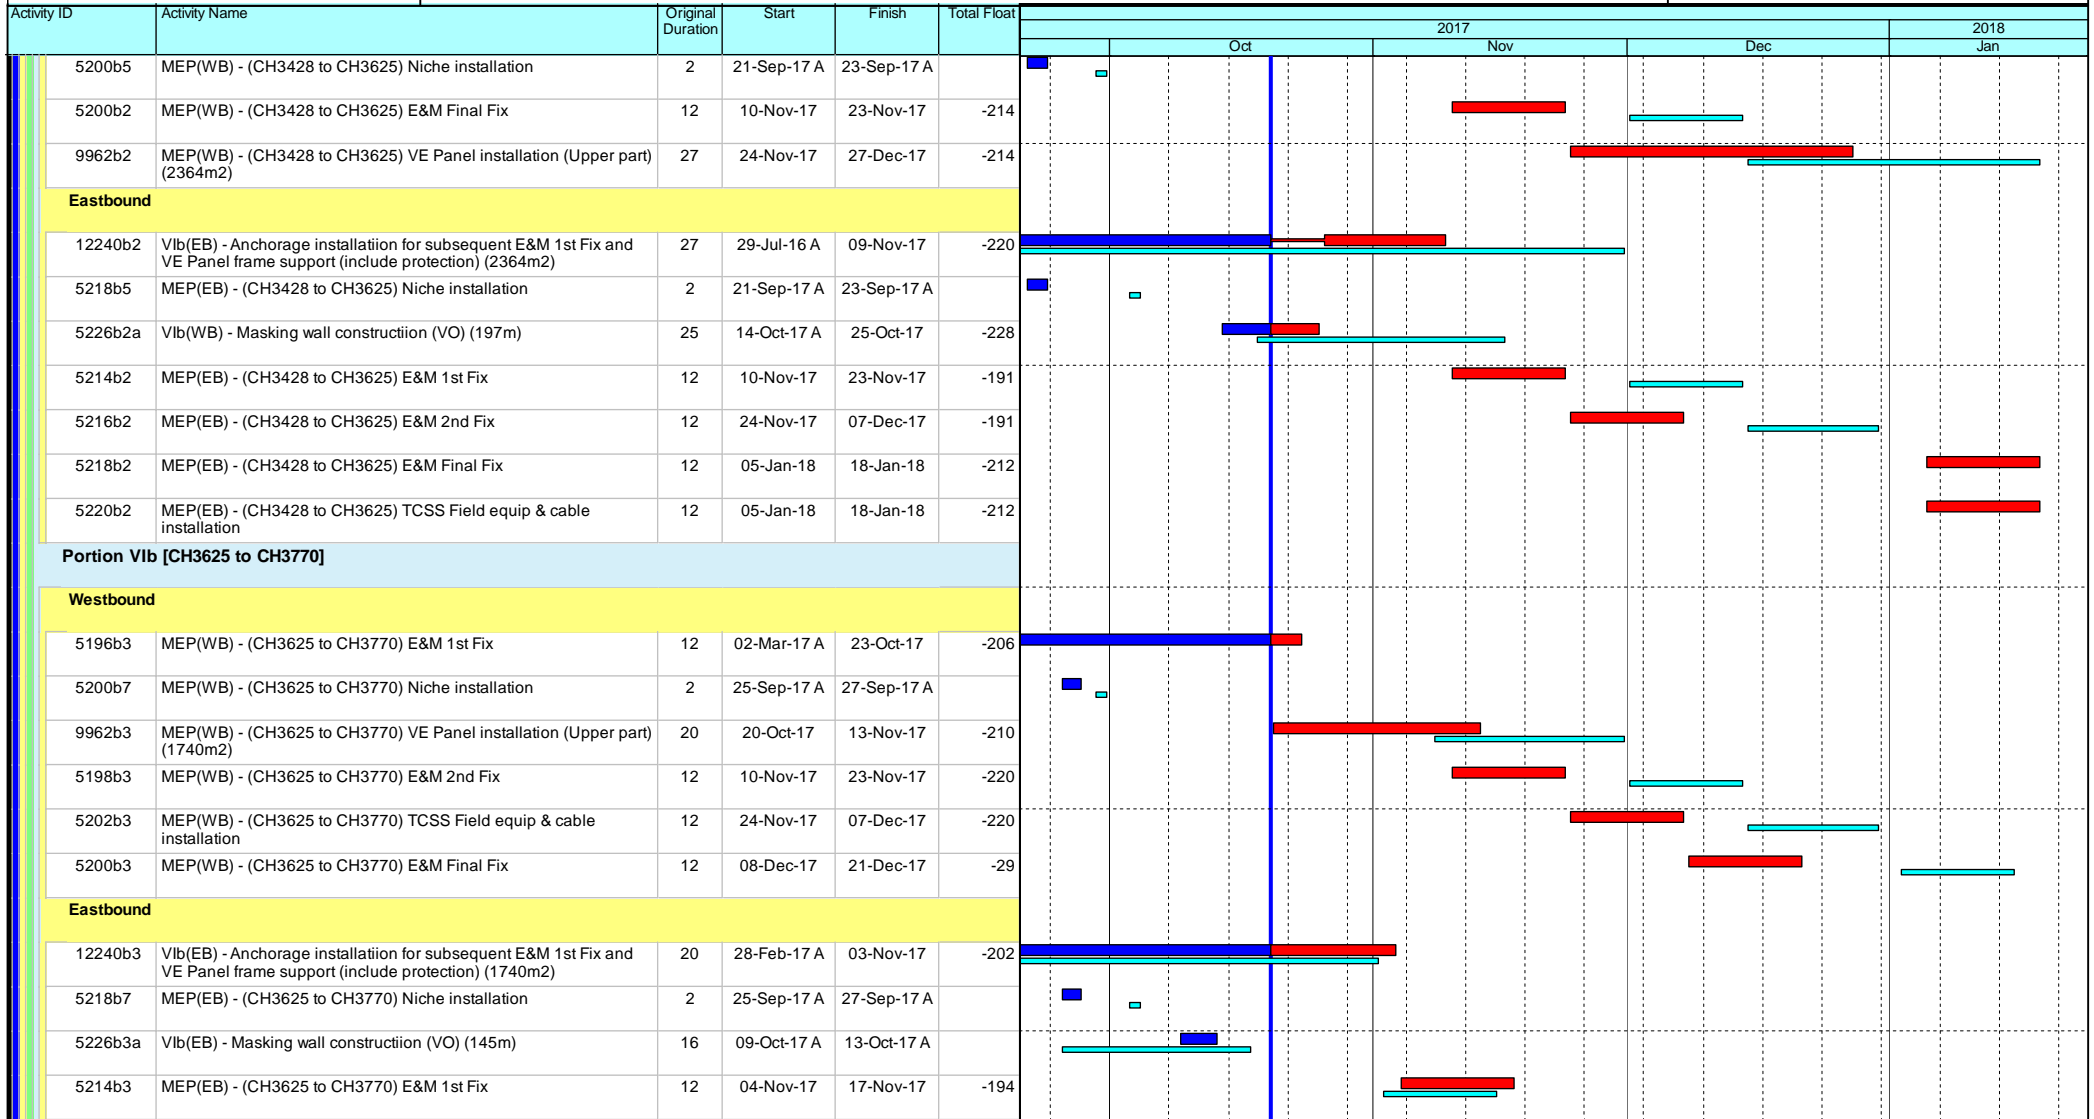

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING


Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 18 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

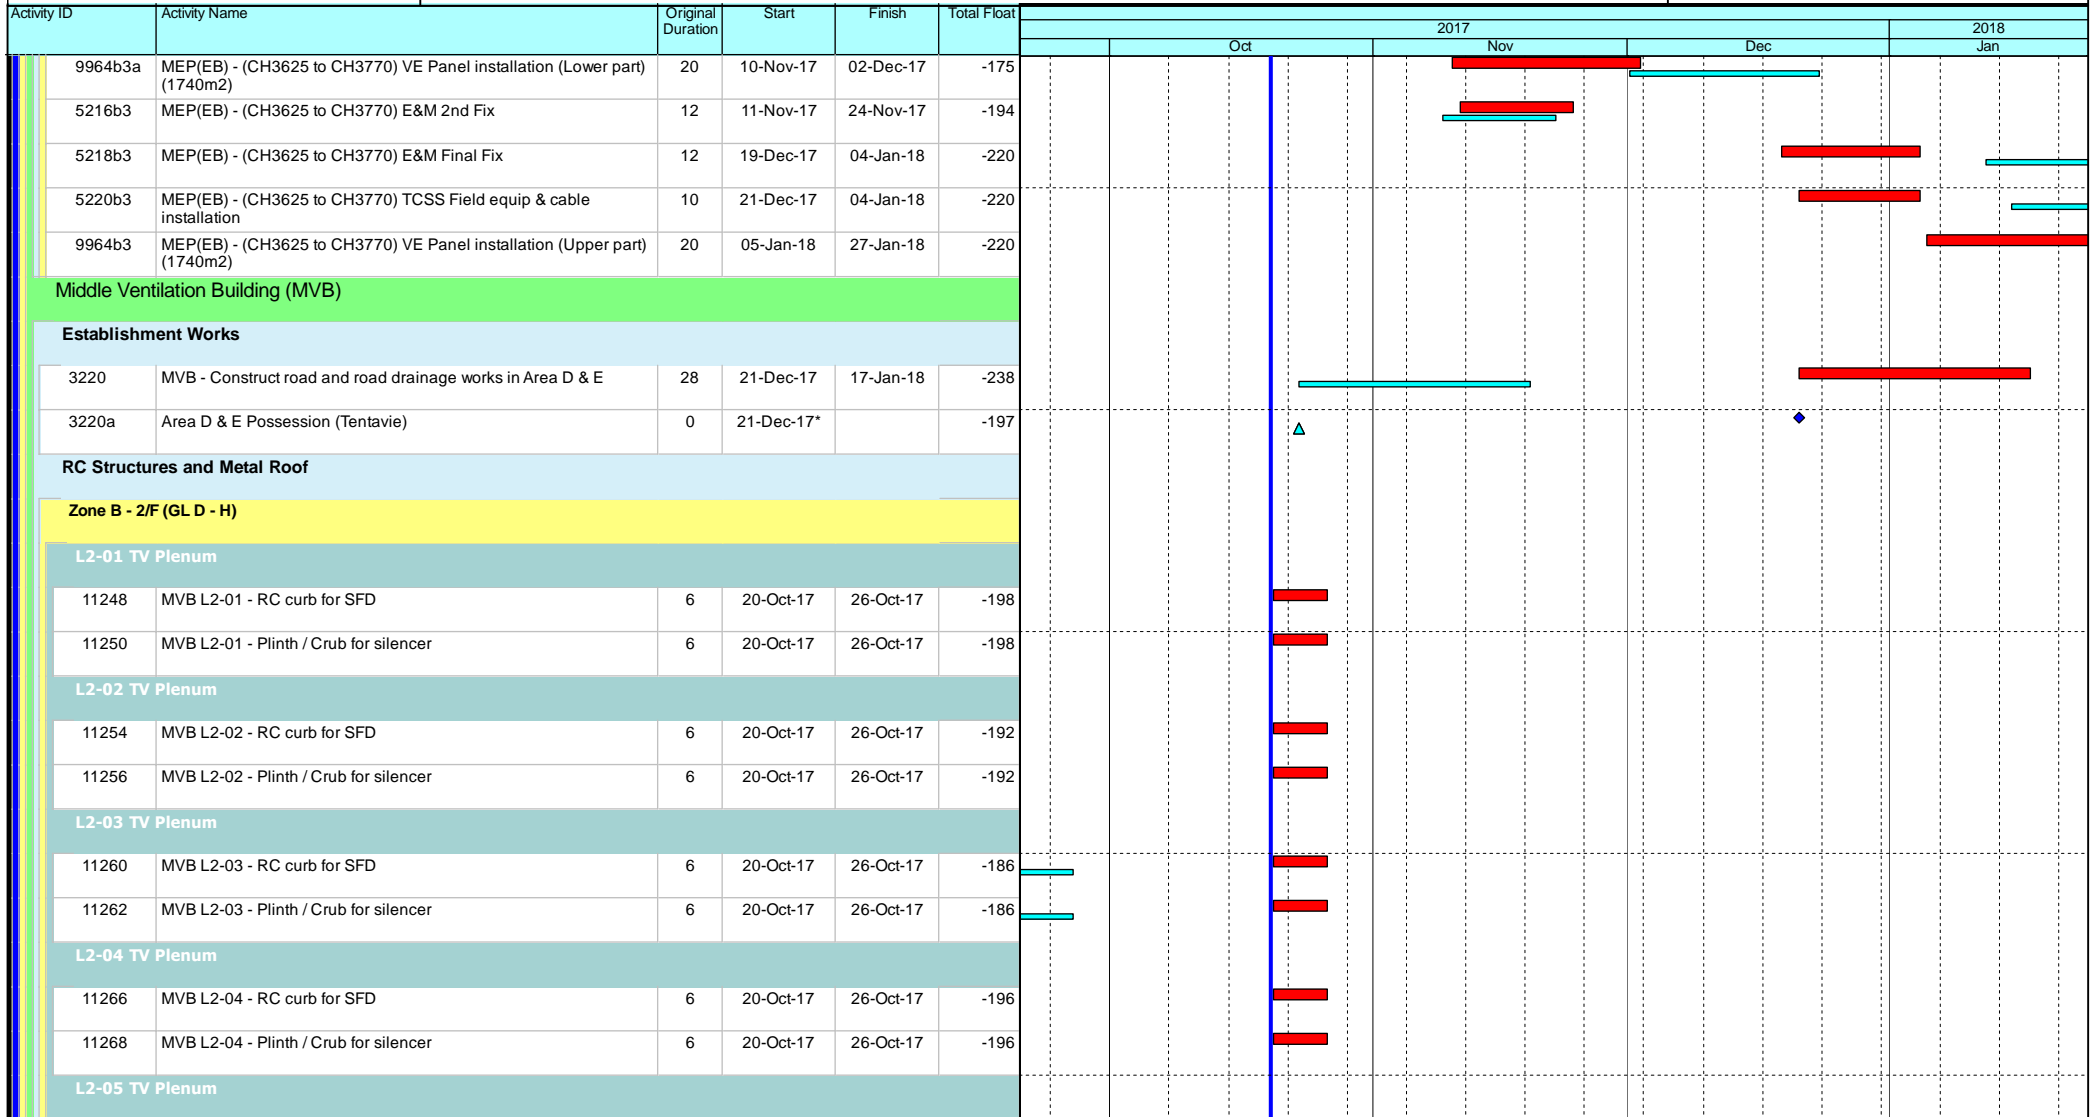

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 19 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

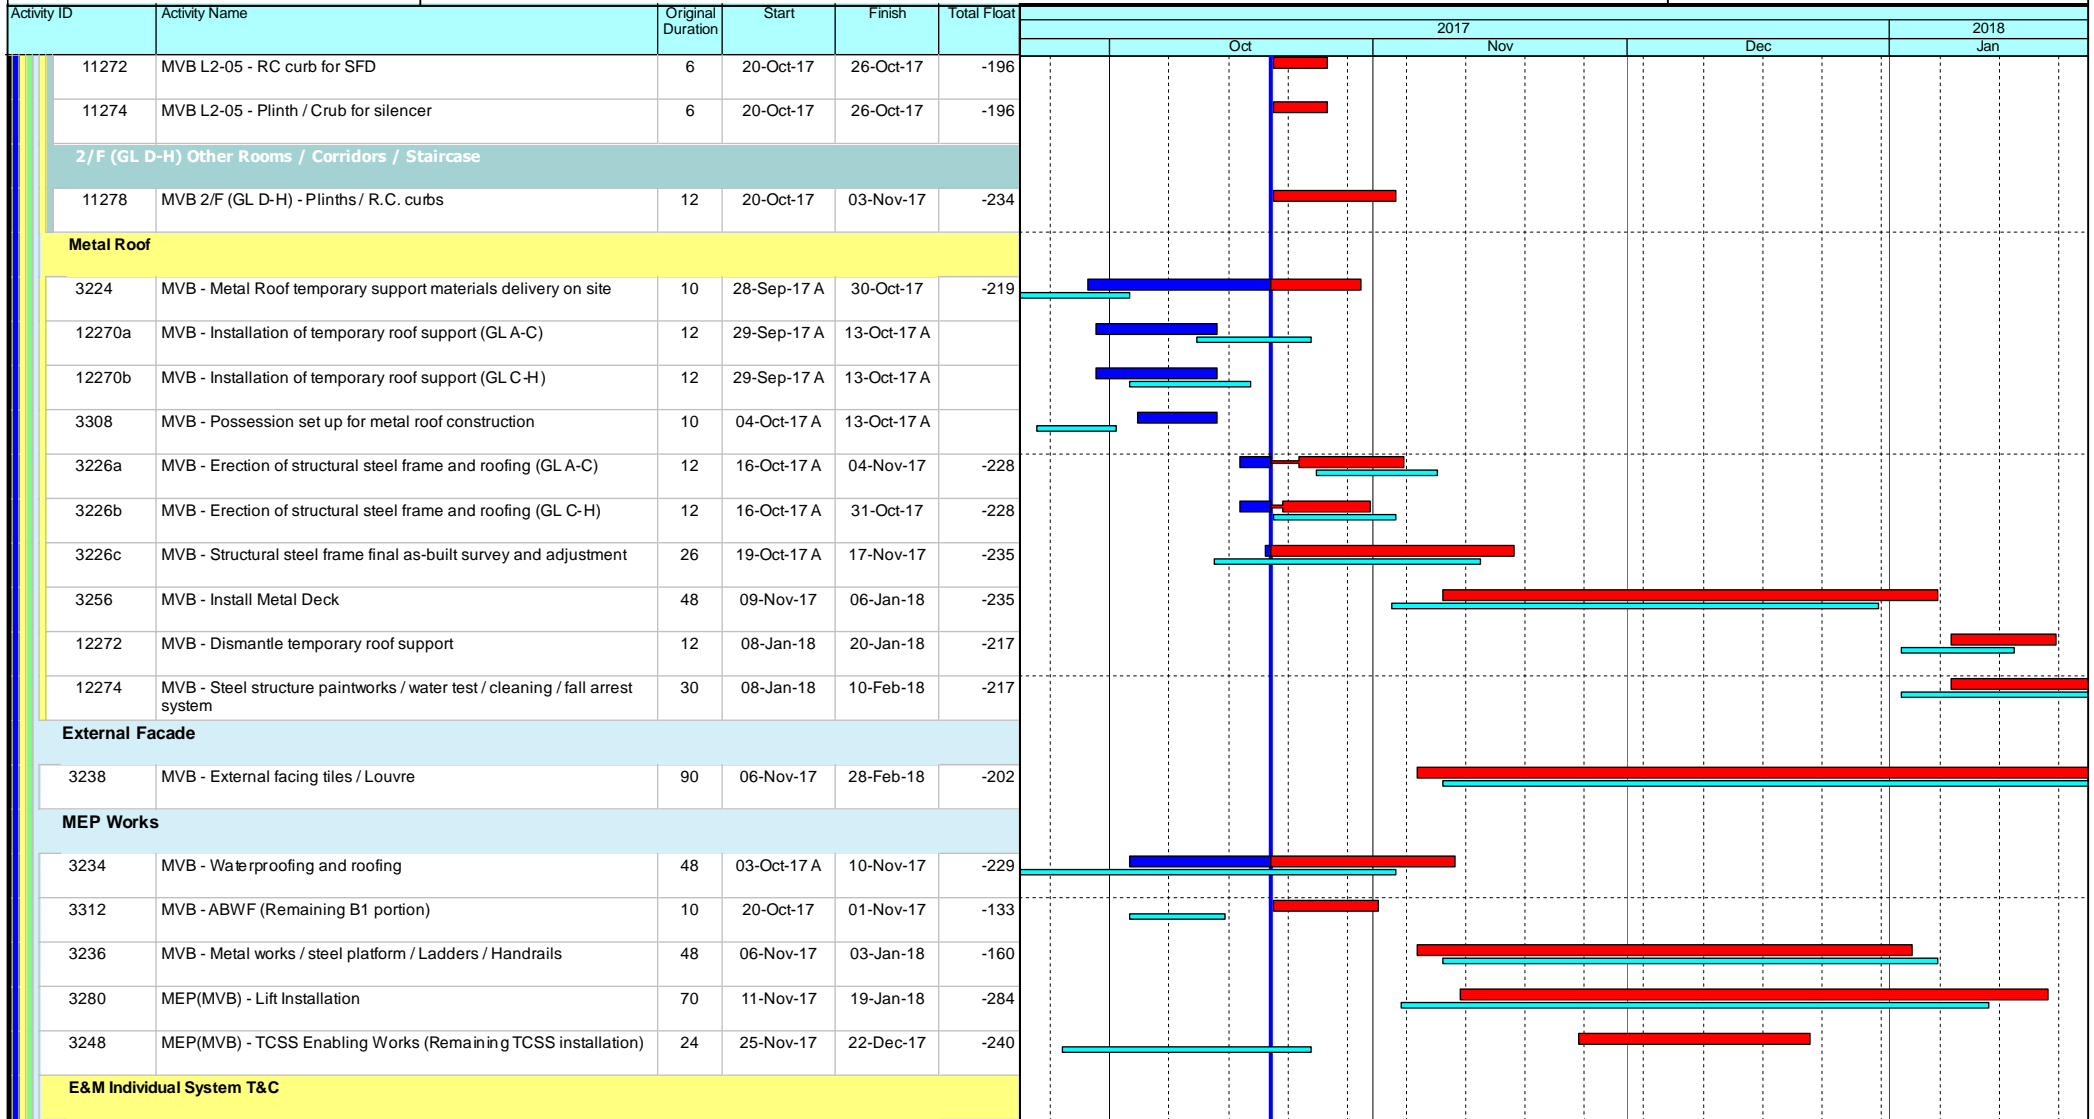

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 20 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

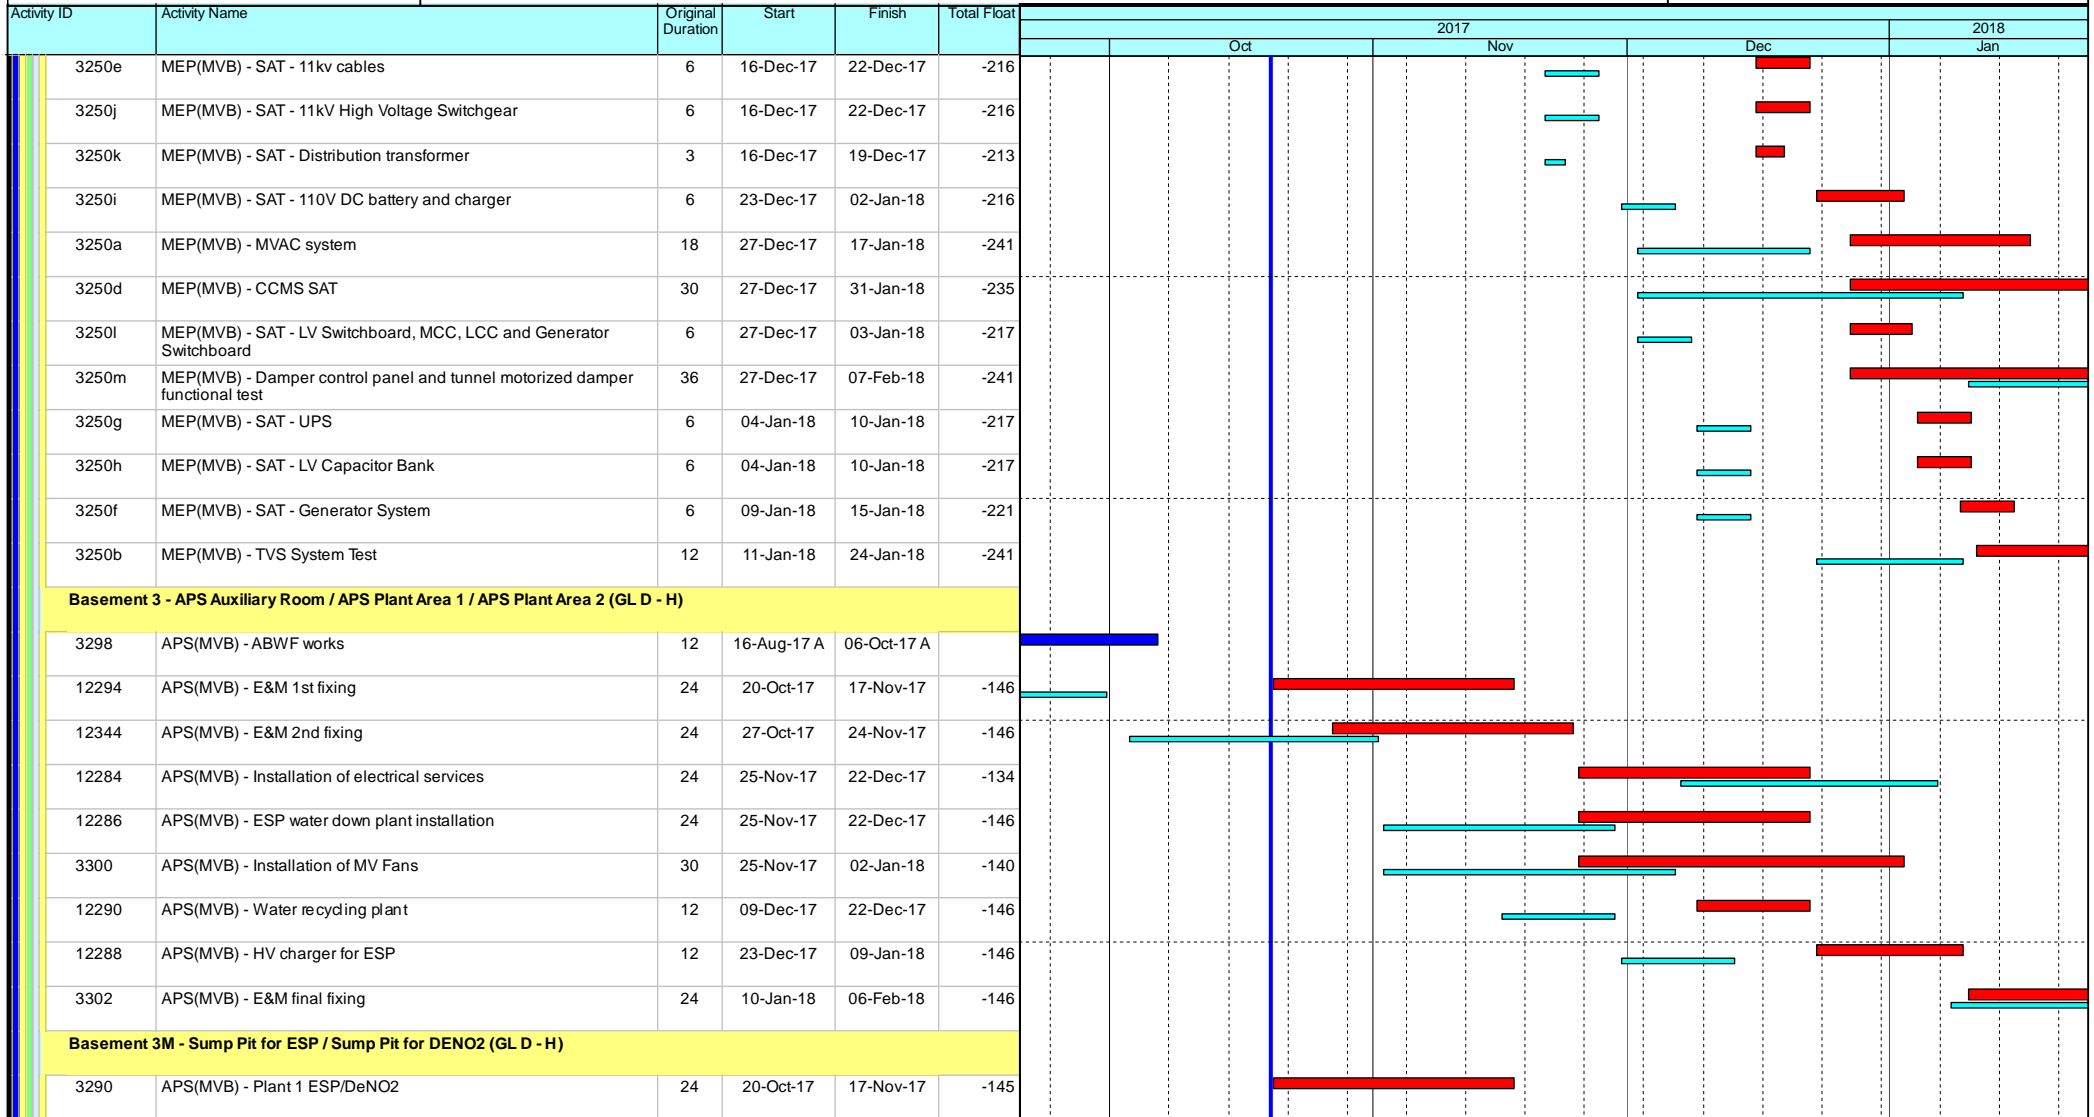

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 21 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

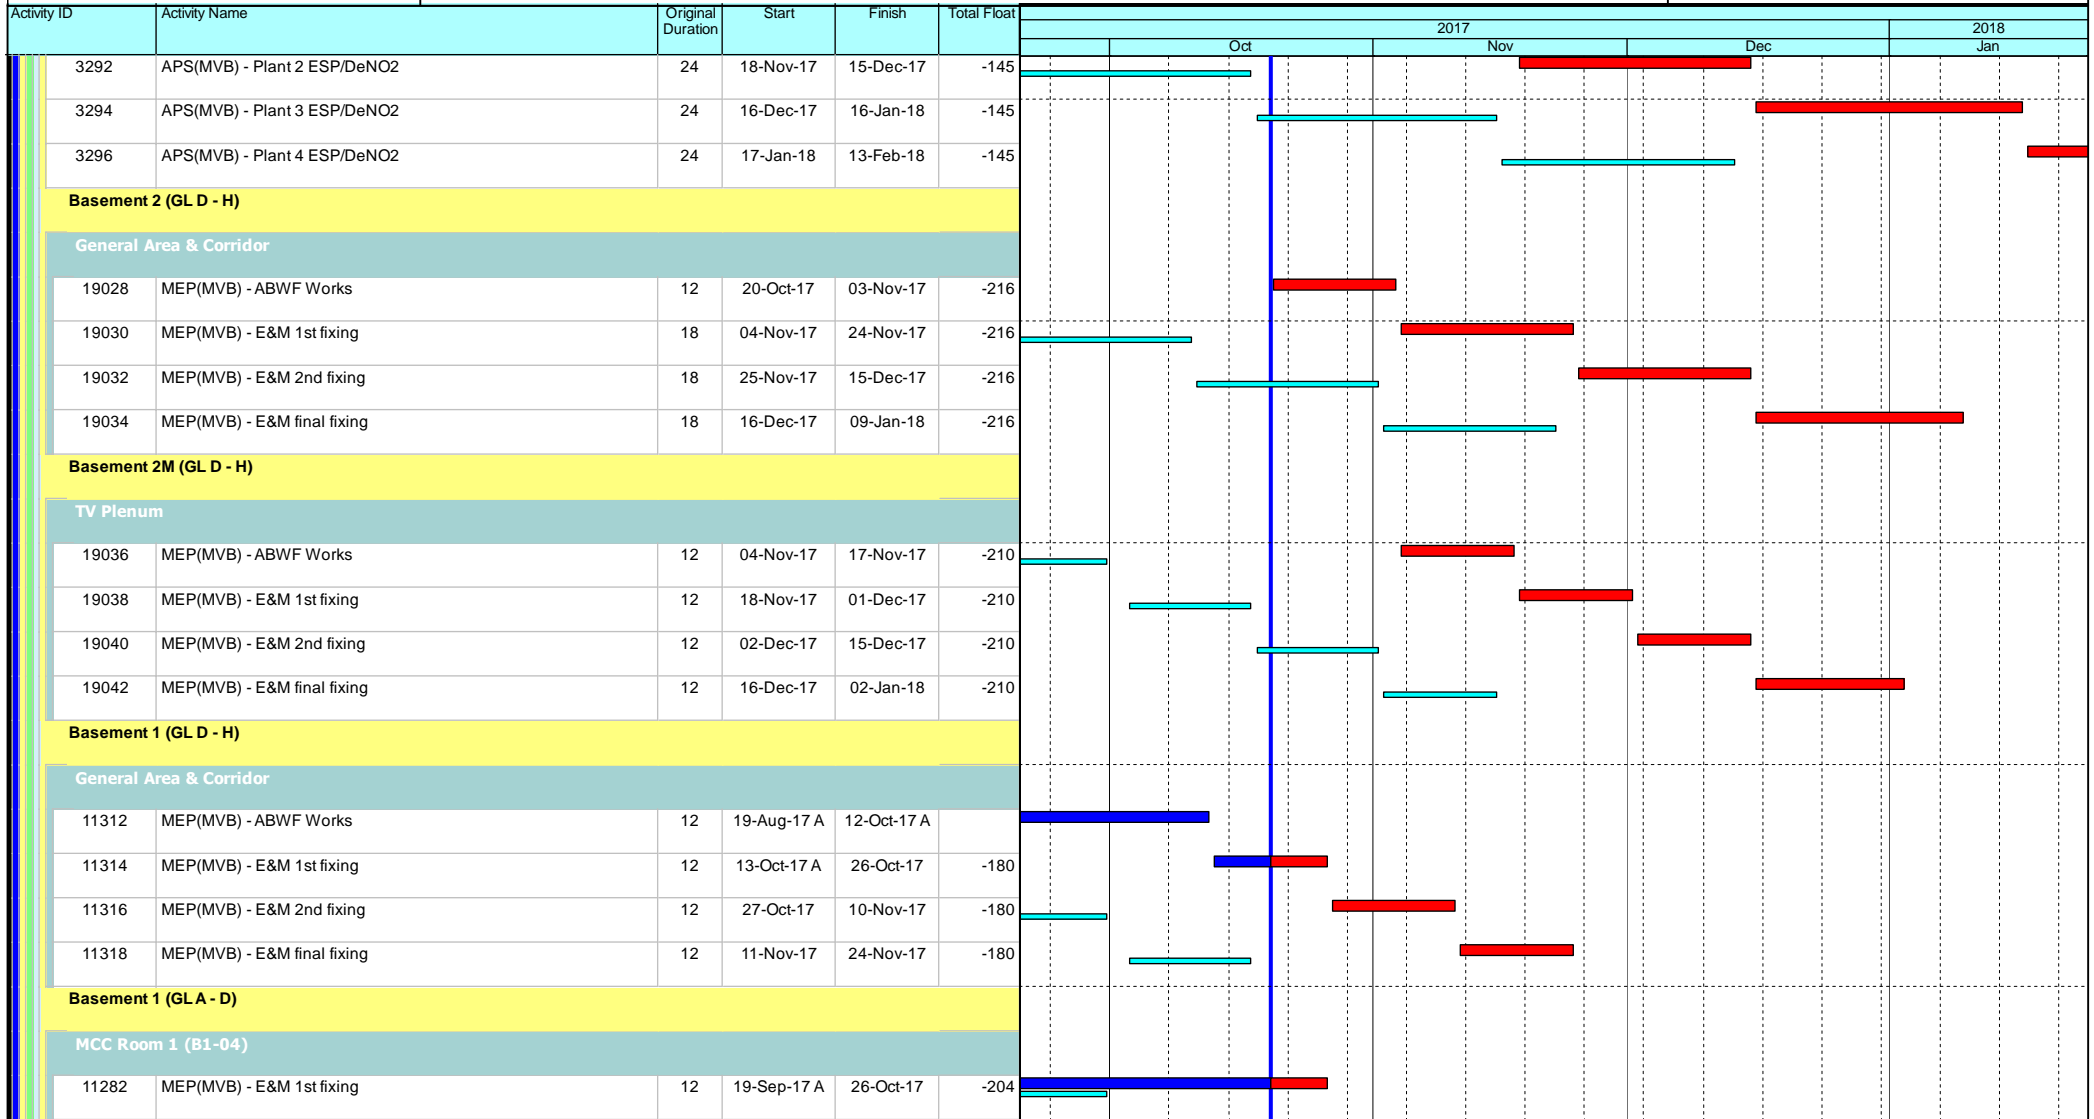

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 22 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

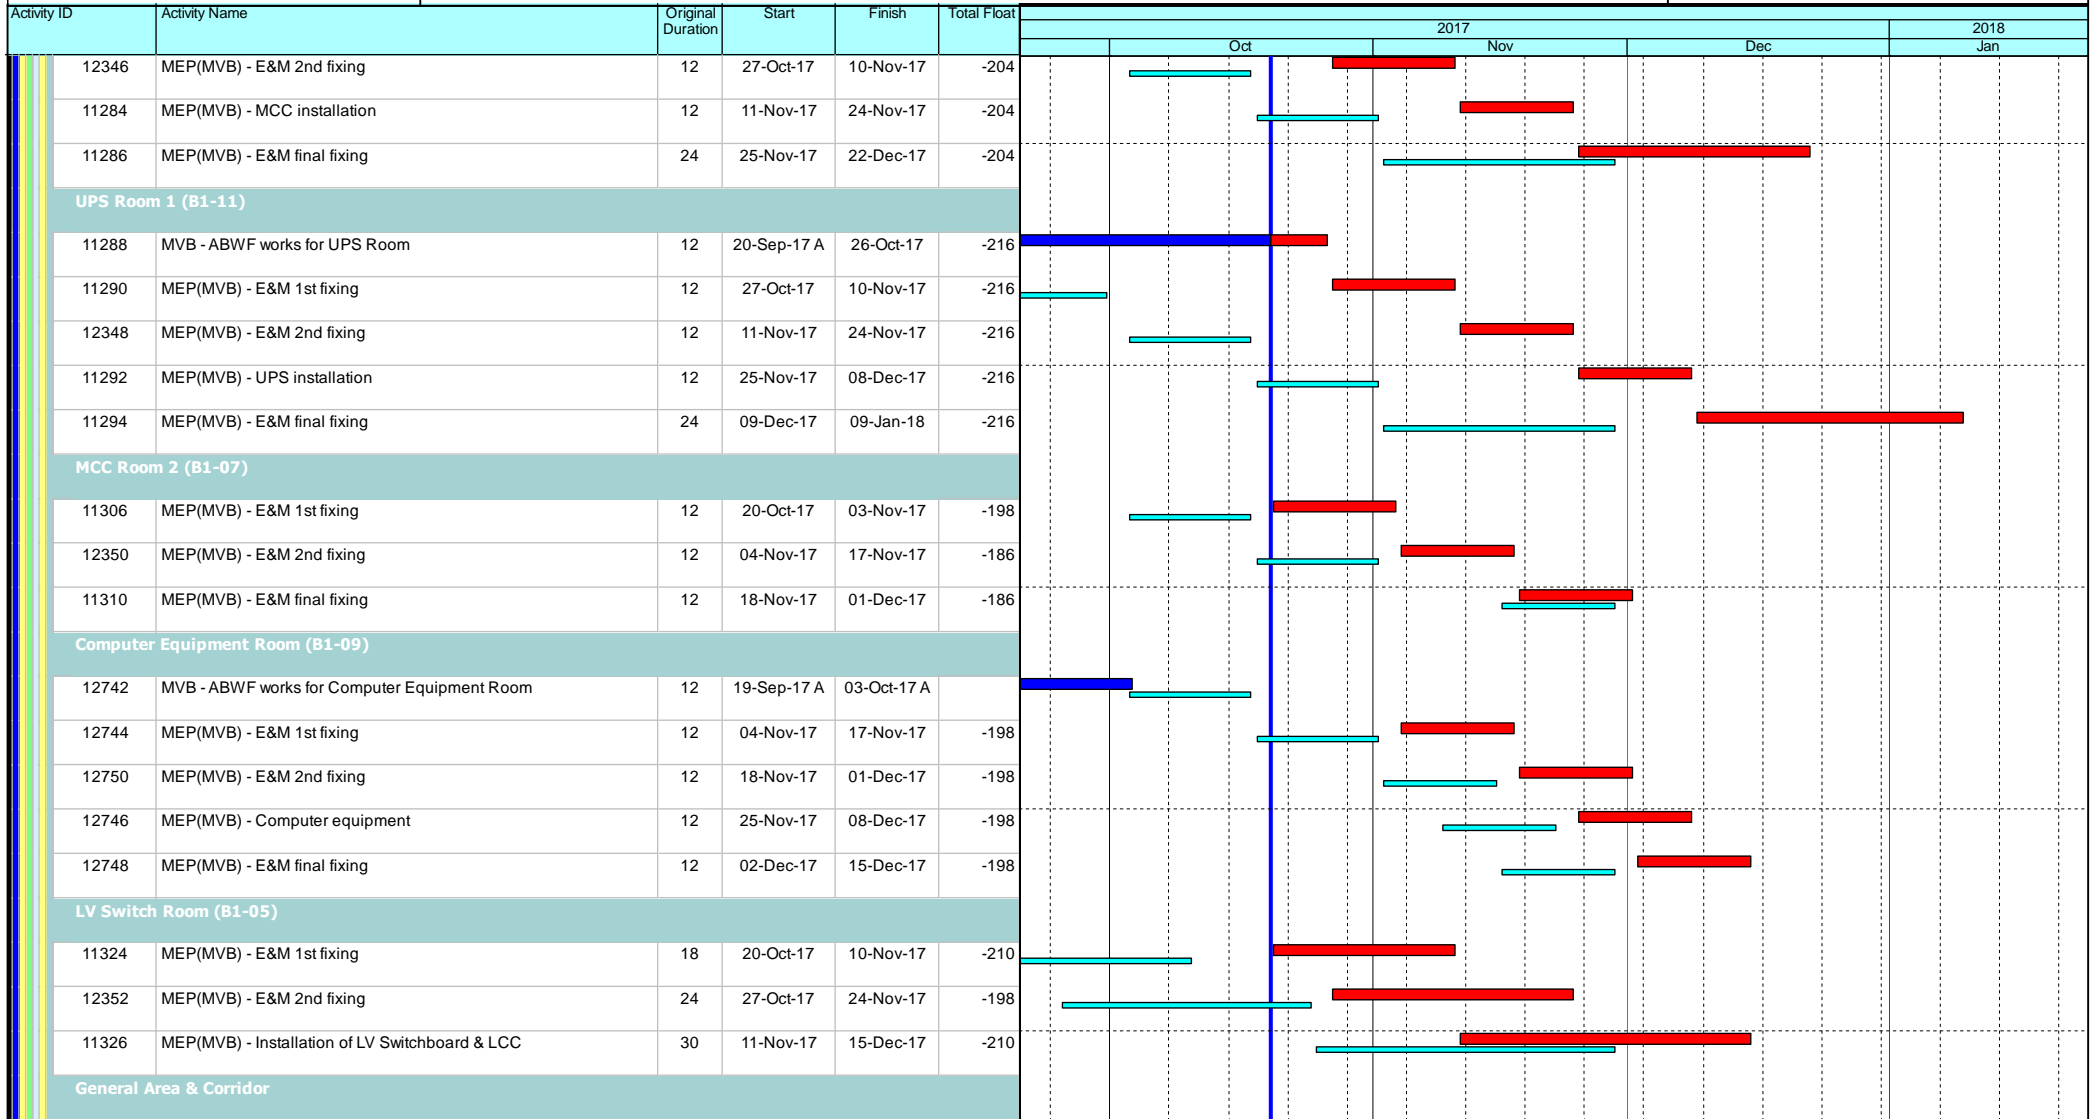

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 23 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

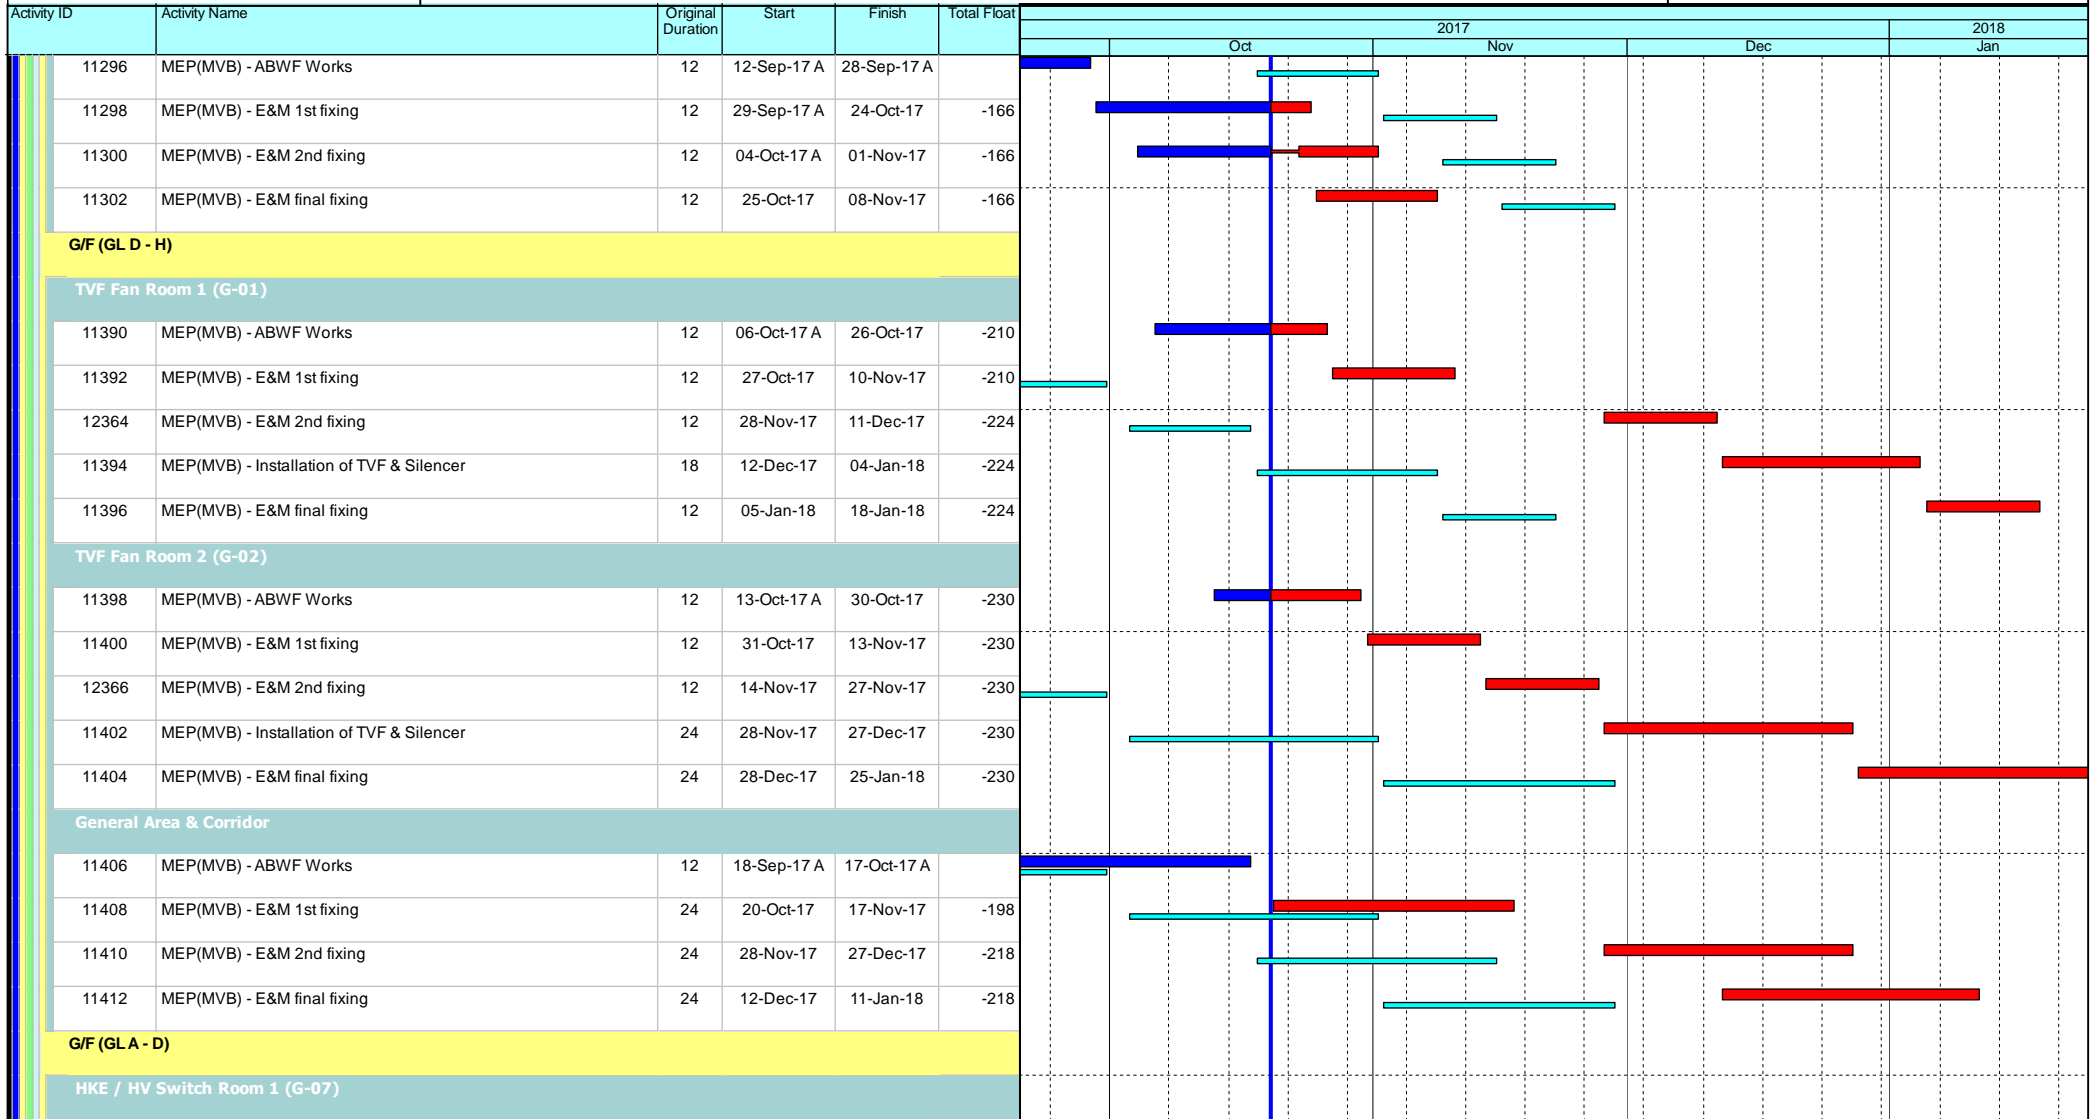

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 24 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

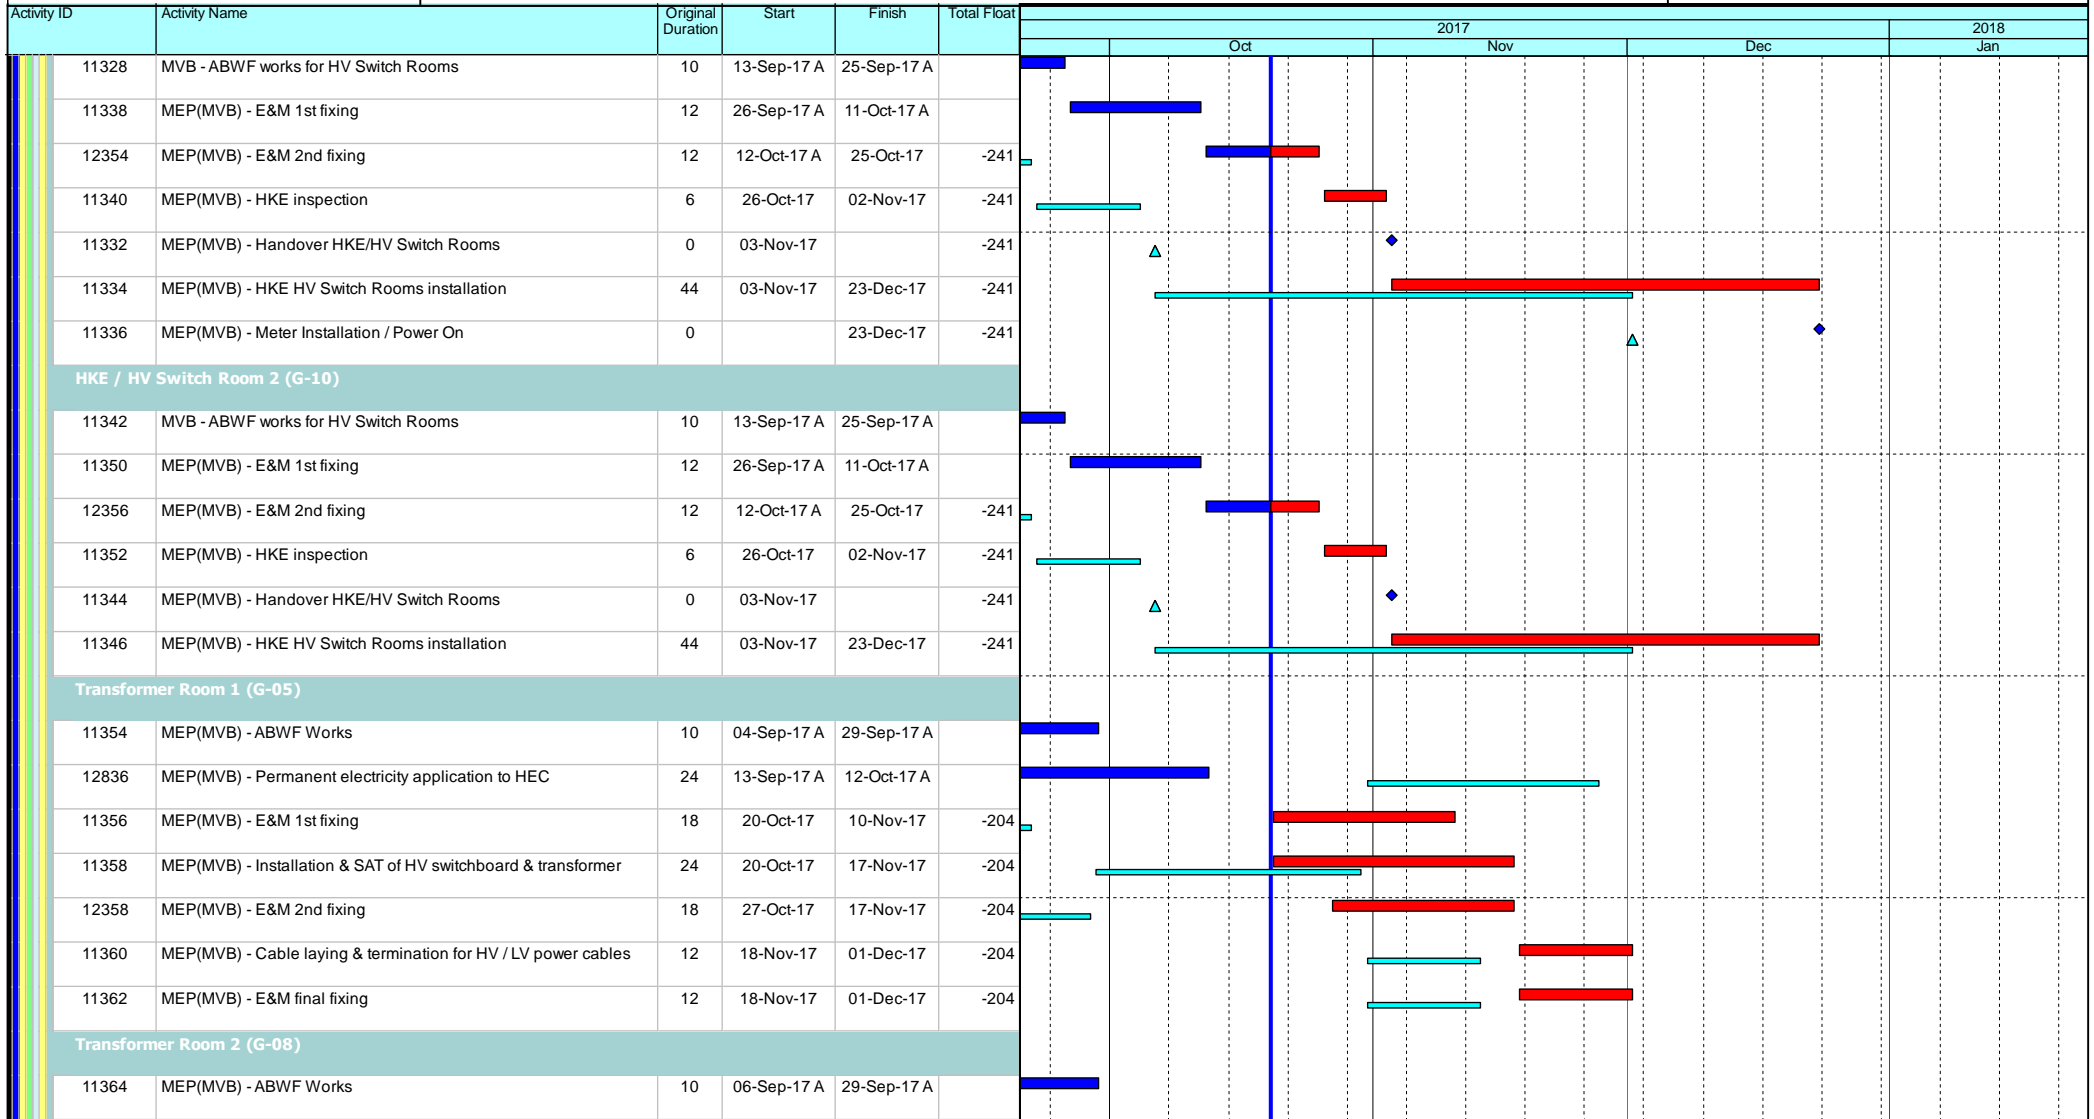

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING


Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 25 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

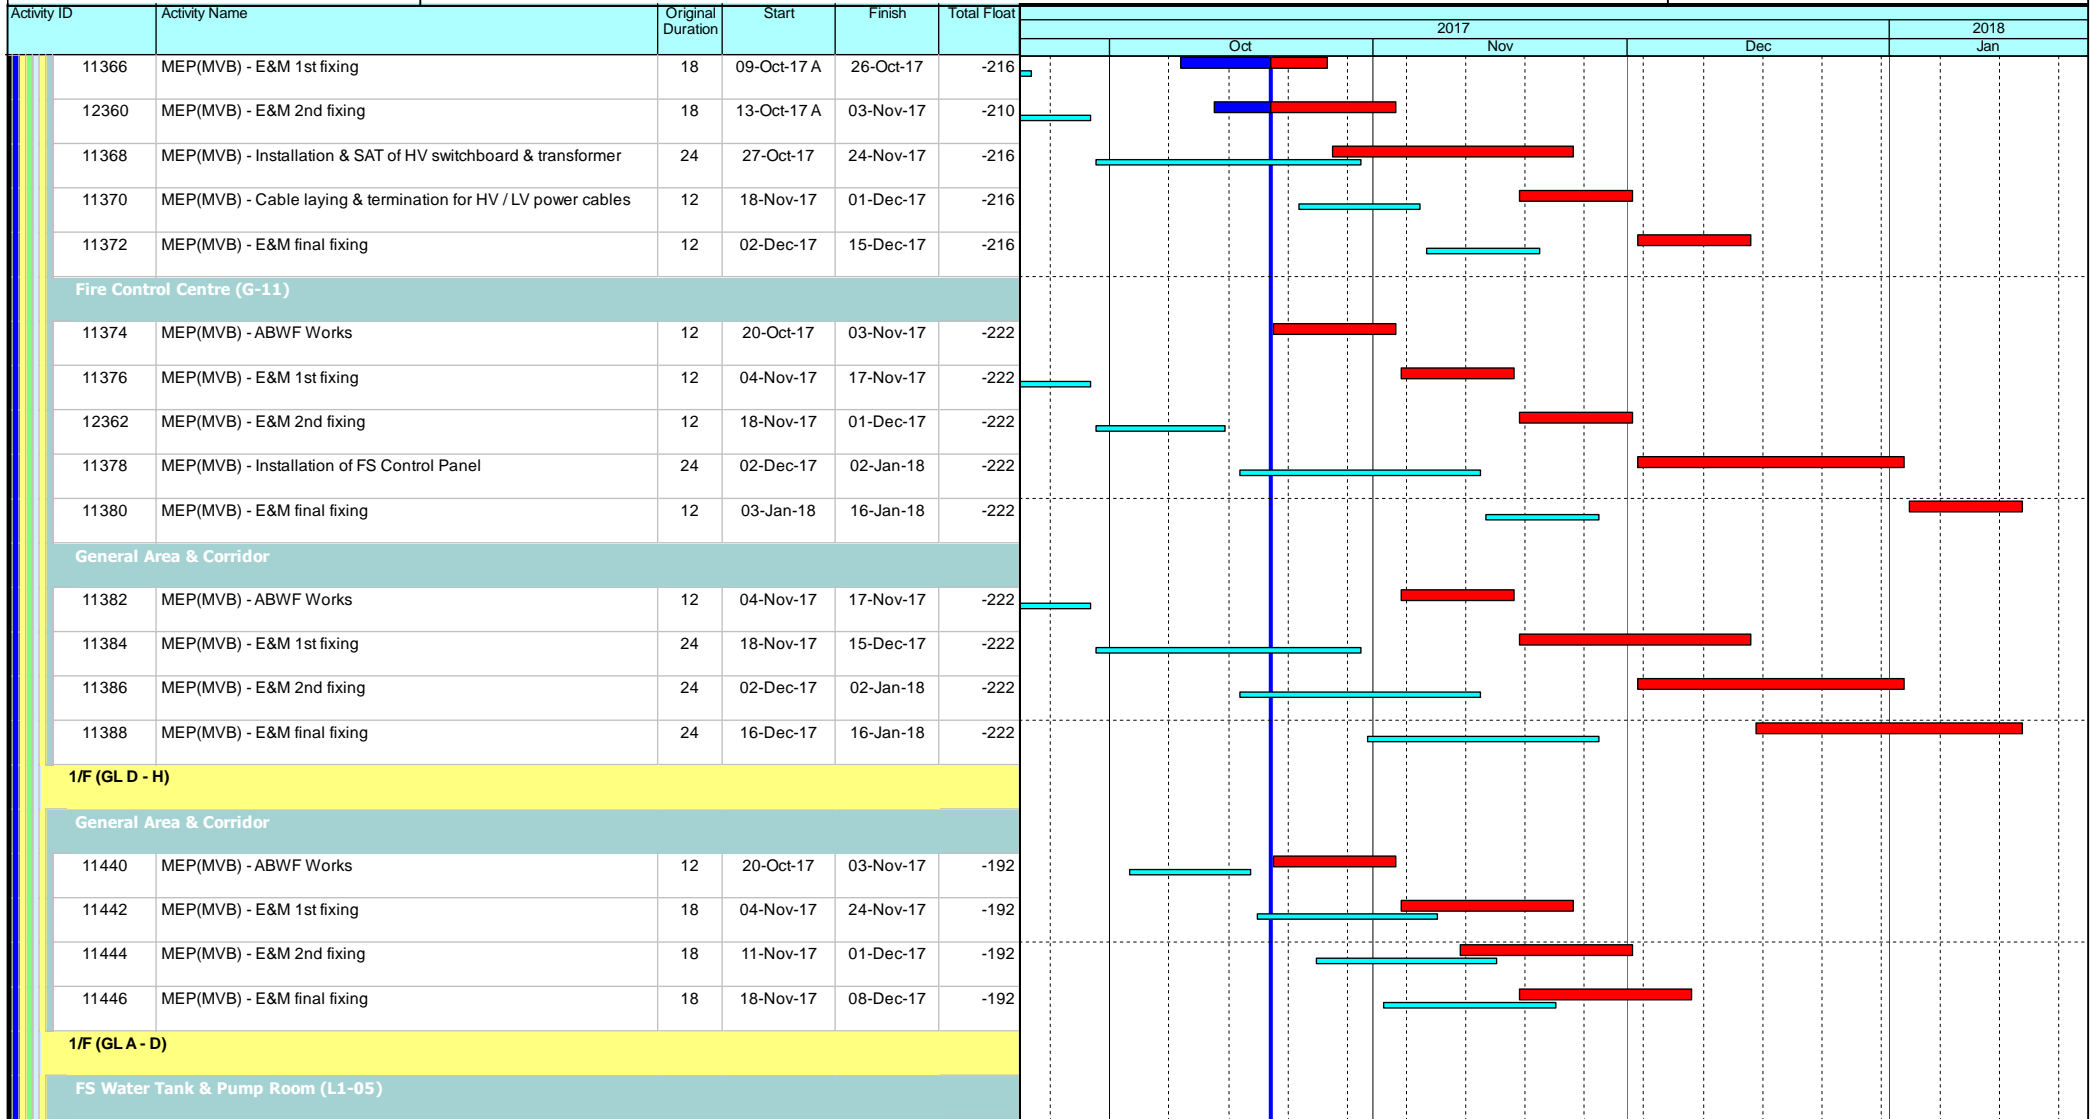

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 26 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

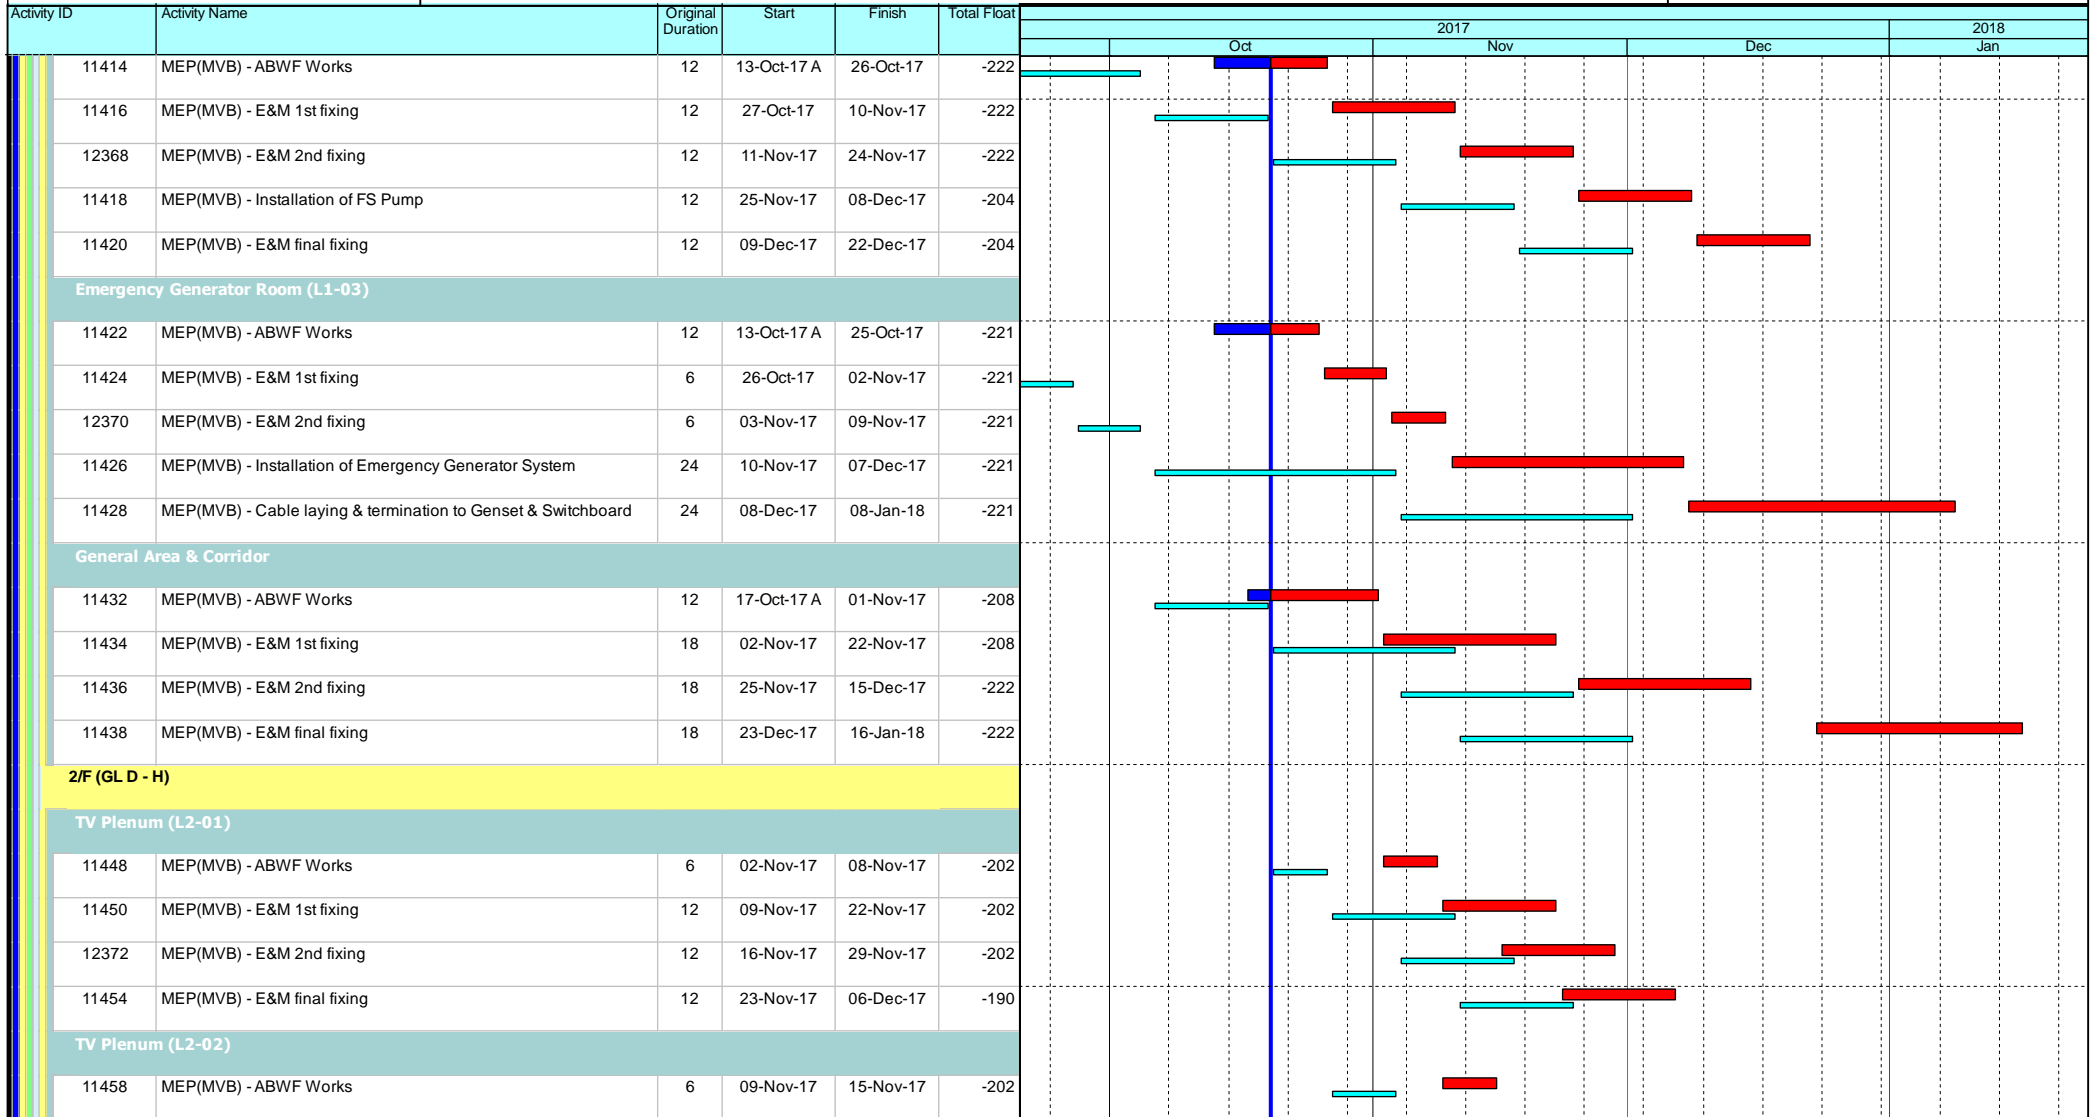

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 27 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

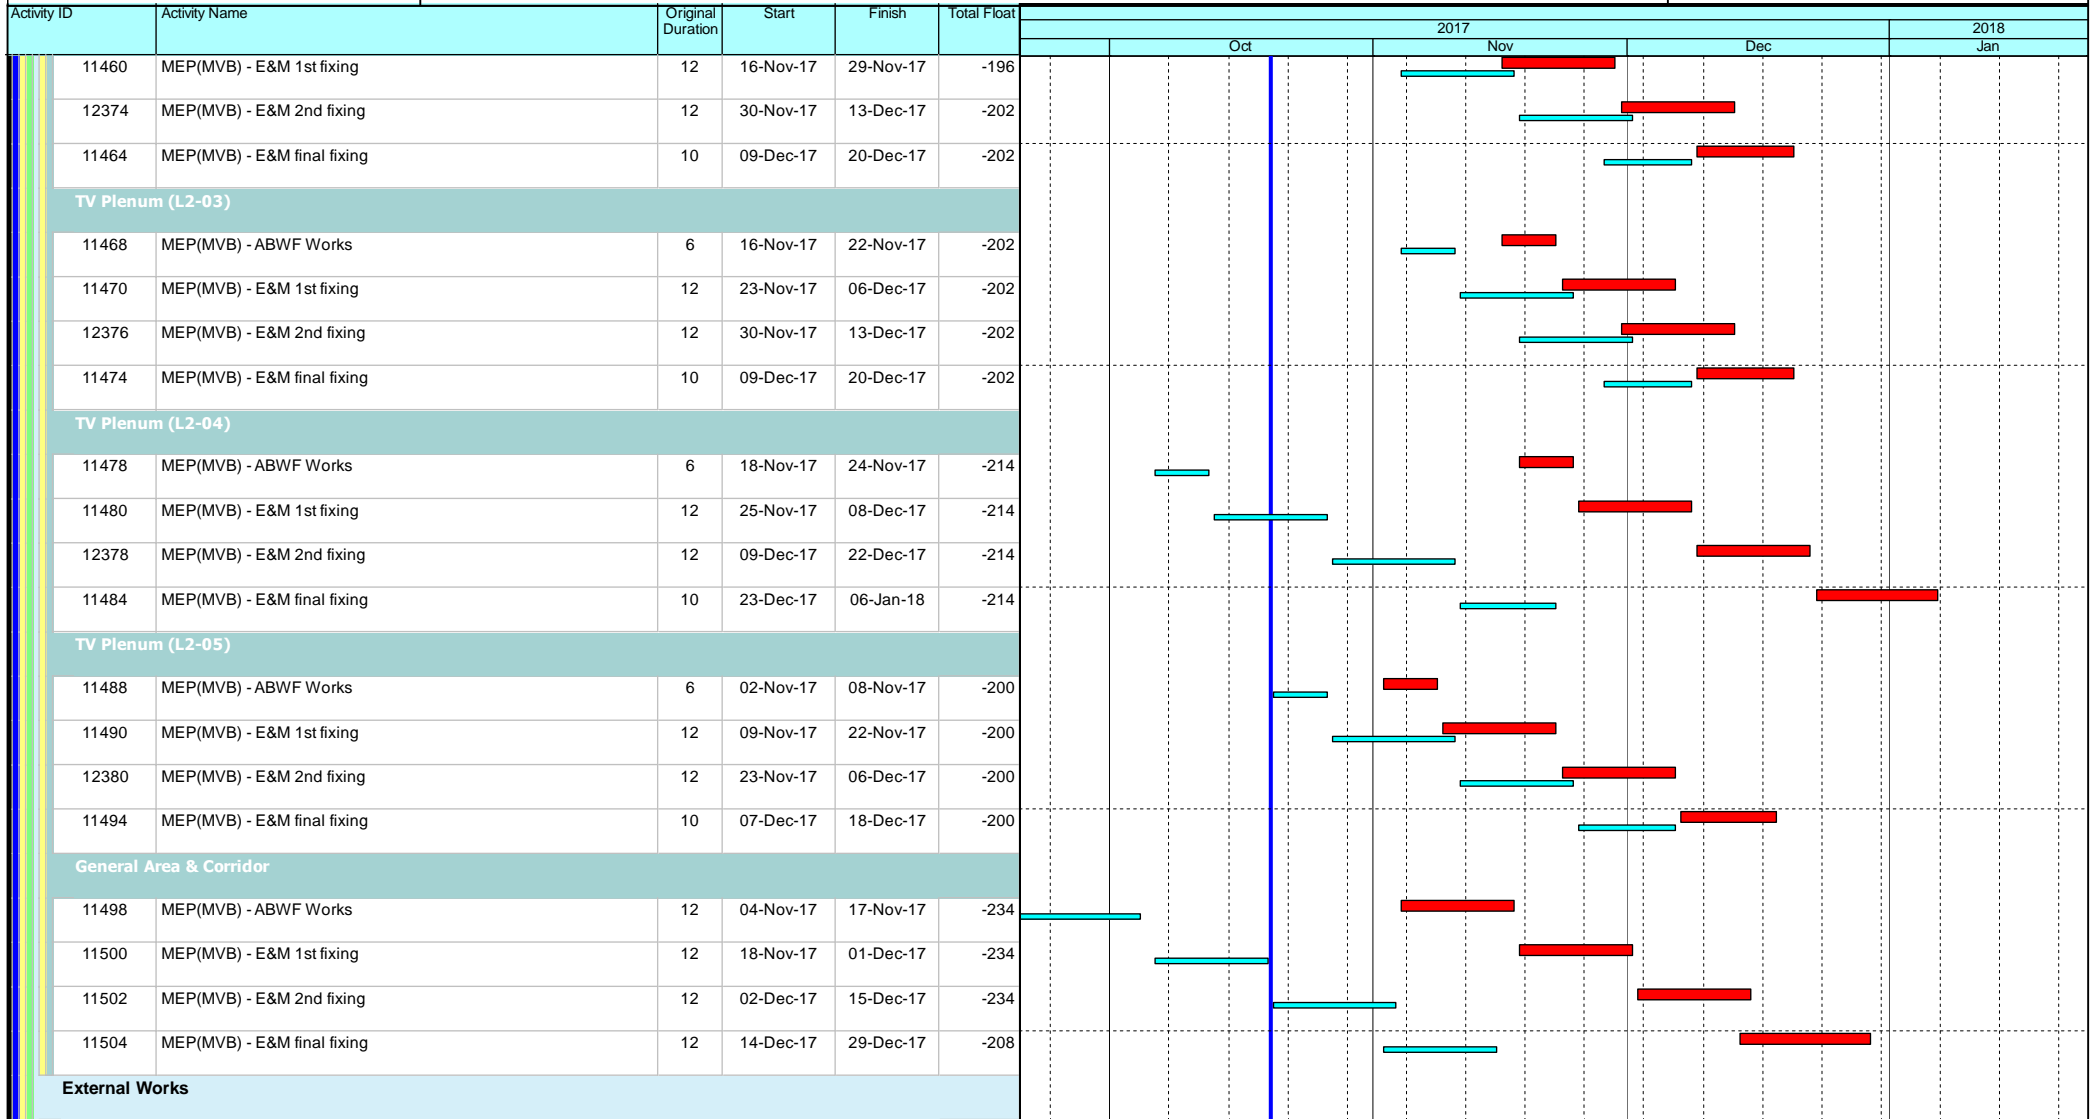

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING

Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 28 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017				2018											
						Oct		Nov	Dec	Jan											
3254	MVB - Road and drainage works (EVA)	30	08-Jan-18	10-Feb-18	-235																
3258	MVB - External concrete pavement	42	08-Jan-18	03-Mar-18	-235																
3260	MVB - External Fence Wall	42	15-Jan-18	10-Mar-18	-211																
Portion IVa Road Surface Area																					
19044	Access date for Portion IVa Road Surface Area (C3 Interface Contractor) (tentative)	0	01-Nov-17*		-200																
19046	TCSS equipment installation & cabling (Tentative)	96	01-Nov-17	02-Mar-18	-200																
19050	Lighting equipment installation & cabling (Tentative)	48	01-Nov-17	28-Dec-17	-42																
19052	Lighting equipment Testing & Commissioning (Tentative)	24	29-Dec-17	26-Jan-18	-42																
Satellite Control Point 3																					
SCP3																					
3758	SCP3 - Construct SCP RC Structures	24	17-Jul-17 A	26-Oct-17	-242																
3772	SCP3 - External Works	30	07-Aug-17 A	26-Oct-17	-224																
3760	SCP3 - ABWF Works	18	27-Oct-17	17-Nov-17	-242																
3762	MEP(SCP3) - E&M 1st Fix	12	18-Nov-17	01-Dec-17	-242																
3764	MEP(SCP3) - E&M 2nd Fix	12	30-Nov-17	13-Dec-17	-242																
10110	MEP(SCP3) - TCSS Enabling Works (Remaining TCSS installation)	12	02-Dec-17	15-Dec-17	-210																
3766	MEP(SCP3) - E&M Final Fix	12	12-Dec-17	27-Dec-17	-242																
3774	SCP3 - Metal works / Glazing / Louver / Handrails	12	28-Dec-17	11-Jan-18	-242																
3768	MEP(SCP3) - E&M Individual System T&C	12	12-Jan-18	25-Jan-18	-242																
East Ventilation Building (EVB - related)																					
Tunnel Section (EVB-related)																					
Portion VIc [CH3770 to CH3800]																					
Westbound																					
5200c2	MEP(WB) - (CH3770 to CH3800) Niche installation	2	20-Oct-17	21-Oct-17	4																

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING

Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 29 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017				2018
						Oct	Nov	Dec	Jan	
5196c	MEP(WB) - (CH3770 to CH3800) E&M 1st Fix	6	14-Nov-17	20-Nov-17	-199					
9962c	MEP(WB) - (CH3770 to CH3800) VE Panel installation (Upper part) (450m2)	5	14-Nov-17	18-Nov-17	-210					
5202c	MEP(WB) - (CH3770 to CH3800) E&M 2nd Fix	12	21-Nov-17	04-Dec-17	-42					
5198c	MEP(WB) - (CH3770 to CH3800) TCSS Field equip & cable installation	5	15-Dec-17	20-Dec-17	-220					
5200c	MEP(WB) - (CH3770 to CH3800) E&M Final Fix	12	21-Dec-17	06-Jan-18	-56					
Eastbound										
5214c	MEP(EB) - (CH3770 to CH3800) E&M 1st Fix	24	14-Apr-17 A	16-Nov-17	-163					
5226c1	Vlc(EB) - Masking wall construction (VO) (30m)	8	02-Oct-17 A	07-Oct-17 A						
9964c1	MEP(EB) - (CH3770 to CH3800) VE Panel installation (Lower part) (450m2)	5	10-Nov-17	15-Nov-17	-207					
5218c2	MEP(EB) - (CH3770 to CH3800) Niche installation	2	10-Nov-17	11-Nov-17	-137					
5220c	MEP(EB) - (CH3770 to CH3800) E&M 2nd Fix	12	17-Nov-17	30-Nov-17	-163					
5216c	MEP(EB) - (CH3770 to CH3800) TCSS Field equip & cable installation	5	17-Nov-17	22-Nov-17	-144					
5218c	MEP(EB) - (CH3770 to CH3800) E&M Final Fix	12	01-Dec-17	14-Dec-17	-163					
9964c	MEP(EB) - (CH3770 to CH3800) VE Panel installation (Upper part) (450m2)	5	15-Dec-17	20-Dec-17	-163					
Portion VII [CH3825 to CH4250] - Original Section in DWP Rev.2a										
5238	Possession of Portion VII	0	20-Oct-17		266					
Portion VII [CH3800 to CH3911]										
Westbound										
9966a4a	MEP(WB) - (CH3800 to CH3911) VE Panel installation (Lower part) (1332m2)	15	04-Jul-17 A	27-Oct-17	-103					
5230a4	MEP(WB) - (CH3800 to CH3911) E&M 2nd Fix	48	14-Aug-17 A	26-Oct-17	-117					
5232a6	MEP(WB) - (CH3800 to CH3911) Niche installation	3	11-Sep-17 A	21-Oct-17	-152					
9966a4	MEP(WB) - (CH3800 to CH3911) VE Panel installation (Upper part) (1332m2)	15	27-Oct-17	14-Nov-17	-117					
5232a4	MEP(WB) - (CH3800 to CH3911) E&M Final Fix	16	18-Nov-17	06-Dec-17	-32					
5234a4	MEP(WB) - (CH3800 to CH3911) TCSS Field equip & cable installation	12	23-Nov-17	06-Dec-17	-43					

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING

Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 30 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017				2018
						Oct	Nov	Dec	Jan	
Eastbound										
5246a4	MEP(EB) - (CH3800 to CH3911) E&M 1st Fix	18	23-Feb-17 A	25-Oct-17	-131					
5248a4	MEP(EB) - (CH3800 to CH3911) E&M 2nd Fix (include Sump II)	12	15-Mar-17 A	02-Nov-17	-137					
5252a4	MEP(EB) - (CH3800 to CH3911) TCSS Field equip & cable installation	12	17-Mar-17 A	02-Nov-17	-132					
5250a6	MEP(EB) - (CH3800 to CH3911) Niche installation	3	11-Sep-17 A	21-Oct-17	-114					
5250a4	MEP(EB) - (CH3800 to CH3911) E&M Final Fix	16	03-Nov-17	21-Nov-17	-137					
9968a4a	MEP(EB) - (CH3800 to CH3911) VE Panel installation (Lower part) (1332m2)	14	16-Nov-17	01-Dec-17	-132					
9968a4	MEP(EB) - (CH3800 to CH3911) VE Panel installation (Upper part) (1332m2)	14	22-Nov-17	07-Dec-17	-137					
Portion VII [CH3911 to CH4250]										
Access Shaft Opening										
10118a4	VII(WB) - Decking for OHVD	12	20-Sep-17 A	20-Oct-17	-184					
10118a5	VII(WB) - Formworking & Rebar fixing for OHVD (coupler issue / drill & fix required)	24	21-Oct-17	18-Nov-17	-184					
10118a6	VII(WB) - Waterproofing & preparation works for OHVD concreting	3	20-Nov-17	22-Nov-17	-184					
10118a7	VII(WB) - Concreting for OHVD slab	1	23-Nov-17	23-Nov-17	-184					
10118a8	VII(WB) - OHVD slab curing	6	24-Nov-17	30-Nov-17	-184					
10118a9	VII(WB) - Dismantle and removal of OHVD scaffolding through the shaft opening	12	01-Dec-17	14-Dec-17	-184					
10118a10	VII(WB) - Scaffolding / Falsework for shaft tunnel slab	9	15-Dec-17	27-Dec-17	-184					
10118a11	VII(WB) - Formworking & rebar fixing for shaft tunnel slab	12	28-Dec-17	11-Jan-18	-184					
10118a12	VII(WB) - Waterproofing & preparation works for shaft tunnel slab concreting	3	12-Jan-18	15-Jan-18	-184					
10118a13	VII(WB) - Concreting for shaft tunnel slab	1	16-Jan-18	16-Jan-18	-184					
10120a1	VII(WB) - Shaft tunnel slab curing	6	17-Jan-18	23-Jan-18	-184					
Westbound										
5228a2	MEP(WB) - (CH3911 to CH4250) E&M 1st Fix	25	14-Mar-17 A	03-Nov-17	-131					
5234a2	MEP(WB) - (CH3911 to CH4250) TCSS Field equip & cable installation	15	15-Mar-17 A	04-Nov-17	-123					

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 31 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

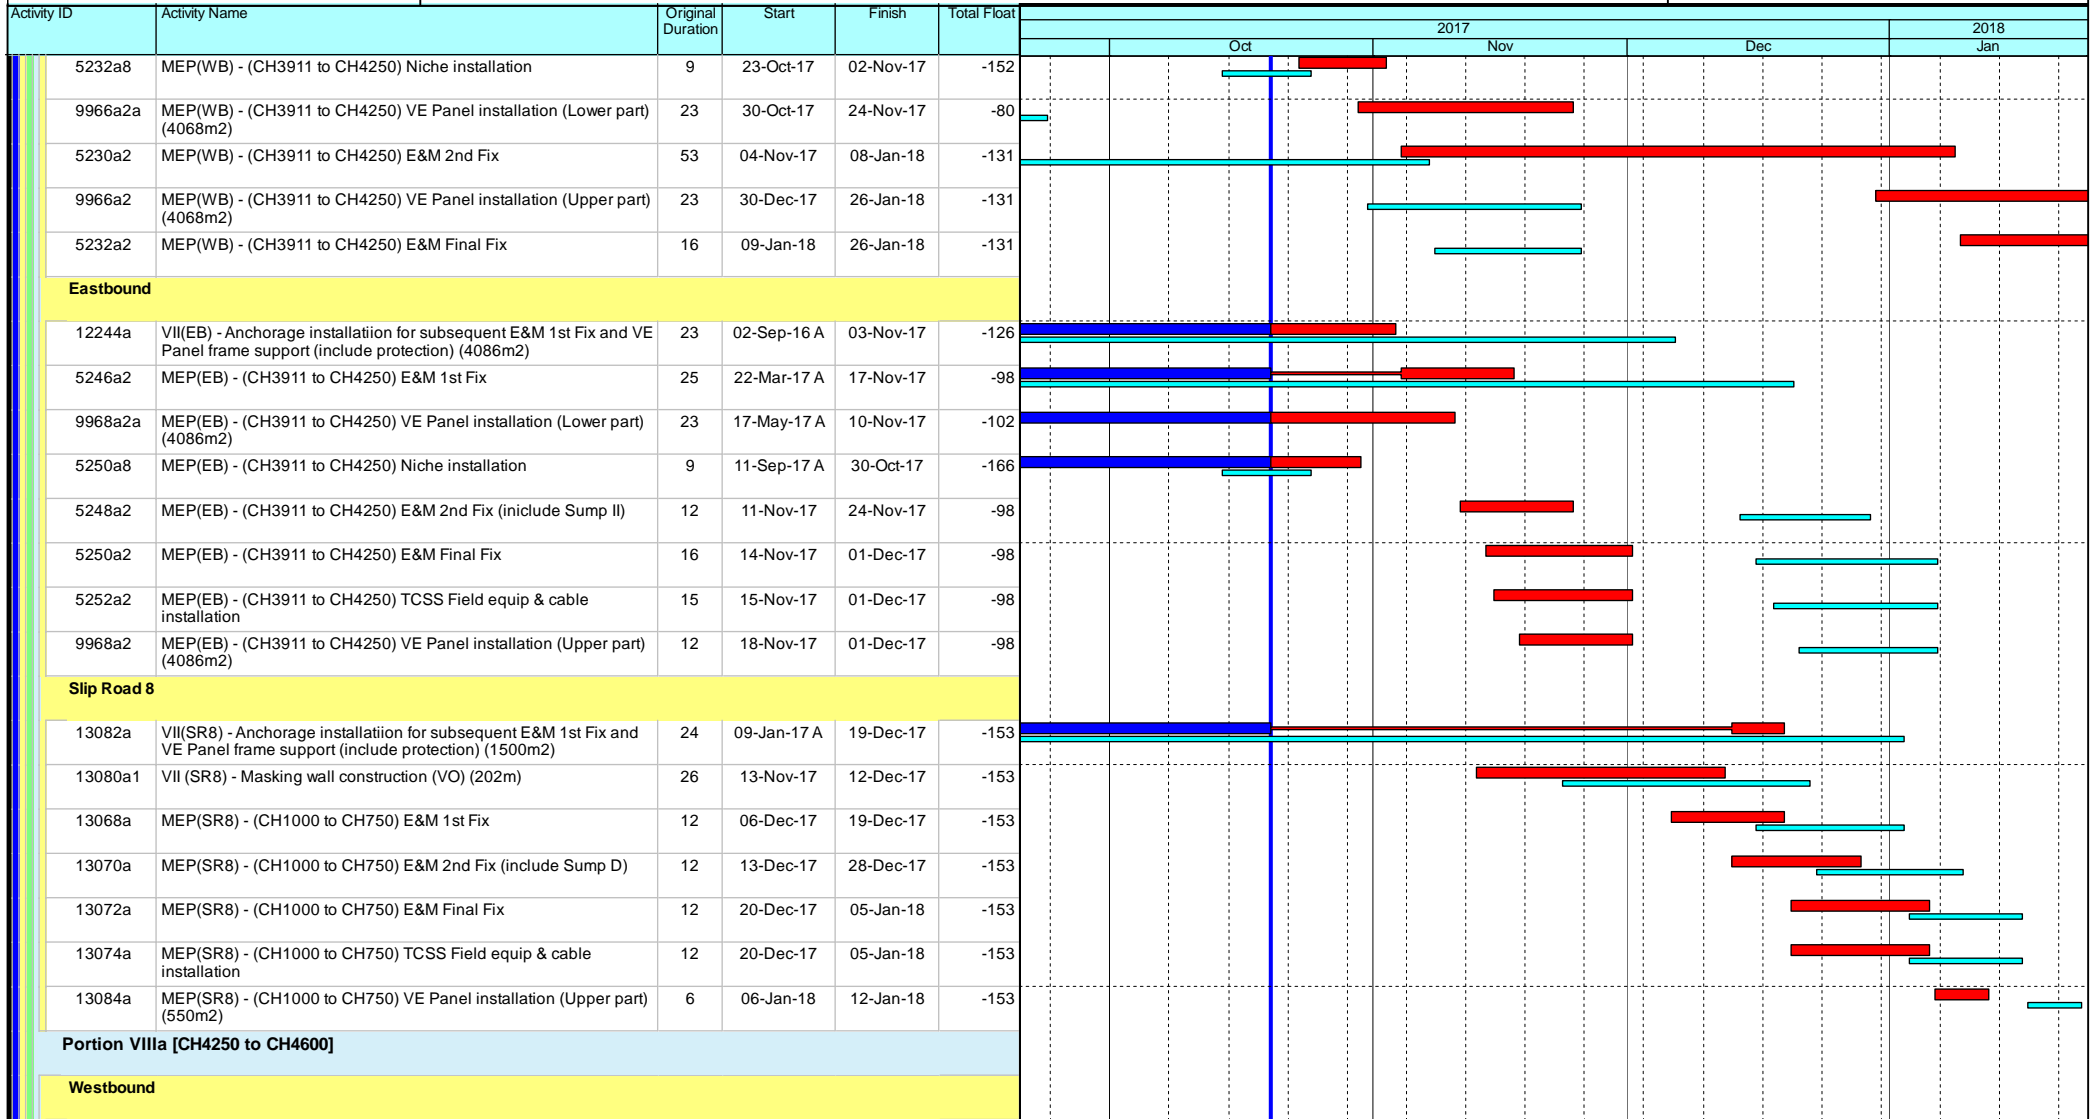

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 32 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

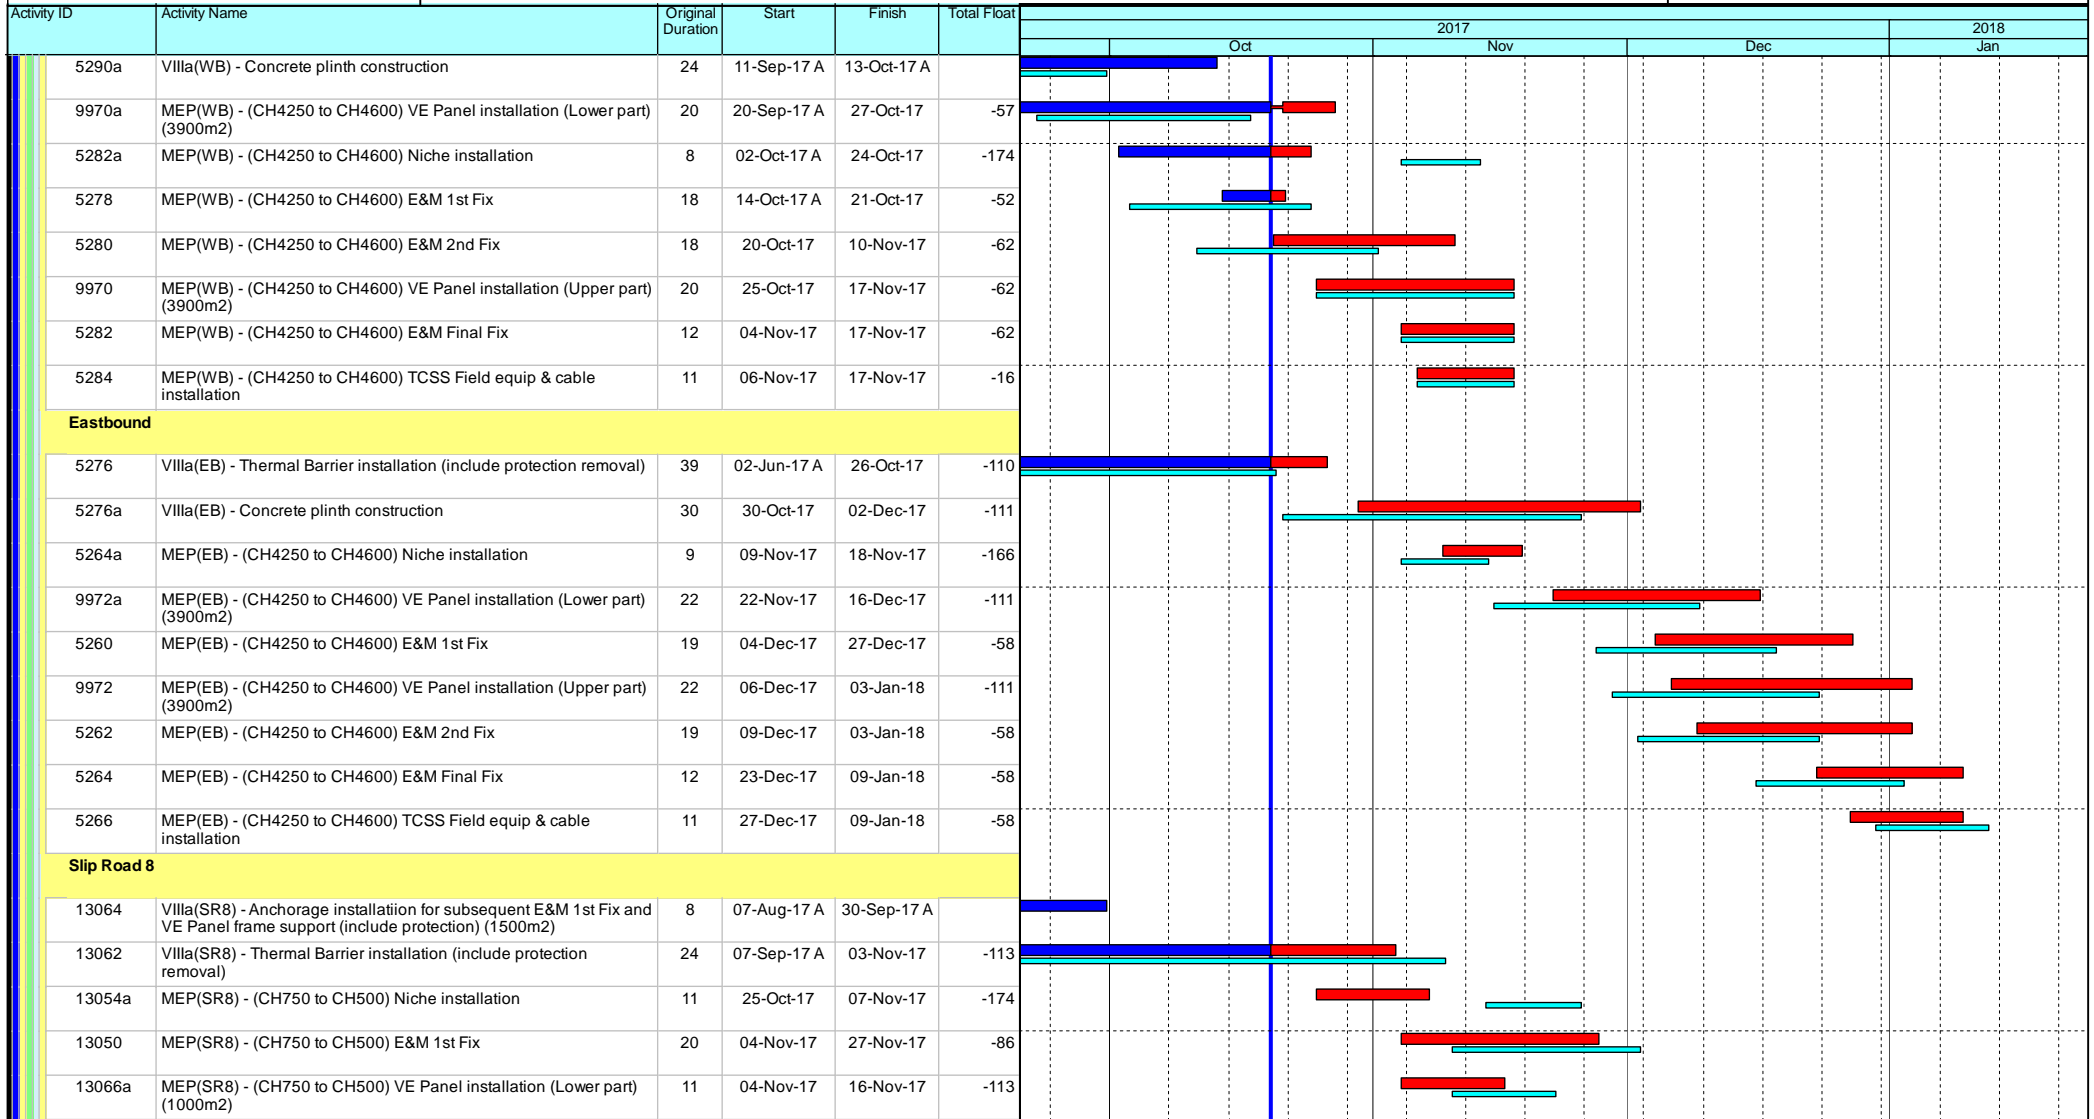

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 33 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

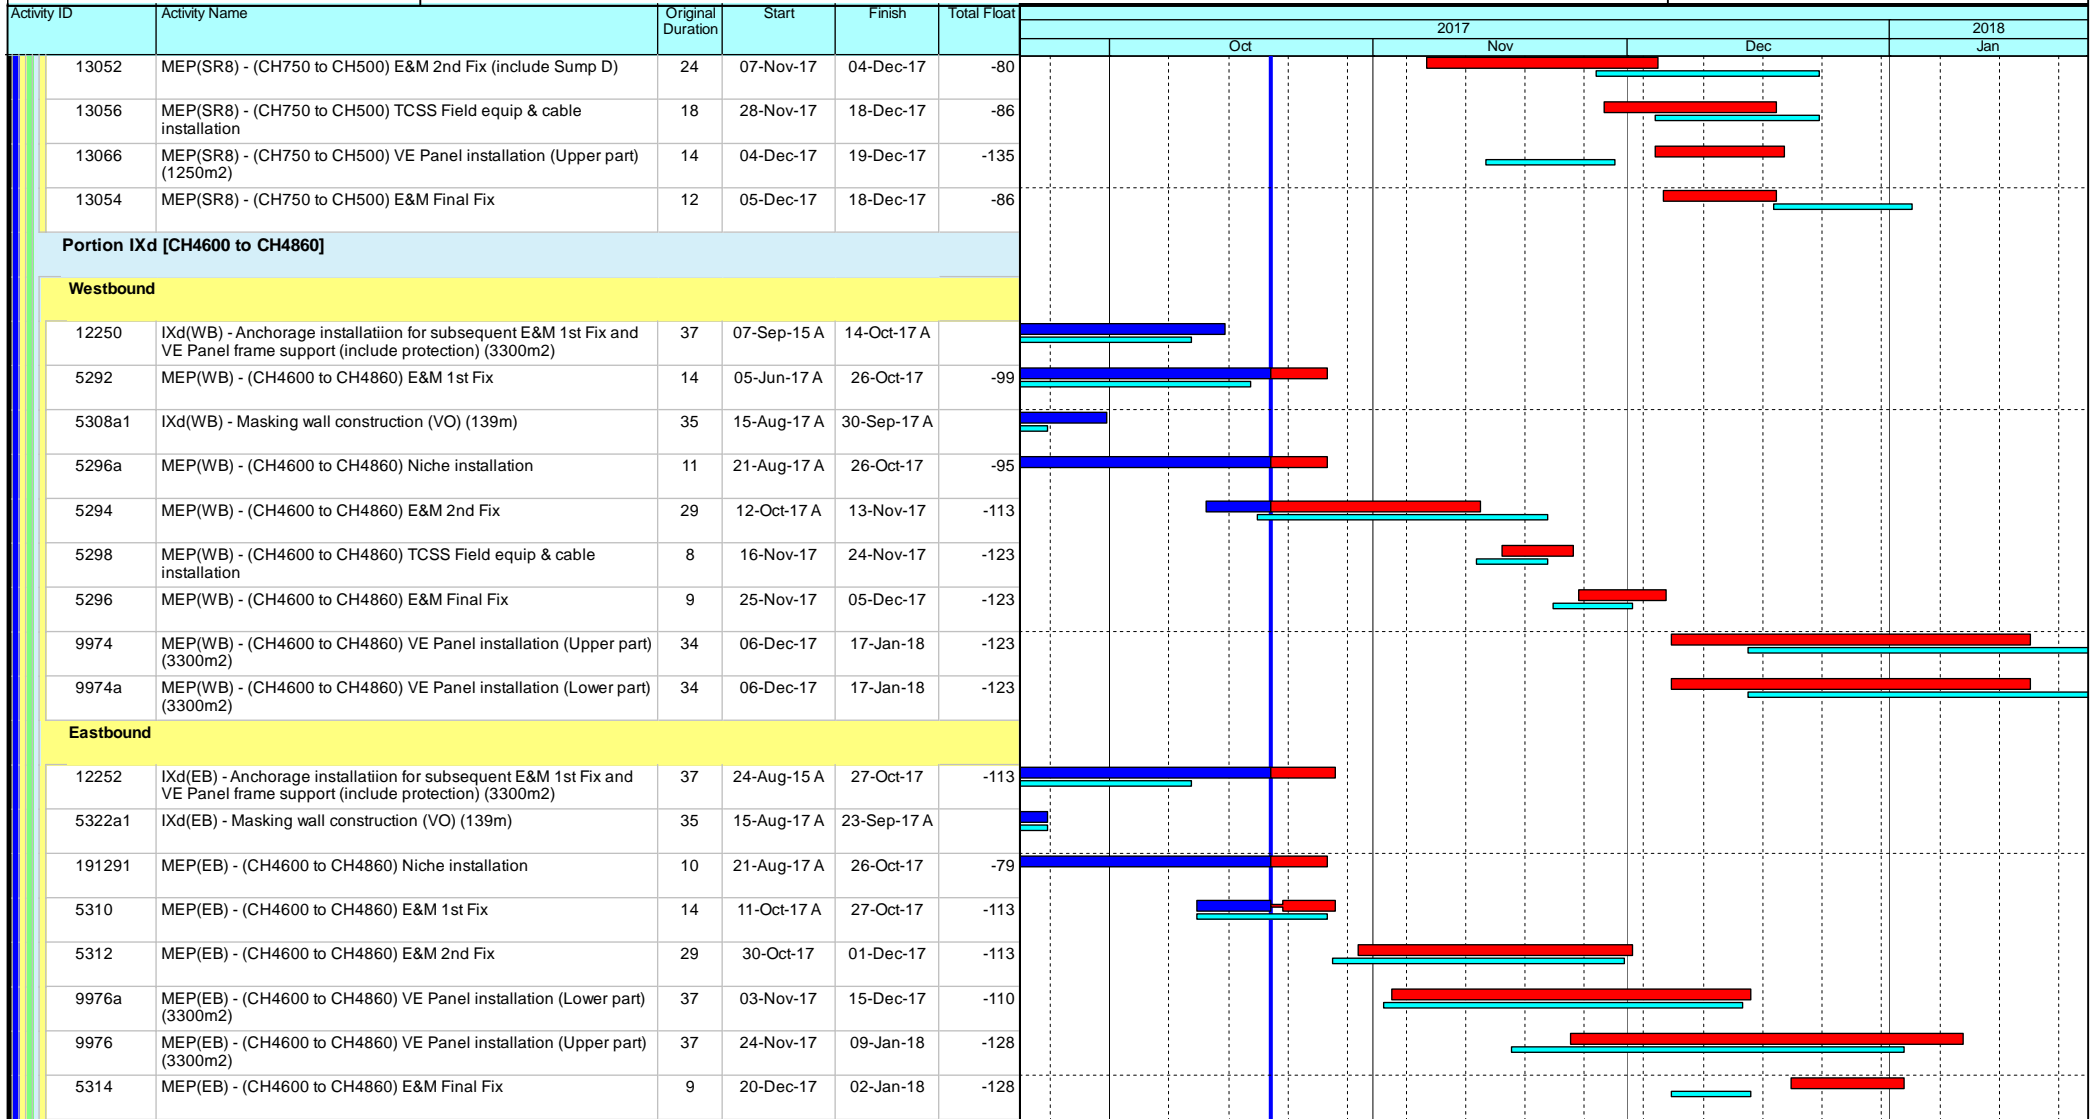

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 34 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

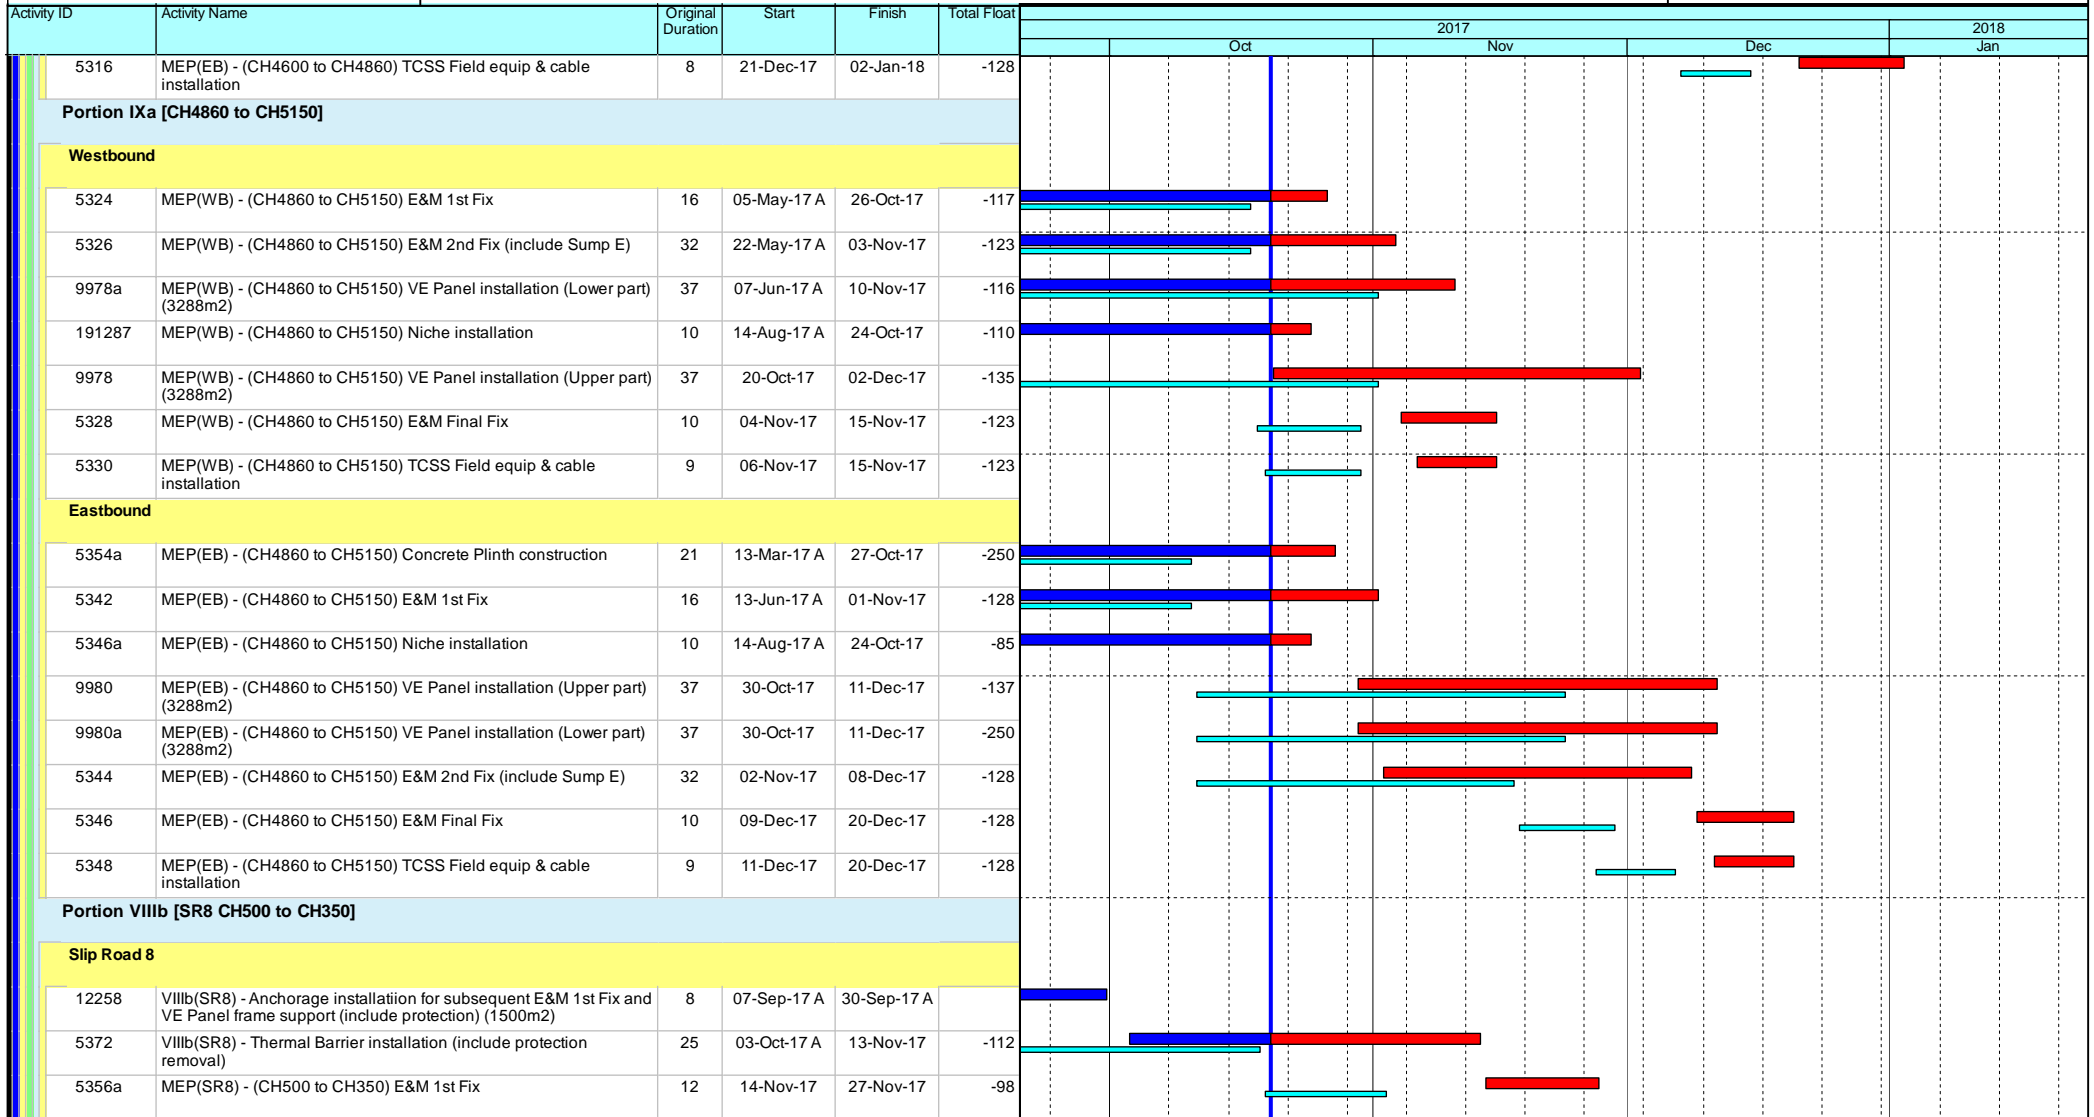

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 35 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

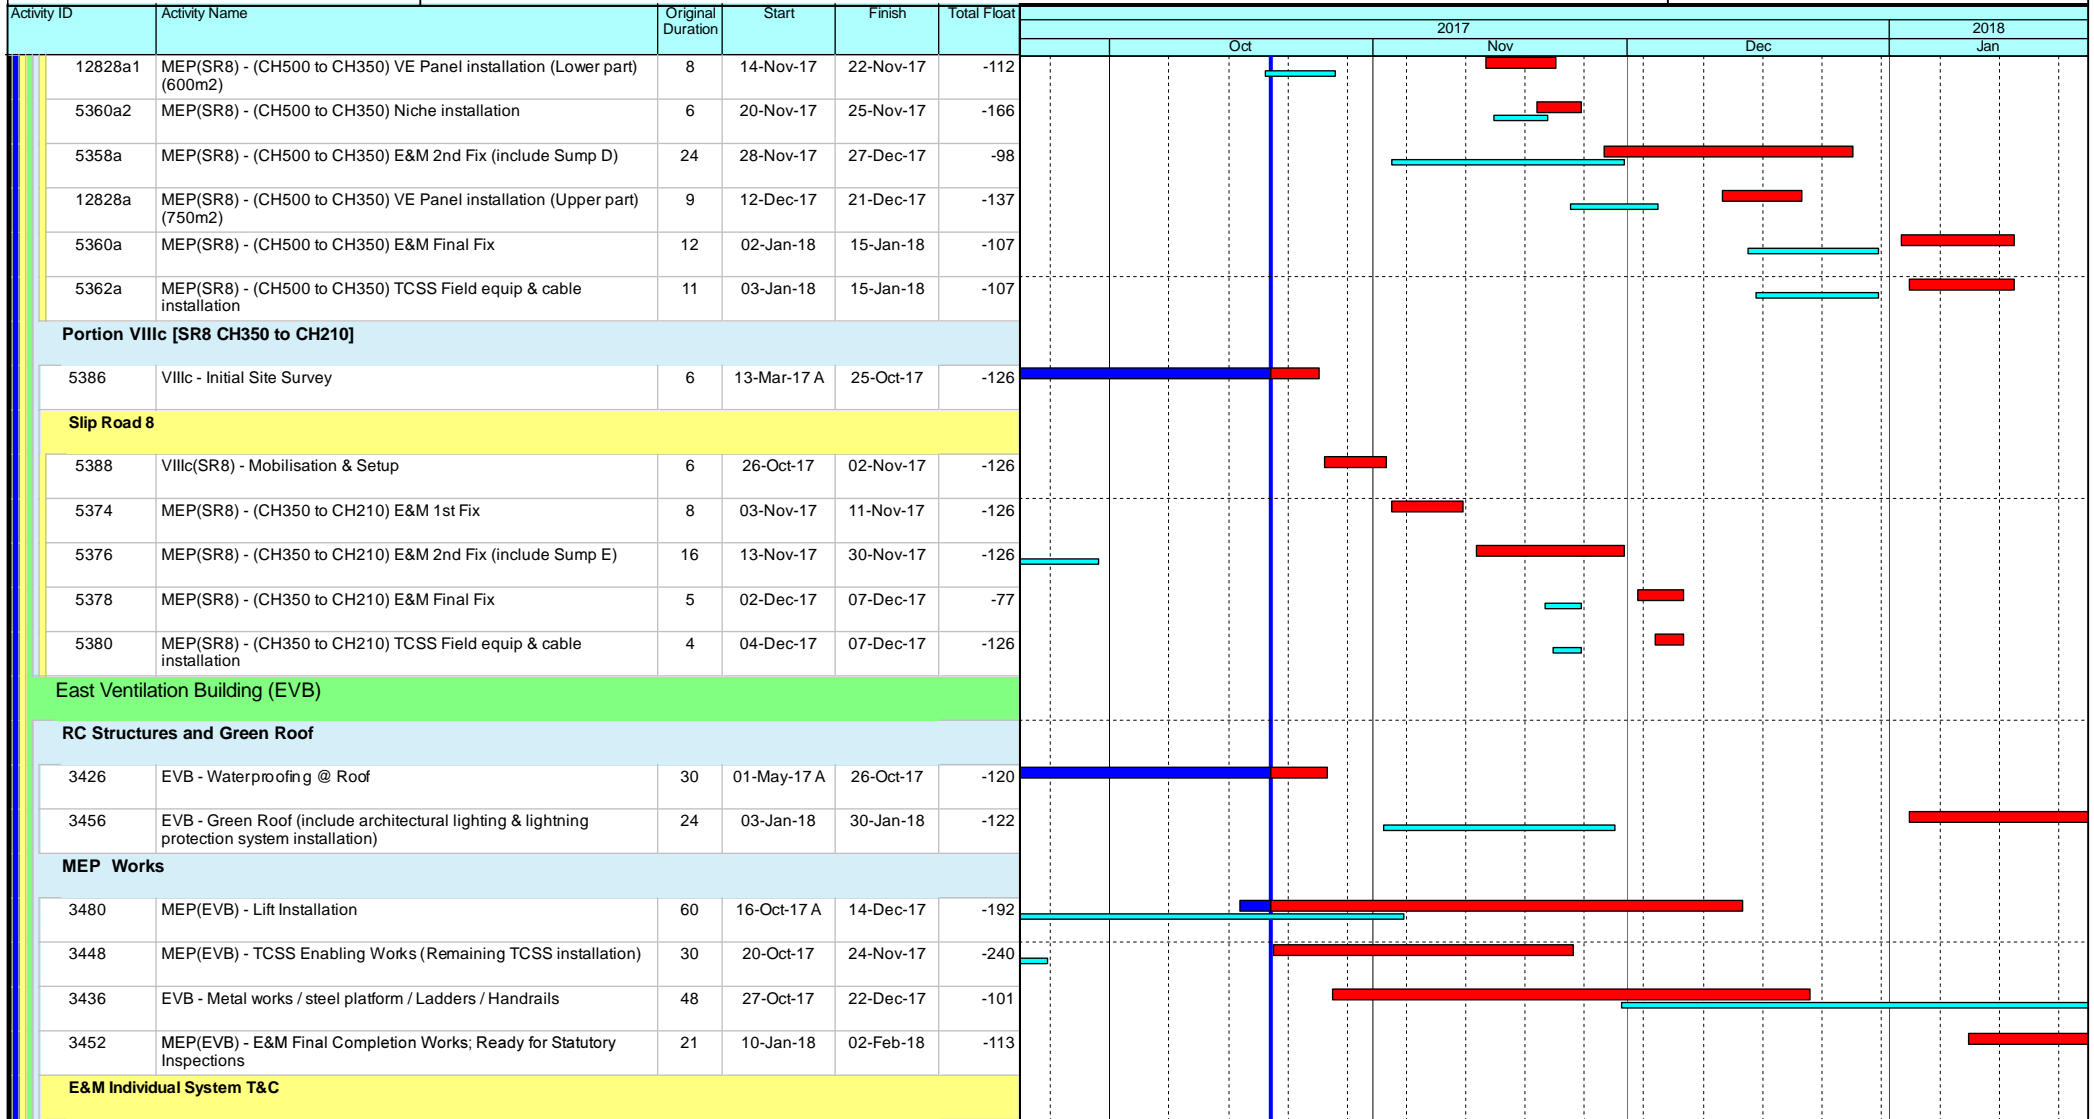

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 36 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

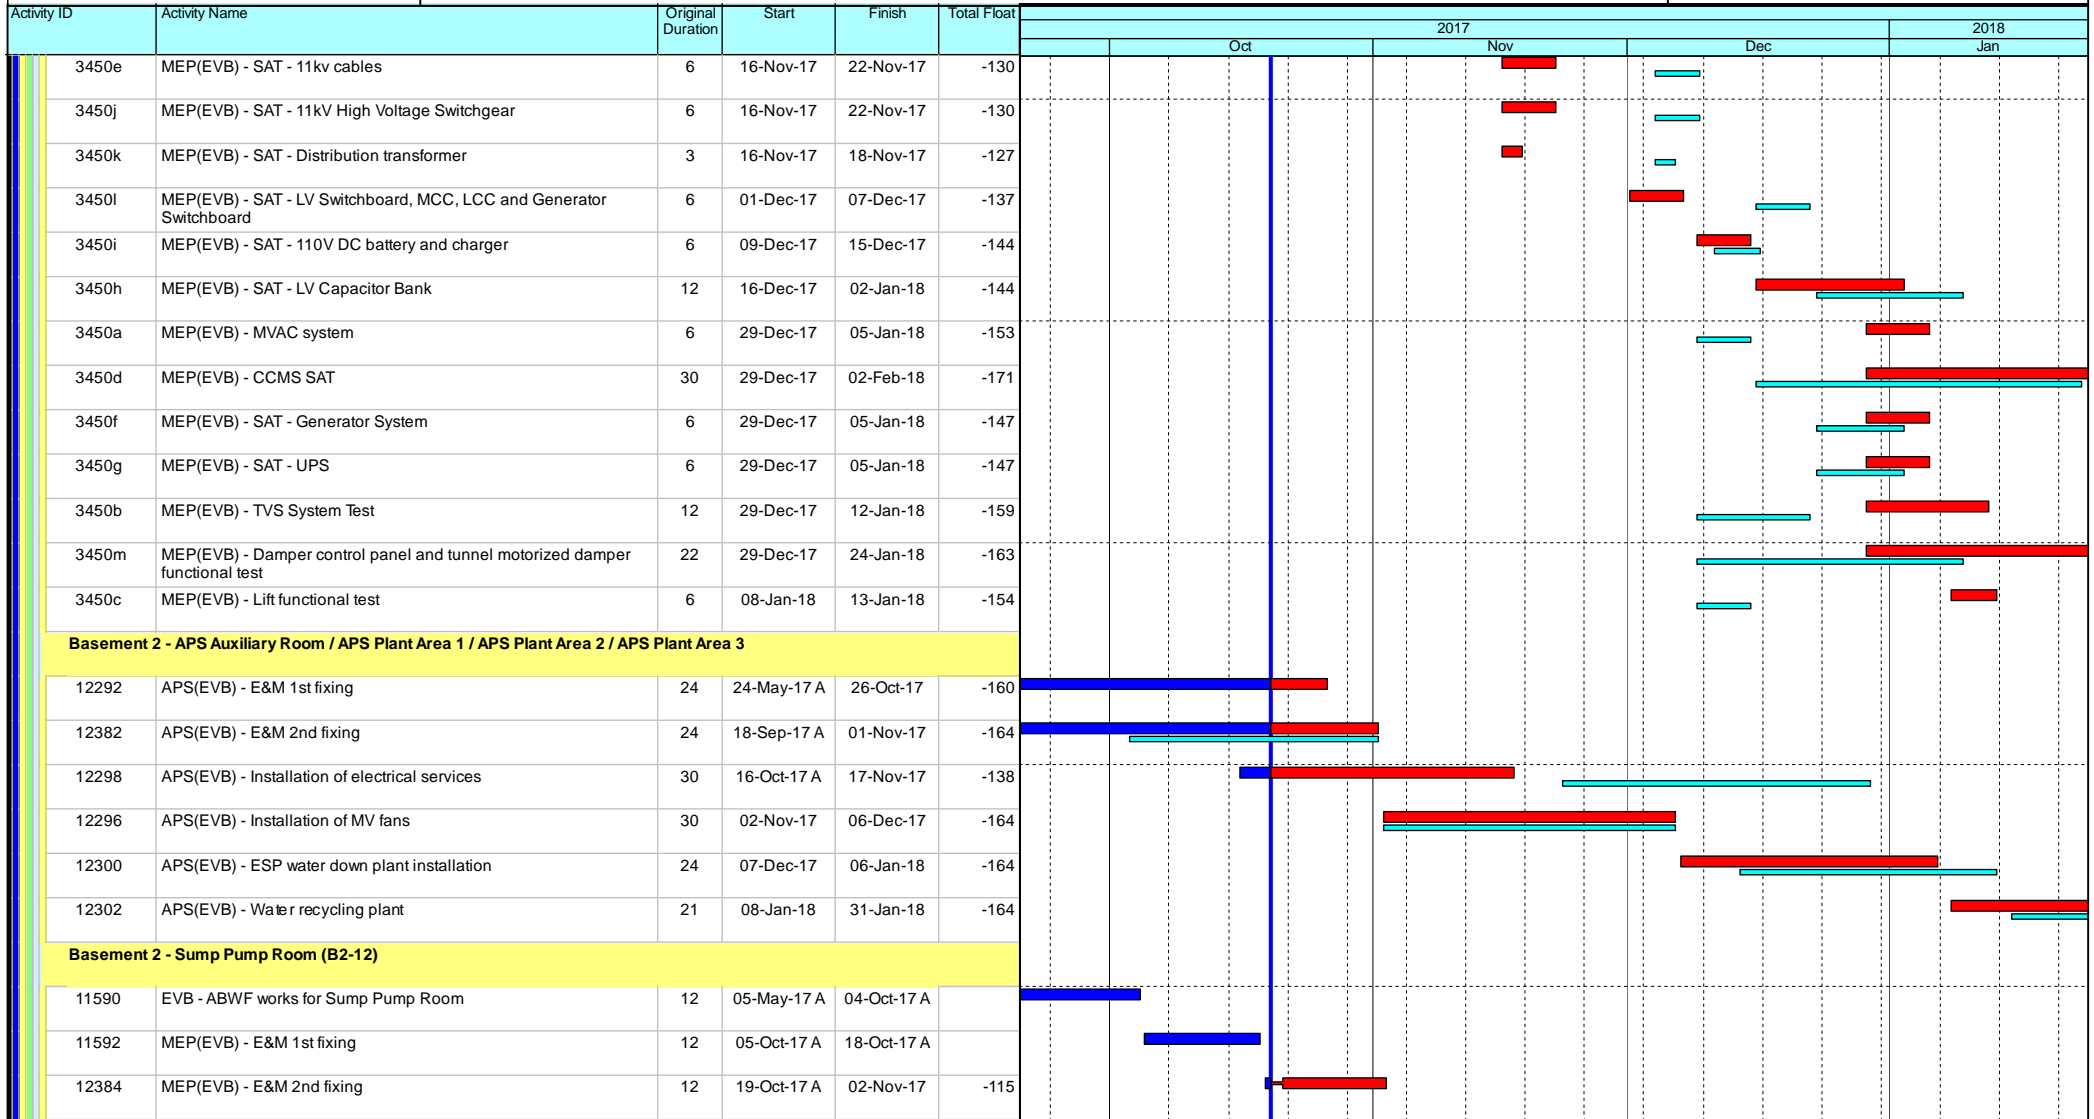

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 37 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

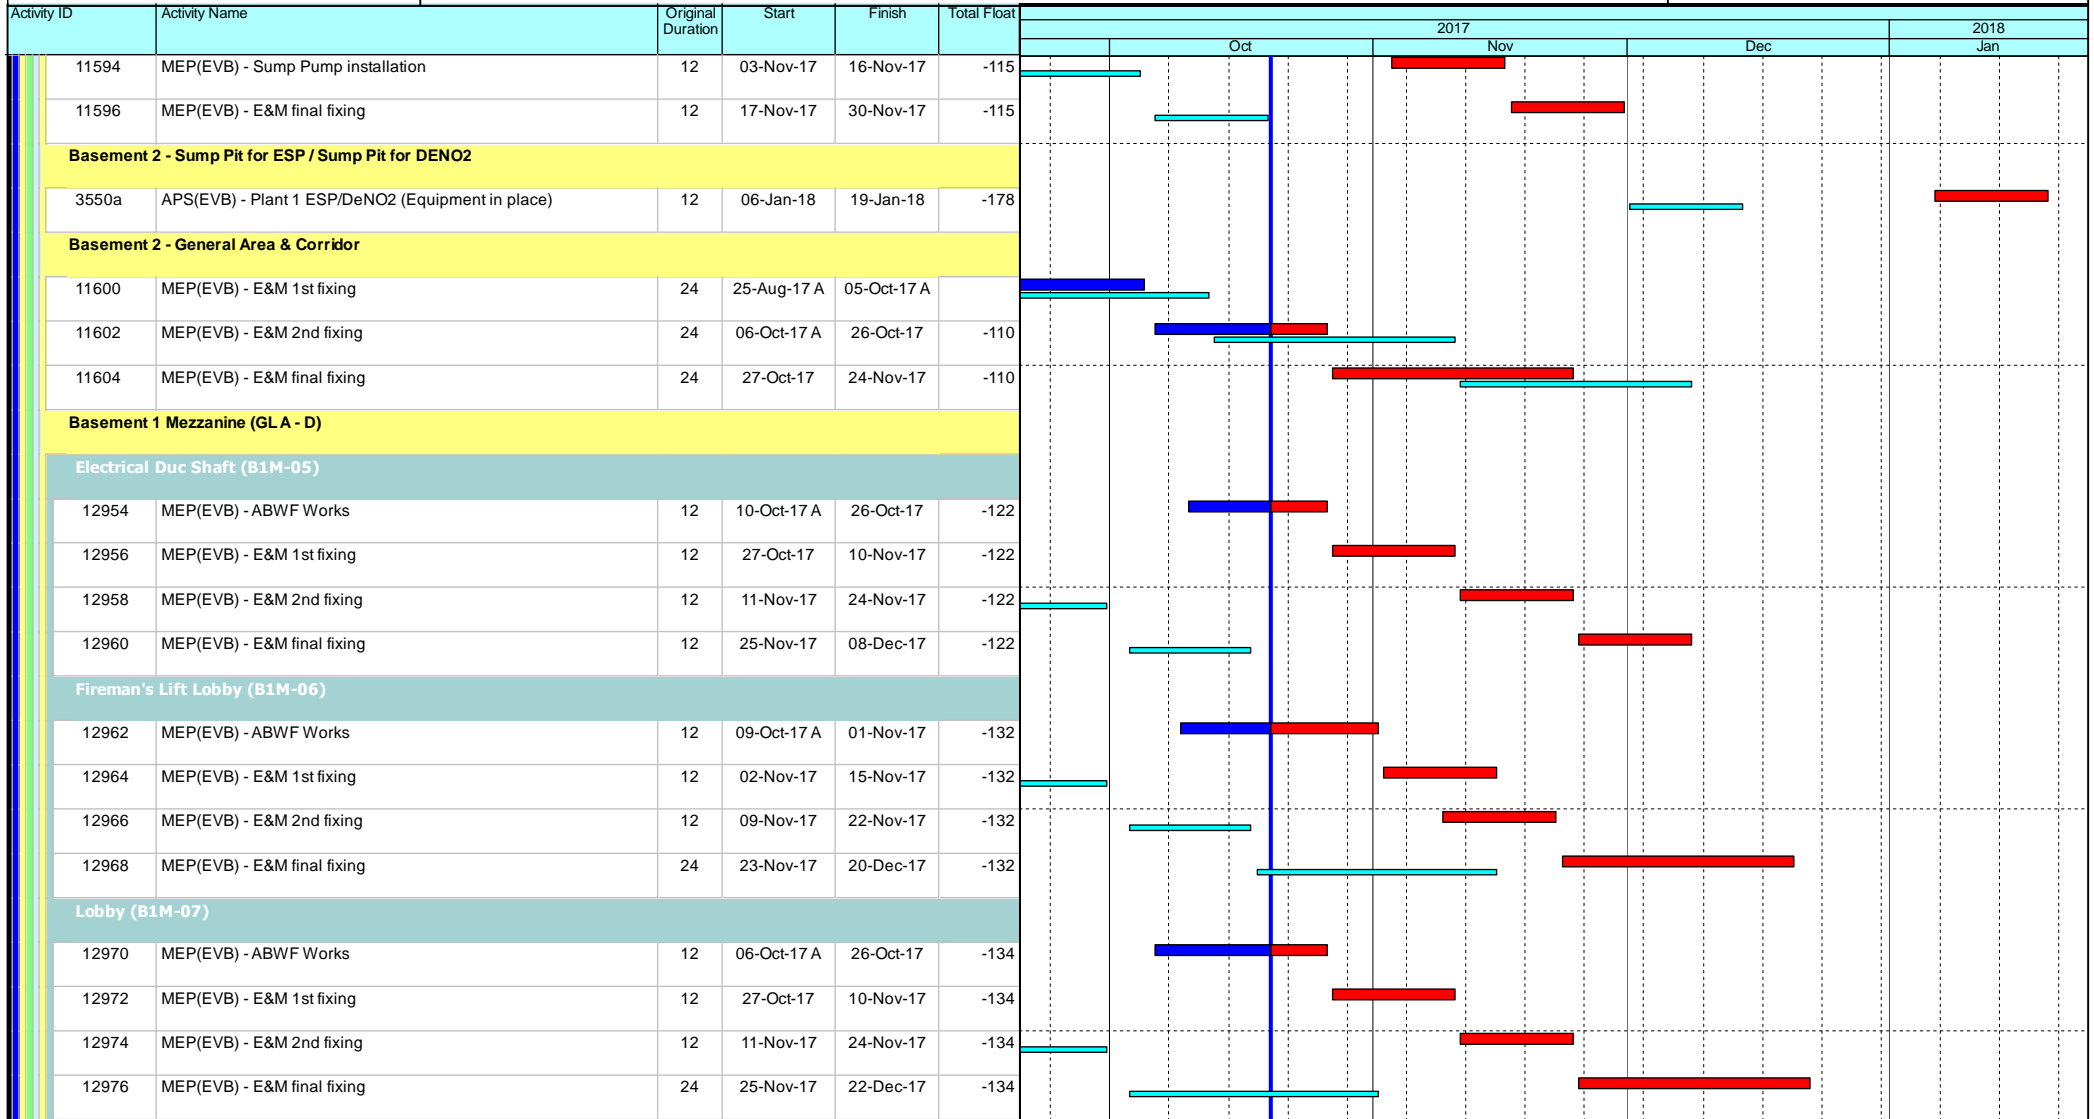

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 38 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

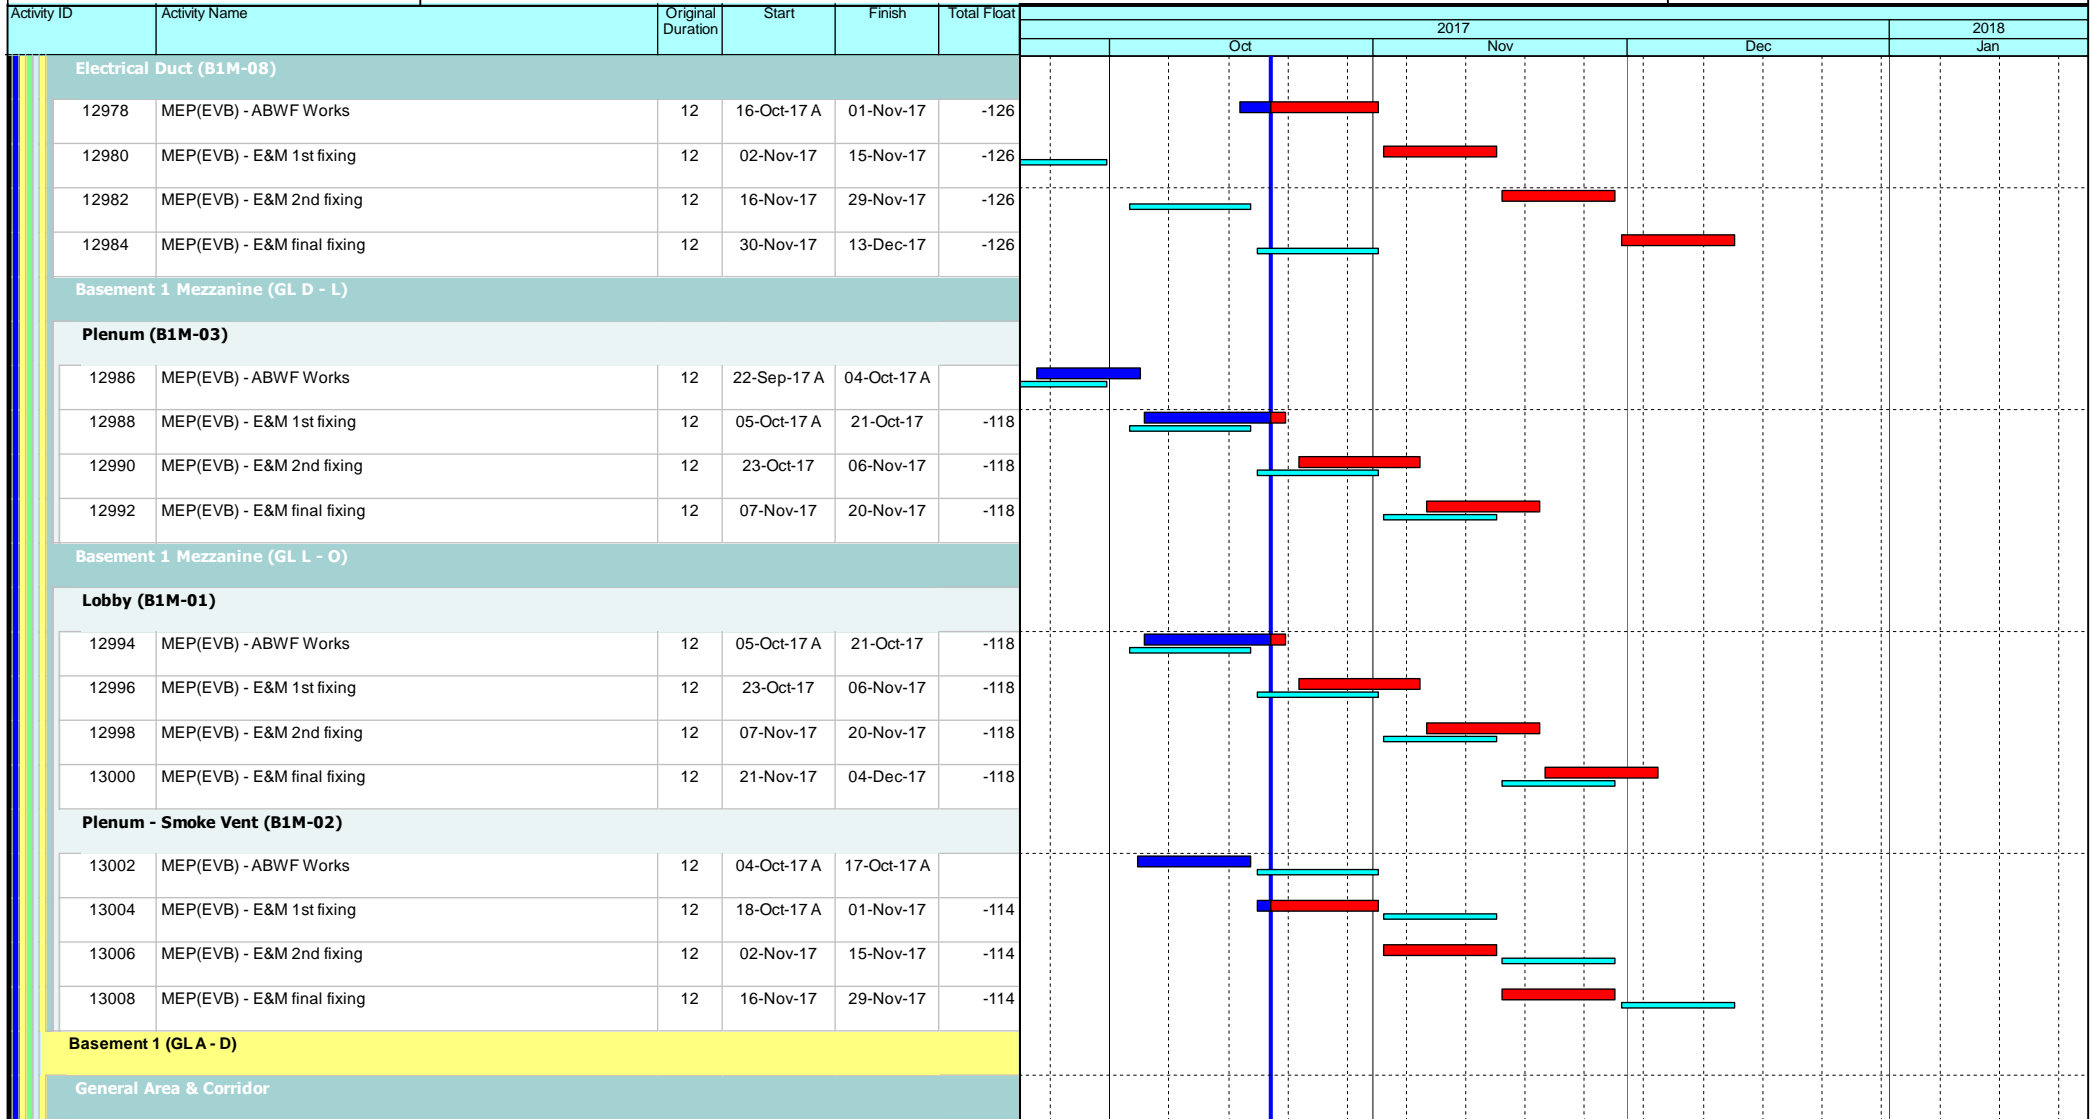

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 39 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

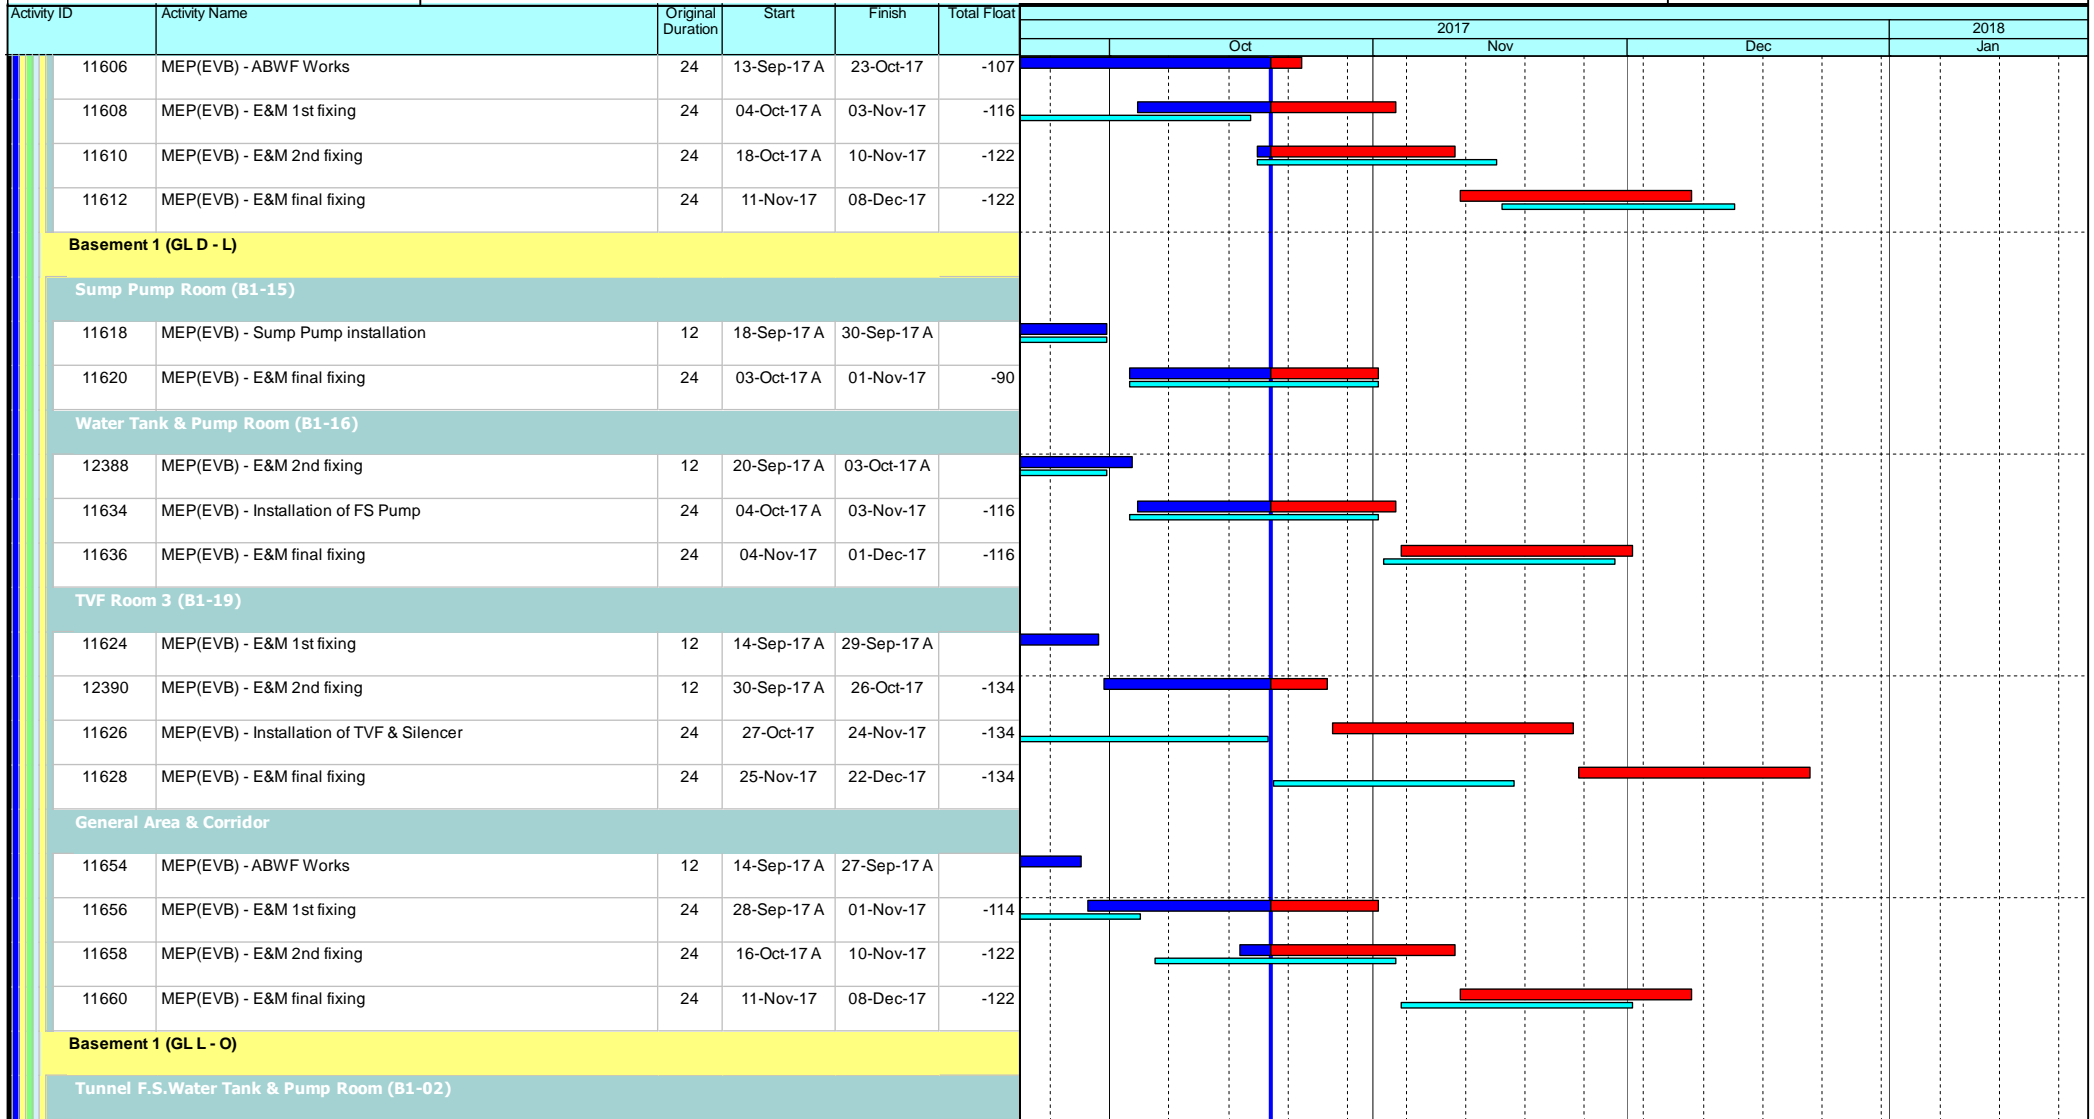

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 40 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

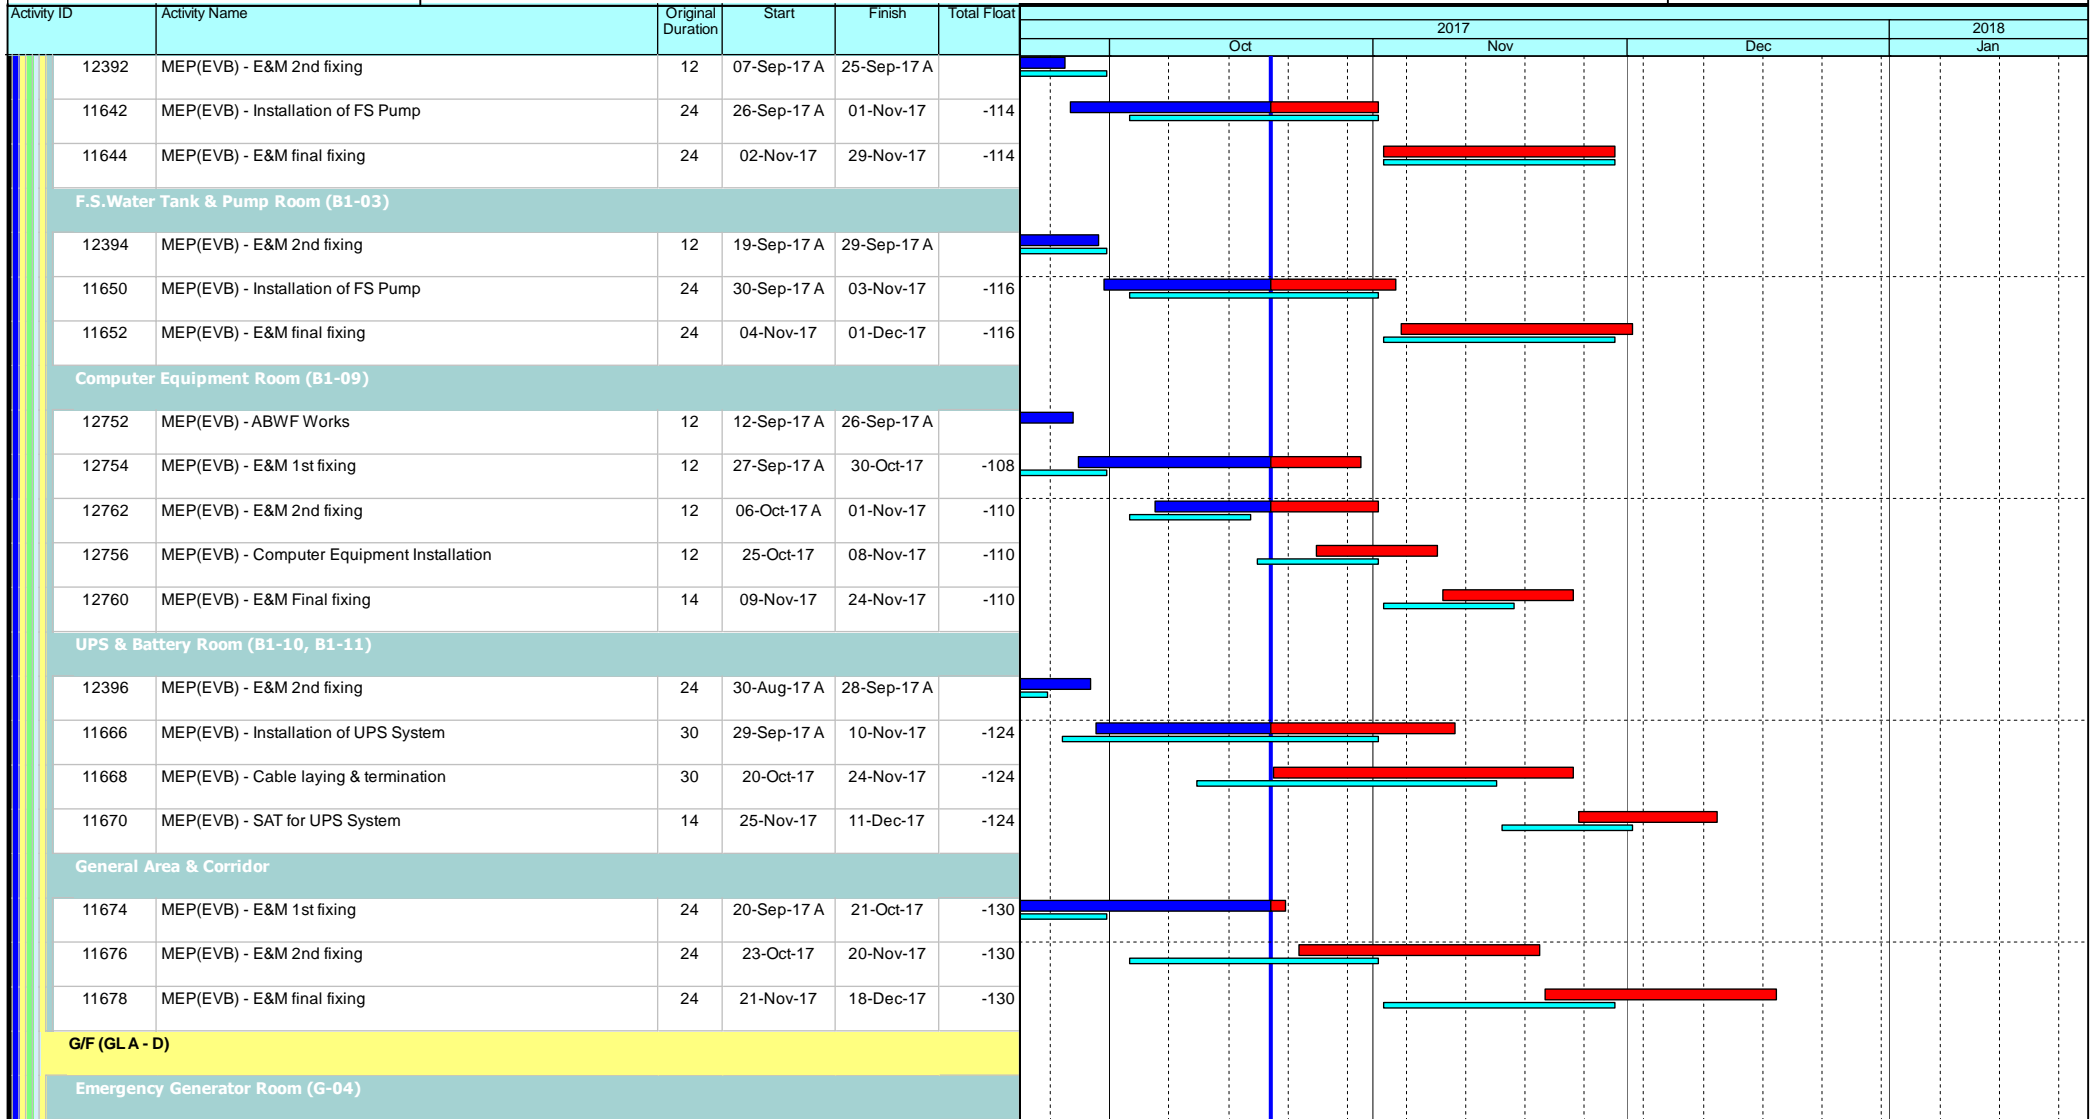

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 41 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

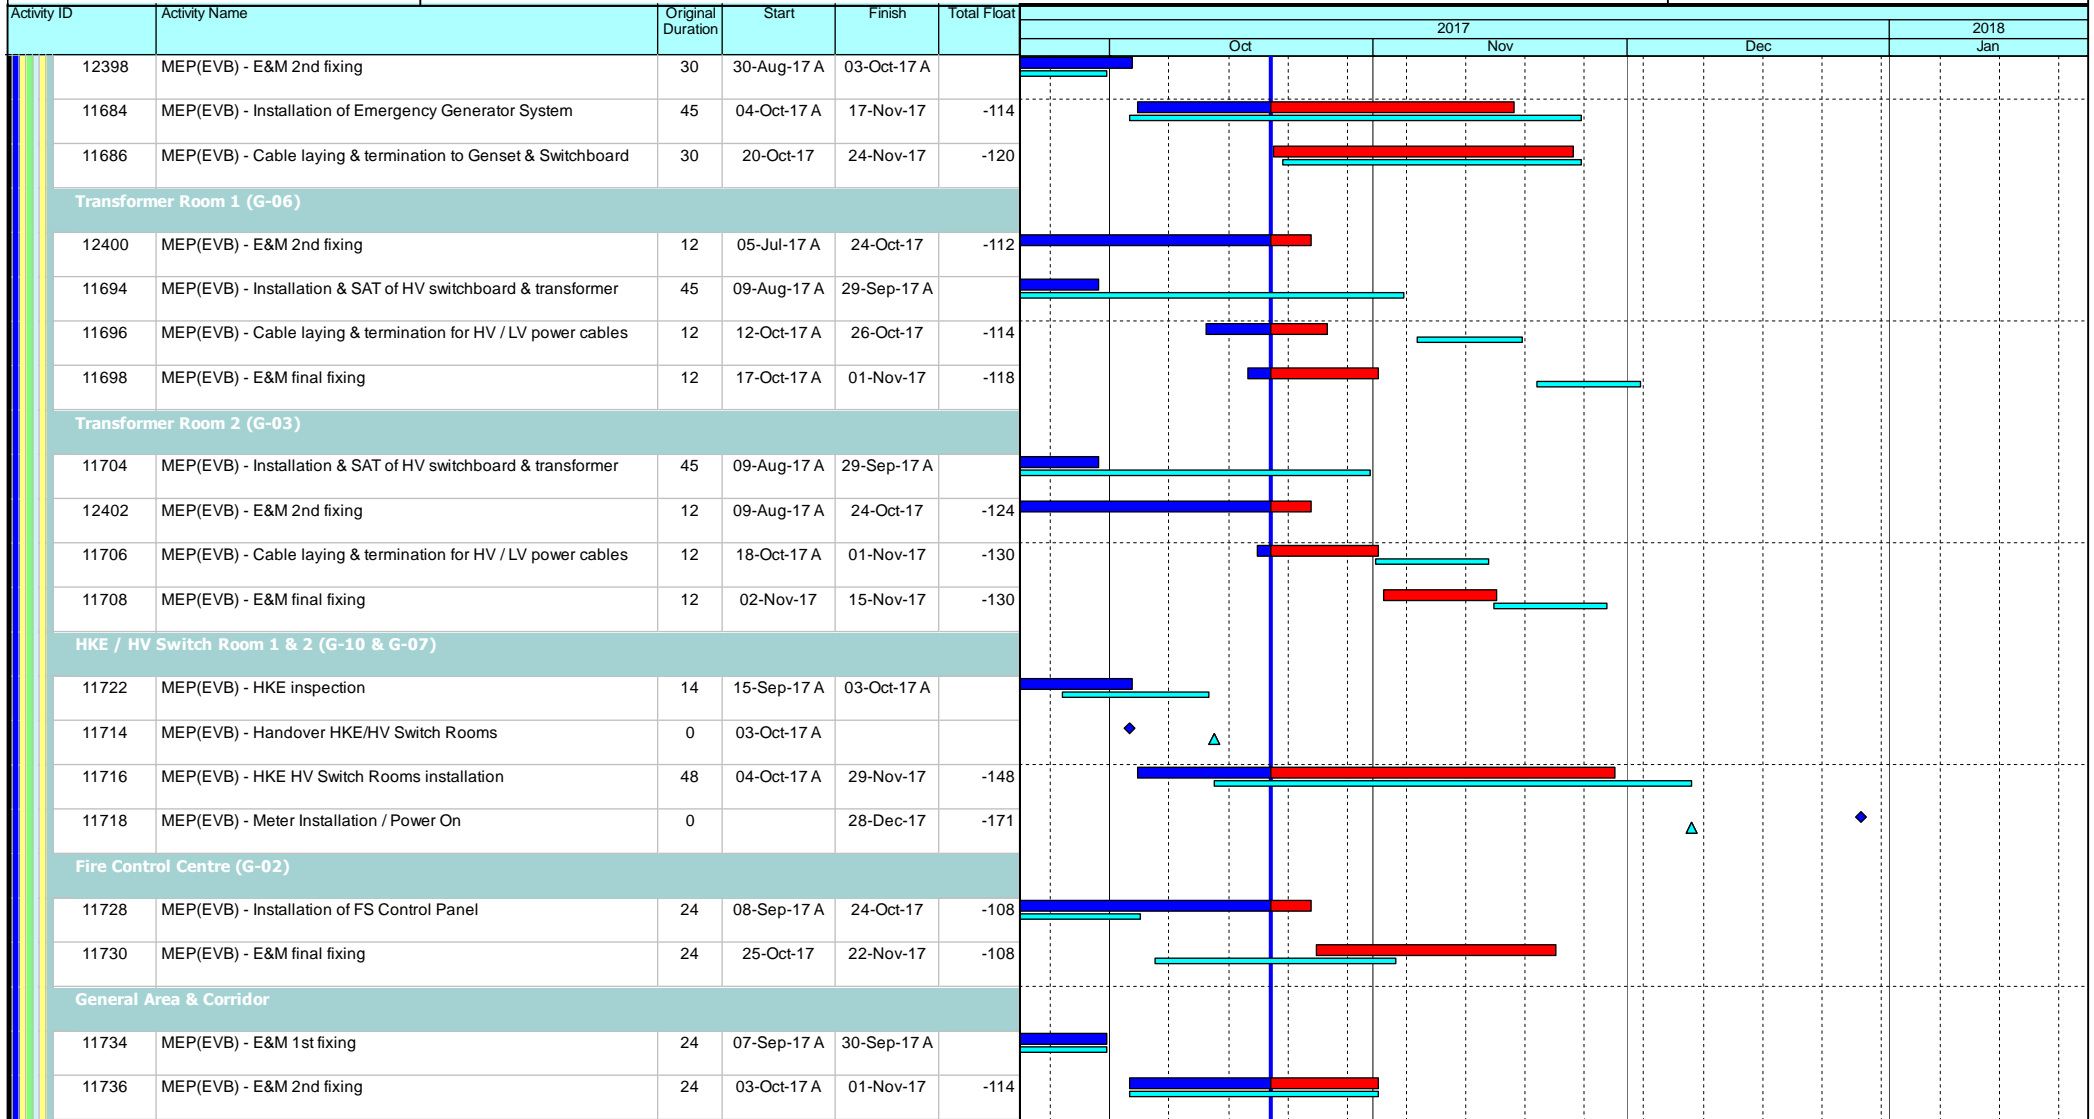

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 42 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

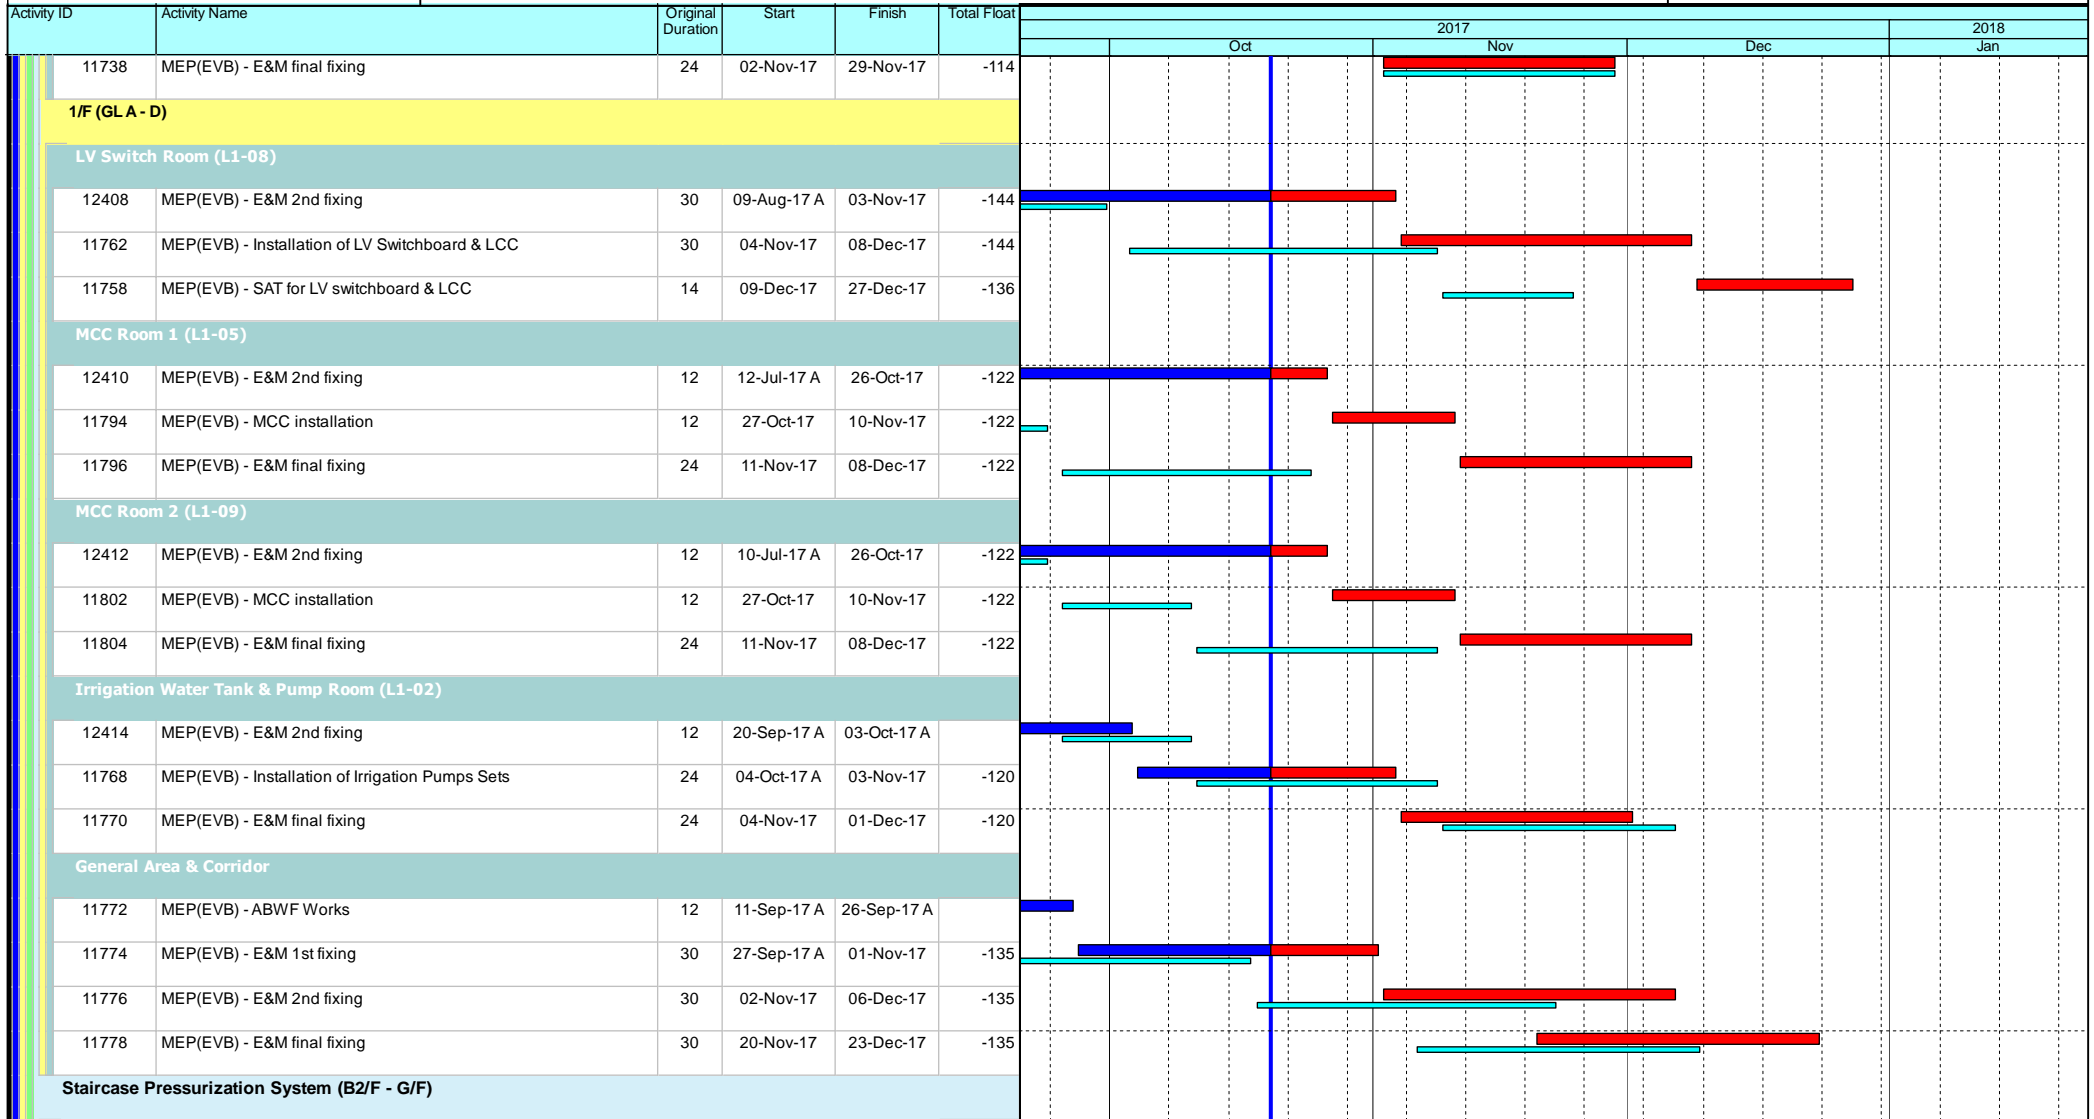

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING

Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 43 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017				2018
						Oct	Nov	Dec	Jan	
B2/F - G/F										
191341	SPS(EVB) - LPF installation	6	13-Dec-17	19-Dec-17	-129					
191343	SPS(EVB) - MSFD installation	6	20-Dec-17	28-Dec-17	-129					
191345	SPS(EVB) - Airduct work and FRP enclosure	24	29-Dec-17	26-Jan-18	-129					
191335	SPS(EVB) - LMCP installation	5	06-Jan-18	11-Jan-18	-129					
191337	SPS(EVB) - Power termination for LMCP	5	12-Jan-18	17-Jan-18	-129					
191339	SPS(EVB) - Conduit and wiring works for SPS control	18	18-Jan-18	07-Feb-18	-129					
191347	SPS(EVB) - SPS control panel installation	5	18-Jan-18	23-Jan-18	-116					
External Works										
191365	EVB - Cable trench for HEC cable laying (U/U obstruction delaying our works)	30	25-Aug-17 A	31-Oct-17	-171					
191367	EVB - Cable ducting for HEC cable laying (Depends on access from C19)	12	16-Oct-17 A	31-Oct-17	-171					
191373b	EVB - Cable ducts / pits construction at EVB external area	39	16-Oct-17 A	30-Nov-17	-136					
191373a	EVB - Cable ducts / pits and cable laying at EVB external area access from C19	0	16-Oct-17 A							
191369	EVB - HKE cable laying	36	01-Nov-17	12-Dec-17	-171					
191373c	EVB - Cable laying at EVB external area (connection to tunnel MCC)	26	07-Nov-17	06-Dec-17	-136					
3454	EVB - Road and drainage works (EVA)	24	09-Nov-17	06-Dec-17	-120					
3458	EVB - External concrete pavement	24	07-Dec-17	06-Jan-18	-120					
191371	EVB - Cable trench backfill	12	13-Dec-17	28-Dec-17	-171					
3462	EVB - Final completion works (include CCMS interface)	30	08-Jan-18	10-Feb-18	-120					
E&M Testing & Commissioning / Statutory Inspection										
3464	MEP(EVB) - E&M System Integrated Testing and Commissioning	36	29-Dec-17	02-Feb-18	-165					
3464a	MEP(EVB) - TVS & CCMS System Integrated Testing and Commissioning	36	29-Dec-17	02-Feb-18	-165					
3464b	MEP(EVB) - Tunnel Lighting & CCMS System Integrated Testing and Commissioning	24	29-Dec-17	21-Jan-18	-153					
3464c	MEP(EVB) - Fire Services & CCMS System Integrated Testing and Commissioning	36	29-Dec-17	02-Feb-18	-165					

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING

Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 44 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017				2018
						Oct	Nov	Dec	Jan	
12608	MEP(EVB) - Submission of Form 5 to EMSD	0	14-Jan-18		-133					◆
Tunnel Flexible Pavement (EVB-related)										
5820	Road(EB) - (CH3770 to CH5149.3) Flexible Pavement	12	10-Jan-18	23-Jan-18	-128					■
Administration Building (ADB)										
RC Structures (Portion Xa / Xb)										
G/F										
GL (C - G)										
G/F (GL C - G) Other Rooms / Corridors / Staircase										
13610	ADB - 1/F (GL C-G) - Plinths / R.C. curbs	30	20-Oct-17	24-Nov-17	-189		■	■		
GL (P - R)										
13182	ADB - G/F (GL P-R) - Formwork for column / walls	8	12-Sep-17 A	26-Oct-17	-231	■	■			
13184	ADB - G/F (GL P-R) - Rebar fixing for column / walls	12	14-Sep-17 A	26-Oct-17	-231	■	■			
13188	ADB - G/F (GL P-R) - Scaffolding for beam & slab	12	18-Sep-17 A	30-Oct-17	-233	■	■			
13190	ADB - G/F (GL P-R) - Decking / Formwork for beam & slab	12	20-Oct-17	03-Nov-17	-233	■	■			
13192	ADB - G/F (GL P-R) - Rebar for beam & slab	12	26-Oct-17	09-Nov-17	-233		■	■		
13186	ADB - G/F (GL P-R) - Concrete for column / walls	1	27-Oct-17	27-Oct-17	259		■			
13194	ADB - G/F (GL P-R) - Close formwork for beam & slab	12	02-Nov-17	15-Nov-17	-233		■	■		
13196	ADB - G/F (GL P-R) - Concrete beam & slab (Roof slab)	1	16-Nov-17	16-Nov-17	-233			■		
G/F (GL P - R) Other Rooms / Corridors / Staircase										
13198	ADB G/F (GL P-R) - Remaining Internal walls / Cast-in items	1	16-Nov-17	16-Nov-17	-182			■		
13200	ADB G/F (GL P-R) - Plinths / R.C. curbs	12	17-Nov-17	30-Nov-17	-182			■	■	
1/F										
GL (A - C)										
1/F (GL A - D) Other Rooms / Corridors / Staircase										

- ◆ Current Milestone
- Level of Effort
- ▲ Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING

Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 45 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017											
						Oct			Nov			Dec			2018		
						1	2	3	1	2	3	1	2	3	Jan	2	3
13220	ADB - 1/F (GL A-C) - Plinths / R.C. curbs	30	25-Aug-17 A	27-Sep-17 A													
External Facade																	
13248	ADB - External facing tiles / Louvre	48	15-Dec-17	12-Feb-18	-157												
MEP & ABWF Works																	
13250	ADB - Water roofing and roofing	24	17-Nov-17	14-Dec-17	-233												
13254	MEP(ADB) - TCSS Enabling Works (Remaining TCSS installation)	30	17-Nov-17	21-Dec-17	-115												
13252	ADB - Metal works / steel platform / Ladders / Handrails	48	15-Dec-17	12-Feb-18	-157												
13260	MEP(ADB) - Lift Installation	60	15-Dec-17	12-Feb-18	-285												
Basement (GL D - F)																	
Sump Pump Room (B-04)																	
13270	MEP(ADB) - ABWF Works	12	20-Oct-17	03-Nov-17	-165												
13272	MEP(ADB) - E&M 1st fixing	12	16-Dec-17	02-Jan-18	-195												
13278	MEP(ADB) - E&M 2nd fixing	12	23-Dec-17	09-Jan-18	-189												
13274	MEP(ADB) - Installation of Sump Pump	24	10-Jan-18	06-Feb-18	-189												
General Area & Corridor																	
13262	MEP(ADB) - ABWF Works	12	04-Nov-17	17-Nov-17	-159												
13264	MEP(ADB) - E&M 1st fixing	24	18-Nov-17	15-Dec-17	-159												
13266	MEP(ADB) - E&M 2nd fixing	24	03-Jan-18	30-Jan-18	-183												
13268	MEP(ADB) - E&M final fixing	24	17-Jan-18	13-Feb-18	-183												
Basement (GL P - R)																	
F.S. Water Tank, Sprinkler Tank & Pump Room (B-13)																	
13288	MEP(ADB) - ABWF Works	12	04-Nov-17	17-Nov-17	-165												
13290	MEP(ADB) - E&M 1st fixing	12	18-Nov-17	01-Dec-17	-165												
13296	MEP(ADB) - E&M 2nd fixing	12	25-Nov-17	08-Dec-17	-165												

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 46 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

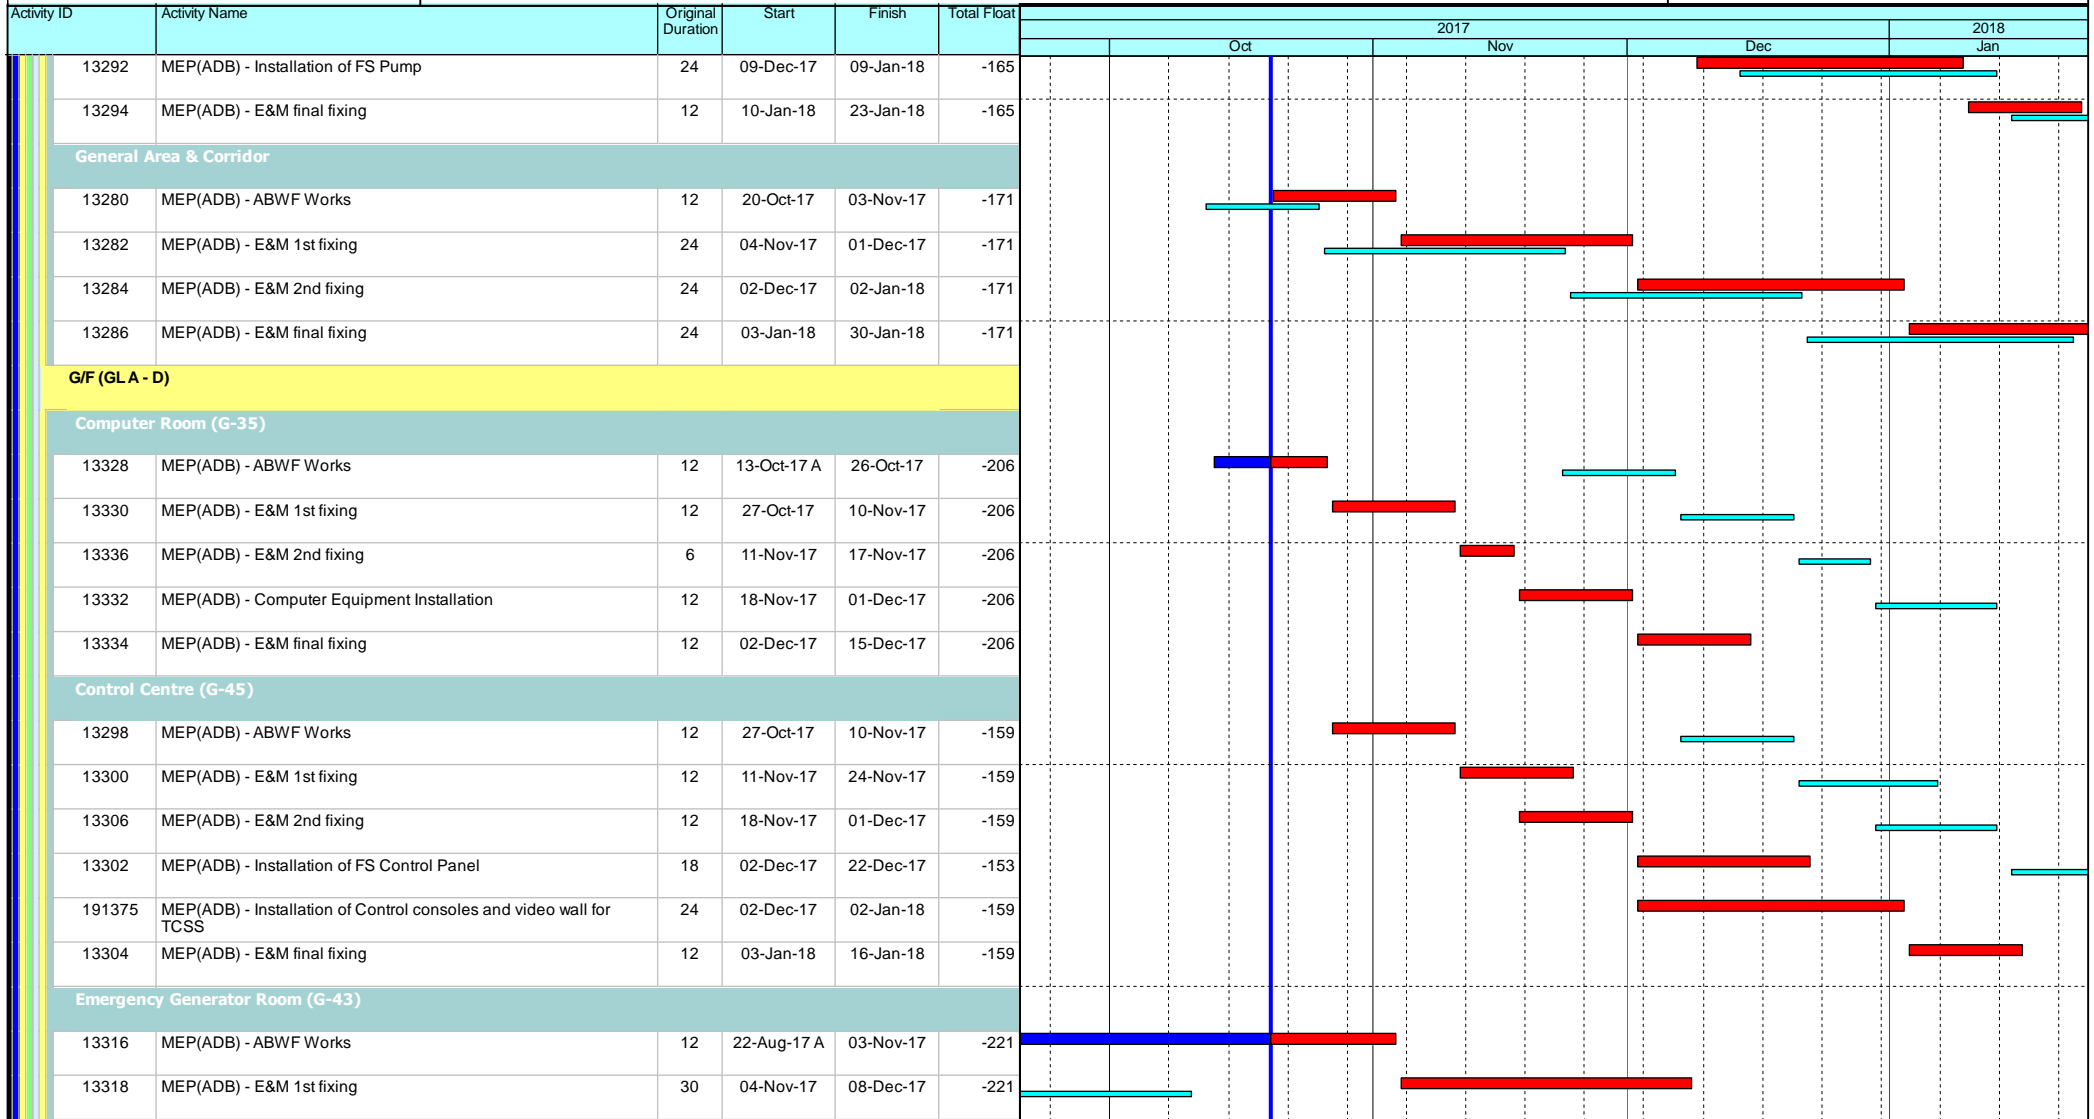

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 47 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

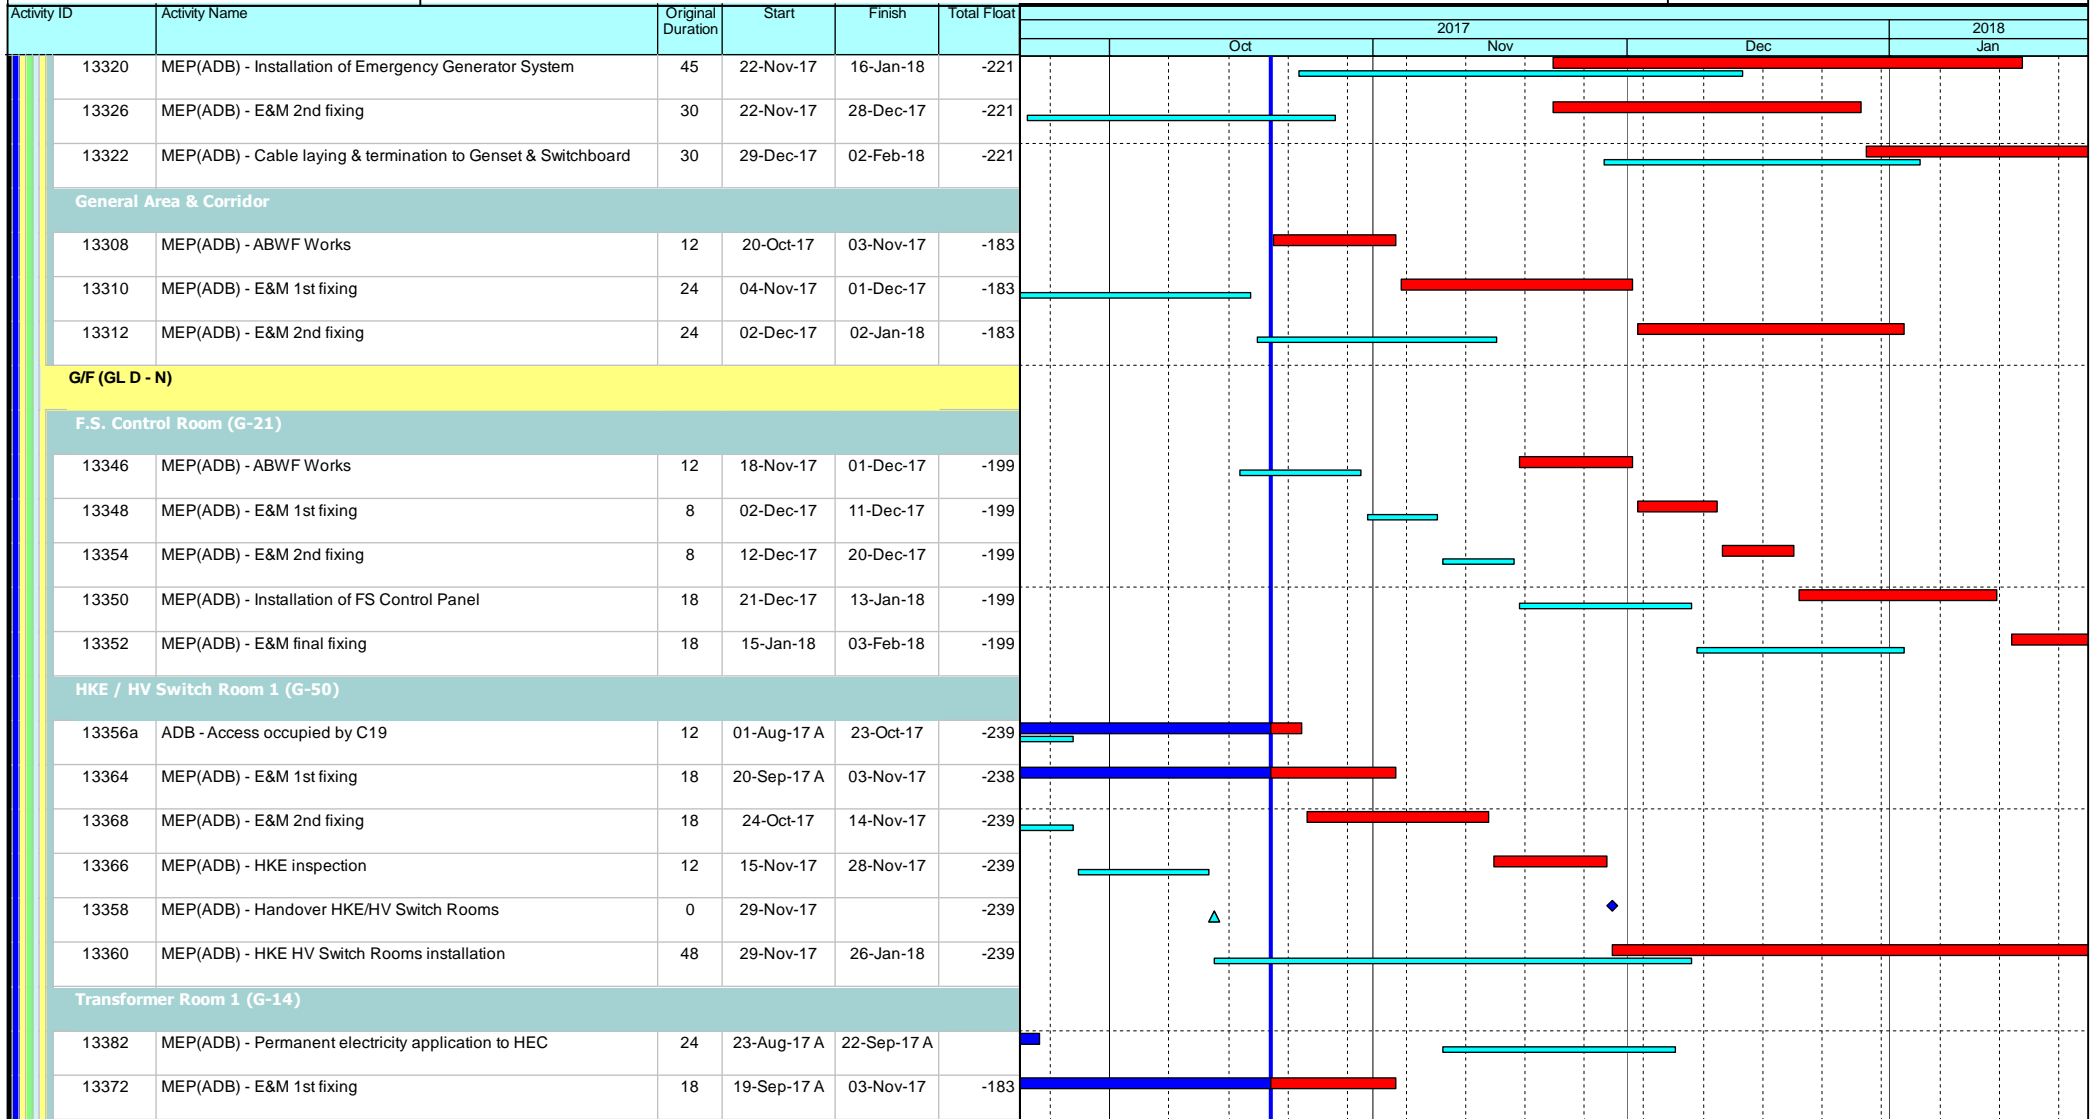

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 48 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

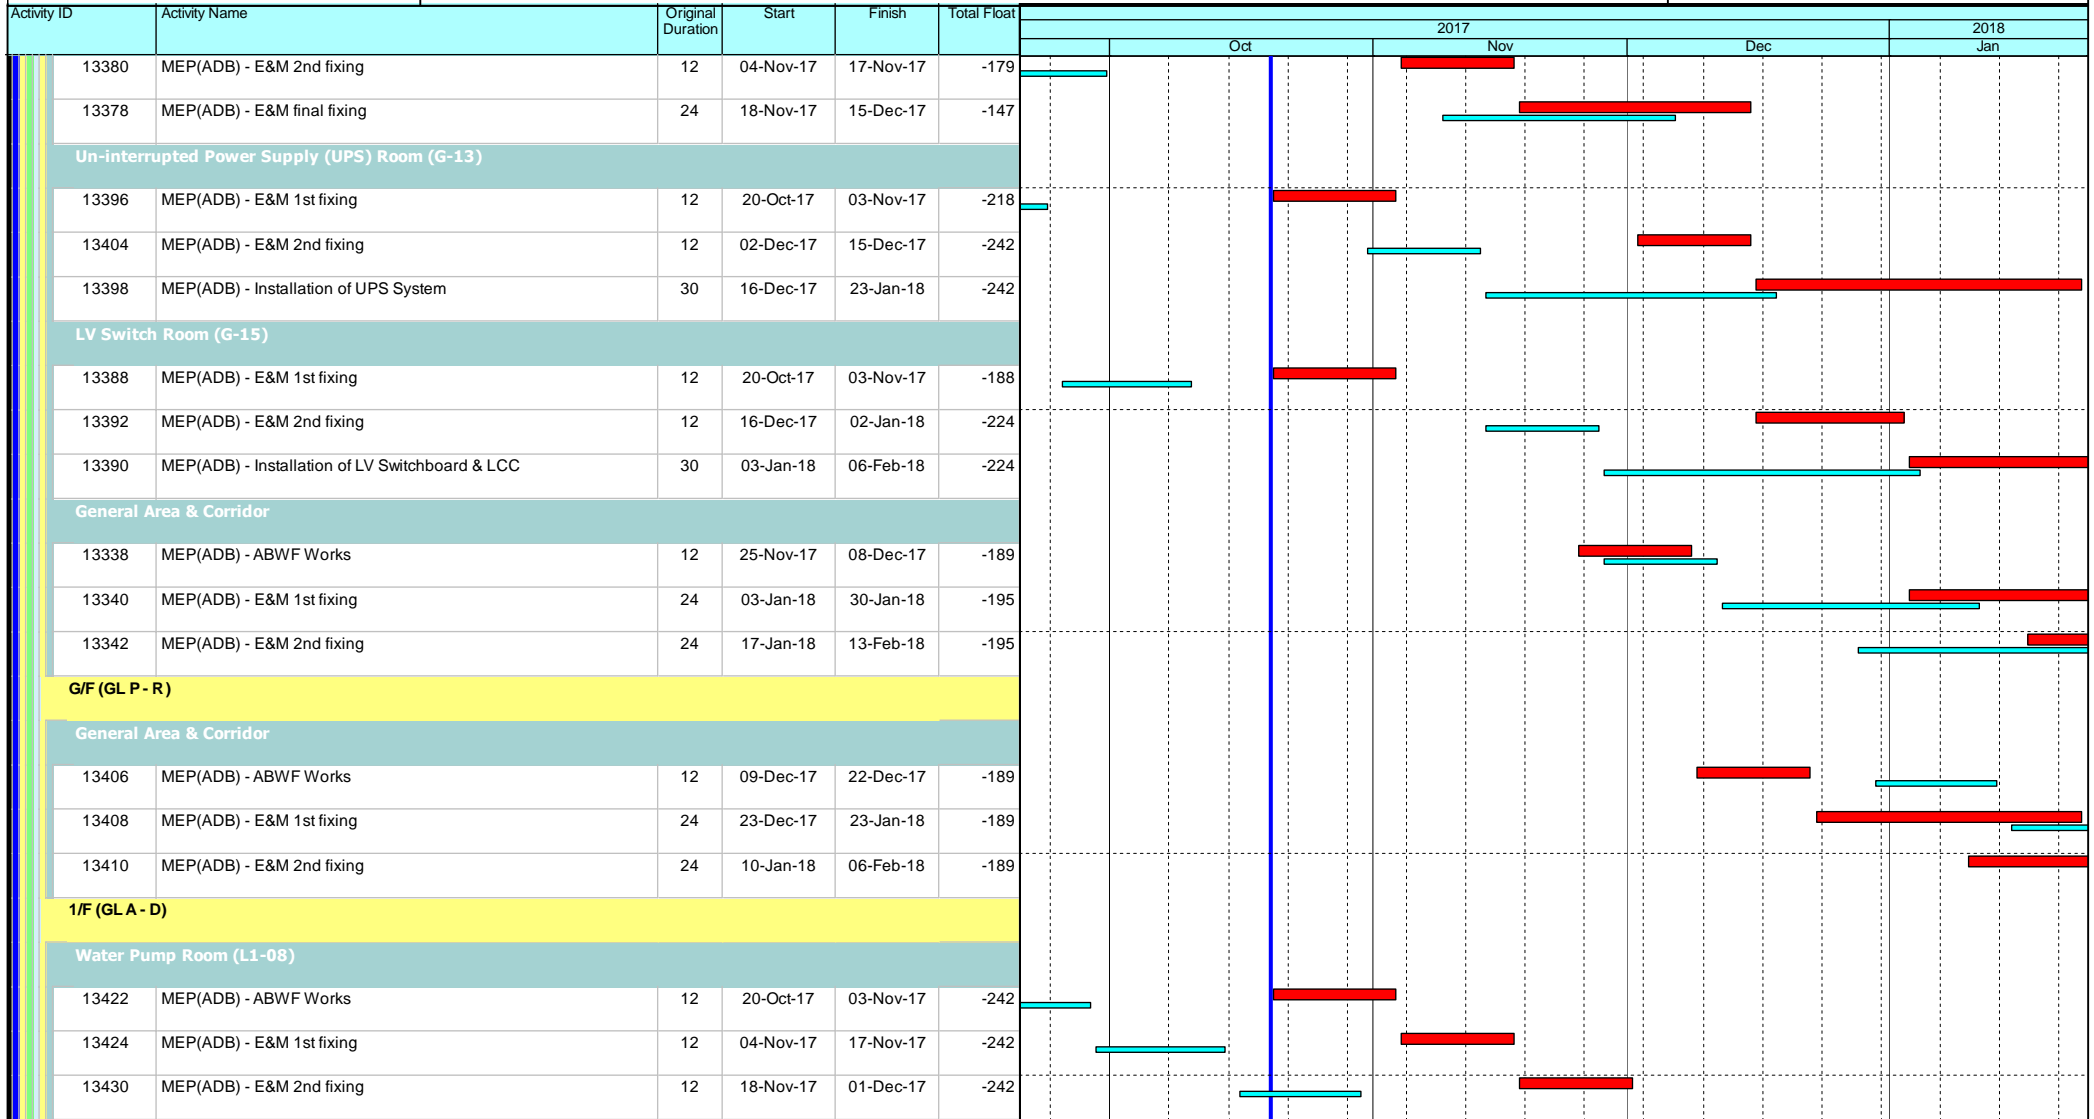

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING

Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 49 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017				2018
						Oct	Nov	Dec	Jan	
13426	MEP(ADB) - Installation of water Pump	24	02-Dec-17	02-Jan-18	-195					
13428	MEP(ADB) - E&M final fixing	24	03-Jan-18	30-Jan-18	-195					
General Area & Corridor										
13414	MEP(ADB) - ABWF Works	12	04-Nov-17	17-Nov-17	-199					
13416	MEP(ADB) - E&M 1st fixing	24	18-Nov-17	15-Dec-17	-195					
13418	MEP(ADB) - E&M 2nd fixing	24	03-Jan-18	30-Jan-18	-195					
External Works										
19120	ADB - Cable trench for HEC cable laying (Oil street to ADB) (Available from C19)	0	23-Oct-17*		-230					
19122	ADB - Cable ducting for HEC cable laying (VO/090) (Depends on access from C19)	12	23-Oct-17	06-Nov-17	-218					
19124	ADB - HKE cable laying (Oil street to ADB) (Depends on HKE schedule and access from C19)	40	07-Nov-17	22-Dec-17	-230					
19124a	ADB - cable trench / ductings ready for HKE cable laying (Oil street to ADB)	0	07-Nov-17		-230					
19126	ADB - Cable trench backfill (assume 3 layers) (Depends on HKE schedule and access from C19)	18	23-Dec-17	16-Jan-18	-230					
13432	ADB - Road and drainage works (EVA)	24	17-Jan-18	13-Feb-18	-170					
East Ventilation Shaft (EVS)										
ABWF Works										
3822	EVS - ABWF (Wet Trade) (Progress affected by high humidity and rainy weather)	60	12-Apr-16 A	26-Oct-17	-145					
3826	EVS - ABWF (Dry Trade)	60	20-Sep-17 A	24-Nov-17	-169					
3830	EVS - Metal works / steel platform / Ladders / Handrails	48	25-Nov-17	23-Jan-18	-169					
External Facade										
19060	EVS -Cone louvre installation	24	07-Feb-17 A	03-Nov-17	-118					
3832	EVS - Architectural Features of EVS	120	12-Jul-17 A	06-Dec-17	-146					
MEP Works										
3836	MEP(EVS) - E&M 1st Fix	12	05-Sep-17 A	26-Oct-17	-121					
3838	MEP(EVS) - E&M 2nd Fix	12	20-Sep-17 A	03-Nov-17	-121					

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 50 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

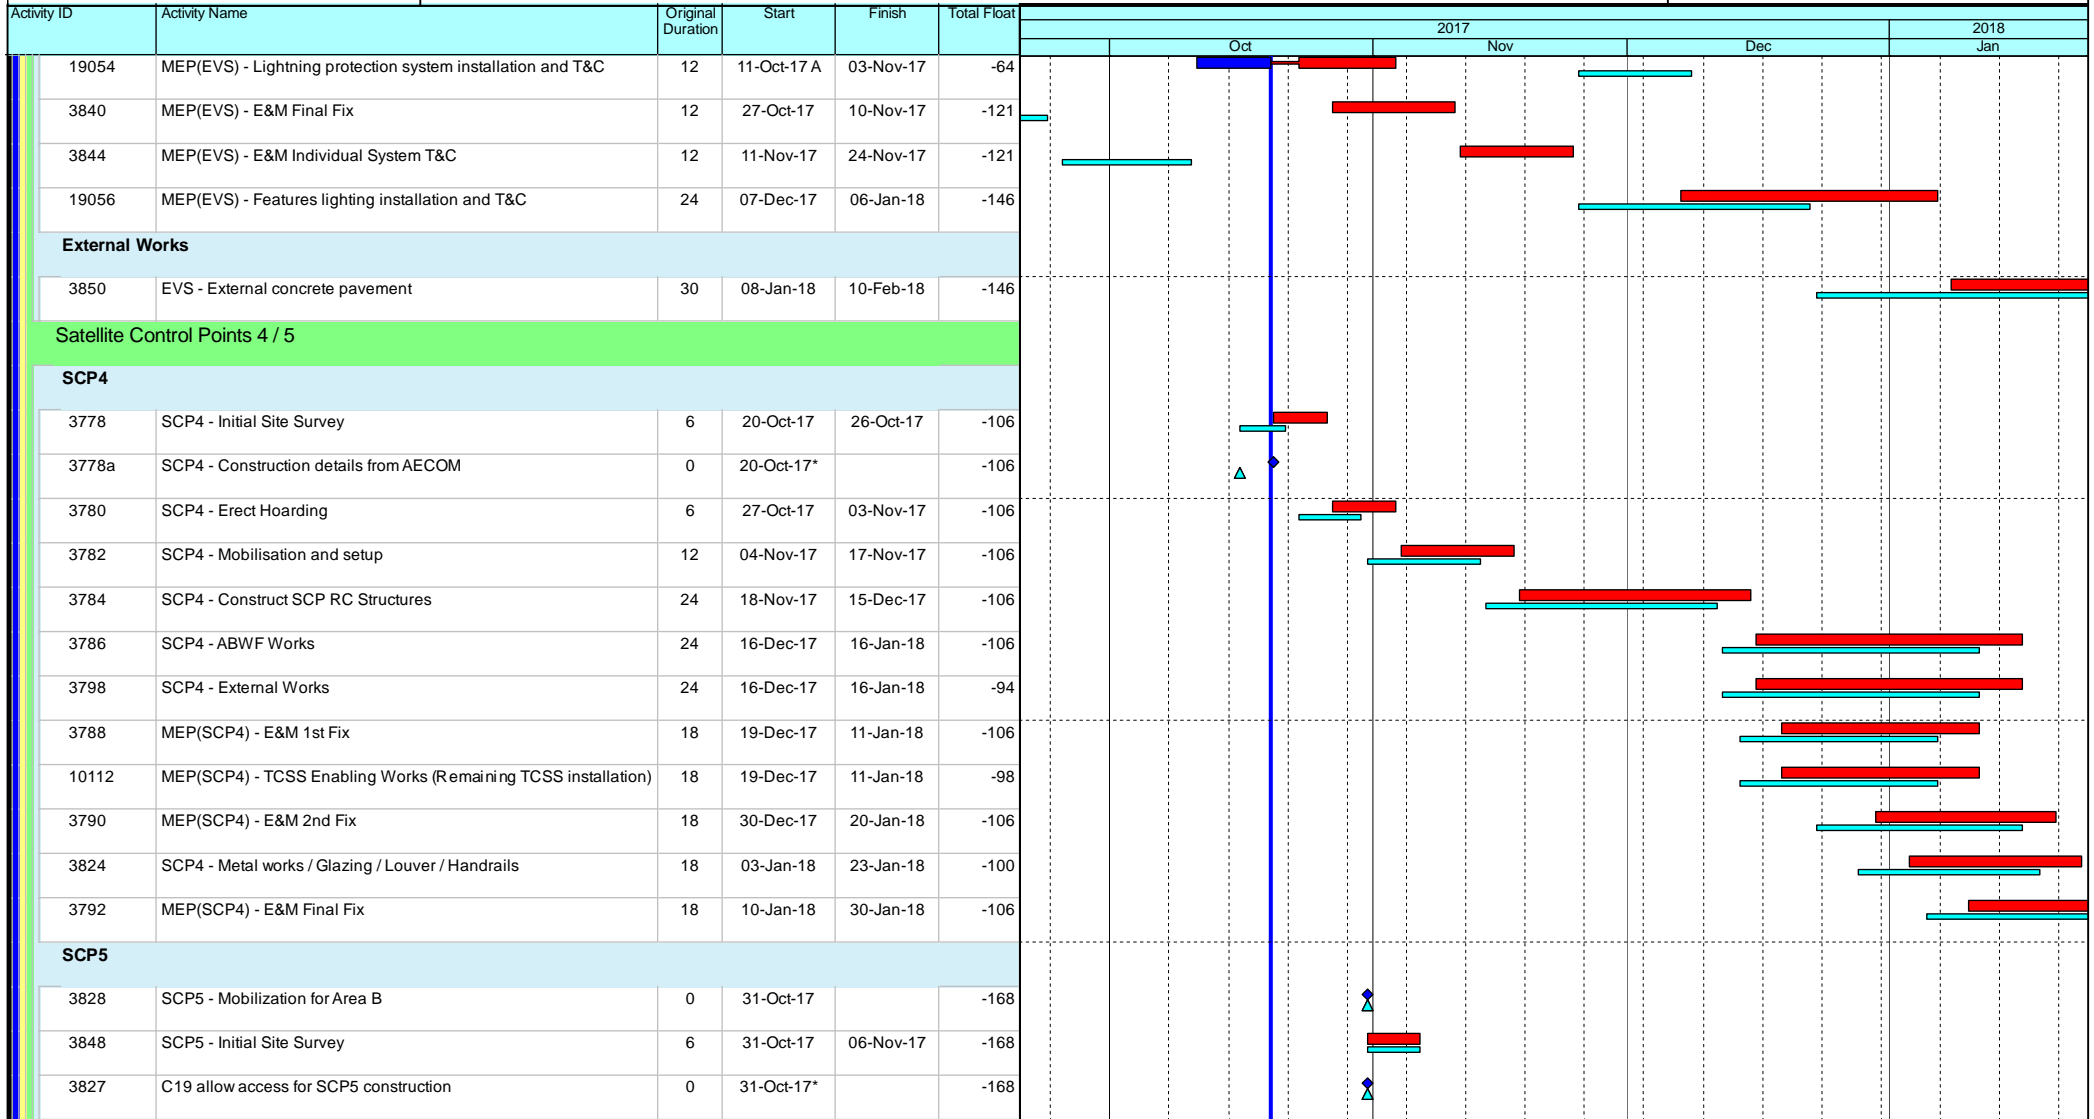

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 51 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

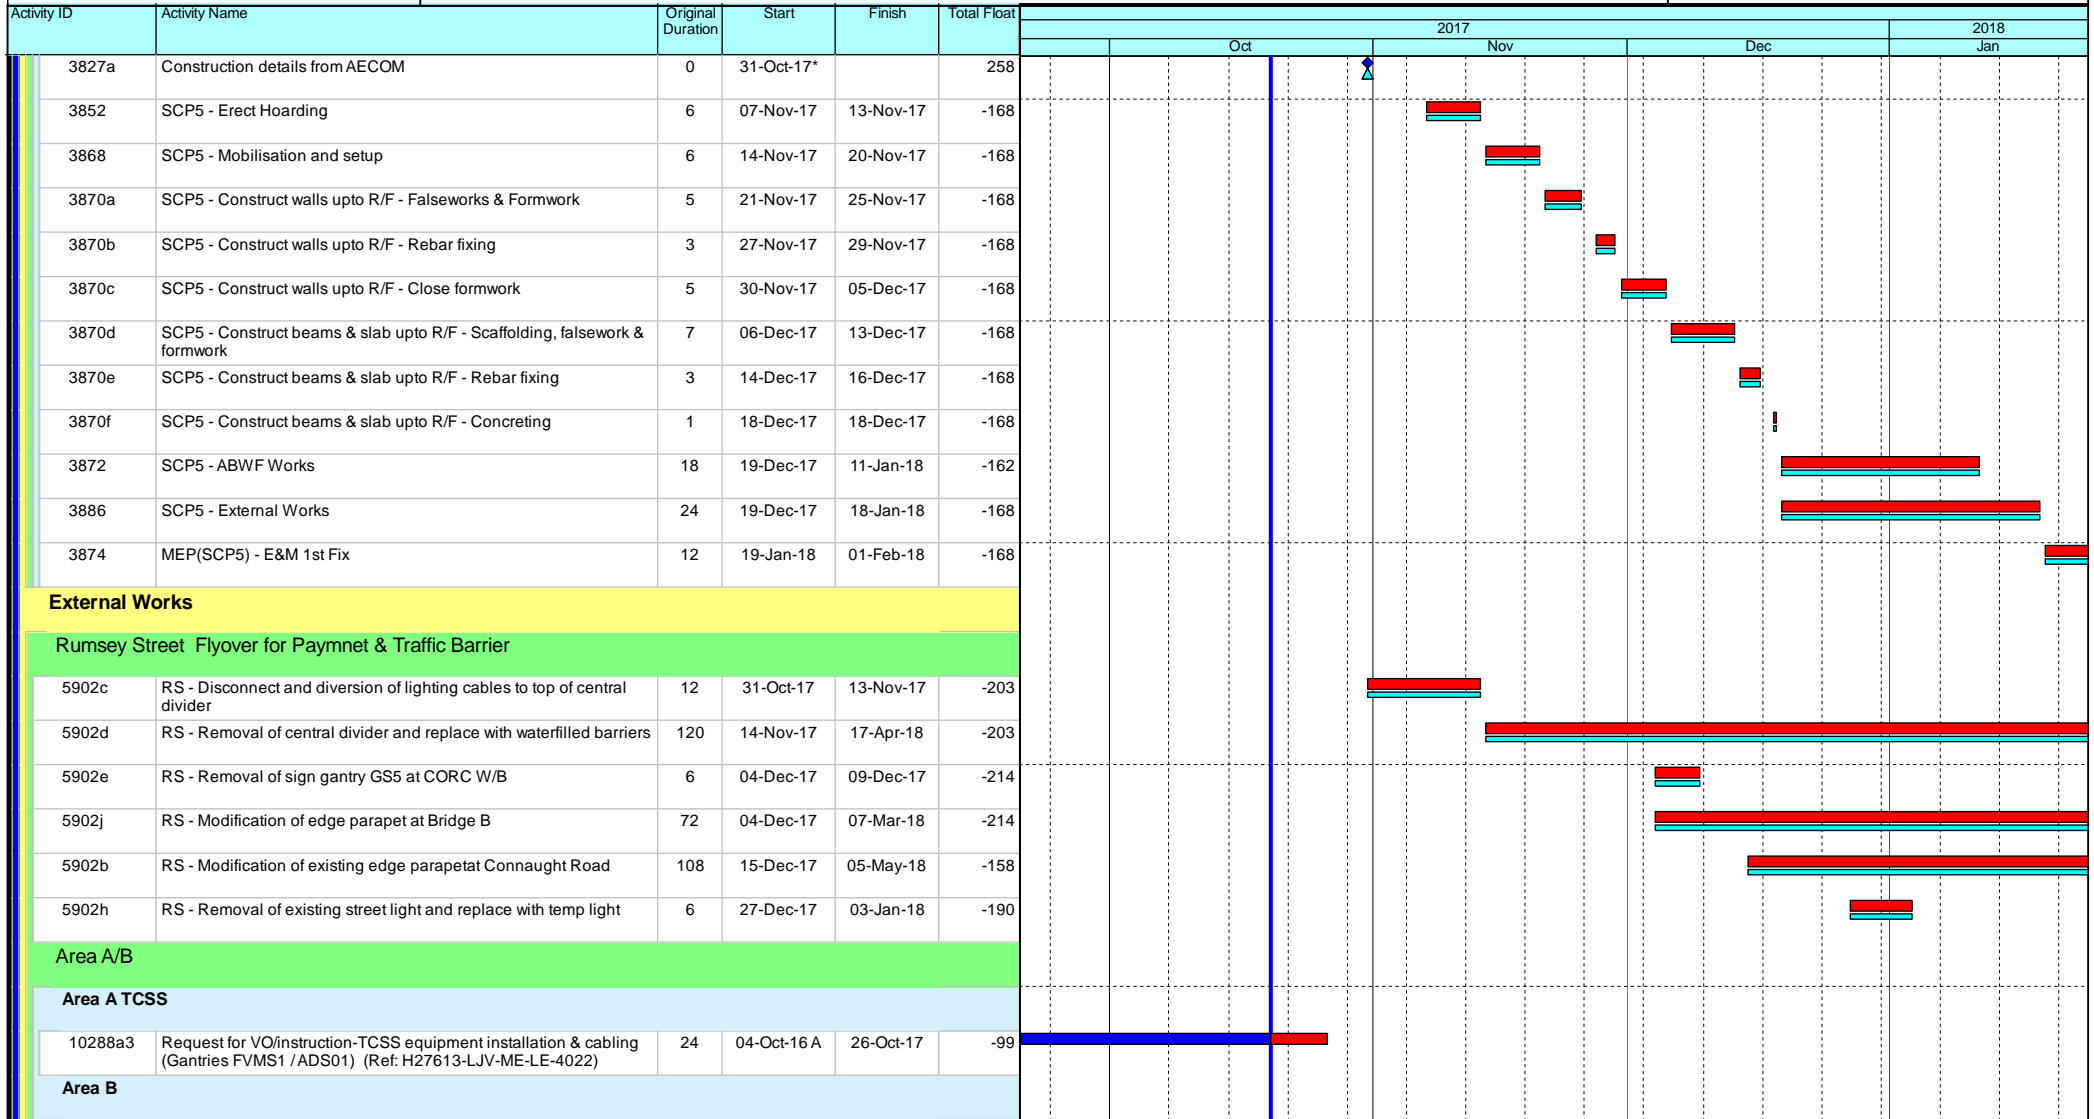

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING



Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 52 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

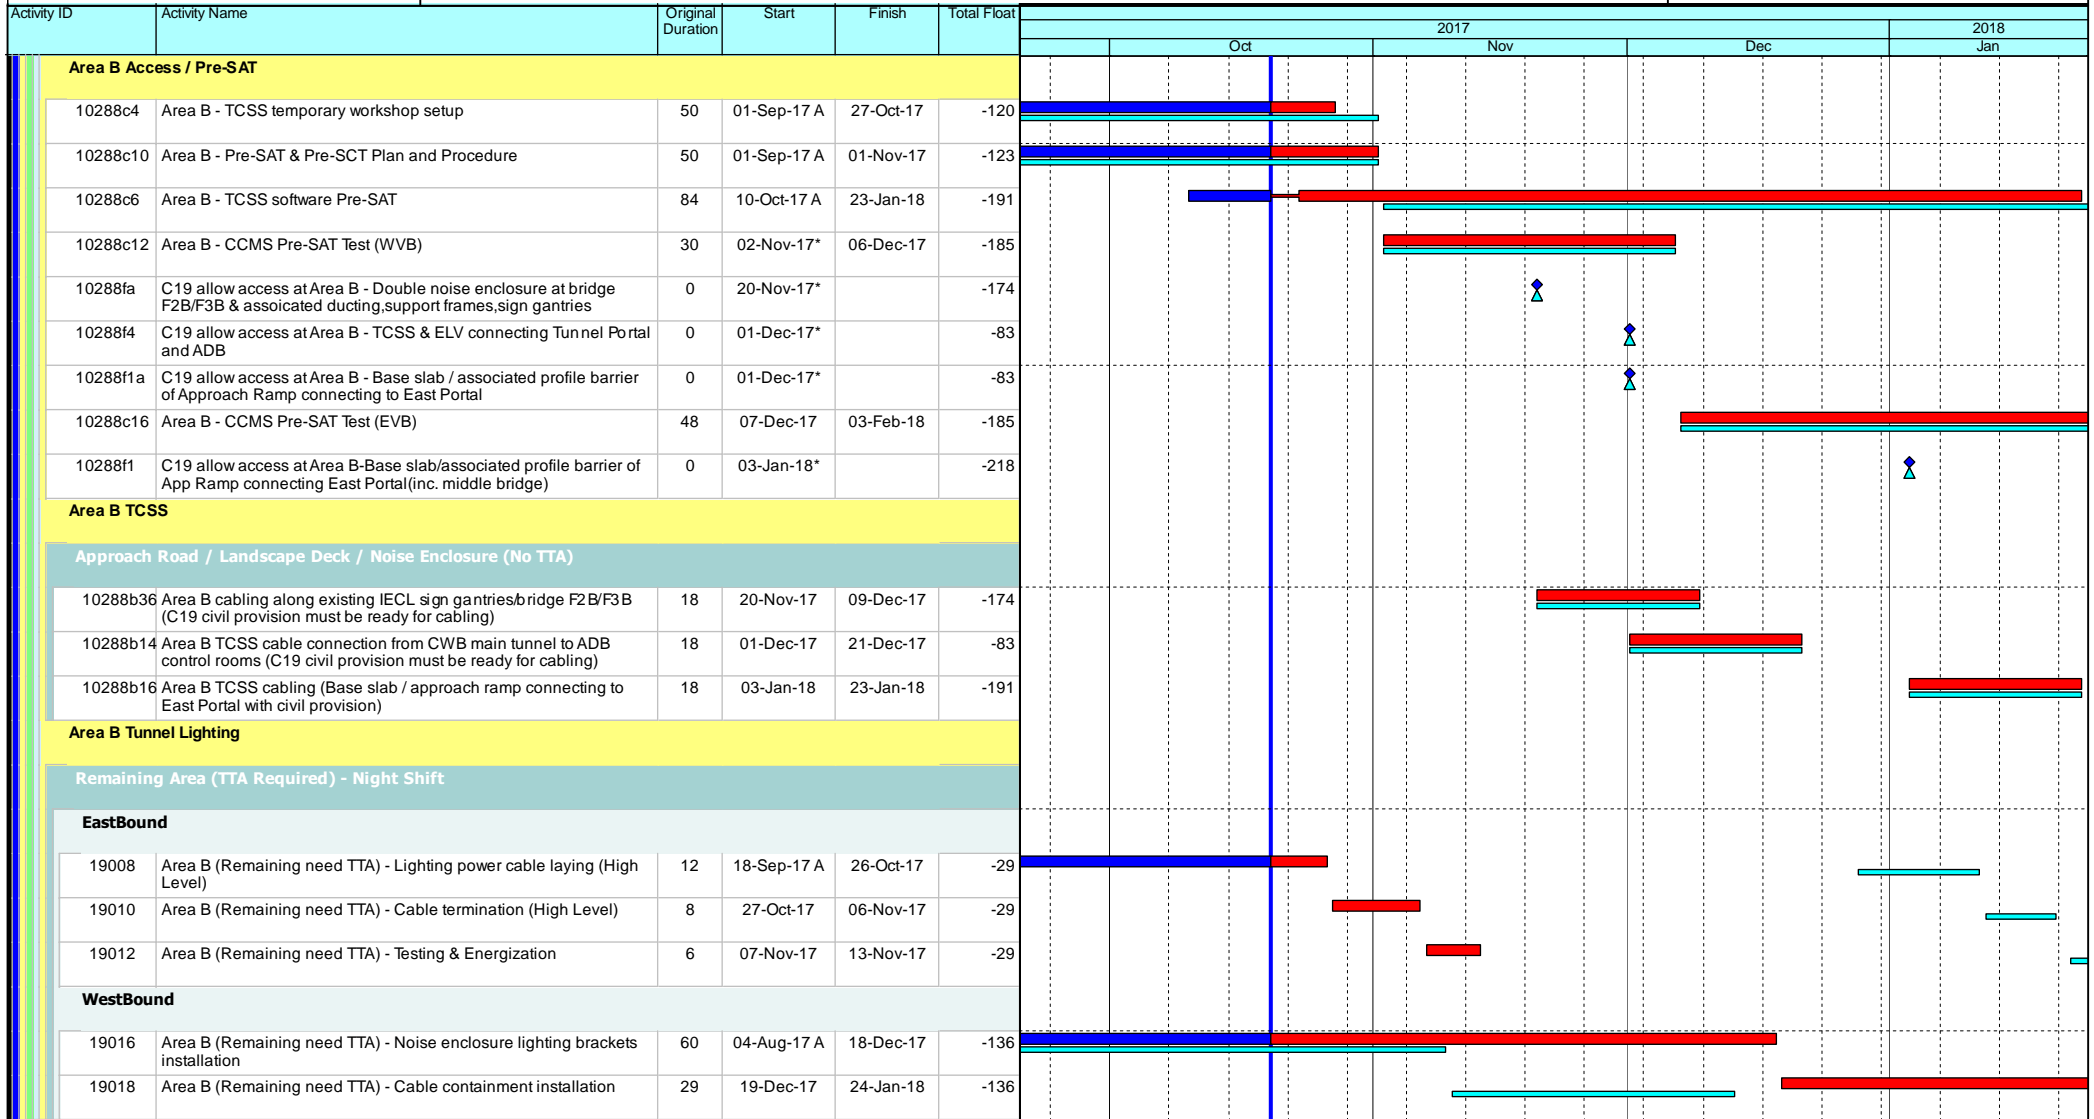

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING

Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 53 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW

Data Date: 20-Oct-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017				2018
						Oct	Nov	Dec	Jan	
Training / Plan / Manual for Project Completion										
Operation Manual for CWB Opening										
10198	Operation Manual for CWB opening - Draft submission (Cost Centre 9A. 9B)	24	03-Jan-18	30-Jan-18	-218					
Training Plan for CWB Opening										
10206	Training Plan for CWB opening - Draft submission	18	06-Nov-17	25-Nov-17	-177					
10206a	Training Plan for CWB opening - Draft approval	18	27-Nov-17	16-Dec-17	-177					
10208	Training Plan for CWB opening - Final submission	18	18-Dec-17	10-Jan-18	-177					
10208a	Training Plan for CWB opening - Final approval	18	11-Jan-18	31-Jan-18	-177					
Training Material for CWB Opening										
10210	Training Material for CWB opening - Draft submission	18	18-Dec-17	10-Jan-18	-177					
10210a	Training Material for CWB opening - Draft approval	18	11-Jan-18	31-Jan-18	-177					

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 44 (October 2017) THREE MONTH ROLLING

Project ID: H2613-U044
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U044
 Page 54 of 54

Date	Revision	Checked	Appro...
20-Sep-17	U043	AT	CW
20-Oct-17	U044	AT	CW
