


Contract No. HK/2009/01

Wan Chai Development Phase II – Central -Wan Chai Bypass at
Hong Kong Convention and Exhibition Centre

Construction Activities for Three Months Rolling

Construction Activities	November 2017	December 2017	January 2018
Reinstatement of Amenity Area			



Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2018	2018	2018	
					Jan	Feb	Mar	
HK/2012/08 Revised Works Programme Rev.12.0(DD 20 November 2017)								
Dredging and Reclamation								
Marine Work Construction								
Zone D								
Seawall Construction - Zone D								
Seawall 10 & 11								
MAR20630	Zone D - Seawall 10 & 11: Install remaining seawall block	14	08-Jan-2018*	21-Jan-2018	[Green bar]			
MAR20650	Zone D - Seawall 10 & 11: Backfill Type A	7	22-Jan-2018	28-Jan-2018	[Green bar]			
MAR20670	Zone D - Seawall 10 & 11: Lay geotextile and filter	7	29-Jan-2018	04-Feb-2018	[Green bar]			
Works for Section Completion								
Construction								
Section III A - Road A2, A4 & A5								
Roadwork & Utilities - Section 1 (L1806 - L1801)								
SIIIA10270	Sec III A - section 1 carriageway - Construct M/H F9	7	20-Dec-2017	29-Dec-2017	[Green bar]			
SIIIA10272	Sec III A - section 1 carriageway - connect M/F F9 to existing pipe	7	30-Dec-2017	08-Jan-2018	[Green bar]			
SIIIA10274	Sec III A - section 1 carriageway - construct M/H F8C	7	20-Dec-2017	29-Dec-2017	[Green bar]			
SIIIA10276	Sec III A - section 1 carriageway - sewerage pipe from M/H F9 to F8C	3	30-Dec-2017	03-Jan-2018	[Green bar]			
SIIIA10278	Sec III A - section 1 carriageway - sewerage pipe from M/H 8C to F8B	15	30-Dec-2017	17-Jan-2018	[Green bar]			
SIIIA10279b	Sec III A - section 1 carriageway - sewerage pipe from M/H 8C to F8B (night time): construct M/H F8B	6	13-Dec-2017 A	28-Dec-2017	[Green bar]			
SIIIA10279c	Sec III A - section 1 carriageway - sewerage pipe from M/H 8C to F8B (night time): construct sewerage pipe	29	02-Jan-2018	03-Feb-2018	[Red bar]			
SIIIA10292	Sec III A - section 1 carriageway - construct M/H F8A	7	09-Jan-2018	16-Jan-2018	[Green bar]			
SIIIA10293	Sec III A - section 1 carriageway - sewerage pipe from M/H F8B - F8A (night time)	6	05-Feb-2018	10-Feb-2018	[Red bar]			
SIIIA10294	Sec III A - section 1 carriageway - sewerage pipe from M/H F8A - F8	11	17-Jan-2018	29-Jan-2018	[Green bar]			
SIIIA10295	Sec III A - carriageway - works prior TTA stage 5: excavation and duct laying of TCSS and public lighting	7	18-Jan-2018	25-Jan-2018	[Green bar]			
SIIIA10296	Sec III A - section 1 carriageway - works prior TTA stage 5: reinstate damaged manhole and pipeline	14	20-Dec-2017	08-Jan-2018	[Green bar]			
SIIIA10297	Sec III A - section 1 carriageway - works prior TTA stage 5: construct 225mm storm drain from D5.2 to existing	7	09-Jan-2018	16-Jan-2018	[Green bar]			
SIIIA10298	Sec III A - section 1 carriageway - works prior TTA stage 5: road kerb	5	26-Jan-2018	31-Jan-2018	[Green bar]			
SIIIA10301	Sec III A - section 1 carriageway - works prior TTA stage 5: road formation	2	01-Feb-2018	02-Feb-2018	[Green bar]			
SIIIA10302	Sec III A - section 1 carriageway - works prior TTA stage 5: laying asphalt	5	03-Feb-2018	08-Feb-2018	[Green bar]			
SIIIA10303	Sec III A - section 1 carriageway - works prior TTA stage 5: road marking & preparation works	3	12-Feb-2018	14-Feb-2018	[Red bar]			
SIIIA10310	Sec III A - section 1 carriageway - TTA stage 5: Implementation of TTA Stage 5	1	15-Feb-2018	15-Feb-2018	[Red dot]			
Roadwork & Utilities - Section 2 (L1810 - L1807)								
SIIIA12550	Sec III A - roadwork and utilities section 2 carriageway - Utilities: HEC along carriageway & Crossroad duct (HEC &	7	25-Nov-2017 A	29-Dec-2017	[Green bar]			
SIIIA12570	Sec III A - roadwork and utilities section 2 carriageway - road kerb & formation	17	30-Dec-2017	19-Jan-2018	[Green bar]			
SIIIA12590	Sec III A - roadwork and utilities section 2 carriageway - black top	7	20-Jan-2018	27-Jan-2018	[Green bar]			

Data Date: 20-Dec-2017

- ◆ Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Remaining Level of Effort

3 Months Rolling Programme for Non-CR III Area (January 2018 - March 2018)
(Ref. to Revised Works Programme Rev.12)

Date	Revision	Checked	Approved
20-Dec-2017	12		



Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2018		
					Jan	Feb	Mar
Roadwork & Utilities - Section 3 (L1808 - L1102)							
SI3A12710	Sec III A - roadwork and utilities section 3 carriageway - Drainage works (L1301 - L1102)	2	11-Dec-2017 A	21-Dec-2017			
SI3A12750	Sec III A - roadwork and utilities section 3 carriageway - gully pipe (L1808A - L1102)	12	22-Dec-2017	08-Jan-2018			
SI3A12762	Sec III A - roadwork and utilities section 3 carriageway - watermain	10	09-Jan-2018	19-Jan-2018			
SI3A12770	Sec III A - roadwork and utilities section 3 carriageway - utilities: HEC ducting (60m) & crossroad duct (PCCW & HGC)	16	20-Jan-2018	07-Feb-2018			
SI3A12790	Sec III A - roadwork and utilities section 3 carriageway - road kerb & formation	17	08-Feb-2018	02-Mar-2018			
Roadwork & Utilities - Section 4 (L1406 - L1401)							
SI3A12950	Sec III A - roadwork and utilities section 4 carriageway - drainage works (L1402 - L1401)	4	11-Dec-2017 A	23-Dec-2017			
SI3A12970	Sec III A - roadwork and utilities section 4 carriageway - gully pipe (L1401)	10	27-Dec-2017	08-Jan-2018			
SI3A13000	Sec III A - roadwork and utilities section 4 carriageway - formation (L1401)	5	09-Jan-2018	13-Jan-2018			
SI3A13050	Sec III A - roadwork and utilities section 4 carriageway - black top (L1401)	5	15-Jan-2018	19-Jan-2018			
Roadwork & Utilities - Section 6 (L1102 - L1411)							
SI3A13380	Sec III A - roadwork and utilities section 6 carriageway - sealing up the gap beneath bay 12 of culvert L	0	08-Nov-2017 A	01-Dec-2017 A			
SI3A13385	Sec III A - roadwork and utilities section 6 carriageway - Waterproofing of water channel	3	02-Dec-2017 A	22-Dec-2017			
SI3A13389	Sec III A - roadwork and utilities section 6 carriageway - Backfilling of water channel from bay 16 to bay 20B	5	23-Dec-2017	30-Dec-2017			
SI3A13395	Sec III A - roadwork and utilities section 6 carriageway - Drainage works (L1101-L1102)	9	02-Jan-2018	11-Jan-2018			
SI3A13399	Sec III A - roadwork and utilities section 6 carriageway - gully pipe (L1101 - L1102)	8	12-Jan-2018	20-Jan-2018			
SI3A13444	Sec III A - roadwork and utilities section 6 carriageway - watermain (road crossing)	7	22-Jan-2018	29-Jan-2018			
SI3A13445	Sec III A - roadwork and utilities section 6 carriageway - utilities: crossed duct(HEC , HGC, PCCW)	13	30-Jan-2018	13-Feb-2018			
SI3A13450	Sec III A - roadwork and utilities section 6 carriageway - road kerb & formation	18	14-Feb-2018	09-Mar-2018			
Section V - Remaining At-Grade Road & Road P2							
Roadwork & Utilities							
Section 1 (L1504 - L1900)							
SV12456	Sec V-Roadwork & Utilities Section 1 - implementation of TTA stage 5E (closure of slow lane at northbound of Expo	1	15-Jan-2018*	15-Jan-2018			
SV12460	Sec V - Roadwork & Utilities Section 1 - drainage works (L1902 - L1900)	15	16-Jan-2018	01-Feb-2018			
SV12462	Sec V - Roadwork & Utilities Section 1 - gully pipe (L1902 - L1900)	6	02-Feb-2018	08-Feb-2018			
SV12464	Sec V - Roadwork & Utilities Section 1 - temp. reinstatement to match with existing Expo Drive	14	09-Feb-2018	28-Feb-2018			
SV12540	Sec V - Roadwork & Utilities Section 1 footpath - Watermain	6	11-Dec-2017 A	28-Dec-2017			
SV12570	Sec V - Roadwork & Utilities Section 1 footpath - utilities:TCSS	30	29-Dec-2017	02-Feb-2018			
SV12580	Sec V - Roadwork & Utilities Section 1 footpath - paving block	29	03-Feb-2018	12-Mar-2018			
Section 2 (L1510 - L1504)							
SV12622	Sec V - Roadwork & Utilities Section 1 Carriageway - gully pipe (L1611 - L1609)	8	13-Dec-2017 A	30-Dec-2017			
SV12624	Sec V - Roadwork & Utilities Section 1 Carriageway - road kerb & formation	21	02-Jan-2018	25-Jan-2018			
SV12626	Sec V - Roadwork & Utilities Section 1 Carriageway - black top	13	26-Jan-2018	09-Feb-2018			
SV12690	Sec V - Roadwork & Utilities Section 2 footpath - Drainage Works (L2104 - L2105)	18	23-Dec-2017	16-Jan-2018			
SV12692	Sec V - Roadwork & Utilities Section 2 footpath - U channel	14	17-Jan-2018	01-Feb-2018			
SV12695	Sec V - Roadwork & Utilities Section 2 footpath - Watermain	13	02-Feb-2018	20-Feb-2018			
Section 3 (Culvert L - L1510)							
SIV12810	Sec V - Roadwork & Utilities Section 3 Carriageway - Gully pipe (Culvert L - L1611)	3	24-Nov-2017 A	22-Dec-2017			
SIV12820	Sec V - Roadwork & Utilities Section 3 Carriageway - Black top	21	23-Dec-2017	19-Jan-2018			



Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2018		
					Jan	Feb	Mar
SIV12844	Sec V - Roadwork & Utilities Section 3 footpath - U channel	6	02-Dec-2017 A	28-Dec-2017			
SIV12850	Sec V - Roadwork & Utilities footpath - Watermain	14	29-Dec-2017	15-Jan-2018			
SIV12860	Sec V - Roadwork & Utilities Section 3 footpath - Utilities: TCSS, HGC, PCCW)	34	16-Jan-2018	27-Feb-2018			
Section IV - Slip Road 3							
Roadwork & Utilities							
Section 1 (L1608 - L1601)							
SIV11740	Sec IV - Re-Possion of the areas S and P	0	08-Dec-2017 A				
SIV11742	Sec IV - Re-Possion of the area at the end of Road P2	0	30-Dec-2017*				
SIV11744	Sec IV - sign gantry DS20 footing (type 1): remove existing 600mm drain pipe	4	20-Dec-2017*	23-Dec-2017			
SIV11745	Sec IV - sign gantry DS20 footing (type 1): excavation	2	27-Dec-2017	28-Dec-2017			
SIV11746	Sec IV - sign gantry DS20 footing (type 1): footing structure	14	29-Dec-2017	15-Jan-2018			
SIV11747	Sec IV - sign gantry DS20 & DS21 footing (type 2): excavation & ELS	21	30-Dec-2017	24-Jan-2018			
SIV11748	Sec IV - sign gantry DS20 & DS21 footing (type 2): footing structure	21	25-Jan-2018	21-Feb-2018			
SIV11760	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Drainage Works (L1607 - L1601)	30	09-Dec-2017 A	26-Jan-2018			
SIV11761	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Drainage Works (L1602 - L2005)	7	16-Jan-2018	23-Jan-2018			
SIV11762	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Drainage Works (L2103-L2101A)	17	27-Jan-2018	15-Feb-2018			
Section 2 (L2301 - L2103)							
SIV11940	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Drainage Works (L2301-L2103)	5	09-Dec-2017 A	27-Dec-2017			
SIV11942	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Gully pipe (L2301-L2013, L1608-L1609)	22	28-Dec-2017	23-Jan-2018			
SIV11960	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Watermain	10	24-Jan-2018	03-Feb-2018			
SIV12010	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Road kerb & formation	20	05-Feb-2018	02-Mar-2018			
Section 3 (M/H1.6 - L2301)							
SIV12092	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Drainage Works (M/H1.7 - L2301)	59	28-Dec-2017	10-Mar-2018			
SIV12096	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - M1.7-M1.6: construct manholes	28	29-Nov-2017 A	24-Jan-2018			
SIV12102	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - M1.7-M1.6: demolish existing seawall	13	25-Jan-2018	08-Feb-2018			
SIV12103	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - M1.7-M1.6: ELS	10	09-Feb-2018	23-Feb-2018			
Section VII - Remainder Works							
Road & Drainage Works (Culvert L - M/H1.7, Adjacent to SR3)							
SVII11600	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - Drainage Works (Culvert L -MH1.7)	59	08-Jan-2018	20-Mar-2018			
Retaining Wall RW5 Construction							
SVII10660	Sec VII - Retaining Wall RW5 (bay 1) - construct base slab and wall	22	05-Feb-2018	05-Mar-2018			
SVII10800	Sec VII - Retaining wall RW5 (bay 3) - construct base slab and wall	22	05-Feb-2018	05-Mar-2018			
Promenade Seawall Parapet Construction & EVA							
Promenade Footpath							
Section 2							
SVII12610	Sec VII - section 2 footpath - drainage works : L2202 - L2203A	20	29-Jan-2018	23-Feb-2018			
Section 3							
SVII12850	Sec VII - section 3 footpath - watermain	17	20-Jan-2018	08-Feb-2018			
SVII12870	Sec VII - section 3 footpath - utilities (HEC, TCSS, HGC, PCCW)	40	09-Feb-2018	03-Apr-2018			
Section 4							



Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2018		
					Jan	Feb	Mar
SVII13050	Sec VII - section 4 footpath - drainage works (L2203 -L2203A)	0	21-Nov-2017 A	14-Dec-2017 A			
SVII13110	Sec VII - section 4 footpath - paving block	25	14-Feb-2018	17-Mar-2018		[Green bar spanning Feb and Mar]	
Section 5							
SVII13270	Sec VII - section 5 footpath - drainage works :L2203A -L2204	10	15-Dec-2017 A	03-Jan-2018	[Green bar]		
SVII13275	Sec VII - section 5 footpath - watermain	14	04-Jan-2018	19-Jan-2018	[Green bar]		
SVII13310	Sec VII - section 5 footpath - utilities: HEC, TCSS, HGC, PCCW	42	20-Jan-2018	13-Mar-2018		[Green bar spanning Feb and Mar]	
Section 6							
SVII13490	Sec VII - section 6 footpath - drainage works(Culvert L - L2204)	14	12-Jan-2018	27-Jan-2018	[Green bar]		
SVII13510	Sec VII - section 6 footpath - watermain	13	03-Feb-2018	21-Feb-2018		[Green bar]	
Section X - Protection & Preservation of Trees							
Soft Landscaping Works							
SX10020	Sec X - Protection & Preservation of Trees	276	31-Jan-2013 A	21-Sep-2018	[Red bar spanning all months]		

Activity ID	Activity Name	Rem Dur	Start	Finish	2017							2018						
					December							January						
					17	24	31	07	14	21	28	04	11	18	25	04	11	18
3MRP (Dec 2017 - Mar 2018)																		
03 - PRELIMINARY WORKS																		
03.3 - Interface Works																		
0330-1040	Relocate FEHD to Permanent Depot	9	30-Dec-17	10-Jan-18	Relocate FEHD to Permanent Depot													
0330-1045	Clean-up Area after Relocation	3	11-Jan-18	13-Jan-18	Clean-up Area after Relocation													
FEHD Permanent Depot																		
0330-1071	Installation of Post (43Nos) > Facility Area 5 & 10	6	20-Dec-17*	27-Dec-17	Installation of Post (43Nos) > Facility Area 5 & 10													
0330-1073	Construction of Steel Roof > Facility Area 5 & 10	6	26-Dec-17	02-Jan-18	Construction of Steel Roof > Facility Area 5 & 10													
0330-1075	Sprinkler System Installation > Facility Area 5 & 10	7	30-Dec-17	08-Jan-18	Sprinkler System Installation > Facility Area 5 & 10													
0330-1077	T & C of Sprinkler System > Facility Area 5 & 10	6	09-Jan-18	15-Jan-18	T & C of Sprinkler System > Facility Area 5 & 10													
0330-1081	Installation of Post (73Nos) > Facility Area 6, 8 & 9	9	20-Dec-17	30-Dec-17	Installation of Post (73Nos) > Facility Area 6, 8 & 9													
0330-1095	Signage Works & remaining light post	3	20-Dec-17	22-Dec-17	Signage Works & remaining light post													
A4910	Road Marking & Misc Works	8	20-Dec-17	29-Dec-17	Road Marking & Misc Works													
10 - SECTION X OF THE WORKS																		
10.1 - E/B Bridges (Bridge D, E and F)																		
10.1.4 - Bridge E / Hing Fat Slip Road																		
Bridge Construction																		
1014-2280	Bridge E - Construct Permanent parapet at "TB" Tie-in	9	08-Sep-17 A	30-Dec-17	Bridge E - Construct Permanent parapet at "TB" Tie-in													
10.3 - Middle Bridge (Bridge F)																		
10.3.2 - Bridge Construction																		
Bridge F3B																		
1032-2550	Bridge F3B - Installation of CC & Temporary Lighting	14	04-Dec-17 A	06-Jan-18	Bridge F3B - Installation of CC & Temporary Lighting													
1032-2560	Bridge F3B - Deck Road Waterproofing, Surfacing & Marking	6	08-Jan-18	13-Jan-18	Bridge F3B - Deck Road Waterproofing, Surfacing & Marking													
1032-2561	Divert 2 Lane Traffic (Stage 1)	0	14-Jan-18		◆ Divert 2 Lane Traffic (Stage 1)													
1032-2562	Bridge F3B - Construct Int. Double Noise Encl. (83m) (stage 2)	26	15-Jan-18	13-Feb-18	Bridge F3B - Construct Int. Double Noise Encl. (83m) (stage 2)													
1032-2563	Bridge F3B - Deck Road Waterproofing, Surfacing & Marking	6	08-Feb-18	14-Feb-18	Bridge F3B - Deck Road Waterproofing, Surfacing & Marking													
1032-2564	Divert 2 Lane Traffic (Stage 2)	0	15-Feb-18		◆ Divert 2 Lane Traffic (Stage 2)													
Bridge F2B																		
1032-3120	Bridge F2B - Construct Int. Double Noise Encl.	14	11-Nov-17 A	06-Jan-18	Bridge F2B - Construct Int. Double Noise Encl.													
1032-3140	Bridge F2B - Deck Road Waterproofing, Surfacing & Marking	6	08-Jan-18	13-Jan-18	Bridge F2B - Deck Road Waterproofing, Surfacing & Marking													
Bridge F1B2																		
1032-3840	Bridge F1B2 - Longitudinal Stitching	33	19-Jan-18	01-Mar-18	Bridge F1B2 - Longitudinal Stitching													
1032-3860	Bridge F1B2 - Southern Parapet	24	14-Dec-17 A	18-Jan-18	Bridge F1B2 - Southern Parapet													
1032-3880	Bridge F1B2 - Construct Int. Double Noise Encl. Bridge F1B2	48	13-Jan-18	13-Mar-18	Bridge F1B2 - Construct Int. Double Noise Encl. Bridge F1B2													
1032-3900	Bridge F1B2 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking	7	14-Mar-18	21-Mar-18	Bridge F1B2 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking													
Bridge F1B1																		
1032-1740	Bridge F1B1 - Longitudinal Stitching	57	16-Dec-17 A	01-Mar-18	Bridge F1B1 - Longitudinal Stitching													
1032-1760	Bridge F1B1 - Construct Median Barriers	30	29-Dec-17	02-Feb-18	Bridge F1B1 - Construct Median Barriers													
1032-1780	Bridge F1B1 - Construct Int. Double Noise Encl. Bridge F1B2	46	16-Jan-18	13-Mar-18	Bridge F1B1 - Construct Int. Double Noise Encl. Bridge F1B2													

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Dec.2017 to 19.Mar.2018)

Activity ID	Activity Name	Rem Dur	Start	Finish	2018																	
					January					February					March				April			
					21	28	04	11	18	25	04	11	18	25	01	08	15	22	29			
3MRP (Jan 2018 - April 2018)																						
03 - PRELIMINARY WORKS																						
03.3 - Interface Works																						
FEHD Permanent Depot																						
0330-1071	Installation of Post (43Nos) > Facility Area 5 & 10	6	22-Jan-18*	27-Jan-18	Installation of Post (43Nos) > Facility Area 5 & 10																	
0330-1073	Construction of Steel Roof > Facility Area 5 & 10	6	26-Jan-18	01-Feb-18	Construction of Steel Roof > Facility Area 5 & 10																	
0330-1075	Sprinkler System Installation > Facility Area 5 & 10	7	31-Jan-18	07-Feb-18	Sprinkler System Installation > Facility Area 5 & 10																	
0330-1077	T & C of Sprinkler System > Facility Area 5 & 10	6	08-Feb-18	14-Feb-18	T & C of Sprinkler System > Facility Area 5 & 10																	
0330-1081	Installation of Post (73Nos) > Facility Area 6, 8 & 9	9	20-Jan-18	30-Jan-18	Installation of Post (73Nos) > Facility Area 6, 8 & 9																	
10 - SECTION X OF THE WORKS																						
10.3 - Middle Bridge (Bridge F)																						
10.3.2 - Bridge Construction																						
Bridge F3B																						
1032-2562	Bridge F3B - Construct Int. Double Noise Encl. (83m) (stage 2)	21	15-Jan-18 A	13-Feb-18	Bridge F3B - Construct Int. Double Noise Encl. (83m) (stage 2)																	
1032-2563	Bridge F3B - Deck Road Waterproofing, Surfacing & Marking	6	08-Feb-18	14-Feb-18	Bridge F3B - Deck Road Waterproofing, Surfacing & Marking																	
1032-2564	Divert 2 Lane Traffic (Stage 2)	0	15-Feb-18		◆ Divert 2 Lane Traffic (Stage 2)																	
Bridge F1B2																						
1032-3840	Bridge F1B2 - Longitudinal Stitching	27	19-Jan-18 A	01-Mar-18	Bridge F1B2 - Longitudinal Stitching																	
1032-3860	Bridge F1B2 - Southern Parapet	5	14-Dec-17 A	25-Jan-18	Bridge F1B2 - Southern Parapet																	
1032-3880	Bridge F1B2 - Construct Int. Double Noise Encl. Bridge F1B2	30	13-Jan-18 A	27-Feb-18	Bridge F1B2 - Construct Int. Double Noise Encl. Bridge F1B2																	
1032-3900	Bridge F1B2 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking	7	02-Mar-18	09-Mar-18	Bridge F1B2 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking																	
Bridge F1B1																						
1032-1740	Bridge F1B1 - Longitudinal Stitching	0	16-Dec-17 A	17-Jan-18 A	Bridge F1B1 - Longitudinal Stitching																	
1032-1780	Bridge F1B1 - Construct Int. Double Noise Encl. Bridge F1B2	30	16-Jan-18 A	27-Feb-18	Bridge F1B1 - Construct Int. Double Noise Encl. Bridge F1B2																	
1032-1800	Bridge F1B1 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking	7	02-Mar-18	09-Mar-18	Bridge F1B1 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking																	
Bridge F5																						
1032-4040	Cutting of Deck Between Temp. TD & E/B > Pier F5-F8	12	15-Feb-18	03-Mar-18	Cutting of Deck Between Temp. TD & E/B > Pier F5-F8																	
1032-4060	Cutting of Deck Between Temp. TD & E/B > Pier F8-F11	12	05-Mar-18	17-Mar-18	Cutting of Deck Between Temp. TD & E/B > Pier F8-F11																	
1032-4080	Cutting of Deck Between Temp. TD & E/B > Pier F11-F14	12	19-Mar-18	03-Apr-18	Cutting of Deck Between Temp. TD & E/B > Pier F11-F14																	
1032-4100	Construction Parapet (Northside) > Pier F5-F8	12	26-Feb-18	10-Mar-18	Construction Parapet (Northside) > Pier F5-F8																	
1032-4120	Construction Parapet (Northside) > Pier F8-F11	12	12-Mar-18	24-Mar-18	Construction Parapet (Northside) > Pier F8-F11																	
1032-4140	Construction Parapet (Northside) > Pier F11-F14	12	26-Mar-18	11-Apr-18	Construction Parapet (Northside) > Pier F11-F14																	
1032-4160	Construct Noise Enclosure (Northside) > Pier F5 - F8	24	12-Mar-18	11-Apr-18	Construct Noise Enclosure (Northside) > Pier F5 - F8																	
All Middle Bridge F (Common)																						
1032-4240	Fresh Water Main 150DI at Bridge F Deck	52	27-Nov-17 A	24-Mar-18	Fresh Water Main 150DI at Bridge F Deck																	
1032-4260	Bridge F Sign Gantries and Misc. Mounting Structure/Support	25	26-Dec-17 A	21-Feb-18*	Bridge F Sign Gantries and Misc. Mounting Structure/Support																	
1032-4356	Sign Gantry (DS06B,DS06A & FADS06) (Nighth work)	50	22-Feb-18	24-Apr-18	Sign Gantry (DS06B,DS06A & FADS06) (Nighth work)																	

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Jan.2018 to 19.Apr.2018)

Activity ID	Activity Name	Original Duration	Start	Finish	2018																		
					Feb	Mar	Apr	May	Jun														
Total		1876d	21-Mar-13 A	21-Jun-18																			
DWP-08 - (2) - Update Progress As of 20 Feb 18		1876d	21-Mar-13 A	21-Jun-18																			
Works in KD8		24d	05-Feb-18 A	27-Feb-18 A																			
TS3W - Remove Temporary Reclamation		24d	05-Feb-18 A	27-Feb-18 A																			
Stage 7 - Remove D-wall W4D13, 14 & W4D12, W4D15 - 16 + W3D8 - W3D11 & Seawall Reinstatement		24d	05-Feb-18 A	27-Feb-18 A																			
Reinstatement of Remaining Vertical Seawall by Land Plants		24d	05-Feb-18 A	27-Feb-18 A																			
MW_1610	Pour concrete behind 5th layer of facing stone	1d	05-Feb-18 A	05-Feb-18 A																			
MW_1630	Erect Formwork for coping	3d	06-Feb-18 A	09-Feb-18 A																			
MW_1640	Pour concrete for coping	1d	10-Feb-18 A	10-Feb-18 A																			
MW_1660	Lay footpath paving blocks	4d	11-Feb-18 A	14-Feb-18 A																			
MW_1650	Backfill up to formation level (6 layers)	13d	26-Feb-18 A	27-Feb-18 A																			
Works in KD6		132d	30-Aug-17 A	20-Mar-18																			
Works in SR8 (Open Cut Method)		132d	30-Aug-17 A	20-Mar-18																			
SR8 (Zone C) - Ch. 528 to Ch. 368		74d	30-Aug-17 A	20-Mar-18																			
Zone C - Tunnel Structure		74d	30-Aug-17 A	20-Mar-18																			
Egress Passage - EP01		74d	30-Aug-17 A	20-Mar-18																			
A9050	Steel Railing - Fabrication & Installation	74d	30-Aug-17 A	20-Mar-18																			
SR8 (Zone B) - Ch.385.000 to Ch.317.500 - (Inside Victoria Park to Tunnel Portal)		16d	21-Feb-18 A	16-Mar-18																			
SR8 (Zone B) Tunnel - ELS / CCT / BF Works (7 Bays Ch. 385.000 to Ch.317.500)		16d	21-Feb-18 A	16-Mar-18																			
Portal Structure		16d	21-Feb-18 A	16-Mar-18																			
Pump House		7d	21-Feb-18 A	28-Feb-18 A																			
Remaining Works inside Pump Sump E		7d	21-Feb-18 A	28-Feb-18 A																			
Pump Sump E Hand Rail		7d	21-Feb-18 A	28-Feb-18 A																			
EXW_2530	Installation of handrail (agreed with CC contract)	7d	21-Feb-18 A	28-Feb-18 A																			
Remaining Works in Zone B		15d	28-Feb-18 A	16-Mar-18																			
Egress Passage		15d	28-Feb-18 A	16-Mar-18																			
EXW_2550	Railing installation (2 nos. - 10m)	15d	28-Feb-18 A	16-Mar-18																			
Works in KD9 (Include Re-provisioning Works of KD4,KD5)		185d	23-Oct-17 A	15-May-18																			
External Works Under KD9		185d	25-Oct-17 A	15-May-18																			
Zone 1		90d	15-Dec-17 A	27-Mar-18																			
Drainage Alignment Confirmation for MH72, 73, 74 due to Tree T1106		90d	15-Dec-17 A	27-Mar-18																			
EXW_1125	Drawing Confirmation and construction for MH2-74A and associated drainage	8d	15-Dec-17 A	25-Mar-18																			
EXW_1145	Pedestrian walkway open to public during Christmas and CNY	90d	23-Jan-18 A	27-Mar-18																			
Zone 2		35d	25-Oct-17 A	04-Apr-18																			
EXW_1890	Irrigation system construction	15d	25-Oct-17 A	04-Apr-18																			
EXW_1880	Boundary fence Installation	30d	01-Nov-17 A	04-Apr-18																			
Zone 3		35d	03-Mar-18	16-Apr-18																			
Traffic Island		35d	03-Mar-18	16-Apr-18																			
EXW_2050	Directional sign DS17 steel frame	7d	03-Mar-18*	10-Mar-18																			
EXW_2060	New VMS6 steel frame	7d	12-Mar-18	19-Mar-18																			
EXW_2070	TCSS and lighting at island	7d	20-Mar-18	26-Mar-18																			
EXW_2080	JTIS (3 nos. footings, 1 no. concrete plinth)	14d	27-Mar-18	16-Apr-18																			
Zone 4 up to Elderly Facilities		90d	30-Jan-18 A	15-May-18																			

Activity ID	Activity Name	Original Duration	Start	Finish	2018											
					Feb	Mar	Apr	May	Jun							
Elderly Facilities V/039 Received on 22 Jun 2017																
EXW_2270	Facilities fabrication	90d	30-Jan-18 A	15-May-18	Facilities fabrication											
Additional Walkway & Arbour V/040 Received on 22 Aug 2017																
EXW_2300	Arbour confirmation and fabrication	60d	15-Feb-18 A	16-Mar-18	Arbour confirmation and fabrication											
EXW_2310	Associated drainage works for the walkway	20d	17-Mar-18	12-Apr-18	Associated drainage works for the walkway											
Reverting Traffic for IEC,VP Rd & TF St & Seawall Reinstatement (KD9)																
TTA Revert Traffic Back to Original Alignment																
East Bound TTA - IEC East Bound, Victoria Park Road & footpath along Sea Side																
TTM Stage 1 - IEC (East Bound)																
Reinstatement Existing Structure																
EB_1020	Install metal parapet on parapet wall (30m)	6d	28-Feb-18	05-Mar-18	Install metal parapet on parapet wall (30m)											
TTM Stage 2 - Revert Traffic back to Original Victoria Road																
Existing Bridge Parapet Reinstatement																
EB_1180	Install metal parapet on parapet wall (40m)	4d	06-Mar-18	09-Mar-18	Install metal parapet on parapet wall (40m)											
TTM Stage 3 - Reinstatement of Footpath along Seafront																
Reinstatement Works in Traffic Deck Part A																
EB_1540	Break two concrete footings	2d	31-Jan-18 A	16-Mar-18	Break two concrete footings											
EB_1520	Break pipe piles and cut sheet pile	6d	10-Feb-18 A	26-Feb-18 A	Break pipe piles and cut sheet pile											
EB_1530	Backfill Subbase material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)	3d	17-Mar-18	19-Mar-18	Backfill Subbase material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)											
Reinstatement of Existing Gas Main																
EB_1560	Excavation for DN400mm Gas main	3d	20-Mar-18	22-Mar-18	Excavation for DN400mm Gas main											
EB_1570	Laying DN400mm gas main by HKCG at VPR footpath	14d	23-Mar-18	05-Apr-18	Laying DN400mm gas main by HKCG at VPR footpath											
West Bound - IEC West Bound & Tsing fung Street																
TTM Stage 2 - Revert Traffic back to Original Tsing Fung Street																
Existing Bridge Parapet Reinstatement																
IECW_1140	Install metal parapet on parapet wall (60m)	5d	28-Feb-18	04-Mar-18	Install metal parapet on parapet wall (60m)											
TTM Stage 3 - Reinstatement of Victoria Park																
Reinstatement Works in Traffic Deck																
IECW_1390	Cut pipe piles and sheet pile	5d	18-Jan-18 A	13-Mar-18	Cut pipe piles and sheet pile											
IECW_1400	Backfill General Fill Material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)	3d	14-Mar-18	16-Mar-18	Backfill General Fill Material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)											
Reinstatement Works inside Victoria Park																
IECW_1440	Reinstatement of Boundary Fence	21d	29-Jan-18 A	17-Mar-18	Reinstatement of Boundary Fence											
IECW_1460	Cutting sheet pile to 1.5m below finish slope profile (MS 169B)	10d	19-Mar-18	28-Mar-18	Cutting sheet pile to 1.5m below finish slope profile (MS 169B)											
IECW_1470	Slope Reinstatement of Victoria Park	21d	26-Mar-18	23-Apr-18	Slope Reinstatement of Victoria Park											
Completion of Minor Outstanding / Remaining Works for KD9																
West Bound - Completion of Minor Outstanding / Remaining Works for KD9																
Minor Reinstatement Works for Tsing Fung Street																
IECW_1530	Laying Public Lighting duct	6d	18-Mar-18	23-Mar-18	Laying Public Lighting duct											
IECW_1540	Installation of public lighting post and connection by HyD	7d	24-Mar-18	30-Mar-18	Installation of public lighting post and connection by HyD											
IECW_1550	Well compact road formation level and subbase for SRT	6d	24-Mar-18	29-Mar-18	Well compact road formation level and subbase for SRT											
Minor Reinstatement Works in IEC West Bound																
IECW_1600	Replacement of new movement joint at IEC W/B (Sun midnight only)	8d	28-Feb-18	07-Mar-18	Replacement of new movement joint at IEC W/B (Sun midnight only)											
IECW_1630	Repairing of 300 dia. concrete pipeline by lining under slow lane of IEC W/B	2d	28-Feb-18*	01-Mar-18	Repairing of 300 dia. concrete pipeline by lining under slow lane of IEC W/B											
IECW_1610	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)	59d	08-Mar-18	05-May-18	Repairing of extg conc deck surface after milling of ten											








Activity ID	Activity Name	Original Duration	Start	Finish	2018					
					Feb	Mar	Apr	May	Jun	
Works in Victoria Park (KD4, KD5, KD9)										
Re-Provisioning Works										
Nursery Compound										
Nursery compound										
ABWF										
Finishes & Waterproofing										
VP_NC_1500	External wall tile cleaning	3d	23-Oct-17 A	20-Mar-18	External wall tile cleaning					
VP_NC_1420	Painting to wall & ceiling in general (final coat)	4d	15-Mar-18*	19-Mar-18	Painting to wall & ceiling in general (final coat)					
Switch room Cut-out Frame & Chequer Plate										
VP_NC_1690	Installation	1d	13-Feb-18 A	14-Feb-18 A	Installation					
Signage										
VP_NC_1720	Installation	7d	21-Feb-18 A	28-Feb-18 A	Installation					
Metal Fence										
VP_NC_1820	Installation	30d	15-Jan-18 A	29-Mar-18	Installation					
E&M										
VP_NC_1890	Form WR1 submission	7d	09-Feb-18 A	13-Feb-18 A	Form WR1 submission					
VP_NC_1900	Expected power on date	7d	14-Feb-18 A	14-Feb-18 A	Expected power on date					
Fire Services										
VP_NC_1960	Pump and water pipe installation	10d	22-Dec-17 A	10-Mar-18	Pump and water pipe installation					
VP_NC_1980	Hose Reel installation, Breakglass and Alarm	3d	10-Feb-18 A	13-Feb-18 A	Hose Reel installation, Breakglass and Alarm					
VP_NC_1930	FS pipe connection from u/g to water meter room	2d	24-Feb-18 A	28-Feb-18 A	FS pipe connection from u/g to water meter room					
Plumbing and Flushing Water Supplies										
VP_NC_2080	Cleaning of potable water pipe and sampling to WSD	7d	17-Feb-18 A	26-Feb-18 A	Cleaning of potable water pipe and sampling to WSD					
VP_NC_2100	WSD Inspection	14d	28-Feb-18	15-Mar-18	WSD Inspection					
GRP Water Tank Installation										
VP_NC_2130	Final As-fitted drawing submission to WSD	7d	30-Jan-18 A	06-Feb-18 A	Final drawing submission to WSD					
External Works Aside Nursery Compound										
Drainage										
VP_NC_2150	U channel at toilet	2d	30-Jan-18 A	31-Jan-18 A	U channel					
VP_NC_2190	SS angle to shower room u channel	1d	31-Jan-18 A	31-Jan-18 A	SS angle to shower room u channel					
VP_NC_2140	Drainage work at External area	15d	28-Feb-18	16-Mar-18	Drainage work at External area					
Water Works										
VP_NC_2220	FS Fresh & Salt Water, Fresh Water and Irrigation System	15d	07-Feb-18 A	27-Feb-18 A	FS Fresh & Salt Water, Fresh Water and Irrigation System					
External Works Around Nursery Compound										
VP_NC_2250	Reinstatement of Existing Boundary Fence Wall Around Nursery Compound	45d	28-Feb-18	24-Apr-18	Reinstatement of Existing Boundary Fence Wall Around Nursery Compound					
KD10 - Preservation and Protection of Trees										
PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	21-Jun-18	Preservation and Protection of Existing Trees					
KD15 & KD8 - Mooring Components Upkeep (CBTS and ATS)										
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	28-Feb-18	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS					

Data Date: 20-Nov-17

HY/2009/18 Central - Wan Chai Bypass (Central Interchange)

TASK filters: 3 Months_1, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017												2018											
						Nov						Dec						Jan						Feb					
Update 2017-11-20 CWB - Central Interchange (2014-06-20) Revised DWP R7																													
PRELIMINARIES																													
Access Dates & Milestones																													
Commencement & Completion																													
1010	Contract DLP and Establishment Works for Landscape Completion	0		20-Nov-17*	-294																								
1005	Contract Construction Completion	0		20-Nov-17*	-659																								
SECTION 7, 7A, 7B & 7C - LANDSCAPE ESTABLISHMENT																													
4030	EST - Portion V Landscape Establishment	365	12-Jan-17 A	11-Jan-18	-800	[Red bar from Nov 12 to Dec 11]																							
SECTION 8 - PRESERVATION & PROTECTION OF TREES																													
4100	Tree - Preservation & Protection of Existing Trees	1759	14-Dec-10 A	20-Nov-17	-659	[Green bar from Dec 14 to Nov 20]																							
Key Dates for Completion of Sections																													
Anticipated Completion																													
1094	KD12 - Anticipated Completion	0		20-Nov-17*	-747																								
1114	KD10 - Anticipated Completion	0		20-Nov-17*	-659																								
1124	KD11 - Anticipated Completion	0		20-Nov-17*	-652																								
1139	KD16 - Anticipated Completion	0		20-Nov-17*	-659																								
1104	KD14 - Anticipated Completion	0		11-Jan-18*	-800													[Blue diamond in Jan 11, 2018]											
Portion Handover Dates																													
Anticipated Handover																													
2960a	Portion IIIA Handover - Remaining (KD3 + 28 days) - (EOT 26.5 days added)	0		20-Nov-17*	-962																								

 Current Milestone	 Remaining W...
 Level of Effort	 Project Baseli...
 Baseline Milestone	
 Actual Work	
 Critical Remaining Work	

Leighton Contractors (Asia) Limited Programme Update 86 (November 2017) THREE MONTH ROLLING

Project ID: U086
 Baseline: DCP7-2c
 Layout: Update Three Month Rolling
 U086
 Page 1 of 1

Date	Revision	Checked	Appro...
20-Oct-17	U085	AT	PT
20-Nov-17	U086	AT	DG

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Feb	Mar	Apr	May
Update 2018-02-20 CWB(CC) - Commissioning Contract (SA)									
PRELIMINARIES AND GENERAL REQUIREMENTS									
Salient Key Dates and Milestones									
Contract Key Dates									
KD007	KD7 - Completion of Section 2 of the Works (1437 days) - include EOT (80 days)	0		03-Feb-18 A		▲			
KD008	KD8 - Completion of Section 3 of the Works (1437 days) - include EOT (80 days)	0		03-Feb-18 A		▲			
Anticipated Completion Dates									
KD01	KD1 - Achievement of Stage 1 (1177 days) - include EOT No.3 (123 days)	0		05-Feb-18 A		▲			
KD02	KD2 - Achievement of Stage 2 (1232 days)	0		15-May-18*	-305			▲	◆
KD03	KD3 - Achievement of Stage 3 (1318 days) - include EOT (140 days)	0		15-May-18*	-219		▲		◆
Possession Dates and Vacation Dates									
PO-IIa	Possession of Portion IIa (Day 1) - WVB below +6.5mPD	1329	28-Feb-14 A	20-Mar-18	-269	[Bar chart showing possession period from Feb to Mar]			
PO-III	Possession of Portion III (Day 120) - CH1805-2600	1209	28-Jun-14 A	20-Mar-18	-284	[Bar chart showing possession period from Jun to Mar]			
PO-Ib	Possession of Portion Ib (Day 242) - CH1580-1805	1087	28-Oct-14 A	20-Mar-18	-264	[Bar chart showing possession period from Oct to Mar]			
PO-IXd	Possession of Portion IXd (Day 266) - CH4600-4860	1063	21-Nov-14 A	20-Mar-18	-195	[Bar chart showing possession period from Nov to Mar]			
PO-XI	Possession of Portion XI (Day 296) - EVS	1033	21-Dec-14 A	20-Mar-18	180	[Bar chart showing possession period from Dec to Mar]			
PO-IIc	Possession of Portion IIc (Day 336) - CH1360-1580	993	30-Jan-15 A	20-Mar-18	-269	[Bar chart showing possession period from Jan to Mar]			
PO-IIb	Possession of Portion IIb (Day 336) - WVB above +6.5mPD	669	30-Jan-15 A	20-Mar-18	-269	[Bar chart showing possession period from Jan to Mar]			
PO-IXa	Possession of Portion IXa (Day 392) - CH4860-5150	937	27-Mar-15 A	20-Mar-18	-195	[Bar chart showing possession period from Mar to Mar]			
PO-Va	Possession of Portion V (Day 607) - CH2950-3210	722	28-Oct-15 A	20-Mar-18	-284	[Bar chart showing possession period from Oct to Mar]			
PO-VII_a1	Possession of Portion VII (Day 762) - CH3911-4250 (below -6.0mPD)	659	30-Dec-15 A	20-Mar-18	-203	[Bar chart showing possession period from Dec to Mar]			
PO-Vc	Possession of Portion V (Day 607) - CH3210-3250	658	15-Jan-16 A	20-Mar-18	-265	[Bar chart showing possession period from Jan to Mar]			
PO-VIb_b1	Possession of Portion VIb (Day 761) - CH3428-3625 (E/B)	619	18-Feb-16 A	20-Mar-18	-279	[Bar chart showing possession period from Feb to Mar]			
PO-VIb_b2	Possession of Portion VIb (Day 761) - CH3428-3625 (W/B)	568	29-Feb-16 A	20-Mar-18	-264	[Bar chart showing possession period from Feb to Mar]			

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 48 (February 2018)

THREE MONTH ROLLING

Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 1 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018				
						Feb	Mar	Apr	May	
PO-Xa_1	Possession of Portion Xa (Day 650) - ADB Southern Portion (AECOM letter ref: 2015007890T)	589	07-Mar-16 A	20-Mar-18	-323					
PO-Xb_1	Possession of Portion Xb (Day 804) - ADB Northern Portion	589	07-Mar-16 A	20-Mar-18	-323					
PO-Vb1	Possession of Portion V (Day 607) - SR3	587	11-Mar-16 A	20-Mar-18	180					
PO-Ia	Possession of Portion Ia (Day 789) - SCB / SCP1 / SCP2 / Rumsey Street Flyover	600	28-Mar-16 A	20-Mar-18	-307					
PO-VII_a2	Possession of Portion VII (Day 762) - CH3800-3911 (below -6.0mPD)	567	31-Mar-16 A	20-Mar-18	-250					
PO-IXc_1	Possession of Portion IXc (Day 712) - EVB above 3.6mPD - Relinquished on 12 Apr 2016	445	29-Jul-16 A	20-Mar-18	-274					
PO-IXb_1	Possession of Portion IXb (Day 712) - EVB (below +3.6mPD to tunnel top slab) - Relinquished on 12 Apr 2016	445	05-Aug-16 A	20-Mar-18	-274					
PO-VIa_a	Possession of Portion VIa (Day 823) - CH3250-3283	425	15-Aug-16 A	20-Mar-18	-269					
PO-Vb2_a	Possession of Portion V (Day 607) - SR2	456	15-Aug-16 A	20-Mar-18	-265					
PO-VIc_a	Possession of Portion VIc (Day 761) - CH3770-3800 (Access Shaft Opening)	391	23-Sep-16 A	20-Mar-18	-264					
PO-VIb_c	Possession of Portion VIb (Day 761) - CH3625-3770	391	23-Sep-16 A	20-Mar-18	-279					
PO-IVa1	Possession of Portion IVa (Day 930) - CH2600-2720	323	30-Nov-16 A	20-Mar-18	-271					
PO-IVb2	Possession of Portion IVb (Day 930) - MVB (GL D-H)	233	28-Feb-17 A	20-Mar-18	-320					
PO-VIIIa_a	Possession of Portion VIIIa (Day 929) - CH4530-4591 W/B	233	28-Feb-17 A	20-Mar-18	-245					
PO-VIIIa	Possession of Portion VIIIa (Day 929) - CH4250-4600 (Remaining)	241	12-Mar-17 A	20-Mar-18	-245					
PO-VIIIb	Possession of Portion VIIIb (Day 929) - SR8 (CH700-350)	233	12-Mar-17 A	20-Mar-18	-192					
PO-VIIIc	Possession of Portion VIIIc (Day 1039) - SR8 (CH350-310) / SCP4	233	12-Mar-17 A	20-Mar-18	-241					
PO-IVa2_a	Possession of Portion IVa (Day 930) - CH2720-2950	241	12-Mar-17 A	20-Mar-18	-267					
PO-IVb1	Possession of Portion IVb (Day 930) - MVB (GL A-C)	239	14-Mar-17 A	20-Mar-18	-320					
PO-IVa2_b	Possession of Portion IVa (Day 930) - SR1	203	30-Mar-17 A	20-Mar-18	-267					
PO-Vb2_b	Possession of Portion V (Day 607) - SCP3	182	03-Jul-17 A	20-Mar-18	-265					
PO-VIb_a	Possession of Portion VIb (Day 761) - CH3400-3428	80	31-Jul-17 A	20-Mar-18	-264					
PO-VIa_b	Possession of Portion VIa (Day 823) - CH3283-3400	80	31-Jul-17 A	20-Mar-18	-284					
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-Feb-18	10-Jun-18	-262					

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 2 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018											
						Feb			Mar			Apr			May		
Submissions and Approvals																	
Initial General Submission																	
10168	Submission of CMC 3DVR	30	20-Mar-18	18-Apr-18	-74												
DETAILED DESIGN OF WORKS																	
Permanent Works Design and Engineering																	
Green Roof on EVB																	
2166	EVB Roof - Engineer review & Approval; Consent to Proceed Construction	24	18-Apr-16 A	06-Mar-18	-279												
Green Wall on ADB																	
10238	ADB Green Wall - Engineer review & Approval; Consent to Proceed Construction	24	07-Mar-16 A	08-Mar-18	-269												
Landscaping & Associated Irrigation System																	
10268	Landscaping - Engineer review & Approval; Consent to Proceed Construction	24	07-Mar-16 A	08-Mar-18	-238												
PROCUREMENT, MANUFACTURING & DELIVERIES																	
Procurement; Manufacturing; Deliveries																	
Green Roof on EVB																	
Shop Drawings																	
12846	EVB Green Roof - Shop Drawings review the Engineer	30	03-Aug-17 A	27-Feb-18	-342												
2230	EVB Green Roof - Obtain Approval for Shop Drawings	0		27-Feb-18	-342												
Procurement & Fabrication																	
2232	EVB Green Roof - Confirm design of embed items	0	07-Mar-18		-349												
2234	EVB Green Roof - Embed fabrication & delivery	30	07-Mar-18	05-Apr-18	-349												
2236	EVB Green Roof - Commence embed installation	0	06-Apr-18		-349												
2238	EVB Green Roof - Green Roof Fabrication & delivery	30	06-Apr-18	05-May-18	-349												
2240	EVB Green Roof - Commence installation	0	06-May-18		-349												
Landscaping and Associated Irrigation System																	

- Current Milestone
- Remaining Work
- Level of Effort
- Project Baseline
- Baseline Milestone
- Actual Work
- Critical Remaining Work

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 3 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

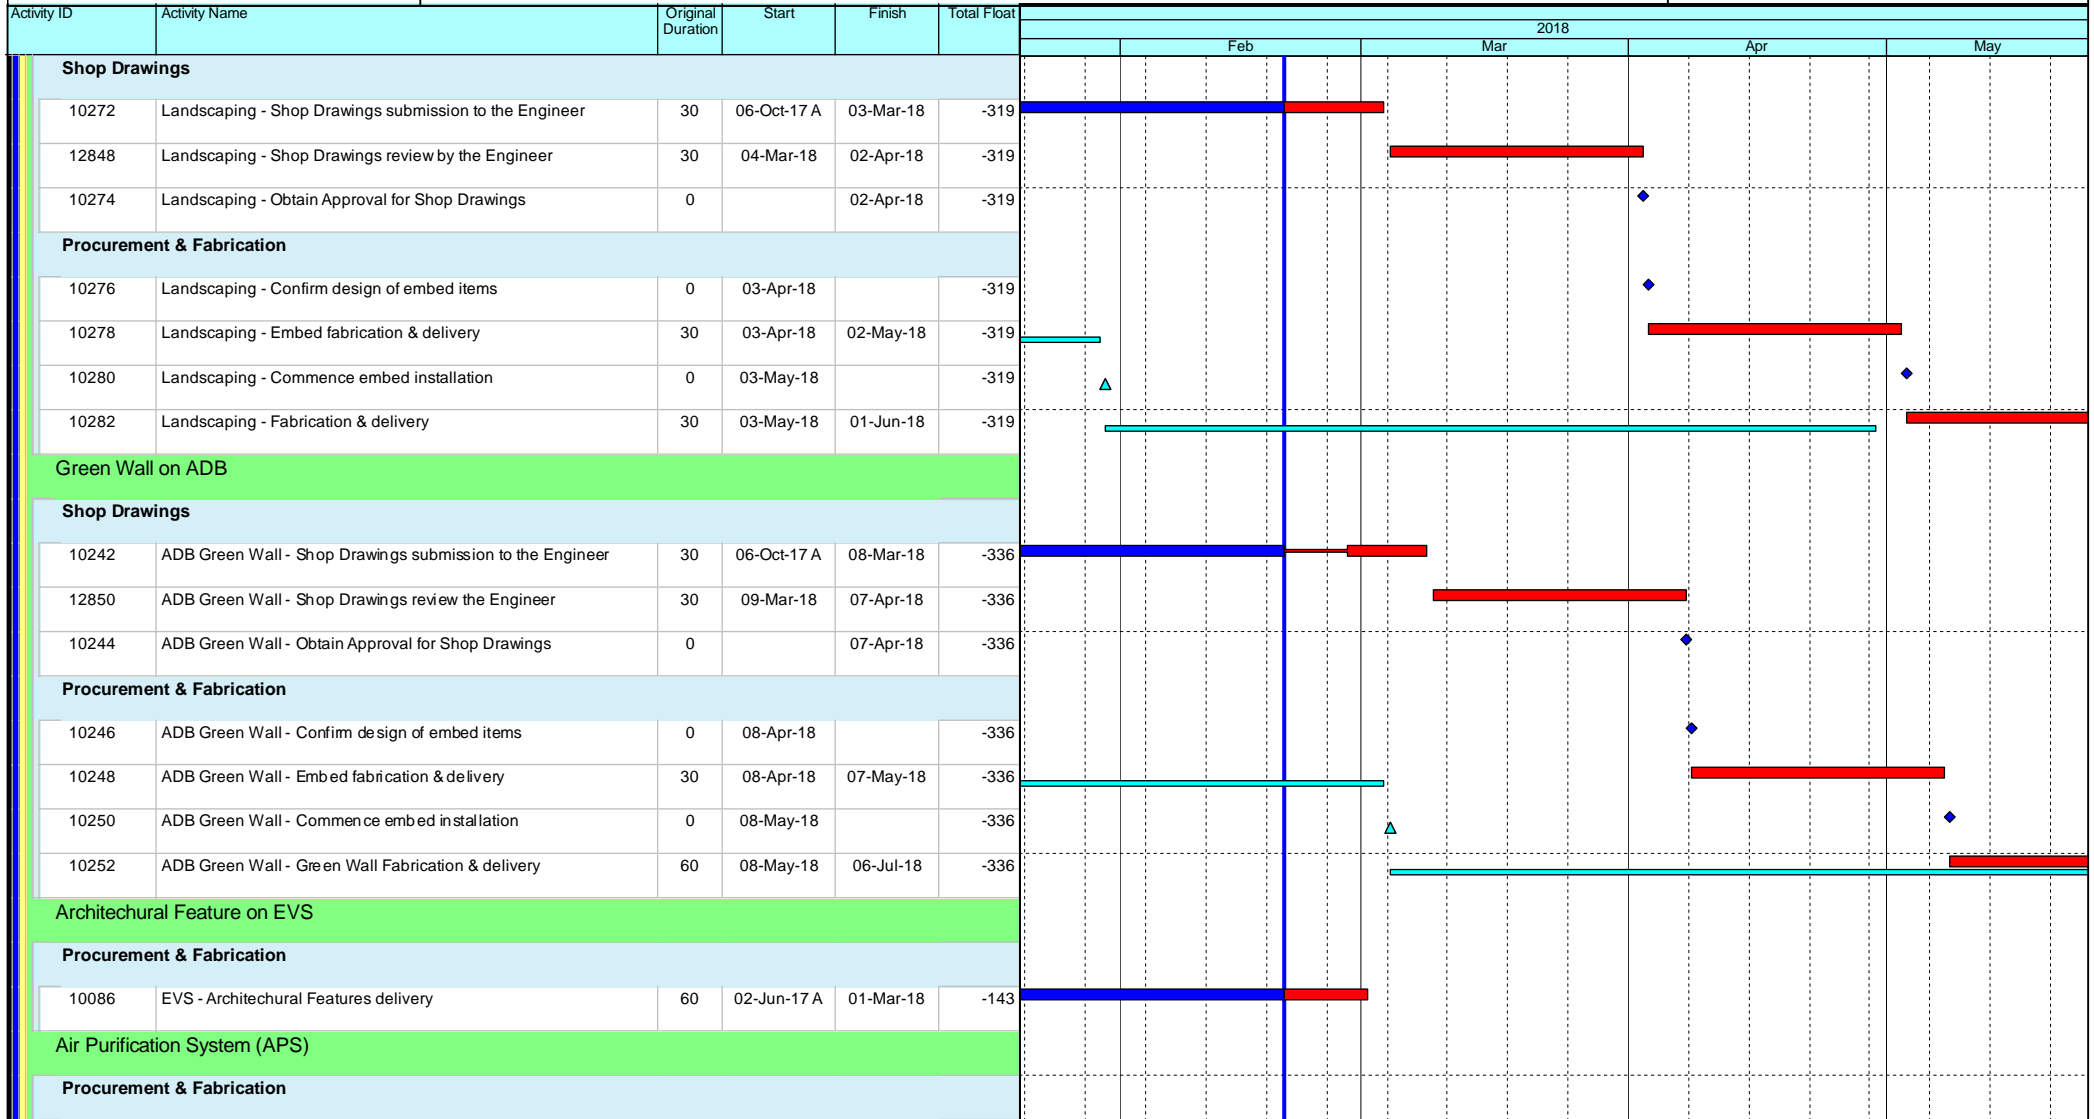

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048
Baseline: SA01
Layout: Update Three Month Rolling
U048
Page 4 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018				
						Feb	Mar	Apr	May	
13664	APS - Ship to HK Store (3rd Batch)	80	03-Aug-17 A	01-Mar-18	-138					
2368	APS - QA Stored Equipment	6	23-Aug-17 A	01-Mar-18	-138					
CONSTRUCTION										
West Ventilation Building (WVB - related)										
Tunnel Section (WVB-related)										
Portion Ia, IIc [CH840 to CH1360]										
13086a	Request for VO / instruction for TCSS equipment installation and cabling (Ganty FADS01) (Ref: H2613-LJV-LE-4022)	24	04-Oct-16 A	15-Mar-18	-162					
13086	TCSS cabling and sign face installation (FADS01)	40	16-Mar-18	07-May-18	-162					
Westbound										
5000	MEP(WB) - (CH840 to CH1360) E&M 1st Fix	29	05-Jun-17 A	01-Mar-18	-134					
5008	MEP(WB) - (CH840 to CH1360) E&M 2nd Fix (include Sump A)	58	12-Jun-17 A	22-Mar-18	-152					
5016	MEP(WB) - (CH840 to CH1360) E&M Final Fix	24	23-Mar-18	24-Apr-18	-152					
5024	MEP(WB) - (CH840 to CH1360) TCSS Field equip & cable installation	18	03-Apr-18	24-Apr-18	-152					
Eastbound										
6100	MEP(EB) - (CH840 to CH1360) E&M 1st Fix	29	01-Mar-17 A	01-Mar-18	-134					
6102	MEP(EB) - (CH840 to CH1360) E&M 2nd Fix (include Sump A)	58	22-May-17 A	22-Mar-18	-152					
6104	MEP(EB) - (CH840 to CH1360) E&M Final Fix	24	23-Mar-18	24-Apr-18	-152					
6106	MEP(EB) - (CH840 to CH1360) TCSS Field equip & cable installation	18	03-Apr-18	24-Apr-18	-152					
West Ventilation Building (WVB)										
RC Structures and Metal Roof										
Metal Roof										
10454	WVB - Touch up (Steel structure)	12	24-Jan-18 A	05-Feb-18 A						
10456	WVB - Touch up (Roof cladding)	12	23-Feb-18	08-Mar-18	-189					
Metal Roof Eastern Side (M.J. East)										

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 5 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

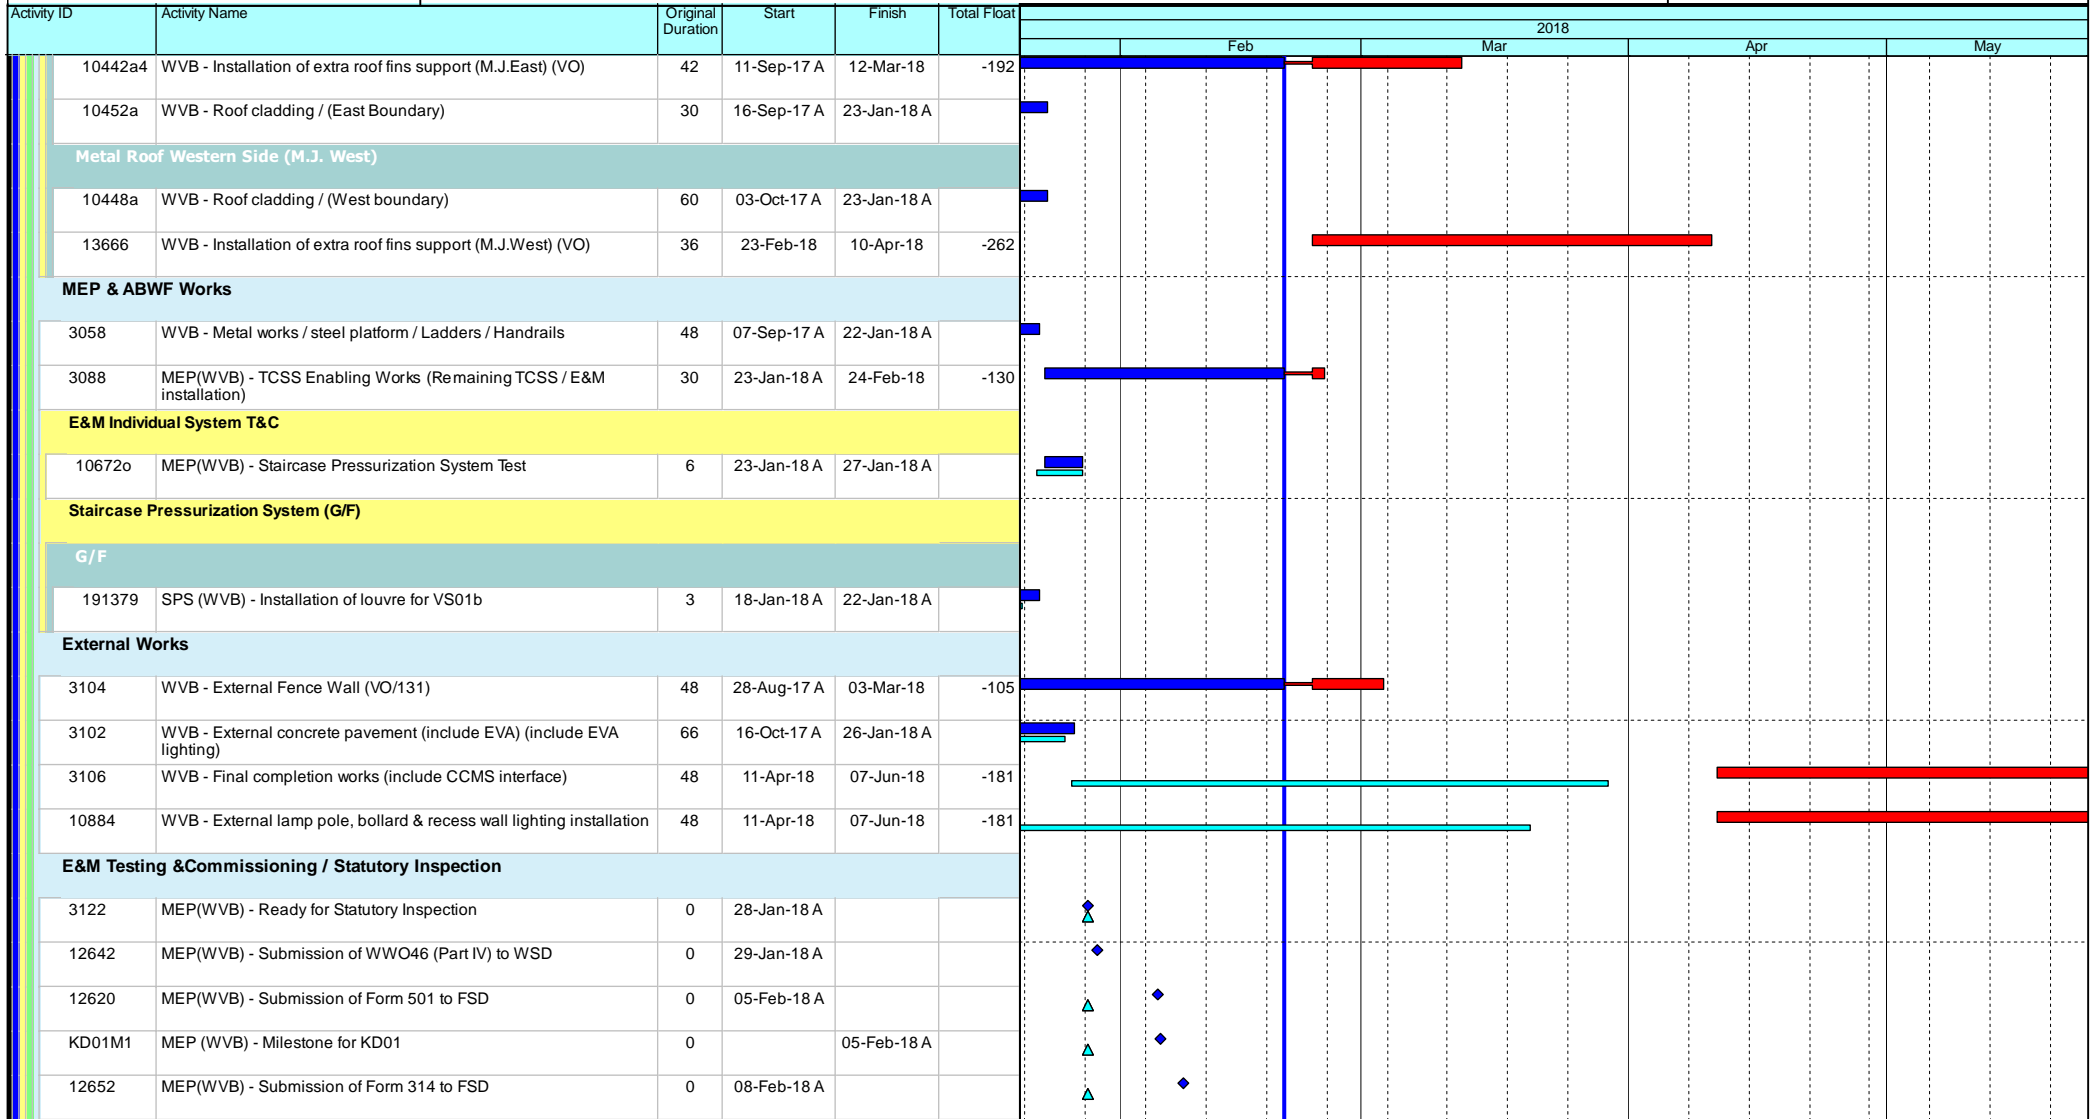

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 6 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

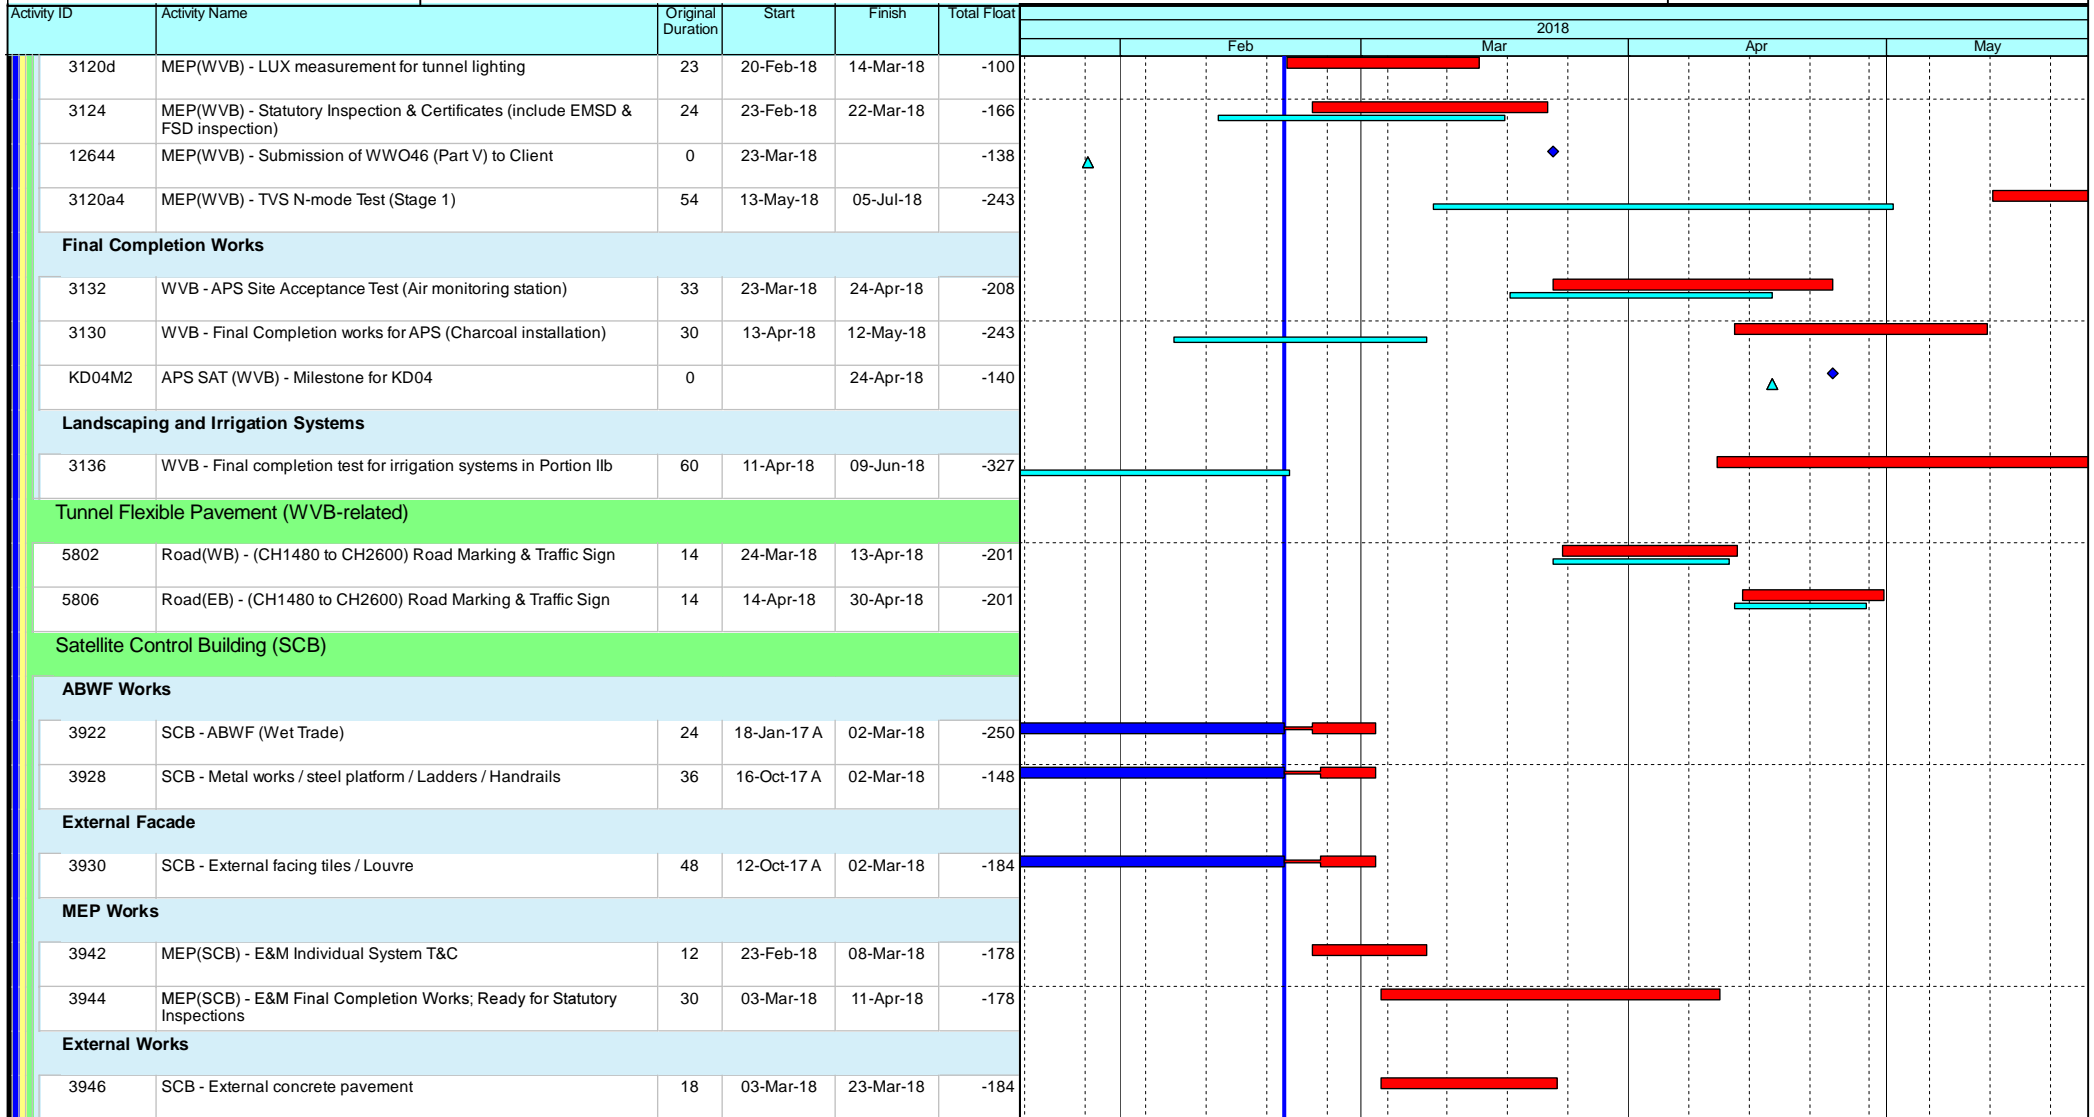

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 7 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

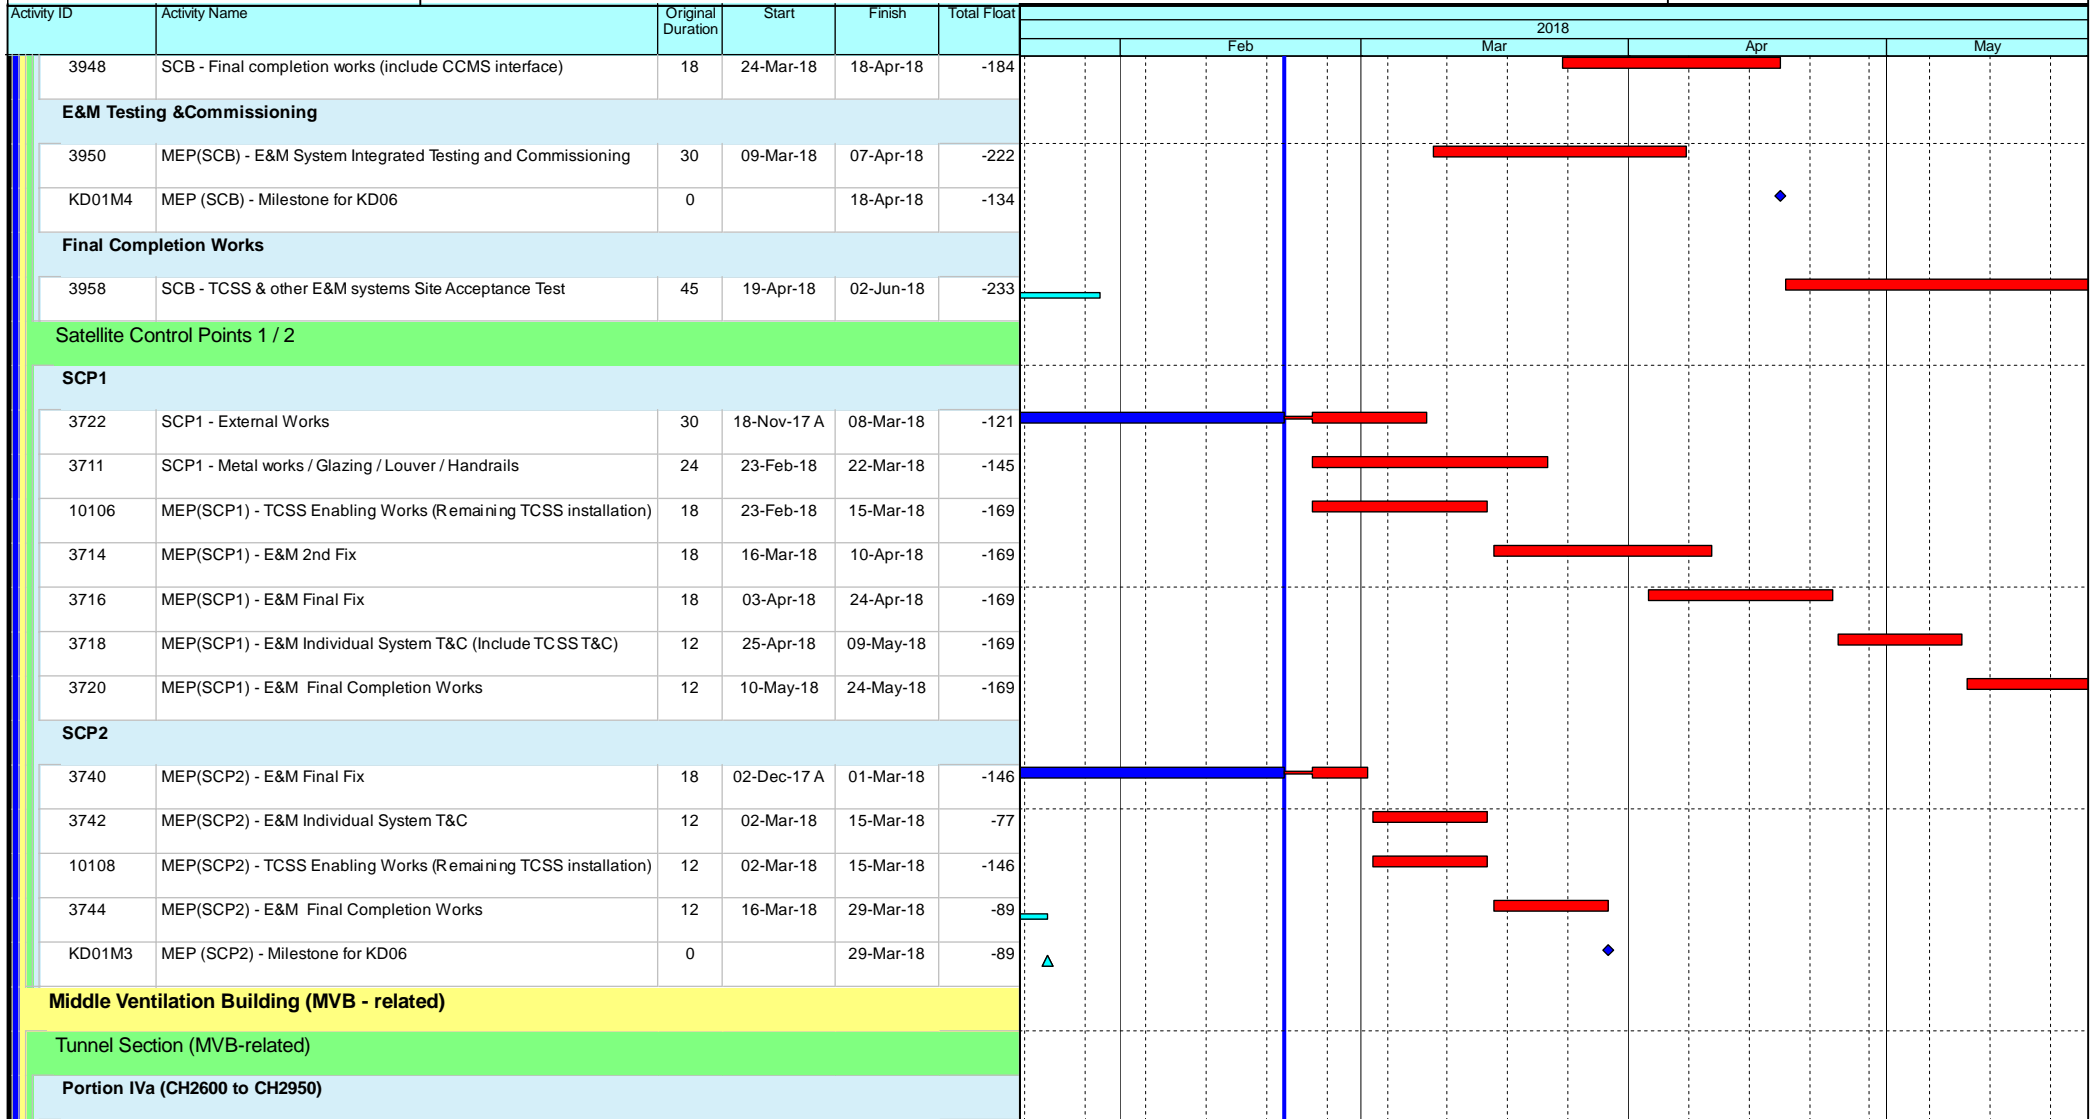

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 8 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018									
						Feb	Mar	Apr	May						
Slip Road 1															
10020	MEP(SR1) - (CH171 to CH271) E&M 2nd Fix (include Sump B)	30	15-Dec-17 A	01-Mar-18	-203										
10022	MEP(SR1) - (CH171 to CH271) E&M Final Fix	4	02-Mar-18	06-Mar-18	-203										
10046a	MEP(SR1) - (CH171 to CH271) VE Panel installation (Lower part) (1200m2)	13	15-Mar-18	29-Mar-18	-210										
10024	MEP(SR1) - (CH171 to CH271) TCSS Field equip & cable installation	6	17-Mar-18	23-Mar-18	-99										
10046	MEP(SR1) - (CH171 to CH271) VE Panel installation (Upper part) (1200m2)	13	20-Mar-18	07-Apr-18	-214										
Westbound (CH2600 to CH2720)															
9950a1	MEP(WB) - (CH2600 to CH2720) VE Panel installation (Lower part) (1400m2)	9	02-Aug-17 A	24-Feb-18	-206										
5102a	MEP(WB) - (CH2600 to CH2720) E&M 2nd Fix	12	23-Nov-17 A	01-Mar-18	-221										
9950a3	MEP(WB) - (CH2600 to CH2720) VE Panel installation (Upper part) (1750m2)	11	05-Mar-18	16-Mar-18	-223										
5104a	MEP(WB) - (CH2600 to CH2720) E&M Final Fix	6	10-Mar-18	16-Mar-18	-93										
5106a	MEP(WB) - (CH2600 to CH2720) TCSS Field equip & cable installation	6	10-Mar-18	16-Mar-18	-223										
Eastbound (CH2600 to CH2720)															
5120a	MEP(EB) - (CH2600 to CH2720) E&M 2nd Fix	7	04-Dec-17 A	24-Feb-18	-218										
9952a1	MEP(EB) - (CH2600 to CH2720) VE Panel installation (Lower part) (1400m2)	9	26-Feb-18	07-Mar-18	-204										
5122a	MEP(EB) - (CH2600 to CH2720) E&M Final Fix	6	03-Mar-18	09-Mar-18	-217										
5124a	MEP(EB) - (CH2600 to CH2720) TCSS Field equip & cable installation	6	03-Mar-18	09-Mar-18	-223										
9952a3	MEP(EB) - (CH2600 to CH2720) VE Panel installation (Upper part) (1750m2)	11	17-Mar-18	29-Mar-18	-223										
Westbound (CH2720 to CH2950)															
5102b	MEP(WB) - (CH2720 to CH2950) E&M 2nd Fix	12	29-Dec-17 A	28-Feb-18	-211										
9950b	MEP(WB) - (CH2720 to CH2950) VE Panel installation (Lower part) (2247m2)	13	23-Feb-18	09-Mar-18	-206										
9950b1	MEP(WB) - (CH2720 to CH2950) VE Panel installation (Upper part) (2247m2)	13	05-Mar-18	19-Mar-18	-214										
5104b	MEP(WB) - (CH2720 to CH2950) E&M Final Fix	12	06-Mar-18	19-Mar-18	-95										
5106b	MEP(WB) - (CH2720 to CH2950) TCSS Field equip & cable installation	12	06-Mar-18	19-Mar-18	-217										

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 9 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

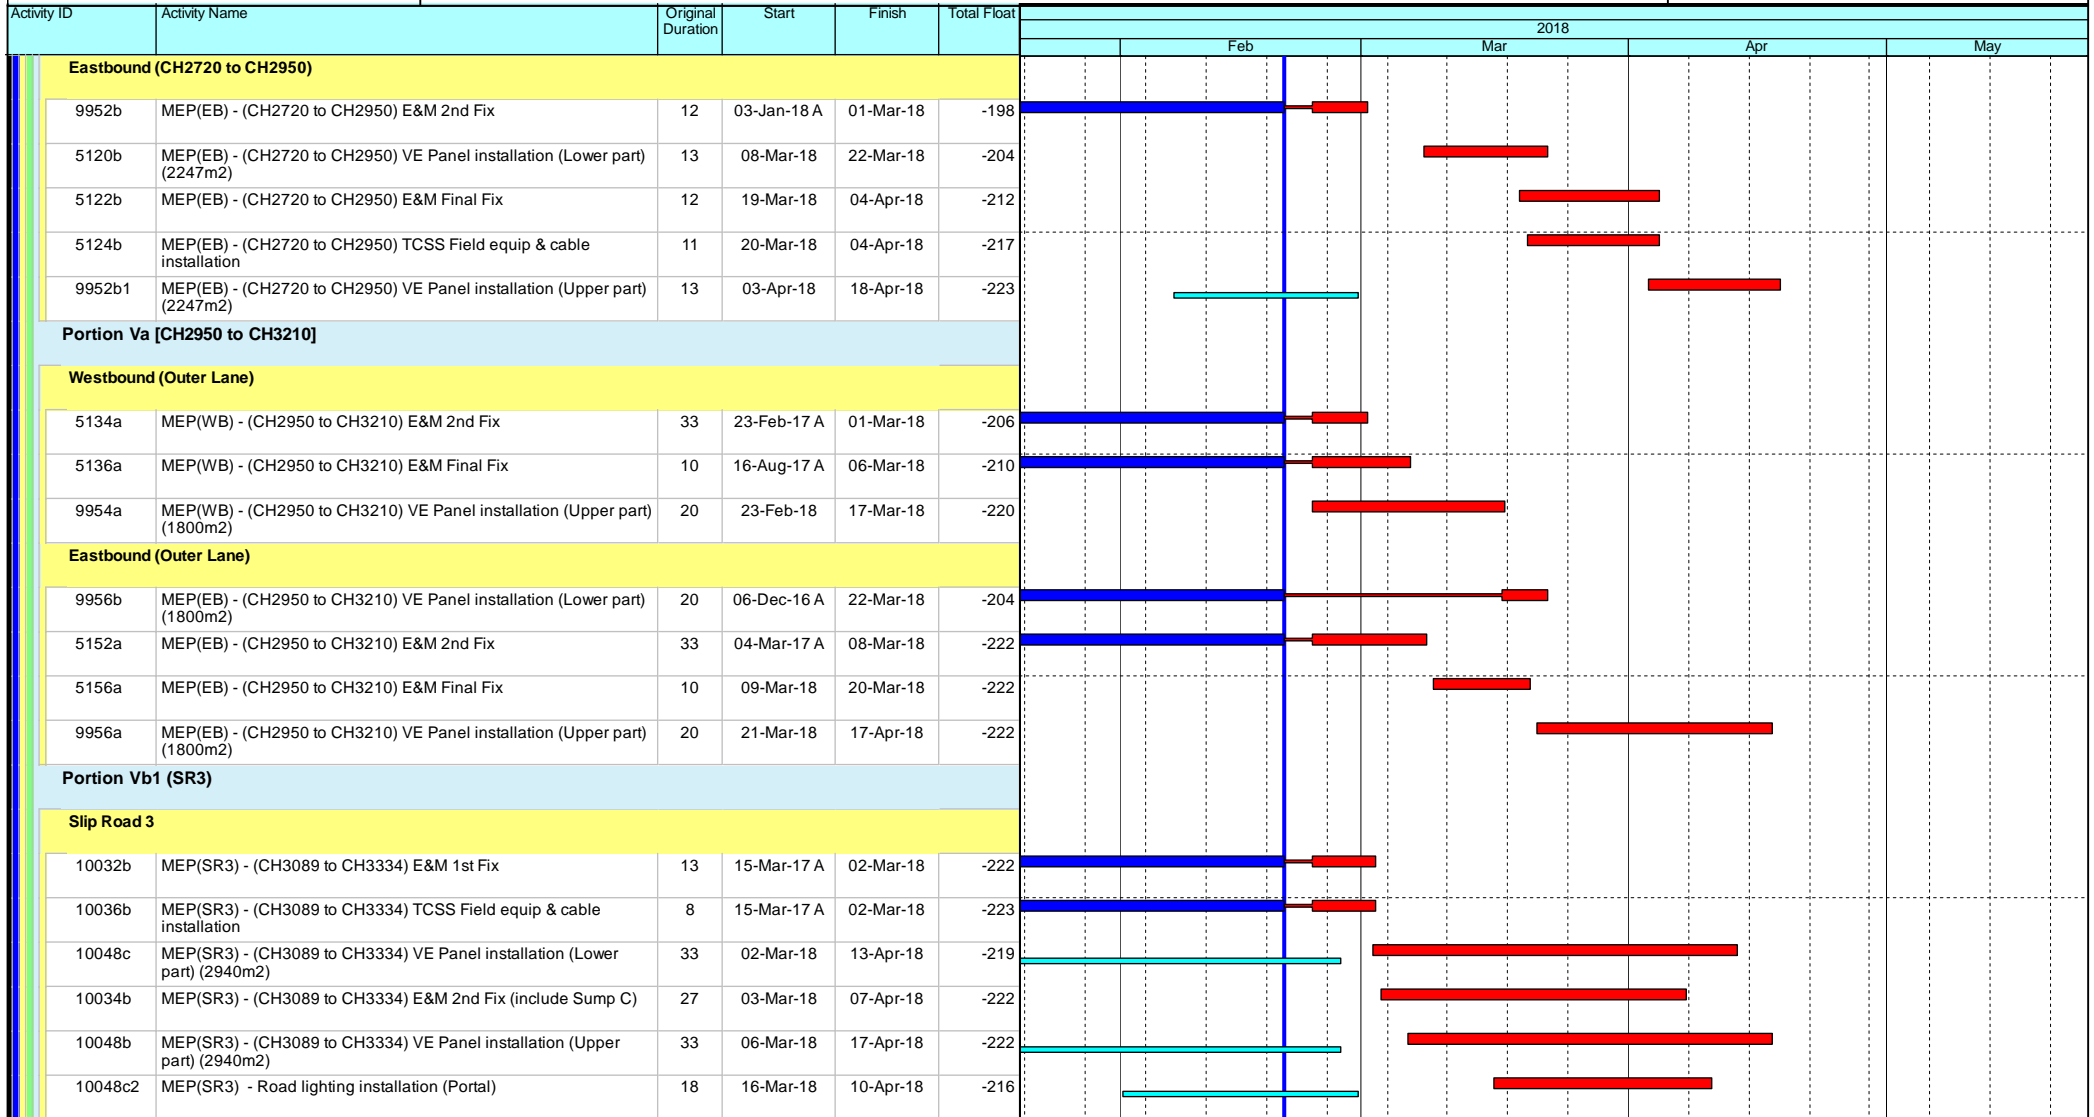

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048
Baseline: SA01
Layout: Update Three Month Rolling
U048
Page 10 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018																	
						Feb			Mar			Apr			May								
10038b	MEP(SR3) - (CH3089 to CH3334) E&M Final Fix	8	09-Apr-18	17-Apr-18	-222																		
Portion Vb2 (SR2 / SCP3)																							
Slip Road 2																							
10050b	MEP(SR2) - (CH3114 to CH3257) E&M 1st Fix	8	08-Mar-17 A	27-Feb-18	-184																		
10056b	MEP(SR2) - (CH3114 to CH3257) TCSS Field equip & cable installation	5	16-Mar-17 A	27-Feb-18	-217																		
10052b	MEP(SR2) - (CH3114 to CH3257) E&M 2nd Fix (include Sump F)	40	15-Jun-17 A	23-Mar-18	-205																		
10064b2	MEP(SR2) - Road lighting installation (Portal)	18	23-Feb-18	15-Mar-18	-216																		
10054b	MEP(SR2) -(CH3114 to CH3257) E&M Final Fix	5	24-Mar-18	29-Mar-18	-145																		
10064b	MEP(SR2) - (CH3114 to CH3257) VE Panel installation (Upper part) (1716m2)	18	12-Apr-18	03-May-18	-152																		
10064c	MEP(SR2) - (CH3114 to CH3257) VE Panel installation (Lower part) (1716m2)	18	12-Apr-18	03-May-18	-152																		
Portion Vc [CH3210 to CH3250]																							
Westbound (Outer Lane)																							
5134c	MEP(WB) - (CH3210 to CH3250) E&M 2nd Fix	18	23-Feb-17 A	05-Mar-18	-199																		
5136c	MEP(WB) - (CH3210 to CH3250) E&M Final Fix	10	06-Mar-18	16-Mar-18	-199																		
9954c	MEP(WB) - (CH3210 to CH3250) VE Panel installation (Upper part) (1800m2)	20	19-Mar-18	14-Apr-18	-220																		
Eastbound (Outer Lane)																							
5152c	MEP(EB) - (CH3210 to CH3250) E&M 2nd Fix	18	02-Mar-17 A	05-Mar-18	-199																		
5156c	MEP(EB) - (CH3210 to CH3250) E&M Final Fix	10	06-Mar-18	16-Mar-18	-199																		
9956c	MEP(EB) - (CH3210 to CH3250) VE Panel installation (Upper part) (1800m2)	20	10-Apr-18	03-May-18	-152																		
Portion VIa [CH3250 to CH3283]																							
Westbound																							
5166a	MEP(WB) - (CH3250 to CH3283) E&M 2nd Fix	6	27-Nov-17 A	27-Feb-18	-217																		
9958a1	MEP(WB) - (CH3250 to CH3283) VE Panel installation (Lower part) (528m2)	6	23-Feb-18	01-Mar-18	-219																		
5170a	MEP(WB) - (CH3250 to CH3283) TCSS Field equip & cable installation	5	28-Feb-18	05-Mar-18	-217																		

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline
- ▲ Baseline Milestone

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 11 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

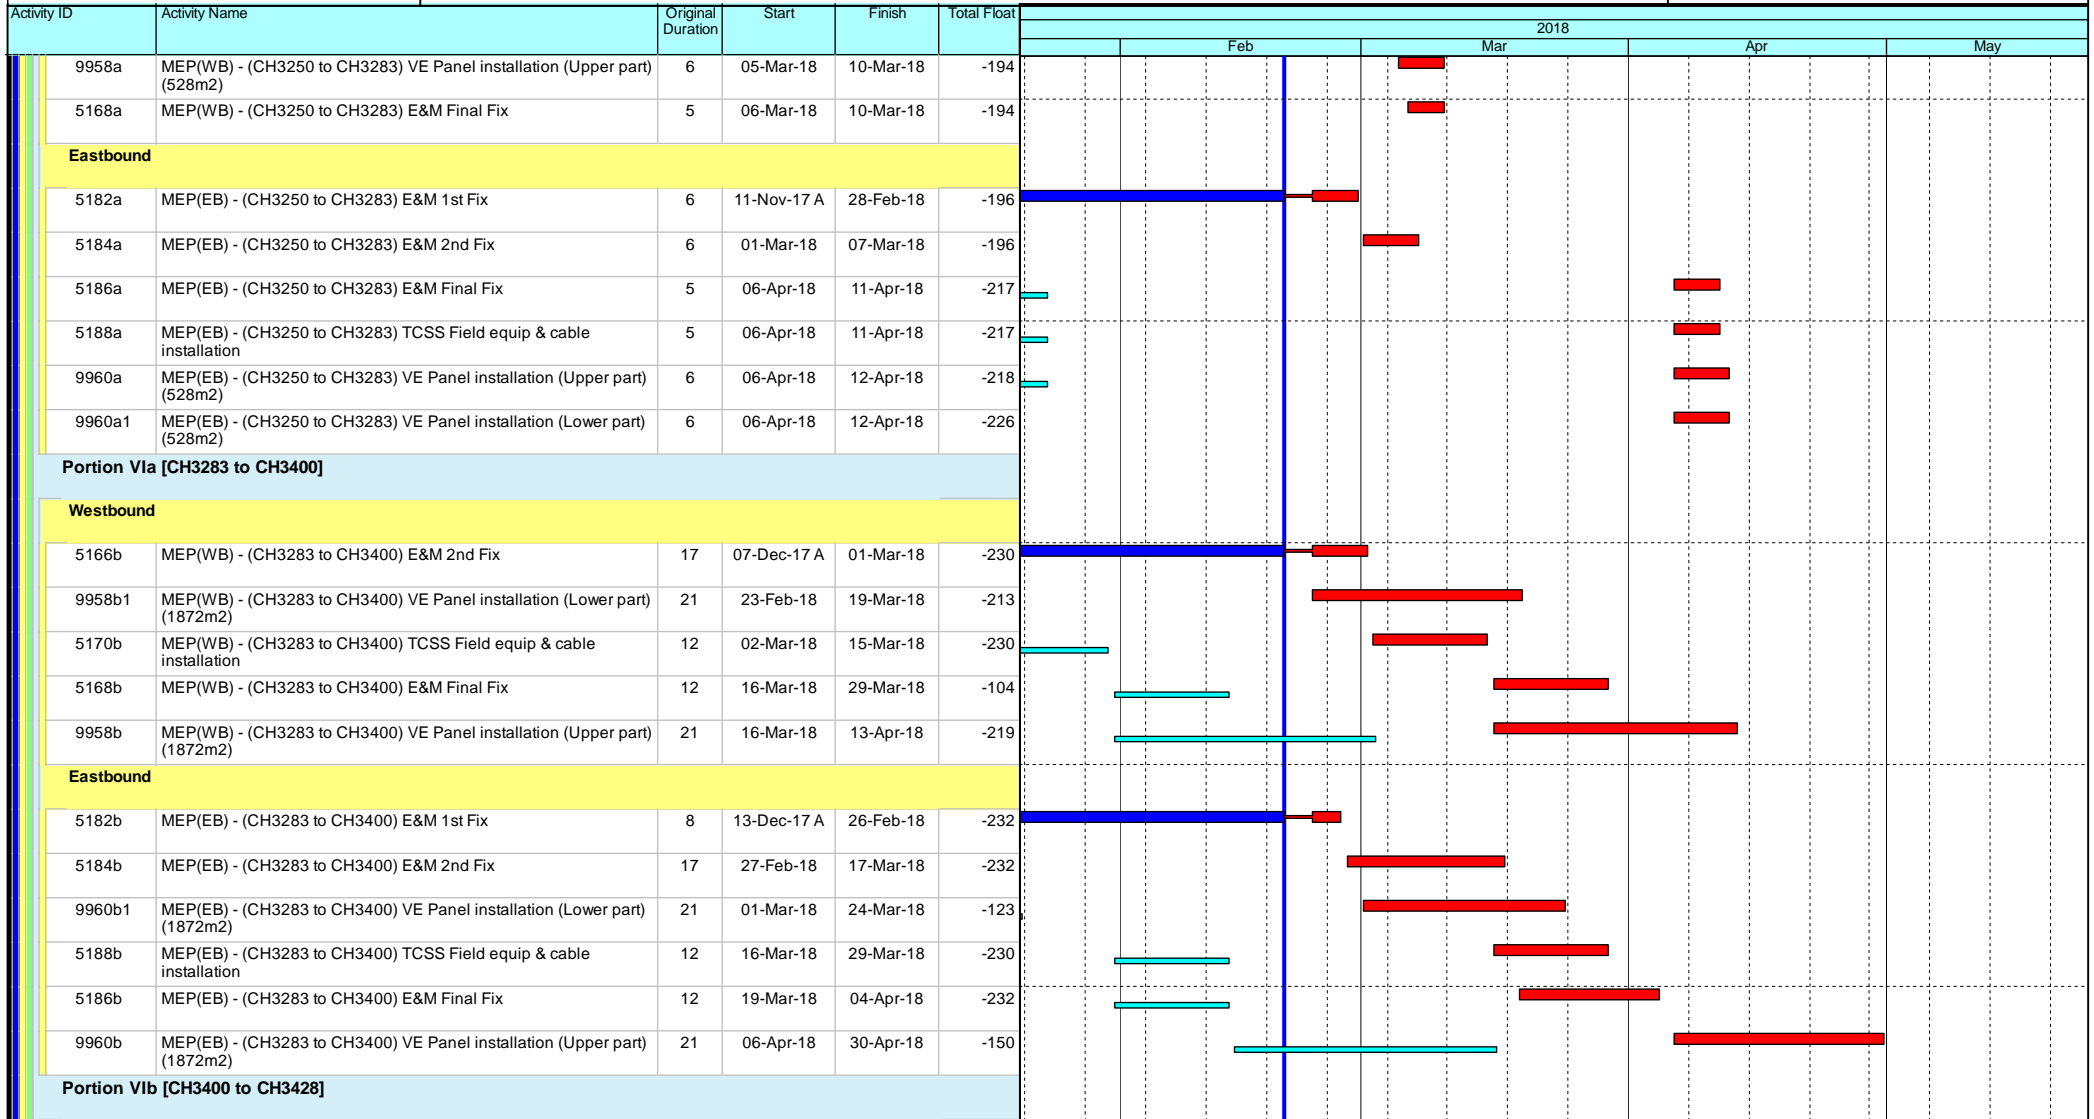

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 12 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

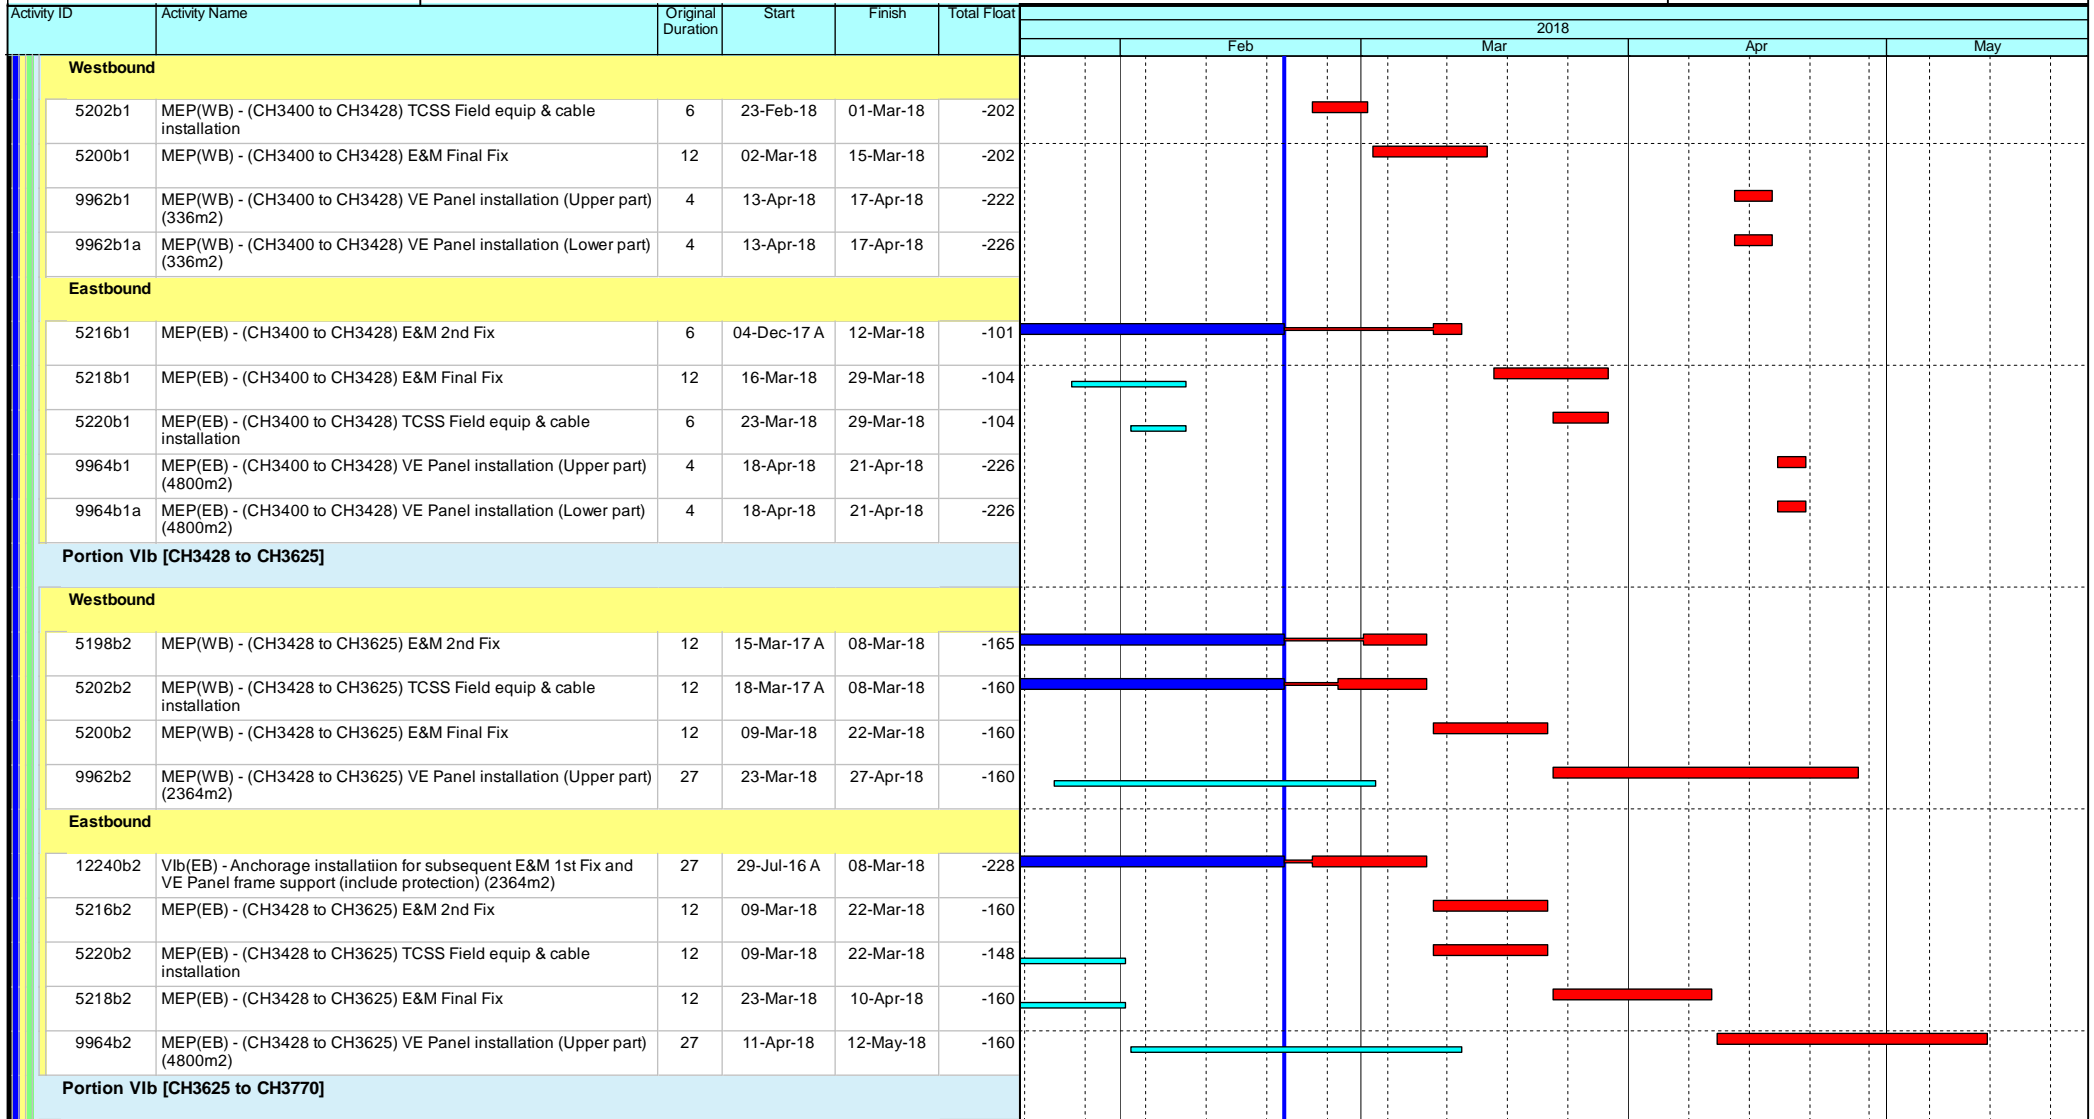

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
Baseline: SA01
Layout: Update Three Month Rolling
U048
Page 13 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

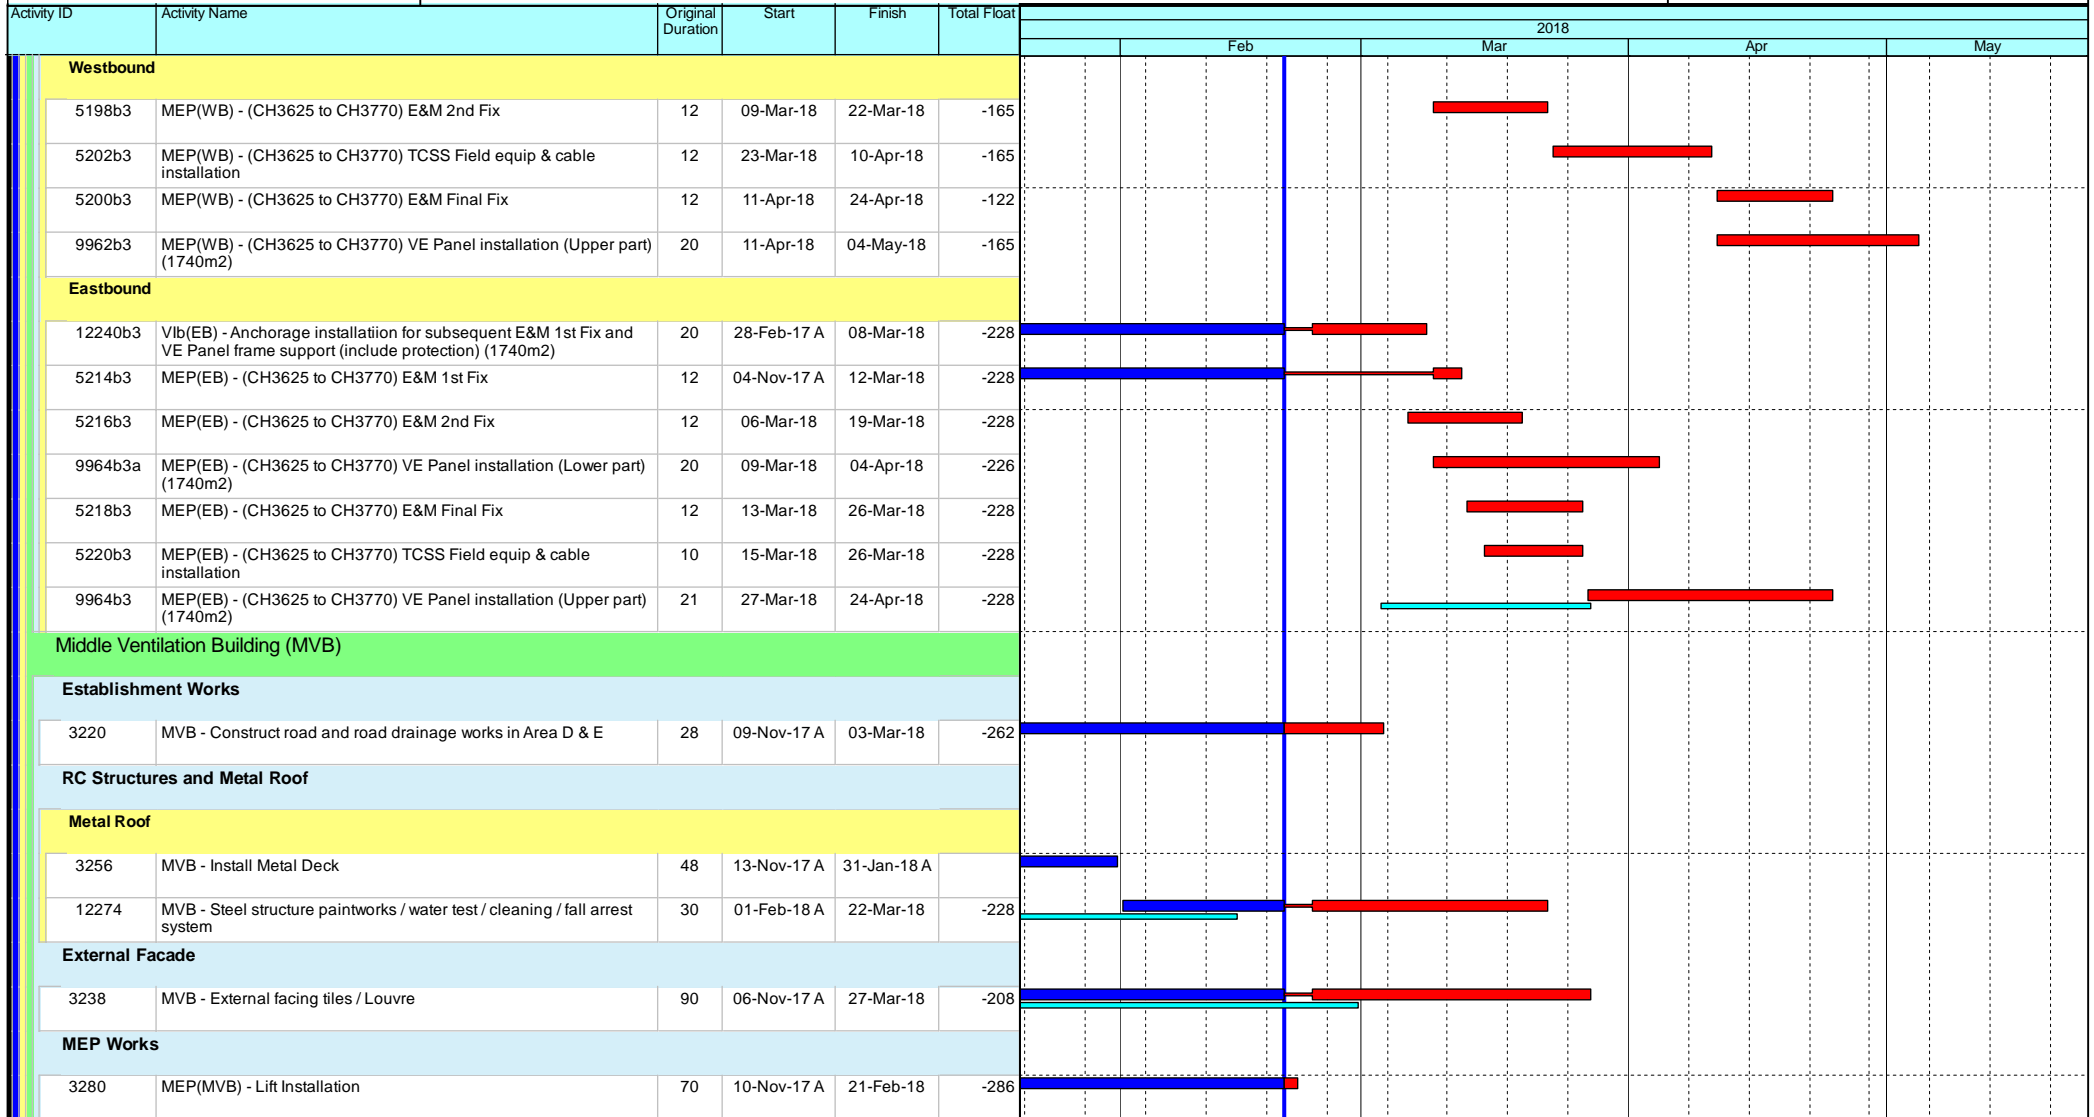

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 14 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

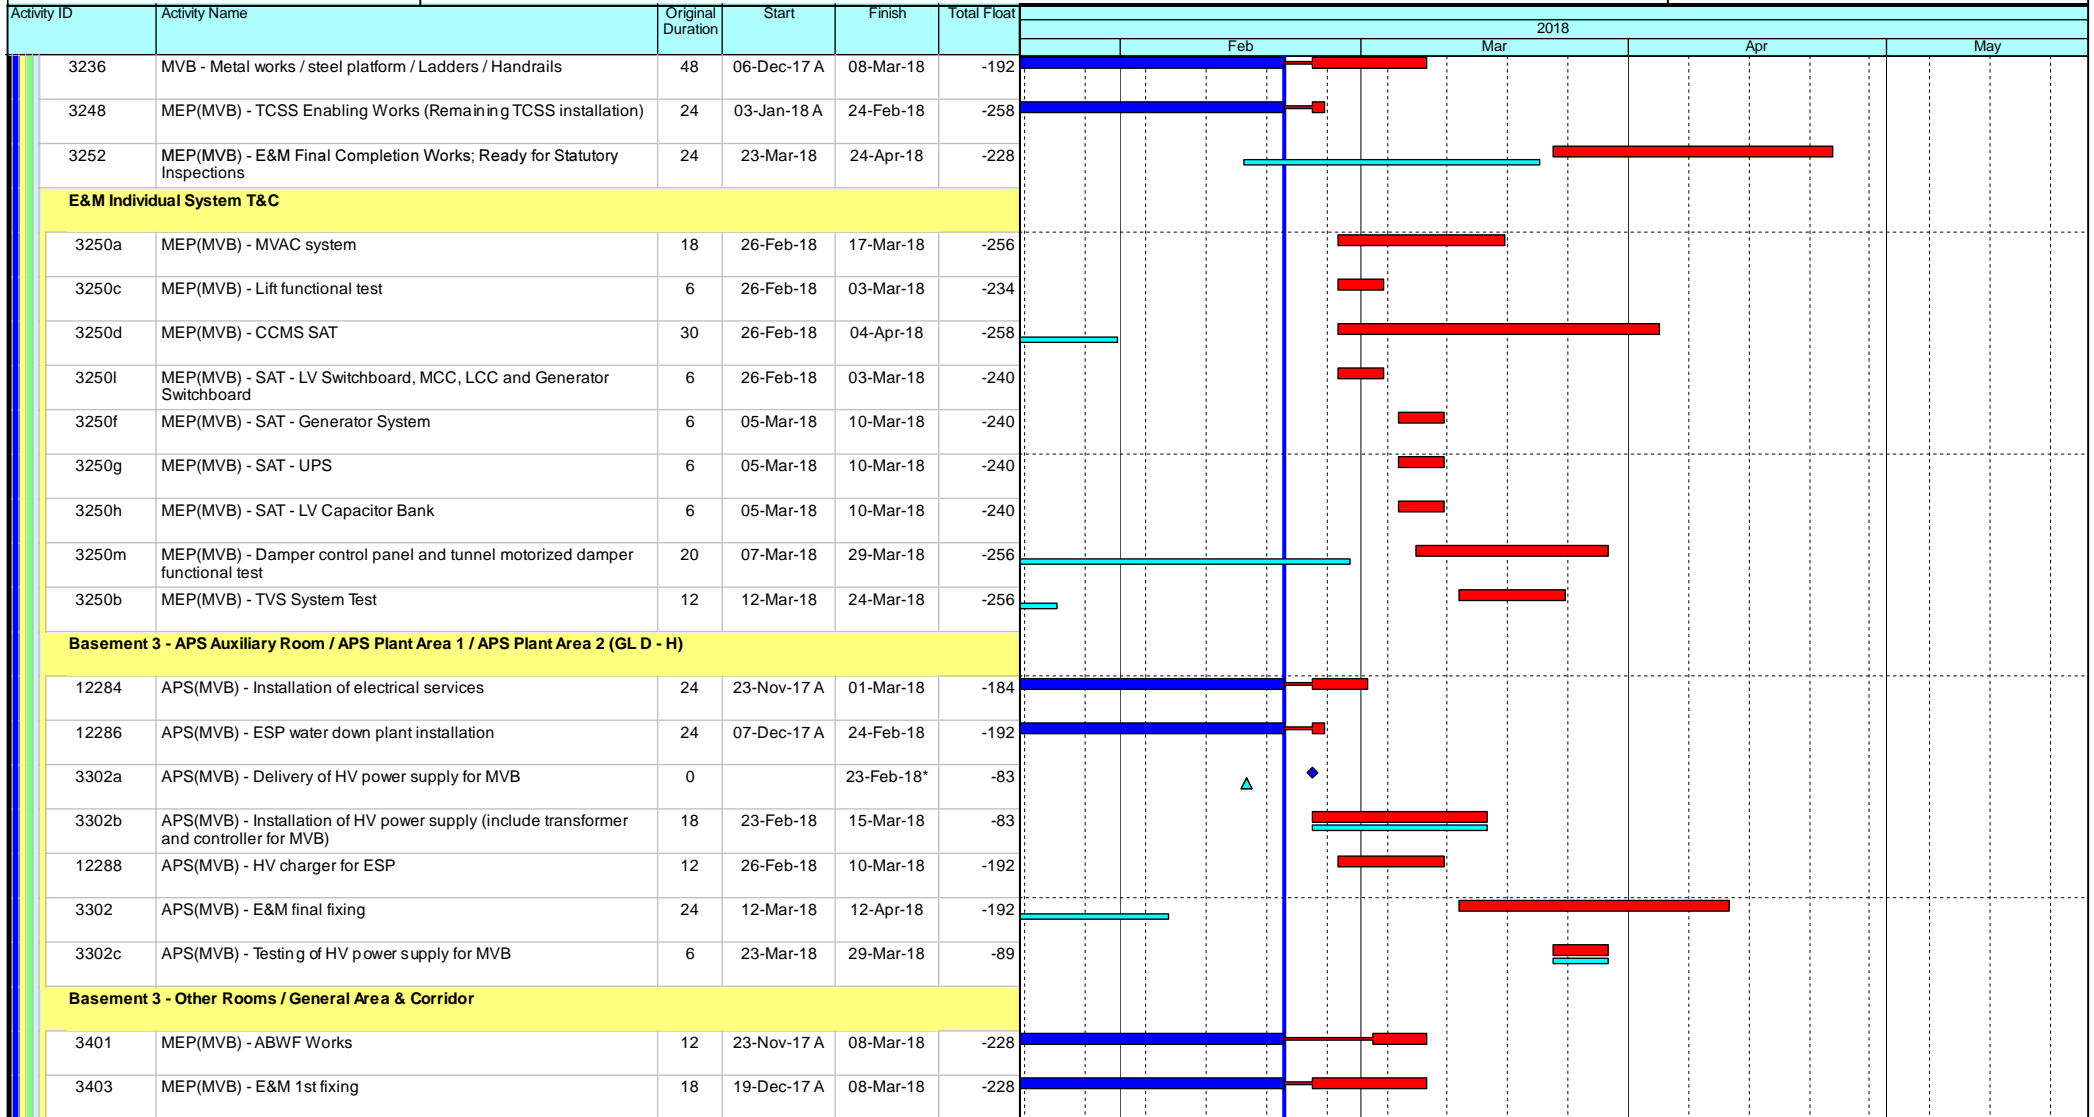

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 15 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

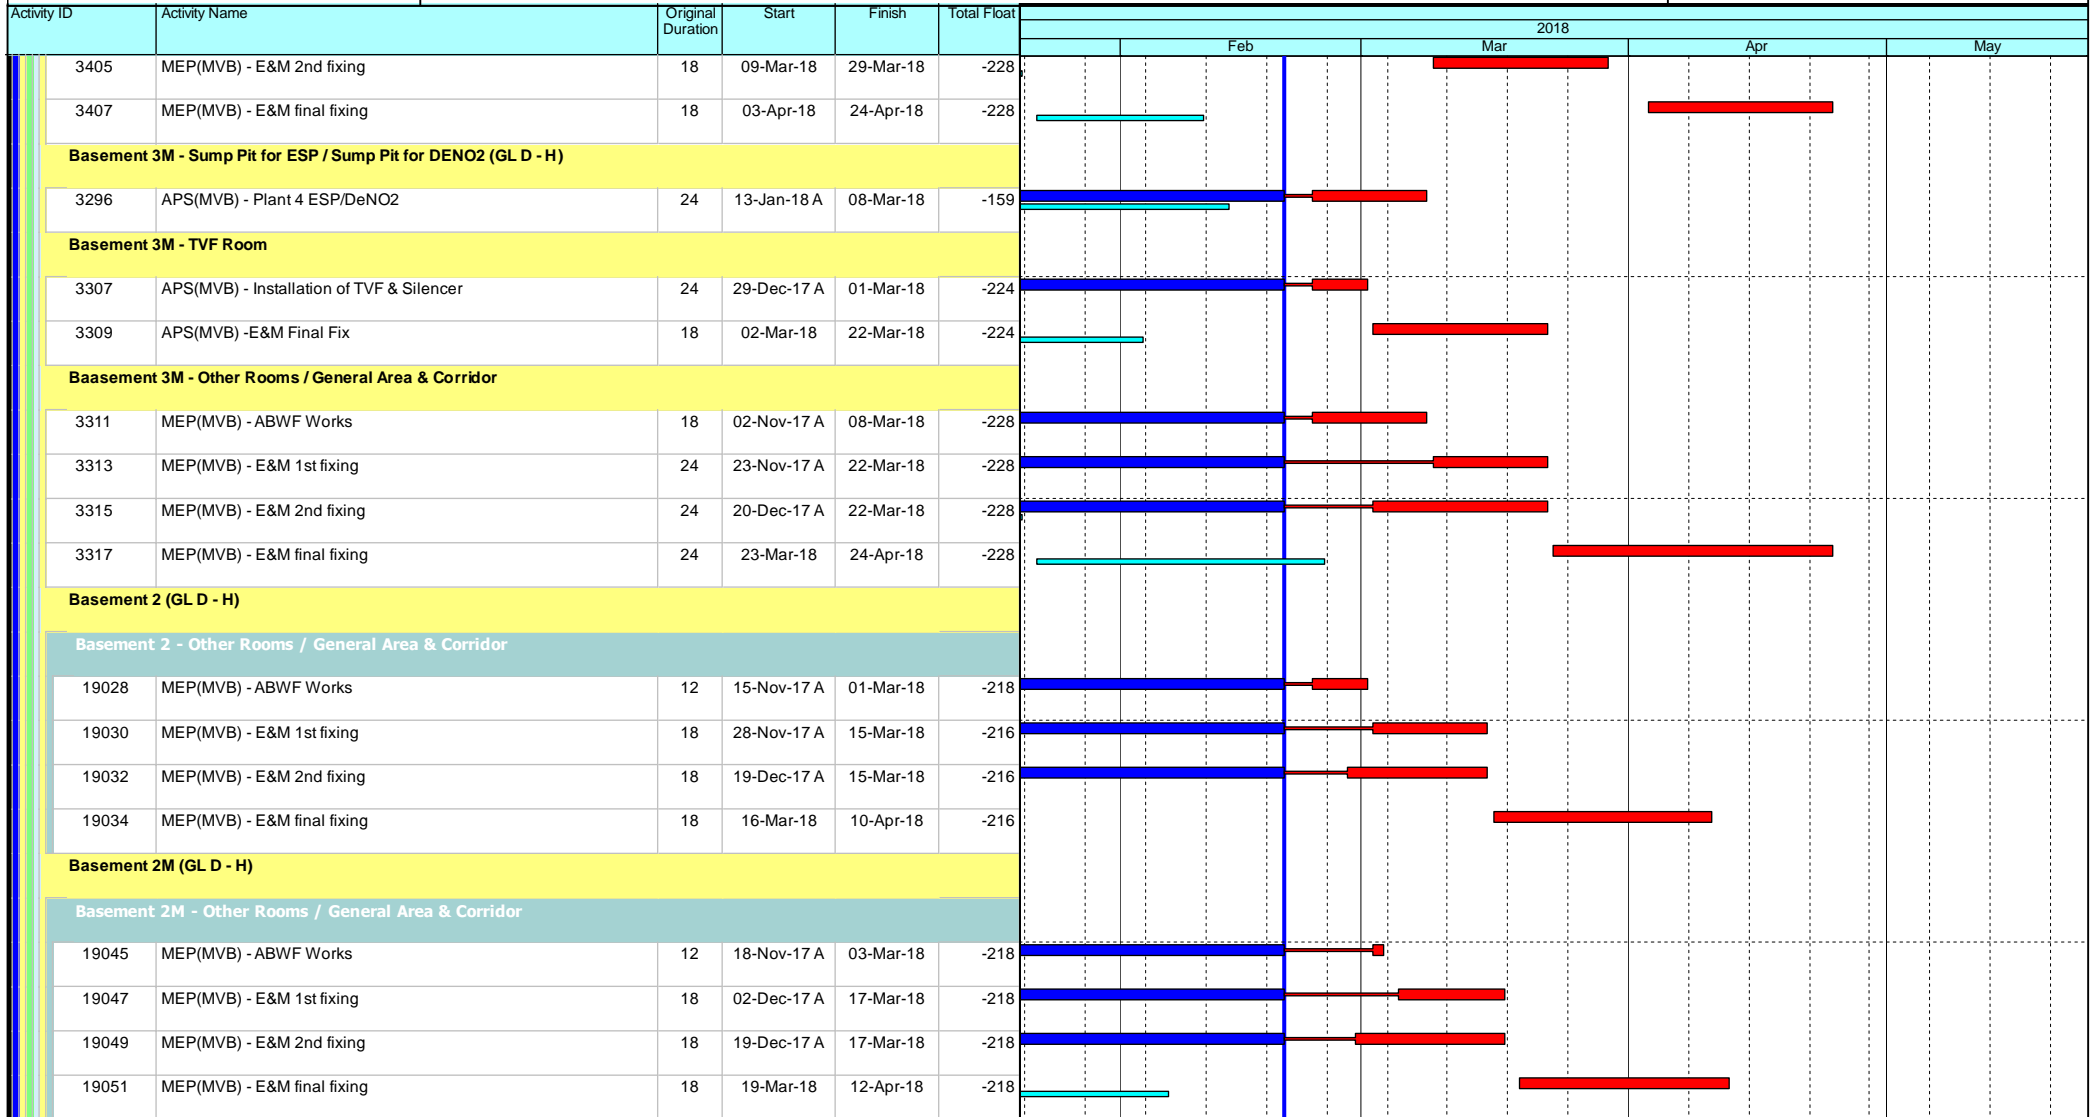

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 16 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

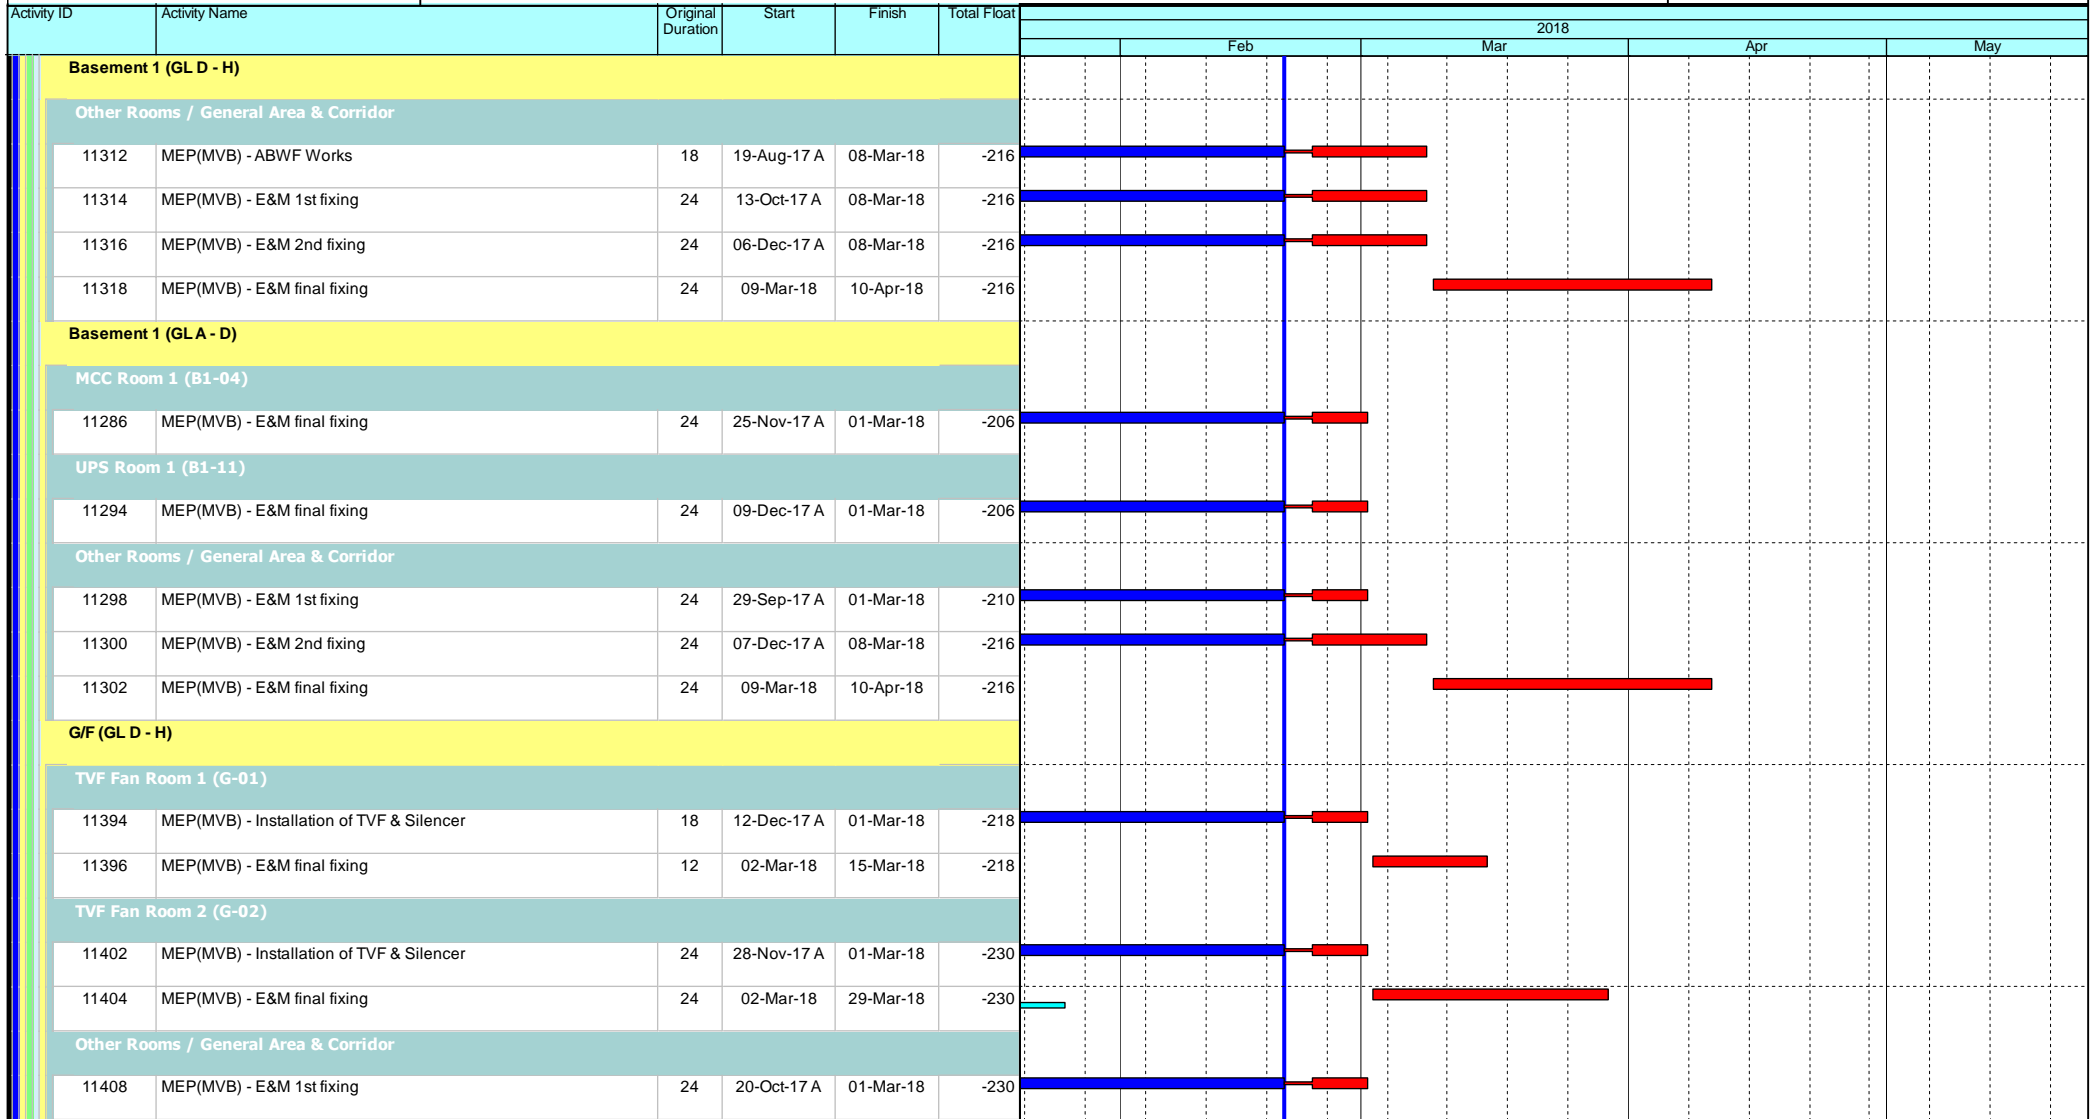

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 17 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

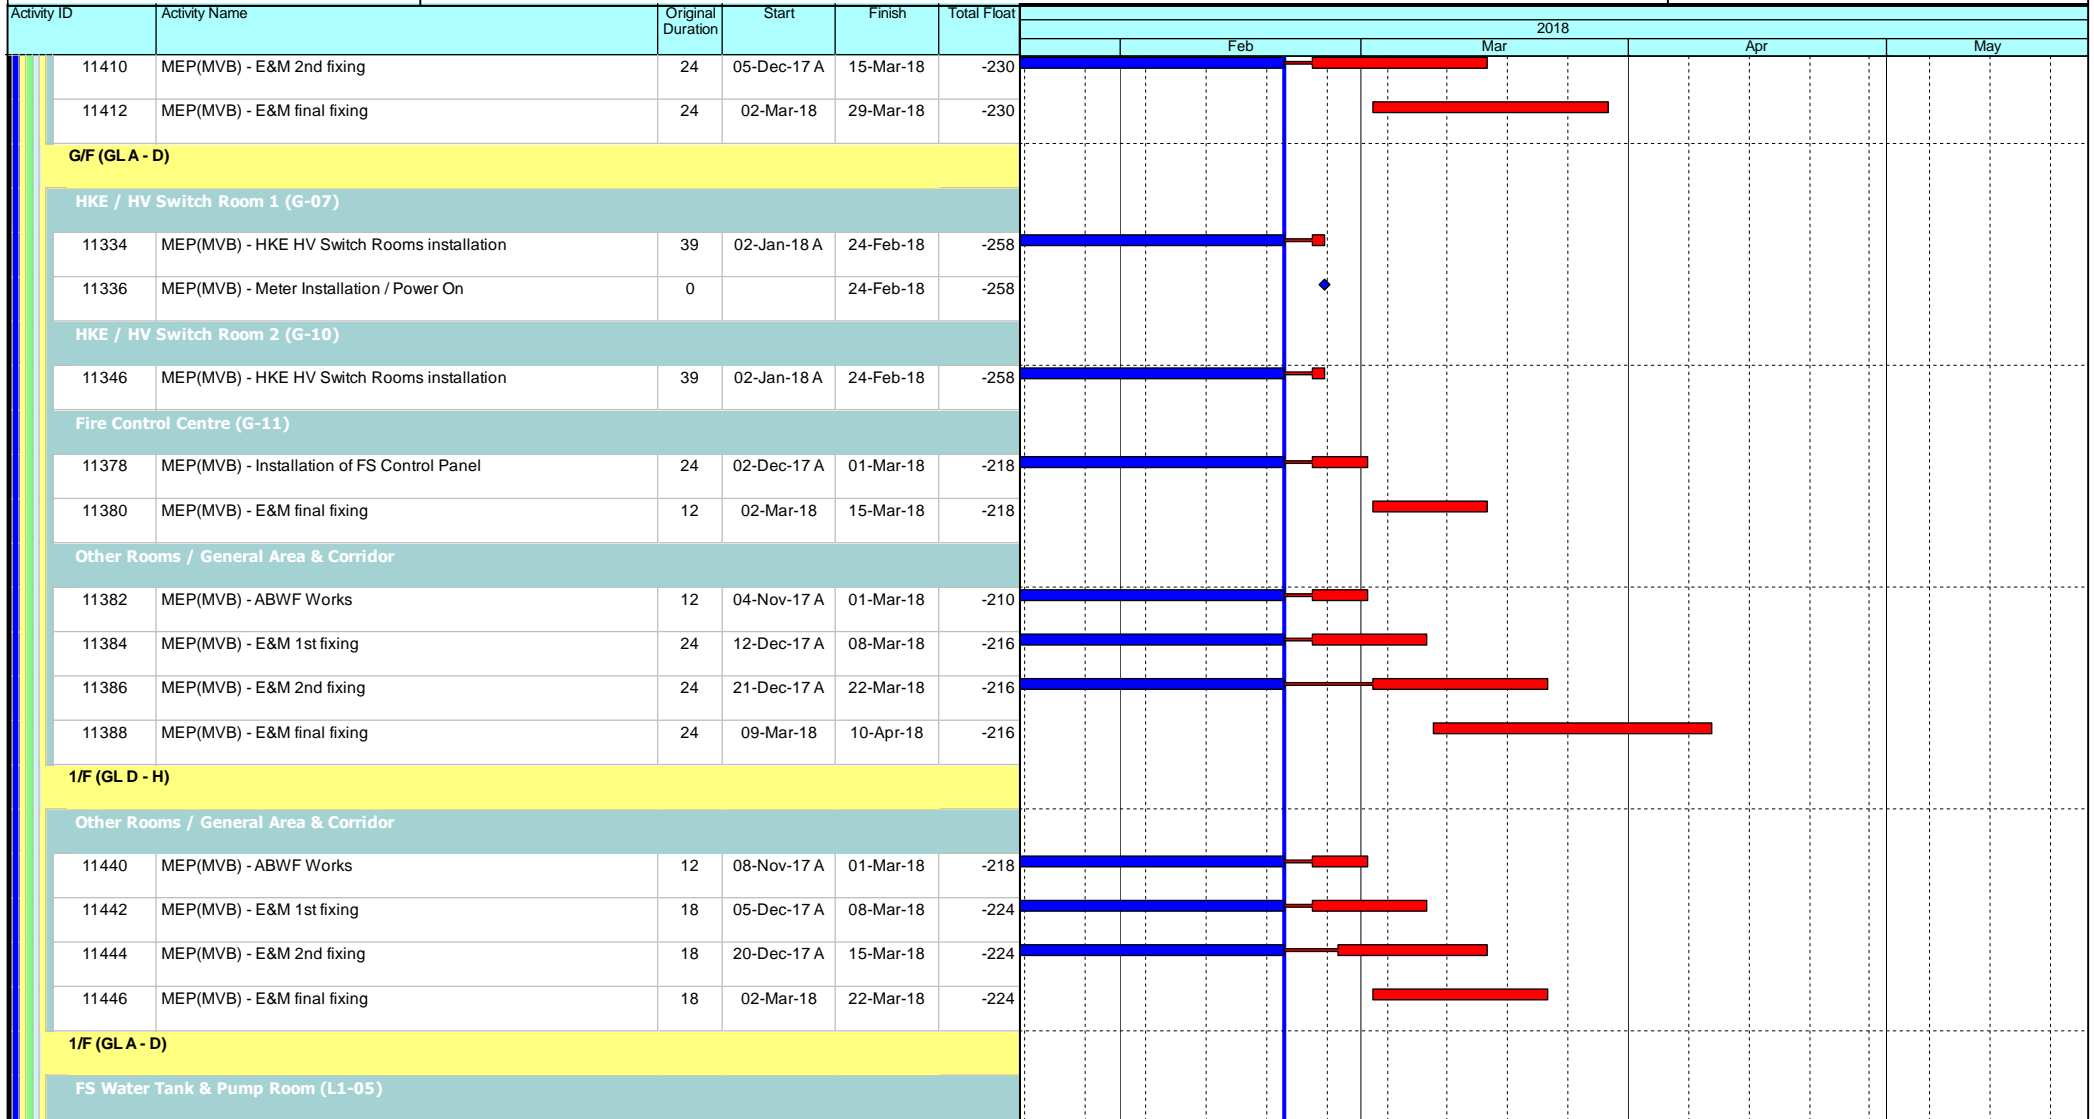

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 18 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

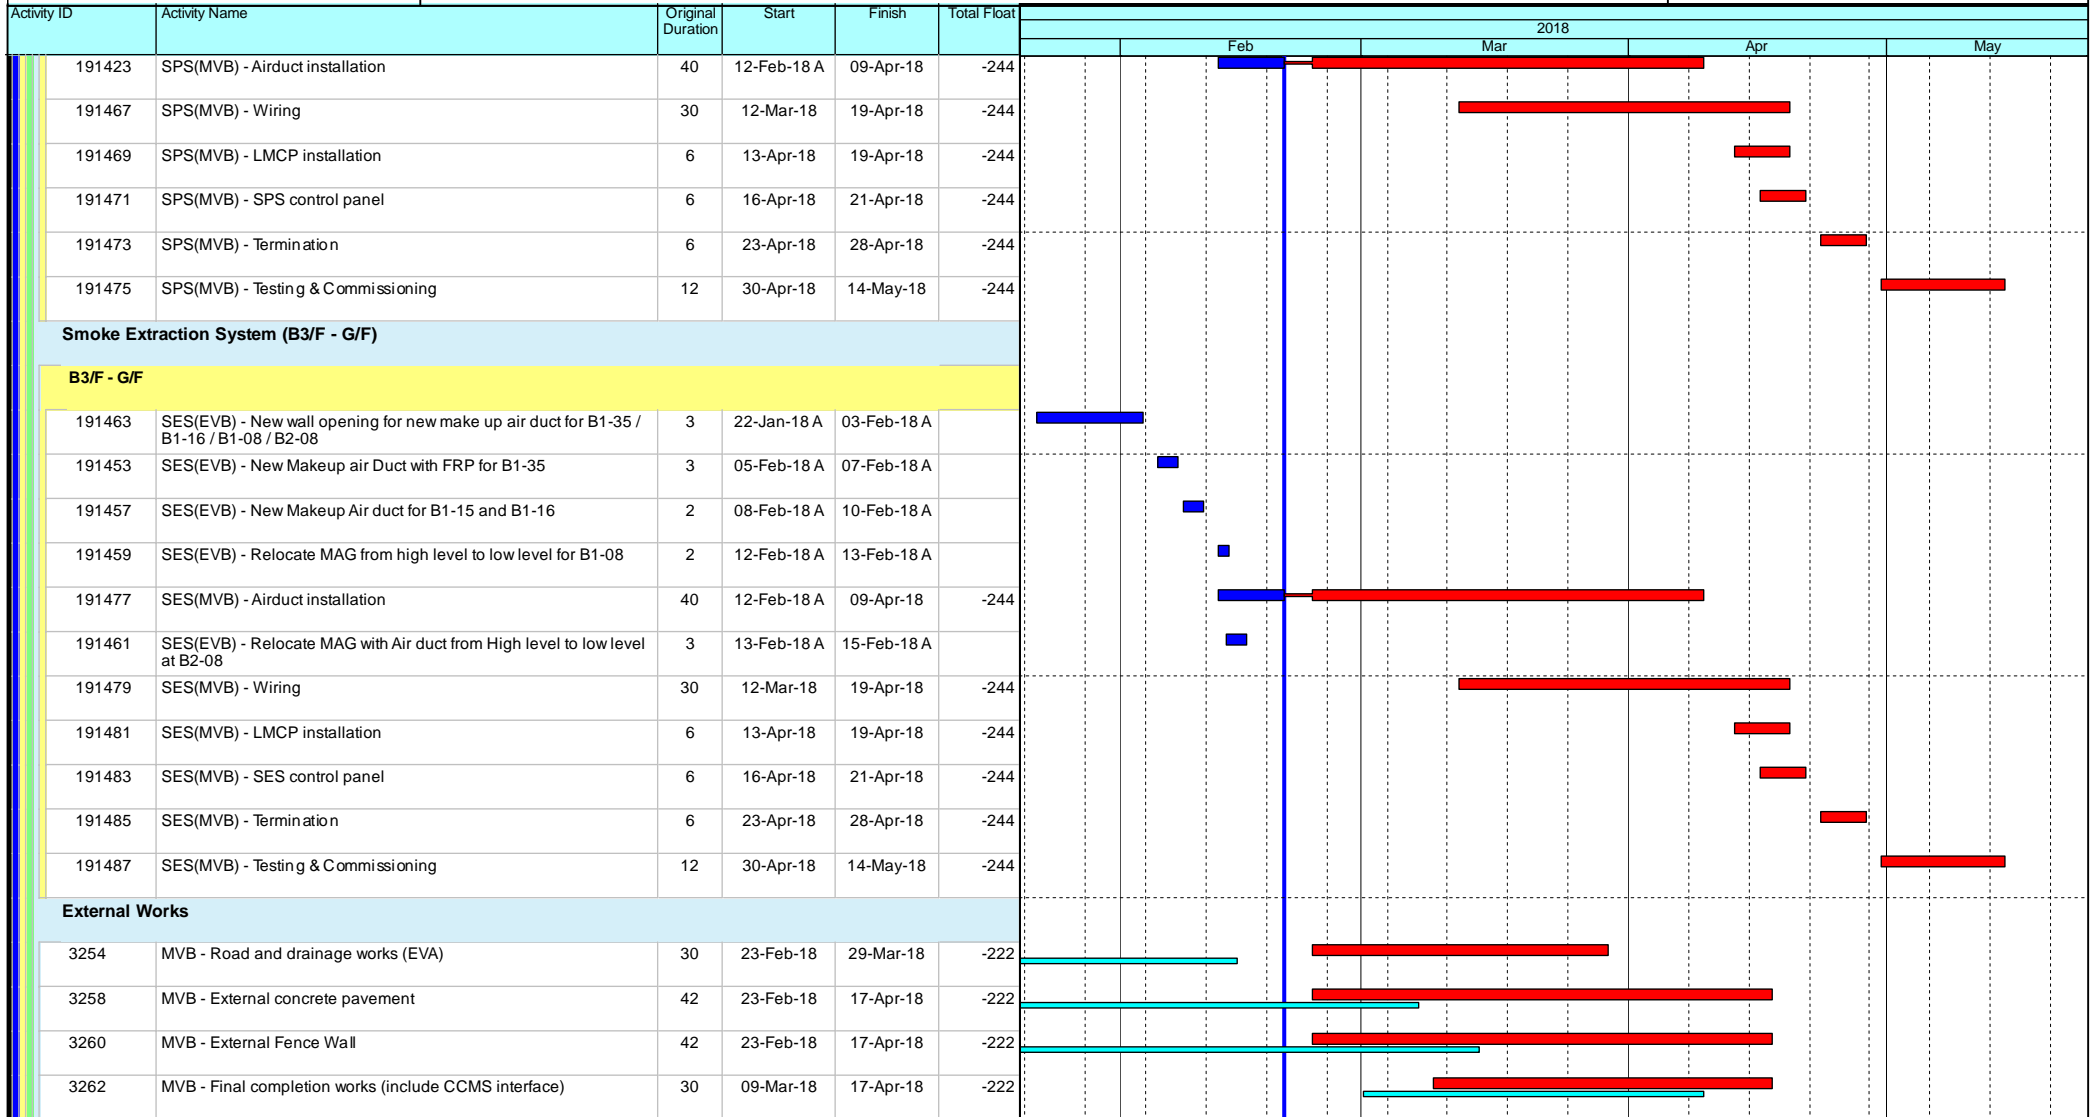

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
Baseline: SA01
Layout: Update Three Month Rolling
U048
Page 20 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

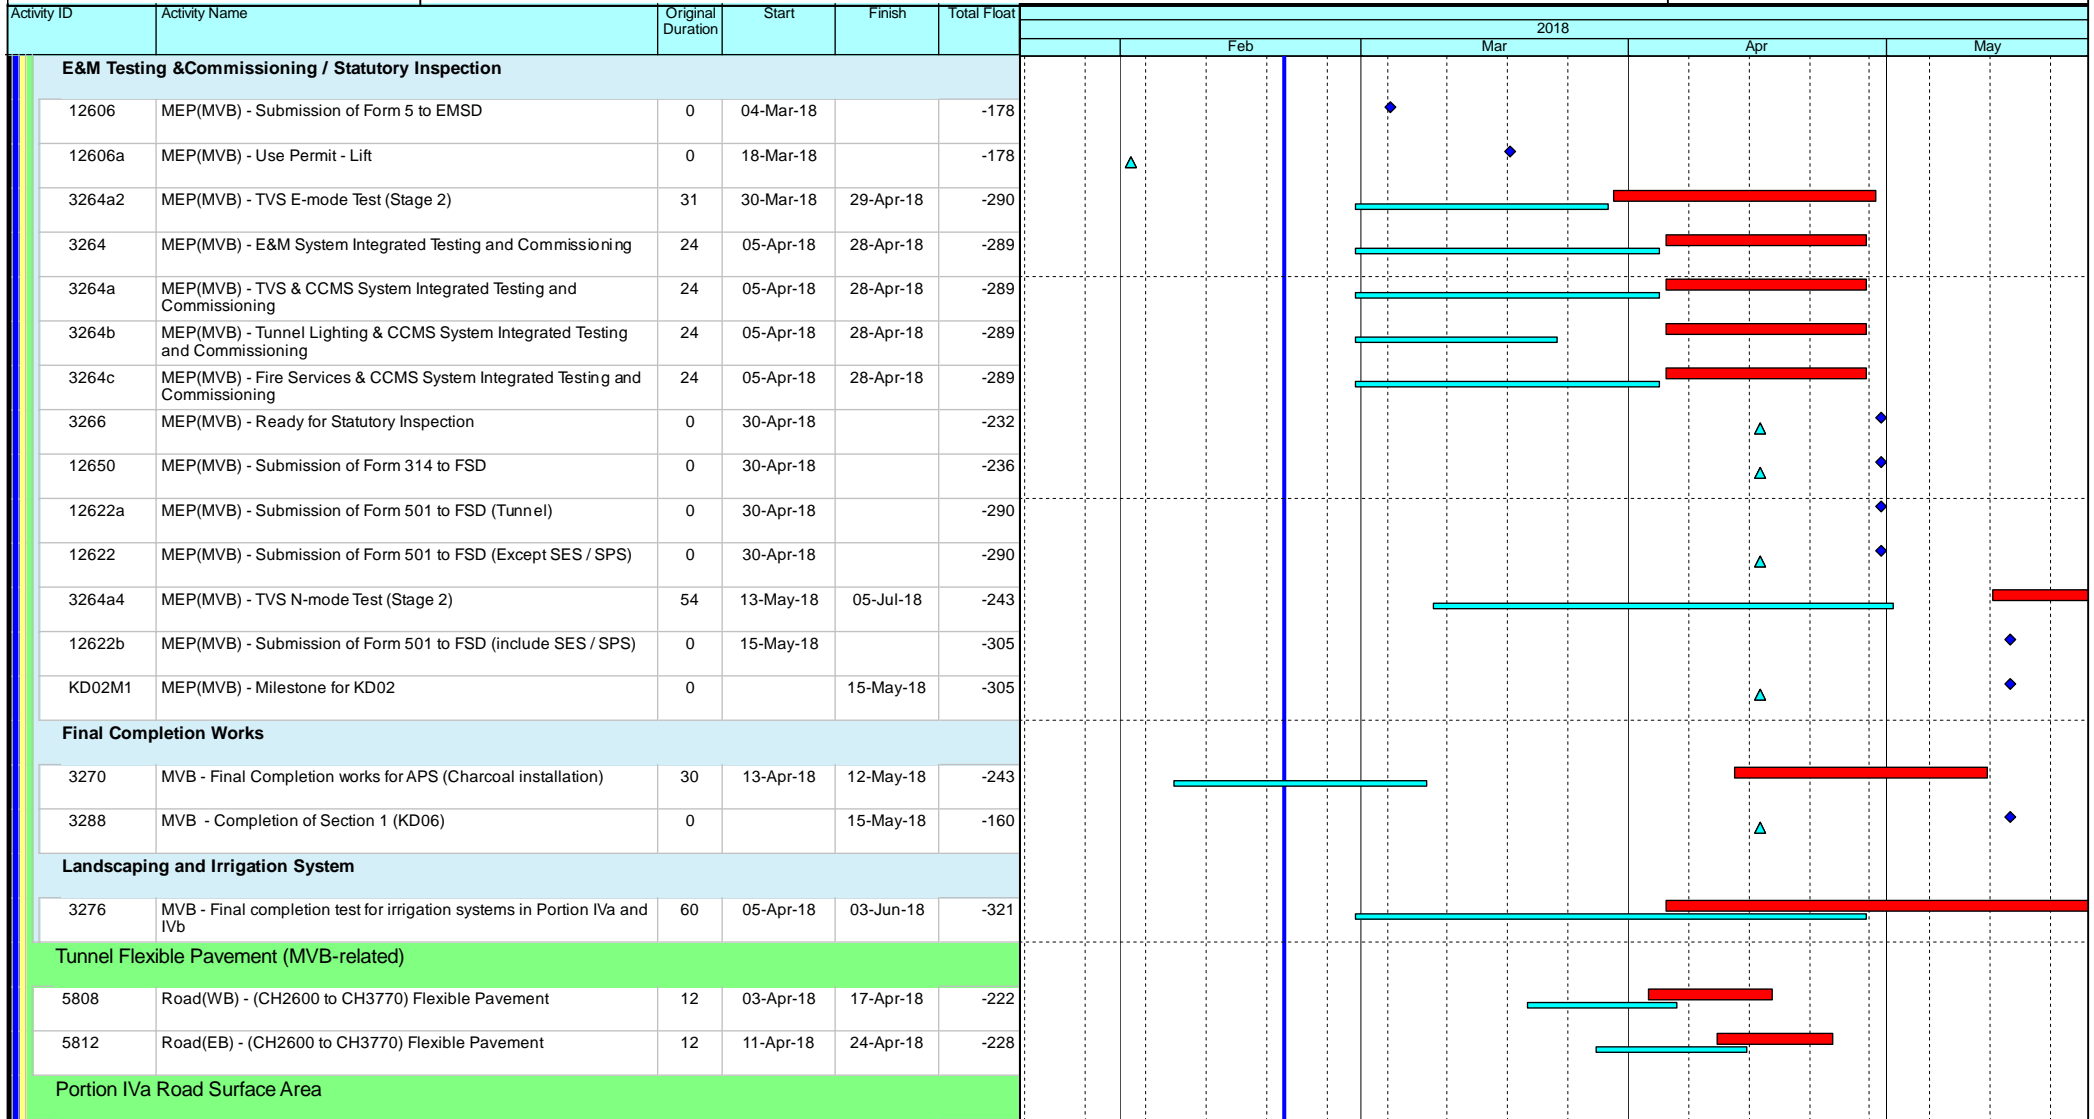

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 21 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

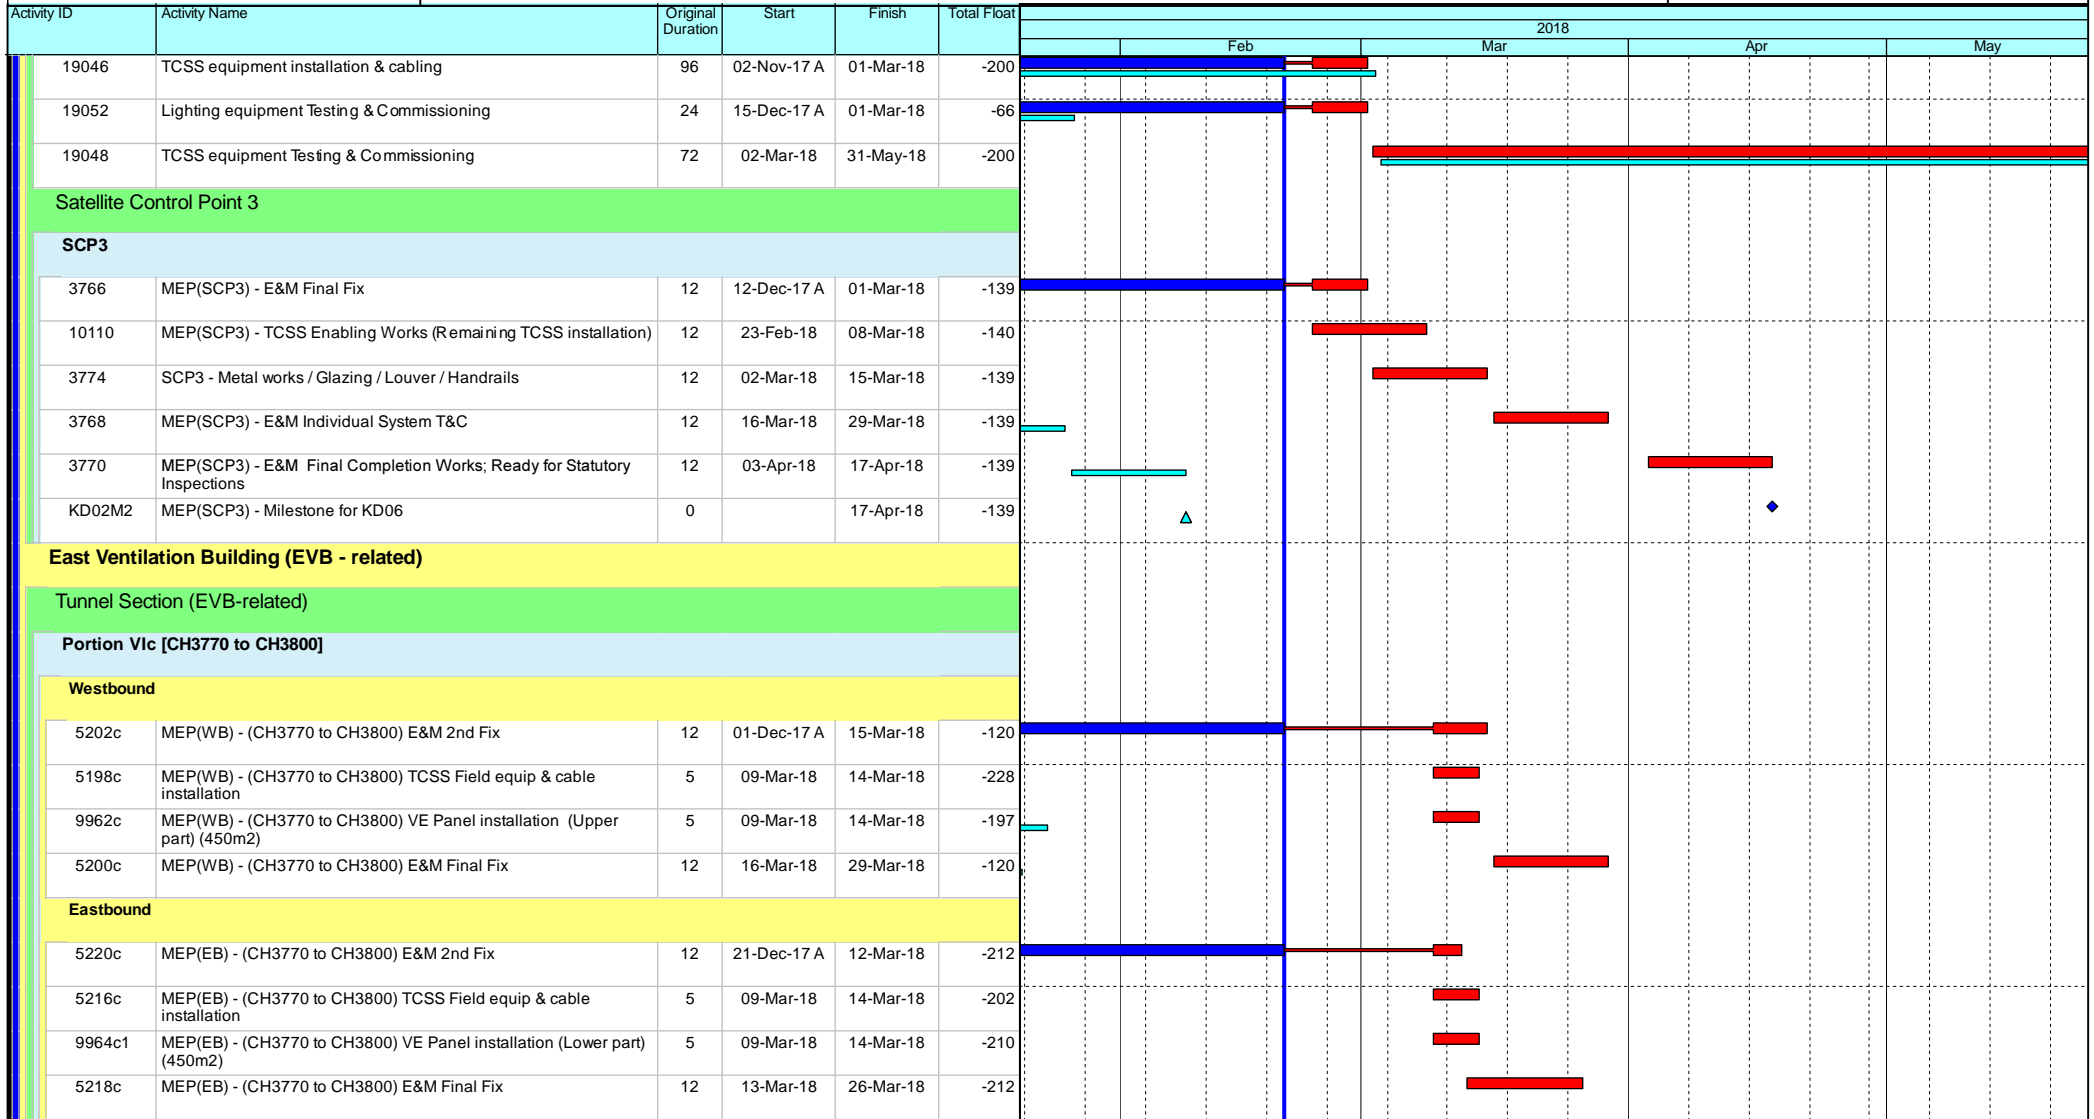

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING


Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 22 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

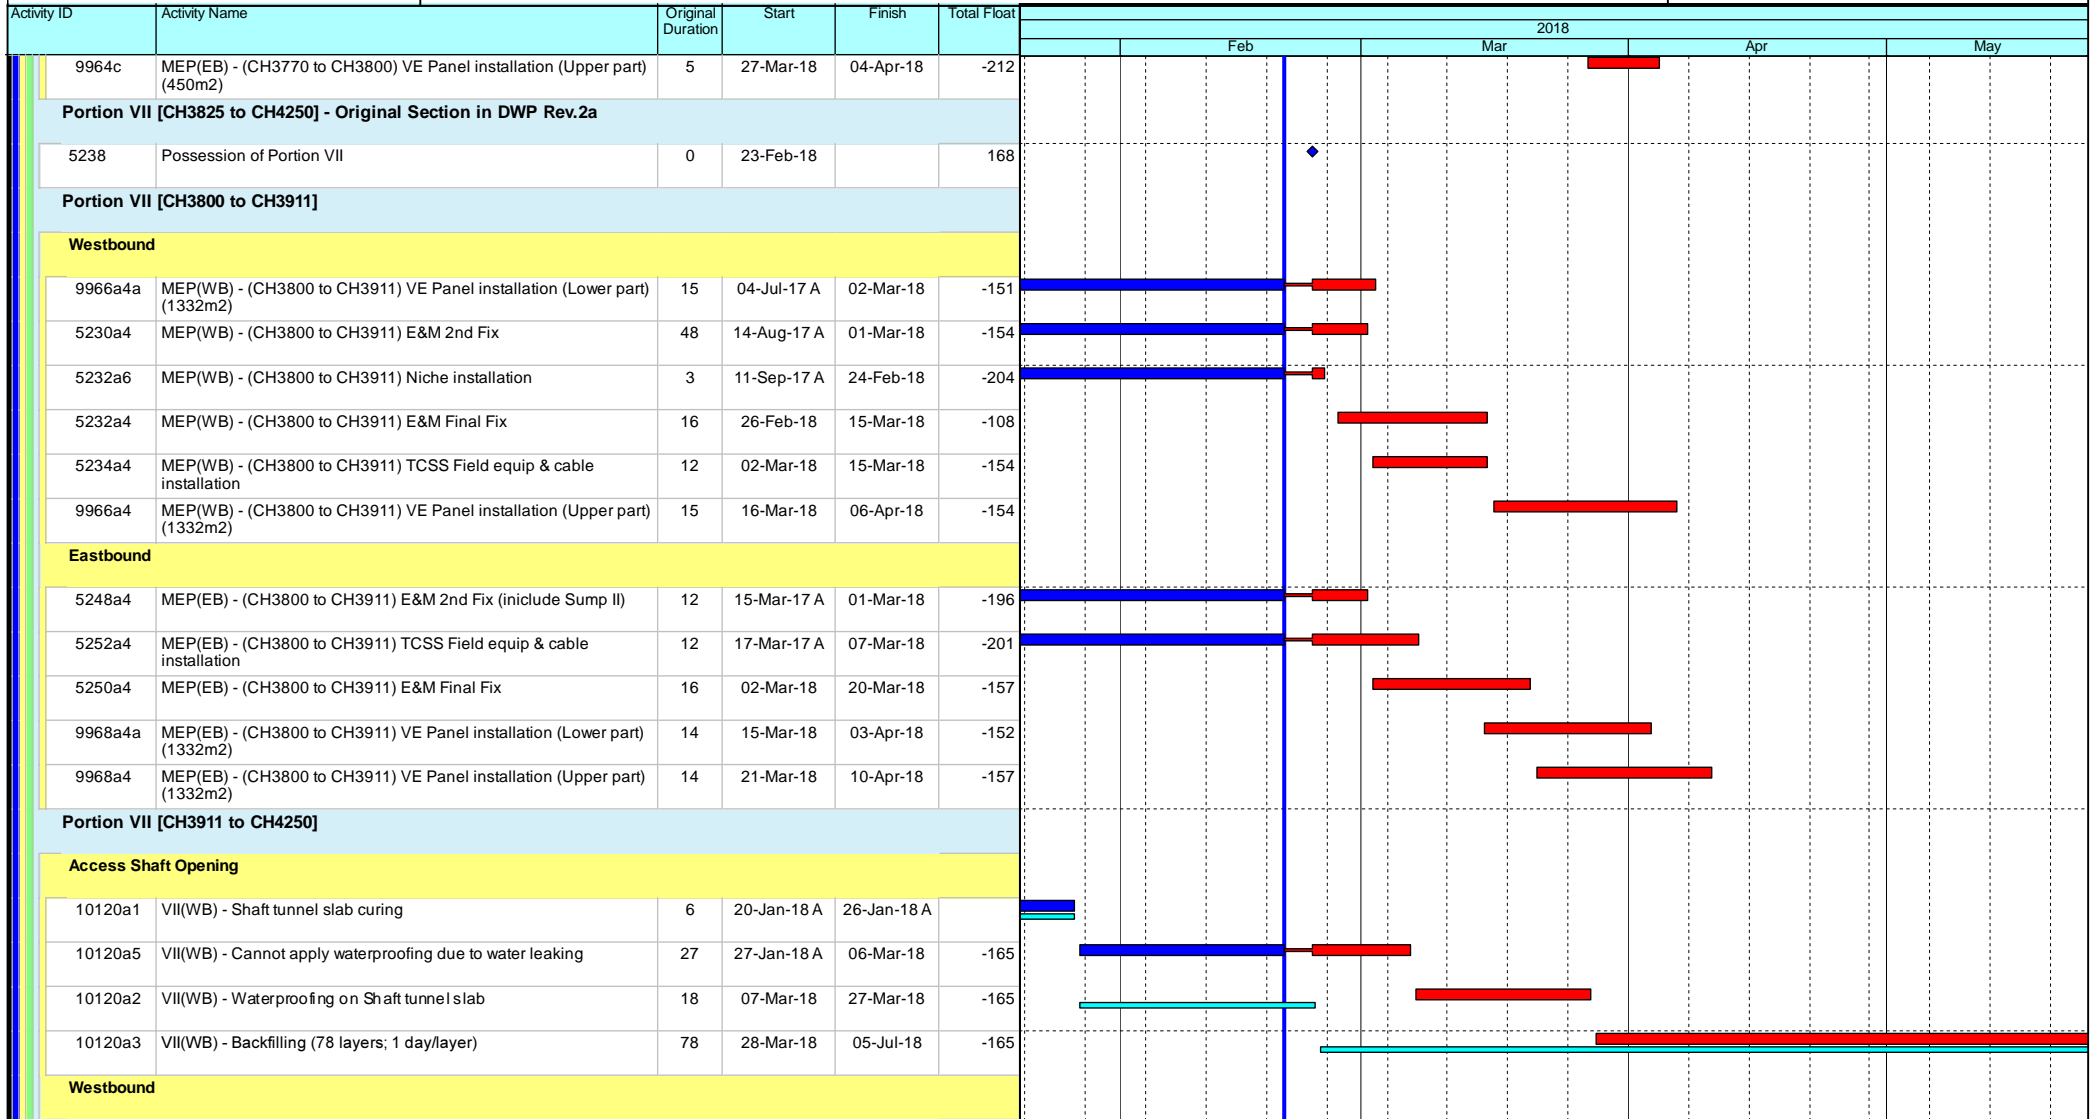

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 23 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018									
						Jan	Feb	Mar	Apr	May					
5234a2	MEP(WB) - (CH3911 to CH4250) TCSS Field equip & cable installation	15	15-Mar-17 A	09-Mar-18	-152										
5230a2	MEP(WB) - (CH3911 to CH4250) E&M 2nd Fix	48	14-Dec-17 A	01-Mar-18	-161										
5232a2	MEP(WB) - (CH3911 to CH4250) E&M Final Fix	16	02-Mar-18	20-Mar-18	-161										
9966a2a	MEP(WB) - (CH3911 to CH4250) VE Panel installation (Lower part) (4068m2)	23	03-Mar-18	29-Mar-18	-151										
9966a2	MEP(WB) - (CH3911 to CH4250) VE Panel installation (Upper part) (4068m2)	21	17-Mar-18	14-Apr-18	-161										
Eastbound															
12244a	VII(EB) - Anchorage installation for subsequent E&M 1st Fix and VE Panel frame support (include protection) (4086m2)	23	02-Sep-16 A	08-Mar-18	-151										
9968a2a	MEP(EB) - (CH3911 to CH4250) VE Panel installation (Lower part) (4086m2)	23	17-May-17 A	15-Mar-18	-152										
5250a2	MEP(EB) - (CH3911 to CH4250) E&M Final Fix	16	23-Feb-18	13-Mar-18	-150										
5252a2	MEP(EB) - (CH3911 to CH4250) TCSS Field equip & cable installation	15	23-Feb-18	12-Mar-18	-149										
9968a2	MEP(EB) - (CH3911 to CH4250) VE Panel installation (Upper part) (4086m2)	12	02-Mar-18	15-Mar-18	-152										
Slip Road 8															
13082a	VII(SR8) - Anchorage installation for subsequent E&M 1st Fix and VE Panel frame support (include protection) (1500m2)	24	09-Jan-17 A	15-Mar-18	-151										
13084a1	MEP(SR8) - (CH1000 to CH750) VE Panel installation (Lower part) (550m2)	6	27-Jun-17 A	22-Mar-18	-151										
13068a	MEP(SR8) - (CH1000 to CH750) E&M 1st Fix	12	23-Dec-17 A	15-Mar-18	-151										
13070a	MEP(SR8) - (CH1000 to CH750) E&M 2nd Fix (include Sump D)	12	09-Mar-18	22-Mar-18	-151										
13072a	MEP(SR8) - (CH1000 to CH750) E&M Final Fix	12	16-Mar-18	29-Mar-18	-151										
13074a	MEP(SR8) - (CH1000 to CH750) TCSS Field equip & cable installation	12	16-Mar-18	29-Mar-18	-151										
13084a	MEP(SR8) - (CH1000 to CH750) VE Panel installation (Upper part) (550m2)	6	23-Mar-18	29-Mar-18	-151										
Portion VIIIa [CH4250 to CH4600]															
Westbound															
9970a	MEP(WB) - (CH4250 to CH4600) VE Panel installation (Lower part) (3900m2)	20	20-Sep-17 A	01-Mar-18	-140										
5282	MEP(WB) - (CH4250 to CH4600) E&M Final Fix	12	06-Jan-18 A	01-Mar-18	-147										
5284	MEP(WB) - (CH4250 to CH4600) TCSS Field equip & cable installation	11	23-Feb-18	07-Mar-18	-152										

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 24 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018									
						Feb	Mar	Apr	May						
5314	MEP(EB) - (CH4600 to CH4860) E&M Final Fix	9	10-Mar-18	20-Mar-18	-149										
Portion IXa [CH4860 to CH5150]															
Westbound															
5326	MEP(WB) - (CH4860 to CH5150) E&M 2nd Fix (include Sump E)	32	22-May-17 A	08-Mar-18	-112										
9978a	MEP(WB) - (CH4860 to CH5150) VE Panel installation (Lower part) (3288m2)	37	07-Jun-17 A	15-Mar-18	-139										
5330	MEP(WB) - (CH4860 to CH5150) TCSS Field equip & cable installation	9	29-Dec-17 A	20-Mar-18	-112										
9978	MEP(WB) - (CH4860 to CH5150) VE Panel installation (Upper part) (3288m2)	37	23-Feb-18	11-Apr-18	-158										
5328	MEP(WB) - (CH4860 to CH5150) E&M Final Fix	10	09-Mar-18	20-Mar-18	-112										
Eastbound															
5344	MEP(EB) - (CH4860 to CH5150) E&M 2nd Fix (include Sump E)	32	12-Dec-17 A	01-Mar-18	-145										
9980	MEP(EB) - (CH4860 to CH5150) VE Panel installation (Upper part) (3288m2)	37	23-Feb-18	11-Apr-18	-158										
9980a	MEP(EB) - (CH4860 to CH5150) VE Panel installation (Lower part) (3288m2)	37	23-Feb-18	11-Apr-18	-158										
5346	MEP(EB) - (CH4860 to CH5150) E&M Final Fix	10	09-Mar-18	20-Mar-18	-112										
5348	MEP(EB) - (CH4860 to CH5150) TCSS Field equip & cable installation	9	10-Mar-18	20-Mar-18	-112										
Portion VIIIb [SR8 CH500 to CH350]															
Slip Road 8															
5356a	MEP(SR8) - (CH500 to CH350) E&M 1st Fix	12	03-Jan-18 A	01-Mar-18	-155										
5358a	MEP(SR8) - (CH500 to CH350) E&M 2nd Fix (include Sump D)	24	03-Jan-18 A	08-Mar-18	-161										
5362a	MEP(SR8) - (CH500 to CH350) TCSS Field equip & cable installation	11	15-Jan-18 A	01-Mar-18	-150										
12828a1	MEP(SR8) - (CH500 to CH350) VE Panel installation (Lower part) (600m2)	8	23-Feb-18	03-Mar-18	-129										
5360a	MEP(SR8) - (CH500 to CH350) E&M Final Fix	12	01-Mar-18	14-Mar-18	-161										
12828a	MEP(SR8) - (CH500 to CH350) VE Panel installation (Upper part) (750m2)	9	05-Mar-18	14-Mar-18	-138										
Portion VIIIc [SR8 CH350 to CH210]															
Slip Road 8															

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 26 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

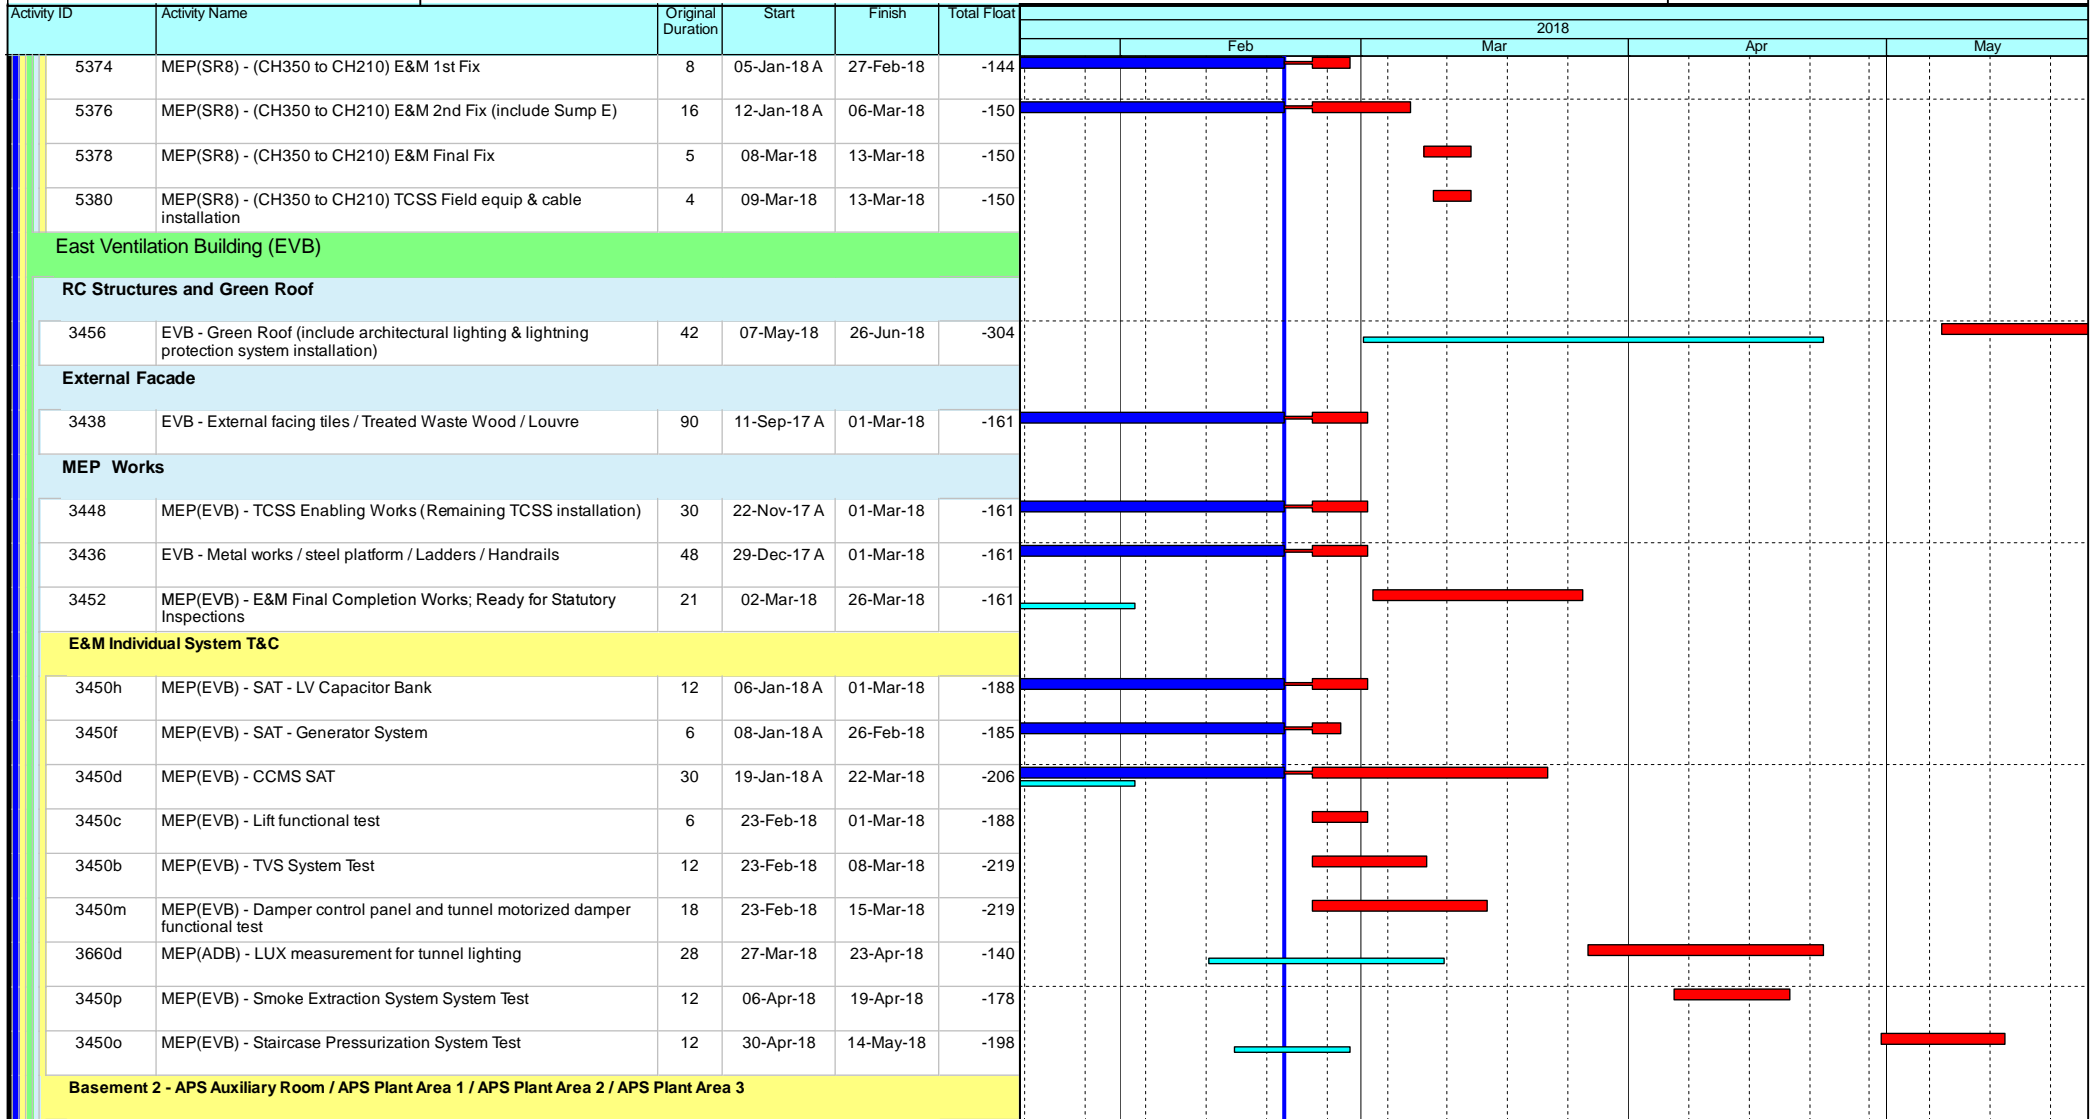

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 27 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

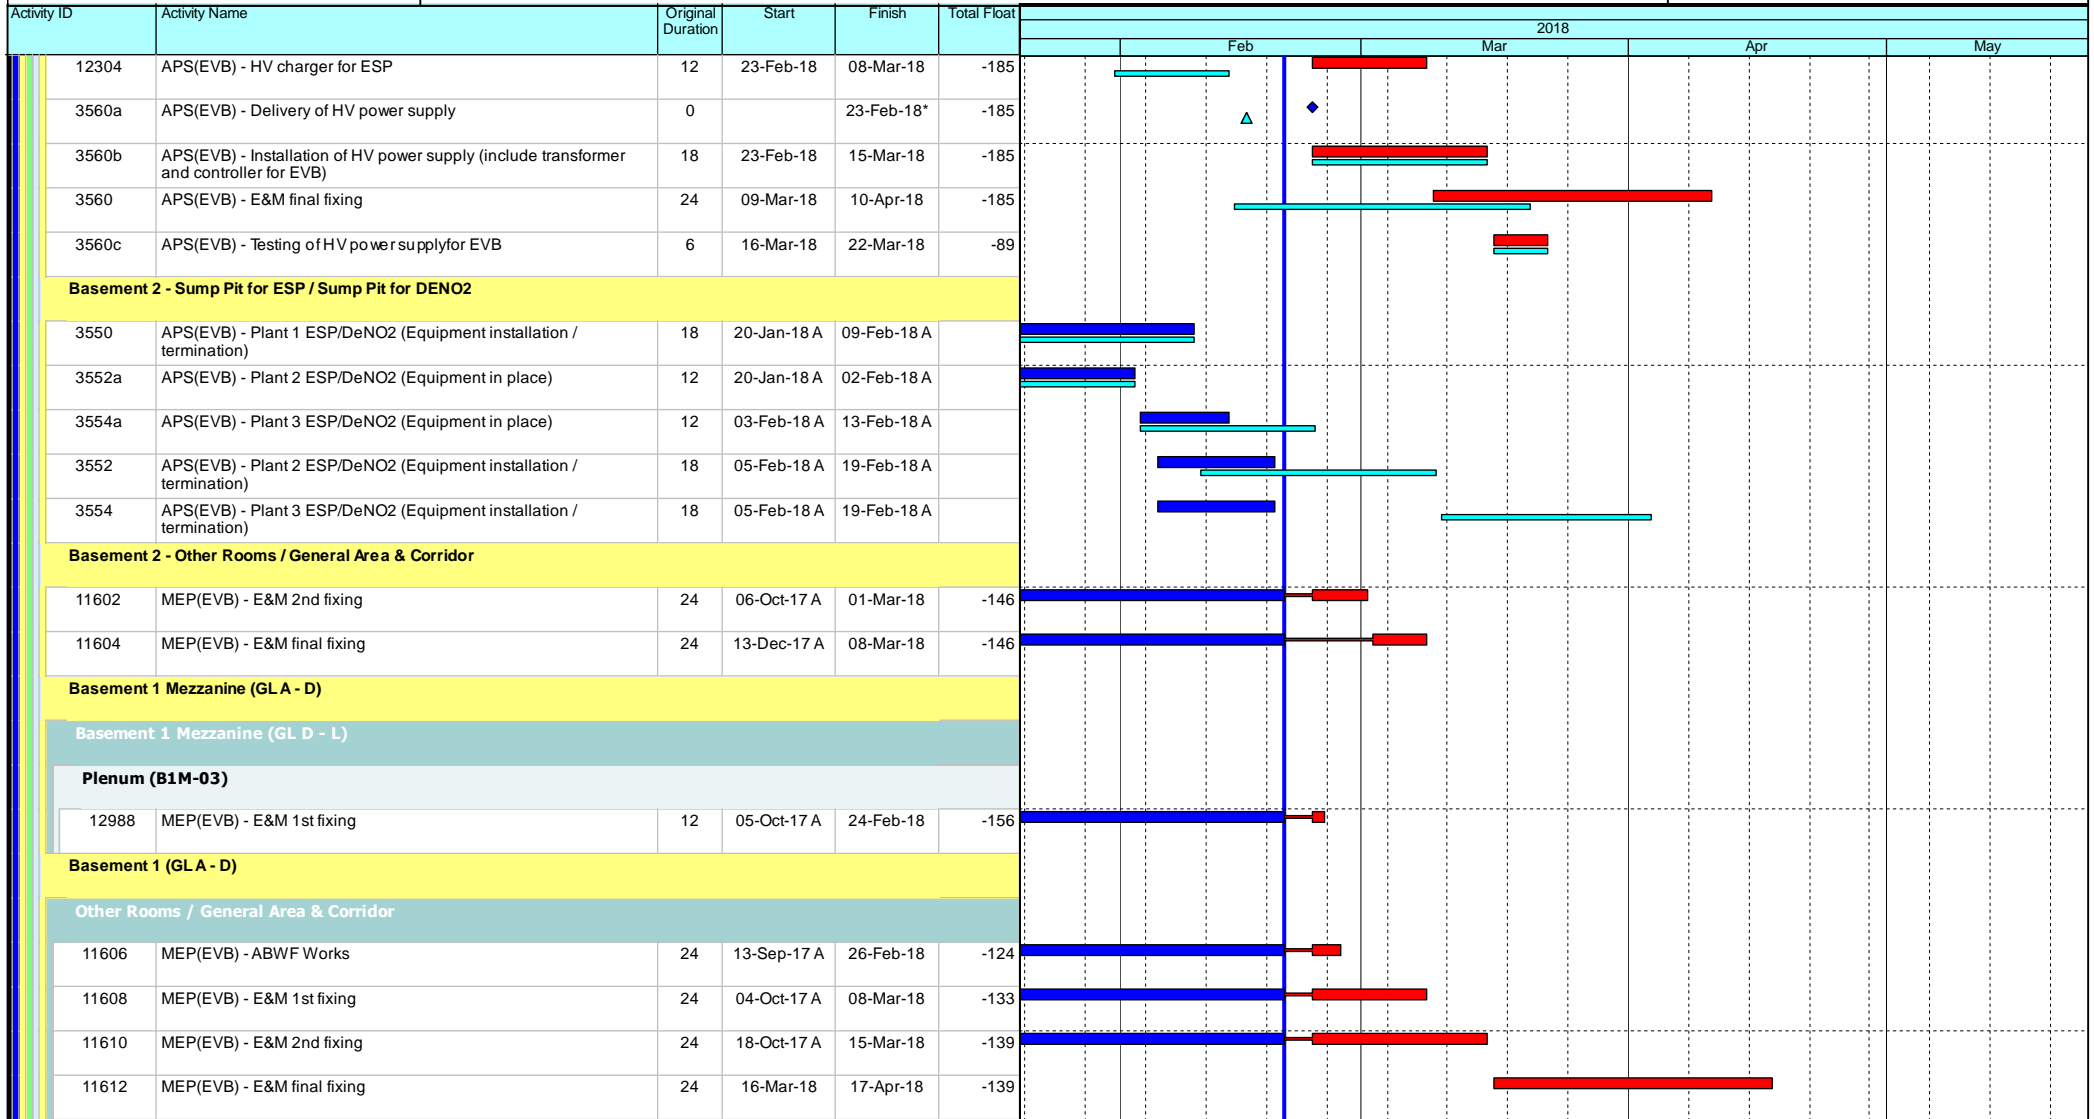

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 28 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

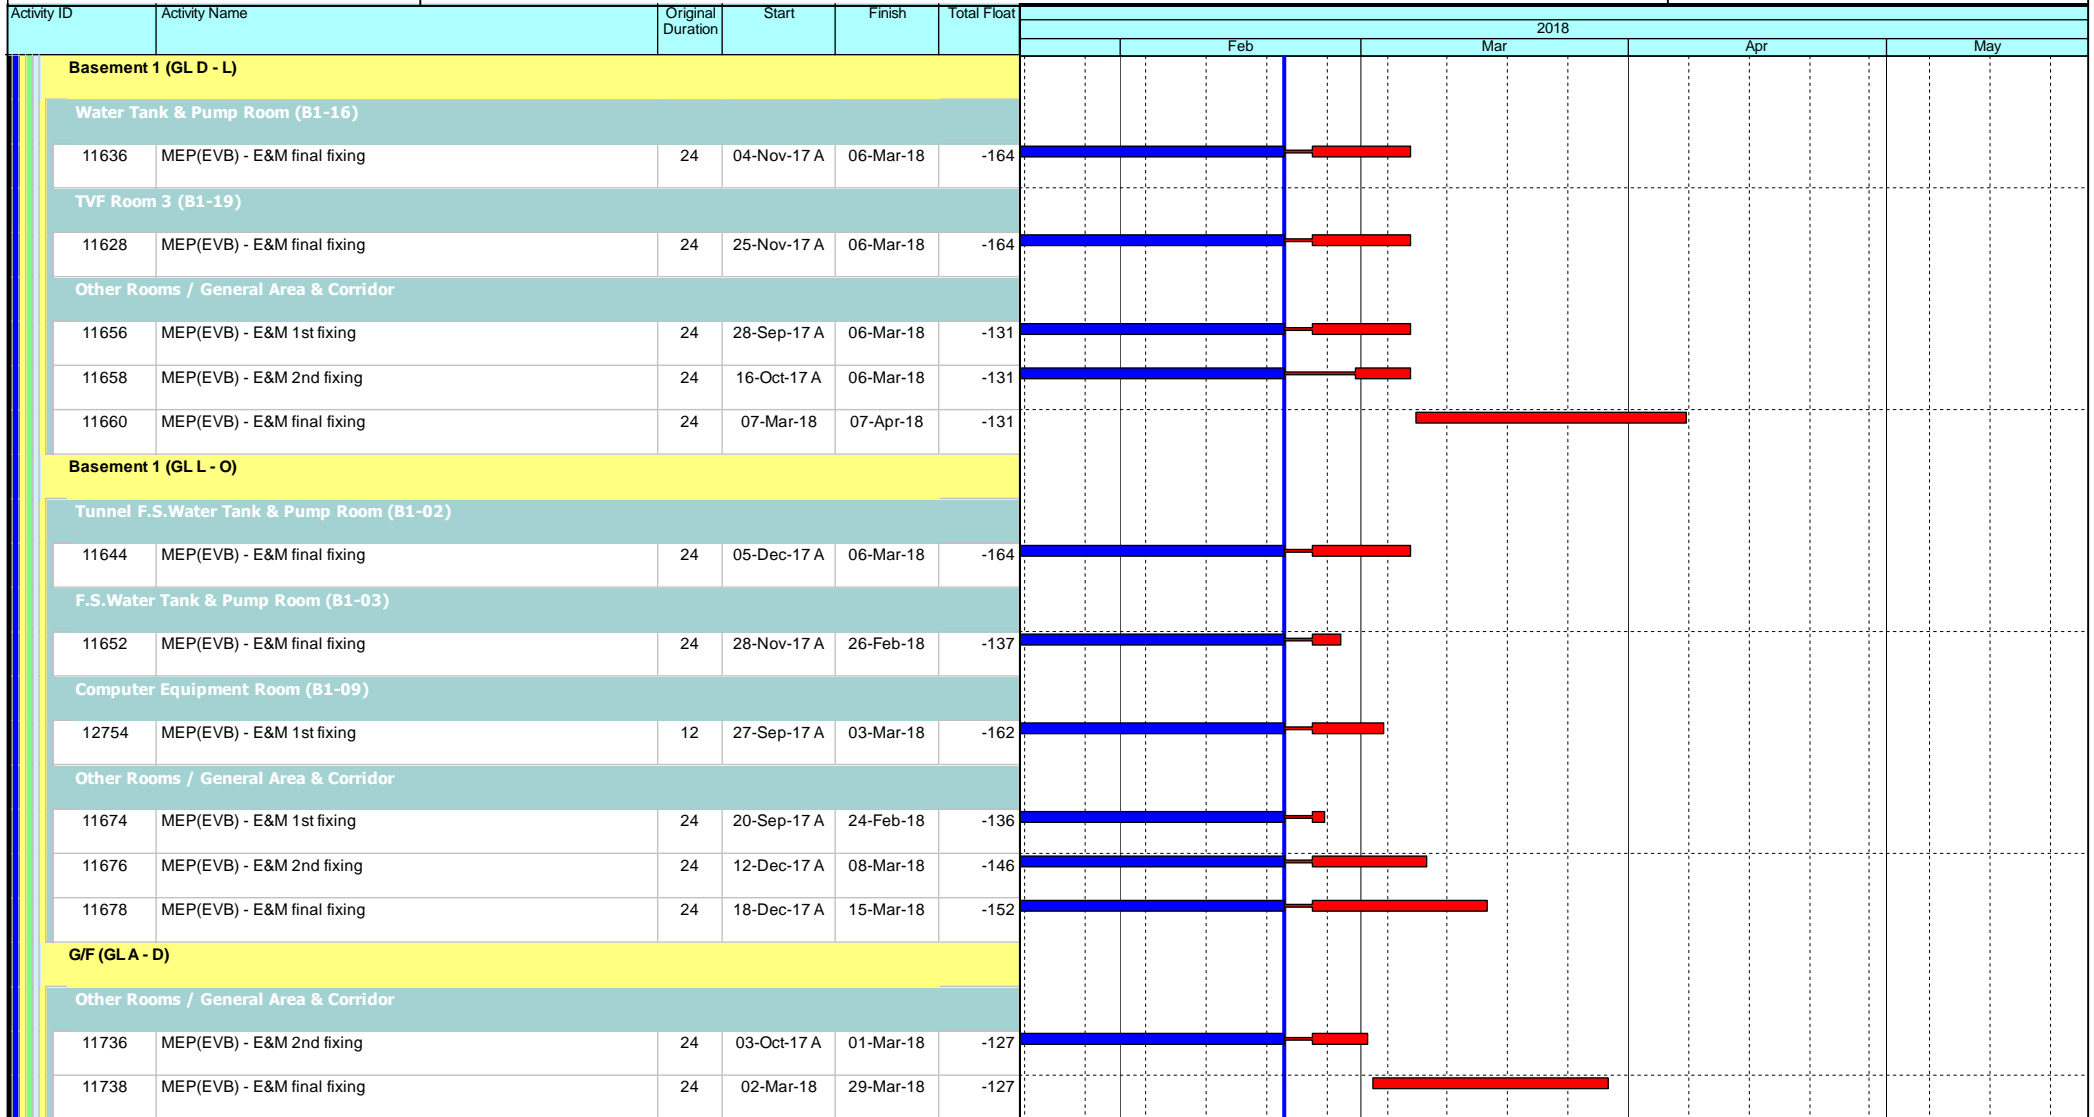

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 29 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

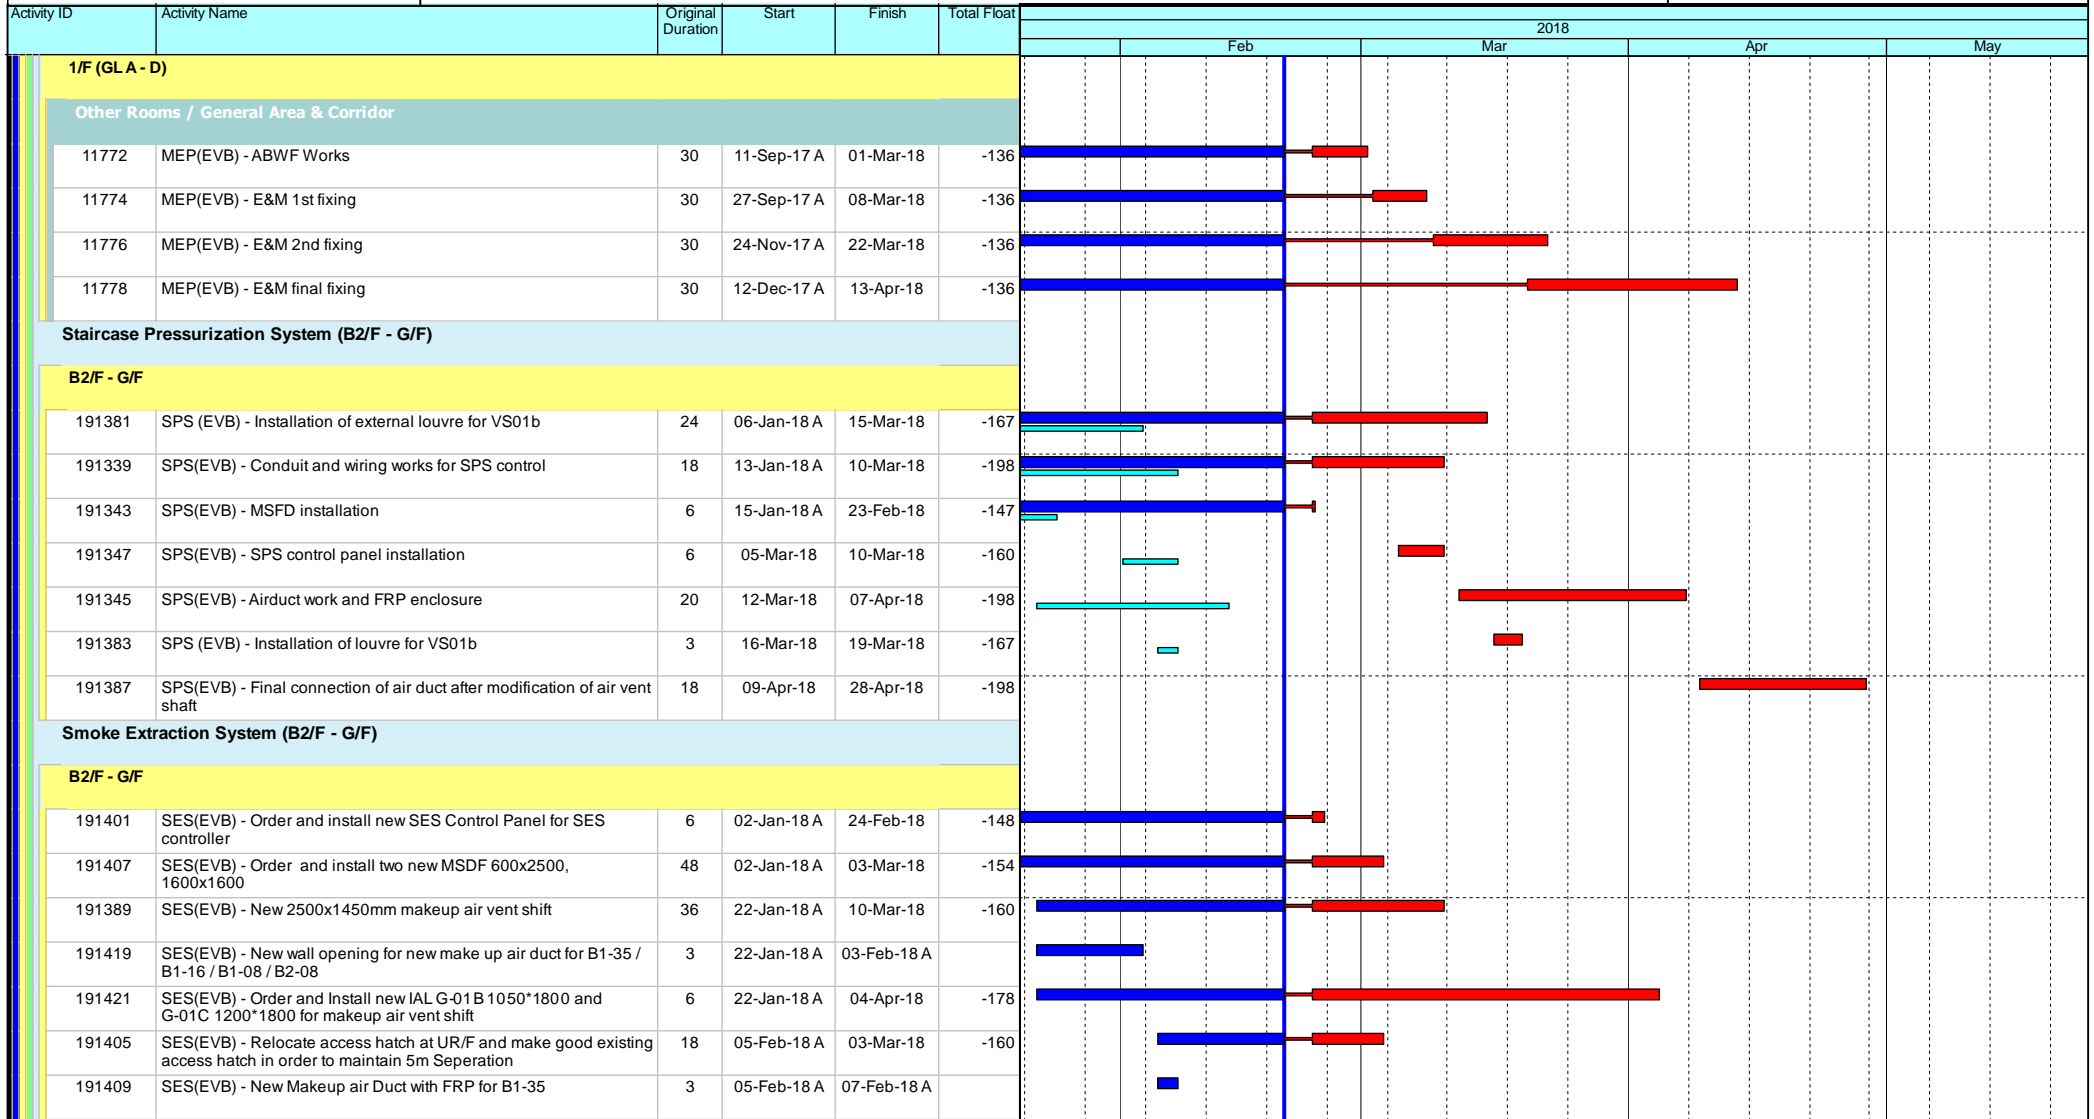

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 30 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

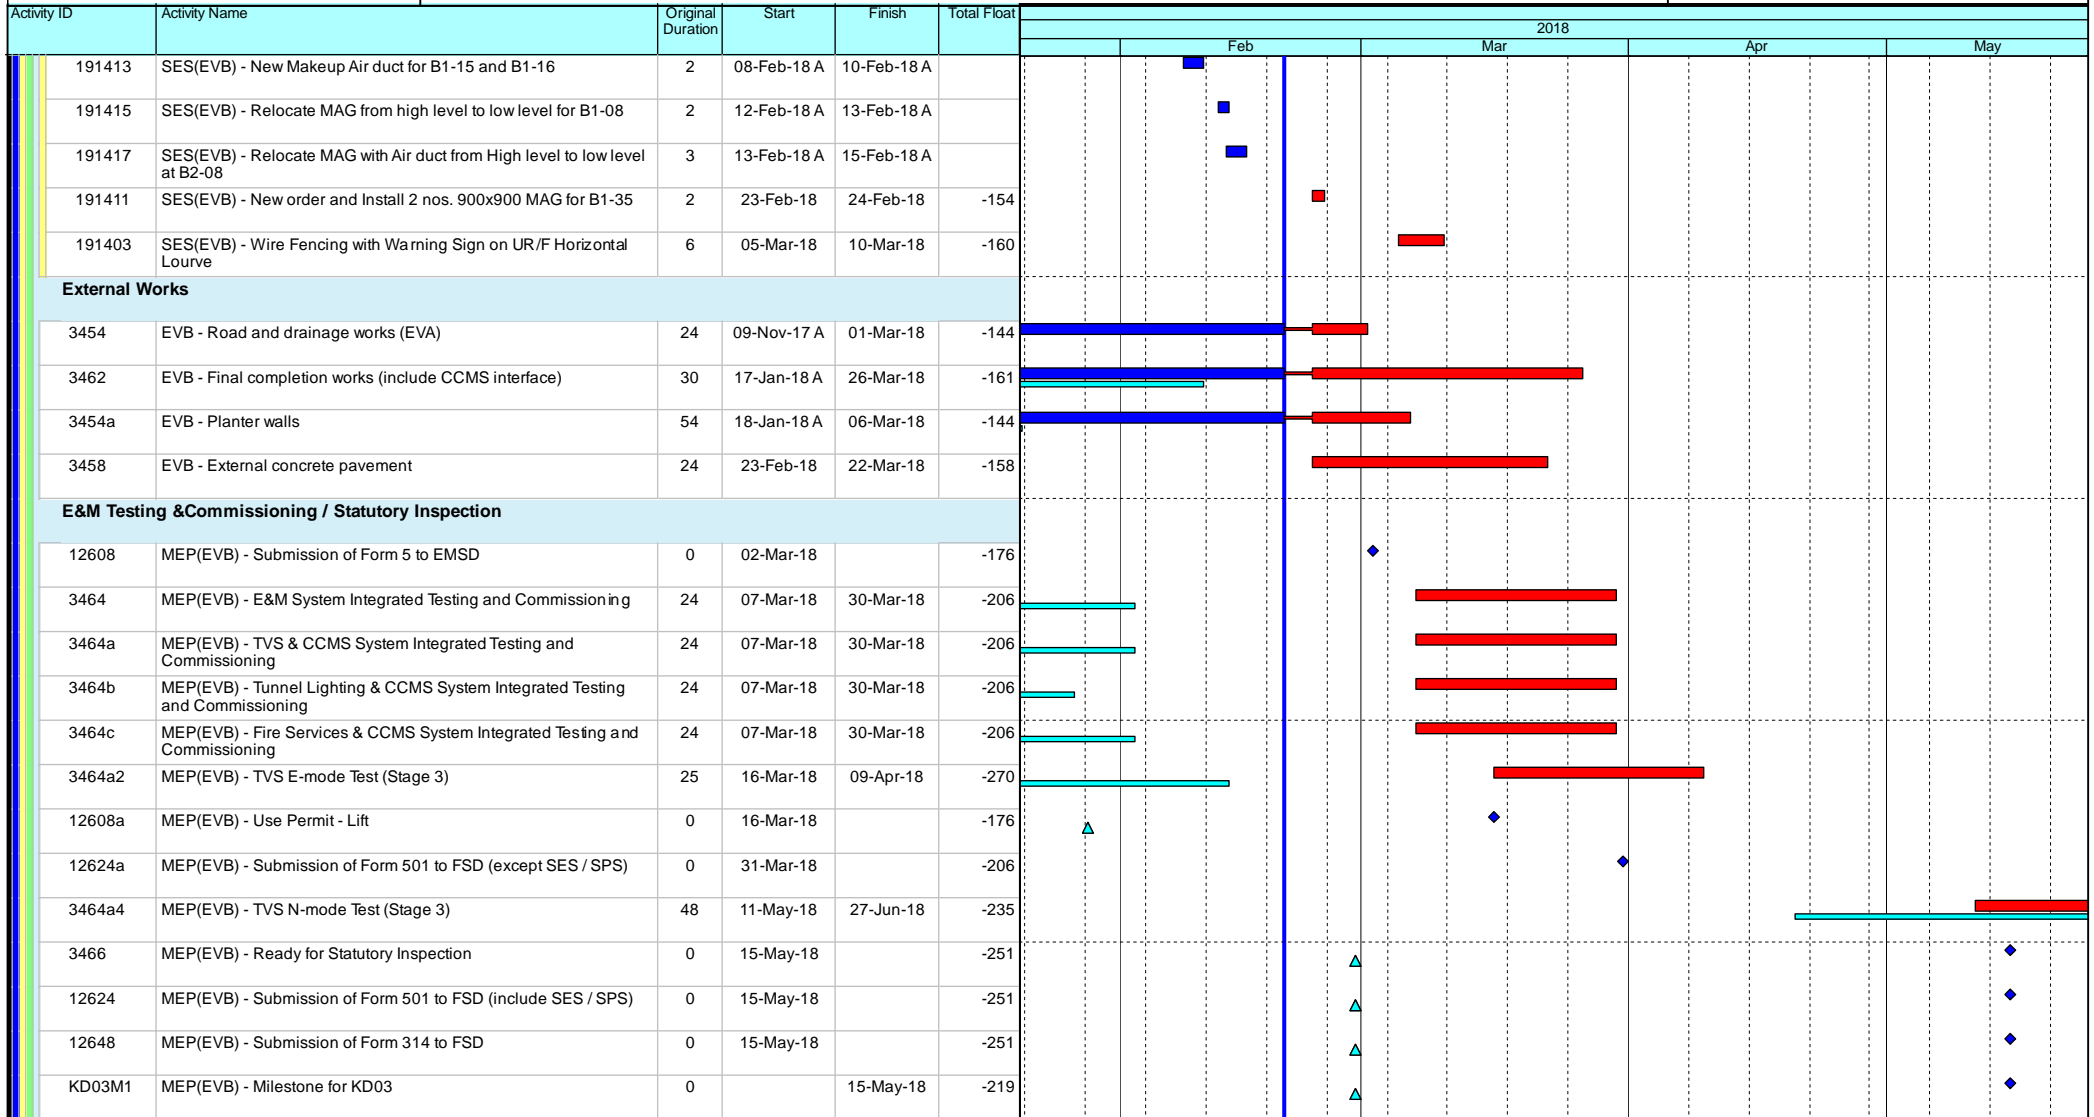

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 31 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

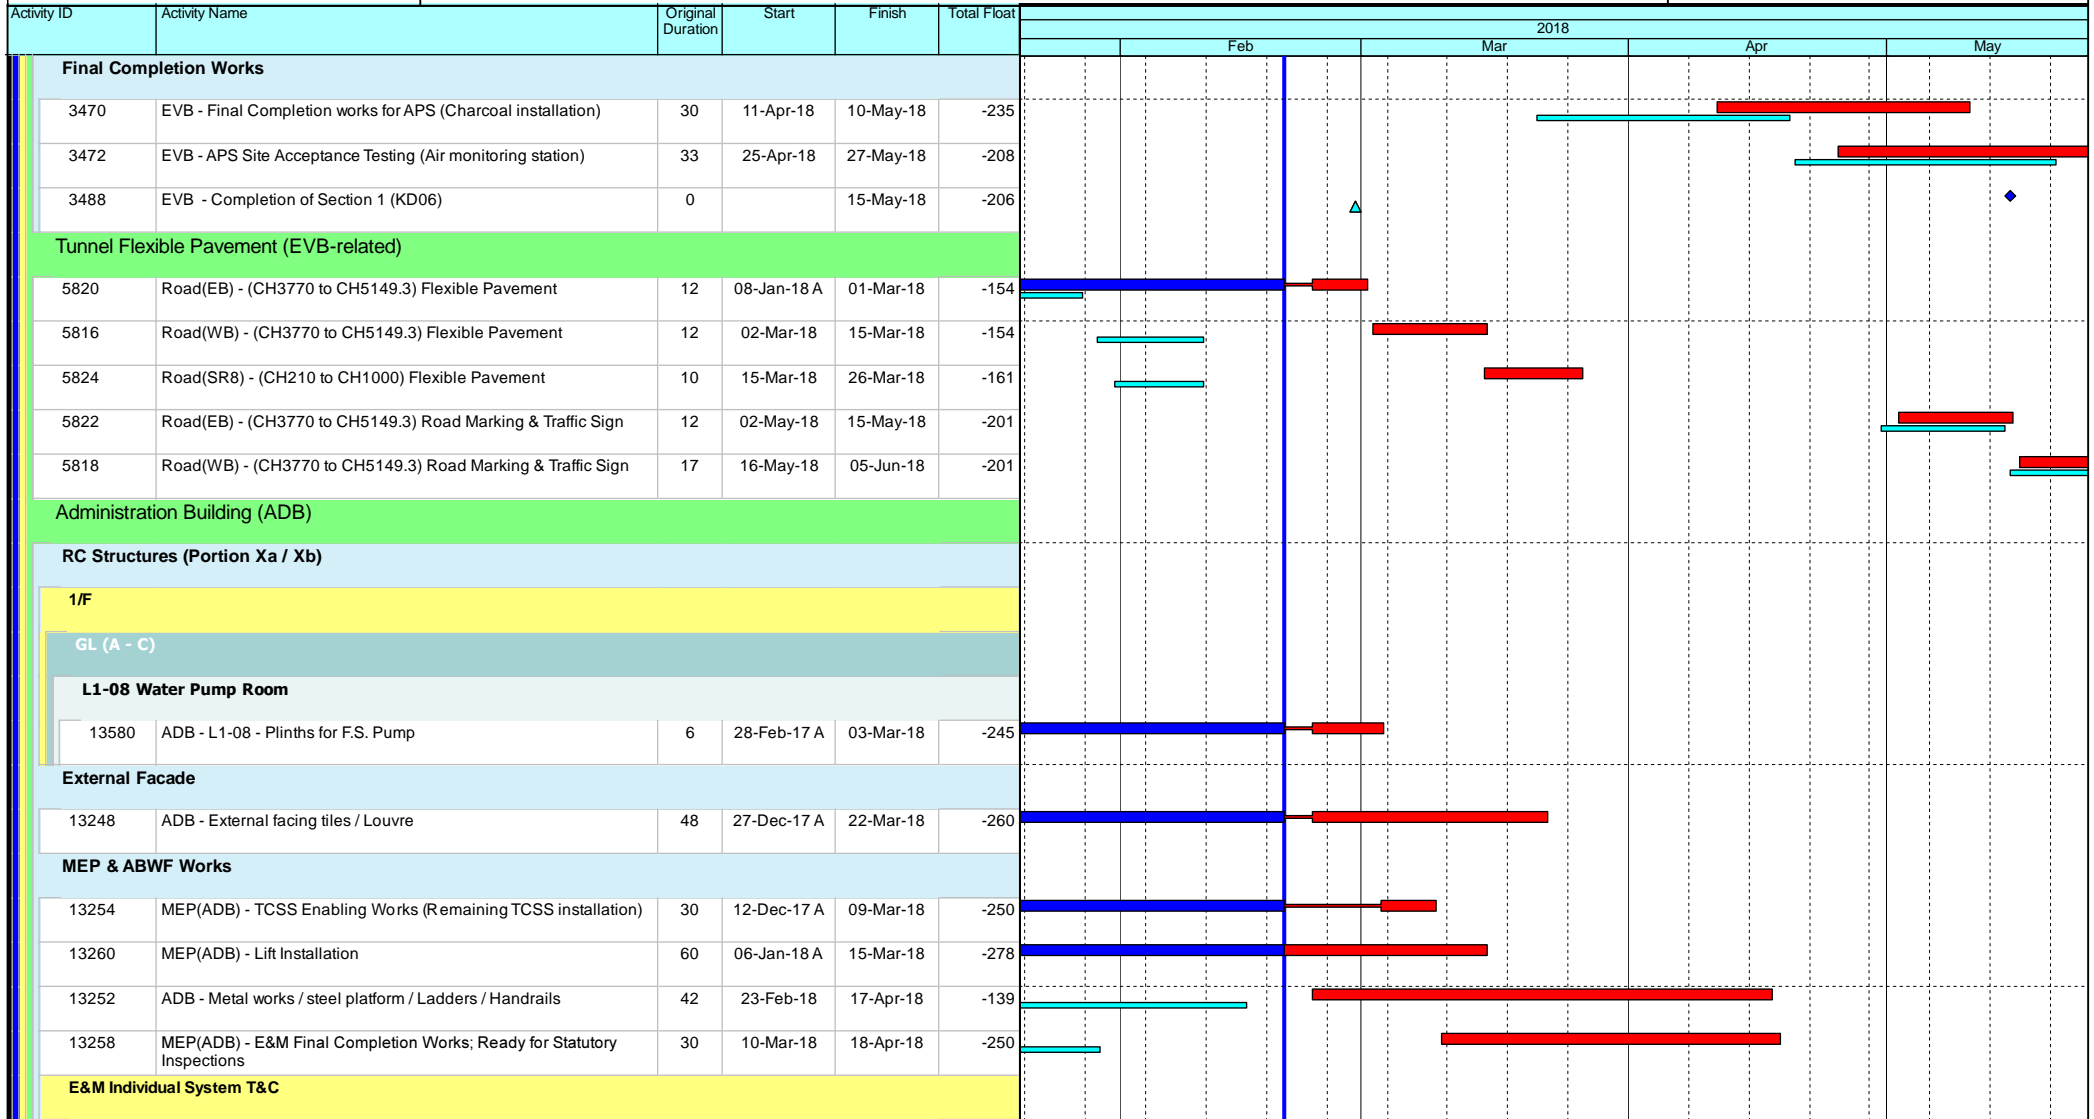

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 32 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

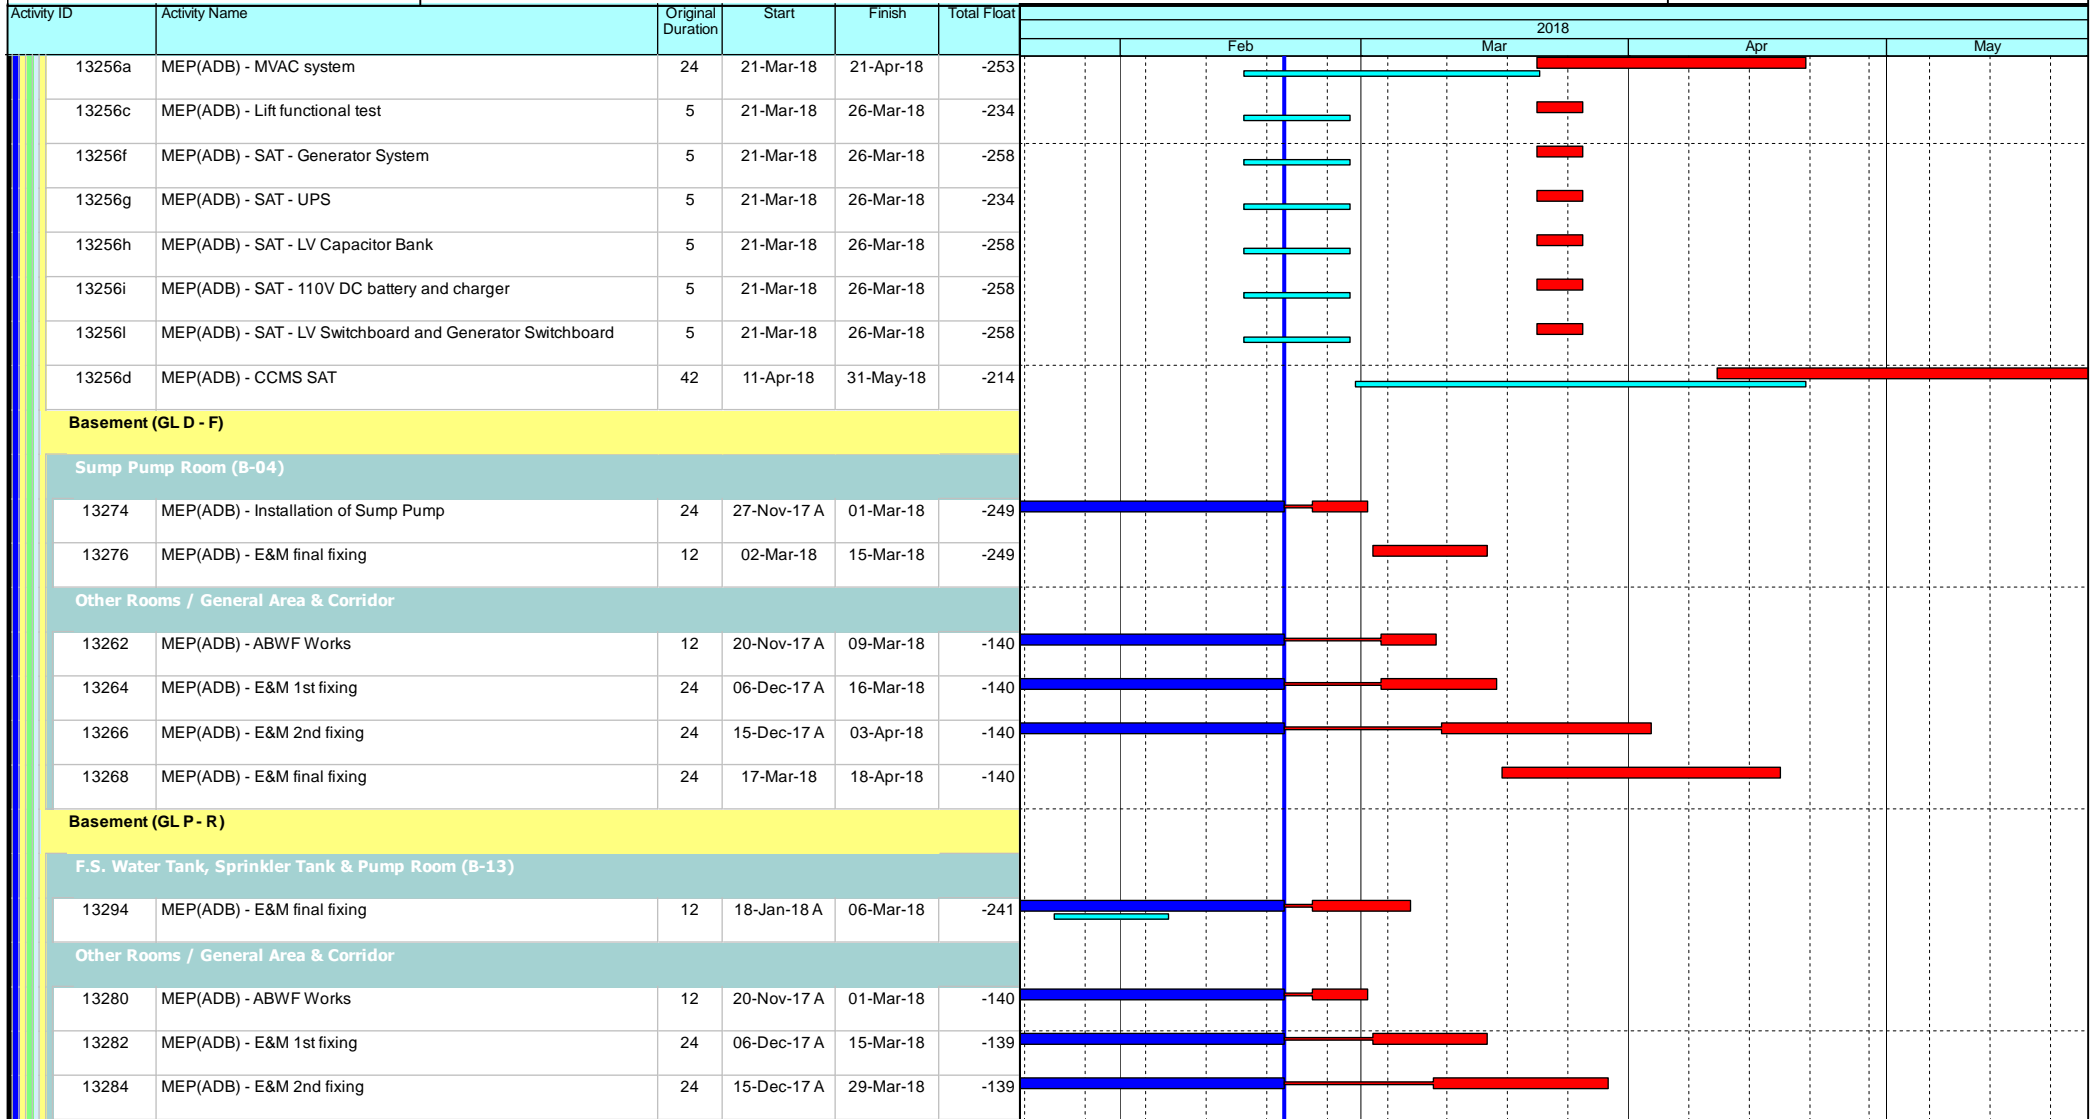

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 33 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

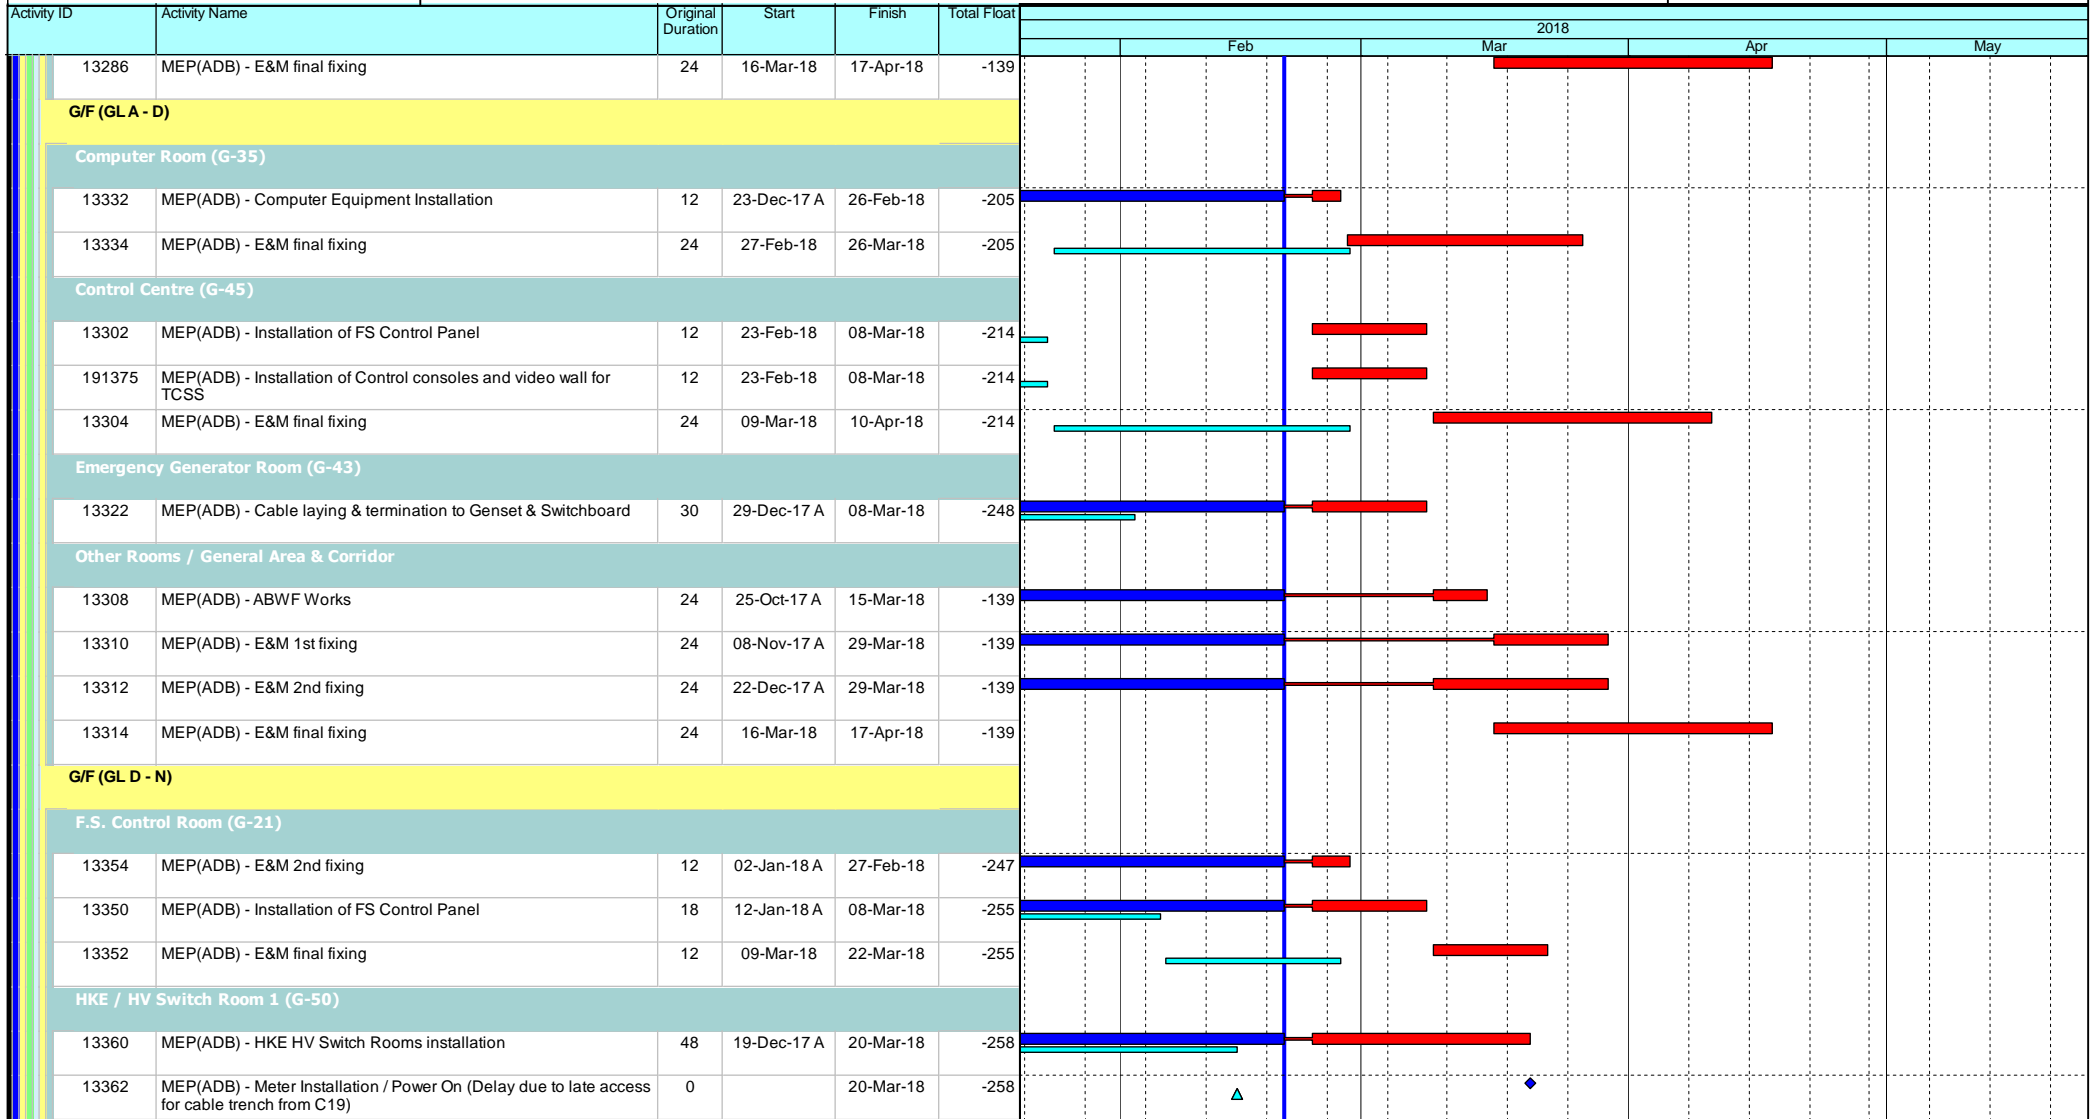

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 34 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018					
						Feb	Mar	Apr	May		
Un-interrupted Power Supply (UPS) Room (G-13)											
13400	MEP(ADB) - Cable laying & termination	28	08-Jan-18 A	08-Mar-18	-224						
Other Rooms / General Area & Corridor											
13338	MEP(ADB) - ABWF Works	24	25-Oct-17 A	01-Mar-18	-157						
13340	MEP(ADB) - E&M 1st fixing	24	13-Dec-17 A	08-Mar-18	-145						
13342	MEP(ADB) - E&M 2nd fixing	24	29-Dec-17 A	15-Mar-18	-151						
13344	MEP(ADB) - E&M final fixing	24	02-Mar-18	29-Mar-18	-151						
G/F (GL P - R)											
Other Rooms / General Area & Corridor											
13406	MEP(ADB) - ABWF Works	12	06-Jan-18 A	08-Mar-18	-157						
13408	MEP(ADB) - E&M 1st fixing	24	10-Jan-18 A	08-Mar-18	-157						
13410	MEP(ADB) - E&M 2nd fixing	24	23-Feb-18	22-Mar-18	-157						
13412	MEP(ADB) - E&M final fixing	24	09-Mar-18	10-Apr-18	-157						
1/F (GL A - D)											
Water Pump Room (L1-08)											
13424	MEP(ADB) - E&M 1st fixing	12	14-Nov-17 A	10-Mar-18	-245						
13430	MEP(ADB) - E&M 2nd fixing	12	18-Dec-17 A	10-Mar-18	-245						
13426	MEP(ADB) - Installation of water Pump	24	28-Dec-17 A	10-Mar-18	-245						
13428	MEP(ADB) - E&M final fixing	24	10-Jan-18 A	15-Mar-18	-249						
Other Rooms / General Area & Corridor											
13414	MEP(ADB) - ABWF Works	24	01-Dec-17 A	01-Mar-18	-243						
13416	MEP(ADB) - E&M 1st fixing	24	14-Dec-17 A	15-Mar-18	-139						
13418	MEP(ADB) - E&M 2nd fixing	24	28-Dec-17 A	29-Mar-18	-139						
13420	MEP(ADB) - E&M final fixing	24	16-Mar-18	17-Apr-18	-139						

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
Baseline: SA01
Layout: Update Three Month Rolling
U048
Page 35 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

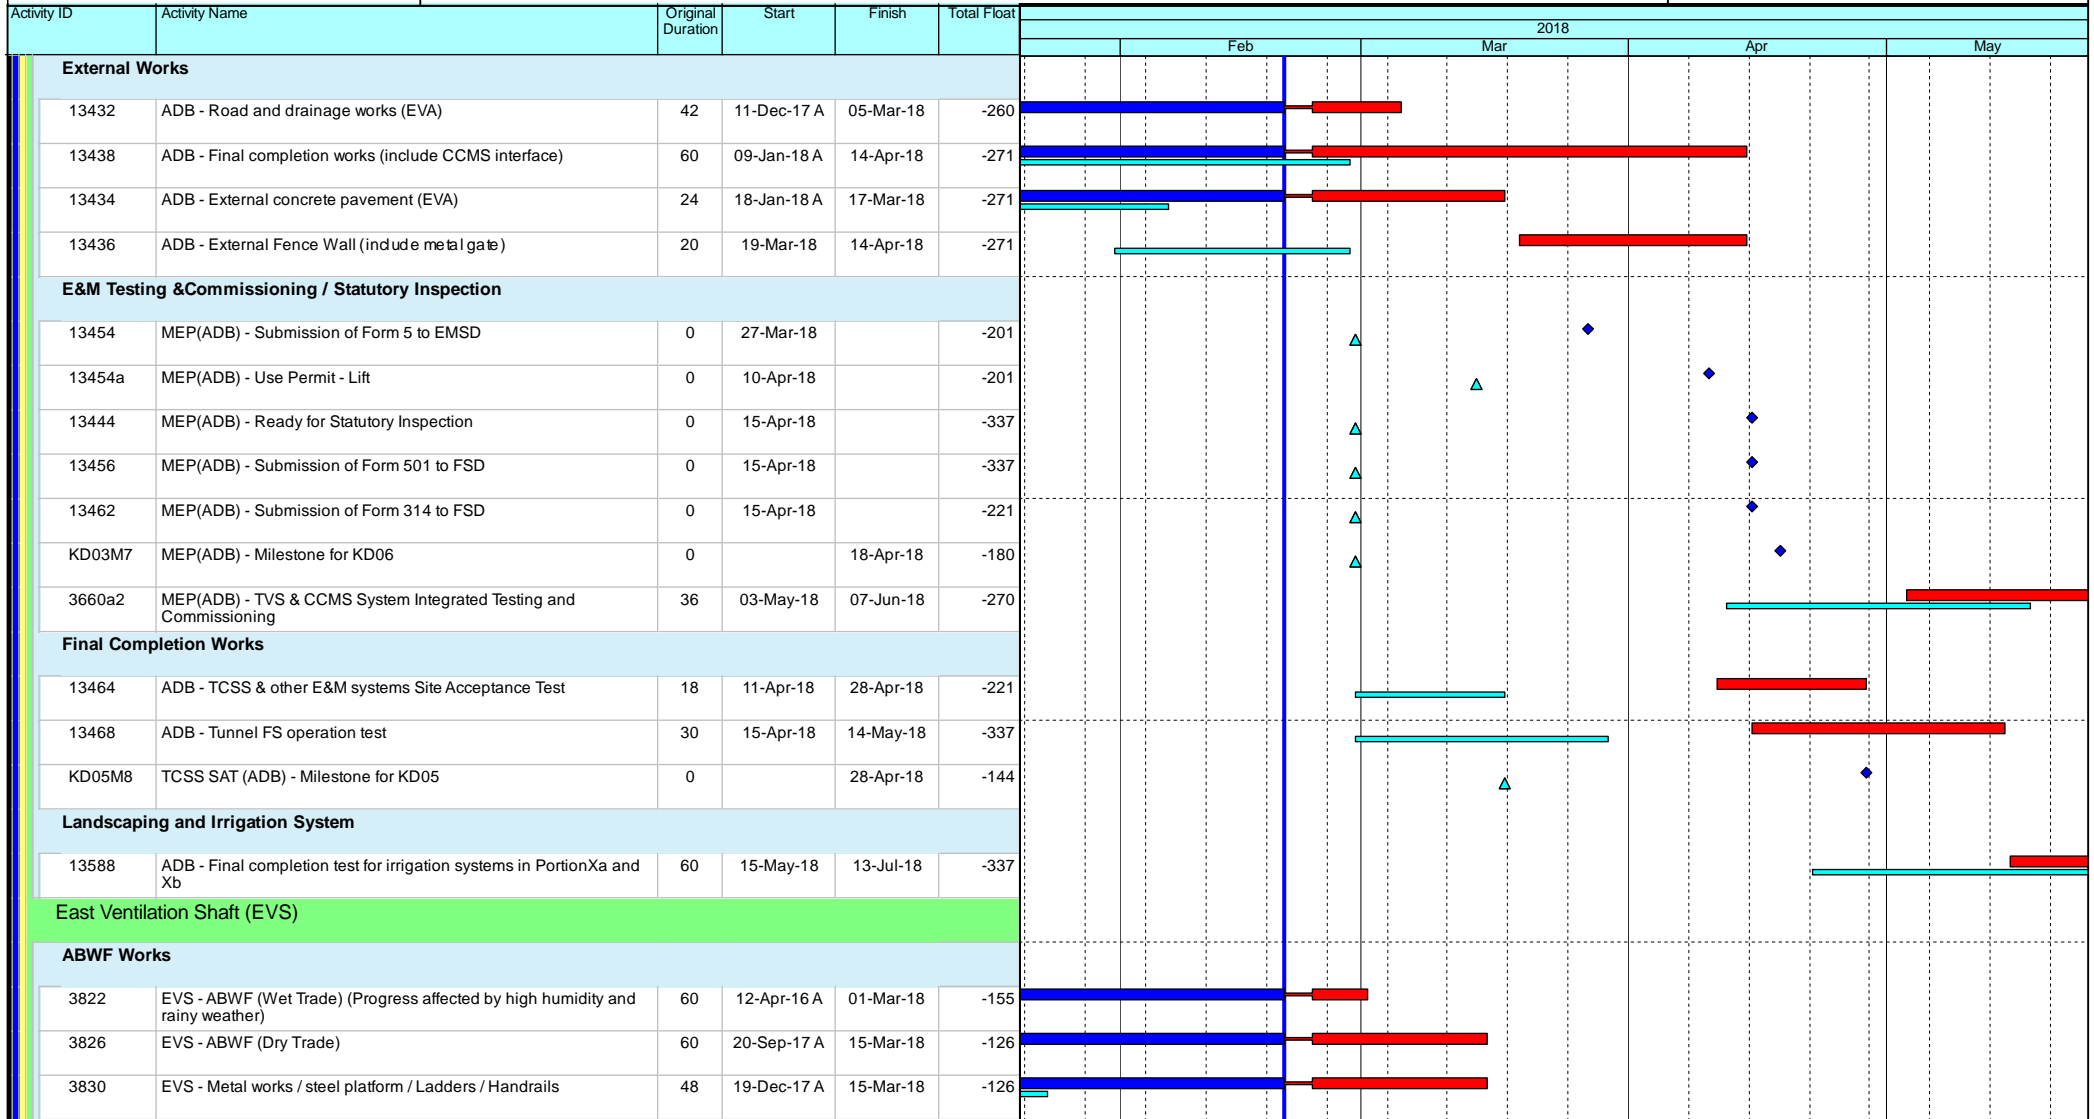

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
Baseline: SA01
Layout: Update Three Month Rolling
U048
Page 36 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

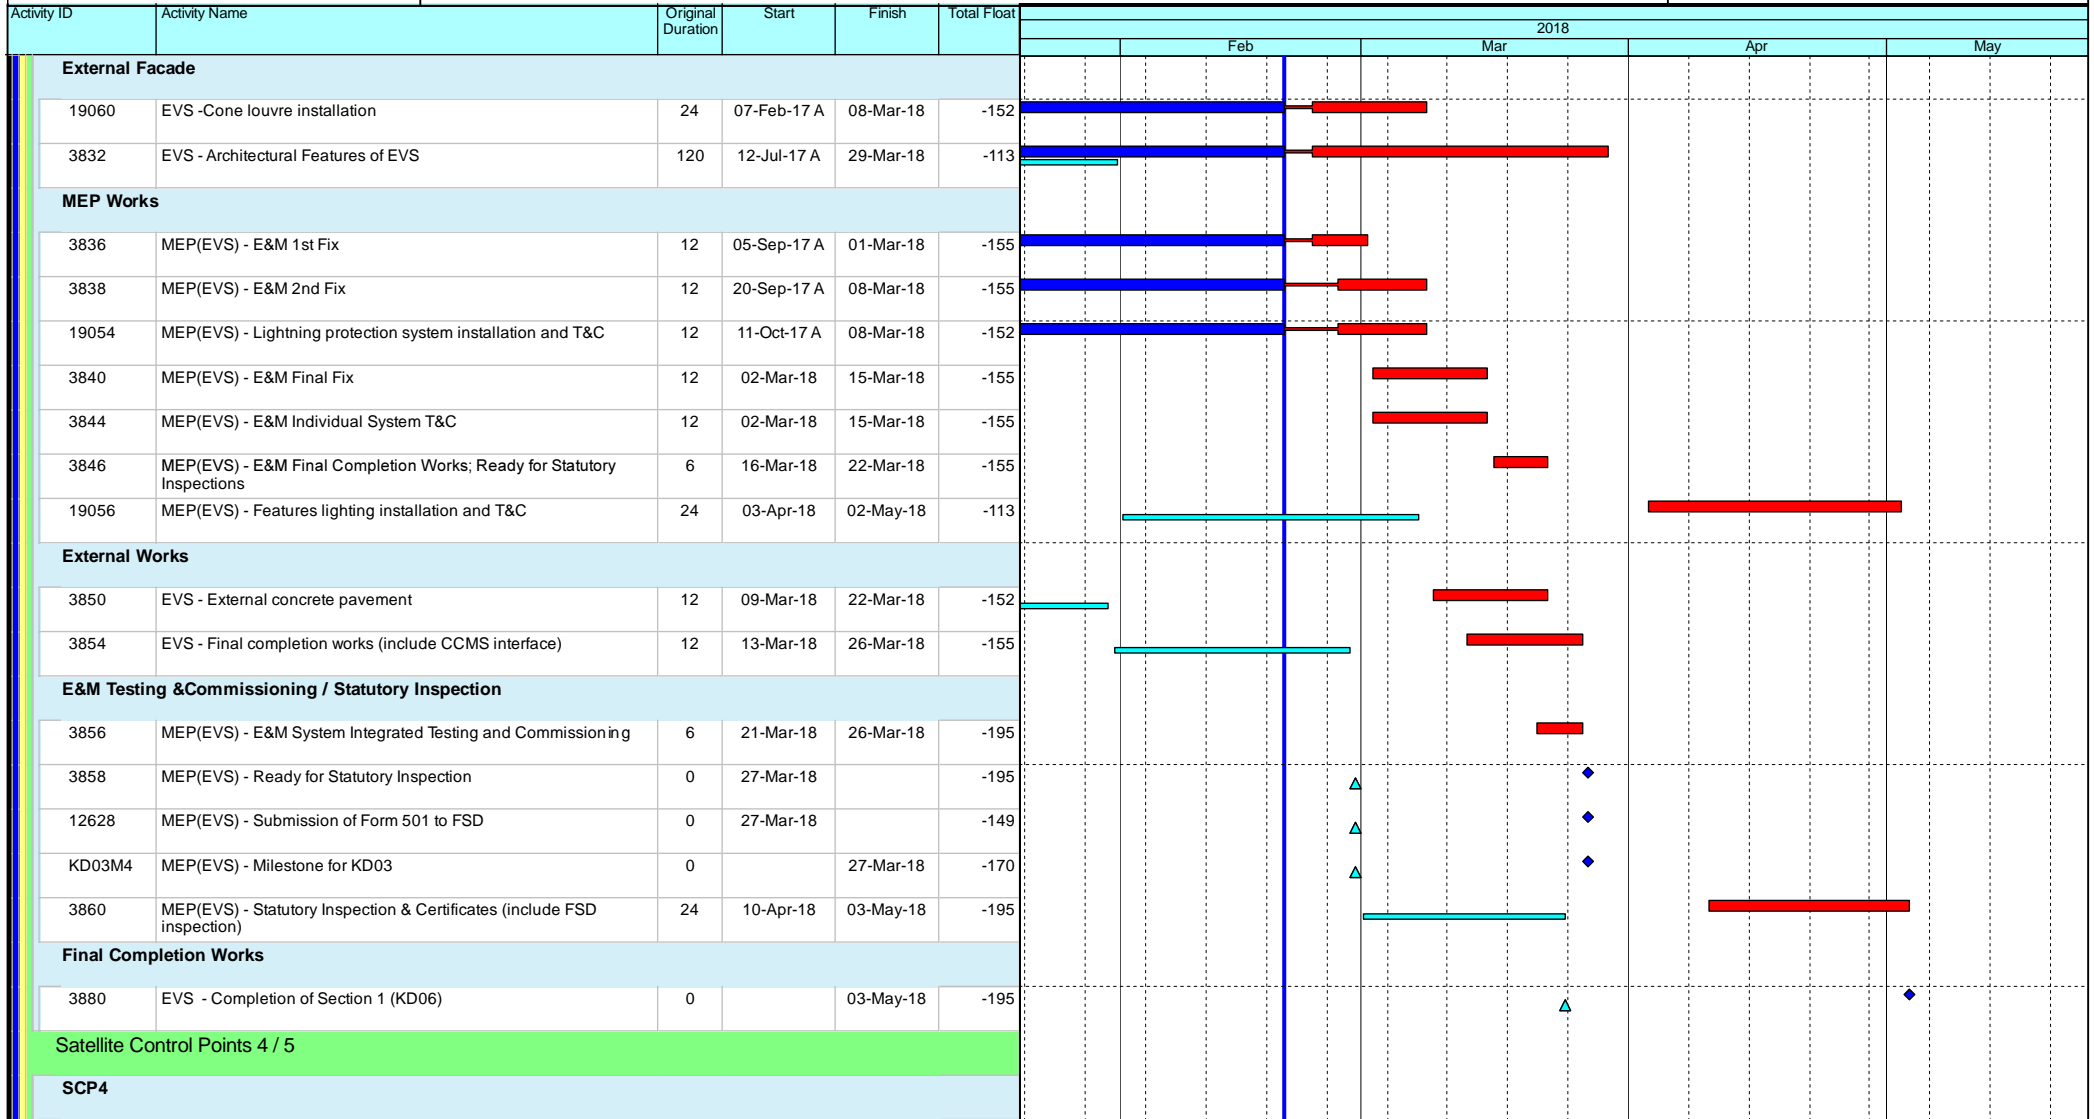

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 37 of 43








Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Feb	Mar	Apr	May
3778	SCP4 - Initial Site Survey	6	23-Feb-18	01-Mar-18	-196				
3778a	SCP4 - Construction details from AECOM	0	23-Feb-18*		-196				
3780	SCP4 - Erect Hoarding	6	02-Mar-18	08-Mar-18	-196				
3782	SCP4 - Mobilisation and setup	12	09-Mar-18	22-Mar-18	-196				
3784	SCP4 - Construct SCP RC Structures	24	23-Mar-18	24-Apr-18	-196				
3786	SCP4 - ABWF Works	24	25-Apr-18	24-May-18	-196				
3798	SCP4 - External Works	24	25-Apr-18	24-May-18	-143				
3788	MEP(SCP4) - E&M 1st Fix	18	27-Apr-18	18-May-18	-196				
10112	MEP(SCP4) - TCSS Enabling Works (Remaining TCSS installation)	18	27-Apr-18	18-May-18	-196				
3790	MEP(SCP4) - E&M 2nd Fix	18	08-May-18	29-May-18	-155				
3824	SCP4 - Metal works / Glazing / Louver / Handrails	18	10-May-18	31-May-18	-149				
3792	MEP(SCP4) - E&M Final Fix	18	17-May-18	07-Jun-18	-155				
SCP5									
3828	SCP5 - Mobilization for Area B	0	23-Feb-18		-207				
3848	SCP5 - Initial Site Survey	6	23-Feb-18	01-Mar-18	-207				
3827	C19 allow access for SCP5 construction	0	23-Feb-18*		-207				
3827a	Construction details from AECOM	0	23-Feb-18*		168				
3852	SCP5 - Erect Hoarding	4	02-Mar-18	06-Mar-18	-207				
3868	SCP5 - Mobilisation and setup	2	07-Mar-18	08-Mar-18	-207				
3870a	SCP5 - Construct walls upto R/F - Falseworks & Formwork	4	09-Mar-18	13-Mar-18	-207				
3870b	SCP5 - Construct walls upto R/F - Rebar fixing	3	14-Mar-18	16-Mar-18	-207				
3870c	SCP5 - Construct walls upto R/F - Close formwork	4	17-Mar-18	21-Mar-18	-207				
3870d	SCP5 - Construct beams & slab upto R/F - Scaffolding, falsework & formwork	4	22-Mar-18	26-Mar-18	-207				
3870e	SCP5 - Construct beams & slab upto R/F - Rebar fixing	3	27-Mar-18	29-Mar-18	-207				

-  Current Milestone
-  Level of Effort
-  Baseline Milestone
-  Actual Work
-  Critical Remaining Work
-  Remaining Work
-  Project Baseline

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 38 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

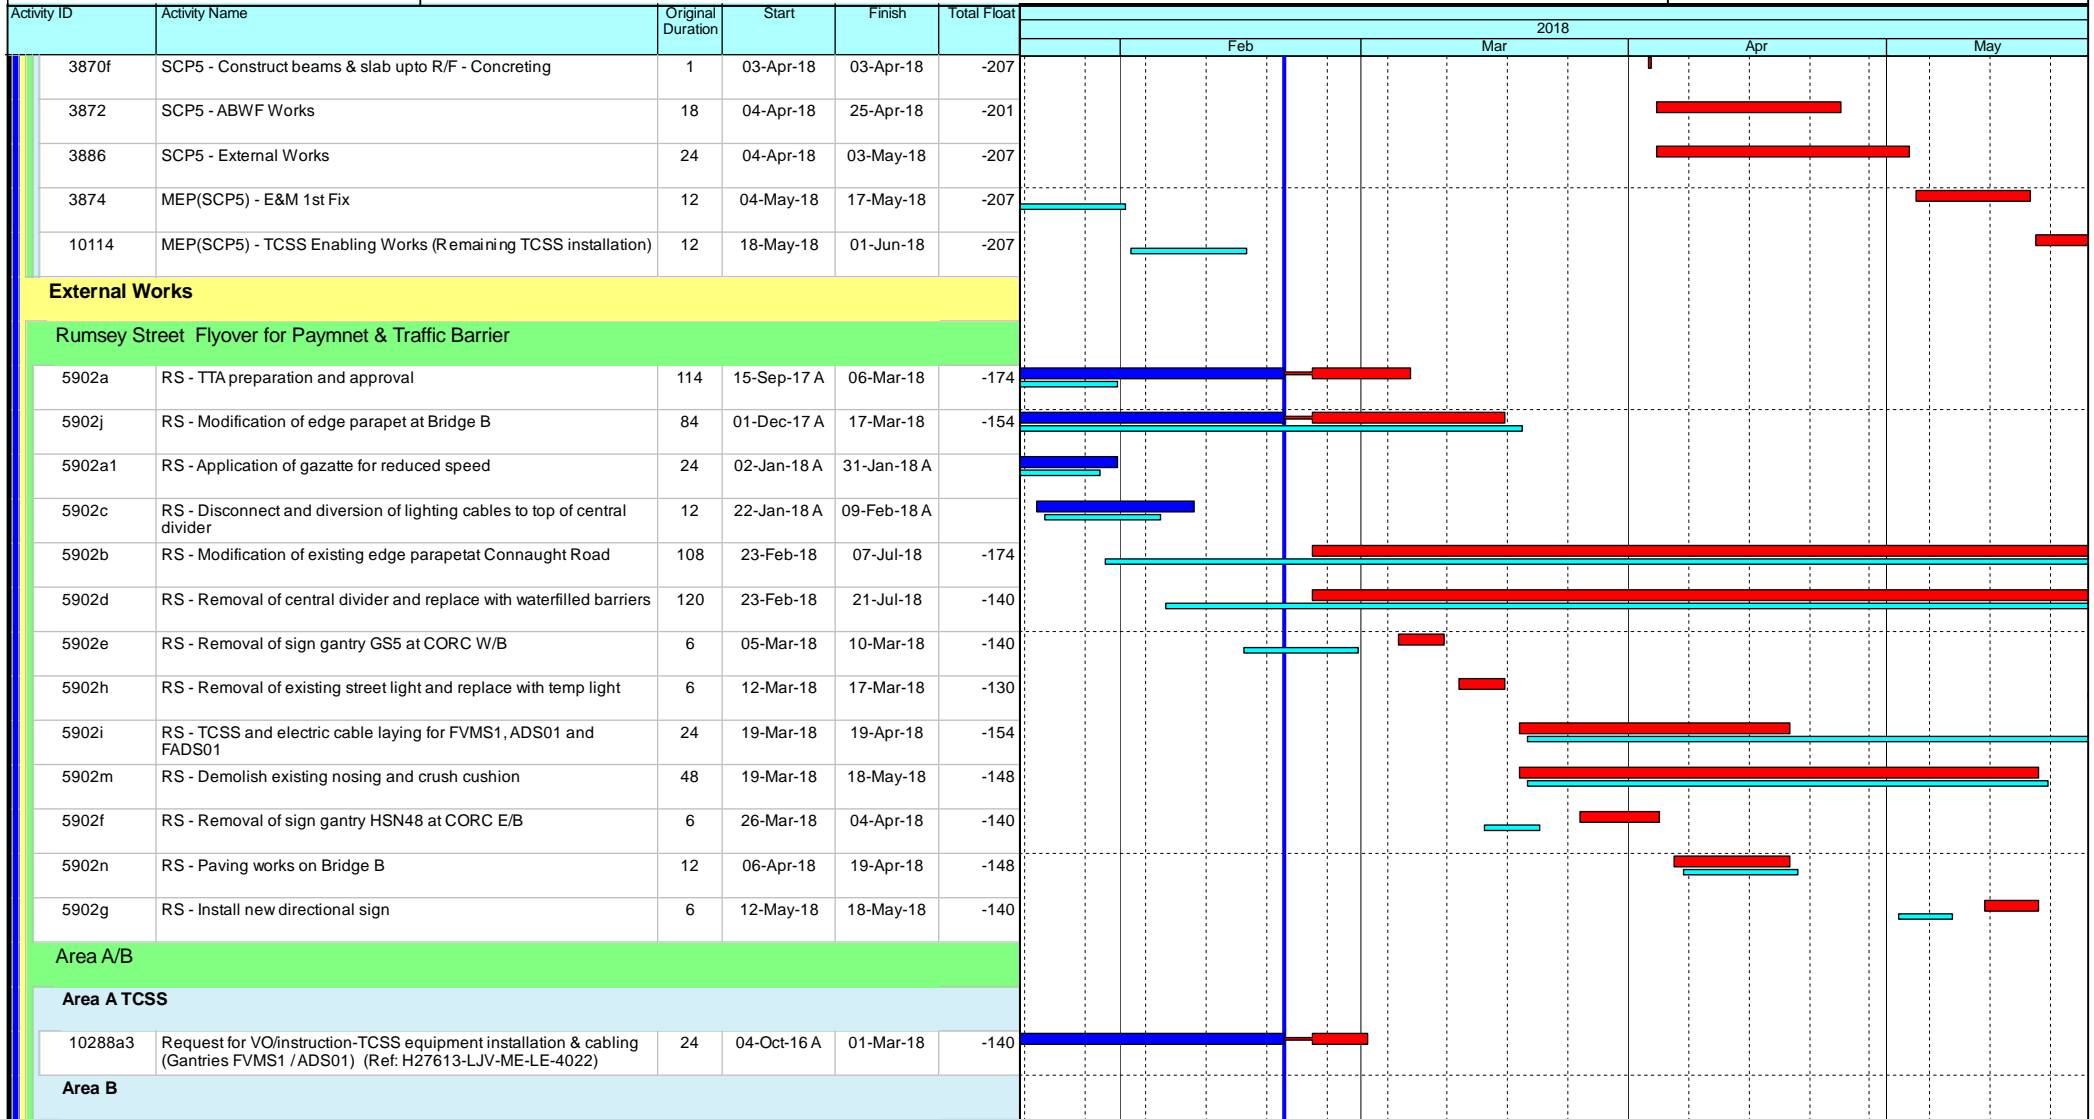

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 39 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

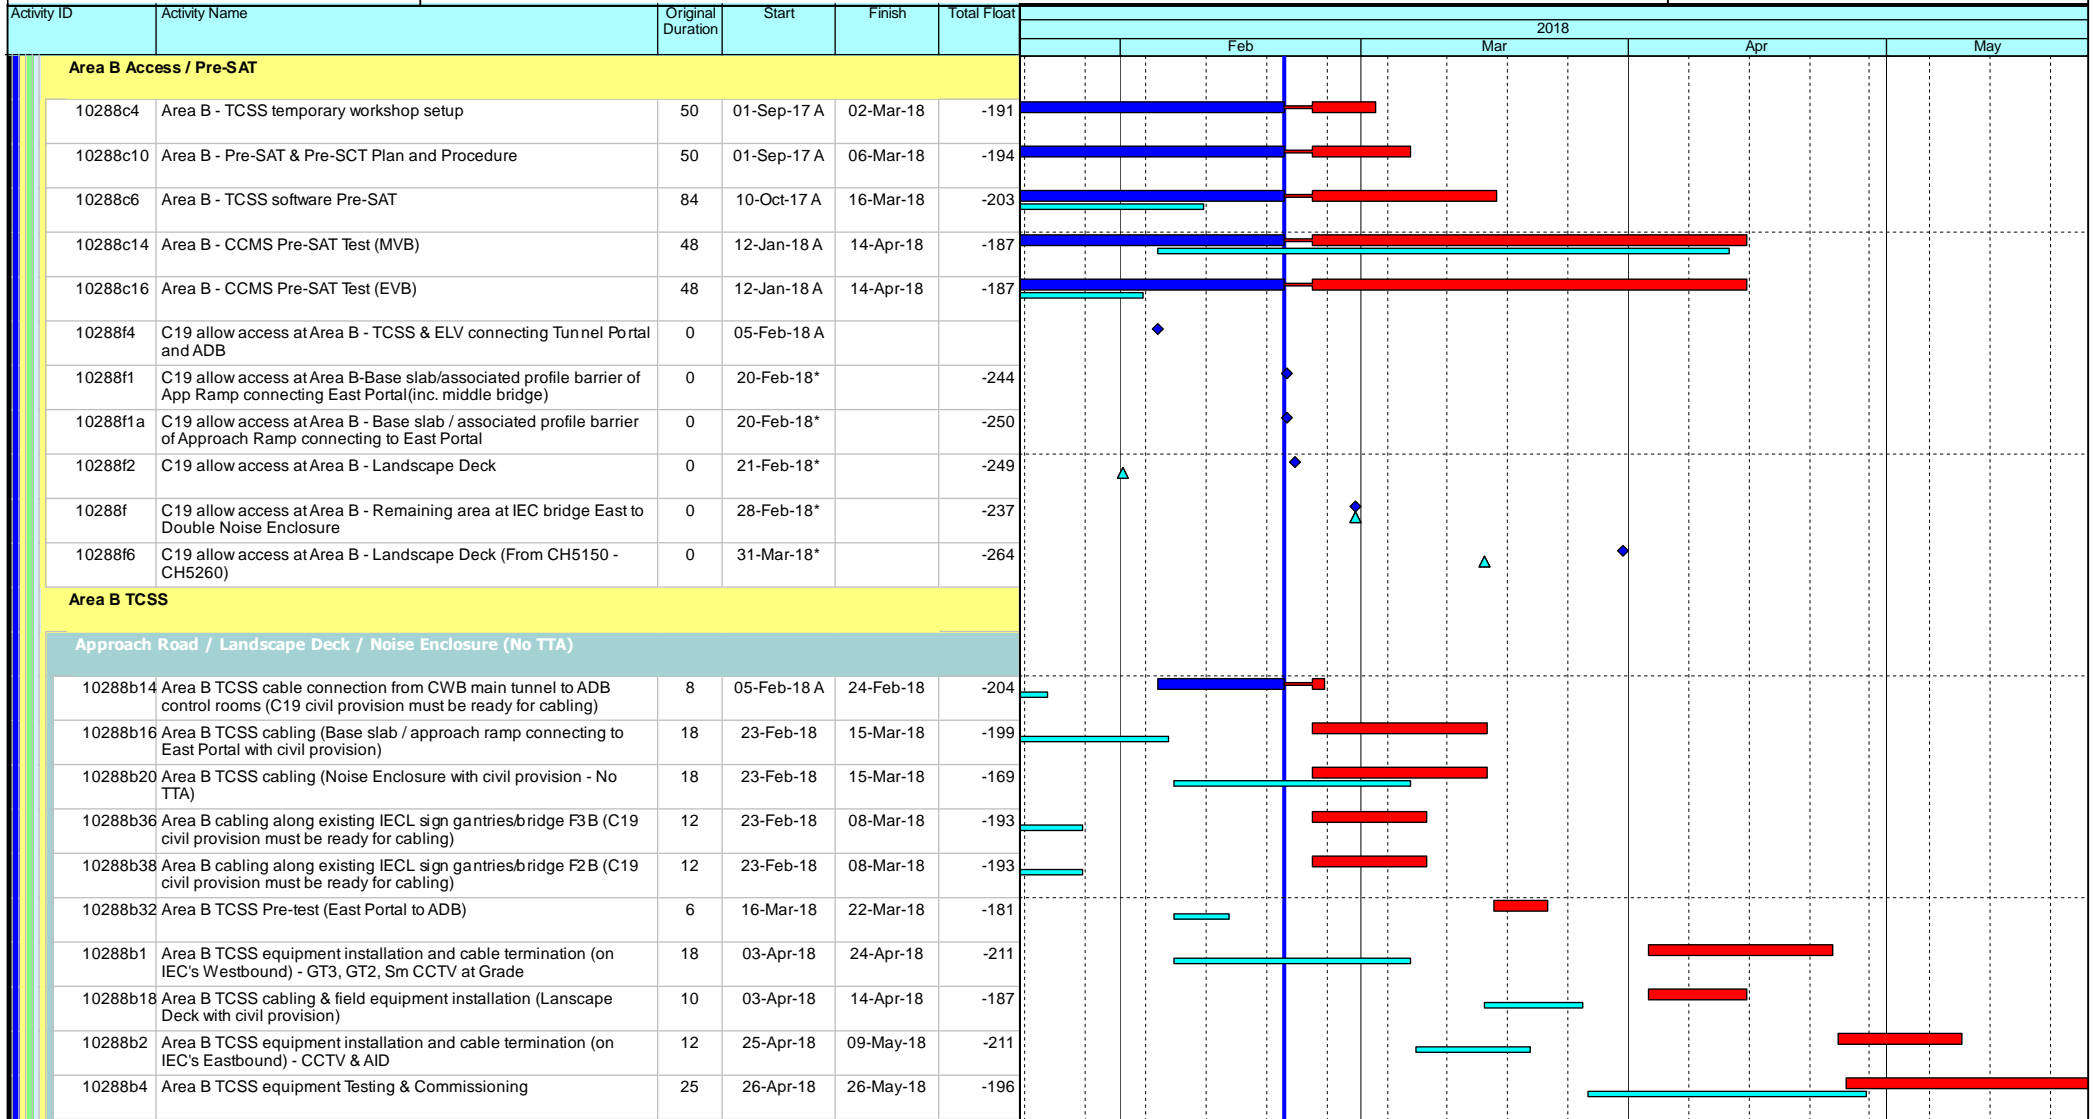

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 40 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

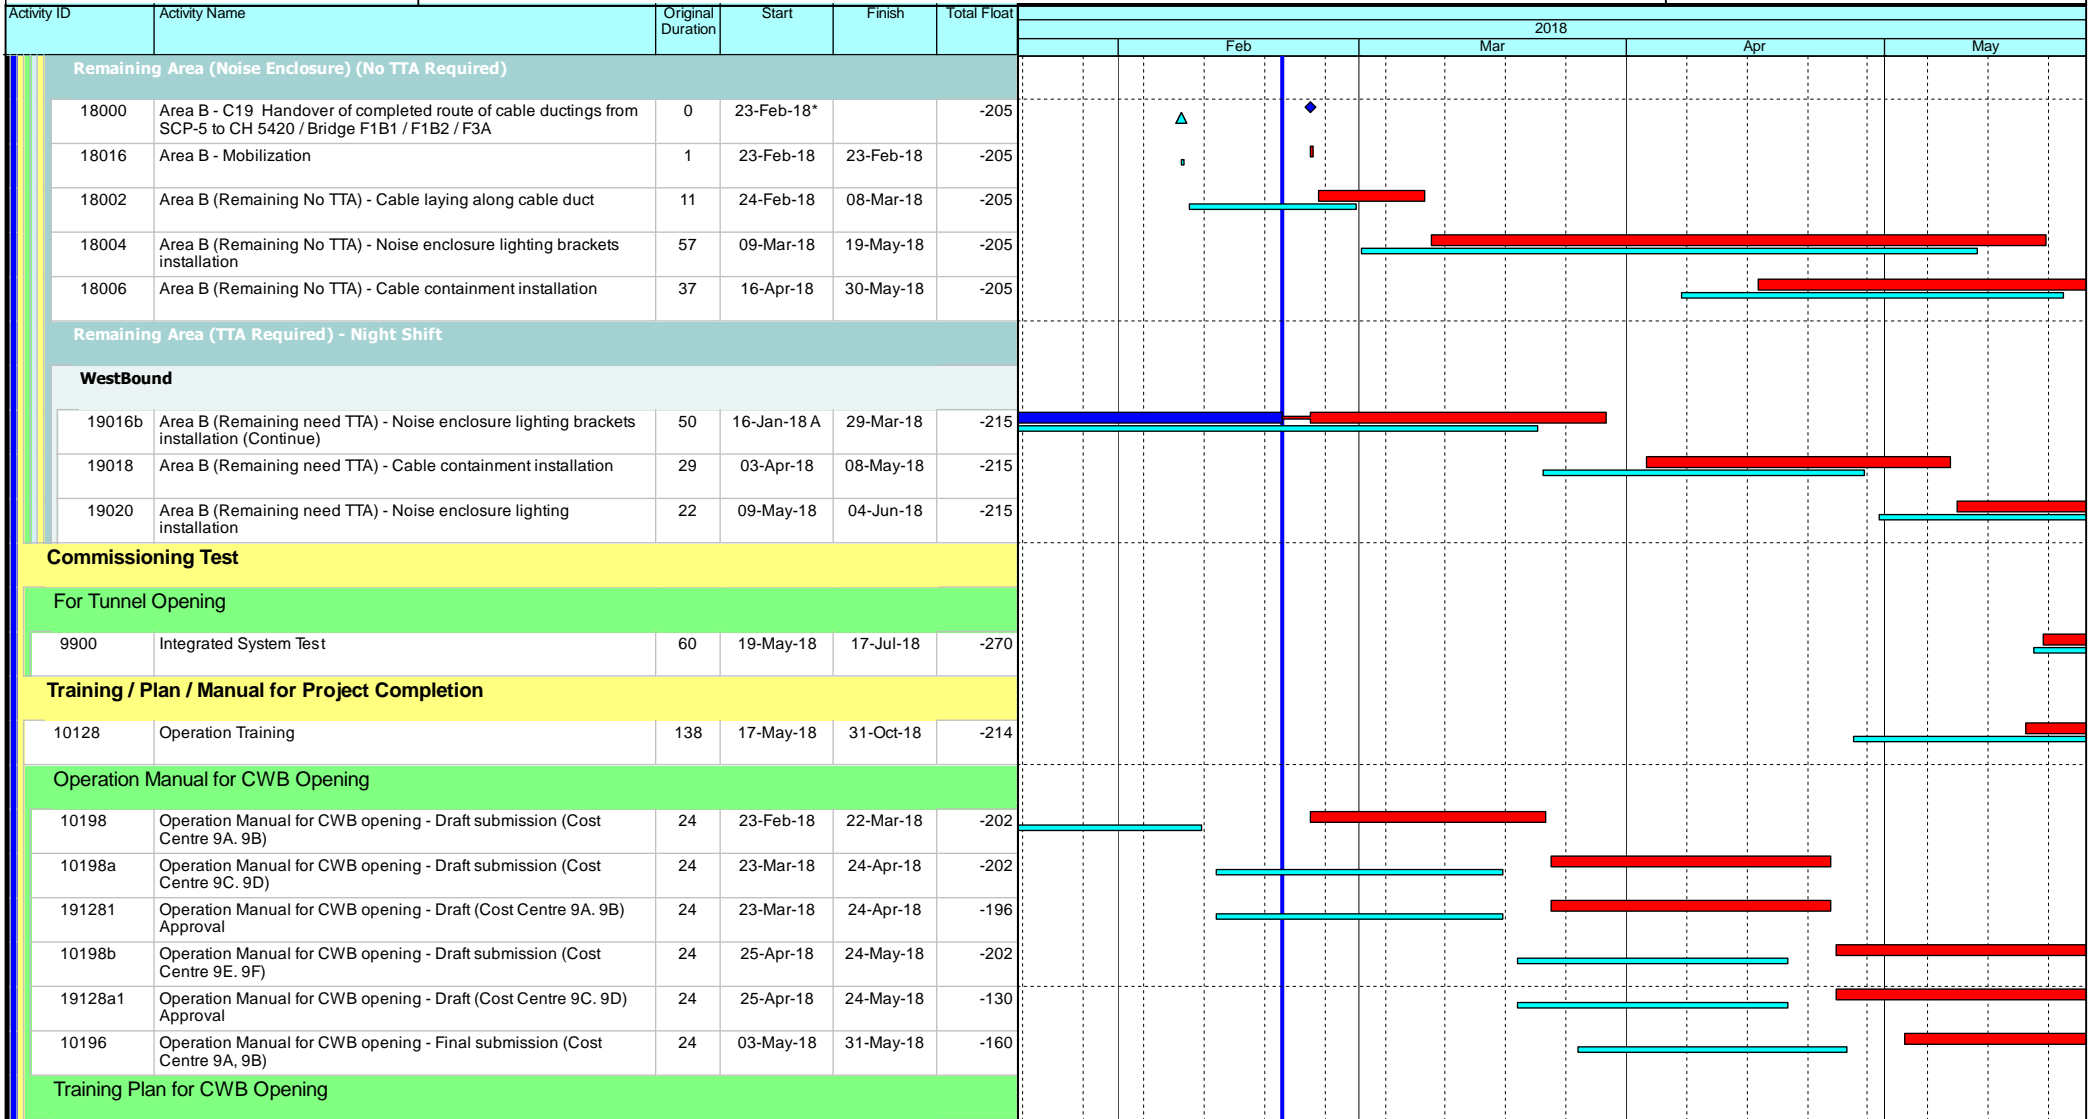

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING


Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 42 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

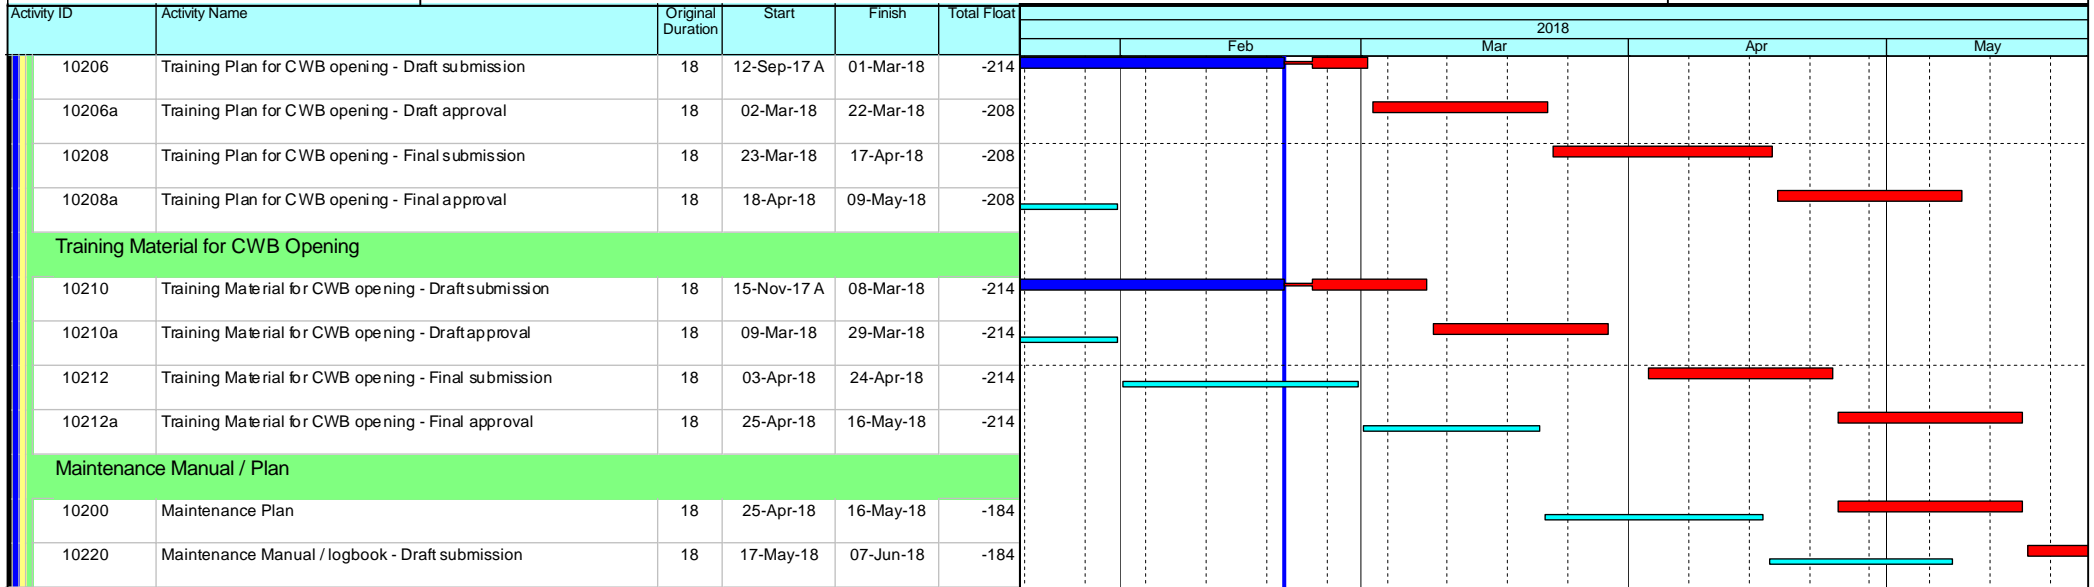

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 43 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW
