




CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019					
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
Promenade Seawall Parapet Construction & EVA																							
SVII12000	Sec VII - Precast parapet	67	18-Nov-17 A	14-May-18	0%																		
SVII12010	Sec VII - Zone CRIII - seawall parapet: Backfilling	14	20-Feb-18	07-Mar-18	0%																		
SVII12120	Sec VII - Zone CRIII - seawall parapet: Construct mass concrete coping	30	08-Mar-18	16-Apr-18	0%																		
SVII12122	Sec VII - Zone CRIII - seawall parapet: reinforced concret coping	17	17-Apr-18	07-May-18	0%																		
SVII12140	Sec VII - Zone CRIII - seawall parapet: construct seawall parapet	30	08-May-18	12-Jun-18	0%																		
SVII12160	Sec VII - CRIII - EVA: watermain	14	13-Jun-18	29-Jun-18	0%																		
SVII12180	Sec VII - CRIII - EVA: U-channel	14	30-Jun-18	17-Jul-18	0%																		
SVII12200	Sec VII - CRIII - EVA: bituminous layer	5	18-Jul-18	23-Jul-18	0%																		
SVII12220	Sec VII - CRIII - EVA: paving block	30	24-Jul-18	27-Aug-18	0%																		
SVII13120	Sec VII - Zone A1, A2 & B - seawall parapet: Construct mass concrete coping	14	28-Dec-17 A	07-Mar-18	68.18%																		
SVII13122	Sec VII - Zone A1, A2 & B - seawall parapet: reinforced concrete coping	18	08-Mar-18	28-Mar-18	0%																		
SVII13140	Sec VII - Zone A1, A2 & B - seawall parapet: Construct seawall parapet	30	09-Apr-18	14-May-18	0%																		
SVII13160	Sec VII - Zone A1, A2 & B - EVA: watermain	14	15-May-18	31-May-18	0%																		
SVII13180	Sec VII - Zone A1, A2 & B - EVA: U-channel	14	01-Jun-18	16-Jun-18	0%																		
SVII13182	Sec VII - Zone A1, A2 & B - EVA: bituminous layer	5	19-Jun-18	23-Jun-18	0%																		
SVII13184	Sec VII - Zone A1, A2 & B - EVA: paving block	30	25-Jun-18	30-Jul-18	0%																		
SVII13200	Sec VII - Zone D - seawall parapet: Remove temporary seawall block	21	07-Mar-18	03-Apr-18	0%																		
SVII13220	Sec VII - Zone D - seawall parapet: Construct mass concrete	30	04-Apr-18	10-May-18	0%																		
SVII13222	Sec VII - Zone D - seawall parapet: reinforced concrete coping	18	11-May-18	01-Jun-18	0%																		
SVII13240	Sec VII - Zone D - seawall parapet: Construct seawall parapet	25	02-Jun-18	03-Jul-18	0%																		
SVII13260	Sec VII - Zone D - EVA : watermain	14	04-Jul-18	19-Jul-18	0%																		
SVII13280	Sec VII - Zone D - EVA : U-channel	14	20-Jul-18	04-Aug-18	0%																		
SVII13300	Sec VII - Zone D - EVA : bituminous layer	5	06-Aug-18	10-Aug-18	0%																		
SVII13320	Sec VII - Zone D - EVA : paving block	30	11-Aug-18	14-Sep-18	0%																		
Promenade Footpath																							
Section 1																							
SVII10440	Sec VII - section 1 footpath - drainage works : connection pipe & U -channel	10	24-May-18	04-Jun-18	0%																		
SVII10445	Sec VII - section 1 footpath - watermain	7	05-Jun-18	12-Jun-18	0%																		
SVII10460	Sec VII - section 1 footpath - lighting	7	13-Jun-18	21-Jun-18	0%																		
SVII10500	Sec VII - section 1 footpath - paving block	21	22-Jun-18	17-Jul-18	0%																		
Section 2																							
SVII12610	Sec VII - section 2 footpath - drainage works : L2202 - L2203A	20	20-Feb-18	14-Mar-18	0%																		
SVII12615	Sec VII - section 2 footpath - watermain	7	15-Mar-18	22-Mar-18	0%																		
SVII12630	Sec VII - section 2 footpath - utilities: TCSS	21	23-Mar-18	20-Apr-18	0%																		
SVII12670	Sec VII - section 2 footpath - paving block	30	21-Apr-18	28-May-18	0%																		
Section 3																							
SVII12850	Sec VII - section 3 footpath - watermain	17	20-Feb-18	10-Mar-18	0%																		
SVII12870	Sec VII - section 3 footpath - utilities (HEC, TCSS, HGC, PCCW)	40	12-Mar-18	02-May-18	0%																		
SVII12875	Sec VII - 3 footpath - drainage works :U chanel	14	03-May-18	18-May-18	0%																		

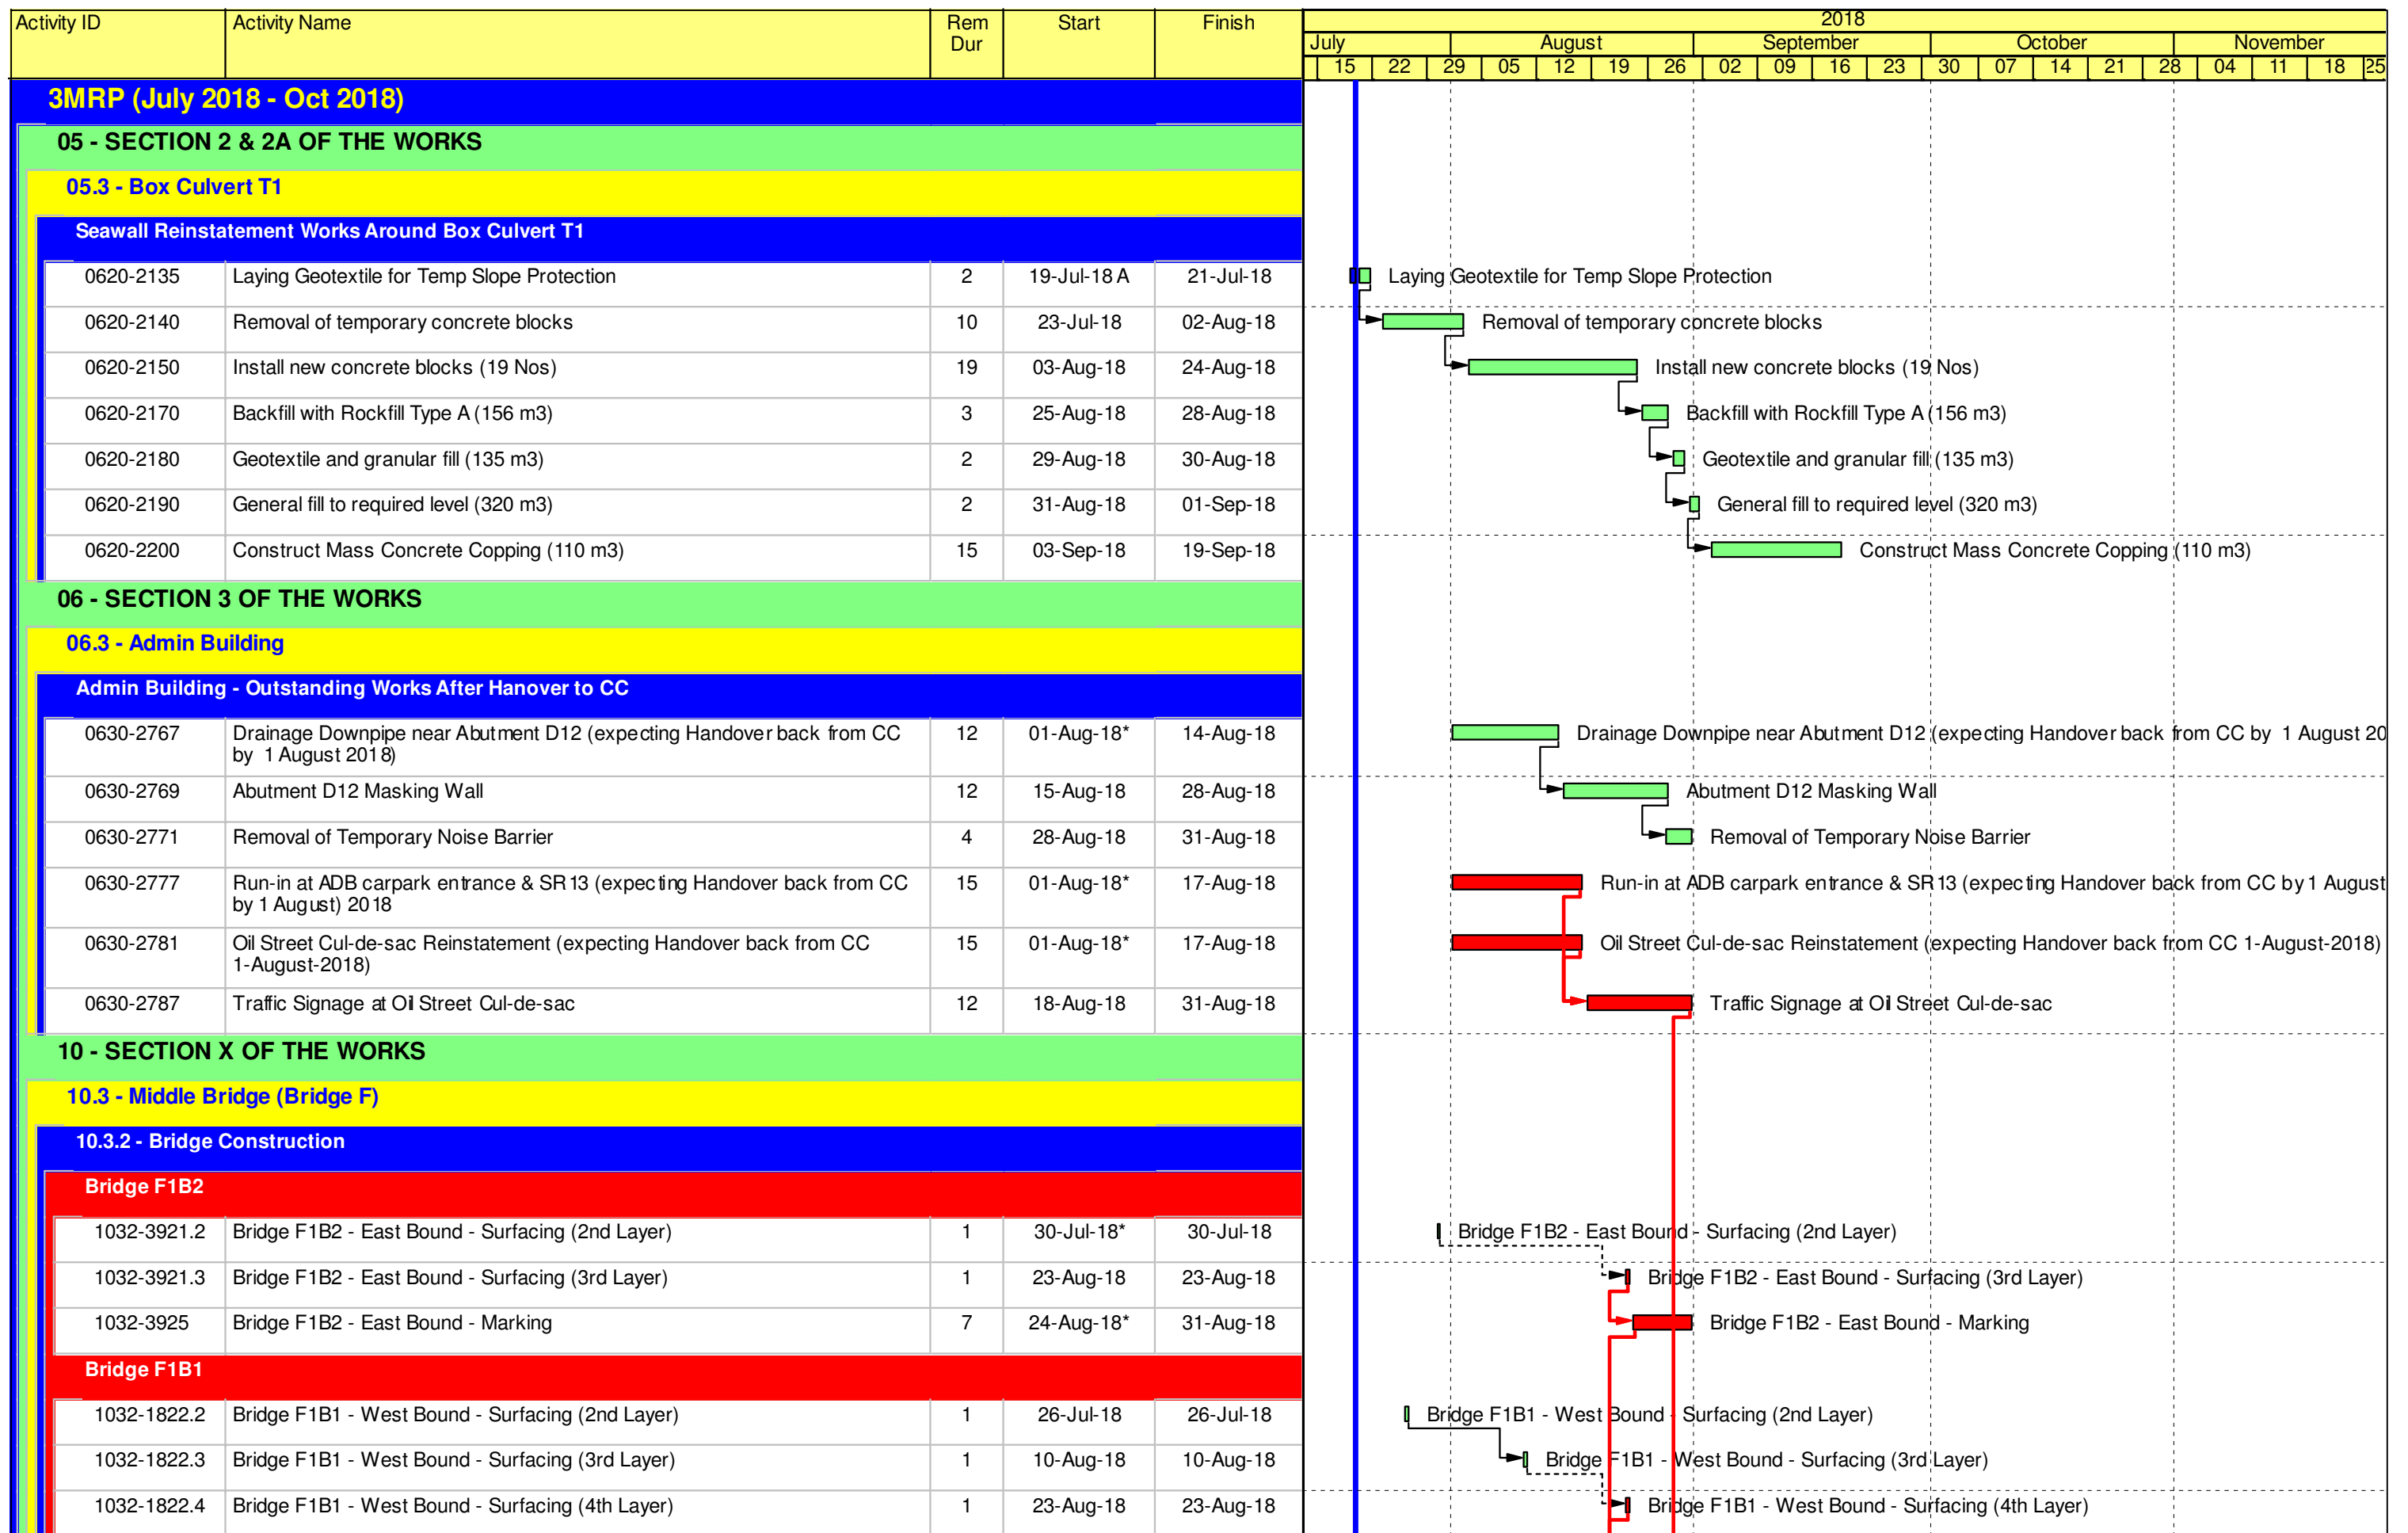

Contract HY/2009/19
Three Months Rolling Programme (20.July.2018 to 20.Oct.2018)


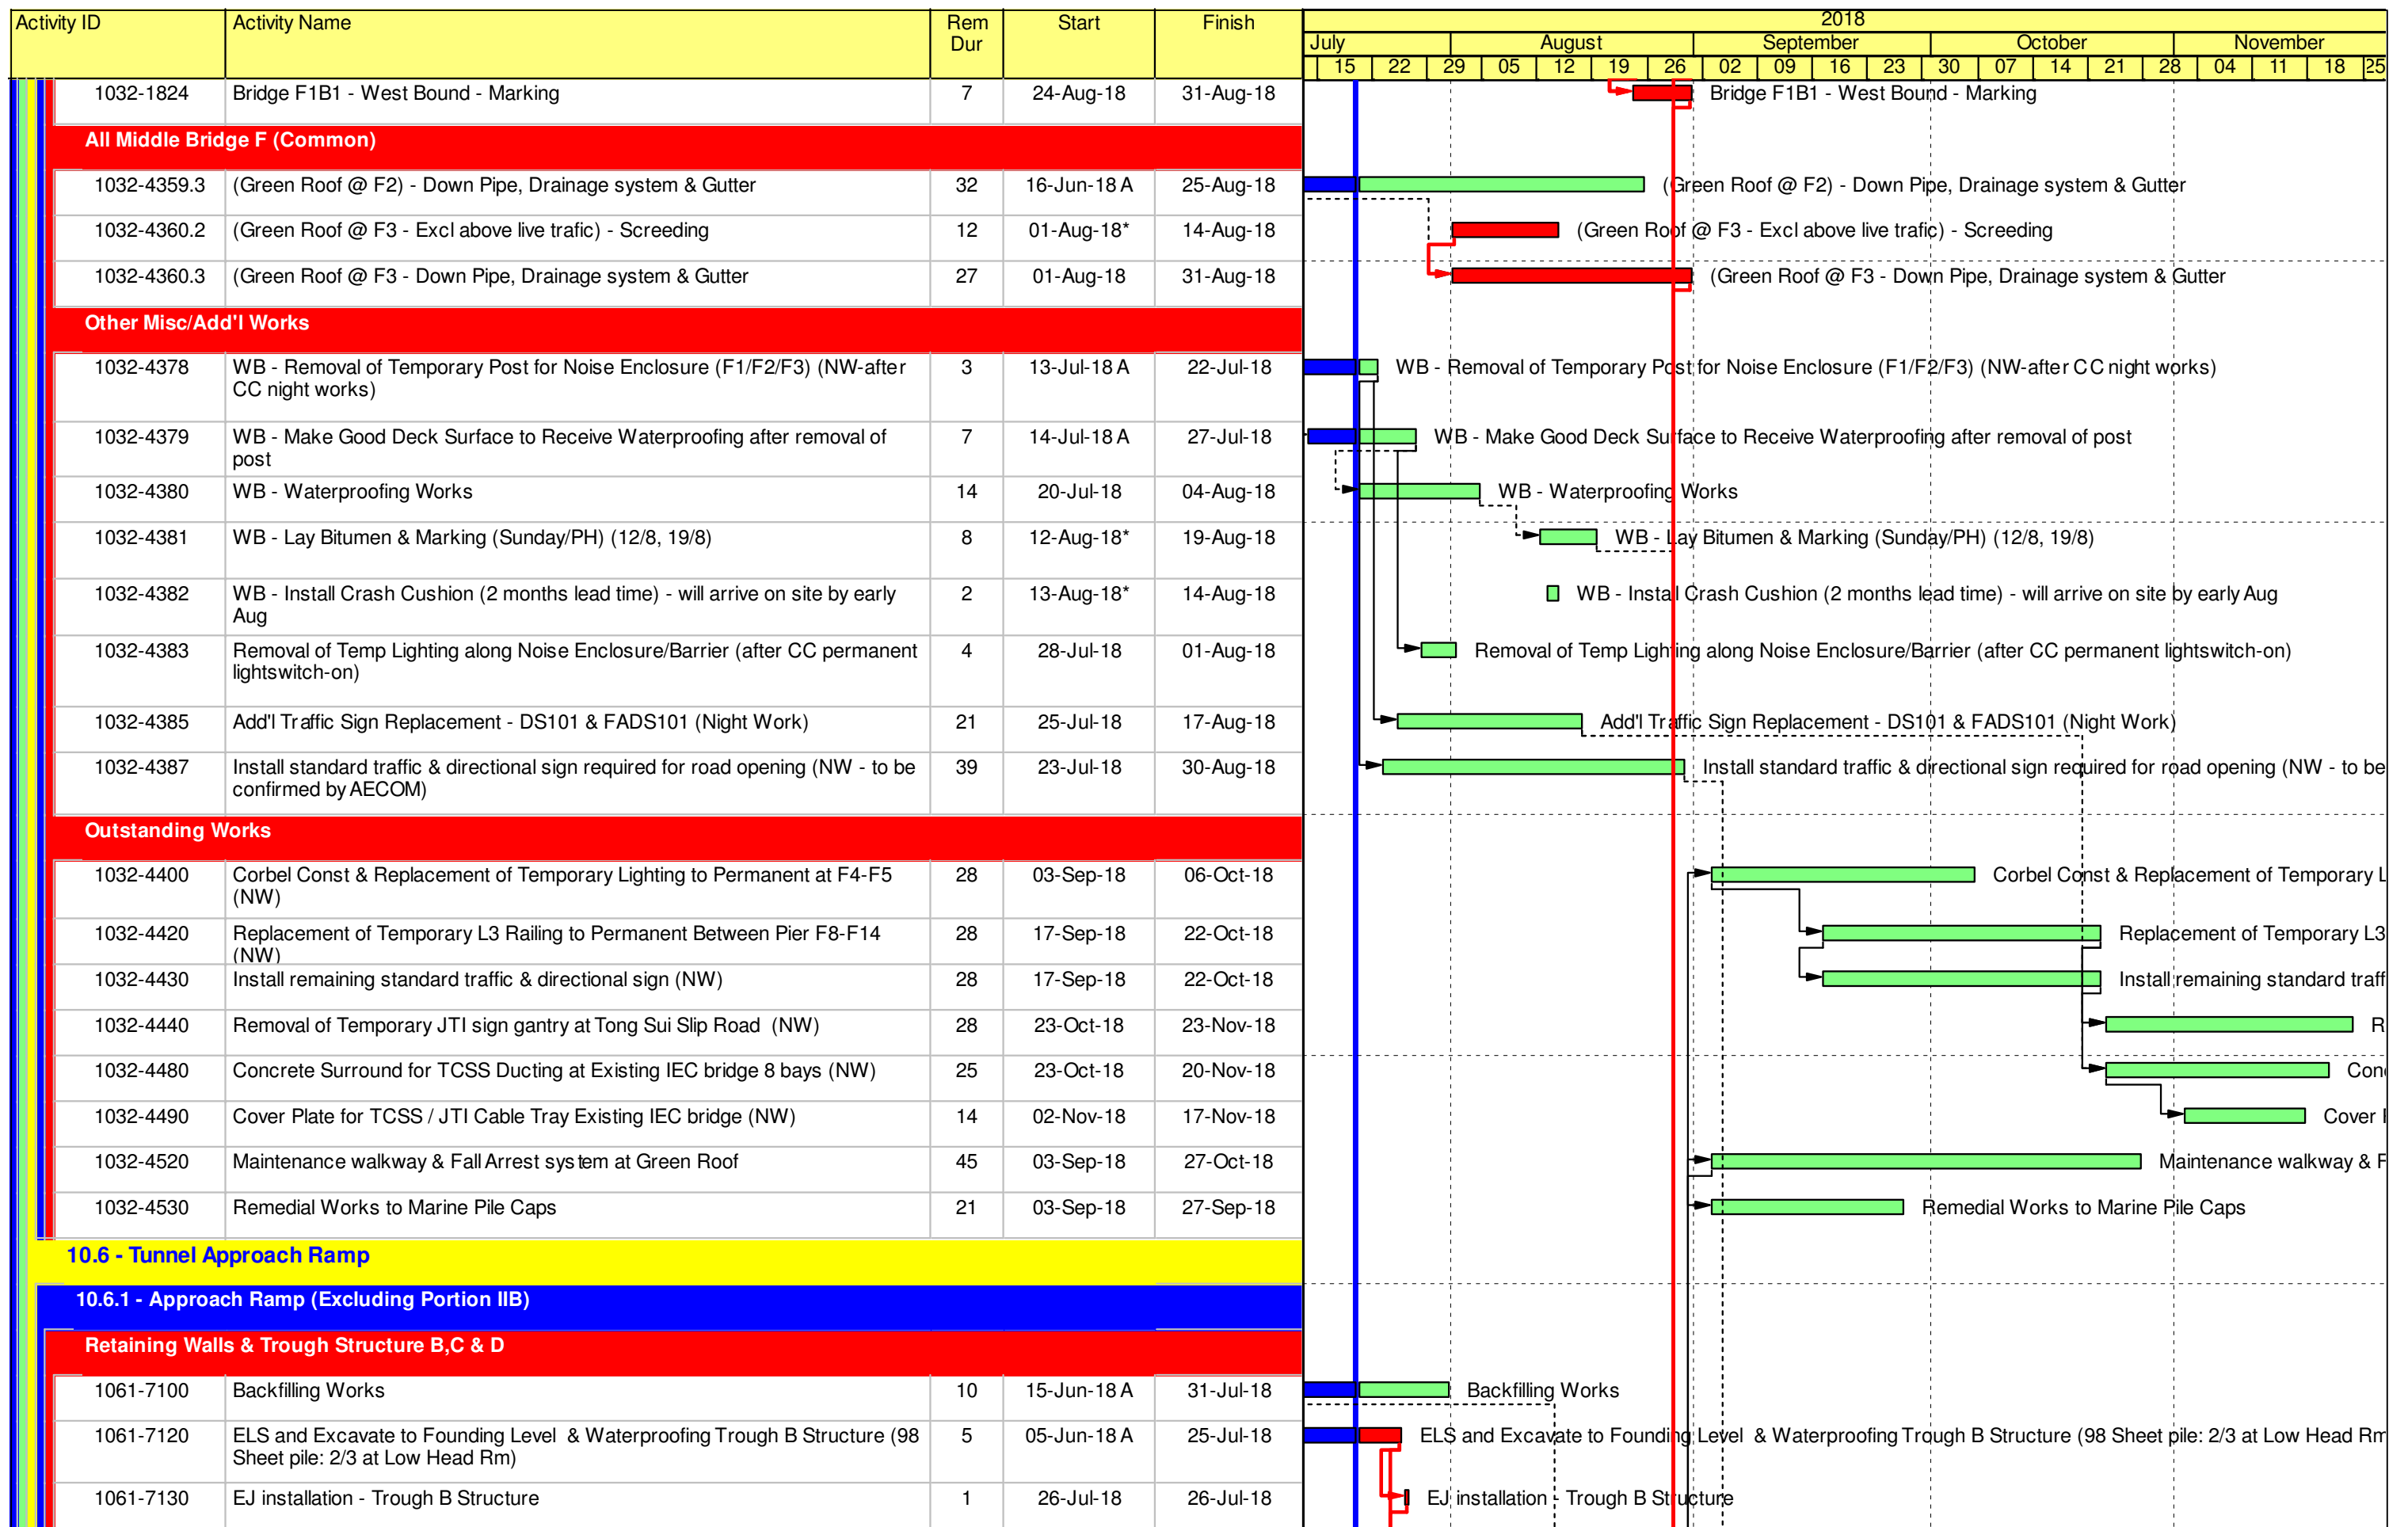


Contract HY/2009/19
Three Months Rolling Programme (20.July.2018 to 20.Oct.2018)

Activity ID	Activity Name	Rem Dur	Start	Finish	2018																		
					July			August			September			October			November						
					15	22	29	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18
1061-7140	Construct Trough Structure B Base Slab	11	27-Jul-18	08-Aug-18																			
1061-7160	Construct Trough Structure B Side Walls	7	09-Aug-18	16-Aug-18																			
1061-7180	Excavate to Founding Level & Waterproofing Trough C Structure	5	05-Jun-18 A	25-Jul-18																			
1061-7190	EJ installation - Trough C Structure	1	26-Jul-18	26-Jul-18																			
1061-7200	Construct Trough Structure C Base Slab (2nd Pour-east part)	5	27-Jul-18	01-Aug-18																			
1061-7210	Construct Trough Structure C Side Walls (1st Pour-west part)	4	17-Jul-18 A	24-Jul-18																			
1061-7220	Construct Trough Structure C Side Walls (2nd Pour-east part)	6	02-Aug-18	08-Aug-18																			
1061-7230	MJ Cover installation - Trough A/B/C Structure	6	14-Aug-18	20-Aug-18																			
1061-7240	Road, Paving & Fencing Works at Trough B/C/D	13	17-Aug-18	31-Aug-18																			
1061-7250	Backfilling Works at Back side of Trough B & C	12	17-Aug-18	30-Aug-18																			
Landscape Deck																							
1061-7464	Bay C5 > Upstand Wall at Bay C5 (east remaining - original end on 16 June 2018 but still waiting to AECOM details)	0	09-Apr-18 A	20-Jul-18																			
1061-7477	Bay C1-C5 > Type 2 Railing Above Landscape Deck (North & South side)	28	21-Jul-18	22-Aug-18																			
1061-7479	Bay C1-C5 > Type 2 Railing Above Landscape Deck (East & West side)	35	18-Oct-18	27-Nov-18																			
1061-7483	Bay C1-C5 > Waterproofing/Screeing/Root Barriers/Draining Composite/Subsoil+Soil Placing	84	12-Jul-18 A	29-Oct-18																			
Road & Other Misc Works																							
1061-7530	WB (Bay C4/C5) - Median Profile Barrier + K1 Kerb	12	16-Jul-18 A	02-Aug-18																			
1061-7545.1	WB - Asphalt laying 1st Layer (C4) (assume 1week for Public Lab Test Result	1	23-Jul-18	23-Jul-18																			
1061-7545.2	WB - Asphalt laying 2nd Layer (C4-C5)	1	31-Jul-18	31-Jul-18																			
1061-7545.3	WB - Asphalt laying 3rd Layer (C4-C5)	1	07-Aug-18	07-Aug-18																			
1061-7545.4	WB - Asphalt laying 4th Layer (C4-C5)	1	14-Aug-18	14-Aug-18																			
1061-7545.5	WB - Asphalt laying 5th Layer (C4-C5)	1	21-Aug-18	21-Aug-18																			
1061-7548	EB (Bay C4/C5) - Median Profile Barrier	12	19-Jul-18 A	02-Aug-18																			
1061-7550.1	EB - Asphalt laying 1st Layer (C4) (assume 1week for Public Lab Test Result	1	23-Jul-18	23-Jul-18																			
1061-7550.2	EB - Asphalt laying 2nd Layer (C4-C5)	1	28-Jul-18	28-Jul-18																			
1061-7550.3	EB - Asphalt laying 3rd Layer (C4-C5)	1	04-Aug-18	04-Aug-18																			
1061-7550.4	EB - Asphalt laying 4th Layer (C4-C5)	1	11-Aug-18	11-Aug-18																			
1061-7550.5	EB - Asphalt laying 5th Layer (C4-C5)	1	18-Aug-18	18-Aug-18																			
1061-7557	Install ADS08A + Sign Facing	8	11-Jun-18 A	28-Jul-18																			
1061-7558	Install GT2 + Sign Facing	8	14-May-18 A	28-Jul-18																			
1061-7600	Approach Ramp Final Road Surfacing & Marking (excl Portion IIB)	9	22-Aug-18	31-Aug-18																			

	Remaining Level of Effort		Remaining Work
	Actual Level of Effort		Critical Remaining Work
	Actual Work		Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.July.2018 to 20.Oct.2018)

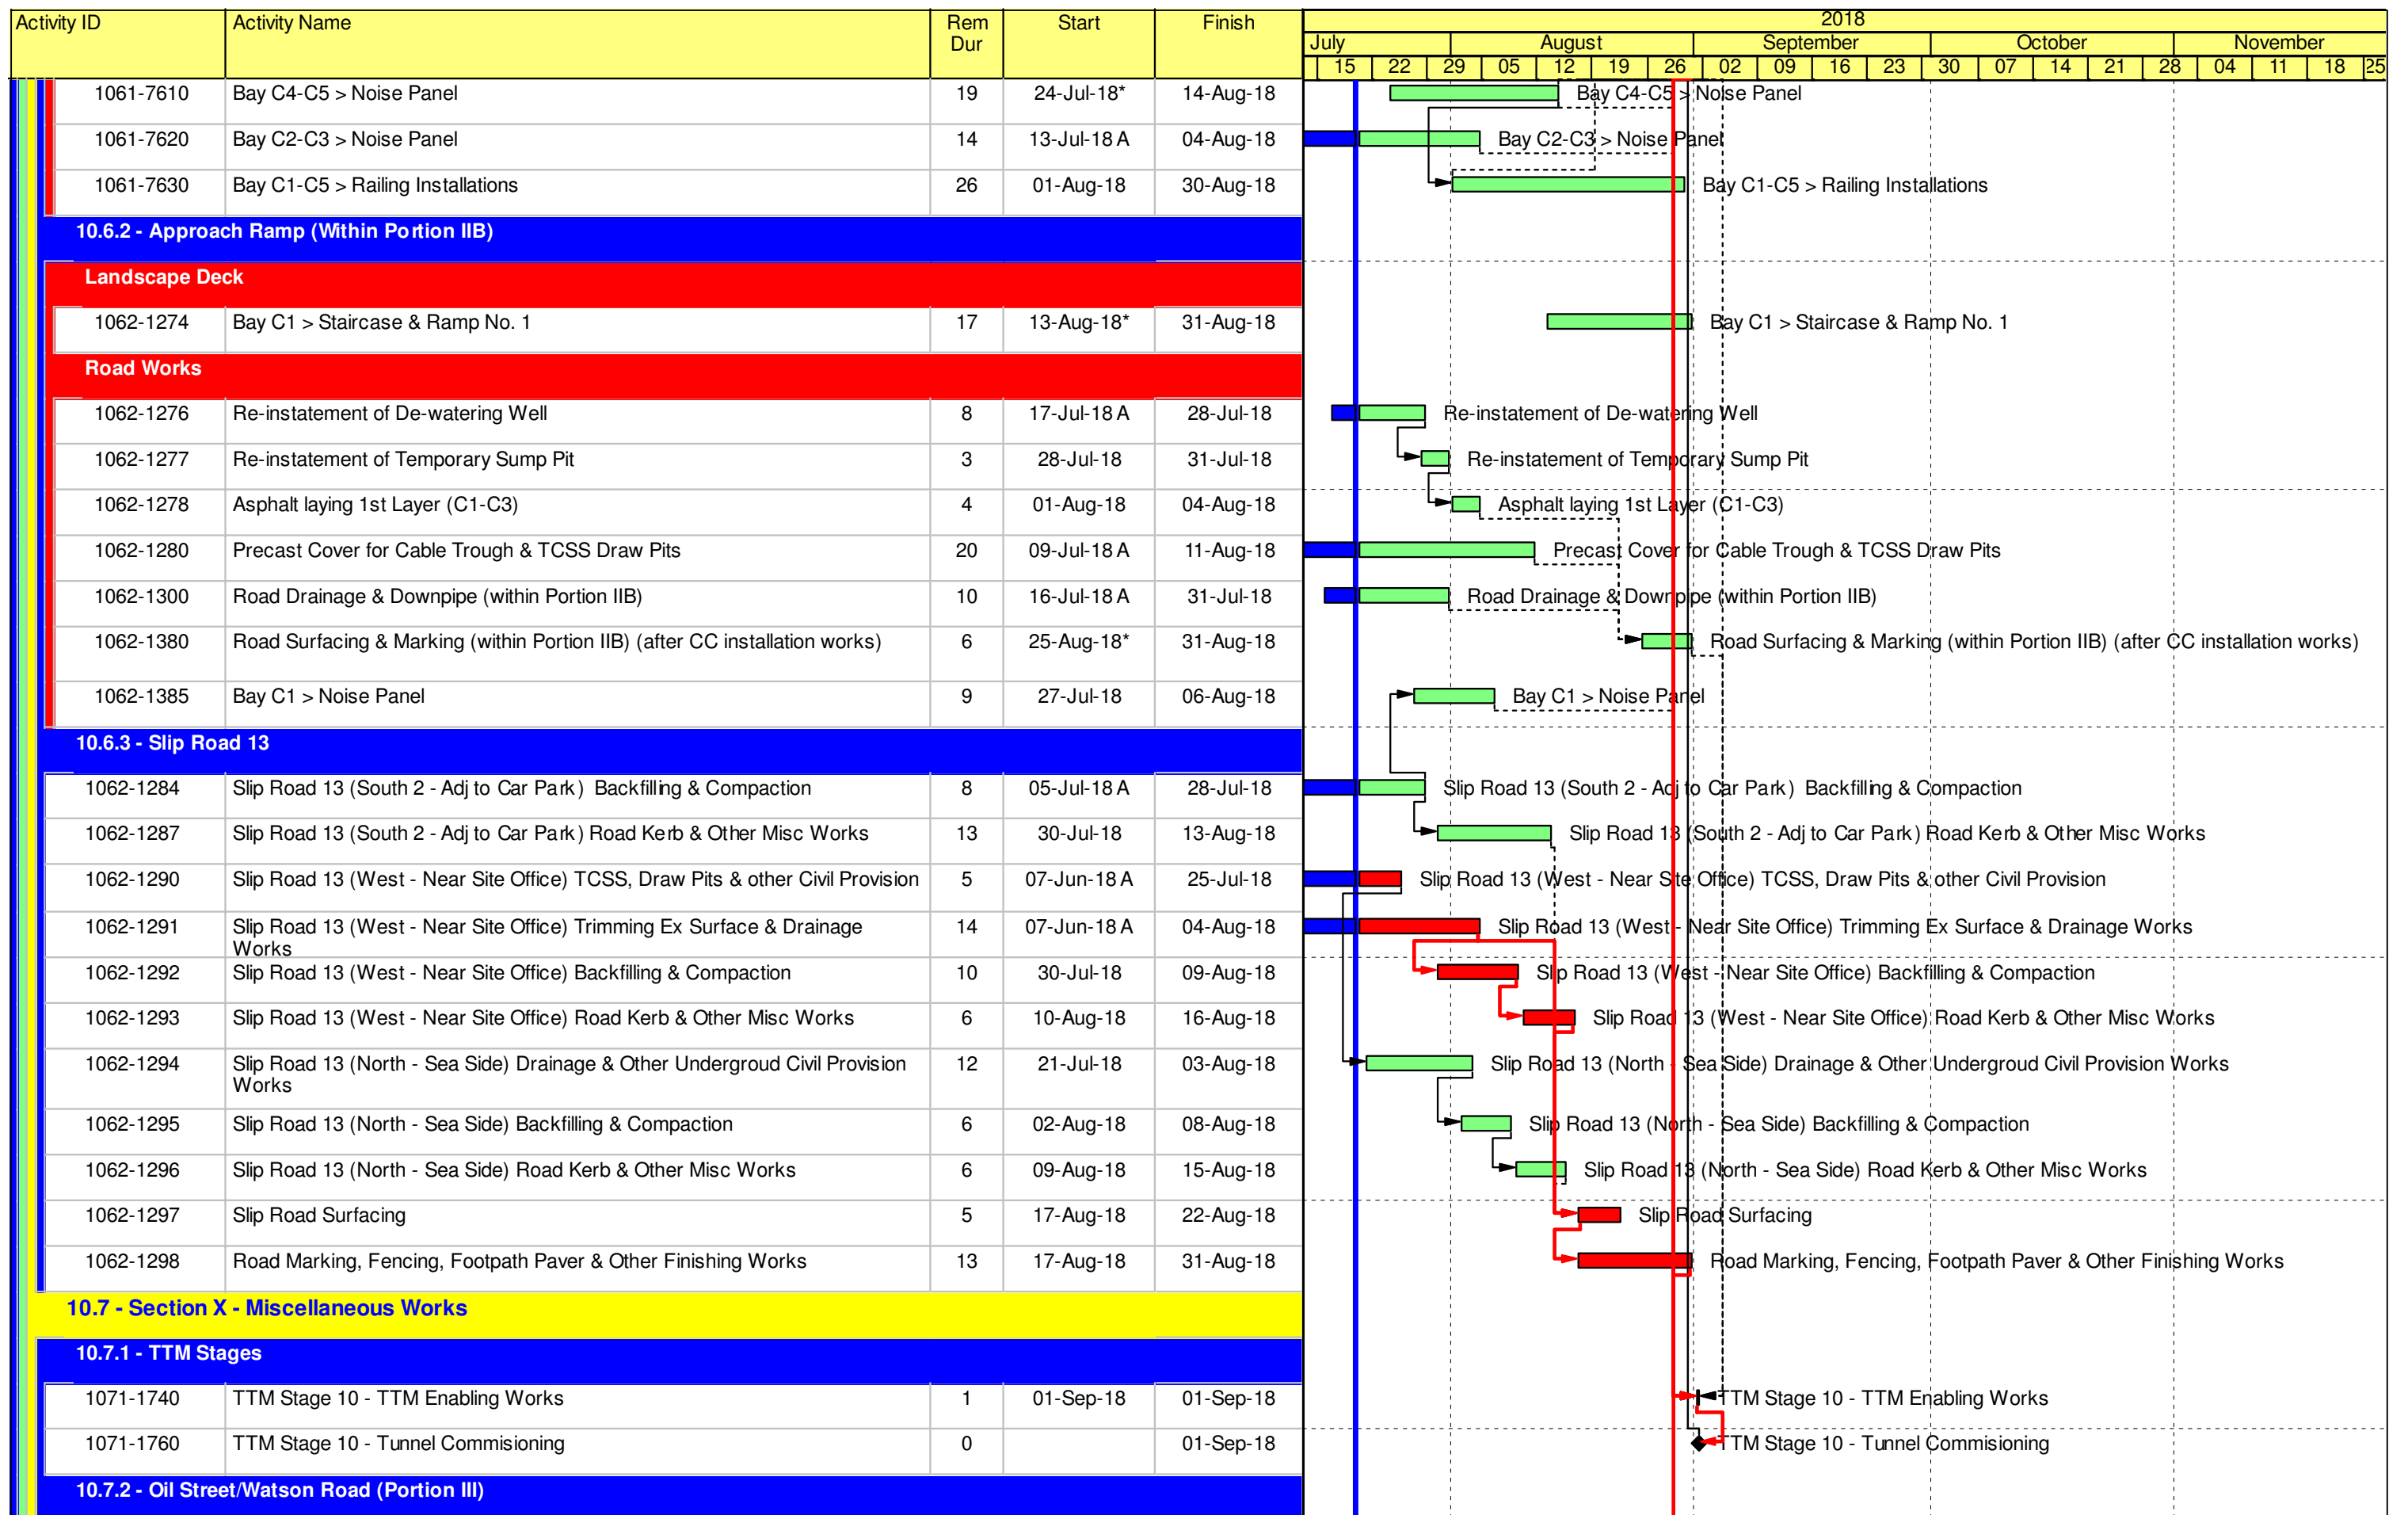

Contract HY/2009/19
Three Months Rolling Programme (20.July.2018 to 20.Oct.2018)

Activity ID	Activity Name	Rem Dur	Start	Finish	2018																				
					July			August			September			October			November								
					15	22	29	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	
1072-1285	Pre-cast Clay Paving EVA to EVB (remaining paver to arrive on site by mid Aug)	32	10-May-18 A	25-Aug-18	Pre-cast Clay Paving EVA to EVB (remaining paver to arrive on site by mid Aug)																				
1072-1287	Road Reinstatement > Watson Road cul-de sac	36	22-May-18 A	30-Aug-18	Road Reinstatement > Watson Road cul-de sac																				
11 - SECTION 11 OF THE WORKS																									
11.0 - Portion XIIC																									
1110-2500	EB - Modification of Road Marking at Hing Fat Slip Road (Night Work)	1	26-Aug-18*	26-Aug-18	EB - Modification of Road Marking at Hing Fat Slip Road (Night Work)																				
11.1 - Portion XIIA - Stage 1																									
11.1.1 - Along Watson Road - Waterwork & Roadworks (Portion XIIA)																									
1110-2853	Road Public Lighting at Watson Road	15	13-Aug-18*	29-Aug-18	Road Public Lighting at Watson Road																				
1110-2857	Installation of Pillar Box for Bridge D & E	15	01-Aug-18*	17-Aug-18	Installation of Pillar Box for Bridge D & E																				
1110-2859	Road Fencing / Street Furniture at Watson Road	12	18-Aug-18	31-Aug-18	Road Fencing / Street Furniture at Watson Road																				
11.1.4 - Footing and frame/pole for directional sign FVMSH2, ADS16 and OHVD (Portion XIIA)																									
1110-2989	Reinstatement of Footpath near FVMSH2 (currently occupied by China State & Leighthon)	15	15-Aug-18*	31-Aug-18	Reinstatement of Footpath near FVMSH2 (currently occupied by China State Leighthon)																				
11.2 - Portion XIIA - Stage 2 - Along Gordon House - Cross road ducting at Hing Fat St (public hol)																									
1110-3020	Miscellaneous Road Works at Portion XIIA (5 TTA - works only on Sun & PH; 12d)(under discussion bet AECOM & TD)	37	20-Jul-18	31-Aug-18	Miscellaneous Road Works at Portion XIIA (5 TTA - works only on Sun & PH; 12d)(under discussion bet AECOM & TD)																				
11.3 - Portion XIIA - Stage 3 - Preparation & works night before road opening																									
1110-3030	Misc Works prior to CWB opening incl preparation - Stage 2	12	18-Aug-18	31-Aug-18	Misc Works prior to CWB opening incl preparation - Stage 2																				

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.July.2018 to 20.Oct.2018)

Activity ID	Activity Name	Original Duration	Start	Finish	2018			
					Jun	Jul	Aug	Sep
Minor Reinstatement Works for Existing Sign Gantry								
EB_1750	Laying Public Lighting duct	3d	30-May-18 A	25-Aug-18	Laying Public Lighting duct			
EB_1780	Erect Sign Gantry Steel Supports and Sign Gantry Beam across VPR and IEC E/B	4d	29-Jul-18	01-Aug-18	Erect Sign Gantry Steel Supports and Sign Gantry Beam across VPR and IEC E/B			
EB_1790	Installation of E & M at Sign Gantry (night work)	1d	02-Aug-18	02-Aug-18	Installation of E & M at Sign Gantry (night work)			
EB_1760	Connection of Public Lighting by HyD (Lighting)	2d	26-Aug-18	27-Aug-18	Connection of Public Lighting by HyD (Lighting)			
Minor Reinstatement Works for Central Median of IEC & Footbridge								
EB_1800	Reconstruction of central divider (6m long, night work)	6d	02-Aug-18	07-Aug-18	Reconstruction of central divider (6m long, night work)			
EB_1810	Dismantlement of temp directional sign mounted on extg footbridge	1d	03-Aug-18	03-Aug-18	Dismantlement of temp directional sign mounted on extg footbridge			
Minor Reinstatement Works for Footpath								
EB_1820	Place kerblines along VPR footpath	3d	18-May-18 A	23-Aug-18	Place kerblines along VPR footpath			
EB_1850	Backfilling subbase material	2d	27-May-18 A	29-May-18 A	subbase material			
EB_1830	Reinstatement of District Council Welcome Sign and opening plaque at Planter area	1d	24-Aug-18	24-Aug-18	Reinstatement of District Council Welcome Sign and opening			
EB_1840	Re-provision of Tree	8d	25-Aug-18	01-Sep-18	Re-provision of Tree			
Minor Reinstatement Works for Bus Stop								
EB_1860	Reinstatement of Permanent Bus Stop	5d	23-May-18 A	26-Jun-18 A	Reinstatement of Permanent Bus Stop			
EB_1870	Relocation of Bus Stop	1d	27-Jun-18 A	27-Jun-18 A	Relocation of Bus Stop			
EB_1880	Reinstate Planter(Previous Temporary Bus Stop)	5d	25-Aug-18	29-Aug-18	Reinstate Planter(Previous Temporary Bus Stop)			
Minor Reinstatement Works for Loop Detector								
EB_1900	Construction of concrete plinth and fix counter housing for Loop Detector (ILDS)	3d	04-Aug-18	06-Aug-18	Construction of concrete plinth and fix counter housing for Loop Detector (ILDS)			
EB_1890	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)	1d	07-Aug-18	07-Aug-18	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)			
West Bound - Completion of Minor Outstanding / Remaining Works for KD9								
Minor Reinstatement Works for Victoria Park								
IECW_1500	Re-provision of Tree	32d	07-Jul-18	07-Aug-18	Re-provision of Tree			
IECW_1510	Laying Irrigation Main	10d	22-Jul-18	31-Jul-18	Laying Irrigation Main			
IECW_1520	Construct Landscape Footpath and Lightings	7d	06-Aug-18	12-Aug-18	Construct Landscape Footpath and Lightings			
Minor Reinstatement Works in IEC West Bound								
IECW_1600	Replacement of new movement joint at IEC W/B (Sun midnight only)	8d	21-Jun-18	28-Jun-18	Replacement of new movement joint at IEC W/B (Sun midnight only)			
IECW_1610	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)	57d	29-Jun-18	24-Aug-18	Repairing of extg conc deck surface after milling of temp asp			
IECW_1640	Erection of new precast concrete panels (12 nos.) at abutment M facing to VPR	2d	25-Aug-18	26-Aug-18	Erection of new precast concrete panels (12 nos.) at abu			
IECW_1620	Repairing of concrete defects on extg concrete deck and abutment M	30d	25-Aug-18	23-Sep-18	Re			
Works in Victoria Park (KD4, KD5, KD9)								
Re-Provisioning Works								
Nursery Compound								
Nursery compound								
ABWF								
Metal Fence								
VP_NC_1820	Installation	30d	05-Apr-18 A	07-Aug-18	Installation			
Fire Services								
VP_NC_2030	FS inspection	14d	21-Jun-18	07-Jul-18	FS inspection			
Plumbing and Flushing Water Supplies								
VP_NC_2100	WSD Inspection	14d	21-Jun-18	07-Jul-18	WSD Inspection			
External Works Aside Nursery Compound								
External Works Around Nursery Compound								








Activity ID	Activity Name	Original Duration	Start	Finish	2018											
					Jun			Jul			Aug			Sep		
					1	2	3	1	2	3	1	2	3	1	2	3
VP_NC_2250	Reinstatement of Existing Boundary Fence Wall Around Nursery Compound	45d	01-Mar-18 A	26-May-18 A	Existing Boundary Fence Wall Around Nursery Compound											
VP_NC_2260	EVA Construction	15d	28-May-18 A	14-Jul-18	EVA Construction											
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks		390d	08-Aug-18	01-Sep-19												
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)		365d	08-Aug-18	07-Aug-19												
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365d	08-Aug-18	07-Aug-19												
KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH>500mm)		365d	02-Sep-18	01-Sep-19												
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365d	02-Sep-18	01-Sep-19												
KD18 - Section 11: Transplanted Trees DBH>500mm in Portion VA and XII		365d	08-Aug-18	07-Aug-19												
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365d	08-Aug-18	07-Aug-19												
KD10 - Preservation and Protection of Trees		1088d	21-Mar-13 A	27-Sep-18												
PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	27-Sep-18												
KD15 & KD8 - Mooring Components Upkeep (CBTS and ATS)		979d	15-May-14 A	21-Jun-18												
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	21-Jun-18	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS											

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Aug	Sep	Oct	Nov
PO-VII_a1	Possession of Portion VII (Day 762) - CH3911-4250 (below -6.0mPD)	659	30-Dec-15 A	17-Sep-18	-263	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-Vc	Possession of Portion V (Day 607) - CH3210-3250	658	15-Jan-16 A	17-Sep-18	-241	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-VIb_b1	Possession of Portion VIb (Day 761) - CH3428-3625 (E/B)	619	18-Feb-16 A	17-Sep-18	-263	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-VIb_b2	Possession of Portion VIb (Day 761) - CH3428-3625 (W/B)	568	29-Feb-16 A	17-Sep-18	-226	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-Xa_1	Possession of Portion Xa (Day 650) - ADB Southern Portion (AECOM letter ref: 2015007890T)	589	07-Mar-16 A	17-Sep-18	-433	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-Xb_1	Possession of Portion Xb (Day 804) - ADB Northern Portion	589	07-Mar-16 A	17-Sep-18	-433	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-Vb1	Possession of Portion V (Day 607) - SR3	587	11-Mar-16 A	17-Sep-18	-1	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-Ia	Possession of Portion Ia (Day 789) - SCB / SCP1 / SCP2 / Rumsey Street Flyover	600	28-Mar-16 A	17-Sep-18	-416	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-VII_a2	Possession of Portion VII (Day 762) - CH3800-3911 (below -6.0mPD)	567	31-Mar-16 A	17-Sep-18	-263	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-IXc_1	Possession of Portion IXc (Day 712) - EVB above 3.6mPD - Relinquished on 12 Apr 2016	445	29-Jul-16 A	17-Sep-18	-409	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-IXb_1	Possession of Portion IXb (Day 712) - EVB (below +3.6mPD to tunnel top slab) - Relinquished on 12 Apr 2016	445	05-Aug-16 A	17-Sep-18	-409	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-VIa_a	Possession of Portion VIa (Day 823) - CH3250-3283	425	15-Aug-16 A	17-Sep-18	-226	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-Vb2_a	Possession of Portion V (Day 607) - SR2	456	15-Aug-16 A	17-Sep-18	-266	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-VIc_a	Possession of Portion VIc (Day 761) - CH3770-3800 (Access Shaft Opening)	391	23-Sep-16 A	17-Sep-18	-263	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-VIb_c	Possession of Portion VIb (Day 761) - CH3625-3770	391	23-Sep-16 A	17-Sep-18	-263	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-IVa1	Possession of Portion IVa (Day 930) - CH2600-2720	323	30-Nov-16 A	17-Sep-18	-249	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-IVb2	Possession of Portion IVb (Day 930) - MVB (GLD-H)	233	28-Feb-17 A	17-Sep-18	-457	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-VIIIa_a	Possession of Portion VIIIa (Day 929) - CH4530-4591 W/B	233	28-Feb-17 A	17-Sep-18	-267	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-VIIIa	Possession of Portion VIIIa (Day 929) - CH4250-4600 (Remaining)	241	12-Mar-17 A	17-Sep-18	-267	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-VIIIb	Possession of Portion VIIIb (Day 929) - SR8 (CH700-350)	233	12-Mar-17 A	17-Sep-18	-249	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-VIIIc	Possession of Portion VIIIc (Day 1039) - SR8 (CH350-310) / SCP4	233	12-Mar-17 A	17-Sep-18	-236	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-IVa2_a	Possession of Portion IVa (Day 930) - CH2720-2950	241	12-Mar-17 A	17-Sep-18	-249	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-IVb1	Possession of Portion IVb (Day 930) - MVB (GLA-C)	239	14-Mar-17 A	17-Sep-18	-457	[Gantt bars for Aug, Sep, Oct, Nov]			
PO-IVa2_b	Possession of Portion IVa (Day 930) - SR1	203	30-Mar-17 A	17-Sep-18	-249	[Gantt bars for Aug, Sep, Oct, Nov]			

-  Current Milestone
-  Remaining Work
-  Level of Effort
-  Project Baseline
-  Baseline Milestone
-  Actual Work
-  Critical Remaining Work

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 2 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Aug	Sep	Oct	Nov
PO-Vb2_b	Possession of Portion V (Day 607) - SCP3	182	03-Jul-17 A	17-Sep-18	-266				
PO-Vlb_a	Possession of Portion Vlb (Day 761) - CH3400-3428	80	31-Jul-17 A	17-Sep-18	-226				
PO-Vla_b	Possession of Portion Vla (Day 823) - CH3283-3400	80	31-Jul-17 A	17-Sep-18	-249				
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-Aug-18	08-Dec-18	-268				
Submissions and Approvals									
Initial General Submission									
10168	Submission of CMC 3DVR	30	20-Aug-18	18-Sep-18	-2				
DETAILED DESIGN OF WORKS									
Permanent Works Design and Engineering									
Green Wall on ADB									
10238	ADB Green Wall - Engineer review & Approval; Consent to Proceed Construction	24	07-Mar-16 A	25-Aug-18	-376				
Landscaping & Associated Irrigation System									
10268	Landscaping - Engineer review & Approval; Consent to Proceed Construction	24	07-Mar-16 A	01-Sep-18	-357				
PROCUREMENT, MANUFACTURING & DELIVERIES									
Procurement; Manufacturing; Deliveries									
Landscaping and Associated Irrigation System									
Shop Drawings									
10272	Landscaping - Shop Drawings submission to the Engineer	30	06-Oct-17 A	31-Aug-18	-469				
12848	Landscaping - Shop Drawings review by the Engineer	30	01-Sep-18	30-Sep-18	-469				
10274	Landscaping - Obtain Approval for Shop Drawings	0		30-Sep-18	-469				
Procurement & Fabrication									
10276	Landscaping - Confirm design of embed items	0	01-Oct-18		-469				
10278	Landscaping - Embed fabrication & delivery	12	01-Oct-18	12-Oct-18	-469				
10280	Landscaping - Commence embed installation	0	13-Oct-18		-469				

- Current Milestone
- Level of Effort
- Project Baseline
- Actual Work
- Critical Remaining Work
- Remaining Work
- Baseline Milestone

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 3 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

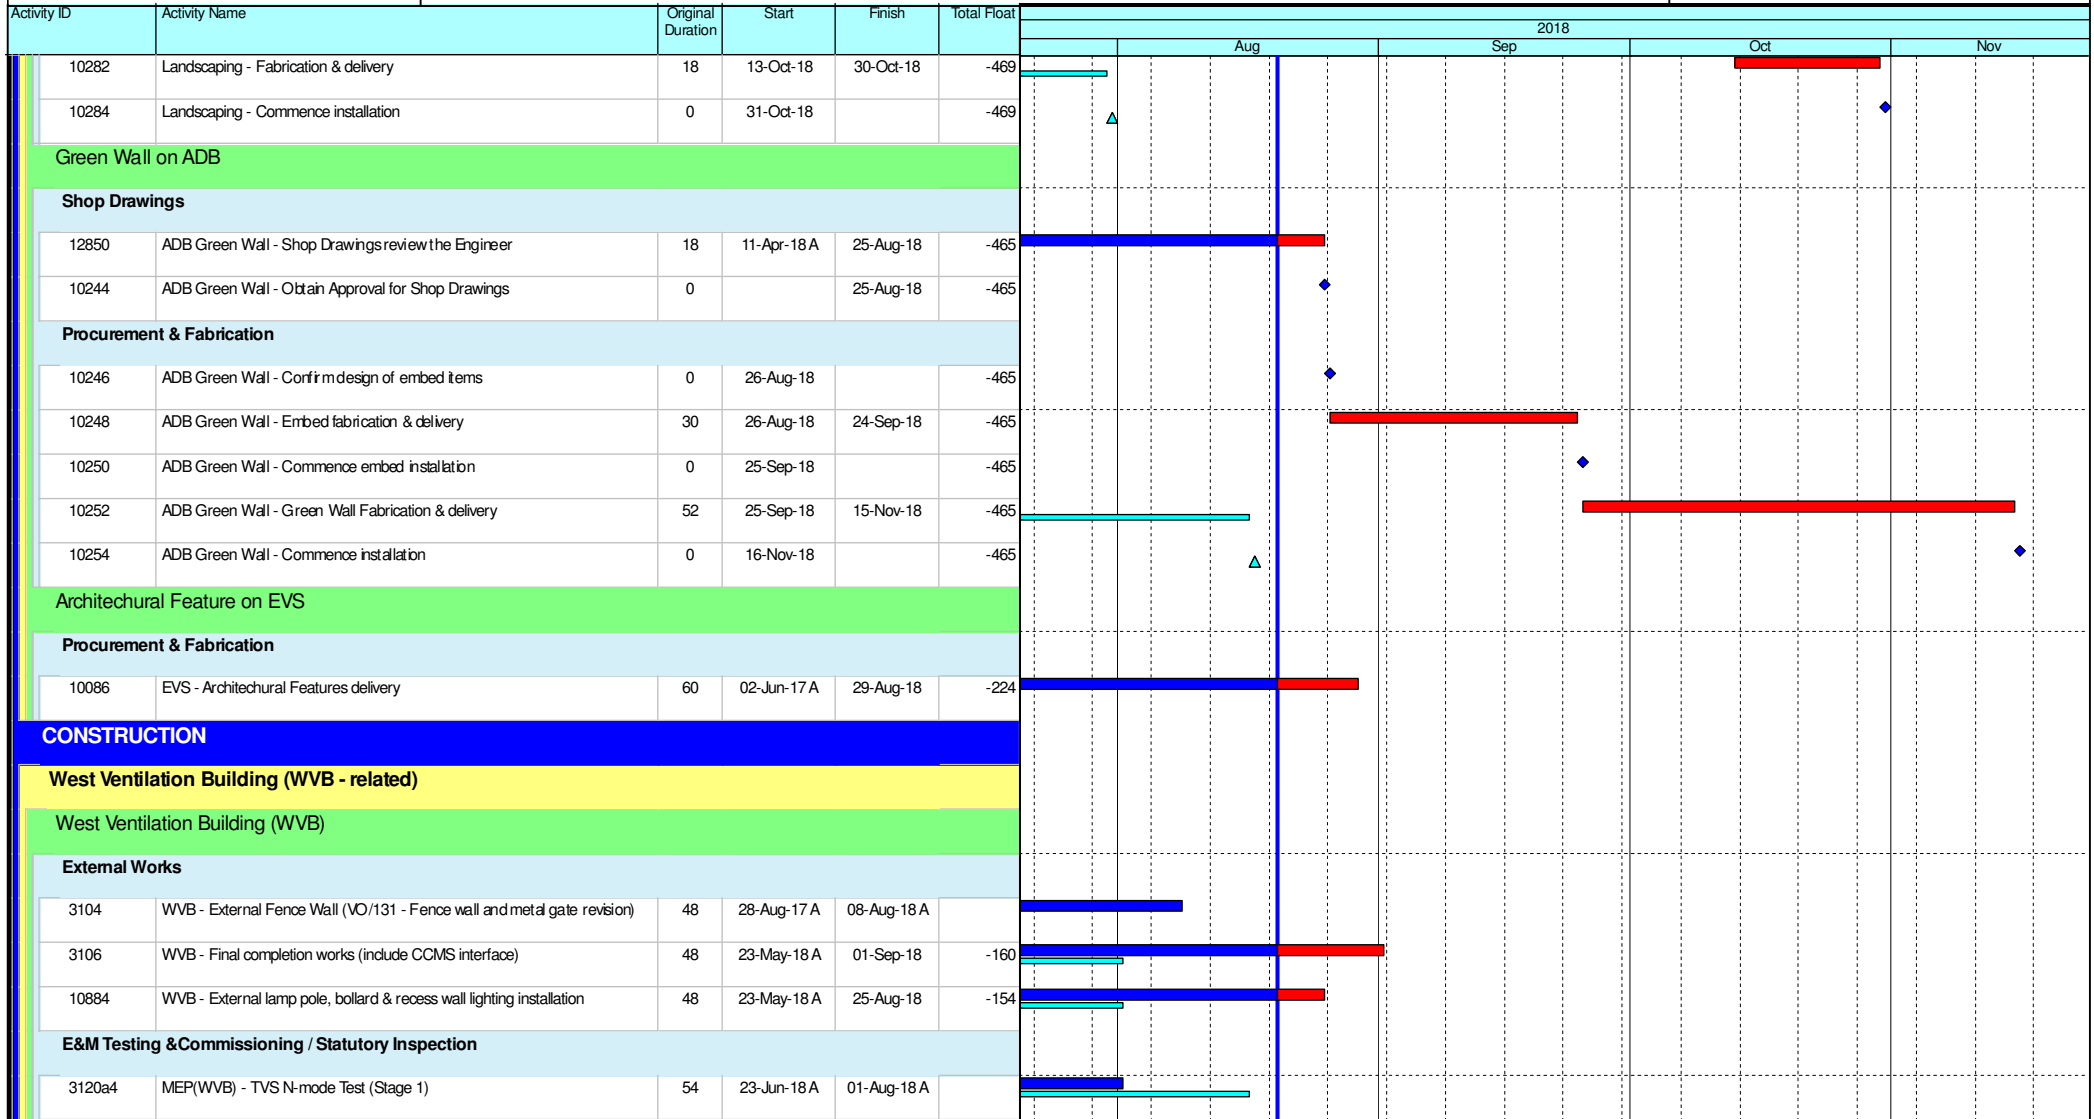

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 4 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

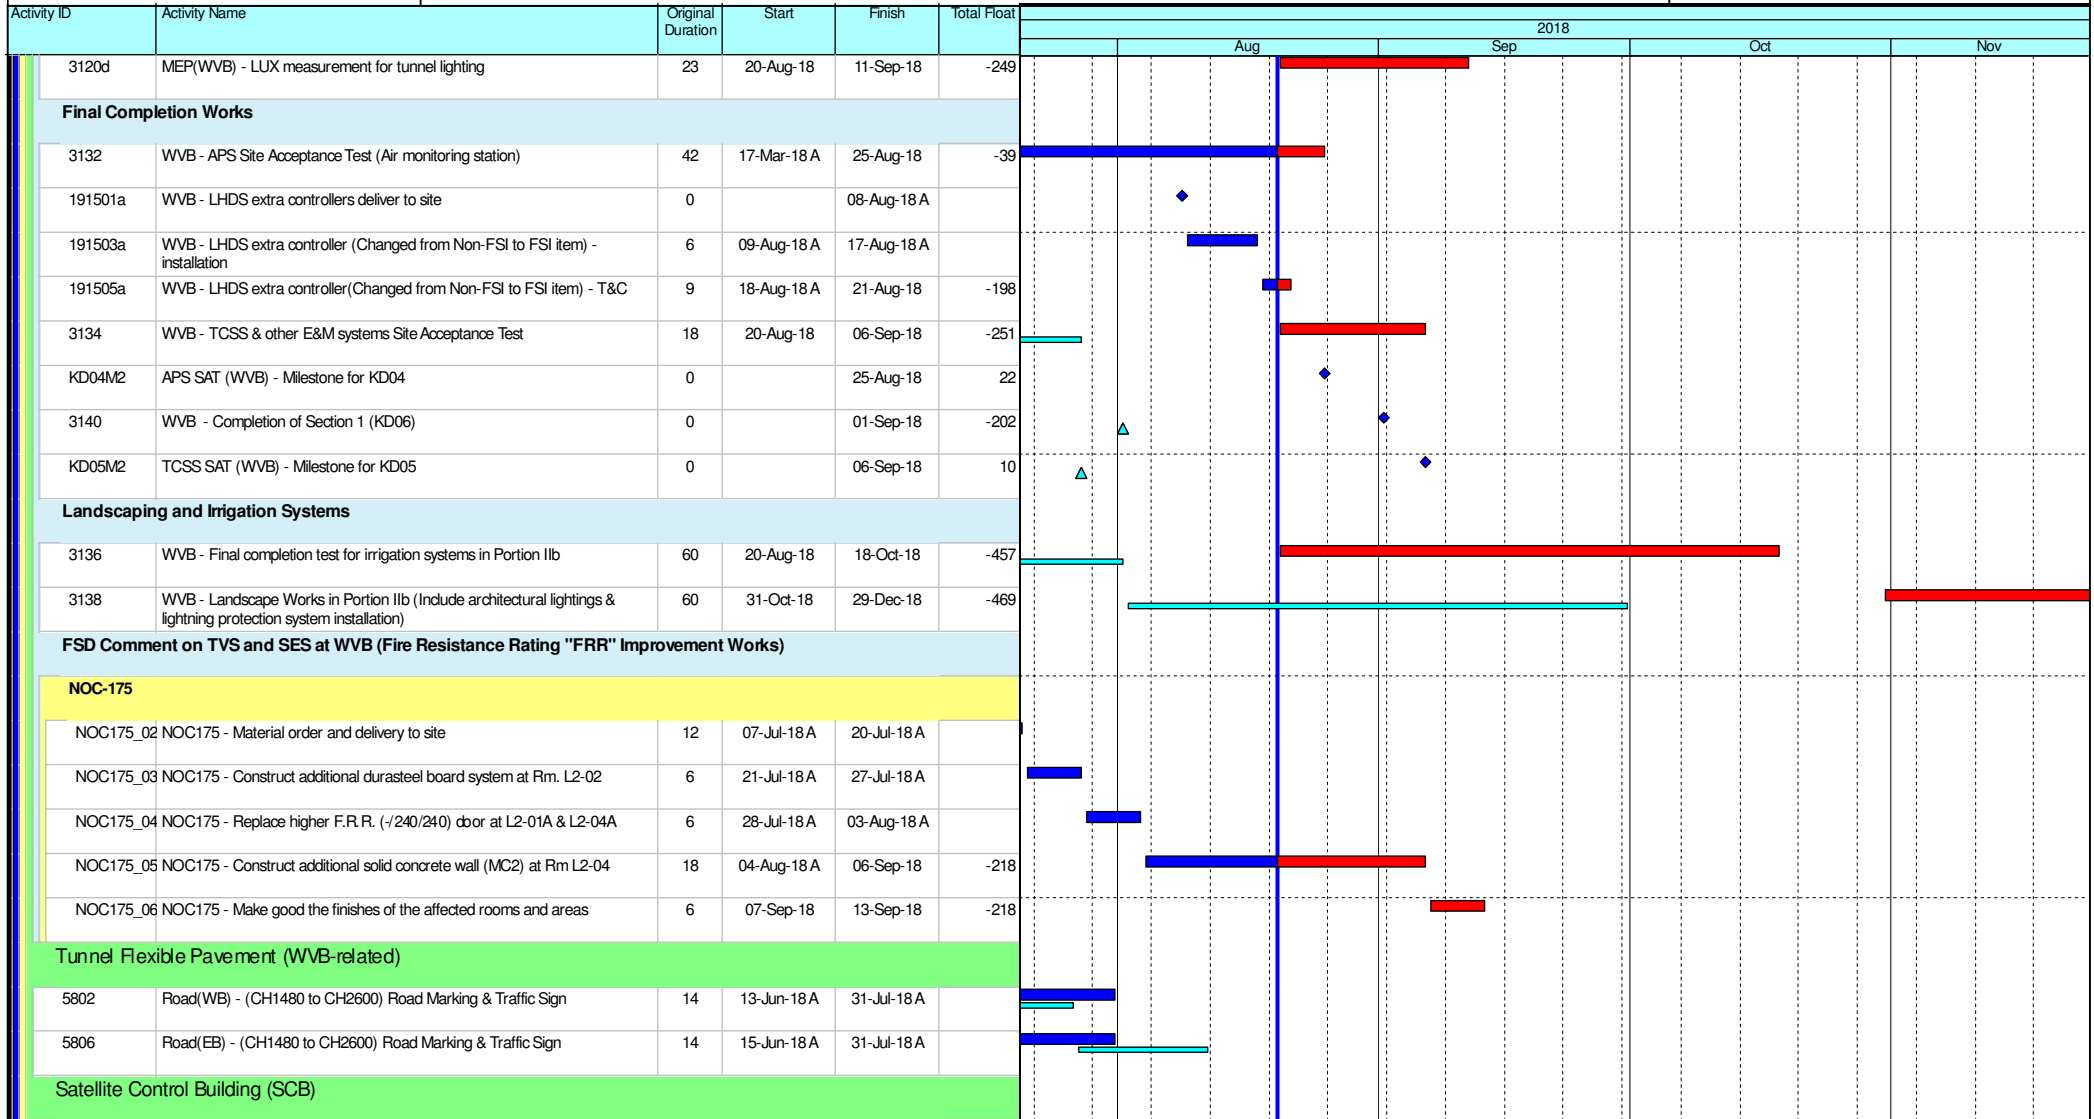

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 5 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018					
						Aug	Sep	Oct	Nov		
Final Completion Works											
3958	SCB - TCSS & other E&M systems Site Acceptance Test	90	10-May-18 A	25-Jul-18 A							
3962	SCB - Completion of Section 1	0		25-Jul-18 A		◆					
KD05M6	TCSS SAT (SCB) - Milestone for KD05	0		25-Jul-18 A		◆					
Satellite Control Points 1 / 2											
SCP1											
3720	MEP (SCP1) - E&M Final Completion Works	12	11-Jul-18 A	26-Jul-18 A							
KD01M2	MEP (SCP1) - Milestone for KD06	0		26-Jul-18 A		◆					
SCP2											
3742	MEP (SCP2) - E&M Individual System T&C	12	10-Jul-18 A	26-Jul-18 A							
3744	MEP (SCP2) - E&M Final Completion Works	12	10-Jul-18 A	26-Jul-18 A							
KD01M3	MEP (SCP2) - Milestone for KD06	0		26-Jul-18 A		◆					
Middle Ventilation Building (MVB - related)											
Tunnel Section (MVB-related)											
Portion IVa (CH2600 to CH2950)											
Slip Road 1											
10024	MEP(SR1) - (CH171 to CH271) TCSS Field equip & cable installation	6	24-May-18 A	27-Aug-18	2						
10046	MEP(SR1) - (CH171 to CH271) VE Panel installation (Upper part) (1200m2)	13	28-Jun-18 A	22-Aug-18	-182						
10046d	VO 238 - SR1 - Installation of granite stone panels / precast concrete panels	40	09-Jul-18 A	28-Jul-18 A							
10046c	VO 238 - SR1 - Construction of D-wall plinth and install wall brackets	12	10-Jul-18 A	23-Aug-18	-213						
10024a	MEP(SR1) - (CH171 to CH271) Access	0	20-Aug-18*		3			◆			
10046e	VO 238 - SR1 - Application of Evonik Protectosil SC60	6	21-Sep-18	28-Sep-18	-213						
Portion Va [CH2950 to CH3210]											
Westbound (Outer Lane)											

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 6 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Aug	Sep	Oct	Nov
9954a	MEP(WB) - (CH2950 to CH3210) VE Panel installation (Upper part) (1800m2)	20	11-Apr-18 A	25-Aug-18	-185				
Eastbound (Outer Lane)									
9956a	MEP(EB) - (CH2950 to CH3210) VE Panel installation (Upper part) (1800m2)	20	09-Apr-18 A	25-Aug-18	-185				
Portion Vb1 (SR3)									
Slip Road 3									
10032b	MEP(SR3) - (CH3089 to CH3334) E&M 1st Fix	13	15-Mar-17 A	23-Aug-18	-183				
10036b	MEP(SR3) - (CH3089 to CH3334) TCSS Field equip & cable installation	8	15-Mar-17 A	23-Aug-18	-183				
10034b	MEP(SR3) - (CH3089 to CH3334) E&M 2nd Fix (include Sump C)	27	11-Apr-18 A	25-Aug-18	-185				
10038b	MEP(SR3) - (CH3089 to CH3334) E&M Final Fix	8	16-Apr-18 A	27-Aug-18	-186				
10048c2	MEP(SR3) - Road lighting installation (Portal)	18	12-Jun-18 A	01-Sep-18	-191				
10048b	MEP(SR3) - (CH3089 to CH3334) VE Panel installation (Upper part) (2940m2)	33	04-Jul-18 A	27-Aug-18	-186				
10048g	VO 238 - Installation of granite stone	5	11-Jul-18 A	30-Jul-18 A					
10048h	VO 238 - Installation of precast concrete	22	24-Jul-18 A	11-Sep-18	-206				
10048i	VO 238 - Application of Evonik Protectosil SC60 at SR3	7	12-Sep-18	19-Sep-18	-206				
Portion Vb2 (SR2 / SCP3)									
Slip Road 2									
10050b	MEP(SR2) - (CH3114 to CH3257) E&M 1st Fix	8	08-Mar-17 A	21-Aug-18	-181				
10056b	MEP(SR2) - (CH3114 to CH3257) TCSS Field equip & cable installation	5	16-Mar-17 A	23-Aug-18	-183				
10052b	MEP(SR2) - (CH3114 to CH3257) E&M 2nd Fix (include Sump F)	40	15-Jun-17 A	25-Aug-18	-185				
10054b	MEP(SR2) - (CH3114 to CH3257) E&M Final Fix	5	08-May-18 A	25-Aug-18	-185				
10064b2	MEP(SR2) - Road lighting installation (Portal)	18	12-Jun-18 A	01-Sep-18	-191				
10064b	MEP(SR2) - (CH3114 to CH3257) VE Panel installation (Upper part) (1716m2)	18	09-Jul-18 A	25-Aug-18	-185				
Portion Vc [CH3210 to CH3250]									
Westbound (Outer Lane)									

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 7 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Aug	Sep	Oct	Nov
9954c	MEP(WB) - (CH3210 to CH3250) VE Panel installation (Upper part) (1800m2)	20	10-Jul-18 A	30-Aug-18	-189				
Eastbound (Outer Lane)									
9956c	MEP(EB) - (CH3210 to CH3250) VE Panel installation (Upper part) (1800m2)	20	06-Jul-18 A	25-Aug-18	-185				
Portion VIa [CH3250 to CH3283]									
Westbound									
9958a	MEP(WB) - (CH3250 to CH3283) VE Panel installation (Upper part) (528m2)	6	19-Apr-18 A	21-Aug-18	-181				
Eastbound									
9960a	MEP(EB) - (CH3250 to CH3283) VE Panel installation (Upper part) (528m2)	6	18-Apr-18 A	21-Aug-18	-181				
Portion VIa [CH3283 to CH3400]									
Westbound									
9958b	MEP(WB) - (CH3283 to CH3400) VE Panel installation (Upper part) (1872m2)	21	10-Apr-18 A	25-Aug-18	-185				
Eastbound									
9960b	MEP(EB) - (CH3283 to CH3400) VE Panel installation (Upper part) (1872m2)	21	16-Apr-18 A	25-Aug-18	-185				
Middle Ventilation Building (MVB)									
External Facade									
3238	MVB - External facing tiles / Louvre	90	06-Nov-17 A	14-Aug-18 A					
MEP Works									
3236	MVB - Metal works / steel platform / Ladders / Handrails	48	06-Dec-17 A	10-Aug-18 A					
3248	MEP(MVB) - TCSS Enabling Works (Remaining TCSS installation)	24	03-Jan-18 A	23-Jul-18 A					
3252	MEP(MVB) - E&M Final Completion Works; Ready for Statutory Inspections	24	31-May-18 A	16-Aug-18 A					
3280a10	Rectification works for lift shaft structure by lift contractor / WDII / C3	6	03-Aug-18 A	09-Aug-18 A					
E&M Individual System T&C									
3250c	MEP(MVB) - Lift functional test	12	06-Jul-18 A	09-Aug-18 A					
Basement 2 (GL D - H)									

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 8 of 27








Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018					
						Aug	Sep	Oct	Nov		
Basement 2 - Other Rooms / General Area & Corridor											
19034	MEP(MVB) - E&M final fixing	18	12-Feb-18 A	25-Jul-18 A							
Basement 2M (GL D - H)											
Basement 2M - Other Rooms / General Area & Corridor											
19051	MEP(MVB) - E&M final fixing	18	07-Mar-18 A	03-Aug-18 A							
Basement 1 (GL D - H)											
Other Rooms / General Area & Corridor											
11318	MEP(MVB) - E&M final fixing	24	20-Feb-18 A	15-Aug-18 A							
Basement 1 (GL A - D)											
MCC Room 1 (B1-04)											
11286	MEP(MVB) - E&M final fixing	24	25-Nov-17 A	14-Aug-18 A							
G/F (GL D - H)											
TVF Fan Room 2 (G-02)											
11404	MEP(MVB) - E&M final fixing	24	03-Mar-18 A	25-Jul-18 A							
Other Rooms / General Area & Corridor											
11412	MEP(MVB) - E&M final fixing	24	21-Feb-18 A	07-Aug-18 A							
G/F (GL A - D)											
Fire Control Centre (G-11)											
11380	MEP(MVB) - E&M final fixing	12	02-Mar-18 A	26-Jul-18 A							
Other Rooms / General Area & Corridor											
11388	MEP(MVB) - E&M final fixing	24	02-Mar-18 A	02-Aug-18 A							
1/F (GL D - H)											
Other Rooms / General Area & Corridor											
11446	MEP(MVB) - E&M final fixing	18	21-Feb-18 A	16-Aug-18 A							

-  Current Milestone
-  Level of Effort
-  Baseline Milestone
-  Actual Work
-  Critical Remaining Work
-  Remaining Work
-  Project Baseline

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 9 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018				
						Aug	Sep	Oct	Nov	
1/F (GLA - D)										
FS Water Tank & Pump Room (L1-05)										
11420	MEP(MVB) - E&M final fixing	12	15-Mar-18 A	24-Jul-18 A						
Other Rooms / General Area & Corridor										
11438	MEP(MVB) - E&M final fixing	18	15-Feb-18 A	09-Aug-18 A						
Smoke Extraction System (B3/F - G/F)										
B3/F - G/F										
191485	SES(MVB) - Termination	6	16-Jun-18 A	23-Jul-18 A						
191487	SES(MVB) - Testing & Commissioning	12	24-Jul-18 A	07-Aug-18 A						
External Works										
3258	MVB - External concrete pavement	42	04-Apr-18 A	30-Aug-18	-158					
3262	MVB - Final completion works (include CCMS interface)	30	05-Apr-18 A	30-Aug-18	-158					
3260	MVB - External Fence Wall	42	10-Apr-18 A	30-Aug-18	-158					
E&M Testing & Commissioning / Statutory Inspection										
3264	MEP(MVB) - E&M System Integrated Testing and Commissioning	24	23-Jul-18 A	31-Aug-18	-261					
3264a	MEP(MVB) - TVS & CCMS System Integrated Testing and Commissioning	24	23-Jul-18 A	31-Aug-18	-261					
3264b	MEP(MVB) - Tunnel Lighting & CCMS System Integrated Testing and Commissioning	24	23-Jul-18 A	31-Aug-18	-261					
3264c	MEP(MVB) - Fire Services & CCMS System Integrated Testing and Commissioning	24	23-Jul-18 A	31-Aug-18	-261					
3264a4	MEP(MVB) - TVS N-mode Test (Stage 2)	54	10-Aug-18 A	31-Aug-18	-238					
12606	MEP(MVB) - Submission of Form 5 to EMSD	0	15-Aug-18 A							
3266	MEP(MVB) - Ready for Statutory Inspection	0	17-Aug-18 A							
12622b	MEP(MVB) - Submission of Form 501 to FSD (include SES / SPS) (Building)	0	17-Aug-18 A							
12650	MEP(MVB) - Submission of Form 314 to FSD	0	17-Aug-18 A							
KD02M1	MEP(MVB) - Milestone for KD02	0		17-Aug-18 A						

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline
- ▲ Baseline Milestone

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 10 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

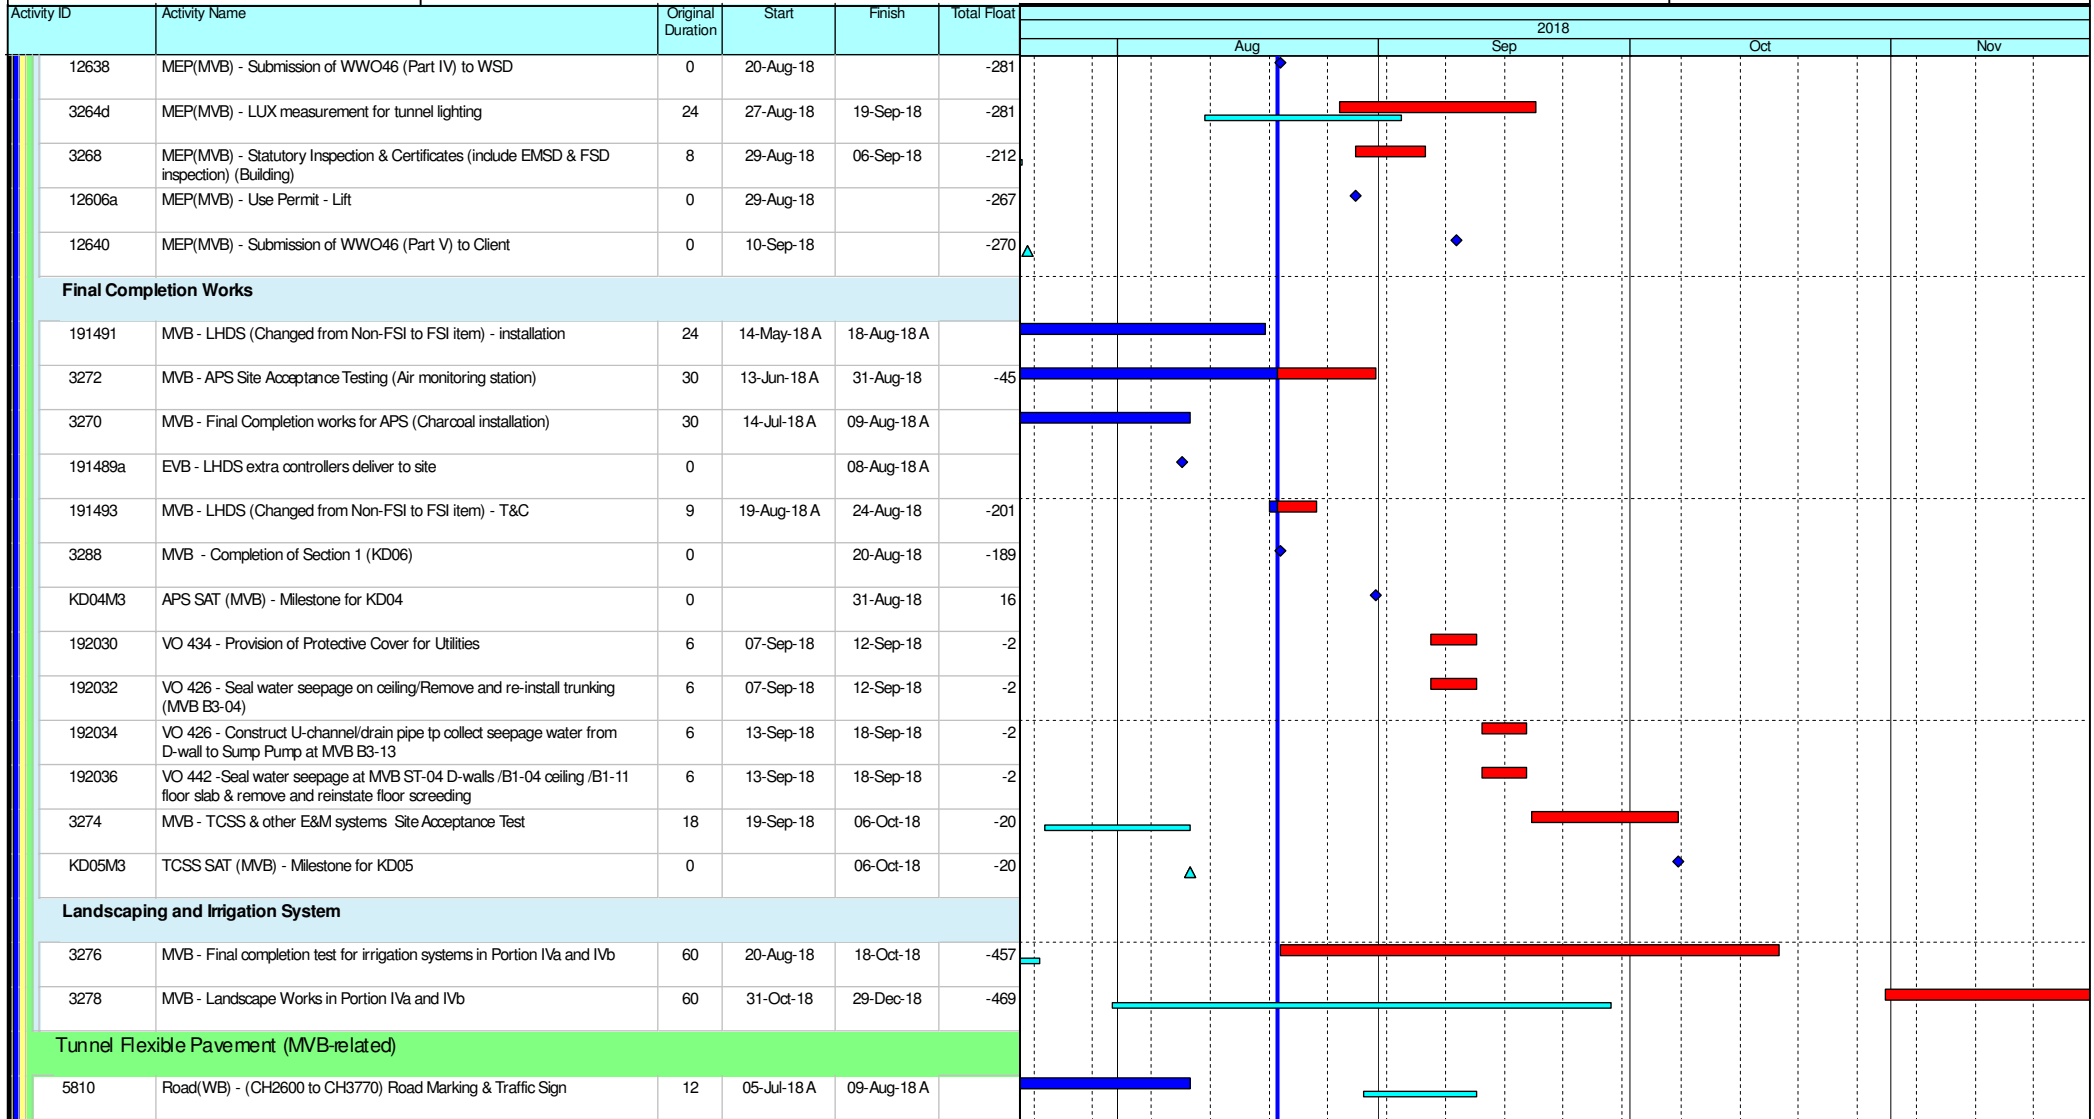

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 11 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

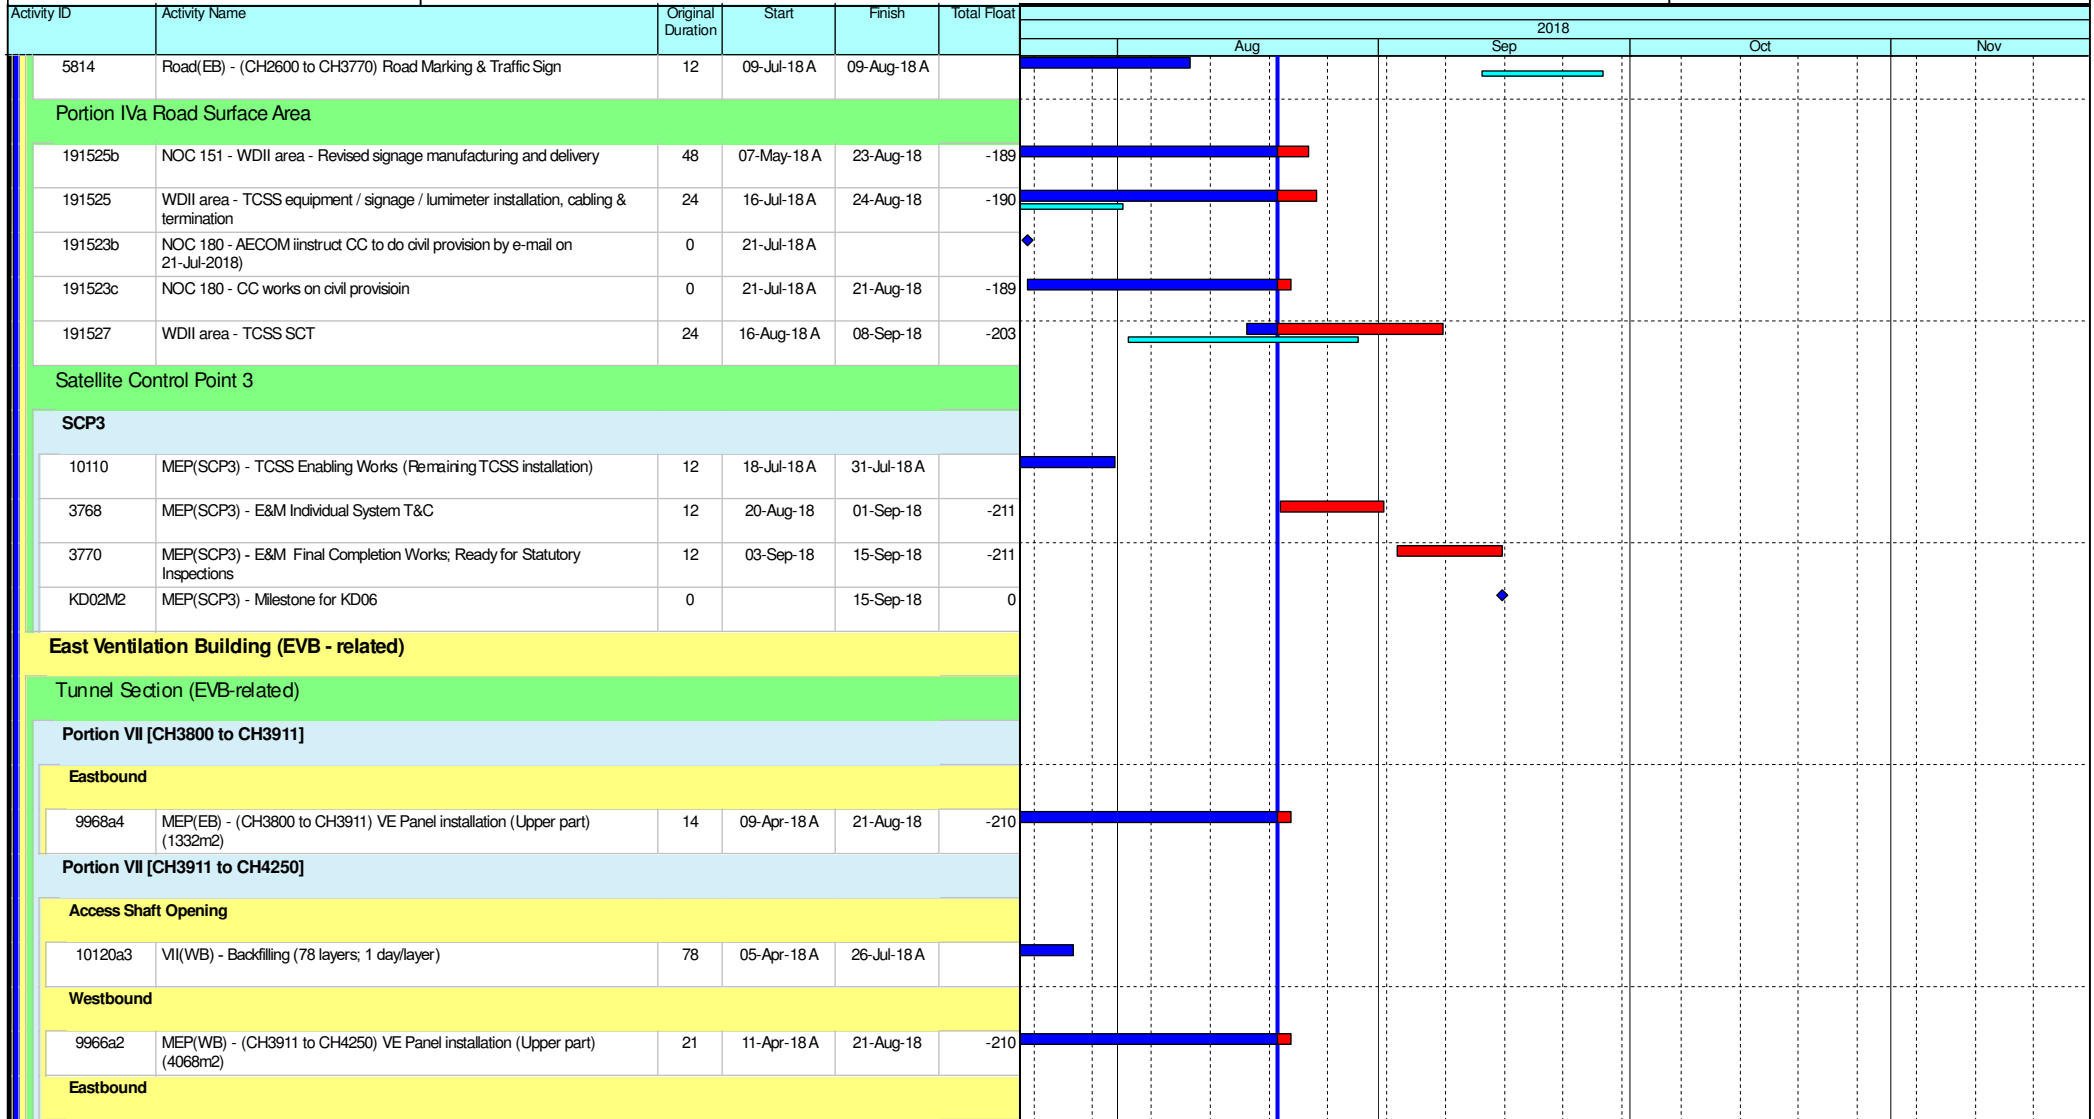

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 12 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Aug	Sep	Oct	Nov
9968a2	MEP(EB) - (CH3911 to CH4250) VE Panel installation (Upper part) (4086m2)	12	14-Apr-18 A	21-Aug-18	-210				
Portion VIIIa [CH4250 to CH4600]									
Eastbound									
9972	MEP(EB) - (CH4250 to CH4600) VE Panel installation (Upper part) (3900m2)	11	24-Jan-18 A	21-Aug-18	-210				
Portion IXd [CH4600 to CH4860]									
Eastbound									
9976	MEP(EB) - (CH4600 to CH4860) VE Panel installation (Upper part) (3300m2)	37	22-Mar-18 A	21-Aug-18	-210				
Portion IXa [CH4860 to CH5150]									
Eastbound									
5346	MEP(EB) - (CH4860 to CH5150) E&M Final Fix	10	14-Mar-18 A	27-Jul-18 A					
9980	MEP(EB) - (CH4860 to CH5150) VE Panel installation (Upper part) (3288m2)	37	05-Apr-18 A	23-Aug-18	-212				
East Ventilation Building (EVB)									
RC Structures and Green Roof									
3456	EVB - Green Roof (include architectural lighting & lightning protection system installation)	42	19-May-18 A	01-Sep-18	-330				
External Facade									
3438	EVB - External facing tiles / Treated Waste Wood / Louvre	90	11-Sep-17 A	22-Sep-18	-298				
192020	VO/335 - Material submission for approval	6	20-Aug-18	25-Aug-18	-30				
191613	VO/335 - Manufacture and delivery of smoke vent cover	24	27-Aug-18	22-Sep-18	-30				
191615	VO/335 - smoke vent cover installation and cable termination	18	24-Sep-18	16-Oct-18	-30				
191617	VO/335 - smoke vent cover T&C (Assume not affecting FSD inspection until further confirmation from AECOM / FSD)	6	18-Oct-18	24-Oct-18	-30				
MEP Works									
3452	MEP(EVB) - E&M Final Completion Works; Ready for Statutory Inspections	21	11-Apr-18 A	01-Sep-18	-220				
E&M Individual System T&C									
3660d	MEP(ADB) - LUX measurement for tunnel lighting	28	20-Aug-18	16-Sep-18	-254				

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 13 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

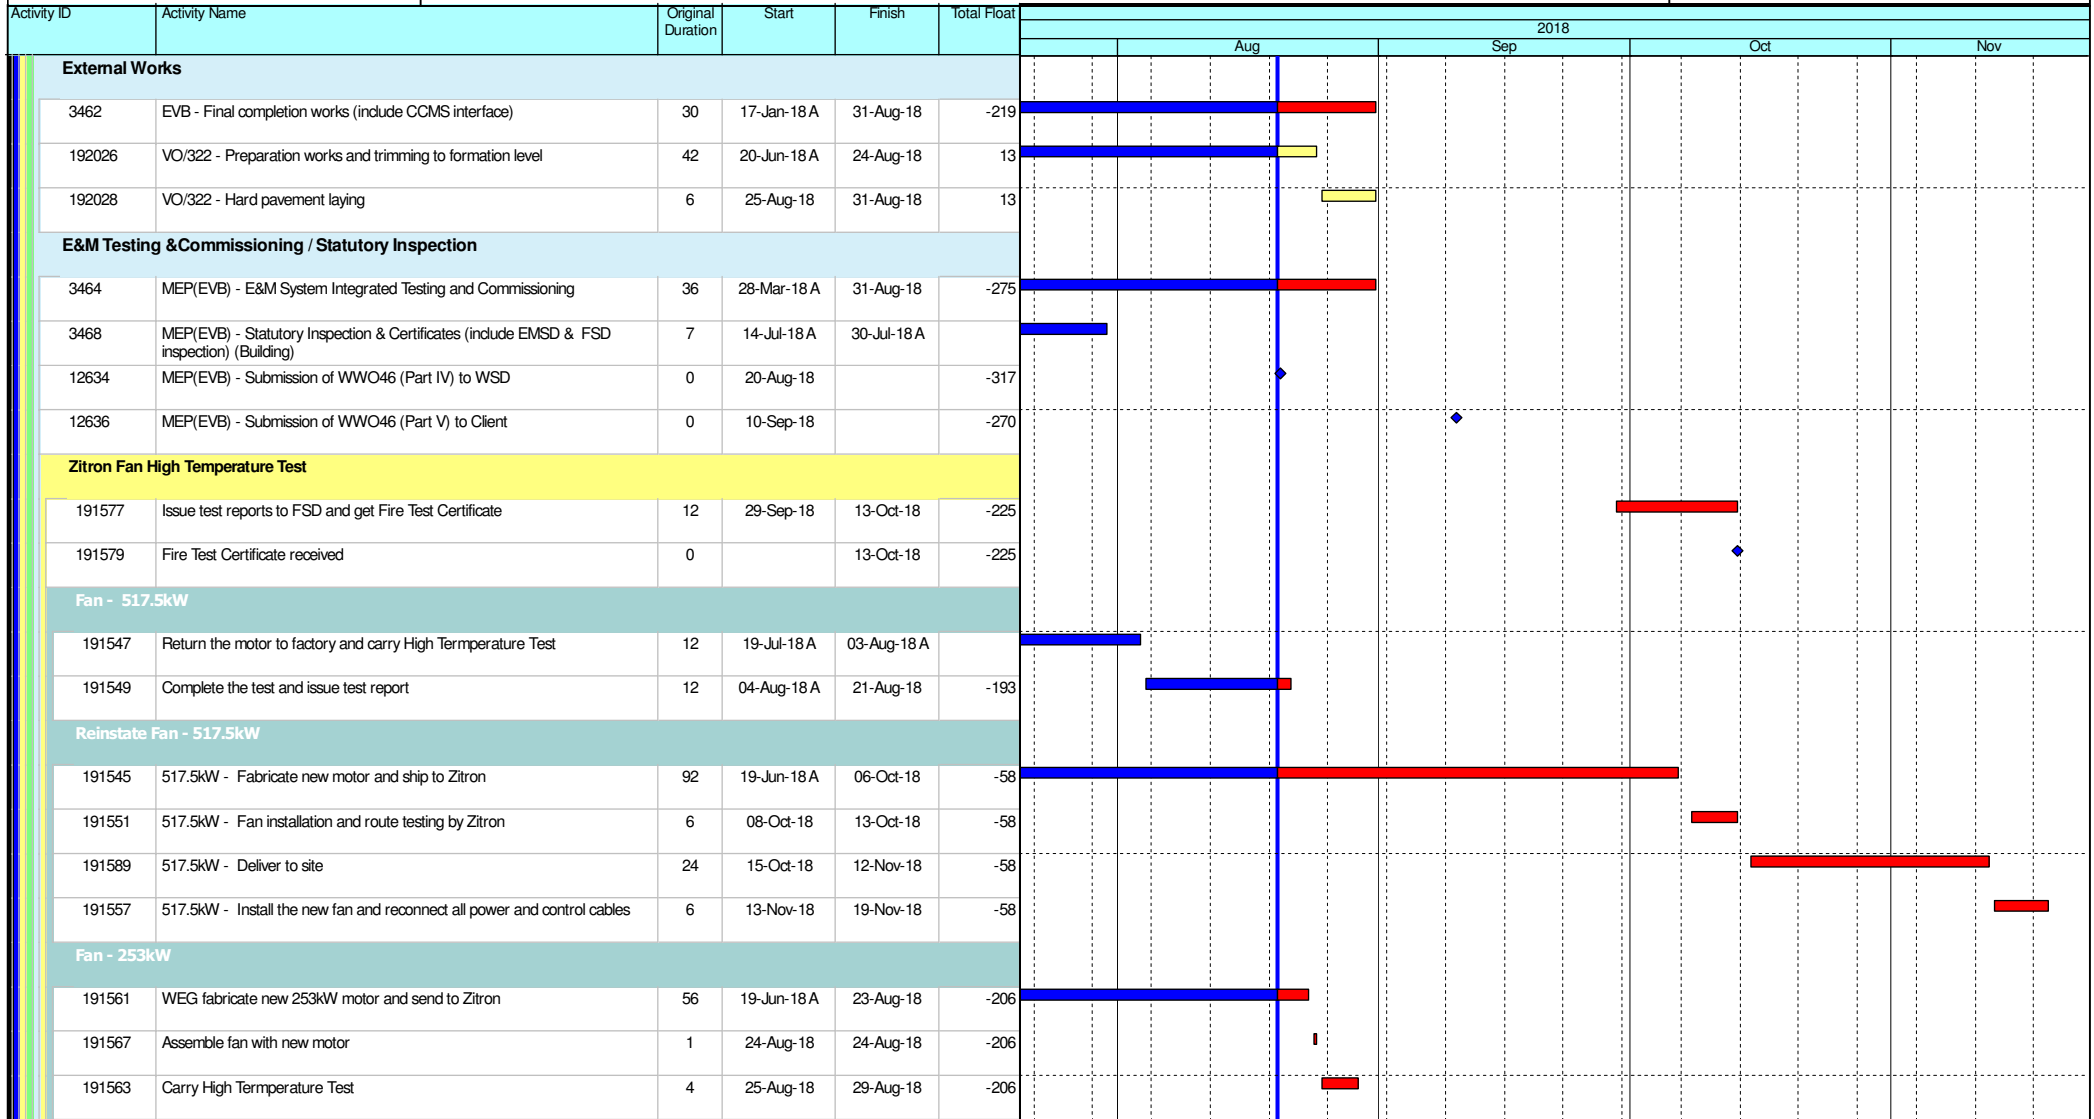

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 14 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

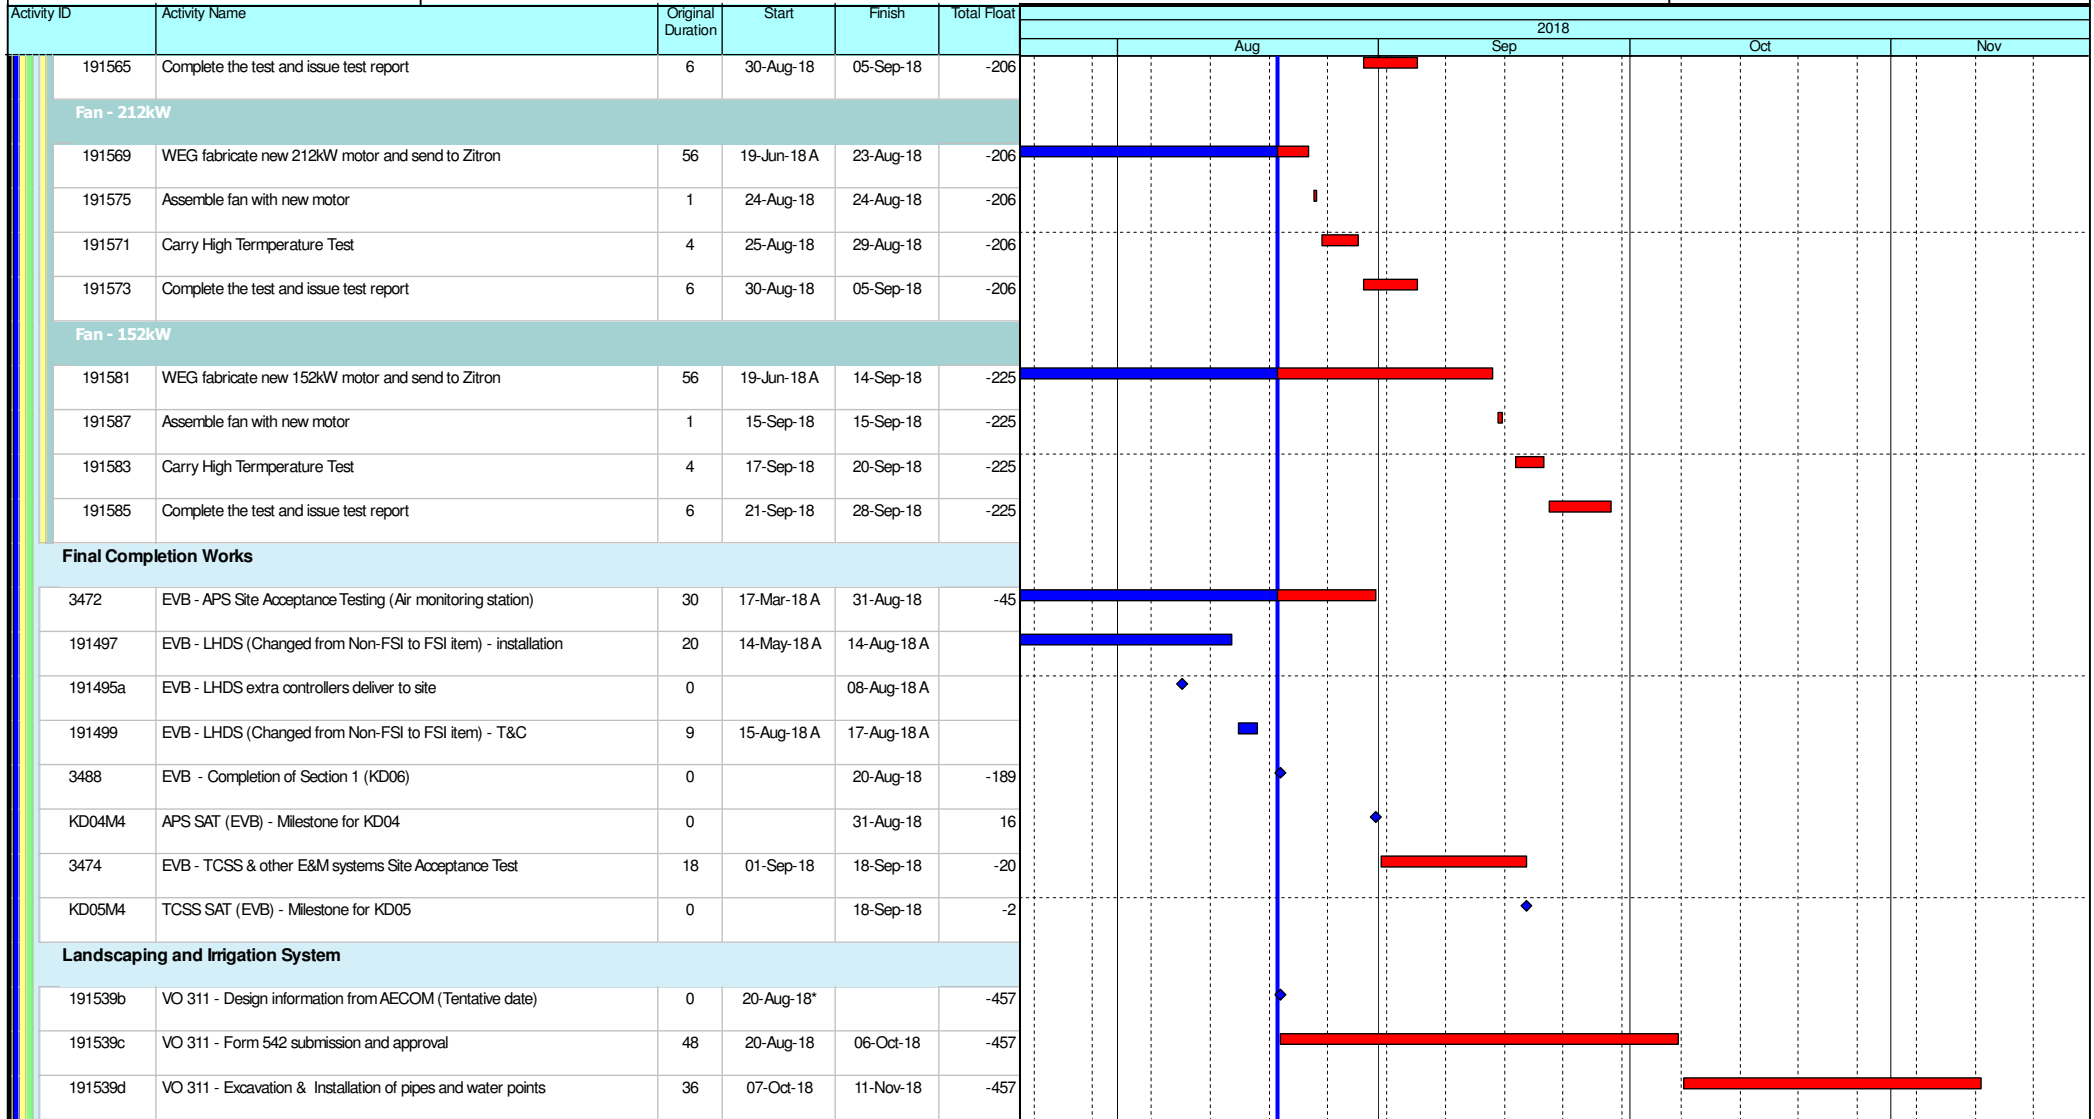

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 15 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

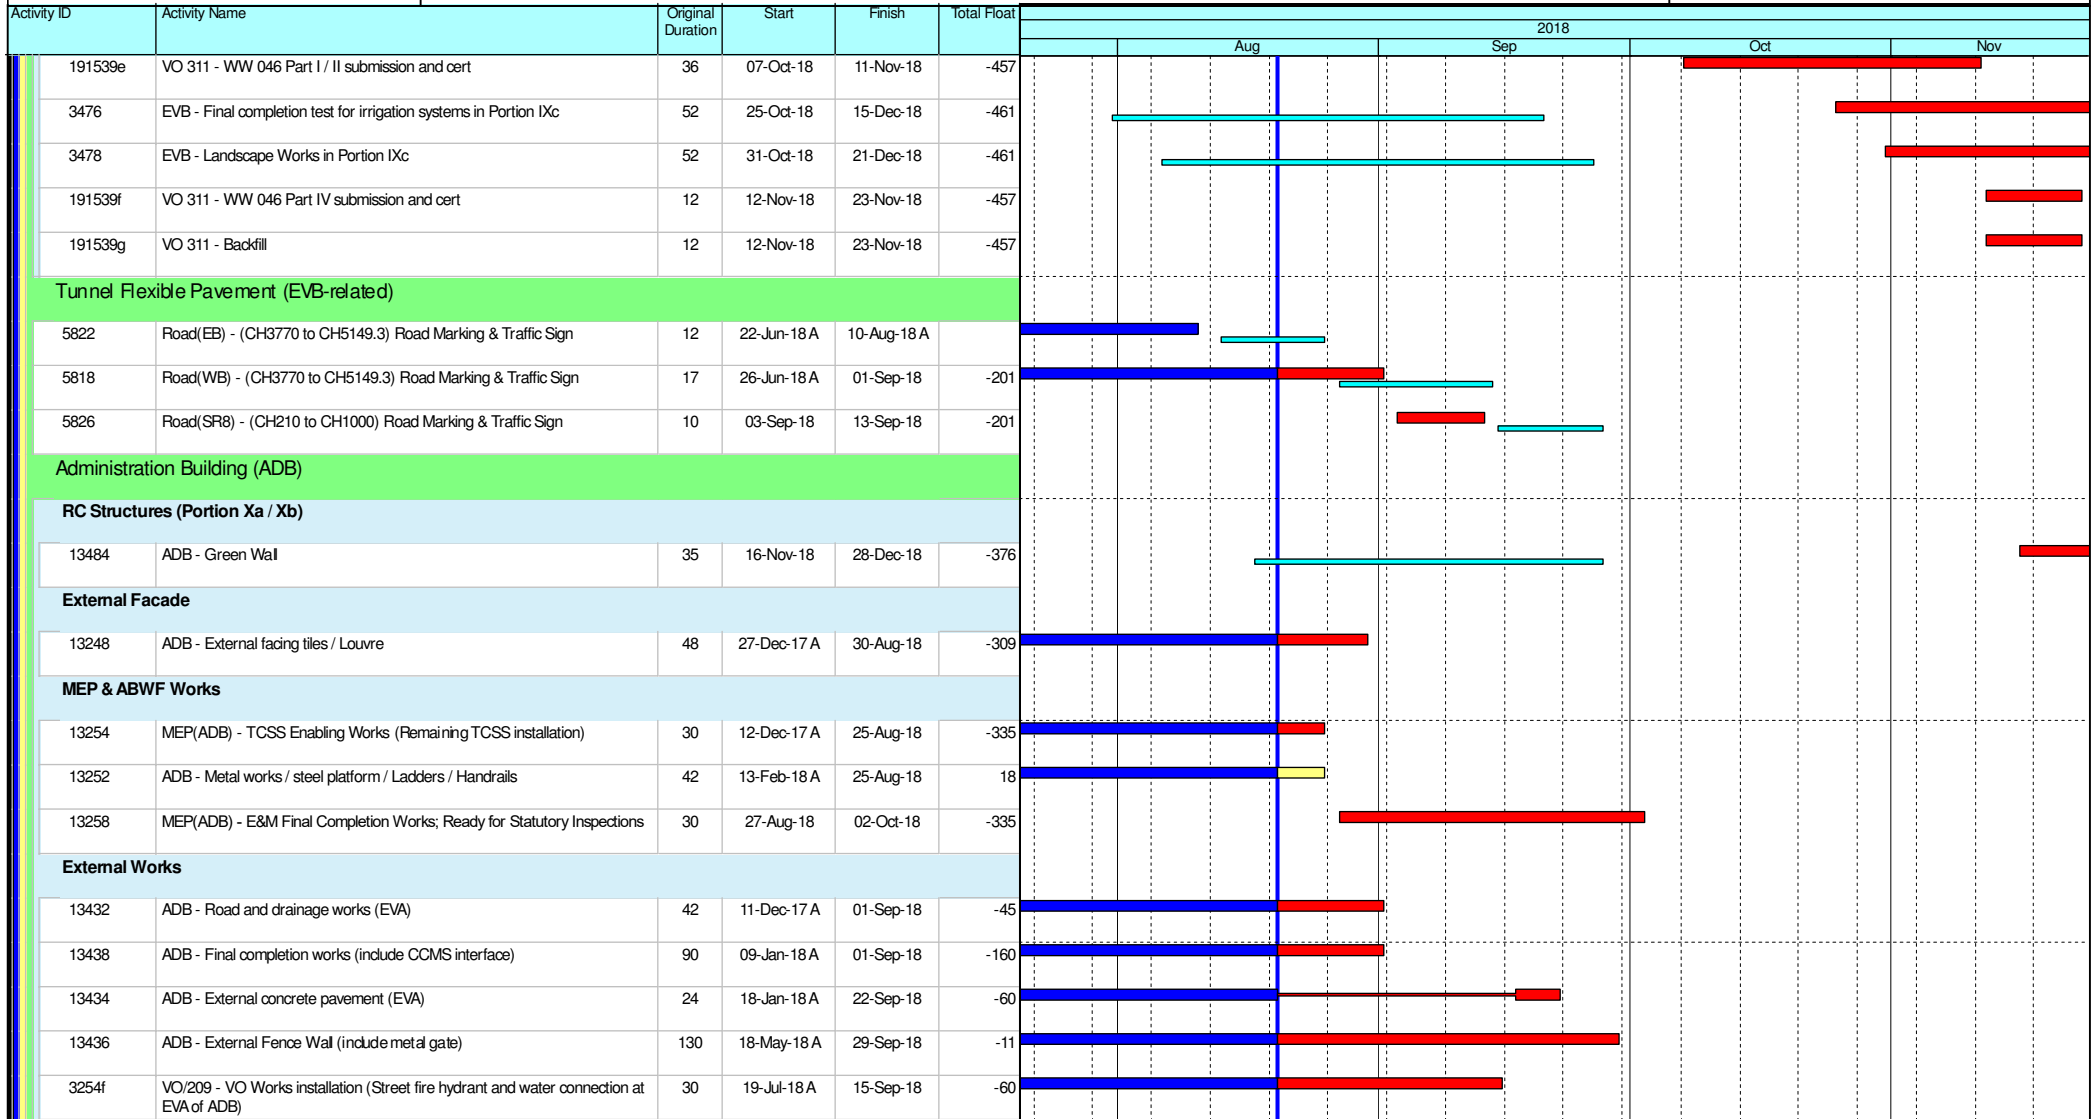

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 16 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

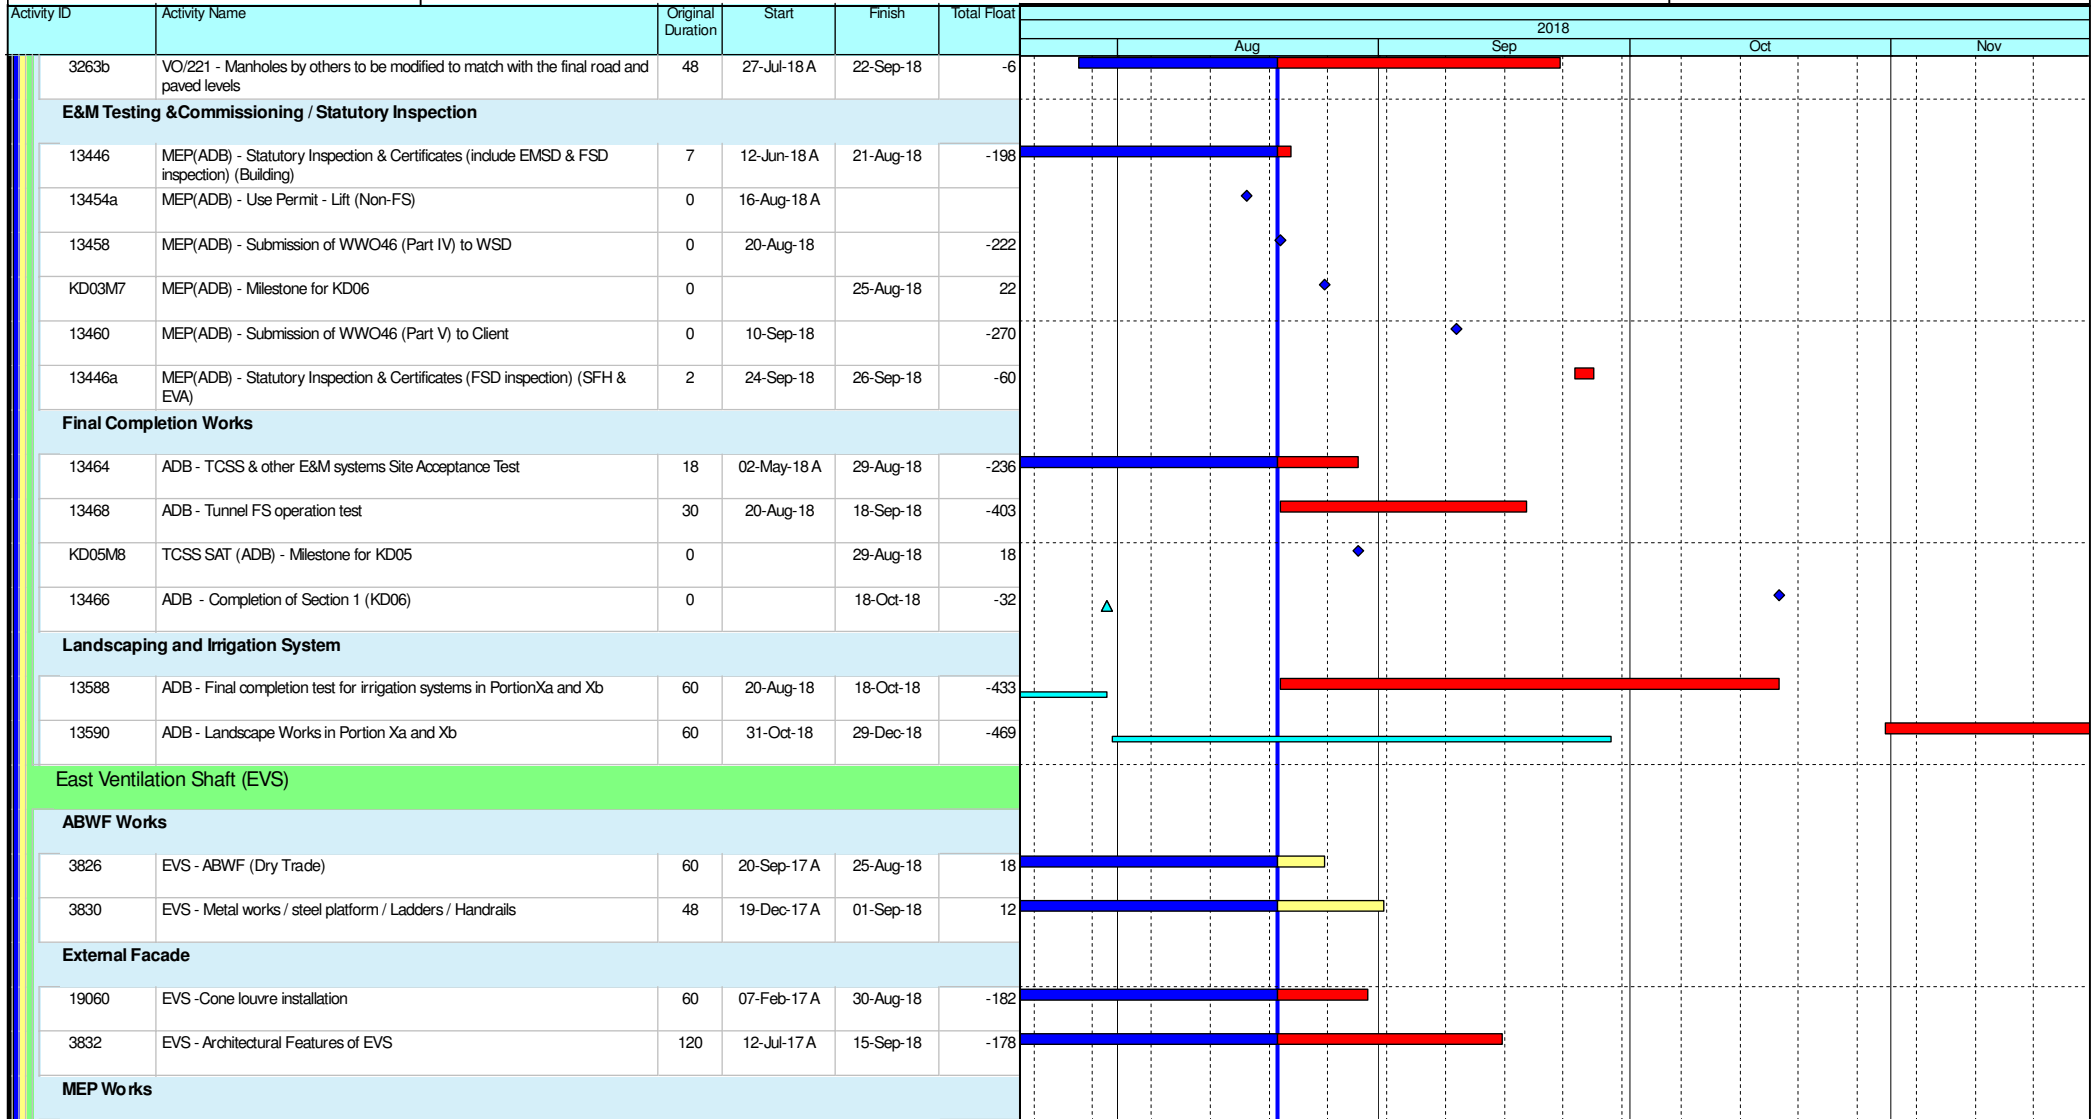

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 17 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

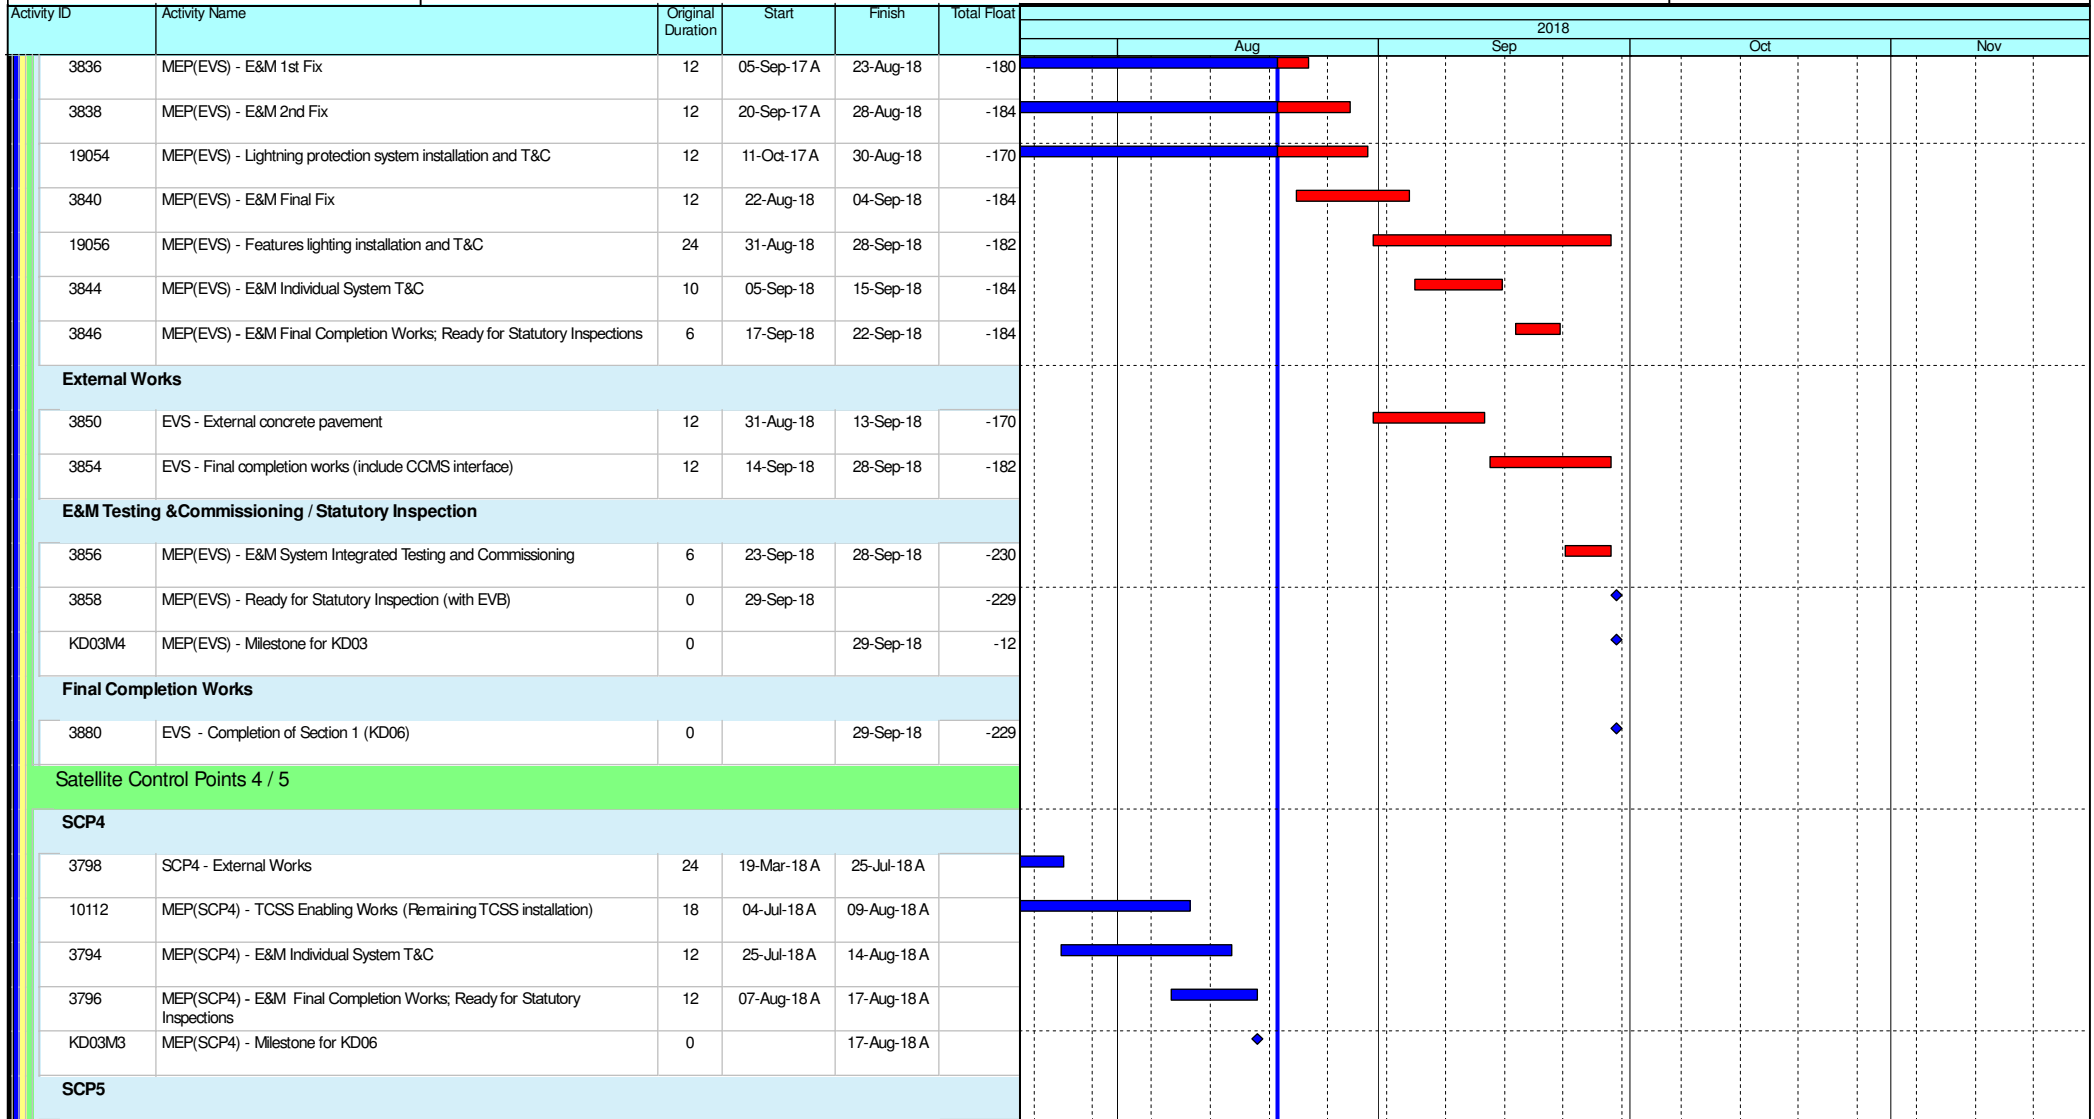

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 18 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Aug	Sep	Oct	Nov
3886	SCP5 - External Works	24	18-Jun-18 A	01-Sep-18	-211				
10114	MEP(SCP5) - TCSS Enabling Works (Remaining TCSS installation)	12	10-Jul-18 A	08-Aug-18 A					
3882	MEP(SCP5) - E&M Individual System T&C	12	20-Aug-18	01-Sep-18	-211				
3884	MEP(SCP5) - E&M Final Completion Works; Ready for Statutory Inspections	12	03-Sep-18	15-Sep-18	-211				
KD03M5	MEP(SCP5) - Milestone for KD06	0		15-Sep-18	0				
External Works									
Rumsey Street Flyover for Paymnet & Traffic Barrier									
5902b	RS - Modification of existing edge parapet at Connaught Road	108	05-Feb-18 A	31-Jul-18 A					
5902d	RS - Removal of central divider and replace with waterfilled barriers	120	10-Feb-18 A	31-Jul-18 A					
5902p	RS - Pavement tie-in works at CORC W/B	30	14-Aug-18 A	15-Sep-18	-215				
5902g	RS - Install new directional sign	6	17-Sep-18	22-Sep-18	-215				
5902r	RS - Road pavement tie-in E/B and W/B of CORC	6	24-Sep-18	02-Oct-18	-215				
5902q	RS - Road marking	6	24-Sep-18	02-Oct-18	-215				
5902m	RS - Demolish existing nosing and crush cushion	48	15-Oct-18	10-Dec-18	-141				
5904a	RS - Construct permanent parapet and nosing	102	15-Oct-18	21-Feb-19	-225				
5902n	RS - Paving works on Bridge B	12	30-Oct-18	12-Nov-18	-141				
Area A/B									
Area ATCSS									
10288a3	Request for VO/instruction-TCSS equipment installation & cabling (Gantries FVMS1 / ADS01) (Ref: H27613-LJV-ME-LE-4022)	24	04-Oct-16 A	25-Aug-18	-185				
Area B									
Area B TCSS									
Approach Road / Landscape Deck / Noise Enclosure (No TTA)									
10288b22	Area B TCSS cable termination (on IEC's Westbound) - DS06B	9	08-Jun-18 A	26-Jul-18 A					
10288b1	Area B TCSS equipment installation and cable termination (on IEC's Westbound) - GT3, GT2, Sm CCTV at Grade	18	13-Jun-18 A	15-Aug-18 A					

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 19 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Aug	Sep	Oct	Nov
10288b2	Area B TCSS equipment installation and cable termination (on IEC's Eastbound) - CCTV & AID	12	11-Jul-18 A	07-Aug-18 A					
10288b36	Area B cabling along existing IECL sign gantries/bridge F3B (C19 civil provision must be ready for cabling)	12	16-Jul-18 A	31-Jul-18 A					
10288b38	Area B cabling along existing IECL sign gantries/bridge F2B (C19 civil provision must be ready for cabling)	12	16-Jul-18 A	15-Aug-18 A					
10288b4	Area B TCSS equipment Testing & Commissioning	25	16-Aug-18 A	01-Sep-18	-203				
NOC 163 - Optical Fibre Damaged - Need to be Replaced (From Gantry ADS06 to ADB Computer Room)									
10288b14	TCSS optic fibre order and delivery	48	25-Jun-18 A	24-Aug-18	-191				
10288b14	Pull out damaged cable (Require TTA for 1 night shift)	2	25-Aug-18	27-Aug-18	-191				
10288b14	Lay the new cable from gantry ADS06 to ADB Computer room (Require TTA for 2 night shifts)	2	28-Aug-18	29-Aug-18	-191				
10288b14	Cable termination at ADB Computer Room (Require TTA for 2 night shifts)	2	30-Aug-18	31-Aug-18	-191				
Noise Enclosure (Live Traffic, TTA) - Night Shift									
10288b6	Area B TCSS equipment installation and cable termination (on IEC's Westbound) - FADS06	10	18-Jun-18 A	15-Aug-18 A					
10288b8	Area B TCSS equipment Testing & Commissioning	20	11-Jul-18 A	30-Aug-18	-201				
10288b10	Area B TCSS equipment installation and cable termination (on IEC's Eastbound) - FADS08A (Works deleted)	6	31-Jul-18 A	31-Jul-18 A					
Existing IEC (Live Traffic, TTA) - Night Shift									
10288b26	Area B TCSS equipment Testing & Commissioning	12	31-Aug-18	13-Sep-18	-201				
Area B Tunnel Lighting									
Landscape Deck (Bay C1 to C5)									
Landscape Deck (Bay C1 & C2A-2 Remaining Bay (W/B))									
10288c28	Cable laying / DALI wiring and cable termination	40	18-Jun-18 A	21-Jul-18 A					
10288c32	Handover to C19 for Asphalt pavement	6	23-Jul-18 A	29-Jul-18 A					
10288c30	T&C and energisation	6	20-Aug-18	25-Aug-18	-203				
10288c34	LUX measurement	18	27-Aug-18	15-Sep-18	-203				
Landscape Deck (Bay C1 & C2A-2 Remaining Bay (E/B))									
10288c40	Cable laying / DALI wiring and cable termination	40	12-Jun-18 A	04-Aug-18 A					

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 20 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Aug	Sep	Oct	Nov
10288c44	Handover to C19 for Asphalt pavement	6	23-Jul-18 A	29-Jul-18 A					
10288c42	T&C and energisation	3	16-Aug-18 A	25-Aug-18	-203				
10288c46	LUX measurement	18	27-Aug-18	15-Sep-18	-203				
Landscape Deck (Bay C2A-1 to B1 & C3 Bay (W/B))									
10288c54	T&C and energisation	6	20-Aug-18	25-Aug-18	-209				
10288c56	Handover to C19 for Asphalt pavement	6	27-Aug-18	01-Sep-18	-209				
10288c58	LUX measurement	18	03-Sep-18	22-Sep-18	-209				
Landscape Deck (Bay C2A-1 to B1 & C3 Bay (E/B))									
10288c68	T&C and energisation	6	20-Aug-18	25-Aug-18	-209				
10288c70	Handover to C19 for Asphalt pavement	6	27-Aug-18	01-Sep-18	-209				
10288c72	LUX measurement	18	03-Sep-18	22-Sep-18	-209				
Landscape Deck (Bay C4 - E/B Slow Lane)									
10288c80	Cable laying / DALI wiring and cable termination	24	11-Jul-18 A	21-Aug-18	-211				
10288c82	T&C and energisation	6	22-Aug-18	28-Aug-18	-211				
10288c90	Handover to C19 for ADS08A sign face installation / Asphalt pavement	18	29-Aug-18	18-Sep-18	-211				
10288c86	LUX measurement	6	19-Sep-18	26-Sep-18	-211				
Landscape Deck (Bay C4 - E/B Fast Lane)									
10288c96	Cable laying / DALI wiring and cable termination	30	13-Jul-18 A	18-Aug-18 A					
10288c104	Lighting / Conduit installation (continue)	6	24-Jul-18 A	30-Jul-18 A					
10288c98	T&C and energisation	6	19-Aug-18 A	25-Aug-18	-203				
10288c100	LUX measurement	18	27-Aug-18	15-Sep-18	-203				
Landscape Deck (Bay C4 - W/B)									
10288c110	Cable laying / DALI wiring and cable termination	36	17-Jul-18 A	25-Aug-18	-209				
10288c150	C19 - Remaining works / Asphalt Paving and Road Marking	24	20-Aug-18	15-Sep-18	-215				

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 21 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

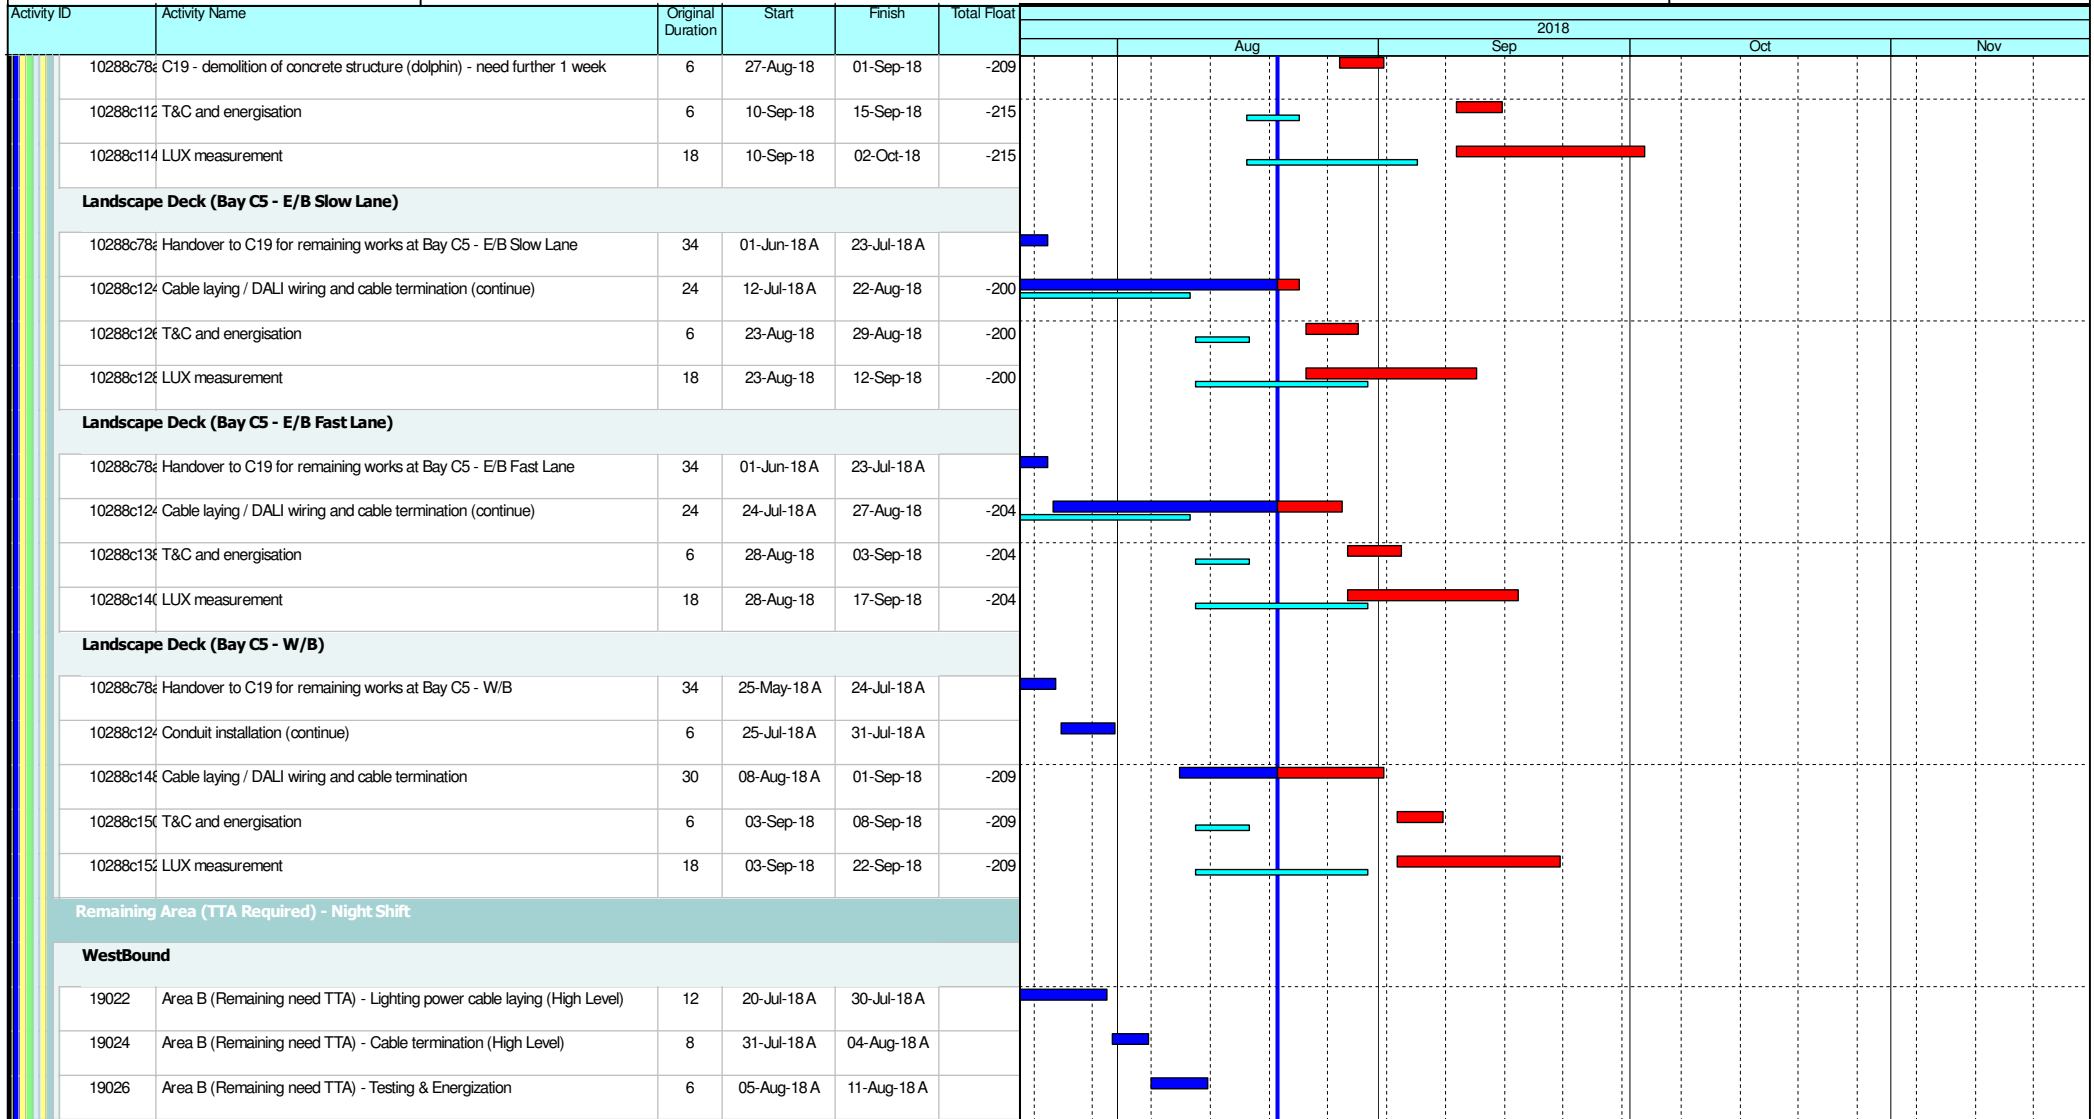

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 22 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

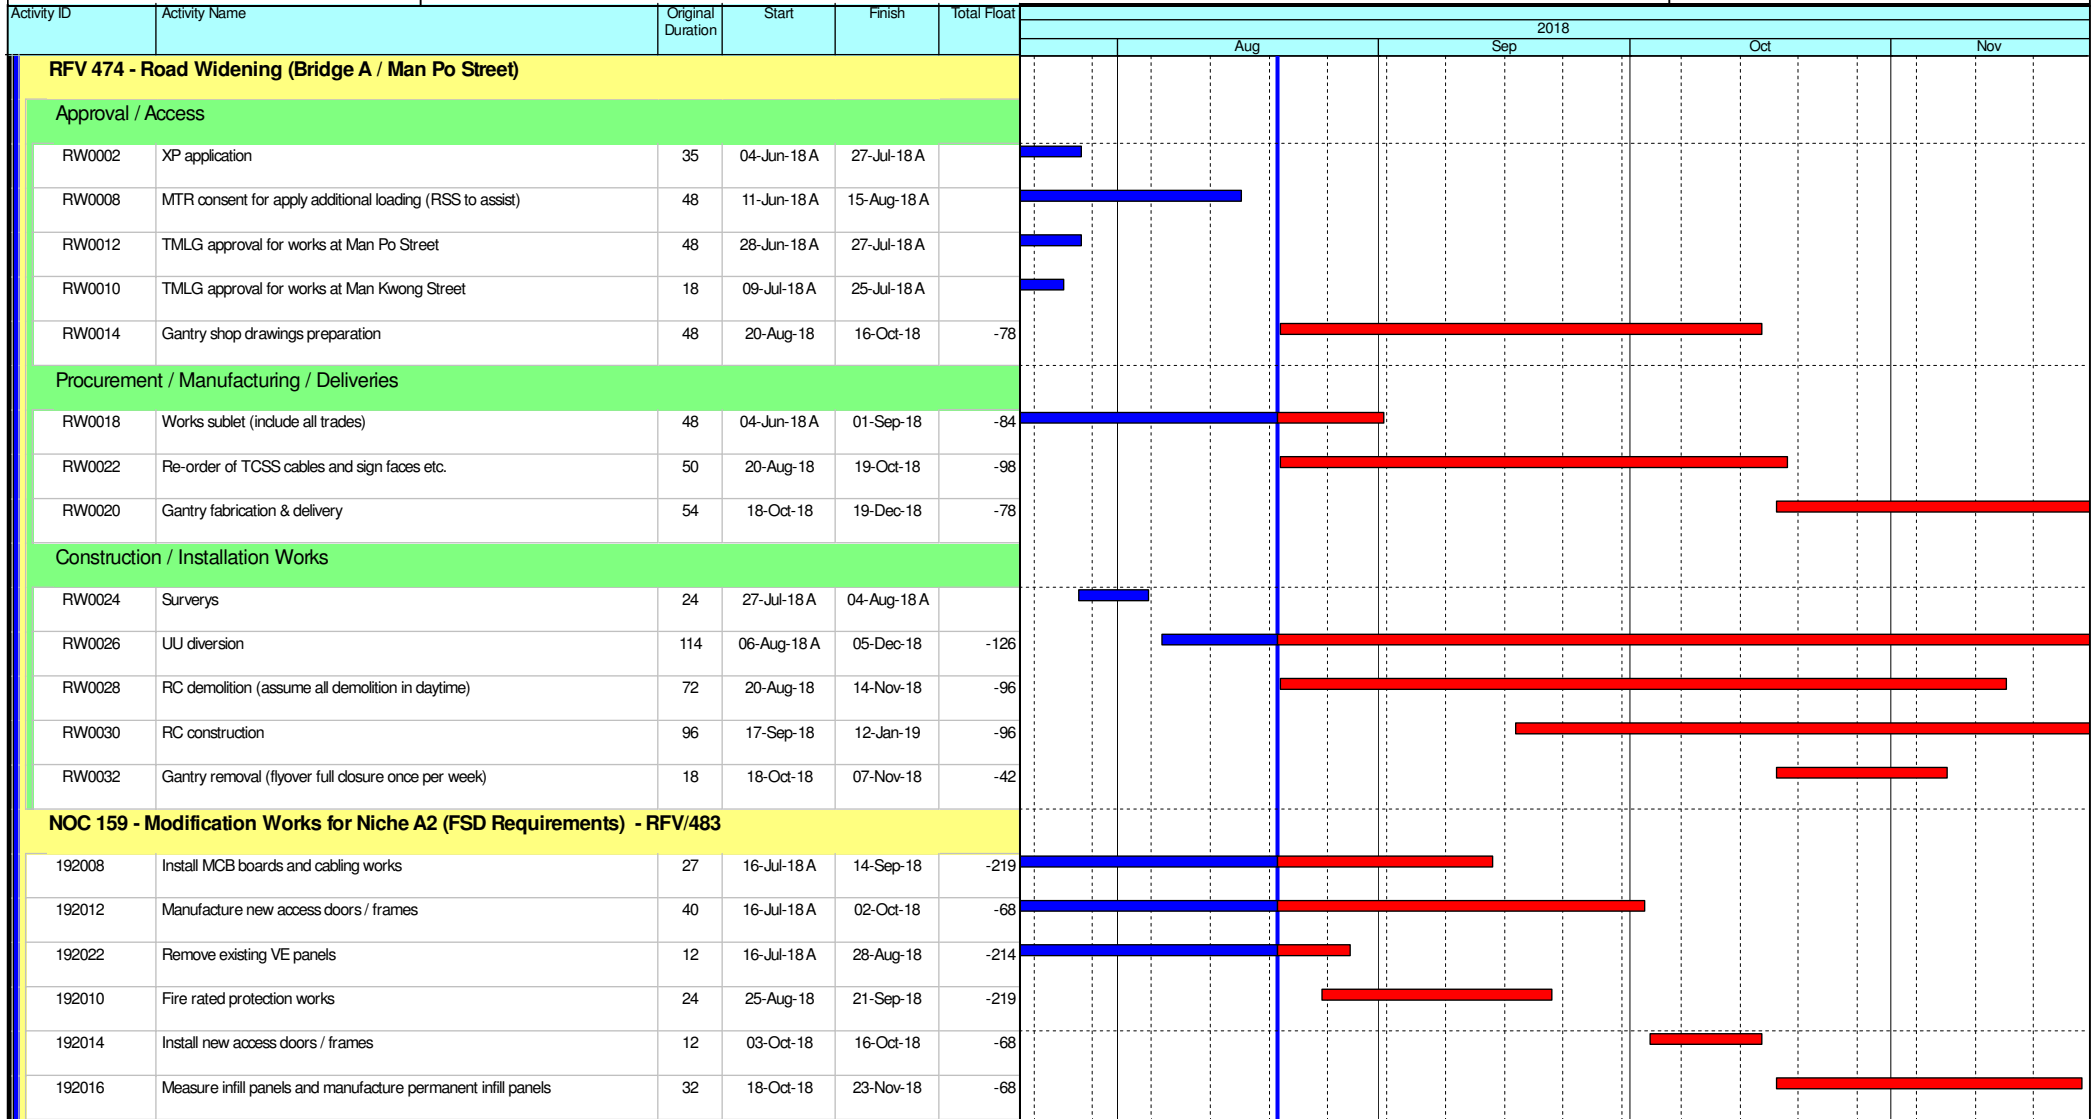

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
Baseline: DWP4
Layout: Update Three Month Rolling
U054
Page 23 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

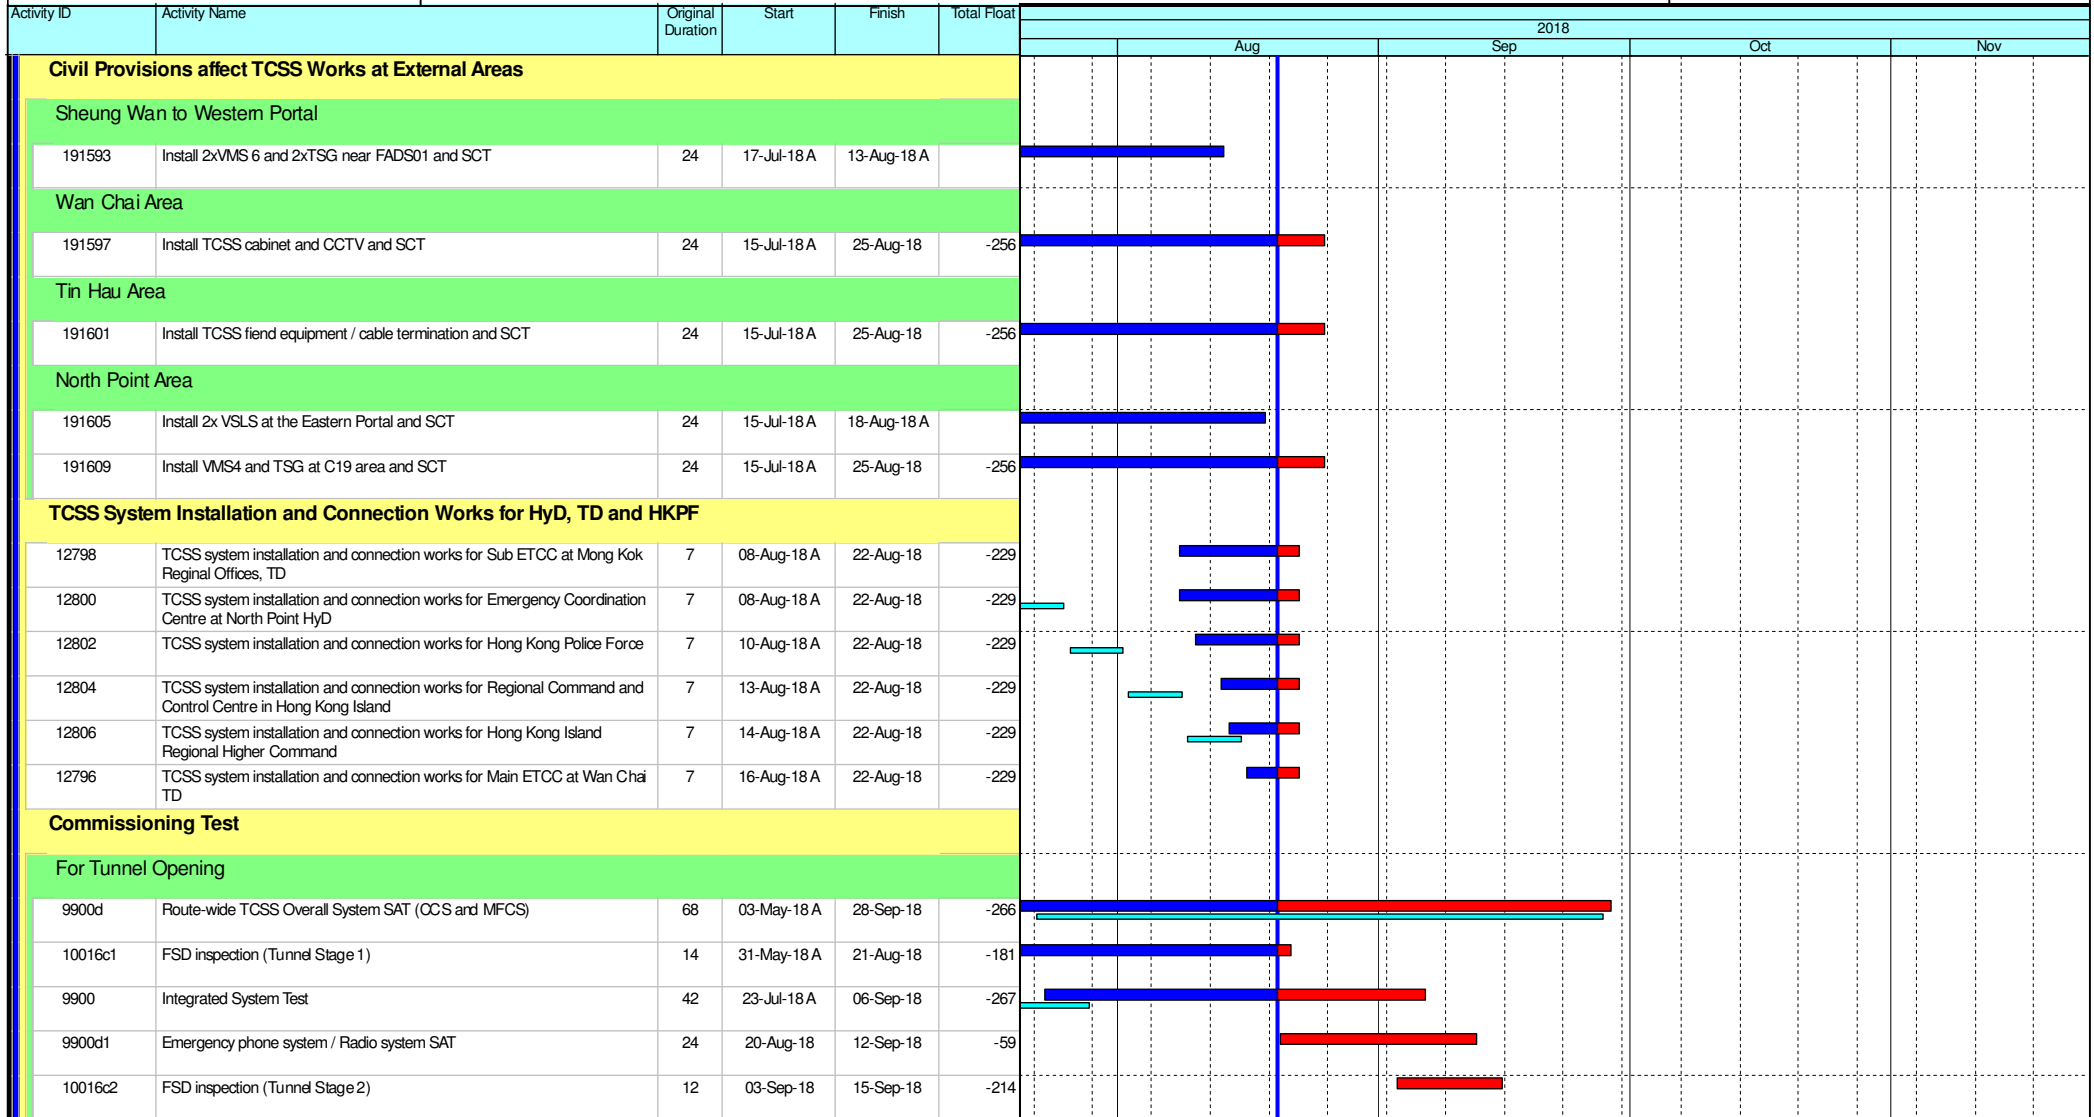

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
Baseline: DWP4
Layout: Update Three Month Rolling
U054
Page 24 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

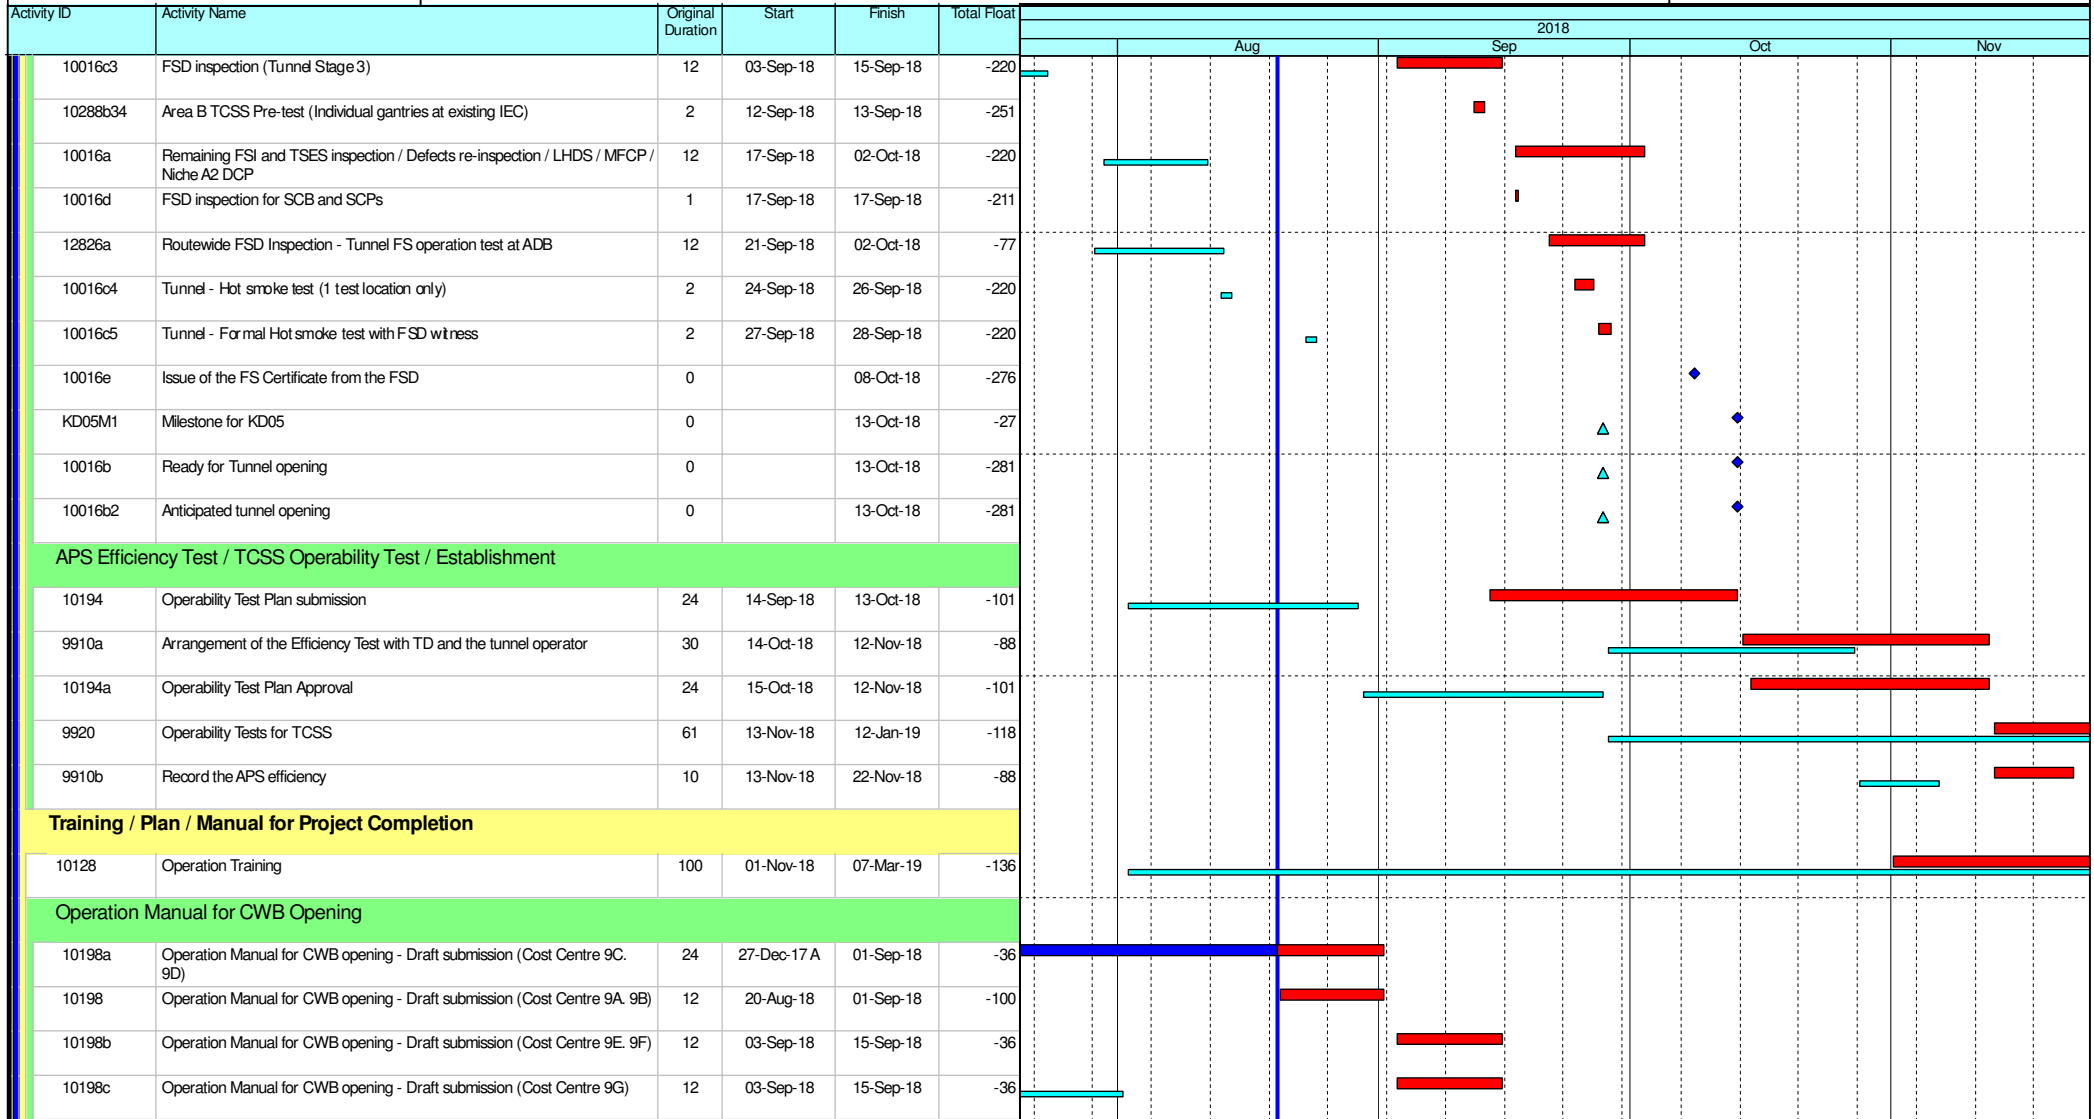

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 25 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

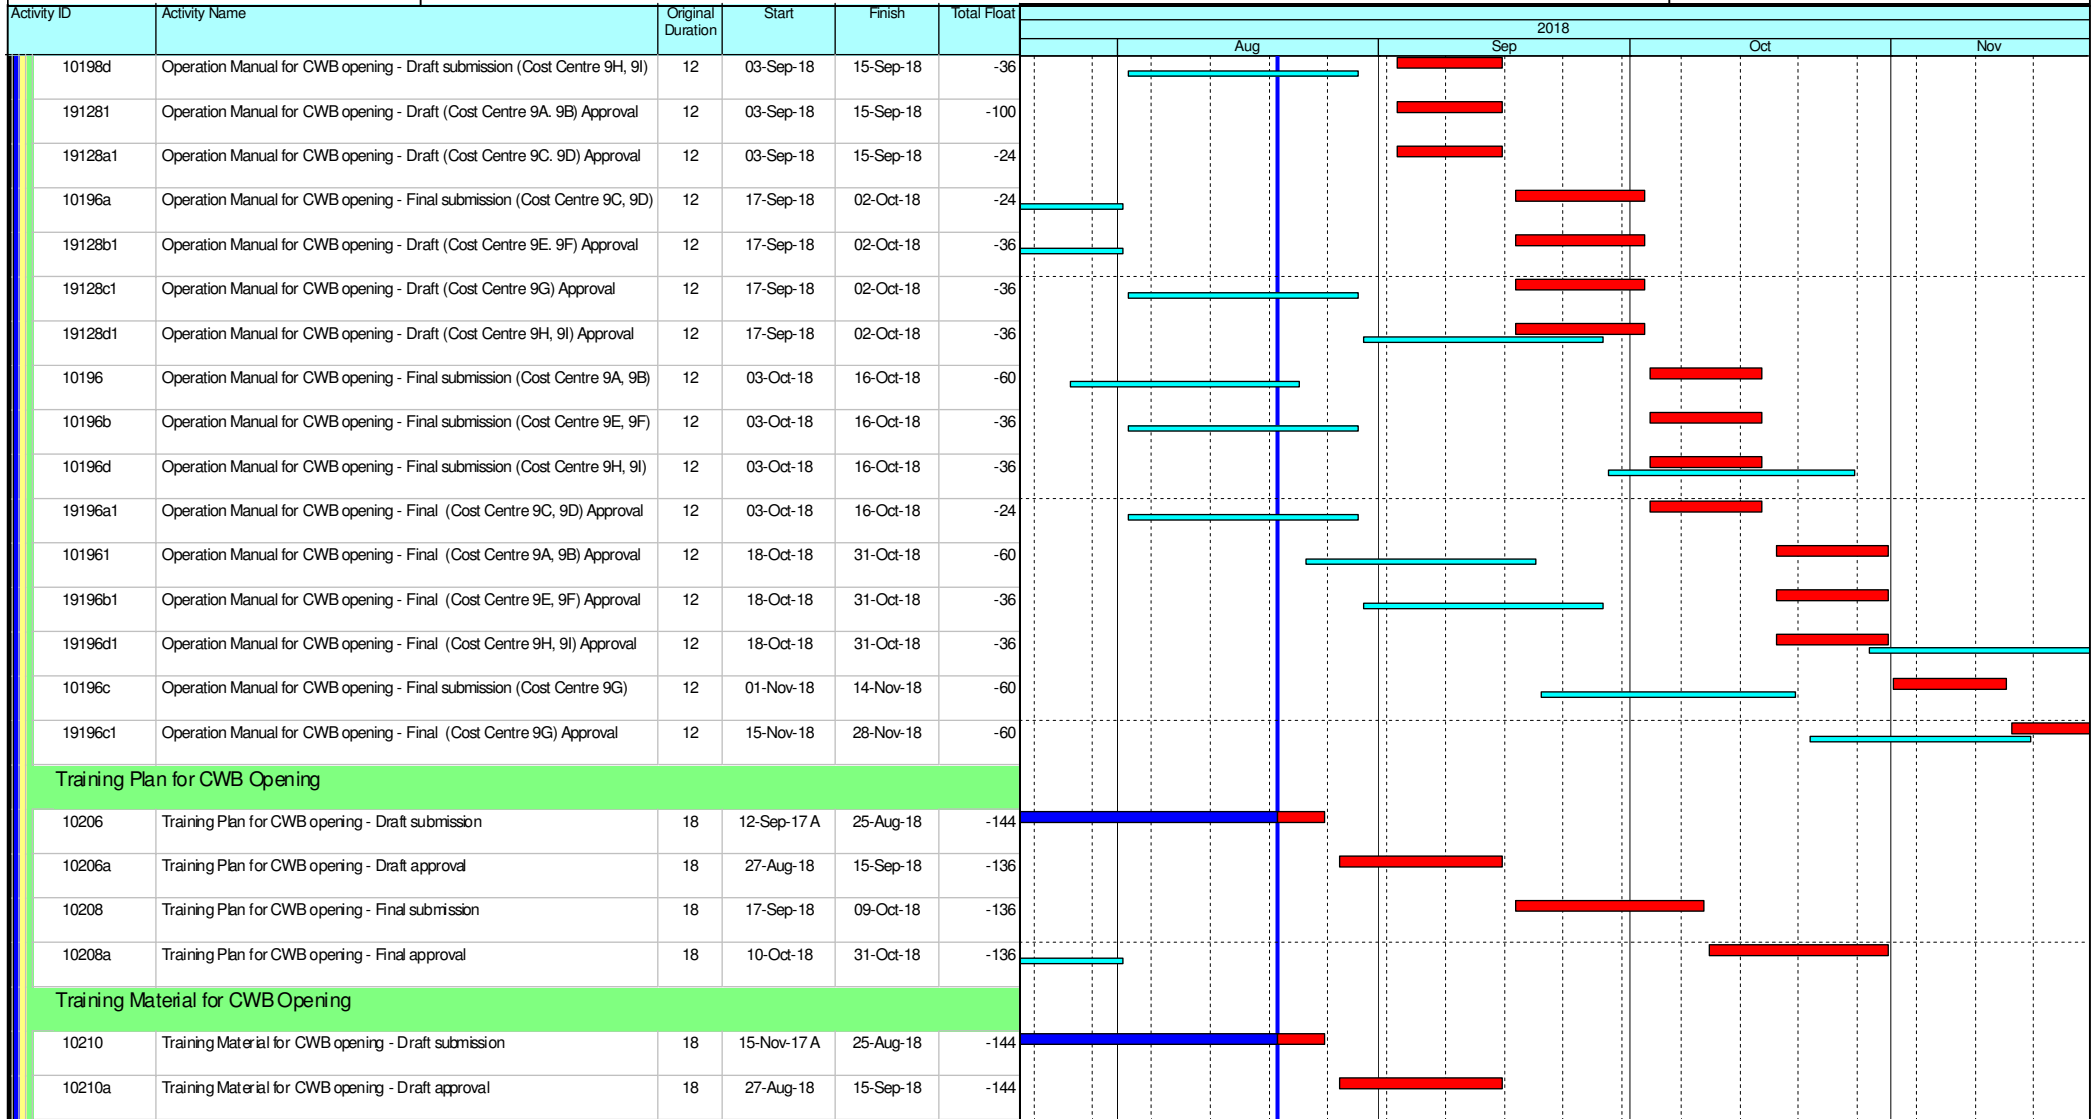

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 26 of 27








Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018																
						Aug			Sep			Oct			Nov							
						1	2	3	1	2	3	1	2	3	1	2	3					
10212	Training Material for CWB opening - Final submission	18	17-Sep-18	09-Oct-18	-144																	
10212a	Training Material for CWB opening - Final approval	18	10-Oct-18	31-Oct-18	-136																	
Maintenance Manual / Plan																						
10200	Maintenance Plan	18	10-Oct-18	31-Oct-18	-144																	
10220	Maintenance Manual / logbook - Draft submission	18	01-Nov-18	21-Nov-18	-144																	

-  Current Milestone
-  Level of Effort
-  Baseline Milestone
-  Actual Work
-  Critical Remaining Work
-  Remaining Work
-  Project Baseline

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 27 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW
