












**CEDD Contract No. HK/2012/08  
Wan Chai Development Phase II  
Central - Wan Chai Bypass at Wan Chai West**

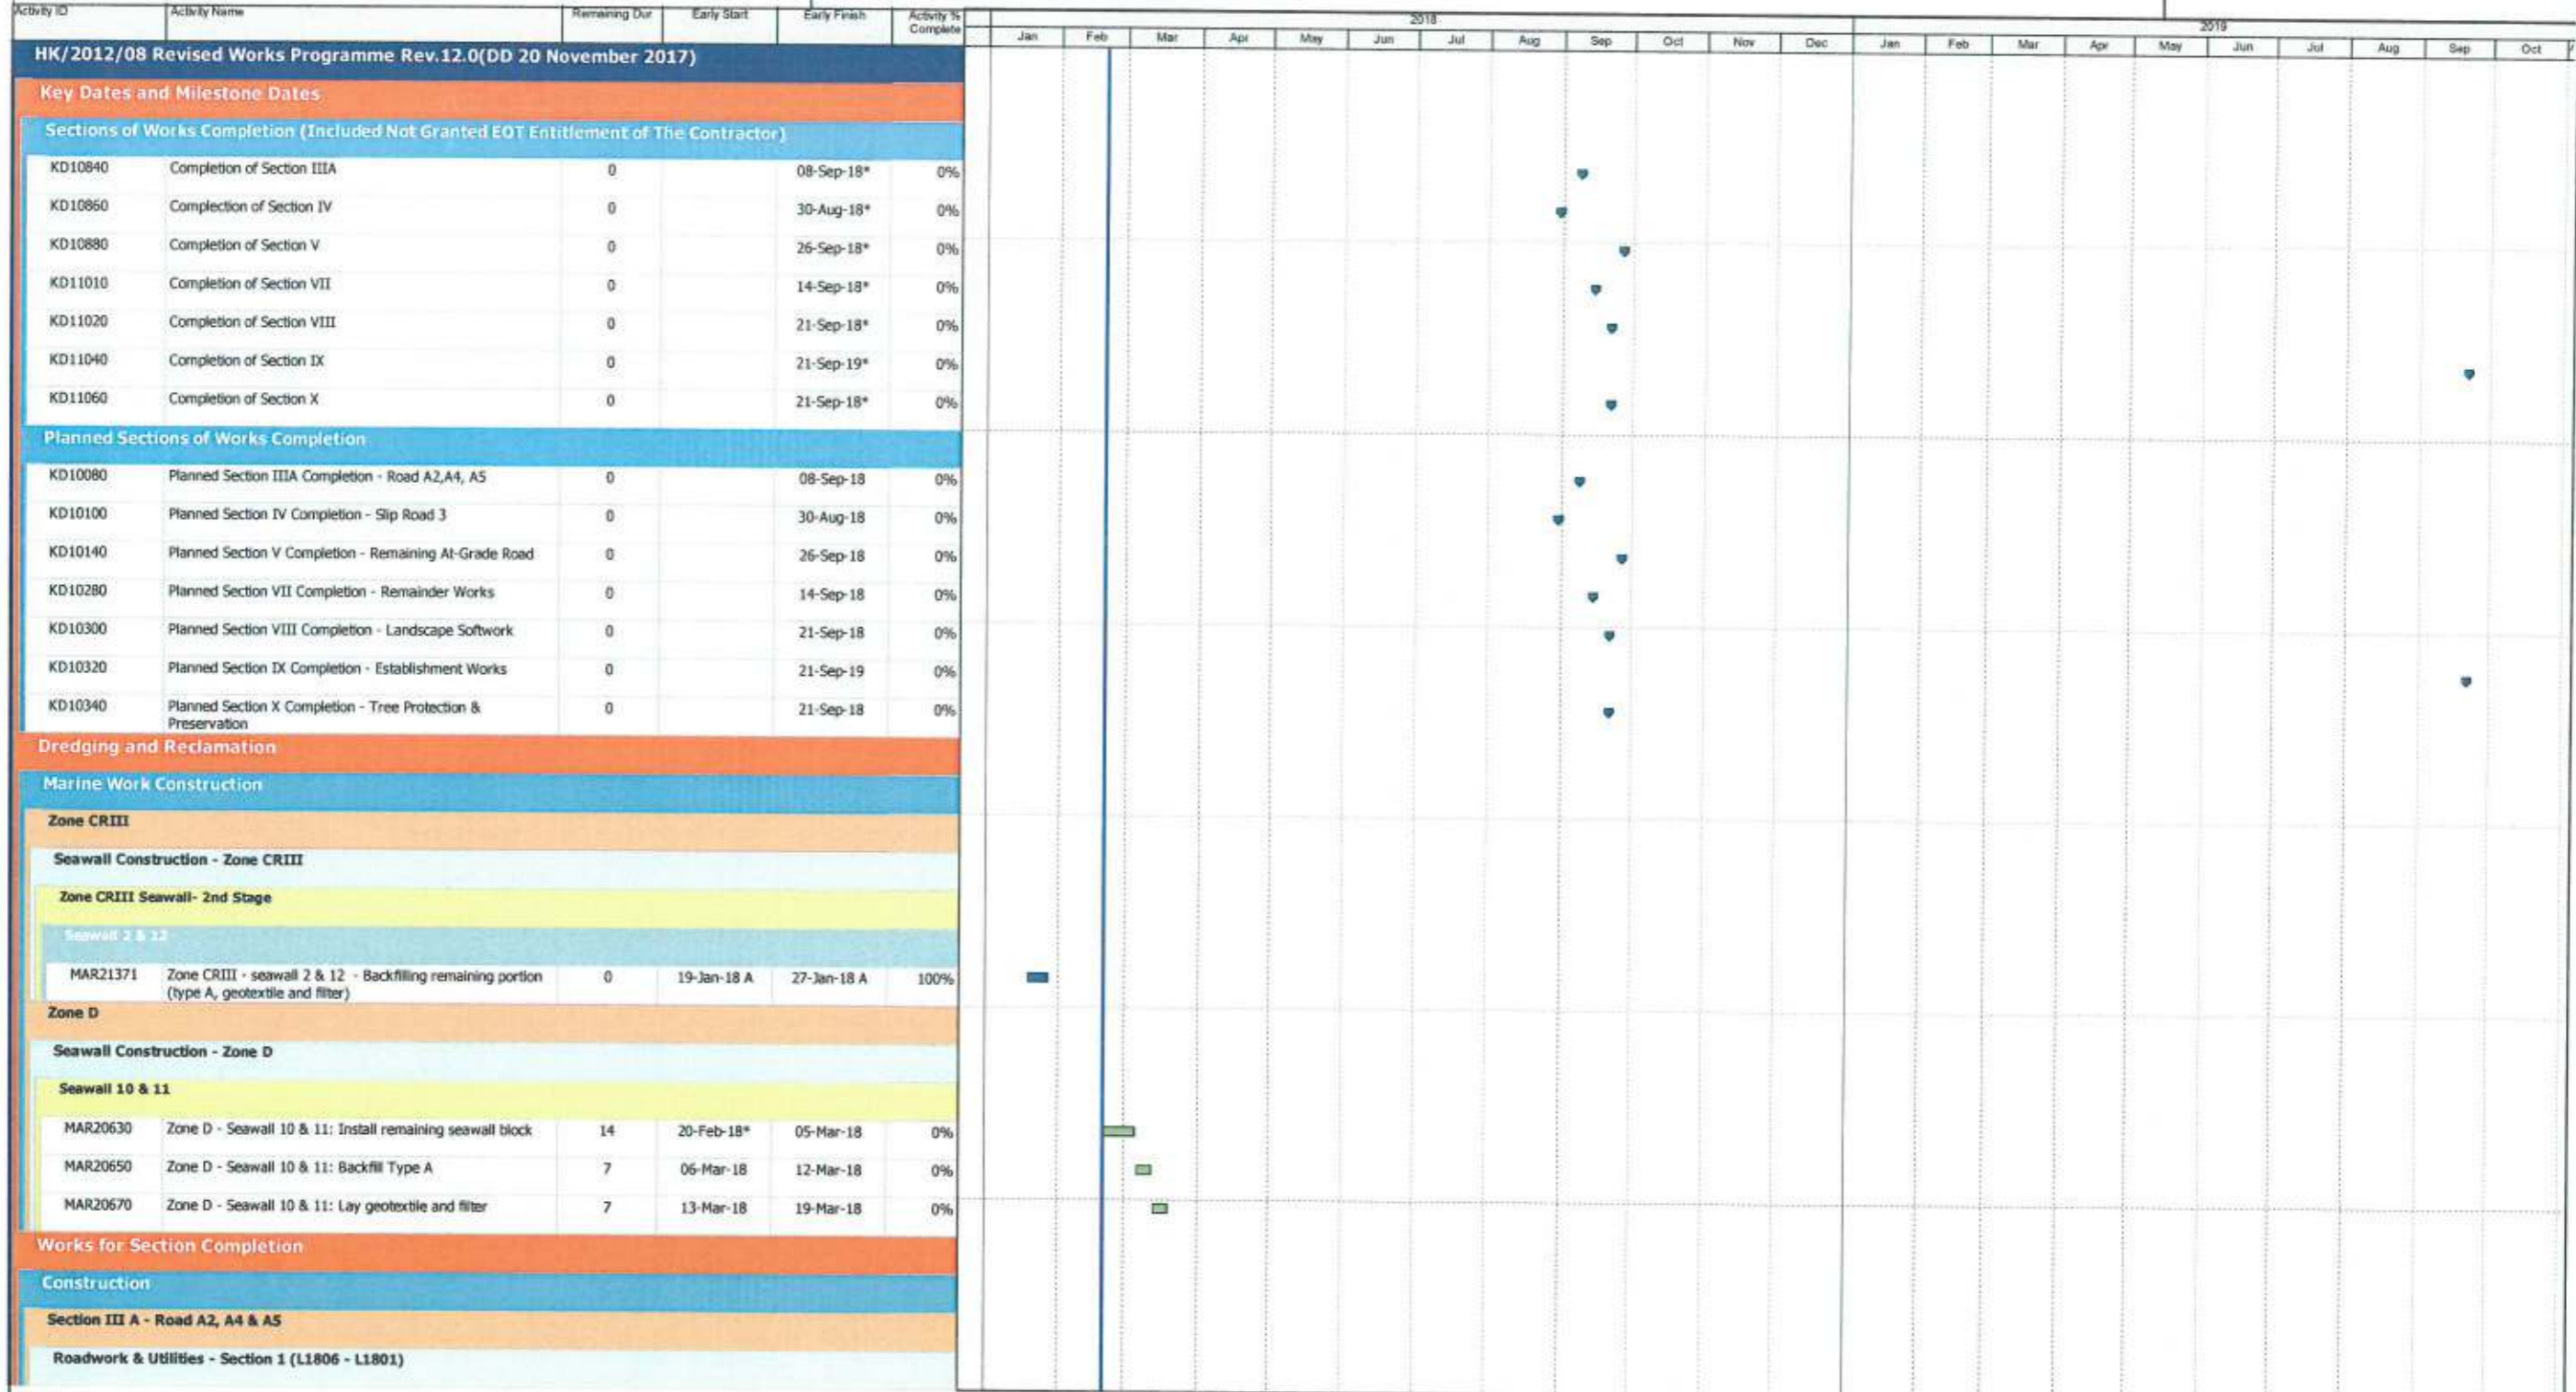

Data Date: 20-Feb-18

- ◆ Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Remaining Level of Effort

**Updated Works Programme Rev.12  
(Ref. to Rev.12 as of 20 Febuary 2018)**

Date	Revision	Checked	Approved
20-Feb-18	12		

**CEDD Contract No. HK/2012/08  
Wan Chai Development Phase II  
Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019											
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
SIIIA10279c	Sec III A - section 1 carriageway - sewerage pipe from M/H 8C to F8B (night time): construct sewerage pipe	0	02-Jan-18 A	03-Feb-18 A	100%																								
SIIIA10293	Sec III A - section 1 carriageway - sewerage pipe from M/H F8B - F8A (night time)	6	05-Feb-18 A	26-Feb-18	0%																								
SIIIA10294	Sec III A - section 1 carriageway - sewerage pipe from M/H F8A - F8	8	17-Jan-18 A	28-Feb-18	27.27%																								
SIIIA10295	Sec III A - carriageway - works prior TTA stage 5: excavation and duct laying of TCSS and public lighting	7	18-Jan-18 A	27-Feb-18	0%																								
SIIIA10298	Sec III A - section 1 carriageway - works prior TTA stage 5: road kerb	5	28-Feb-18	05-Mar-18	0%																								
SIIIA10301	Sec III A - section 1 carriageway - works prior TTA stage 5: road formation	2	06-Mar-18	07-Mar-18	0%																								
SIIIA10302	Sec III A - section 1 carriageway - works prior TTA stage 5: laying asphalt	5	08-Mar-18	13-Mar-18	0%																								
SIIIA10303	Sec III A - section 1 carriageway - works prior TTA stage 5: road marking & preparation works	3	14-Mar-18	16-Mar-18	0%																								
SIIIA10310	Sec III A - section 1 carriageway - TTA stage 5: Implementation of TTA Stage 5	1	17-Mar-18	17-Mar-18	0%																								
SIIIA10310a	Sec III A - section 1 carriageway - TTA stage 5: remaining sewerage pipe for M/H F8A - M/H F8	12	19-Mar-18	04-Apr-18	0%																								
SIIIA10310b	Sec III A - section 1 carriageway - TTA stage 5: remaining sewerage pipe for M/H F8A - M/H F8B	18	06-Apr-18	26-Apr-18	0%																								
SIIIA10310c	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - remove sheetpile at U-trough west	5	19-Mar-18	23-Mar-18	0%																								
SIIIA10310d	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - remove temp. road access bay 5 of SR1	21	24-Mar-18	21-Apr-18	0%																								
SIIIA10310e	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - construct upstand wall above Dwall	25	23-Apr-18	23-May-18	0%																								
SIIIA10310f	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - roadside barrier	14	24-May-18	08-Jun-18	0%																								
SIIIA10310g	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - road formation	7	09-Jun-18	16-Jun-18	0%																								
SIIIA10310h	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - laying asphalt with transition slab	14	19-Jun-18	05-Jul-18	0%																								
SIIIA10312	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L2202 - L2201)	15	19-Mar-18	09-Apr-18	0%																								
SIIIA10312a	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L1805 - L1801)	15	10-Apr-18	26-Apr-18	0%																								
SIIIA10312b	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L1805-1807)	12	27-Apr-18	11-May-18	0%																								
SIIIA10313	Sec III A - roadwork and utilities section 1 carriageway - gully pipe (L1807 - L1801)	14	07-May-18	23-May-18	0%																								
SIIIA10320	Sec III A - roadwork and utilities section 1 carriageway - fresh watermain	7	24-May-18	31-May-18	0%																								
SIIIA10340	Sec III A - roadwork and utilities section 1 carriageway - utilities: HEC (80m) along carriageway	14	01-Jun-18	16-Jun-18	0%																								
SIIIA10360	Sec III A - roadwork and utilities section 1 carriageway - road kerb & formation	14	19-Jun-18	05-Jul-18	0%																								
SIIIA10400	Sec III A - roadwork and utilities section 1 carriageway - black top	7	06-Jul-18	13-Jul-18	0%																								
SIIIA10420	Sec III A - Implementation of TTA Stage 7P (Closure of U-turn at Expo Drive)	1	14-Jul-18	14-Jul-18	0%																								
SIIIA10440	Sec III A - roadwork and utilities section 1 carriageway : breaking existing asphalt	10	16-Jul-18	26-Jul-18	0%																								
SIIIA10460	Sec III A - roadwork and utilities section 1 carriageway: road kerb and formation	14	27-Jul-18	11-Aug-18	0%																								
SIIIA10480	Sec III A - roadwork and utilities section 1 carriageway : black top	10	13-Aug-18	23-Aug-18	0%																								
SIIIA10500	Sec III A - roadwork and utilities section 1 carriageway : roadmarking and road furniture	14	24-Aug-18	08-Sep-18	0%																								
<b>Roadwork &amp; Utilities - Section 2 (L1810 - L1807)</b>																													
SIIIA12590	Sec III A - roadwork and utilities section 2 carriageway - black top	0	20-Jan-18 A	27-Jan-18 A	100%																								
<b>Roadwork &amp; Utilities - Section 3 (L1808 - L1102)</b>																													
SIIIA12770	Sec III A - roadwork and utilities section 3 carriageway - utilities: HEC ducting (60m) & crossroad duct (PCCW & HGC)	0	20-Jan-18 A	07-Feb-18 A	100%																								
SIIIA12790	Sec III A - roadwork and utilities section 3 carriageway - road kerb & formation	17	08-Feb-18 A	10-Mar-18	0%																								
SIIIA12810	Sec III A - roadwork and utilities section 3 carriageway - black top	7	12-Mar-18	19-Mar-18	0%																								
<b>Roadwork &amp; Utilities - Section 6 (L1102 - L1411)</b>																													
SIIIA13399	Sec III A - roadwork and utilities section 6 carriageway - gully pipe (L1101 - L1102)	0	12-Jan-18 A	26-Jan-18 A	100%																								
SIIIA13444	Sec III A - roadwork and utilities section 6 carriageway - watermain (road crossing)	0	27-Jan-18 A	03-Feb-18 A	100%																								
SIIIA13445	Sec III A - roadwork and utilities section 6 carriageway - utilities: crossed duct(HEC, HGC, PCCW)	13	05-Feb-18 A	06-Mar-18	0%																								








**CEDD Contract No. HK/2012/08  
Wan Chai Development Phase II  
Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019											
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
						(Gantt chart grid with month labels)																							
SIV12121	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Drainage Works (M1.6-C1.1-C1.2): Backfilling & shift lane	6	16-May-18	23-May-18	0%	[Gantt bar from 16-May-18 to 23-May-18]																							
SIV12122	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Drainage Works (M1.6-C1.1-C1.2): Construct MH C1.2	5	24-May-18	29-May-18	0%	[Gantt bar from 24-May-18 to 29-May-18]																							
SIV12140	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Gully pipe (M/H 1.7 - L2301)	32	10-Apr-18	17-May-18	0%	[Gantt bar from 10-Apr-18 to 17-May-18]																							
SIV12150	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Road kerb	14	18-May-18	04-Jun-18	0%	[Gantt bar from 18-May-18 to 04-Jun-18]																							
SIV12155	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - formation	10	05-Jun-18	15-Jun-18	0%	[Gantt bar from 05-Jun-18 to 15-Jun-18]																							
SIV12160	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Black top	7	16-Jun-18	25-Jun-18	0%	[Gantt bar from 16-Jun-18 to 25-Jun-18]																							
SIV12170	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - Utilities: TCSS	21	10-May-18	04-Jun-18	0%	[Gantt bar from 10-May-18 to 04-Jun-18]																							
SIV12180	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - U channel	10	05-Jun-18	15-Jun-18	0%	[Gantt bar from 05-Jun-18 to 15-Jun-18]																							
SIV12220	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - Paving block	25	16-Jun-18	17-Jul-18	0%	[Gantt bar from 16-Jun-18 to 17-Jul-18]																							
SIV12222	Achievement of Section IV of the Works	0		30-Aug-18	0%	[Gantt bar from 30-Aug-18 to 30-Aug-18]																							
<b>Section VII - Remainder Works</b>																													
<b>Road &amp; Drainage Works (Culvert L - M/H1.7, Adjacent to SR3)</b>																													
SVII11600	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - Drainage Works (Culvert L - M/H1.7)	48	08-Jan-18 A	20-Apr-18	18.64%	[Gantt bar from 08-Jan-18 to 20-Apr-18]																							
SVII11620	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway : traffic diversion at Lung King Street	3	21-Apr-18	24-Apr-18	0%	[Gantt bar from 21-Apr-18 to 24-Apr-18]																							
SVII11640	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - Gully pipe (Culvert L - M/H1.7)	27	25-Apr-18	28-May-18	0%	[Gantt bar from 25-Apr-18 to 28-May-18]																							
SVII11650	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - TCSS duct	7	29-May-18	05-Jun-18	0%	[Gantt bar from 29-May-18 to 05-Jun-18]																							
SVII11654	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - road kerb & formation	14	06-Jun-18	22-Jun-18	0%	[Gantt bar from 06-Jun-18 to 22-Jun-18]																							
SVII11660	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - Black top	6	23-Jun-18	29-Jun-18	0%	[Gantt bar from 23-Jun-18 to 29-Jun-18]																							
SVII11680	Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - U channel	14	29-May-18	13-Jun-18	0%	[Gantt bar from 29-May-18 to 13-Jun-18]																							
SVII11700	Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - utilities: TCSS	14	14-Jun-18	30-Jun-18	0%	[Gantt bar from 14-Jun-18 to 30-Jun-18]																							
SVII11720	Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - paving block	14	03-Jul-18	18-Jul-18	0%	[Gantt bar from 03-Jul-18 to 18-Jul-18]																							
<b>Retaining Wall RW5 Construction</b>																													
SVII10660	Sec VII - Retaining Wall RW5 (bay 1) - construct base slab and wall	22	20-Mar-18	18-Apr-18	0%	[Gantt bar from 20-Mar-18 to 18-Apr-18]																							
SVII10680	Sec VII - Retaining wall RW5 (bay 2) - construct base slab and wall	22	19-Apr-18	15-May-18	0%	[Gantt bar from 19-Apr-18 to 15-May-18]																							
SVII10800	Sec VII - Retaining wall RW5 (bay 3) - construct base slab and wall	22	20-Mar-18	18-Apr-18	0%	[Gantt bar from 20-Mar-18 to 18-Apr-18]																							
SVII10820	Sec VII - Retaining wall RW5 (bay 4) - construct base slab and wall	22	19-Apr-18	15-May-18	0%	[Gantt bar from 19-Apr-18 to 15-May-18]																							
SVII10860	Sec VII - Retaining wall RW5 - curing, removal formwork	8	16-May-18	25-May-18	0%	[Gantt bar from 16-May-18 to 25-May-18]																							
<b>Landing Steps Construction</b>																													
<b>Landing Steps BSW13</b>																													
SVII10900	Sec VII - Landing steps (BSW13) - install vertical fender / step fender	15	15-May-18	01-Jun-18	0%	[Gantt bar from 15-May-18 to 01-Jun-18]																							
SVII10920	Sec VII - Landing steps (BSW13) - install s.s. handrail / tactile / sign board / bollard	25	02-Jun-18	03-Jul-18	0%	[Gantt bar from 02-Jun-18 to 03-Jul-18]																							
<b>Landing Steps BSW4</b>																													
SVII10980	Sec VII - Landing steps (BSW4) - install vertical fender / step fender	15	20-Jun-18	07-Jul-18	0%	[Gantt bar from 20-Jun-18 to 07-Jul-18]																							
SVII11000	Sec VII - Landing steps (BSW4) - install s.s. handrail / tactile / sign board / bollard	25	09-Jul-18	06-Aug-18	0%	[Gantt bar from 09-Jul-18 to 06-Aug-18]																							
<b>Landing Steps BSW5</b>																													
SVII11060	Sec VII - Landing steps (BSW5) - install vertical fender / step fender	15	25-Jul-18	10-Aug-18	0%	[Gantt bar from 25-Jul-18 to 10-Aug-18]																							
SVII11080	Sec VII - Landing steps (BSW5) - install s.s. handrail / tactile / sign board / bollard	25	11-Aug-18	08-Sep-18	0%	[Gantt bar from 11-Aug-18 to 08-Sep-18]																							
<b>Landing Steps BSW9</b>																													
SVII11140	Sec VII - Landing steps (BSW9) - install vertical fender / step fender	15	13-Jun-18	30-Jun-18	0%	[Gantt bar from 13-Jun-18 to 30-Jun-18]																							
SVII11160	Sec VII - Landing steps (BSW9) - install s.s. handrail / tactile / sign board / bollard	25	03-Jul-18	31-Jul-18	0%	[Gantt bar from 03-Jul-18 to 31-Jul-18]																							

**CEDD Contract No. HK/2012/08  
Wan Chai Development Phase II  
Central - Wan Chai Bypass at Wan Chai West**


Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019					
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
<b>Promenade Seawall Parapet Construction &amp; EVA</b>																							
SVII12000	Sec VII - Precast parapet	67	18-Nov-17 A	14-May-18	0%																		
SVII12010	Sec VII - Zone CRIII - seawall parapet: Backfilling	14	20-Feb-18	07-Mar-18	0%																		
SVII12120	Sec VII - Zone CRIII - seawall parapet: Construct mass concrete coping	30	08-Mar-18	16-Apr-18	0%																		
SVII12122	Sec VII - Zone CRIII - seawall parapet: reinforced concret coping	17	17-Apr-18	07-May-18	0%																		
SVII12140	Sec VII - Zone CRIII - seawall parapet: construct seawall parapet	30	08-May-18	12-Jun-18	0%																		
SVII12160	Sec VII - CRIII - EVA: watermain	14	13-Jun-18	29-Jun-18	0%																		
SVII12180	Sec VII - CRIII - EVA: U-channel	14	30-Jun-18	17-Jul-18	0%																		
SVII12200	Sec VII - CRIII - EVA: bituminous layer	5	18-Jul-18	23-Jul-18	0%																		
SVII12220	Sec VII - CRIII - EVA: paving block	30	24-Jul-18	27-Aug-18	0%																		
SVII13120	Sec VII - Zone A1, A2 & B - seawall parapet: Construct mass concrete coping	14	28-Dec-17 A	07-Mar-18	68.18%																		
SVII13122	Sec VII - Zone A1, A2 & B - seawall parapet: reinforced concrete coping	18	08-Mar-18	28-Mar-18	0%																		
SVII13140	Sec VII - Zone A1, A2 & B - seawall parapet: Construct seawall parapet	30	09-Apr-18	14-May-18	0%																		
SVII13160	Sec VII - Zone A1, A2 & B - EVA: watermain	14	15-May-18	31-May-18	0%																		
SVII13180	Sec VII - Zone A1, A2 & B - EVA: U-channel	14	01-Jun-18	16-Jun-18	0%																		
SVII13182	Sec VII - Zone A1, A2 & B - EVA: bituminous layer	5	19-Jun-18	23-Jun-18	0%																		
SVII13184	Sec VII - Zone A1, A2 & B - EVA: paving block	30	25-Jun-18	30-Jul-18	0%																		
SVII13200	Sec VII - Zone D - seawall parapet: Remove temporary seawall block	21	07-Mar-18	03-Apr-18	0%																		
SVII13220	Sec VII - Zone D - seawall parapet: Construct mass concrete	30	04-Apr-18	10-May-18	0%																		
SVII13222	Sec VII - Zone D - seawall parapet: reinforced concrete coping	18	11-May-18	01-Jun-18	0%																		
SVII13240	Sec VII - Zone D - seawall parapet: Construct seawall parapet	25	02-Jun-18	03-Jul-18	0%																		
SVII13260	Sec VII - Zone D - EVA : watermain	14	04-Jul-18	19-Jul-18	0%																		
SVII13280	Sec VII - Zone D - EVA : U-channel	14	20-Jul-18	04-Aug-18	0%																		
SVII13300	Sec VII - Zone D - EVA : bituminous layer	5	06-Aug-18	10-Aug-18	0%																		
SVII13320	Sec VII - Zone D - EVA : paving block	30	11-Aug-18	14-Sep-18	0%																		
<b>Promenade Footpath</b>																							
<b>Section 1</b>																							
SVII10440	Sec VII - section 1 footpath - drainage works : connection pipe & U -channel	10	24-May-18	04-Jun-18	0%																		
SVII10445	Sec VII - section 1 footpath - watermain	7	05-Jun-18	12-Jun-18	0%																		
SVII10460	Sec VII - section 1 footpath - lighting	7	13-Jun-18	21-Jun-18	0%																		
SVII10500	Sec VII - section 1 footpath - paving block	21	22-Jun-18	17-Jul-18	0%																		
<b>Section 2</b>																							
SVII12610	Sec VII - section 2 footpath - drainage works : L2202 - L2203A	20	20-Feb-18	14-Mar-18	0%																		
SVII12615	Sec VII - section 2 footpath - watermain	7	15-Mar-18	22-Mar-18	0%																		
SVII12630	Sec VII - section 2 footpath - utilities: TCSS	21	23-Mar-18	20-Apr-18	0%																		
SVII12670	Sec VII - section 2 footpath - paving block	30	21-Apr-18	28-May-18	0%																		
<b>Section 3</b>																							
SVII12850	Sec VII - section 3 footpath - watermain	17	20-Feb-18	10-Mar-18	0%																		
SVII12870	Sec VII - section 3 footpath - utilities (HEC, TCSS, HGC, PCCW)	40	12-Mar-18	02-May-18	0%																		
SVII12875	Sec VII - 3 footpath - drainage works :U chanel	14	03-May-18	18-May-18	0%																		



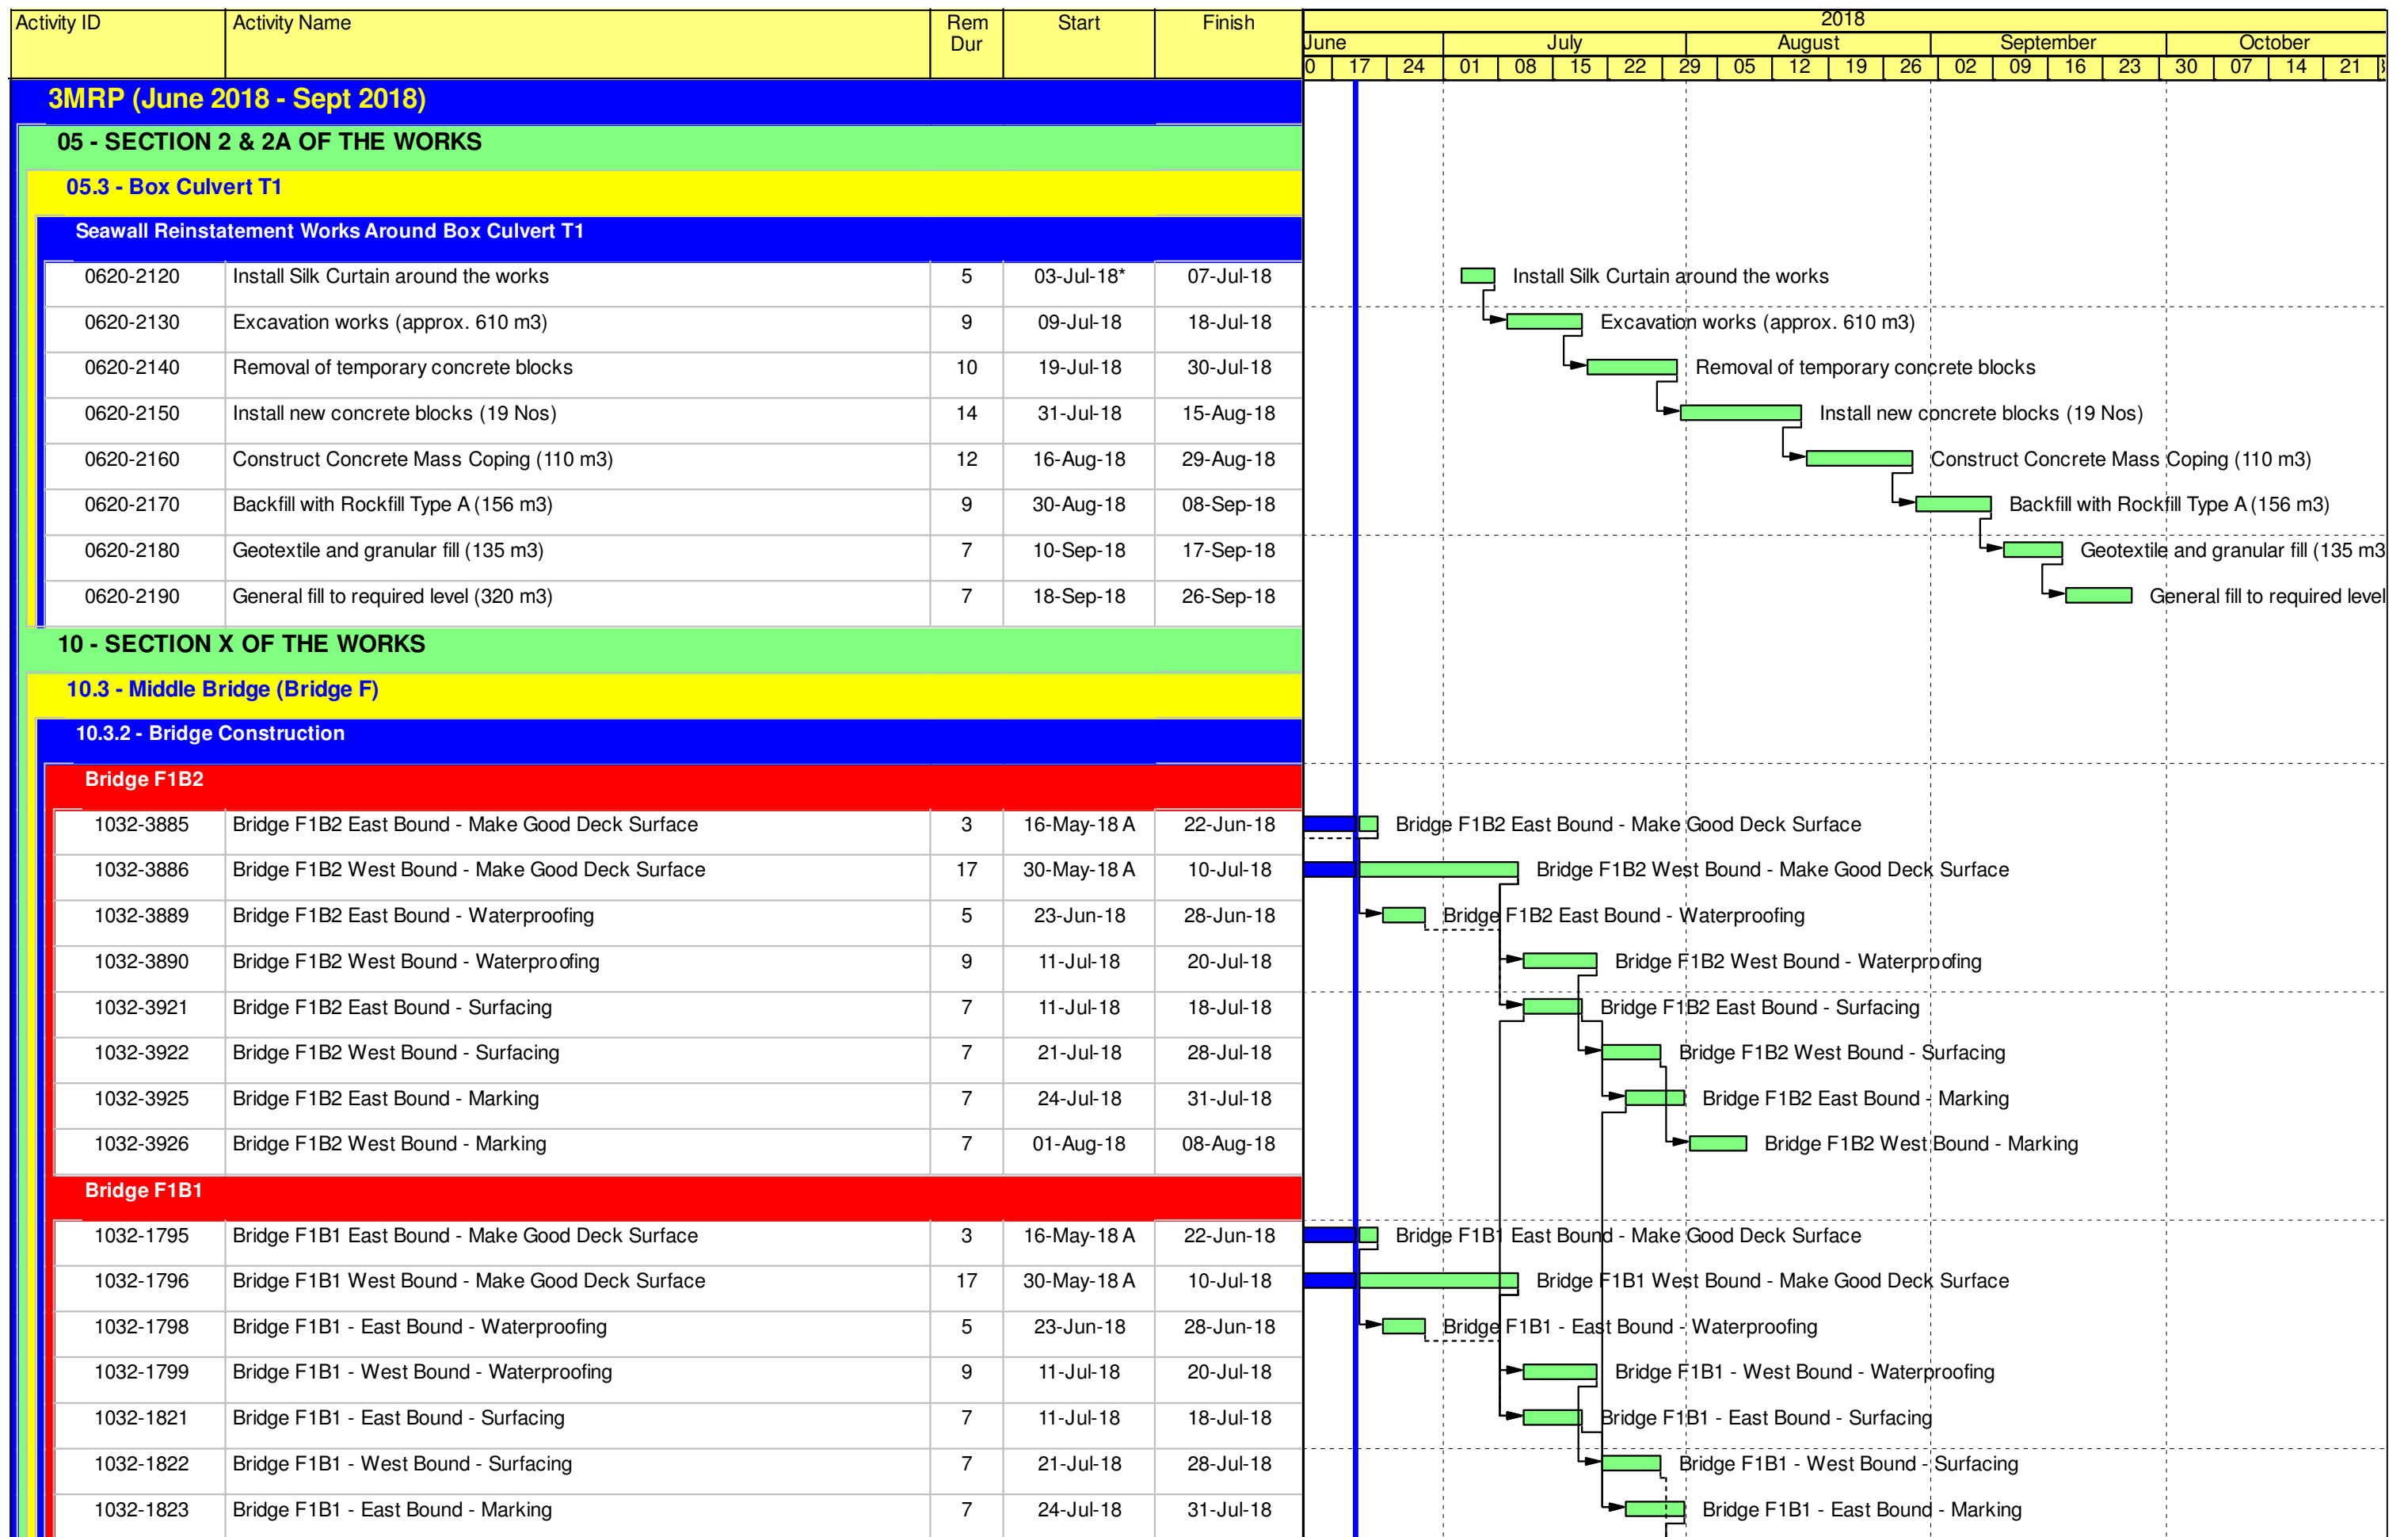

█ Remaining Level of Effort    █ Remaining Work  
█ Actual Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.June.2018 to 20.Sept.2018)**

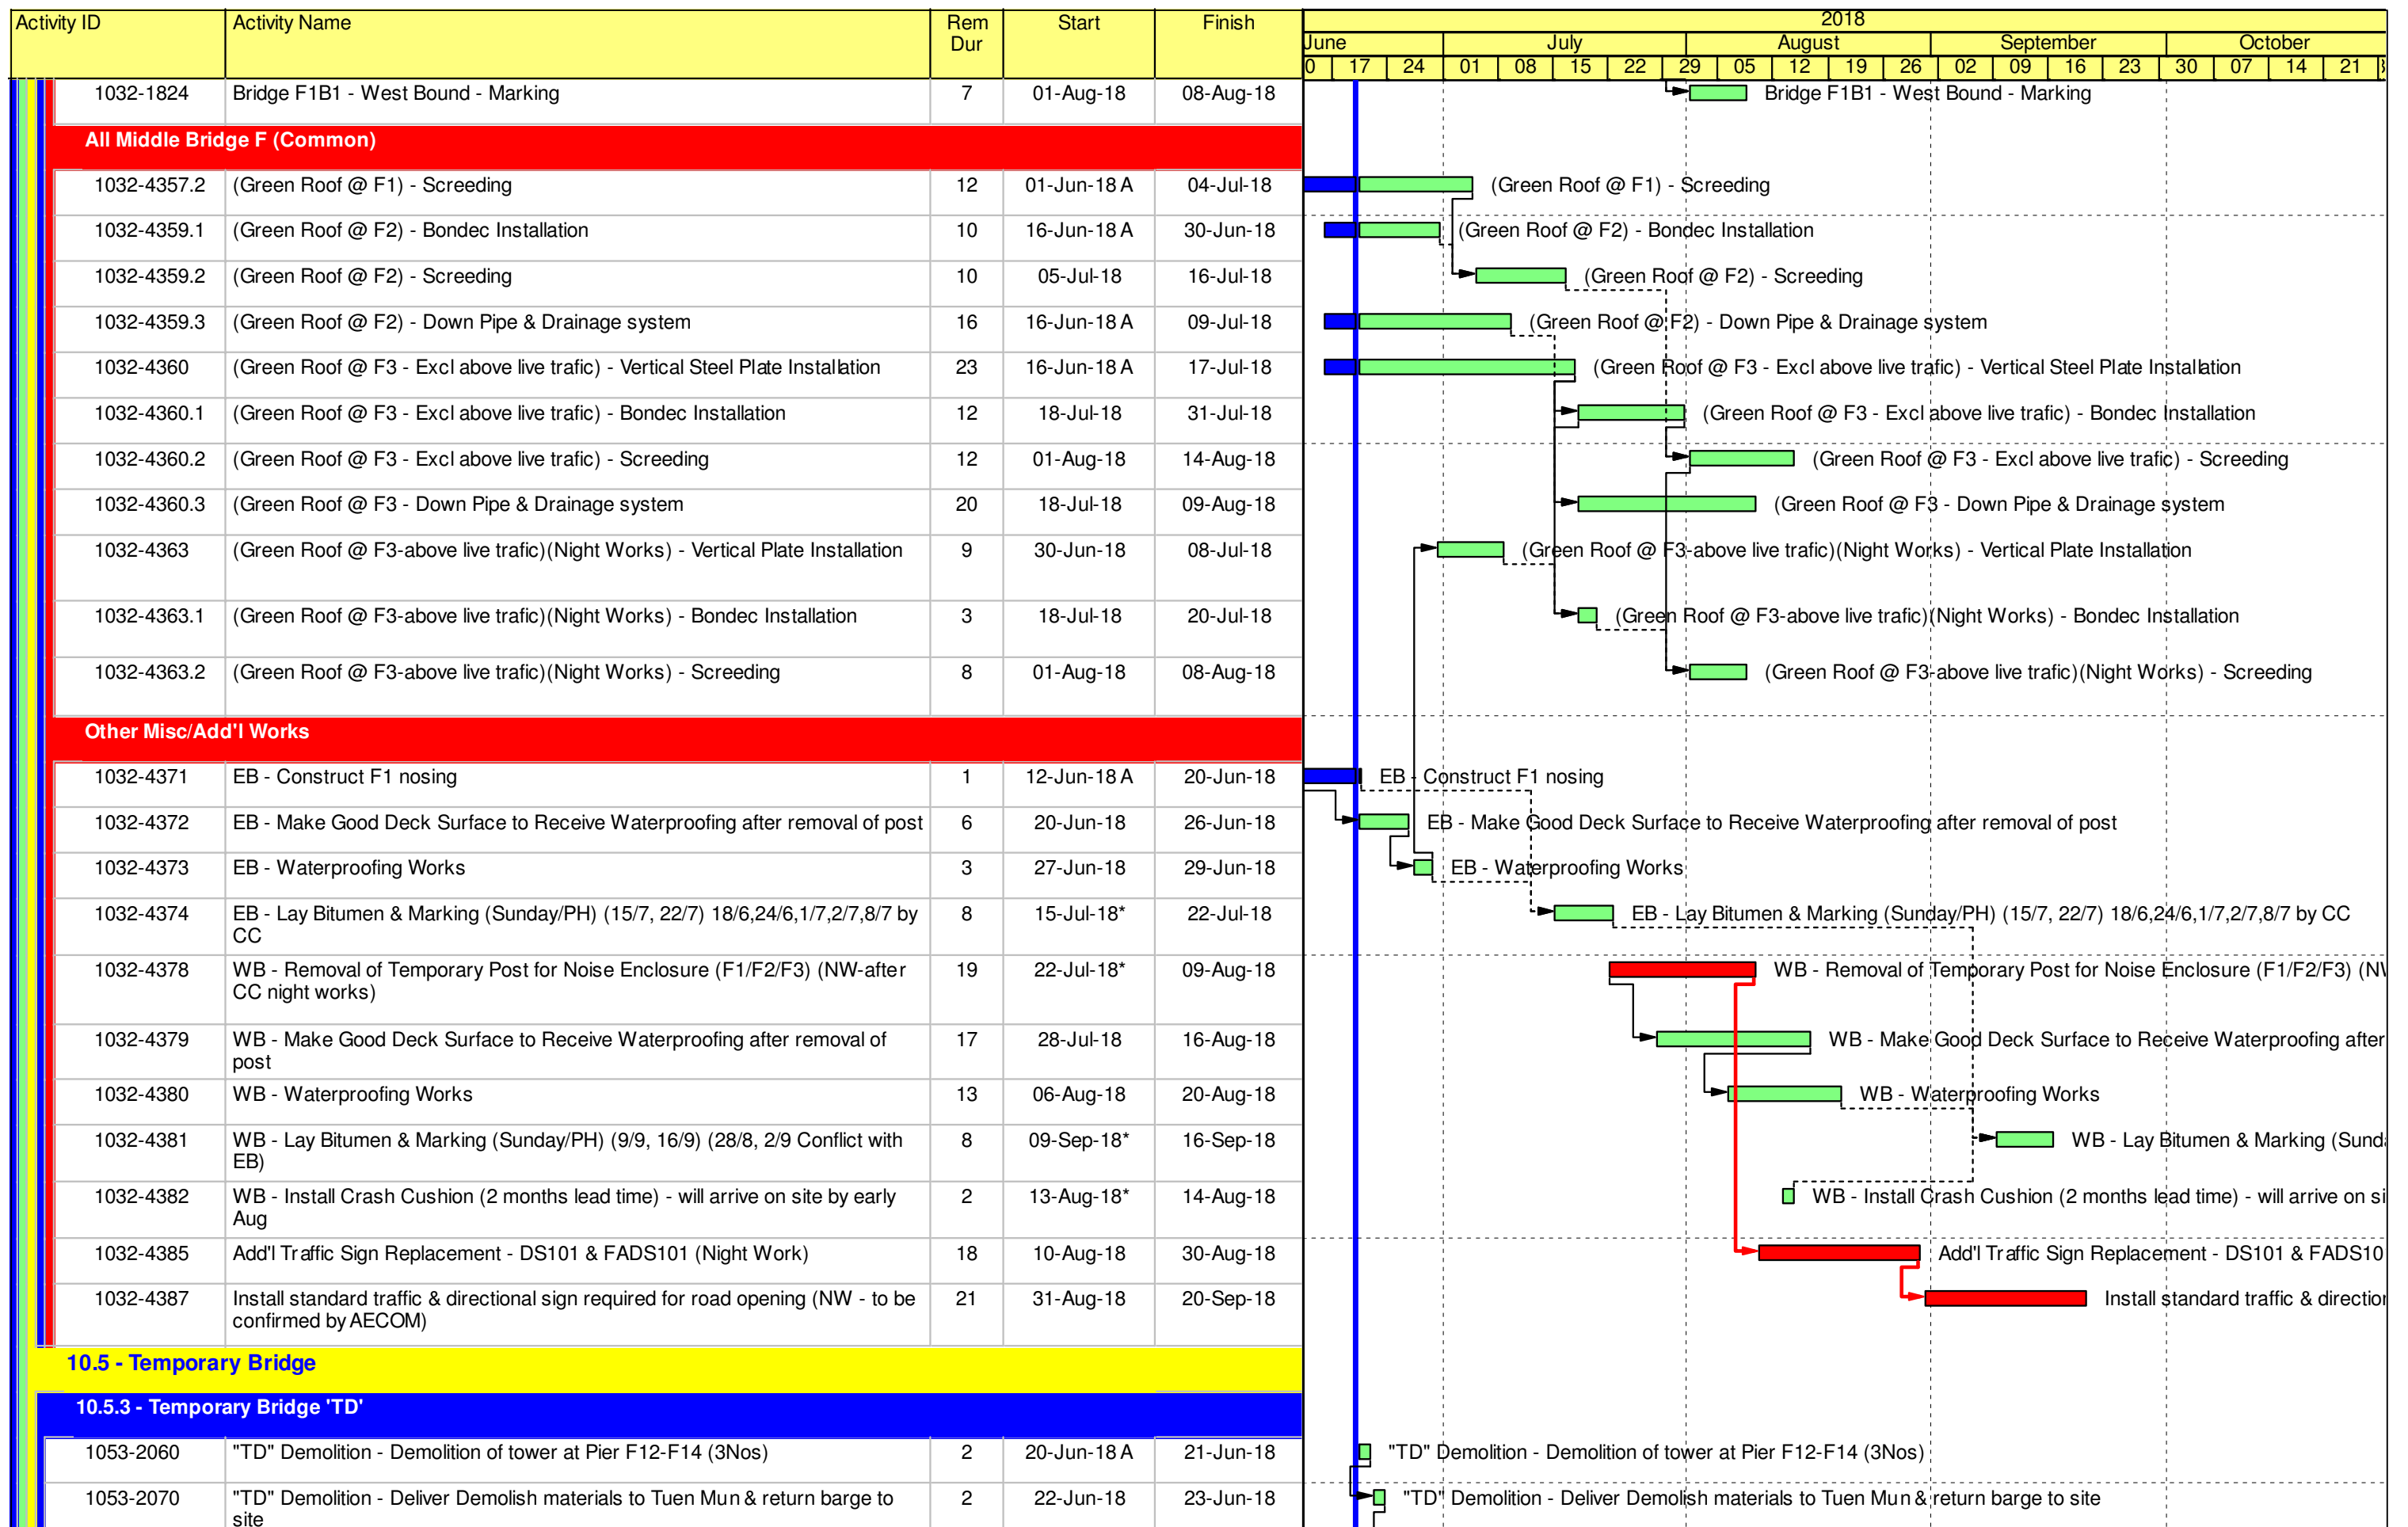

Activity ID	Activity Name	Rem Dur	Start	Finish	2018																			
					June			July				August				September				October				
					0	17	24	01	08	15	22	29	05	12	19	26	02	09	16	23	30	07	14	21
1053-2080	"TD" Demolition - Remove beam from F9-F10 (5Nos; E10-E14)	3	25-Jun-18	27-Jun-18																				
1053-2100	"TD" Demolition - Remove beam from F5-F7 (5Nos; W1-W5)	3	28-Jun-18	30-Jun-18																				
1053-2110	"TD" Demolition - Demolition of tower at Pier F5-F6 & F10 (3Nos)	3	03-Jul-18	05-Jul-18																				
1053-2120	"TD" Demolition - Deliver Demolish materials to Tuen Mun & return barge to site	2	06-Jul-18	07-Jul-18																				
1053-2130	"TD" Demolition - Remove beam from F7-F9 (9Nos; W6-W9 & C1-C5)	4	09-Jul-18	12-Jul-18																				
1053-2140	"TD" Demolition - Demolition of tower at Pier F9-F7 (3Nos)	3	13-Jul-18	16-Jul-18																				

**10.6 - Tunnel Approach Ramp**

**10.6.1 - Approach Ramp (Excluding Portion IIB)**

**Retaining Walls & Trough Structure B,C & D**

1061-7120	ELS and Excavate to Founding Level & Waterproofing Trough B Structure (98 Sheet pile: 2/3 at Low Head Rm)	15	05-Jun-18 A	07-Jul-18																		
1061-7130	EJ installation - Trough B Structure	1	09-Jul-18	09-Jul-18																		
1061-7140	Construct Trough Structure B Base Slab	14	10-Jul-18	25-Jul-18																		
1061-7160	Construct Trough Structure B Side Walls	10	26-Jul-18	06-Aug-18																		
1061-7180	Excavate to Founding Level & Waterproofing Trough C Structure	2	05-Jun-18 A	21-Jun-18																		
1061-7190	EJ installation - Trough C Structure	1	22-Jun-18	22-Jun-18																		
1061-7200	Construct Trough Structure C Base Slab	14	23-Jun-18	10-Jul-18																		
1061-7220	Construct Trough Structure C Side Walls	10	11-Jul-18	21-Jul-18																		
1061-7230	MJ Cover installation - Trough A/B/C Structure (material not yet confirm; need 2 months lead time)	9	07-Aug-18	16-Aug-18																		
1061-7240	Road, Paving & Fencing Works at Trough B/C/D	8	17-Aug-18	25-Aug-18																		
1061-7250	Backfilling Works at Back side of Trough B & C	12	07-Aug-18	20-Aug-18																		

**Landscape Deck**

1061-7464	Bay C5 > Upstand Wall at Bay C5 (east remaining - waiting to AECOM details)	24	09-Apr-18 A	18-Jul-18																		
-----------	---	----	-------------	-----------	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

**Road & Other Misc Works**

1061-7510	WB (Bay C4/C5) - Drainage installation (4 manhole; 6 gullies: 125m 225Dia pipe)	6	05-Jun-18 A	26-Jun-18																		
1061-7520	EB (Bay C4/C5) - Drainage installation (3 manhole; 4 gullies: 185m 225Dia pipe)	18	20-Jun-18	11-Jul-18																		
1061-7530	WB (Bay C4/C5) - Median Profile Barrier & Kerb	18	27-Jun-18	18-Jul-18																		
1061-7540	EB (Bay C4/C5) - Median Profile Barrier & Kerb	18	12-Jul-18	01-Aug-18																		
1061-7545	WB - Sub-base (Bay C4/C5) and Asphalt laying (C2.5-C5)	7	19-Jul-18	26-Jul-18																		
1061-7547	EB - Sub-base (Bay C4/C5) and Asphalt laying (C2.5-C5)	7	02-Aug-18	09-Aug-18																		
1061-7550	Install VMS 2,3 & 4 (Still waiting for setting out for VMS4 at C5)	4	14-Jun-18 A	23-Jun-18																		
1061-7600	Approach Ramp Final Road Surfacing & Marking (excl Portion IIB)	7	23-Aug-18*	30-Aug-18																		

- ▬ Remaining Level of Effort
- ▬ Actual Level of Effort
- ▬ Critical Remaining Work
- ▬ Actual Work
- ▬ Remaining Work
- ▬ Critical Remaining Work
- ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.June.2018 to 20.Sept.2018)**

Activity ID	Activity Name	Rem Dur	Start	Finish	2018																											
					June			July				August				September				October												
					0	17	24	01	08	15	22	29	05	12	19	26	02	09	16	23	30	07	14	21	28							
1061-7610	Bay C4-C5 > Noise Panel & Railing Installations	21	27-Jul-18	20-Aug-18	Bay C4-C5 > Noise Panel & Railing Installations																											
1061-7620	Bay C2-C3 > Noise Panel & Railing Installations	14	23-Jul-18	07-Aug-18	Bay C2-C3 > Noise Panel & Railing Installations																											
<b>10.6.2 - Approach Ramp (Within Portion IIB)</b>																																
<b>Structure</b>																																
<b>Phase II - Landscape Deck Bay C2 (1)</b>																																
<b>Wall - Upper Portion</b>																																
A1260	Vertical Water Proofing & Backfilling	6	25-May-18 A	26-Jun-18	Vertical Water Proofing & Backfilling																											
<b>Phase II - Landscape Deck Bay C1 (2)</b>																																
<b>Wall - Upper Portion</b>																																
A1420	Vertical Water Proofing & Backfilling	6	25-May-18 A	26-Jun-18	Vertical Water Proofing & Backfilling																											
<b>Phase II - Landscape Deck Bay C1 (3)</b>																																
<b>Wall - Upper Portion</b>																																
A1580	Vertical Water Proofing & Backfilling	6	29-May-18 A	26-Jun-18	Vertical Water Proofing & Backfilling																											
<b>Phase II - Landscape Deck Bay C1 (4)</b>																																
<b>Wall - Upper Portion</b>																																
A1750	Vertical Water Proofing & Backfilling	6	31-May-18 A	26-Jun-18	Vertical Water Proofing & Backfilling																											
<b>Phase II - Landscape Deck Bay C1 (5)</b>																																
<b>Wall - Upper Portion</b>																																
A1910	Vertical Water Proofing & Backfilling	6	31-May-18 A	26-Jun-18	Vertical Water Proofing & Backfilling																											
<b>Road Works</b>																																
1062-1276	Re-instatement of De-watering Well	14	27-Jun-18*	13-Jul-18	Re-instatement of De-watering Well																											
1062-1277	Re-instatement of Temporary Sump Pit	7	14-Jul-18	21-Jul-18	Re-instatement of Temporary Sump Pit																											
1062-1278	Masking at D-wall side wall at Bay C1-5 (2 pours/face)(waiting confirmation w/ CC for access date)	18	24-May-18 A	11-Jul-18	Masking at D-wall side wall at Bay C1-5 (2 pours/face)(waiting confirmation w/ CC for access date)																											
1062-1300	Road Drainage & Downpipe (within Portion IIB)	24	27-Jun-18*	25-Jul-18	Road Drainage & Downpipe (within Portion IIB)																											
1062-1380	Road Surfacing & Marking (within Portion IIB) (after CC installation works)	6	31-Jul-18*	06-Aug-18	Road Surfacing & Marking (within Portion IIB) (after CC installation works)																											
1062-1385	Construct Noise Panel Trough A (within Portion IIB)	9	20-Jul-18	30-Jul-18	Construct Noise Panel Trough A (within Portion IIB)																											
<b>10.6.3 - Slip Road 13</b>																																
1062-1283	Slip Road 13 (South 2 - Adj to Car Park) Breaking Ex. Concrete & Drainage Works & other Under Ground Civil Provisions	10	24-May-18 A	30-Jun-18	Slip Road 13 (South 2 - Adj to Car Park) Breaking Ex. Concrete & Drainage Works & other Under Ground Civil Provisions																											
1062-1284	Slip Road 13 (South 2 - Adj to Car Park) Backfilling & Compaction	12	28-Jun-18	12-Jul-18	Slip Road 13 (South 2 - Adj to Car Park) Backfilling & Compaction																											
1062-1287	Slip Road 13 (South 2 - Adj to Car Park) Road Kerb & Other Misc Works	8	13-Jul-18	21-Jul-18	Slip Road 13 (South 2 - Adj to Car Park) Road Kerb & Other Misc Works																											
1062-1290	Slip Road 13 (West - Near Site Office) TCSS, Draw Pits & other Civil Provision	19	07-Jun-18 A	12-Jul-18	Slip Road 13 (West - Near Site Office) TCSS, Draw Pits & other Civil Provision																											

■ Remaining Level of Effort    ■ Remaining Work  
■ Actual Level of Effort        ■ Critical Remaining Work  
■ Actual Work                        ◆ ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.June.2018 to 20.Sept.2018)**



Activity ID	Activity Name	Rem Dur	Start	Finish	2018																								
					June					July					August					September					October				
					0	17	24	01	08	15	22	29	05	12	19	26	02	09	16	23	30	07	14	21	28				
1062-1291	Slip Road 13 (West - Near Site Office) Trimming Ex Surface & Drainage Works	13	07-Jun-18 A	05-Jul-18	Slip Road 13 (West - Near Site Office) Trimming Ex Surface & Drainage Works																								
1062-1292	Slip Road 13 (West - Near Site Office) Backfilling & Compaction	8	06-Jul-18	14-Jul-18	Slip Road 13 (West - Near Site Office) Backfilling & Compaction																								
1062-1293	Slip Road 13 (West - Near Site Office) Road Kerb & Other Misc Works	8	16-Jul-18	24-Jul-18	Slip Road 13 (West - Near Site Office) Road Kerb & Other Misc Works																								
1062-1294	Slip Road 13 (North - Sea Side) Drainage & Other Underground Civil Provision Works	14	25-Jun-18	11-Jul-18	Slip Road 13 (North - Sea Side) Drainage & Other Underground Civil Provision Works																								
1062-1295	Slip Road 13 (North - Sea Side) Backfilling & Compaction	8	12-Jul-18	20-Jul-18	Slip Road 13 (North - Sea Side) Backfilling & Compaction																								
1062-1296	Slip Road 13 (North - Sea Side) Road Kerb & Other Misc Works	8	21-Jul-18	30-Jul-18	Slip Road 13 (North - Sea Side) Road Kerb & Other Misc Works																								
1062-1297	Slip Road Surfacing	5	31-Jul-18	04-Aug-18	Slip Road Surfacing																								
1062-1298	Road Marking, Fencing & Other Finishing Works	17	06-Aug-18	24-Aug-18	Road Marking, Fencing & Other Finishing Works																								
<b>10.7 - Section X - Miscellaneous Works</b>																													
<b>10.7.2 - Oil Street/Watson Road (Portion III)</b>																													
1072-1285	Pre-cast Clay Paving EVA to EVB (remaining paver to arrive on site by mid Aug)	57	10-May-18 A	25-Aug-18	Pre-cast Clay Paving EVA to EVB (remaining paver to arrive on site by mid Aug)																								
1072-1287	Road Reinstatement > Watson Road cul-de sac	12	22-May-18 A	04-Jul-18	Road Reinstatement > Watson Road cul-de sac																								
<b>11 - SECTION 11 OF THE WORKS</b>																													
<b>11.0 - Portion XIIC</b>																													
1110-2500	EB - Modification of Road Marking at Hing Fat Slip Road (Night Work)	1	26-Aug-18*	26-Aug-18	EB - Modification of Road Marking at Hing Fat Slip Road																								
<b>11.1 - Portion XIIA - Stage 1</b>																													
<b>11.1.4 - Footing and frame/pole for directional sign FVMSH2, ADS16 and OHVD (Portion XIIA)</b>																													
1110-2970	FVMSH2	18	07-May-18 A	11-Jul-18	FVMSH2																								
1110-2980	DS15 (Frame)	6	19-Jun-18 A	26-Jun-18	DS15 (Frame)																								
1110-2985	DS18	10	20-Jun-18	30-Jun-18	DS18																								
1110-2987	OHVD at Tsing Fung Street Flyover	17	05-Jul-18*	24-Jul-18	OHVD at Tsing Fung Street Flyover																								
<b>11.2 - Portion XIIA - Stage 2 - Along Gordon House - Cross road ducting at Hing Fat St (public hol)</b>																													
1110-3020	Miscellaneous Road Works at Portion XIIA (5 TTA arrangement - works only on Sunday & public holiday; 12days)	56	04-Jul-18	06-Sep-18	Miscellaneous Road Works at Portion XIIA (5 TTA arrangement - works only on Sunday & public holiday; 12days)																								
<b>11.3 - Portion XIIA - Stage 3 - Preparation &amp; works night before road opening</b>																													
1110-3030	Misc Works prior to CWB opening incl preparation - Stage 2	12	06-Sep-18	19-Sep-18	Misc Works prior to CWB opening																								

█ Remaining Level of Effort    █ Remaining Work  
█ Actual Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.June.2018 to 20.Sept.2018)**

Activity ID	Activity Name	Original Duration	Start	Finish	2018											
					Jun			Jul			Aug			Sep		
<b>Total</b>		2356d	21-Mar-13 A	01-Sep-19												
<b>DWP-08 - (2) - Update Progress As of 20 Jun 18</b>		2356d	21-Mar-13 A	01-Sep-19												
<b>Works in KD9 (Include Re-provisioning Works of KD4,KD5)</b>		247d	30-Jan-18 A	23-Sep-18												
<b>External Works Under KD9</b>		151d	30-Jan-18 A	17-Sep-18												
<b>Zone 1</b>		60d	18-Apr-18 A	27-May-18 A												
<b>Drainage Alignment Confirmation for MH72, 73, 74 due to Tree T1106</b>		60d	18-Apr-18 A	27-May-18 A												
EXW_1155	Confirmation, TTA application and construction of re-routing of drainage works near RW8E side	60d	18-Apr-18 A	27-May-18 A	TTA application and construction of re-routing of drainage works near RW8E side											
<b>Zone 4 up to Elderly Facilities</b>		125d	30-Jan-18 A	17-Sep-18												
<b>Elderly Facilities V/039 Received on 22 Jun 2017</b>		100d	30-Jan-18 A	17-Sep-18												
EXW_2270	Facilities fabrication	90d	30-Jan-18 A	13-Aug-18	Facilities fabrication											
EXW_2280	Ground levelling, drainage works and safety met installation	30d	14-Aug-18	17-Sep-18	Ground levelling											
<b>Additional Walkway &amp; Arbour V/040 Received on 22 Aug 2017</b>		93d	28-Mar-18 A	28-Jul-18												
EXW_2310	Associated drainage works for the walkway	20d	28-Mar-18 A	23-May-18 A	Works for the walkway											
EXW_2320	Arbour installation and walkway construction	30d	03-May-18 A	28-Jul-18	Arbour installation and walkway construction											
<b>Reverting Traffic for IEC,VP Rd &amp; TF St &amp; Seawall Reinstatement (KD9)</b>		164d	26-Mar-18 A	23-Sep-18												
<b>TTA Revert Traffic Back to Original Alignment</b>		105d	26-Mar-18 A	28-Jul-18												
<b>East Bound TTA - IEC East Bound, Victoria Park Road &amp; footpath along Sea Side</b>		93d	28-Mar-18 A	28-Jul-18												
<b>TTM Stage 1 - IEC (East Bound)</b>		6d	21-Jun-18	26-Jun-18												
<b>Reinstatement Existing Structure</b>		6d	21-Jun-18	26-Jun-18												
EB_1020	Install metal parapet on parapet wall (30m)	6d	21-Jun-18	26-Jun-18	Install metal parapet on parapet wall (30m)											
<b>TTM Stage 2 - Revert Traffic back to Original Victoria Road</b>		4d	27-Jun-18	30-Jun-18												
<b>Existing Bridge Parapet Reinstatement</b>		4d	27-Jun-18	30-Jun-18												
EB_1180	Install metal parapet on parapet wall (40m)	4d	27-Jun-18	30-Jun-18	Install metal parapet on parapet wall (40m)											
<b>TTM Stage 3 - Reinstatement of Footpath along Seafront</b>		93d	28-Mar-18 A	28-Jul-18												
<b>Reinstatement of Existing Utilities at Existing Footpath</b>		86d	28-Mar-18 A	24-Jul-18												
EB_1600	Lay HGC, PCCW, Whart T&T and NWT telecom ducts and construct drawpits	10d	28-Mar-18 A	24-Jul-18	Lay HGC, PCCW, Whart T&T and NWT telecom ducts and construct drawpits											
EB_1620	Reinstate permanent water main	5d	18-Apr-18 A	17-Jul-18	Reinstate permanent water main											
EB_1580	Water main Connection by WSD	2d	20-Jun-18 A	20-Jun-18 A	Water main Connection by WSD											
<b>Reinstatement of Permanent Footpath at Seafront</b>		49d	27-May-18 A	26-Jul-18												
EB_1630	Backfilling Subbase	3d	27-May-18 A	29-May-18 A	Subbase											
EB_1640	Concreting of Permanent Footpath	4d	29-May-18 A	25-Jul-18	Concreting of Permanent Footpath											
EB_1650	Pedestrian diversion on Permanent Footpath	1d	26-Jul-18	26-Jul-18	Pedestrian diversion on Permanent Footpath											
<b>Reinstatement Works in Traffic Deck Part B</b>		3d	07-May-18 A	28-Jul-18												
EB_1700	Backfill Type B Material up to 2m below F.F.L (Compaction by proof rolling method of 0.2m each layer)	3d	07-May-18 A	28-Jul-18	Backfill Type B Material up to 2m below F.F.L (Compaction by proof rolling method of 0.2m each layer)											
<b>West Bound - IEC West Bound &amp; Tsing fung Street</b>		74d	26-Mar-18 A	06-Jul-18												
<b>TTM Stage 2 - Revert Traffic back to Original Tsing Fung Street</b>		5d	21-Jun-18	25-Jun-18												
<b>Existing Bridge Parapet Reinstatement</b>		5d	21-Jun-18	25-Jun-18												
IECW_1140	Install metal parapet on parapet wall (60m)	5d	21-Jun-18	25-Jun-18	Install metal parapet on parapet wall (60m)											
<b>TTM Stage 3 - Reinstatement of Victoria Park</b>		21d	26-Mar-18 A	06-Jul-18												
<b>Reinstatement Works inside Victoria Park</b>		21d	26-Mar-18 A	06-Jul-18												
IECW_1470	Slope Reinstatement of Victoria Park	21d	26-Mar-18 A	06-Jul-18	Slope Reinstatement of Victoria Park											
<b>Completion of Minor Outstanding / Remaining Works for KD9</b>		110d	18-May-18 A	23-Sep-18												
<b>East Bound - Minor Outstanding Works in Footpath after Substantial Completion of KD9</b>		88d	18-May-18 A	01-Sep-18												



- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Date	Revision	Checked	Approved
20-Jun-18	DWP-08 (2) - 3 Months Rolling	TL	TL

Activity ID	Activity Name	Original Duration	Start	Finish	2018			
					Jun	Jul	Aug	Sep
<b>Minor Reinstatement Works for Existing Sign Gantry</b>								
EB_1750	Laying Public Lighting duct	3d	30-May-18 A	25-Aug-18	Laying Public Lighting duct			
EB_1780	Erect Sign Gantry Steel Supports and Sign Gantry Beam across VPR and IEC E/B	4d	29-Jul-18	01-Aug-18	Erect Sign Gantry Steel Supports and Sign Gantry Beam across VPR and IEC E/B			
EB_1790	Installation of E & M at Sign Gantry (night work)	1d	02-Aug-18	02-Aug-18	Installation of E & M at Sign Gantry (night work)			
EB_1760	Connection of Public Lighting by HyD (Lighting)	2d	26-Aug-18	27-Aug-18	Connection of Public Lighting by HyD (Lighting)			
<b>Minor Reinstatement Works for Central Median of IEC &amp; Footbridge</b>								
EB_1800	Reconstruction of central divider (6m long, night work)	6d	02-Aug-18	07-Aug-18	Reconstruction of central divider (6m long, night work)			
EB_1810	Dismantlement of temp directional sign mounted on extg footbridge	1d	03-Aug-18	03-Aug-18	Dismantlement of temp directional sign mounted on extg footbridge			
<b>Minor Reinstatement Works for Footpath</b>								
EB_1820	Place kerblines along VPR footpath	3d	18-May-18 A	23-Aug-18	Place kerblines along VPR footpath			
EB_1850	Backfilling subbase material	2d	27-May-18 A	29-May-18 A	subbase material			
EB_1830	Reinstatement of District Council Welcome Sign and opening plaque at Planter area	1d	24-Aug-18	24-Aug-18	Reinstatement of District Council Welcome Sign and opening			
EB_1840	Re-provision of Tree	8d	25-Aug-18	01-Sep-18	Re-provision of Tree			
<b>Minor Reinstatement Works for Bus Stop</b>								
EB_1860	Reinstatement of Permanent Bus Stop	5d	23-May-18 A	26-Jun-18 A	Reinstatement of Permanent Bus Stop			
EB_1870	Relocation of Bus Stop	1d	27-Jun-18 A	27-Jun-18 A	Relocation of Bus Stop			
EB_1880	Reinstate Planter(Previous Temporary Bus Stop)	5d	25-Aug-18	29-Aug-18	Reinstate Planter(Previous Temporary Bus Stop)			
<b>Minor Reinstatement Works for Loop Detector</b>								
EB_1900	Construction of concrete plinth and fix counter housing for Loop Detector (ILDS)	3d	04-Aug-18	06-Aug-18	Construction of concrete plinth and fix counter housing for Loop Detector (ILDS)			
EB_1890	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)	1d	07-Aug-18	07-Aug-18	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)			
<b>West Bound - Completion of Minor Outstanding / Remaining Works for KD9</b>								
<b>Minor Reinstatement Works for Victoria Park</b>								
IECW_1500	Re-provision of Tree	32d	07-Jul-18	07-Aug-18	Re-provision of Tree			
IECW_1510	Laying Irrigation Main	10d	22-Jul-18	31-Jul-18	Laying Irrigation Main			
IECW_1520	Construct Landscape Footpath and Lightings	7d	06-Aug-18	12-Aug-18	Construct Landscape Footpath and Lightings			
<b>Minor Reinstatement Works in IEC West Bound</b>								
IECW_1600	Replacement of new movement joint at IEC W/B (Sun midnight only)	8d	21-Jun-18	28-Jun-18	Replacement of new movement joint at IEC W/B (Sun midnight only)			
IECW_1610	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)	57d	29-Jun-18	24-Aug-18	Repairing of extg conc deck surface after milling of temp asp			
IECW_1640	Erection of new precast concrete panels (12 nos.) at abutment M facing to VPR	2d	25-Aug-18	26-Aug-18	Erection of new precast concrete panels (12 nos.) at abu			
IECW_1620	Repairing of concrete defects on extg concrete deck and abutment M	30d	25-Aug-18	23-Sep-18	Re			
<b>Works in Victoria Park (KD4, KD5, KD9)</b>								
<b>Re-Provisioning Works</b>								
<b>Nursery Compound</b>								
<b>Nursery compound</b>								
<b>ABWF</b>								
<b>Metal Fence</b>								
VP_NC_1820	Installation	30d	05-Apr-18 A	07-Aug-18	Installation			
<b>Fire Services</b>								
VP_NC_2030	FS inspection	14d	21-Jun-18	07-Jul-18	FS inspection			
<b>Plumbing and Flushing Water Supplies</b>								
VP_NC_2100	WSD Inspection	14d	21-Jun-18	07-Jul-18	WSD Inspection			
<b>External Works Aside Nursery Compound</b>								
<b>External Works Around Nursery Compound</b>								

Activity ID	Activity Name	Original Duration	Start	Finish	2018											
					Jun			Jul			Aug			Sep		
					1	2	3	4	5	6	7	8	9	10	11	12
VP_NC_2250	Reinstatement of Existing Boundary Fence Wall Around Nursery Compound	45d	01-Mar-18 A	26-May-18 A	<del>Existing Boundary Fence Wall Around Nursery Compound</del>											
VP_NC_2260	EVA Construction	15d	28-May-18 A	14-Jul-18	EVA Construction											
<b>KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks</b>		<b>390d</b>	<b>08-Aug-18</b>	<b>01-Sep-19</b>												
<b>KD11 - Section 7A: Portion XIV &amp; XV (Victoria Park Open Space)</b>		<b>365d</b>	<b>08-Aug-18</b>	<b>07-Aug-19</b>												
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365d	08-Aug-18	07-Aug-19												
<b>KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH&gt;500mm)</b>		<b>365d</b>	<b>02-Sep-18</b>	<b>01-Sep-19</b>												
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365d	02-Sep-18	01-Sep-19												
<b>KD18 - Section 11: Transplanted Trees DBH&gt;500mm in Portion VA and XII</b>		<b>365d</b>	<b>08-Aug-18</b>	<b>07-Aug-19</b>												
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365d	08-Aug-18	07-Aug-19												
<b>KD10 - Preservation and Protection of Trees</b>		<b>1088d</b>	<b>21-Mar-13 A</b>	<b>27-Sep-18</b>												
PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	27-Sep-18												
<b>KD15 &amp; KD8 - Mooring Components Upkeep (CBTS and ATS)</b>		<b>979d</b>	<b>15-May-14 A</b>	<b>21-Jun-18</b>												
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	21-Jun-18	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS											

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018											
						May			Jun			Jul			Aug		
<b>Update 2018-05-20 CWB(CC) - Commissioning Contract (SA)</b>																	
<b>PRELIMINARIES AND GENERAL REQUIREMENTS</b>																	
<b>Salient Key Dates and Milestones</b>																	
<b>Anticipated Completion Dates</b>																	
KD03	KD3 - Achievement of Stage 3 (1385 days) - include EOT No.7 (207 days)	0		04-Jun-18*	-171	◆											
KD02	KD2 - Achievement of Stage 2 (1634 days) - include EOT No.9 (402 days)	0		29-Jun-18*	53	◆											
KD04	KD4 - Achievement of Stage 4 (1710 days) - include EOT No.9 (414 days)	0		30-Jun-18*	78	◆ ▲											
<b>Possession Dates and Vacation Dates</b>																	
PO-IIa	Possession of Portion IIa (Day 1) - WVB below +6.5mPD	1329	28-Feb-14 A	17-Jun-18	-216	—											
PO-III	Possession of Portion III (Day 120) - CH1805-2600	1209	28-Jun-14 A	17-Jun-18	-224	—											
PO-Ib	Possession of Portion Ib (Day 242) - CH1580-1805	1087	28-Oct-14 A	17-Jun-18	-216	—											
PO-IXd	Possession of Portion IXd (Day 266) - CH4600-4860	1063	21-Nov-14 A	17-Jun-18	-224	—											
PO-XI	Possession of Portion XI (Day 296) - EVS	1033	21-Dec-14 A	17-Jun-18	91	—											
PO-IIc	Possession of Portion IIc (Day 336) - CH1360-1580	993	30-Jan-15 A	17-Jun-18	-216	—											
PO-IIb	Possession of Portion IIb (Day 336) - WVB above +6.5mPD	669	30-Jan-15 A	17-Jun-18	-216	—											
PO-IXa	Possession of Portion IXa (Day 392) - CH4860-5150	937	27-Mar-15 A	17-Jun-18	-224	—											
PO-Va	Possession of Portion V (Day 607) - CH2950-3210	722	28-Oct-15 A	17-Jun-18	-206	—											
PO-VII_a1	Possession of Portion VII (Day 762) - CH3911-4250 (below -6.0mPD)	659	30-Dec-15 A	17-Jun-18	-190	—											
PO-Vc	Possession of Portion V (Day 607) - CH3210-3250	658	15-Jan-16 A	17-Jun-18	-188	—											
PO-VIb_b1	Possession of Portion VIb (Day 761) - CH3428-3625 (E/B)	619	18-Feb-16 A	17-Jun-18	-172	—											
PO-VIb_b2	Possession of Portion VIb (Day 761) - CH3428-3625 (W/B)	568	29-Feb-16 A	17-Jun-18	-166	—											
PO-Xa_1	Possession of Portion Xa (Day 650) - ADB Southern Portion (AECOM letter ref: 2015007890T)	589	07-Mar-16 A	17-Jun-18	-353	—											
PO-Xb_1	Possession of Portion Xb (Day 804) - ADB Northern Portion	589	07-Mar-16 A	17-Jun-18	-353	—											
PO-Vb1	Possession of Portion V (Day 607) - SR3	587	11-Mar-16 A	17-Jun-18	91	—											

- ◆ Current Milestone
- Level of Effort
- ▲ Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 1 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
						PO-Ia	Possession of Portion Ia (Day 789) - SCB / SCP1 / SCP2 / Rumsey Street Flyover	600	28-Mar-16 A
PO-VII_a2	Possession of Portion VII (Day 762) - CH3800-3911 (below -6.0mPD)	567	31-Mar-16 A	17-Jun-18	-190				
PO-IXc_1	Possession of Portion IXc (Day 712) - EVB above 3.6mPD - Relinquished on 12 Apr 2016	445	29-Jul-16 A	17-Jun-18	-353				
PO-IXb_1	Possession of Portion IXb (Day 712) - EVB (below +3.6mPD to tunnel top slab) - Relinquished on 12 Apr 2016	445	05-Aug-16 A	17-Jun-18	-353				
PO-VIa_a	Possession of Portion VIa (Day 823) - CH3250-3283	425	15-Aug-16 A	17-Jun-18	-167				
PO-Vb2_a	Possession of Portion V (Day 607) - SR2	456	15-Aug-16 A	17-Jun-18	-183				
PO-VIc_a	Possession of Portion VIc (Day 761) - CH3770-3800 (Access Shaft Opening)	391	23-Sep-16 A	17-Jun-18	-172				
PO-VIb_c	Possession of Portion VIb (Day 761) - CH3625-3770	391	23-Sep-16 A	17-Jun-18	-172				
PO-IVa1	Possession of Portion IVa (Day 930) - CH2600-2720	323	30-Nov-16 A	17-Jun-18	-172				
PO-IVb2	Possession of Portion IVb (Day 930) - MVB (GLD-H)	233	28-Feb-17 A	17-Jun-18	-367				
PO-VIIIa_a	Possession of Portion VIIIa (Day 929) - CH4530-4591 W/B	233	28-Feb-17 A	17-Jun-18	-224				
PO-VIIIa	Possession of Portion VIIIa (Day 929) - CH4250-4600 (Remaining)	241	12-Mar-17 A	17-Jun-18	-224				
PO-VIIIb	Possession of Portion VIIIb (Day 929) - SR8 (CH700-350)	233	12-Mar-17 A	17-Jun-18	-187				
PO-VIIIc	Possession of Portion VIIIc (Day 1039) - SR8 (CH350-310) / SCP4	233	12-Mar-17 A	17-Jun-18	-190				
PO-IVa2_a	Possession of Portion IVa (Day 930) - CH2720-2950	241	12-Mar-17 A	17-Jun-18	-172				
PO-IVb1	Possession of Portion IVb (Day 930) - MVB (GLA-C)	239	14-Mar-17 A	17-Jun-18	-367				
PO-IVa2_b	Possession of Portion IVa (Day 930) - SR1	203	30-Mar-17 A	17-Jun-18	-172				
PO-Vb2_b	Possession of Portion V (Day 607) - SCP3	182	03-Jul-17 A	17-Jun-18	-183				
PO-VIb_a	Possession of Portion VIb (Day 761) - CH3400-3428	80	31-Jul-17 A	17-Jun-18	-166				
PO-VIa_b	Possession of Portion VIa (Day 823) - CH3283-3400	80	31-Jul-17 A	17-Jun-18	-206				
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-May-18	07-Sep-18	-185				
<b>Submissions and Approvals</b>									
Initial General Submission									
10168	Submission of CMC 3DVR	30	20-May-18	18-Jun-18	90				

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 2 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

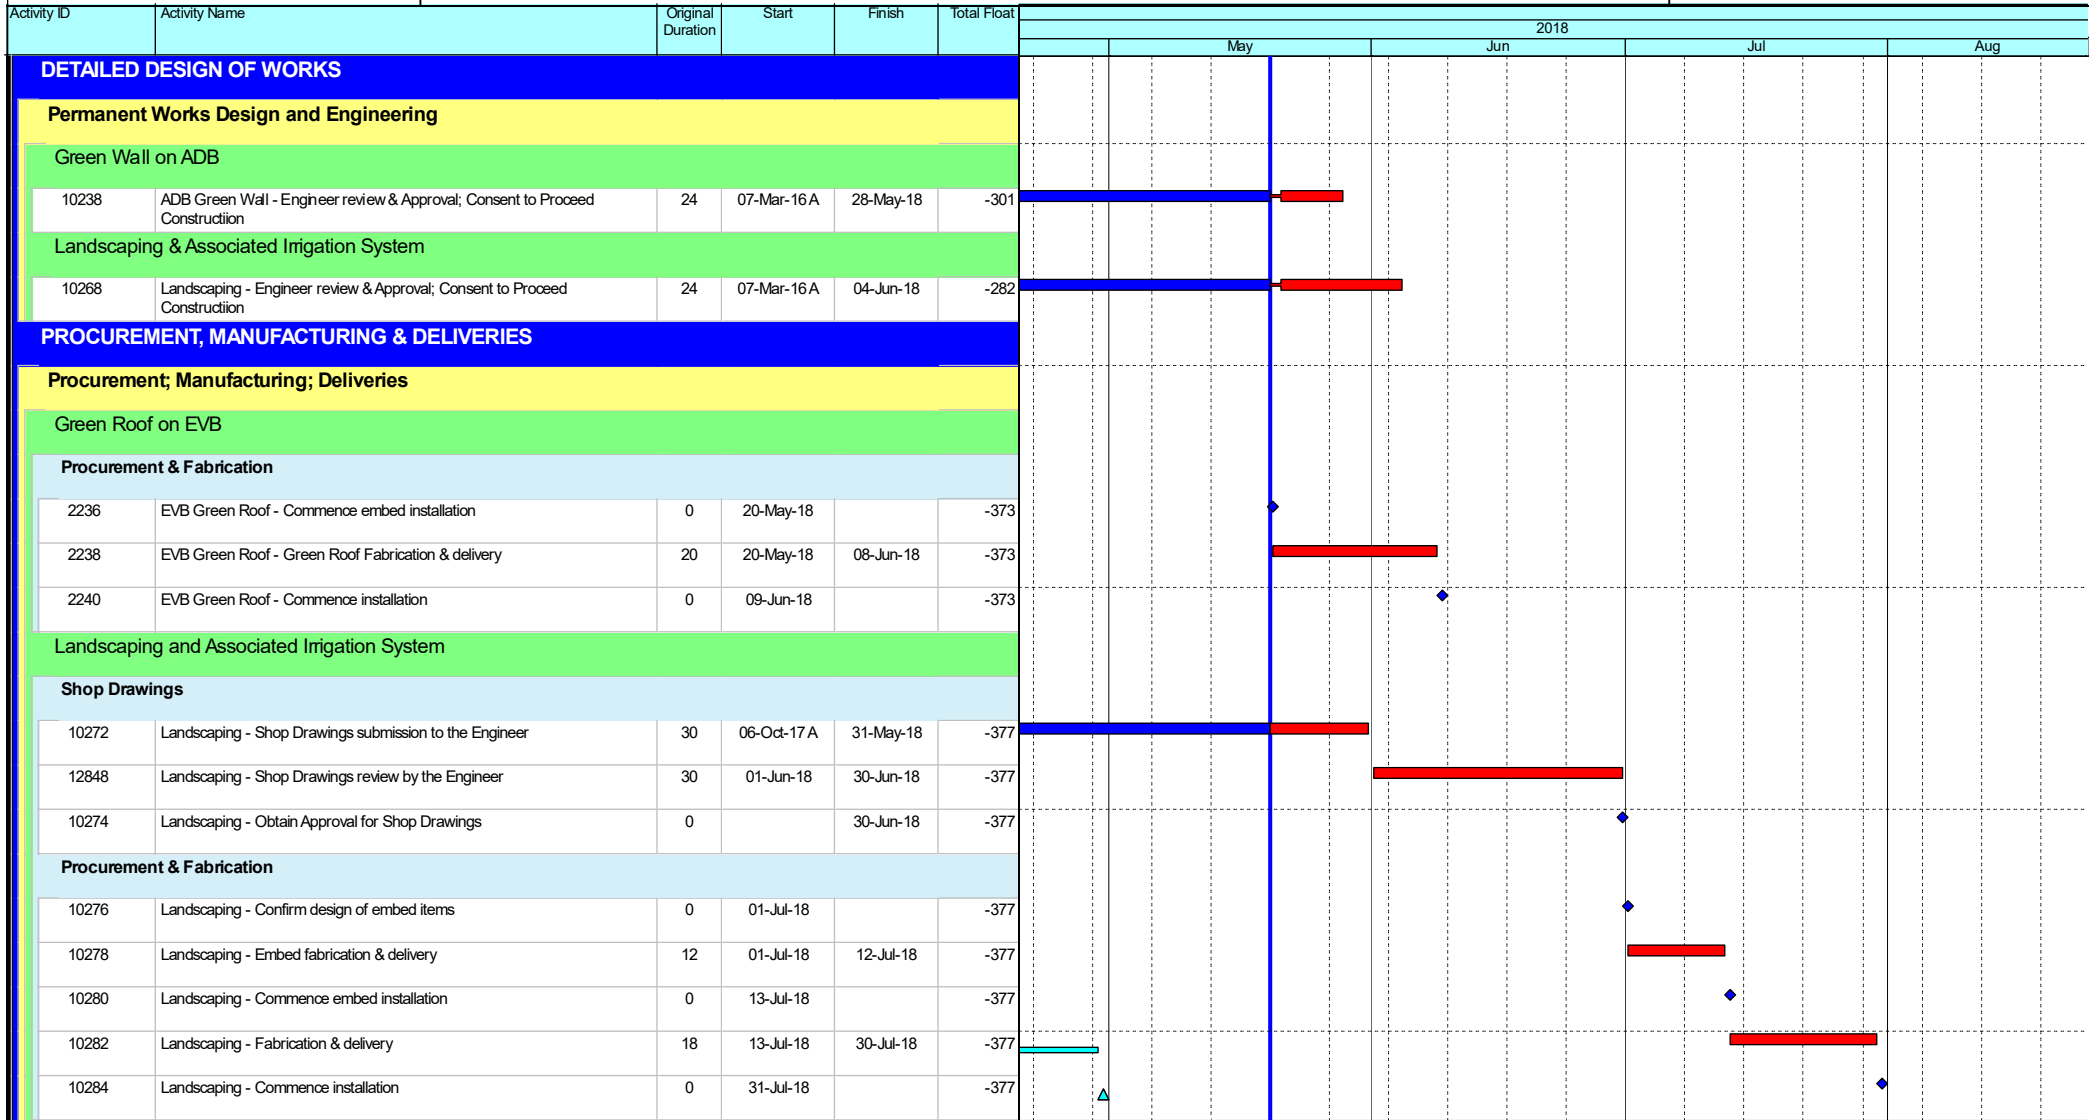

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
Baseline: SA01  
Layout: Update Three Month Rolling  
U051  
Page 3 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
<b>Green Wall on ADB</b>									
<b>Shop Drawings</b>									
12850	ADB Green Wall - Shop Drawings review the Engineer	18	11-Apr-18 A	26-May-18	-374				
10244	ADB Green Wall - Obtain Approval for Shop Drawings	0		26-May-18	-374				
<b>Procurement &amp; Fabrication</b>									
10246	ADB Green Wall - Confirm design of embed items	0	27-May-18		-374				
10248	ADB Green Wall - Embed fabrication & delivery	30	27-May-18	25-Jun-18	-374				
10250	ADB Green Wall - Commence embed installation	0	26-Jun-18		-374				
10252	ADB Green Wall - Green Wall Fabrication & delivery	52	26-Jun-18	16-Aug-18	-374				
10254	ADB Green Wall - Commence installation	0	17-Aug-18		-374				
<b>Architectural Feature on EVS</b>									
<b>Procurement &amp; Fabrication</b>									
10086	EVS - Architectural Features delivery	60	02-Jun-17 A	29-May-18	-150				
<b>Air Purification System (APS)</b>									
<b>Procurement &amp; Fabrication</b>									
13664	APS - Ship to HK Store (3rd Batch)	80	03-Aug-17 A	30-May-18	-155				
2368	APS - QA Stored Equipment	6	23-Aug-17 A	30-May-18	-155				
<b>CONSTRUCTION</b>									
<b>West Ventilation Building (WVB - related)</b>									
<b>Tunnel Section (WVB-related)</b>									
<b>Portion 1a, 1lc [CH840 to CH1360]</b>									
13086	TCSS cabling and sign face installation (FADS01)	40	21-May-18*	09-Jul-18	44				
<b>Westbound</b>									
5016	MEP(WB) - (CH840 to CH1360) E&M Final Fix	24	23-Mar-18 A	04-Jun-18	72				

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 4 of 34



Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW



Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

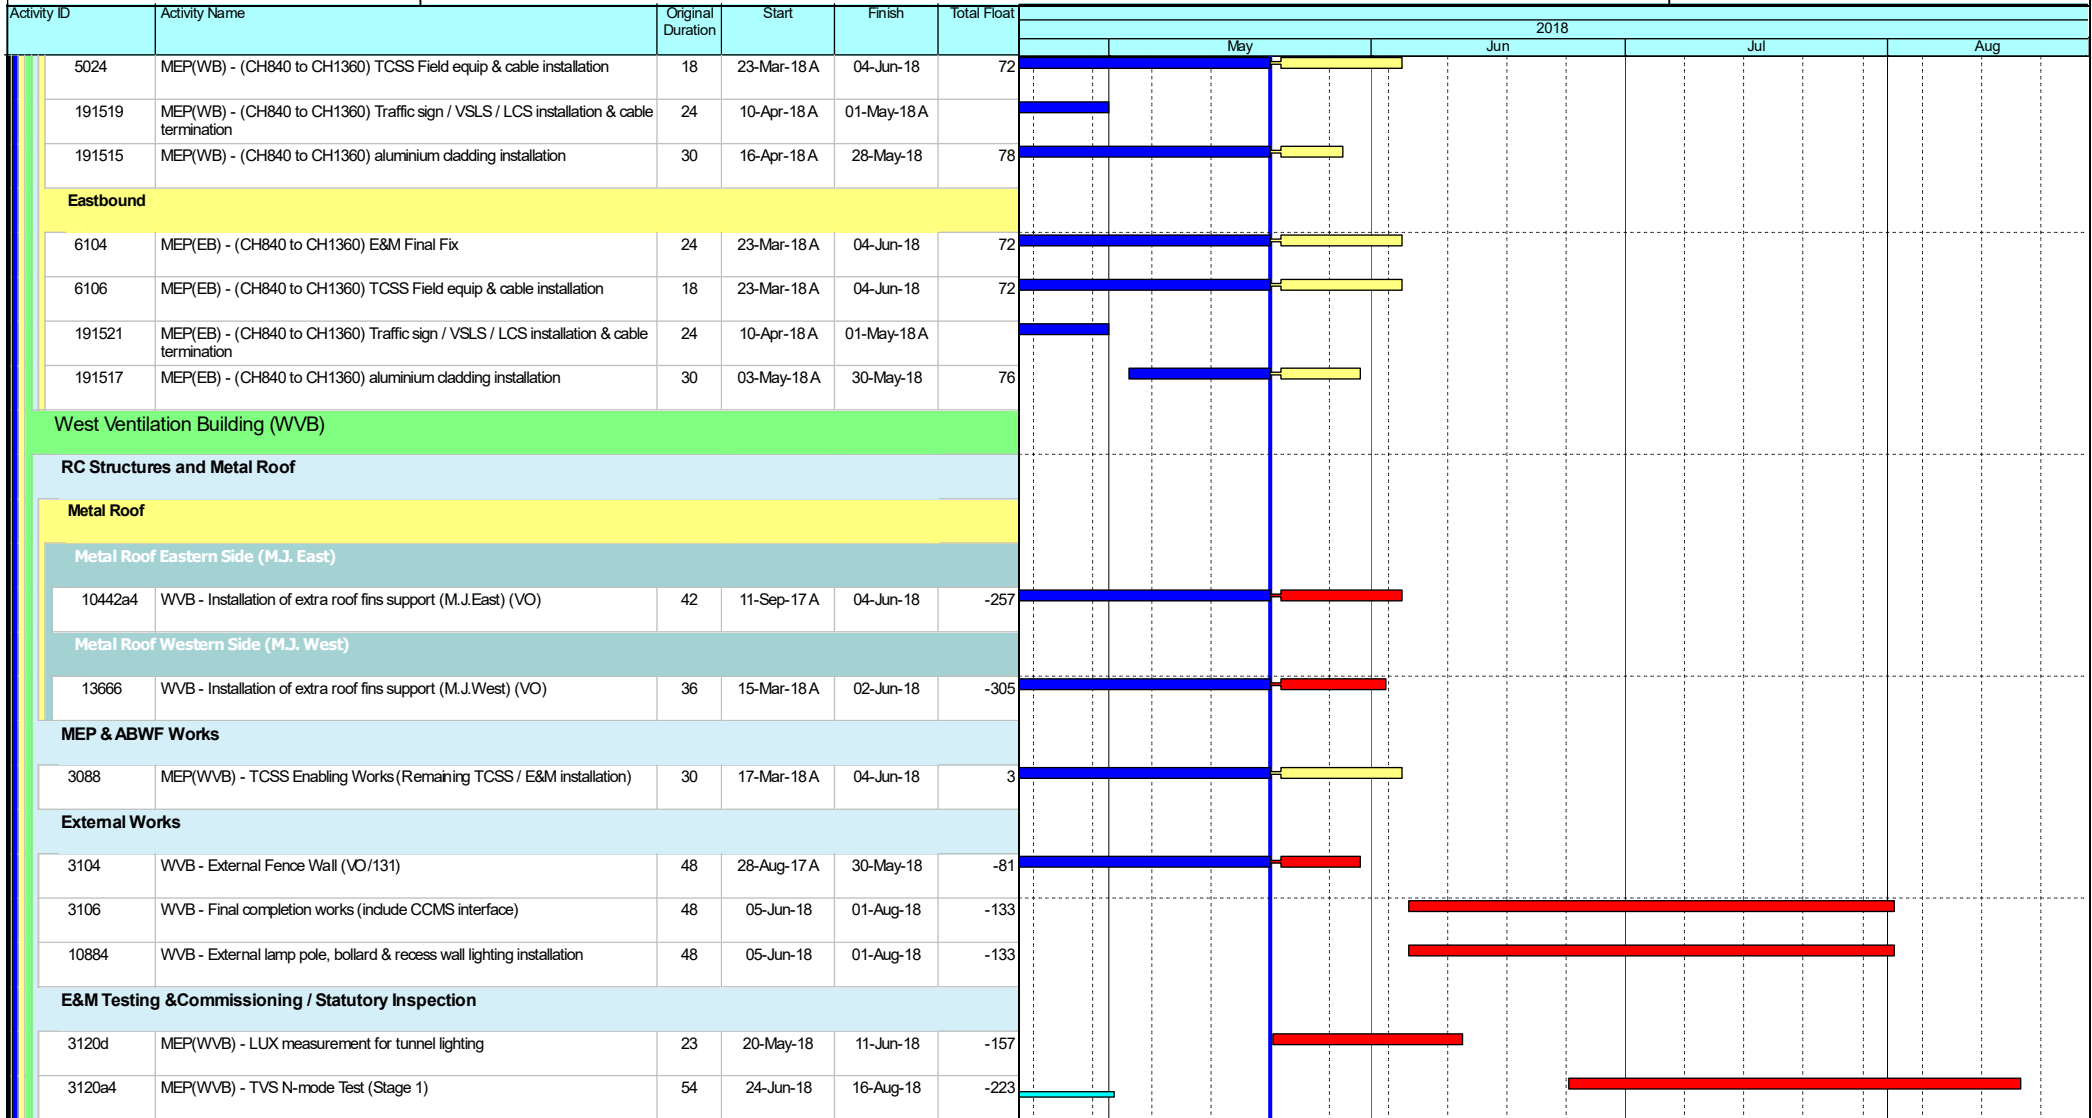

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 5 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
<b>Final Completion Works</b>									
191501	WVB - LHDS (Changed from Non-FSI to FSI item) - manufacture and delivery	36	14-Feb-18 A	12-May-18 A					
3132	WVB - APS Site Acceptance Test (Air monitoring station)	42	17-Mar-18 A	31-May-18	17				
191503	WVB - LHDS (Changed from Non-FSI to FSI item) - installation	30	14-May-18 A	13-Jun-18	-155				
KD04M2	APS SAT (WVB) - Milestone for KD04	0		31-May-18	108				
191505	WVB - LHDS (Changed from Non-FSI to FSI item) - T&C	8	14-Jun-18	23-Jun-18	-155				
3134	WVB - TCSS & other E&M systems Site Acceptance Test	18	10-Jul-18	27-Jul-18	51				
KD05M2	TCSS SAT (WVB) - Milestone for KD05	0		27-Jul-18	51				
3140	WVB - Completion of Section 1 (KD06)	0		01-Aug-18	-171				
<b>Landscaping and Irrigation Systems</b>									
3136	WVB - Final completion test for irrigation systems in Portion IIb	60	03-Jun-18	01-Aug-18	-379				
3138	WVB - Landscape Works in Portion IIb (Include architectural lightings & lightning protection system installation)	60	02-Aug-18	30-Sep-18	-379				
<b>Tunnel Flexible Pavement (WVB-related)</b>									
5802	Road(WB) - (CH1480 to CH2600) Road Marking & Traffic Sign	14	11-Jul-18	26-Jul-18	-212				
5806	Road(EB) - (CH1480 to CH2600) Road Marking & Traffic Sign	14	27-Jul-18	11-Aug-18	-212				
<b>Satellite Control Building (SCB)</b>									
<b>External Facade</b>									
3930	SCB - External facing tiles / Louvre	48	12-Oct-17 A	03-May-18 A					
<b>MEP Works</b>									
3944	MEP(SCB) - E&M Final Completion Works, Ready for Statutory Inspections	30	18-Apr-18 A	07-May-18 A					
<b>External Works</b>									
3948	SCB - Final completion works (include CCMS interface)	18	04-Apr-18 A	24-Apr-18 A					
<b>E&amp;M Testing &amp; Commissioning</b>									
3950	MEP (SCB) - E&M System Integrated Testing and Commissioning	30	18-Apr-18 A	09-May-18 A					

- Current Milestone
- Remaining Work
- Level of Effort
- Project Baseline
- Baseline Milestone
- Actual Work
- Critical Remaining Work

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 6 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018				
						May	Jun	Jul	Aug	
KD01M4	MEP (SCB) - Milestone for KD06	0		24-Apr-18 A						
<b>Final Completion Works</b>										
3958	SCB - TCSS & other E&M systems Site Acceptance Test	45	20-May-18	03-Jul-18	-142		[Red Bar]			
3962	SCB - Completion of Section 1	0		03-Jul-18	-142					◆
KD05M6	TCSS SAT (SCB) - Milestone for KD05	0		03-Jul-18	75					◆
<b>Satellite Control Points 1 / 2</b>										
<b>SCP1</b>										
3716	MEP (SCP1) - E&M Final Fix	18	04-Apr-18 A	23-May-18	73	[Blue Bar]				
3718	MEP (SCP1) - E&M Individual System T&C (Include TCSS T&C)	12	24-May-18	06-Jun-18	73		[Yellow Bar]			
3720	MEP (SCP1) - E&M Final Completion Works	12	07-Jun-18	21-Jun-18	73			[Yellow Bar]		
KD01M2	MEP (SCP1) - Milestone for KD06	0		21-Jun-18	73					◆
<b>SCP2</b>										
3740	MEP (SCP2) - E&M Final Fix	18	02-Dec-17 A	23-May-18	85	[Blue Bar]				
3742	MEP (SCP2) - E&M Individual System T&C	12	24-May-18	06-Jun-18	85		[Yellow Bar]			
3744	MEP (SCP2) - E&M Final Completion Works	12	24-May-18	06-Jun-18	85		[Yellow Bar]			
KD01M3	MEP (SCP2) - Milestone for KD06	0		06-Jun-18	85					◆
<b>Middle Ventilation Building (MVB - related)</b>										
<b>Tunnel Section (MVB-related)</b>										
<b>Portion IVa (CH2600 to CH2950)</b>										
<b>Slip Road 1</b>										
10022	MEP(SR1) - (CH171 to CH271) E&M Final Fix	4	15-Mar-18 A	23-May-18	-131	[Blue Bar]				
10046	MEP(SR1) - (CH171 to CH271) VE Panel installation (Upper part) (1200m2)	13	24-May-18	07-Jun-18	-131		[Red Bar]			
10046a	MEP(SR1) - (CH171 to CH271) VE Panel installation (Lower part) (1200m2)	13	24-May-18	07-Jun-18	-131		[Red Bar]			
10024	MEP(SR1) - (CH171 to CH271) TCSS Field equip & cable installation	6	26-May-18	01-Jun-18	74		[Yellow Bar]			

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 7 of 34


Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
10046b	VO 238 - SR1 - Anticipated handover from WDII	0	01-Jun-18*		-183				
10046c	VO 238 - SR1 - Construction of D-wall plinth and install wall brackets	12	01-Jun-18	14-Jun-18	-183				
10046d	VO 238 - SR1 - Installation of granite stone panels / precast concrete panels	40	15-Jun-18	02-Aug-18	-183				
10046e	VO 238 - SR1 - Application of Evonik Protectosil SC60	6	03-Aug-18	09-Aug-18	-183				
<b>Portion Va [CH2950 to CH3210]</b>									
<b>Westbound (Outer Lane)</b>									
5136a	MEP(WB) - (CH2950 to CH3210) E&M Final Fix	10	16-Aug-17 A	23-May-18	-150				
9954a	MEP(WB) - (CH2950 to CH3210) VE Panel installation (Upper part) (1800m2)	20	11-Apr-18 A	28-May-18	-154				
<b>Eastbound (Outer Lane)</b>									
5156a	MEP(EB) - (CH2950 to CH3210) E&M Final Fix	10	03-Apr-18 A	23-May-18	-118				
9956a	MEP(EB) - (CH2950 to CH3210) VE Panel installation (Upper part) (1800m2)	20	09-Apr-18 A	04-Jun-18	-128				
<b>Portion Vb1 (SR3)</b>									
<b>Slip Road 3</b>									
10032b	MEP(SR3) - (CH3089 to CH3334) E&M 1st Fix	13	15-Mar-17 A	25-May-18	-132				
10036b	MEP(SR3) - (CH3089 to CH3334) TCSS Field equip & cable installation	8	15-Mar-17 A	25-May-18	-132				
10048c	MEP(SR3) - (CH3089 to CH3334) VE Panel installation (Lower part) (2940m2)	33	06-Mar-18 A	29-May-18	-135				
10034b	MEP(SR3) - (CH3089 to CH3334) E&M 2nd Fix (include Sump C)	27	11-Apr-18 A	28-May-18	-134				
10038b	MEP(SR3) - (CH3089 to CH3334) E&M Final Fix	8	16-Apr-18 A	29-May-18	-135				
10048b	MEP(SR3) - (CH3089 to CH3334) VE Panel installation (Upper part) (2940m2)	33	21-May-18	29-Jun-18	-161				
10048d	VO 238 - Prepare and finalize design of grouting pad	11	21-May-18*	02-Jun-18	-184				
10048e	VO 238 - Construction of grouting pad	5	04-Jun-18	08-Jun-18	-184				
10048f	VO 238 - Drill and fix wall bracket	11	09-Jun-18	22-Jun-18	-184				
10048c2	MEP(SR3) - Road lighting installation (Portal)	18	12-Jun-18	04-Jul-18	-164				
10048h	VO 238 - Installation of precast concrete	22	23-Jun-18	19-Jul-18	-184				



### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
Baseline: SA01  
Layout: Update Three Month Rolling  
U051  
Page 8 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
10048g	VO 238 - Installation of granite stone	5	26-Jun-18	30-Jun-18	-169				
10048i	VO 238 - Application of Evonik Protectosil SC60 at SR3	7	20-Jul-18	27-Jul-18	-184				
<b>Portion Vb2 (SR2 / SCP3)</b>									
<b>Slip Road 2</b>									
10050b	MEP(SR2) - (CH3114 to CH3257) E&M 1st Fix	8	08-Mar-17 A	23-May-18	-136				
10056b	MEP(SR2) - (CH3114 to CH3257) TCSS Field equip & cable installation	5	16-Mar-17 A	25-May-18	-143				
10052b	MEP(SR2) - (CH3114 to CH3257) E&M 2nd Fix (include Sump F)	40	15-Jun-17 A	04-Jun-18	-146				
10064c	MEP(SR2) - (CH3114 to CH3257) VE Panel installation (Lower part) (1716m2)	18	02-Mar-18 A	28-May-18	-122				
10064b2	MEP(SR2) - Road lighting installation (Portal)	18	21-May-18	11-Jun-18	-164				
10054b	MEP(SR2) -(CH3114 to CH3257) E&M Final Fix	5	30-May-18	04-Jun-18	-146				
10064b	MEP(SR2) - (CH3114 to CH3257) VE Panel installation (Upper part) (1716m2)	18	05-Jun-18	26-Jun-18	-146				
<b>Portion Vc [CH3210 to CH3250]</b>									
<b>Westbound (Outer Lane)</b>									
5136c	MEP(WB) - (CH3210 to CH3250) E&M Final Fix	10	15-Mar-18 A	23-May-18	-130				
9954c	MEP(WB) - (CH3210 to CH3250) VE Panel installation (Upper part) (1800m2)	20	29-May-18	21-Jun-18	-154				
<b>Eastbound (Outer Lane)</b>									
5156c	MEP(EB) - (CH3210 to CH3250) E&M Final Fix	10	11-Apr-18 A	23-May-18	-118				
9956c	MEP(EB) - (CH3210 to CH3250) VE Panel installation (Upper part) (1800m2)	20	02-Jun-18	26-Jun-18	-146				
<b>Portion VIa [CH3250 to CH3283]</b>									
<b>Westbound</b>									
5166a	MEP(WB) - (CH3250 to CH3283) E&M 2nd Fix	6	27-Nov-17 A	23-May-18	-130				
5168a	MEP(WB) - (CH3250 to CH3283) E&M Final Fix	5	17-Apr-18 A	24-May-18	-131				
9958a	MEP(WB) - (CH3250 to CH3283) VE Panel installation (Upper part) (526m2)	6	19-Apr-18 A	24-May-18	-131				
<b>Eastbound</b>									

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Actual Work
- ▬ Critical Remaining Work
- Remaining Work
- Project Baseline
- ▲ Baseline Milestone

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 9 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
5182a	MEP(EB) - (CH3250 to CH3283) E&M 1st Fix	6	11-Nov-17 A	23-May-18	-118				
5184a	MEP(EB) - (CH3250 to CH3283) E&M 2nd Fix	6	06-Mar-18 A	24-May-18	-119				
5186a	MEP(EB) - (CH3250 to CH3283) E&M Final Fix	5	22-Mar-18 A	25-May-18	-120				
9960a	MEP(EB) - (CH3250 to CH3283) VE Panel installation (Upper part) (528m2)	6	18-Apr-18 A	26-May-18	-121				
<b>Portion VIa [CH3283 to CH3400]</b>									
<b>Westbound</b>									
5166b	MEP(WB) - (CH3283 to CH3400) E&M 2nd Fix	17	07-Dec-17 A	28-May-18	-128				
5168b	MEP(WB) - (CH3283 to CH3400) E&M Final Fix	12	04-Apr-18 A	28-May-18	78				
9958b	MEP(WB) - (CH3283 to CH3400) VE Panel installation (Upper part) (1872m2)	21	10-Apr-18 A	01-Jun-18	-138				
<b>Eastbound</b>									
5186b	MEP(EB) - (CH3283 to CH3400) E&M Final Fix	12	06-Mar-18 A	28-May-18	-168				
9960b	MEP(EB) - (CH3283 to CH3400) VE Panel installation (Upper part) (1872m2)	21	16-Apr-18 A	04-Jun-18	-128				
<b>Portion VIb [CH3400 to CH3428]</b>									
<b>Eastbound</b>									
5218b1	MEP(EB) - (CH3400 to CH3428) E&M Final Fix	12	03-Apr-18 A	23-May-18	82				
<b>Middle Ventilation Building (MVB)</b>									
<b>External Facade</b>									
3238	MVB - External facing tiles / Louvre	90	06-Nov-17 A	30-May-18	-177				
<b>MEP Works</b>									
3280	MEP(MVB) - Lift Installation	70	10-Nov-17 A	23-May-18	-316				
3236	MVB - Metal works / steel platform / Ladders / Handrails	48	06-Dec-17 A	28-May-18	-151				
3248	MEP(MVB) - TCSS Enabling Works (Remaining TCSS installation)	24	03-Jan-18 A	23-May-18	-296				
3280a	MEP(MVB) - lift shaft water leakage (Fix by C19) - Tentative fixed date on 31-May-2018	70	17-May-18 A	23-May-18	-316				
3252	MEP(MVB) - E&M Final Completion Works; Ready for Statutory Inspections	24	31-May-18	28-Jun-18	-177				

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 10 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018					
						May	Jun	Jul	Aug		
<b>E&amp;M Individual System T&amp;C</b>											
3250d	MEP(MVB) - CCMS SAT	12	07-Apr-18 A	11-May-18 A							
3250a	MEP(MVB) - MVAC system	12	23-Apr-18 A	05-May-18 A							
3250h	MEP(MVB) - SAT - LV Capacitor Bank	6	25-Apr-18 A	28-Apr-18 A							
3250b	MEP(MVB) - TVS System Test	12	03-May-18 A	05-May-18 A							
3250m	MEP(MVB) - Damper control panel and tunnel motorized damper functional test	6	09-May-18 A	23-May-18	-296						
3250g	MEP(MVB) - SAT - UPS	6	10-May-18 A	15-May-18 A							
3250c	MEP(MVB) - Lift functional test	6	24-May-18	30-May-18	-253						
<b>Basement 3 - APS Auxiliary Room / APS Plant Area 1 / APS Plant Area 2 (GL D - H)</b>											
3302	APS(MVB) - E&M final fixing	24	01-Mar-18 A	24-May-18	-175						
<b>Basement 3 - Other Rooms / General Area &amp; Corridor</b>											
3407	MEP(MVB) - E&M final fixing	18	12-Mar-18 A	23-May-18	-147						
<b>Basement 3M - Sump Pit for ESP / Sump Pit for DENO2 (GL D - H)</b>											
3296	APS(MVB) - Plant 4 ESP/DeNO2	24	13-Jan-18 A	30-May-18	-170						
<b>Basement 3M - TVF Room</b>											
3309	APS(MVB) - E&M Final Fix	18	07-Mar-18 A	23-May-18	-164						
<b>Basement 3M - Other Rooms / General Area &amp; Corridor</b>											
3313	MEP(MVB) - E&M 1st fixing	24	23-Nov-17 A	25-May-18	-149						
3315	MEP(MVB) - E&M 2nd fixing	24	20-Dec-17 A	28-May-18	-151						
3317	MEP(MVB) - E&M final fixing	24	07-Feb-18 A	04-Jun-18	-157						
<b>Basement 2 (GL D - H)</b>											
<b>Basement 2 - Other Rooms / General Area &amp; Corridor</b>											
19030	MEP(MVB) - E&M 1st fixing	18	28-Nov-17 A	25-May-18	-149						
19032	MEP(MVB) - E&M 2nd fixing	18	19-Dec-17 A	28-May-18	-151						

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
Baseline: SA01  
Layout: Update Three Month Rolling  
U051  
Page 11 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
19034	MEP(MVB) - E&M final fixing	18	12-Feb-18 A	01-Jun-18	-155				
<b>Basement 2M (GL D - H)</b>									
Basement 2M - Other Rooms / General Area & Corridor									
19047	MEP(MVB) - E&M 1st fixing	18	02-Dec-17 A	28-May-18	-151				
19049	MEP(MVB) - E&M 2nd fixing	18	19-Dec-17 A	01-Jun-18	-155				
19051	MEP(MVB) - E&M final fixing	18	07-Mar-18 A	04-Jun-18	-157				
<b>Basement 1 (GL D - H)</b>									
Other Rooms / General Area & Corridor									
11314	MEP(MVB) - E&M 1st fixing	24	13-Oct-17 A	25-May-18	-149				
11316	MEP(MVB) - E&M 2nd fixing	24	06-Dec-17 A	28-May-18	-151				
11318	MEP(MVB) - E&M final fixing	24	20-Feb-18 A	01-Jun-18	-155				
<b>Basement 1 (GL A - D)</b>									
MCC Room 1 (B1-04)									
11286	MEP(MVB) - E&M final fixing	24	25-Nov-17 A	25-May-18	-166				
UPS Room 1 (B1-11)									
11294	MEP(MVB) - E&M final fixing	24	09-Dec-17 A	25-May-18	-166				
<b>G/F (GL D - H)</b>									
TVF Fan Room 1 (G-01)									
11396	MEP(MVB) - E&M final fixing	12	01-Mar-18 A	23-May-18	-164				
TVF Fan Room 2 (G-02)									
11404	MEP(MVB) - E&M final fixing	24	03-Mar-18 A	25-May-18	-166				
Other Rooms / General Area & Corridor									
11412	MEP(MVB) - E&M final fixing	24	21-Feb-18 A	23-May-18	-164				
<b>G/F (GL A - D)</b>									

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 12 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW



Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018					
						May	Jun	Jul	Aug		
<b>Fire Control Centre (G-11)</b>											
11380	MEP(MVB) - E&M final fixing	12	02-Mar-18 A	25-May-18	-166						
<b>Other Rooms / General Area &amp; Corridor</b>											
11384	MEP(MVB) - E&M 1st fixing	24	12-Dec-17 A	23-May-18	-147						
11386	MEP(MVB) - E&M 2nd fixing	24	21-Dec-17 A	28-May-18	-151						
11388	MEP(MVB) - E&M final fixing	24	02-Mar-18 A	01-Jun-18	-155						
<b>1/F (GL D - H)</b>											
<b>Other Rooms / General Area &amp; Corridor</b>											
11446	MEP(MVB) - E&M final fixing	18	21-Feb-18 A	23-May-18	-164						
<b>1/F (GL A - D)</b>											
<b>FS Water Tank &amp; Pump Room (L1-05)</b>											
11420	MEP(MVB) - E&M final fixing	12	15-Mar-18 A	23-May-18	-164						
<b>Other Rooms / General Area &amp; Corridor</b>											
11434	MEP(MVB) - E&M 1st fixing	18	14-Dec-17 A	23-May-18	-147						
11436	MEP(MVB) - E&M 2nd fixing	18	29-Dec-17 A	28-May-18	-151						
11438	MEP(MVB) - E&M final fixing	18	15-Feb-18 A	04-Jun-18	-157						
<b>Staircase Pressurization System (B3/F - G/F)</b>											
<b>B3/F - G/F</b>											
191513	SPS(MVB) - new by-pass MSFD	18	16-Apr-18 A	23-Apr-18 A							
191469	SPS(MVB) - LMCP installation	6	18-Apr-18 A	20-Apr-18 A							
191471	SPS(MVB) - SPS control panel	6	18-Apr-18 A	23-Apr-18 A							
191473	SPS(MVB) - Termination	6	24-Apr-18 A	25-Apr-18 A							
191475	SPS(MVB) - Testing & Commissioning	12	26-Apr-18 A	04-May-18 A							
<b>Smoke Extraction System (B3/F - G/F)</b>											

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 13 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

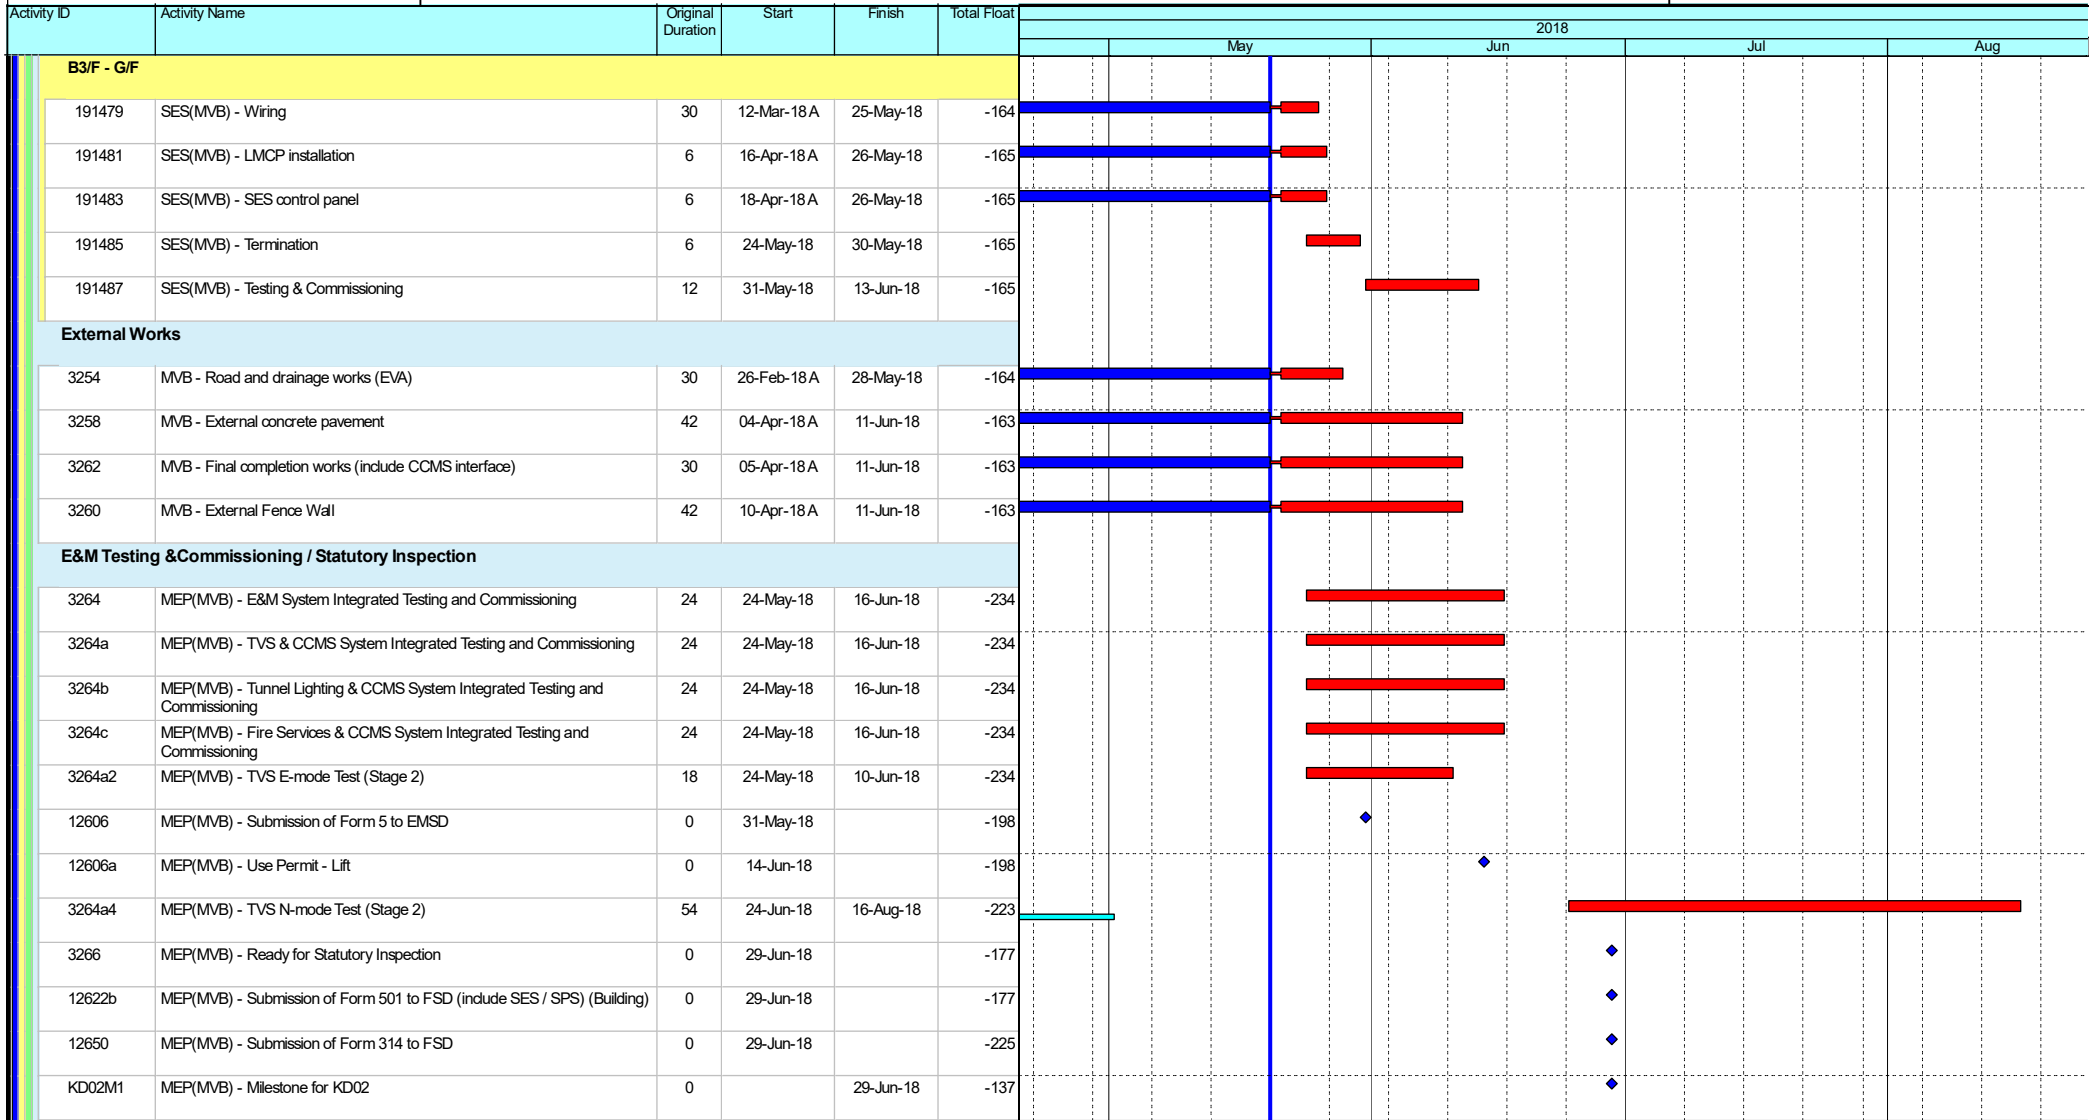

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 14 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

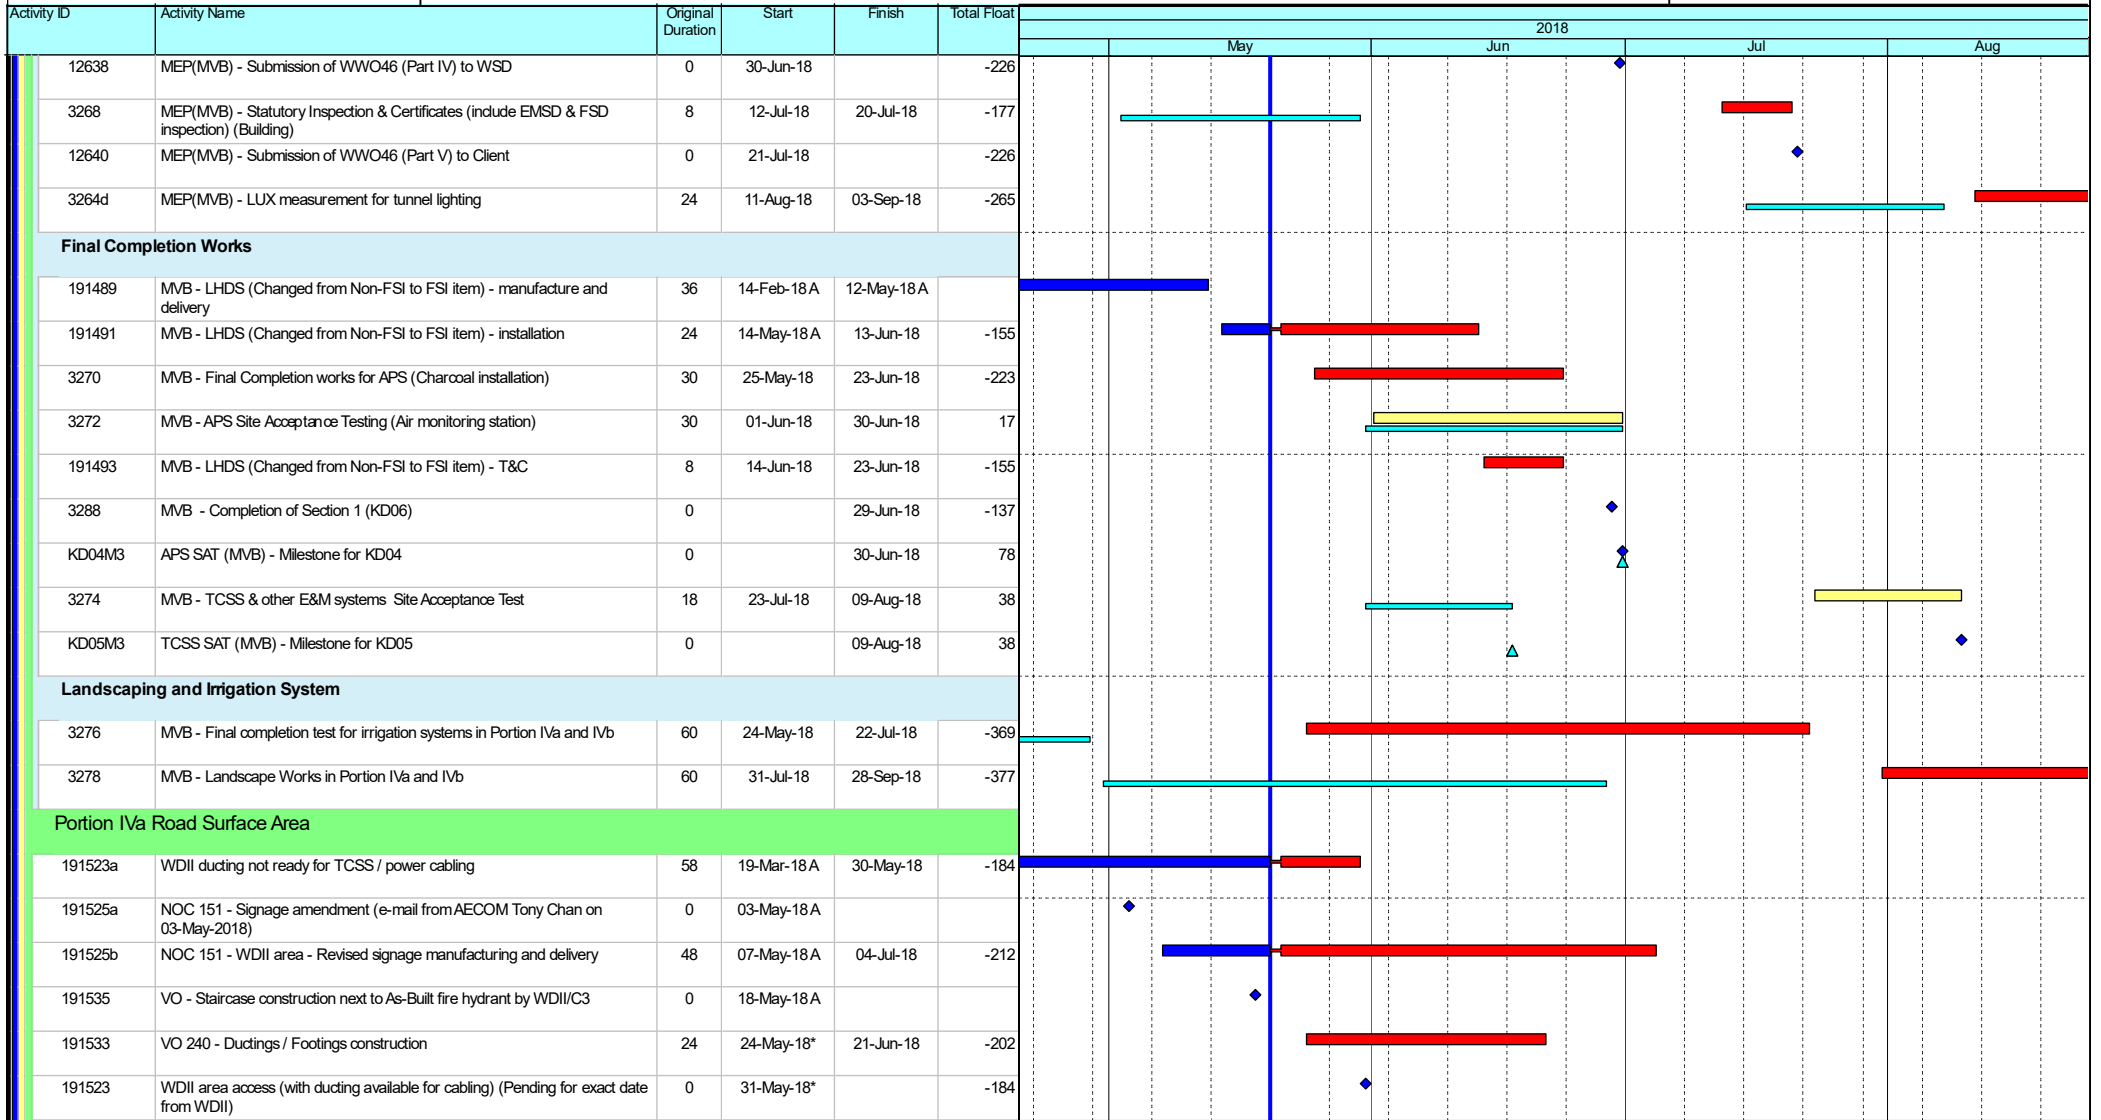

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 15 of 34








Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
191537	VO - Staircase construction and railing installation	12	11-Jun-18*	25-Jun-18	-174				
191525	WDII area - TCSS equipment / signage / lumimeter installation, cabling & termination	24	05-Jul-18	01-Aug-18	-212				
191527	WDII area - TCSS SCT	24	02-Aug-18	29-Aug-18	-212				
<b>Satellite Control Point 3</b>									
<b>SCP3</b>									
3766	MEP(SCP3) - E&M Final Fix	12	12-Dec-17 A	23-May-18	73				
3774	SCP3 - Metal works / Glazing / Louver / Handrails	12	19-Apr-18 A	04-May-18 A					
10110	MEP(SCP3) - TCSS Enabling Works (Remaining TCSS installation)	12	21-May-18	04-Jun-18	3				
3768	MEP(SCP3) - E&M Individual System T&C	12	24-May-18	06-Jun-18	73				
3770	MEP(SCP3) - E&M Final Completion Works; Ready for Statutory Inspections	12	07-Jun-18	21-Jun-18	73				
KD02M2	MEP(SCP3) - Milestone for KD06	0		21-Jun-18	73				
<b>East Ventilation Building (EVB - related)</b>									
<b>Tunnel Section (EVB-related)</b>									
<b>Portion VIc [CH3770 to CH3800]</b>									
<b>Eastbound</b>									
5220c	MEP(EB) - (CH3770 to CH3800) E&M 2nd Fix	12	21-Dec-17 A	23-May-18	-123				
5218c	MEP(EB) - (CH3770 to CH3800) E&M Final Fix	12	13-Mar-18 A	28-May-18	-127				
9964c	MEP(EB) - (CH3770 to CH3800) VE Panel installation (Upper part) (450m2)	5	29-May-18	02-Jun-18	-127				
<b>Portion VII [CH3800 to CH3911]</b>									
<b>Eastbound</b>									
9968a4	MEP(EB) - (CH3800 to CH3911) VE Panel installation (Upper part) (1332m2)	14	09-Apr-18 A	25-May-18	-138				
<b>Portion VII [CH3911 to CH4250]</b>									
<b>Access Shaft Opening</b>									
10120a2	VII(WB) - Waterproofing on Shaft tunnel slab	18	17-Mar-18 A	18-May-18 A					

-  Current Milestone
-  Level of Effort
-  Baseline Milestone
-  Actual Work
-  Critical Remaining Work
-  Remaining Work
-  Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 16 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
10120a3	VI(WB) - Backfilling (78 layers; 1 day/layer)	78	05-Apr-18 A	23-May-18	97				
<b>Westbound</b>									
5232a2	MEP(WB) - (CH3911 to CH4250) E&M Final Fix	16	23-Mar-18 A	23-May-18	-136				
9966a2	MEP(WB) - (CH3911 to CH4250) VE Panel installation (Upper part) (4068m2)	21	11-Apr-18 A	25-May-18	-138				
<b>Eastbound</b>									
5250a2	MEP(EB) - (CH3911 to CH4250) E&M Final Fix	16	29-Mar-18 A	23-May-18	-151				
9968a2	MEP(EB) - (CH3911 to CH4250) VE Panel installation (Upper part) (4086m2)	12	14-Apr-18 A	25-May-18	-153				
<b>Portion VIIa [CH4250 to CH4600]</b>									
<b>Eastbound</b>									
9972	MEP(EB) - (CH4250 to CH4600) VE Panel installation (Upper part) (3900m2)	11	24-Jan-18 A	23-May-18	-136				
<b>Portion IXd [CH4600 to CH4860]</b>									
<b>Eastbound</b>									
9976	MEP(EB) - (CH4600 to CH4860) VE Panel installation (Upper part) (3300m2)	37	22-Mar-18 A	25-May-18	-138				
5314	MEP(EB) - (CH4600 to CH4860) E&M Final Fix	9	30-Mar-18 A	23-May-18	-136				
<b>Portion IXa [CH4860 to CH5150]</b>									
<b>Eastbound</b>									
5346	MEP(EB) - (CH4860 to CH5150) E&M Final Fix	10	14-Mar-18 A	23-May-18	67				
5348	MEP(EB) - (CH4860 to CH5150) TCSS Field equip & cable installation	9	04-Apr-18 A	23-May-18	67				
9980	MEP(EB) - (CH4860 to CH5150) VE Panel installation (Upper part) (3288m2)	37	05-Apr-18 A	28-May-18	-140				
<b>Portion VIIIc [SR8 CH350 to CH210]</b>									
<b>Slip Road 8</b>									
5378	MEP(SR8) - (CH350 to CH210) E&M Final Fix	5	03-Apr-18 A	23-May-18	-151				
<b>East Ventilation Building (EVB)</b>									
<b>RC Structures and Green Roof</b>									

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 17 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
3456	EVB - Green Roof (include architectural lighting & lightning protection system installation)	42	09-Jun-18	30-Jul-18	-297				
<b>External Facade</b>									
3438	EVB - External facing tiles / Treated Waste Wood / Louvre	90	11-Sep-17 A	28-May-18	-155				
<b>MEP Works</b>									
3436	EVB - Metal works / steel platform / Ladders / Handrails	48	29-Dec-17 A	28-May-18	-155				
3452	MEP(EVB) - E&M Final Completion Works; Ready for Statutory Inspections	21	11-Apr-18 A	04-Jun-18	-161				
<b>E&amp;M Individual System T&amp;C</b>									
3450d	MEP(EVB) - CCMS SAT	30	19-Jan-18 A	28-May-18	-249				
3450p	MEP(EVB) - Smoke Extraction System System Test	12	09-Mar-18 A	14-May-18 A					
3450c	MEP(EVB) - Lift functional test	6	18-Apr-18 A	10-May-18 A					
3450o	MEP(EVB) - Staircase Pressurization System Test	15	20-May-18	03-Jun-18	-202				
3660d	MEP(ADB) - LUX measurement for tunnel lighting	28	20-May-18	16-Jun-18	-162				
<b>Basement 1 (GL D - L)</b>									
<b>Water Tank &amp; Pump Room (B1-16)</b>									
11636	MEP(EVB) - E&M final fixing	24	04-Nov-17 A	03-May-18 A					
<b>TVF Room 3 (B1-19)</b>									
11628a4	MEP(EVB) - Thermal enclosure for actuator T&C	6	17-Apr-18 A	21-May-18	-192				
<b>Staircase Pressurization System (B2/F - G/F)</b>									
<b>B2/F - G/F</b>									
191531b	VO/232 - Lift Pressurization System (LPS) installation	49	12-Mar-18 A	12-May-18 A					
191345	SPS(EVB) - Airduct work and FRP enclosure	20	15-Mar-18 A	04-May-18 A					
191387	SPS(EVB) - Final connection of air duct after modification of air vent shaft	18	28-Mar-18 A	05-May-18 A					
191531c	Take down part of LPS system for injection - leakage from C19 concrete wall	1	10-May-18 A	10-May-18 A					
191531e	Change rusted pipes	3	11-May-18 A	14-May-18 A					

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 18 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
191531d	Install the part of LPS system back for FSD inspection	3	17-May-18 A	19-May-18 A					
<b>External Works</b>									
3454	EVB - Road and drainage works (EVA)	24	09-Nov-17 A	25-May-18	-153	[Gantt bar: blue from May to mid-May, red from mid-May to end of May]			
3462	EVB - Final completion works (include CCMS interface)	30	17-Jan-18 A	26-Jun-18	-179	[Gantt bar: blue from May to mid-May, red from mid-May to end of May]			
3458	EVB - External concrete pavement	24	24-Feb-18 A	28-May-18	-155	[Gantt bar: blue from May to mid-May, red from mid-May to end of May]			
<b>E&amp;M Testing &amp; Commissioning / Statutory Inspection</b>									
3464a	MEP(EVB) - TVS & CCMS System Integrated Testing and Commissioning	36	26-Mar-18 A	07-Jun-18	-225	[Gantt bar: blue from May to mid-May, red from mid-May to end of May]			
3464b	MEP(EVB) - Tunnel Lighting & CCMS System Integrated Testing and Commissioning	24	26-Mar-18 A	07-Jun-18	-225	[Gantt bar: blue from May to mid-May, red from mid-May to end of May]			
3464c	MEP(EVB) - Fire Services & CCMS System Integrated Testing and Commissioning	36	26-Mar-18 A	12-May-18 A		[Gantt bar: blue from May to mid-May]			
3464	MEP(EVB) - E&M System Integrated Testing and Commissioning	36	28-Mar-18 A	07-Jun-18	-209	[Gantt bar: blue from May to mid-May, red from mid-May to end of May]			
3464a2	MEP(EVB) - TVS E-mode Test (Stage 3)	25	03-Apr-18 A	15-May-18 A		[Gantt bar: blue from May to mid-May]			
KD03M1	MEP(EVB) - Milestone for KD03	0		16-May-18 A		[Milestone diamond]			
12608	MEP(EVB) - Submission of Form 5 to EMSD	0	19-May-18 A			[Milestone diamond]			
3464a4	MEP(EVB) - TVS N-mode Test (Stage 3)	48	31-May-18	17-Jul-18	-193	[Gantt bar: cyan from May to mid-May, red from mid-May to end of May]			
12608a	MEP(EVB) - Use Permit - Lift	0	02-Jun-18		-185	[Milestone diamond]			
3466	MEP(EVB) - Ready for Statutory Inspection	0	04-Jun-18		-202	[Milestone diamond]			
12624	MEP(EVB) - Submission of Form 501 to FSD (include SES / SPS) (Building)	0	04-Jun-18		-155	[Milestone diamond]			
12648	MEP(EVB) - Submission of Form 314 to FSD	0	04-Jun-18		-202	[Milestone diamond]			
12634	MEP(EVB) - Submission of WWO46 (Part IV) to WSD	0	06-Jun-18		-202	[Milestone diamond]			
3468	MEP(EVB) - Statutory Inspection & Certificates (include EMSD & FSD inspection) (Building)	7	19-Jun-18	26-Jun-18	-157	[Gantt bar: red from mid-May to end of May]			
12636	MEP(EVB) - Submission of WWO46 (Part V) to Client	0	27-Jun-18		-202	[Milestone diamond]			
<b>Final Completion Works</b>									
191495	EVB - LHDS (Changed from Non-FSI to FSI item) - manufacture and delivery	36	14-Feb-18 A	12-May-18 A		[Gantt bar: blue from May to mid-May]			
3472	EVB - APS Site Acceptance Testing (Air monitoring station)	30	17-Mar-18 A	31-May-18	17	[Gantt bar: blue from May to mid-May, yellow from mid-May to end of May]			

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Project Baseline
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Baseline Milestone

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 19 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

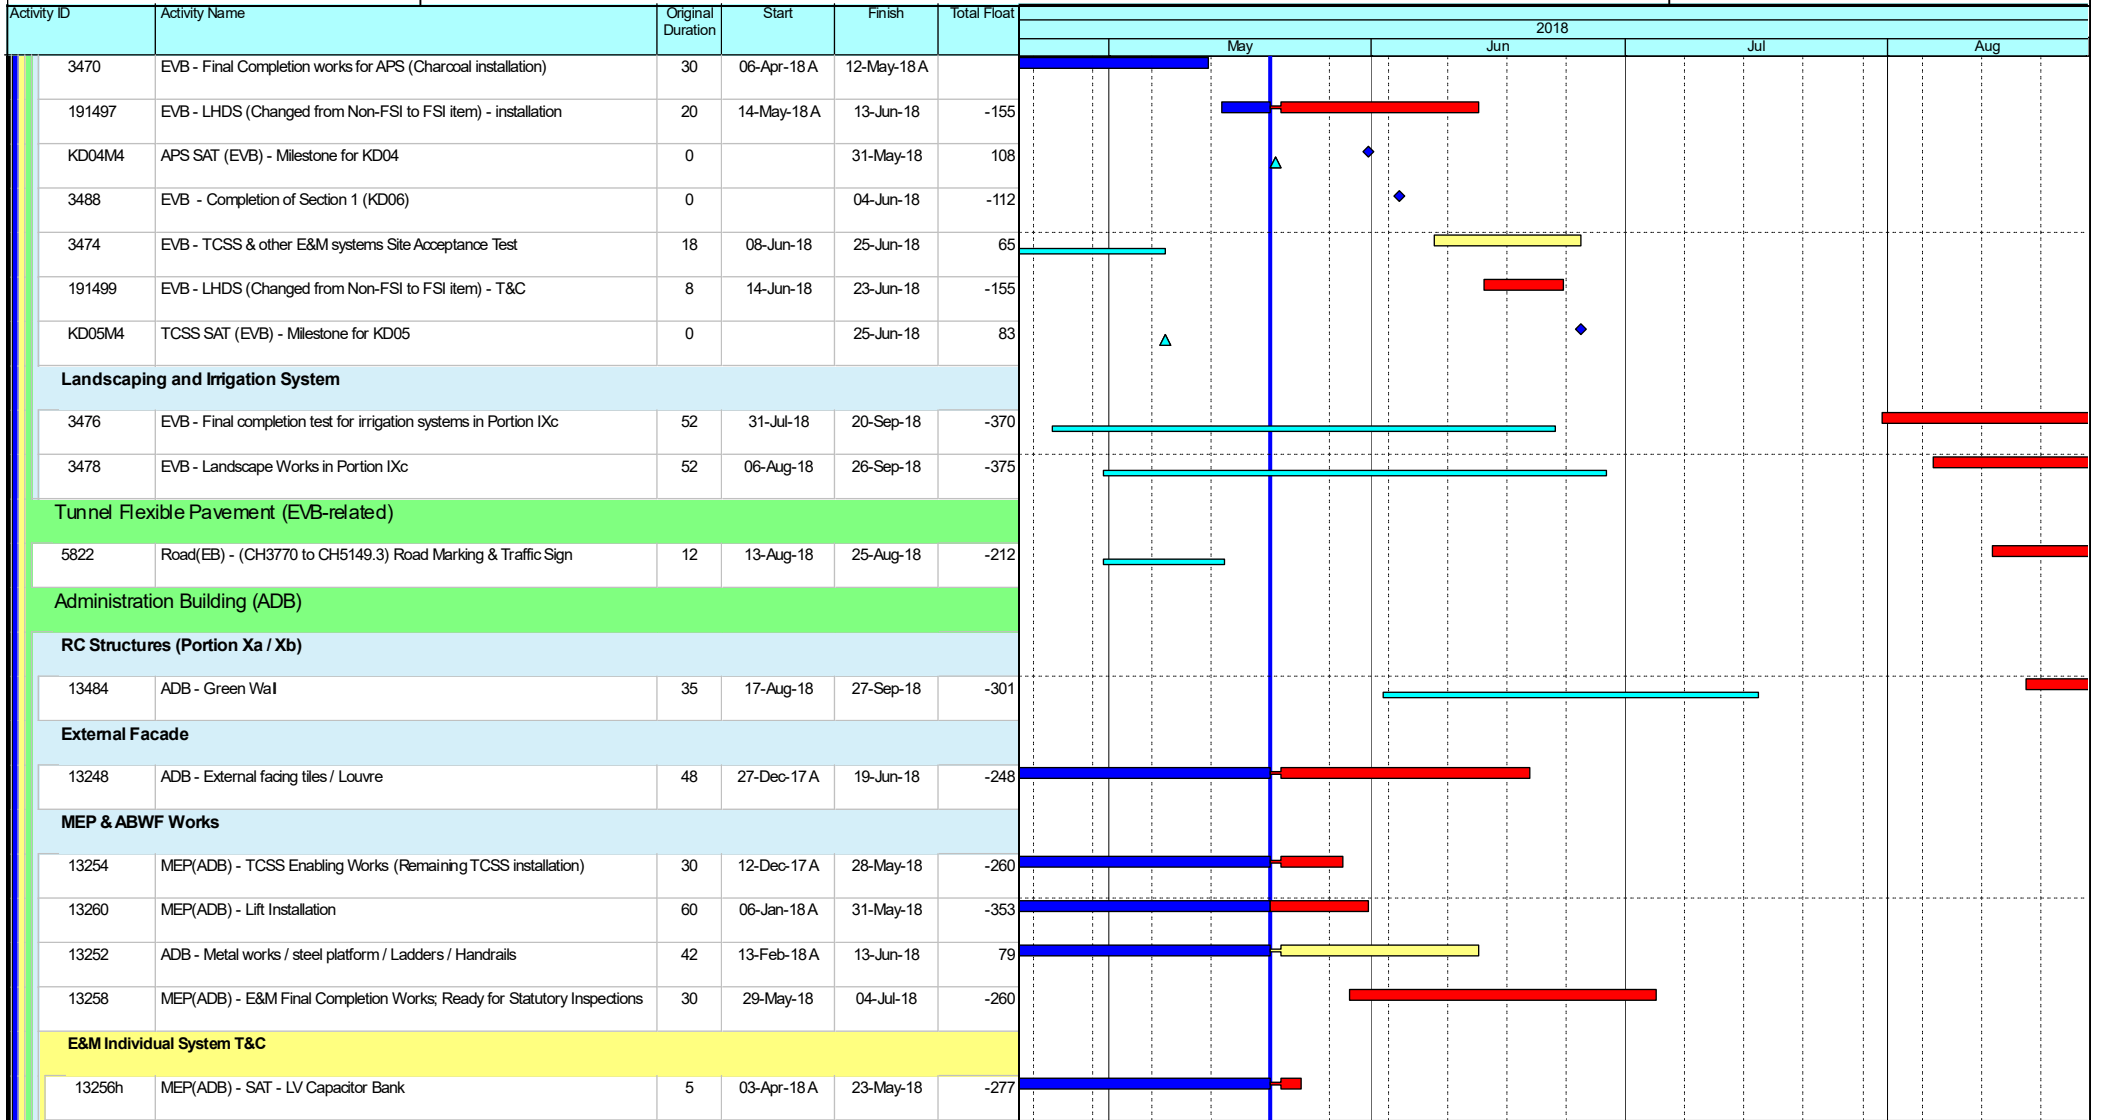

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 20 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW



Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
13256d	MEP(ADB) - CCMS SAT	42	18-Apr-18 A	04-Jul-18	-169				
13256c	MEP(ADB) - Lift functional test	5	26-May-18	31-May-18	-284				
<b>Basement (GL D - F)</b>									
Other Rooms / General Area & Corridor									
13266	MEP(ADB) - E&M 2nd fixing	24	15-Dec-17 A	23-May-18	97				
13268	MEP(ADB) - E&M final fixing	24	02-Mar-18 A	28-May-18	93				
<b>Basement (GL P - R)</b>									
F.S. Water Tank, Sprinkler Tank & Pump Room (B-13)									
13294	MEP(ADB) - E&M final fixing	12	18-Jan-18 A	26-May-18	-255				
Other Rooms / General Area & Corridor									
13286	MEP(ADB) - E&M final fixing	24	06-Feb-18 A	23-May-18	97				
<b>G/F (GL A - D)</b>									
Computer Room (G-35)									
13334	MEP(ADB) - E&M final fixing	24	08-Mar-18 A	26-Apr-18 A					
Control Centre (G-45)									
13304	MEP(ADB) - E&M final fixing	24	12-Mar-18 A	26-Apr-18 A					
Other Rooms / General Area & Corridor									
13310	MEP(ADB) - E&M 1st fixing	24	08-Nov-17 A	23-May-18	97				
13312	MEP(ADB) - E&M 2nd fixing	24	22-Dec-17 A	25-May-18	95				
13314	MEP(ADB) - E&M final fixing	24	05-Feb-18 A	01-Jun-18	89				
<b>G/F (GL D - N)</b>									
Other Rooms / General Area & Corridor									
13340	MEP(ADB) - E&M 1st fixing	24	13-Dec-17 A	23-May-18	-136				
13342	MEP(ADB) - E&M 2nd fixing	24	29-Dec-17 A	25-May-18	-138				

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 21 of 34


Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
13344	MEP(ADB) - E&M final fixing	24	07-Feb-18 A	01-Jun-18	-144				
<b>G/F (GL P - R)</b>									
<b>Other Rooms / General Area &amp; Corridor</b>									
13408	MEP(ADB) - E&M 1st fixing	24	10-Jan-18 A	23-May-18	-136				
13410	MEP(ADB) - E&M 2nd fixing	24	13-Feb-18 A	25-May-18	-138				
13412	MEP(ADB) - E&M final fixing	24	06-Mar-18 A	28-May-18	-140				
<b>1/F (GL A - D)</b>									
<b>Water Pump Room (L1-08)</b>									
13430	MEP(ADB) - E&M 2nd fixing	12	18-Dec-17 A	23-May-18	-252				
13426	MEP(ADB) - Installation of water Pump	24	28-Dec-17 A	23-May-18	-252				
13428	MEP(ADB) - E&M final fixing	24	10-Jan-18 A	26-May-18	-255				
<b>External Works</b>									
13432	ADB - Road and drainage works (EVA)	42	11-Dec-17 A	28-May-18	-91				
13438	ADB - Final completion works (include CCMS interface)	60	09-Jan-18 A	30-Jun-18	-107				
13434	ADB - External concrete pavement (EVA)	24	18-Jan-18 A	30-Jun-18	-107				
3254b	VO/209 - Design submission for approval (re-submitted and rejected twice) (Form 542)	0	05-Mar-18 A	03-May-18 A					
3254c	VO/209 - Design re-submission for approval (Form 542)	0	15-May-18 A						
13436	ADB - External Fence Wall (include metal gate)	21	18-May-18 A	30-Jun-18	-107				
3254d	VO/209 - Design approval (Tentative)	0		25-May-18*	-107				
3254e	VO/209 - WWO46 Part I & II approval	12	26-May-18	08-Jun-18	-107				
3254f	VO/209 - VO Works installation (Street fire hydrant and water connection at EVA of ADB)	12	09-Jun-18	23-Jun-18	-107				
<b>E&amp;M Testing &amp; Commissioning / Statutory Inspection</b>									
13458	MEP(ADB) - Submission of WWO46 (Part IV) to WSD	0	26-May-18		-191				
13444	MEP(ADB) - Ready for Statutory Inspection (Building)	0	28-May-18		-255				



### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
Baseline: SA01  
Layout: Update Three Month Rolling  
U051  
Page 22 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
13456	MEP(ADB) - Submission of Form 501 to FSD (Building)	0	28-May-18		-255				
13462	MEP(ADB) - Submission of Form 314 to FSD	0	28-May-18		-148				
13454	MEP(ADB) - Submission of Form 5 to EMSD	0	01-Jun-18		-184				
3660a2	MEP(ADB) - TVS & CCMS System Integrated Testing and Commissioning	36	06-Jun-18	11-Jul-18	-217				
13446	MEP(ADB) - Statutory Inspection & Certificates (include EMSD & FSD inspection) (Building)	7	08-Jun-18	15-Jun-18	-149				
KD03M7	MEP(ADB) - Milestone for KD06	0		13-Jun-18	95				
13454a	MEP(ADB) - Use Permit - Lift (Non-FS)	0	15-Jun-18		94				
13460	MEP(ADB) - Submission of WWO46 (Part V) to Client	0	16-Jun-18		-191				
13446a	MEP(ADB) - Statutory Inspection & Certificates (FSD inspection) (SFH & EVA)	2	03-Jul-18	04-Jul-18	-2				
<b>Final Completion Works</b>									
191507	ADB - MFCP manufacture & delivery	44	05-Apr-18 A	19-May-18 A					
13464	ADB - TCSS & other E&M systems Site Acceptance Test	18	02-May-18 A	29-May-18	-212				
191509	ADB - MFCP installation	18	20-May-18	06-Jun-18	-196				
13468	ADB - Tunnel FS operation test	30	28-May-18	26-Jun-18	-319				
KD05M8	TCSS SAT (ADB) - Milestone for KD05	0		29-May-18	110				
191511	ADB - MFCPT&C	14	07-Jun-18	20-Jun-18	-196				
13466	ADB - Completion of Section 1 (KD06)	0		30-Jul-18	48				
<b>Landscaping and Irrigation System</b>									
13588	ADB - Final completion test for irrigation systems in PortionXa and Xb	60	01-Jun-18	30-Jul-18	-353				
13590	ADB - Landscape Works in Portion Xa and Xb	60	31-Jul-18	28-Sep-18	-377				
<b>East Ventilation Shaft (EVS)</b>									
<b>ABWF Works</b>									
3826	EVS - ABWF (Dry Trade)	60	20-Sep-17 A	28-May-18	93				
3830	EVS - Metal works / steel platform / Ladders / Handrails	48	19-Dec-17 A	04-Jun-18	87				

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Project Baseline
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Baseline Milestone
- ▬ Baseline Milestone

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 23 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018					
						May	Jun	Jul	Aug		
<b>External Facade</b>											
19060	EVS - Cone louvre installation	60	07-Feb-17 A	19-Jun-18	-121						
3832	EVS - Architectural Features of EVS	120	12-Jul-17 A	26-Jun-18	-115						
<b>MEP Works</b>											
3836	MEP(EVS) - E&M 1st Fix	12	05-Sep-17 A	25-May-18	-113						
3838	MEP(EVS) - E&M 2nd Fix	12	20-Sep-17 A	30-May-18	-117						
19054	MEP(EVS) - Lightning protection system installation and T&C	12	11-Oct-17 A	01-Jun-18	-95						
3840	MEP(EVS) - E&M Final Fix	12	31-May-18	13-Jun-18	-117						
3844	MEP(EVS) - E&M Individual System T&C	12	14-Jun-18	28-Jun-18	-117						
19056	MEP(EVS) - Features lighting installation and T&C	24	20-Jun-18	18-Jul-18	-121						
3846	MEP(EVS) - E&M Final Completion Works; Ready for Statutory Inspections	6	29-Jun-18	06-Jul-18	-117						
<b>External Works</b>											
3850	EVS - External concrete pavement	12	20-Jun-18	04-Jul-18	-109						
3854	EVS - Final completion works (include CCMS interface)	12	28-Jun-18	12-Jul-18	-116						
<b>E&amp;M Testing &amp; Commissioning / Statutory Inspection</b>											
3856	MEP(EVS) - E&M System Integrated Testing and Commissioning	6	07-Jul-18	12-Jul-18	-152						
3858	MEP(EVS) - Ready for Statutory Inspection (with EVB)	0	13-Jul-18		-151						
KD03M4	MEP(EVS) - Milestone for KD03	0		13-Jul-18	66						
<b>Final Completion Works</b>											
3880	EVS - Completion of Section 1 (KD06)	0		13-Jul-18	-151						
<b>Satellite Control Points 4 / 5</b>											
<b>SCP4</b>											
3824	SCP4 - Metal works / Glazing / Louver / Handrails	18	02-Mar-18 A	05-May-18 A							
3788	MEP(SCP4) - E&M 1st Fix	18	12-Mar-18 A	25-May-18	11						

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 24 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

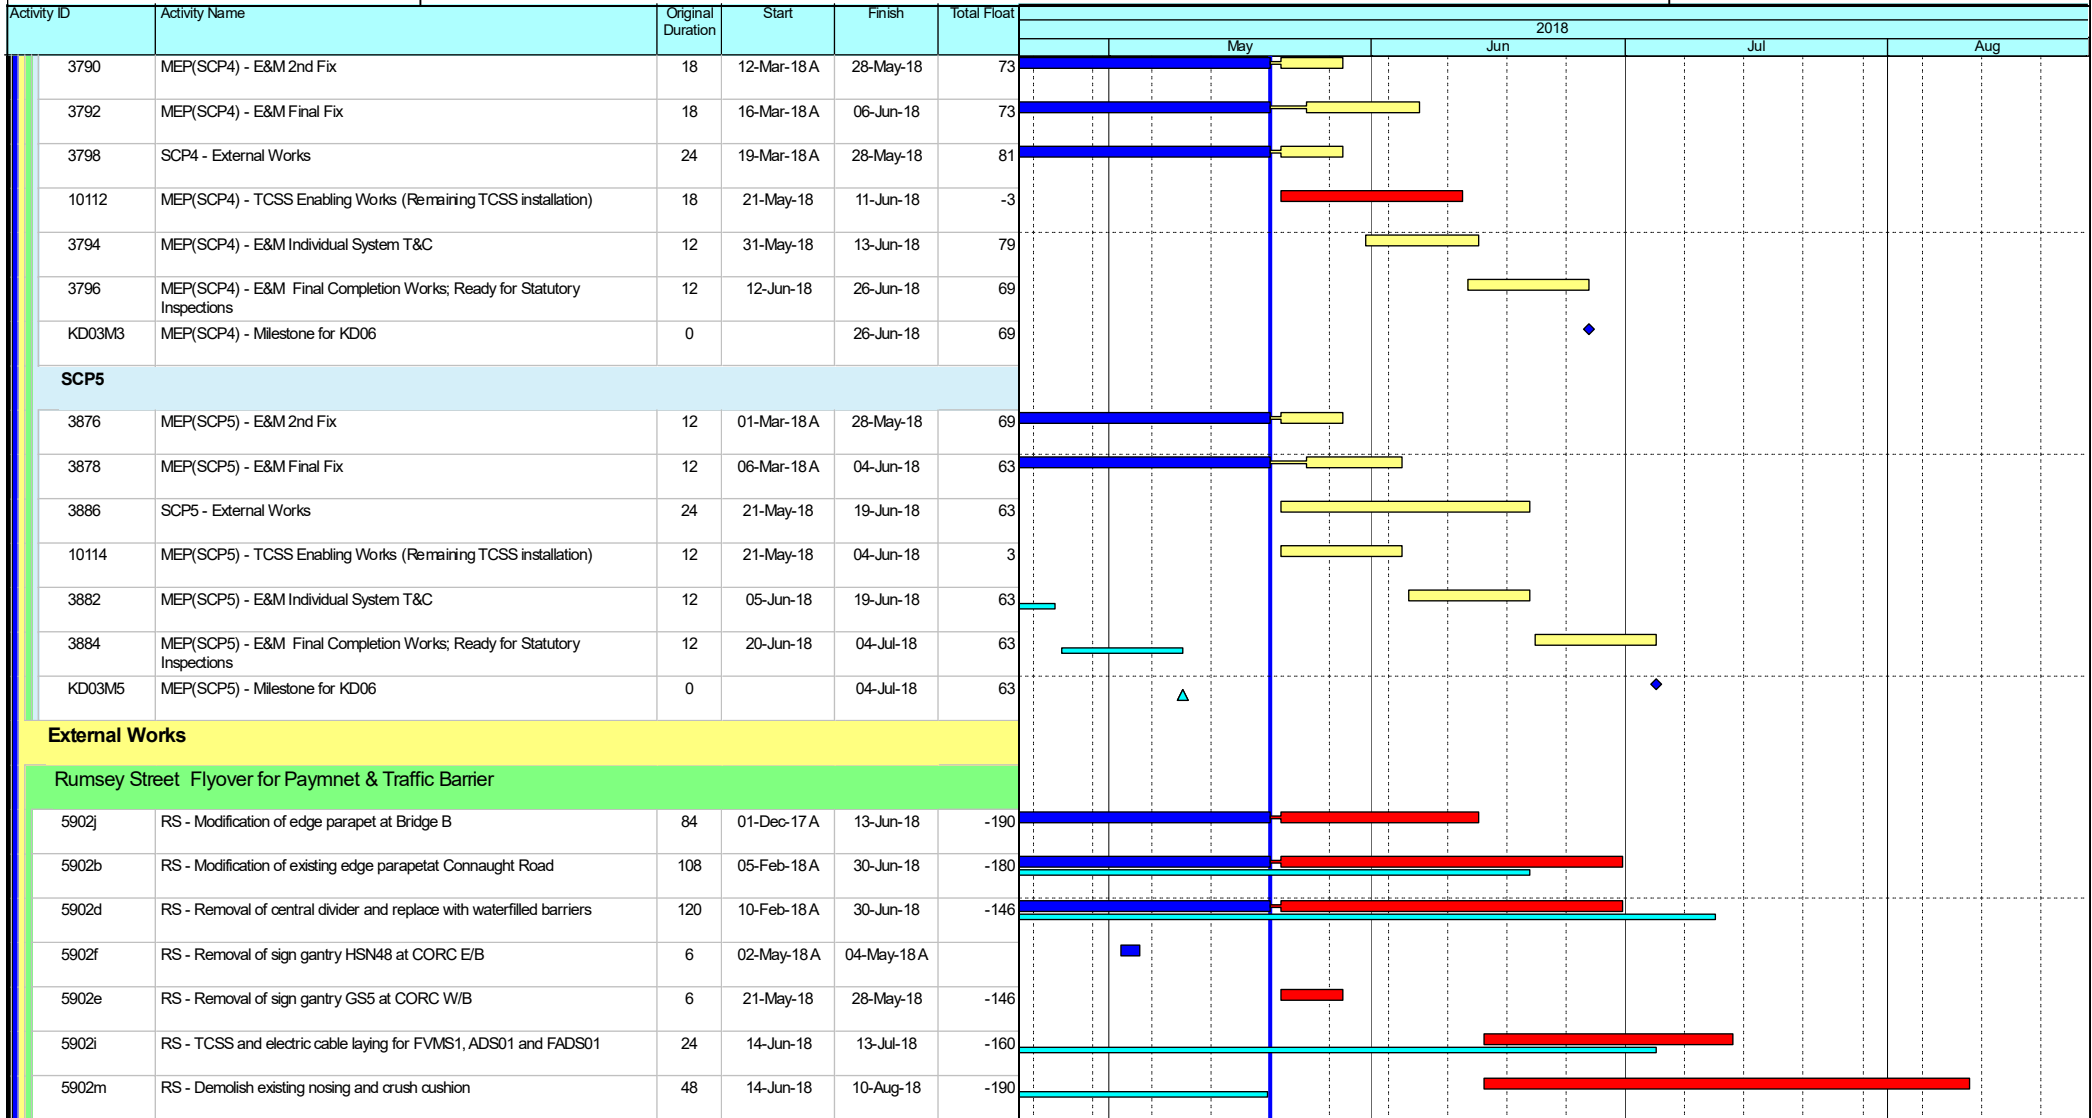

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
Baseline: SA01  
Layout: Update Three Month Rolling  
U051  
Page 25 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
5902g	RS - Install new directional sign	6	20-Jun-18	26-Jun-18	-146				
5902n	RS - Paving works on Bridge B	12	29-Jun-18	13-Jul-18	-190				
5902p	RS - Pavement tie-in works at CORC W/B	36	14-Jul-18	24-Aug-18	-190				
<b>VO/217 - TCSS and JTIS for sign face ADS16 at Hing Fat Street</b>									
5906d	VO/217 - Ducts/drawpits at parking spaces section 1, 2 & 3	18	03-Apr-18 A	24-Apr-18 A					
5906b	VO/217 - Cross road duct	36	16-Apr-18 A	29-May-18	-177				
5906c	VO/217 - Ducts/drawpits at left side F/P section 1 & 2	6	16-Apr-18 A	21-Apr-18 A					
5906g	VO/217 - Ducts/drawpits at right side F/P	6	23-Apr-18 A	28-Apr-18 A					
5906e	VO/217 - Ducts/drawpits at exit of parking area	24	25-Apr-18 A	24-May-18	96				
5906f	VO/217 - Ducts/drawpits at north of carpark F/P	10	30-Apr-18 A	11-May-18 A					
5906h	VO/217 - Cross road ducts at J/O HIFS and TSFS left / right lane	24	12-May-18 A	09-Jun-18	-177				
<b>Area A/B</b>									
<b>Area ATCSS</b>									
10288a3	Request for VO/instruction-TCSS equipment installation & cabling (Gantries FVMS1/ADS01) (Ref: H27613-LJV-ME-LE-4022)	24	04-Oct-16 A	28-May-18	-146				
<b>Area B</b>									
<b>Area B Access / Pre-SAT</b>									
10288f	C19 allow access at Area B - Remaining area at IEC bridge East to Double Noise Enclosure	0	03-May-18 A						
10288f6	C19 allow access at Area B - Landscape Deck (From CH5150 - CH5260) - Remaining	0	14-May-18 A						
10288f8	C19 allow access at Area B - Landscape Deck (From CH5150 - CH5260) - W/B	0	16-May-18 A						
<b>Area B TCSS</b>									
<b>Approach Road / Landscape Deck / Noise Enclosure (No TTA)</b>									
10288b16	Area B TCSS cabling (Base slab / approach ramp connecting to East Portal with civil provision)	18	20-Feb-18 A	04-Jun-18	-173				
10288b40	Area B TCSS equipment installation (on IEC's Westbound) - DS06B	9	14-May-18 A	15-May-18 A					
10288b20	Area B TCSS cabling (Noise Enclosure with civil provision - No TTA)	18	21-May-18	11-Jun-18	-136				

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline
- ▲ Baseline Milestone

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 26 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

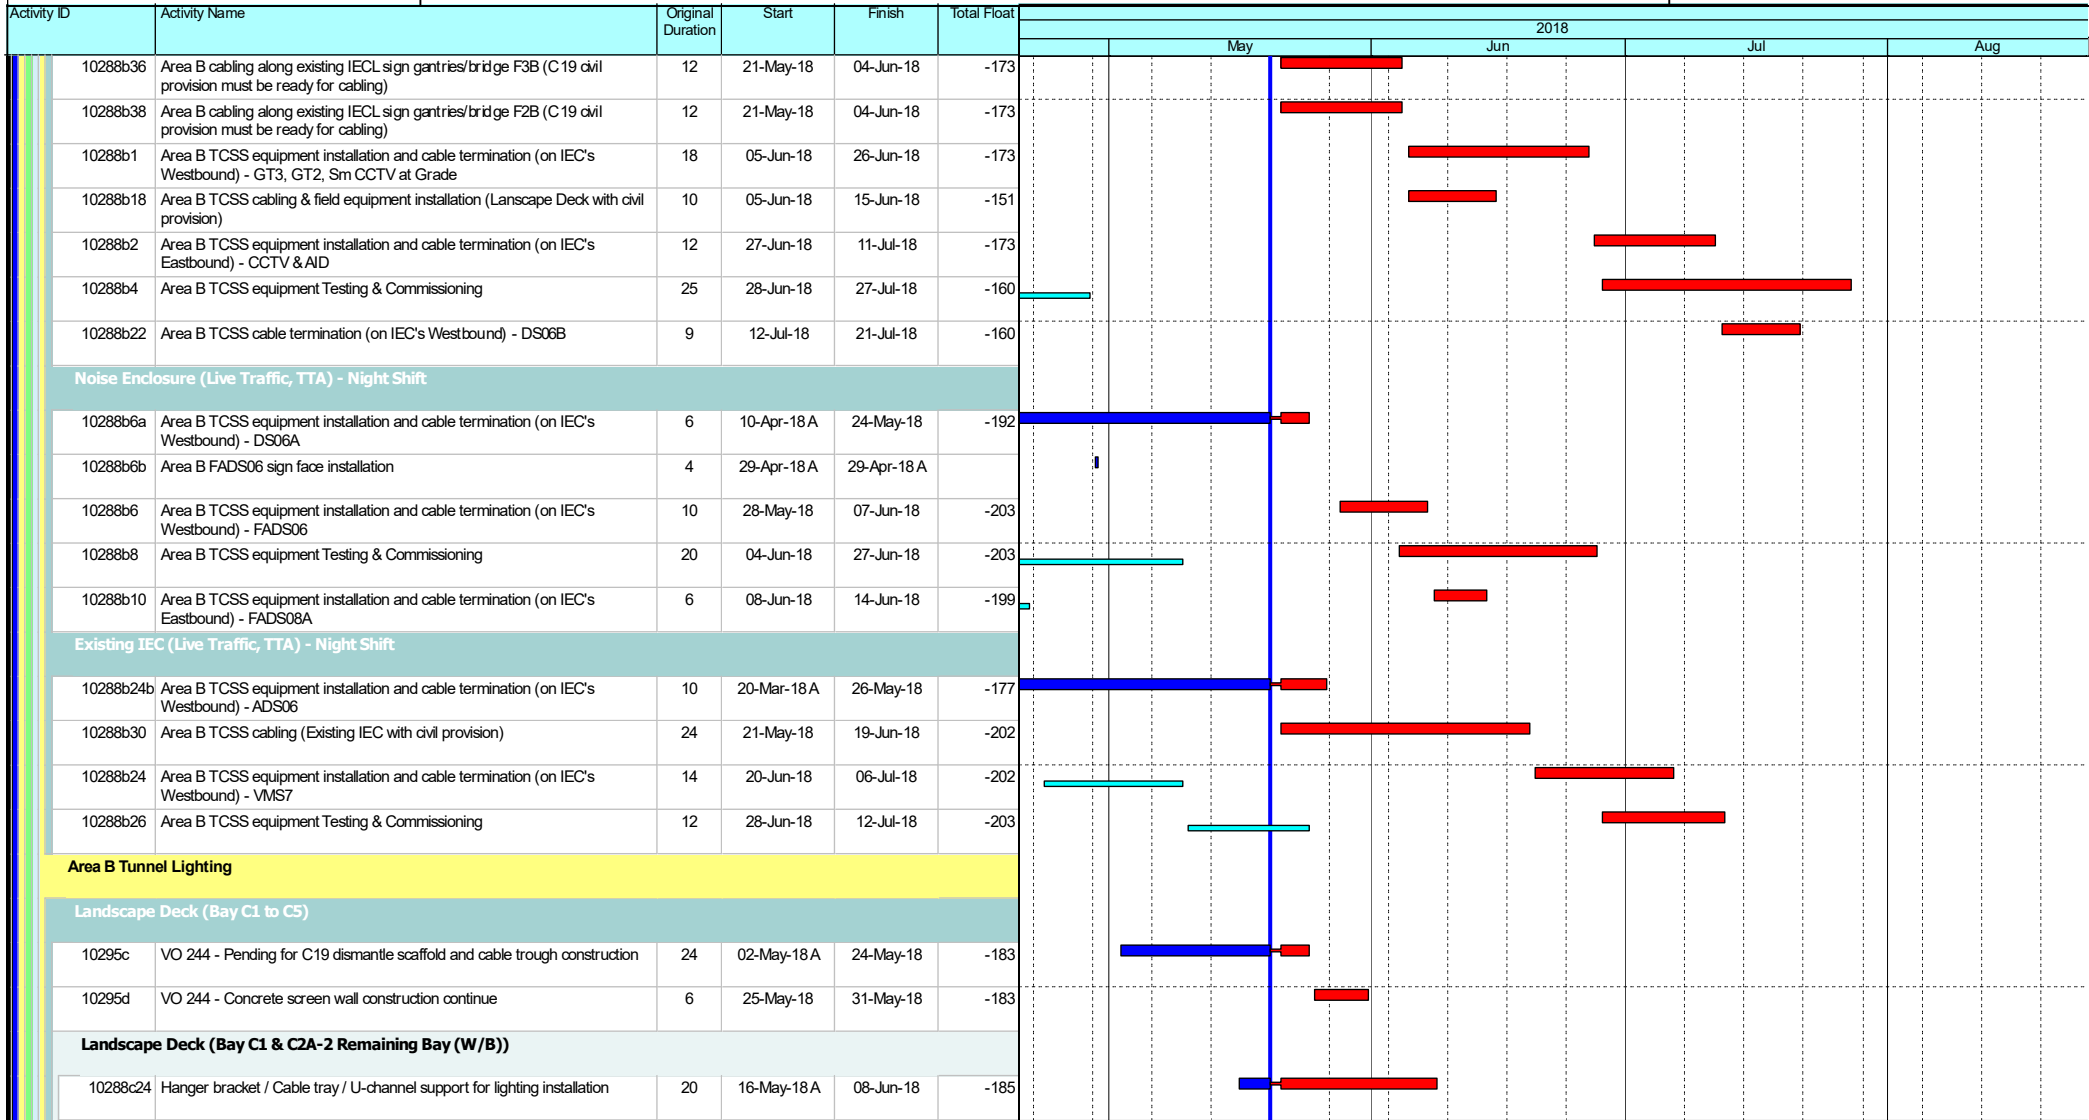

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 27 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

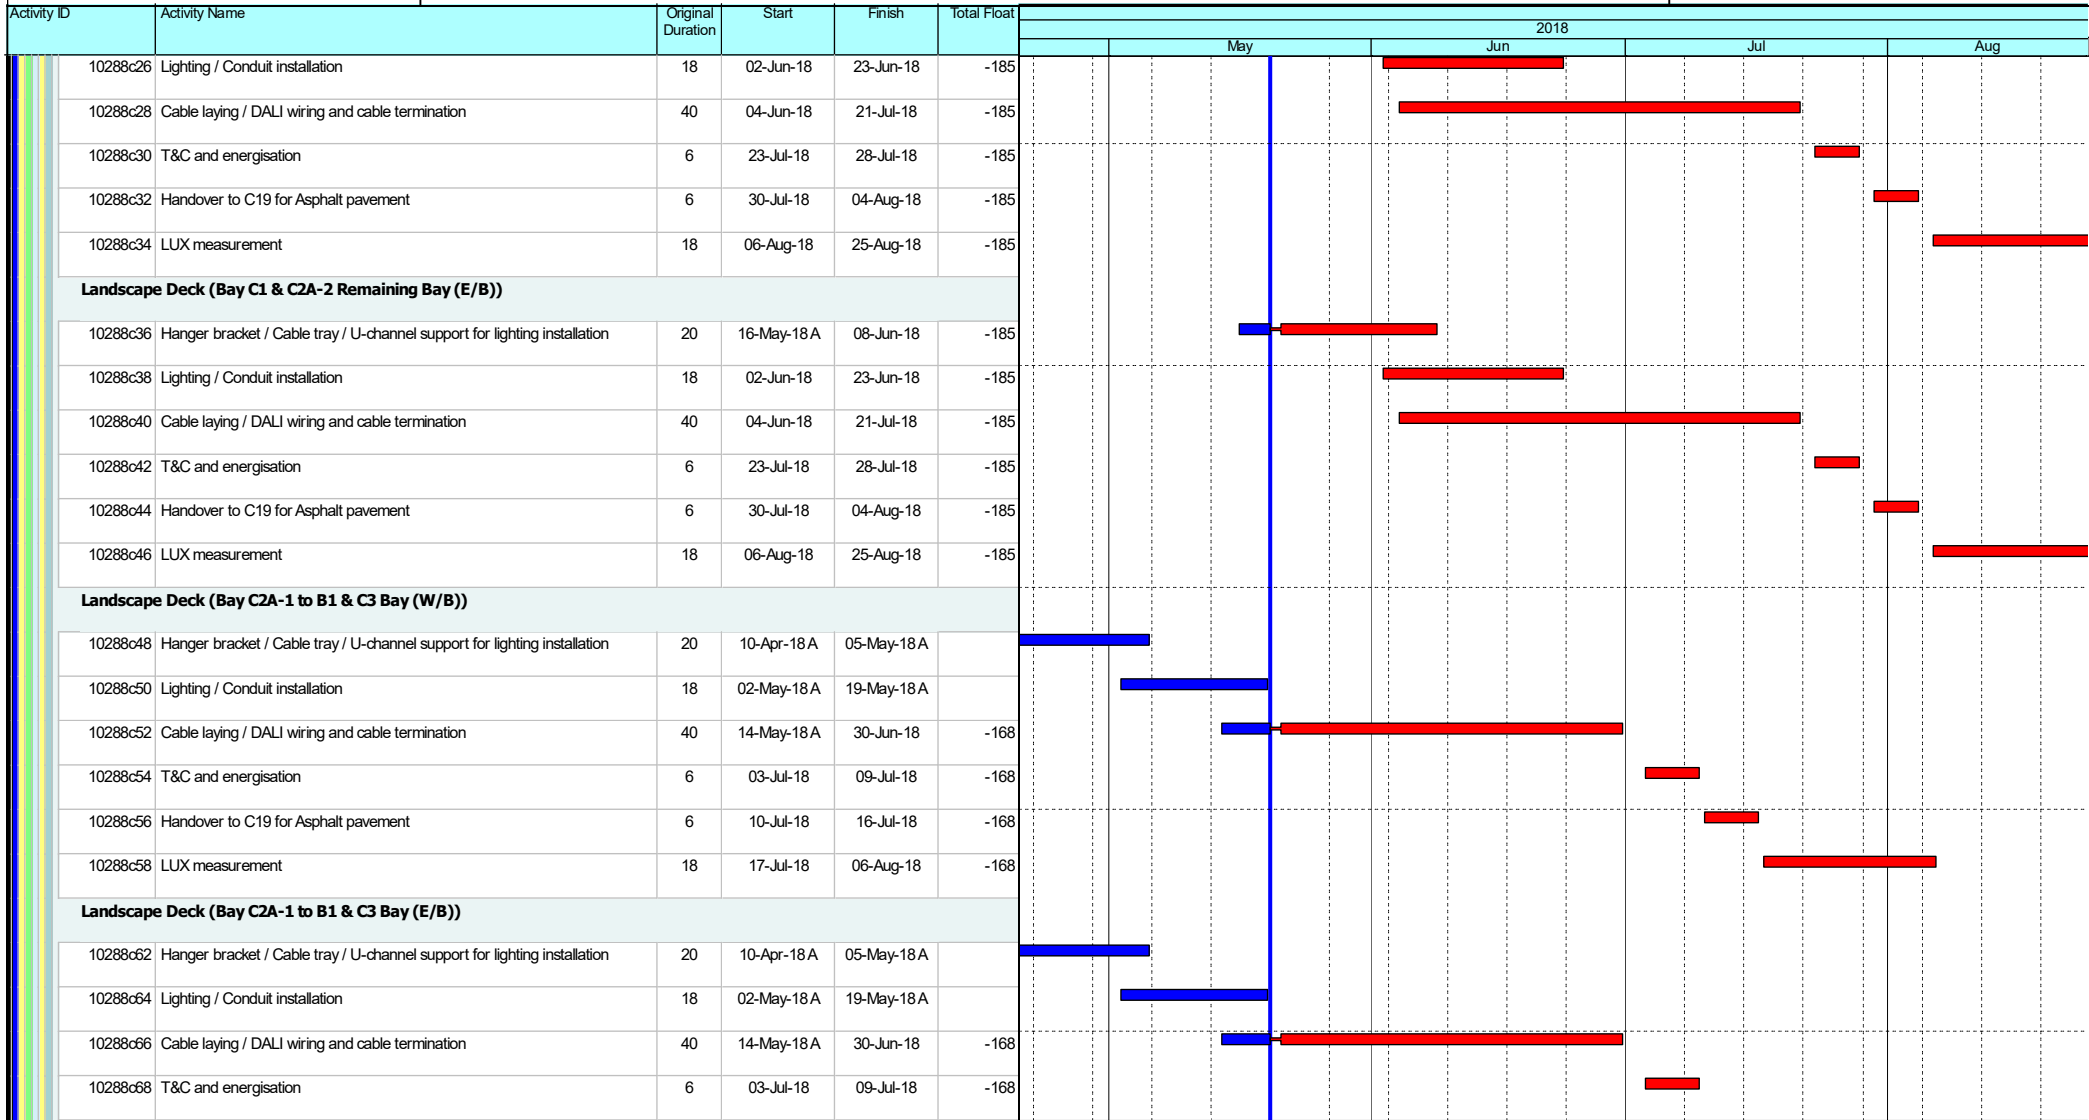

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 28 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW



Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
10288c70	Handover to C19 for Asphalt pavement	6	10-Jul-18	16-Jul-18	-168				
10288c72	LUX measurement	18	17-Jul-18	06-Aug-18	-168				
<b>Landscape Deck (Bay C4 - E/B Slow Lane)</b>									
10288c76	Hanger bracket / Cable tray / U-channel support for lighting installation	18	06-Jun-18	27-Jun-18	-193				
10288c88	Access date - Bay C4 - E/B Slow Lane	0	06-Jun-18*		-193				
10288c78	Lighting / Conduit installation	6	21-Jun-18	27-Jun-18	-191				
10288c78	Handover to C19 for backfilling & paving	10	30-Jun-18	12-Jul-18	-193				
10288c80	Cable laying / DALI wiring and cable termination	28	13-Jul-18	14-Aug-18	-193				
10288c90	Lighting / Conduit installation (continue)	6	13-Jul-18	19-Jul-18	-171				
10288c82	T&C and energisation	6	15-Aug-18	21-Aug-18	-193				
10288c86	LUX measurement	18	15-Aug-18	04-Sep-18	-193				
<b>Landscape Deck (Bay C4 - E/B Fast Lane)</b>									
10288c92	Hanger bracket / Cable tray / U-channel support for lighting installation	22	26-Apr-18 A	23-May-18	-194				
10288c10	Access date - Bay C4 - E/B Fast Lane	0	26-Apr-18 A		-194				
10288c94	Lighting / Conduit installation	11	17-May-18 A	30-May-18	-194				
10288c78	Handover to C19 for remaining works at Bay C4 & C5	34	31-May-18	11-Jul-18	-194				
10288c96	Cable laying / DALI wiring and cable termination	30	12-Jul-18	15-Aug-18	-194				
10288c10	Lighting / Conduit installation (continue)	6	12-Jul-18	18-Jul-18	-170				
10288c98	T&C and energisation	6	16-Aug-18	22-Aug-18	-194				
10288c10	LUX measurement	18	16-Aug-18	05-Sep-18	-194				
<b>Landscape Deck (Bay C4 - W/B)</b>									
10288c10	Hanger bracket / Cable tray / U-channel support for lighting installation	22	26-Apr-18 A	23-May-18	-194				
10288c11	Access date - Bay C4 - W/B	0	26-Apr-18 A		-194				
10288c10	Lighting / Conduit installation	11	17-May-18 A	30-May-18	-194				

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline
- ▲ Baseline Milestone

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 29 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018				
						May	Jun	Jul	Aug	
10288c78	Handover to C19 for remaining works at Bay C4 & C5	34	31-May-18	11-Jul-18	-194		[Red bar]			
10288c110	Cable laying / DALI wiring and cable termination	30	12-Jul-18	15-Aug-18	-194			[Red bar]		
10288c111	Lighting / Conduit installation (continue)	6	12-Jul-18	18-Jul-18	-170			[Red bar]		
10288c112	T&C and energisation	6	16-Aug-18	22-Aug-18	-194				[Red bar]	
10288c114	LUX measurement	18	16-Aug-18	05-Sep-18	-194				[Red bar]	
<b>Landscape Deck (Bay C5 - E/B Slow Lane)</b>										
10288c120	Hanger bracket / Cable tray / U-channel support for lighting installation	22	26-Apr-18 A	17-May-18 A		[Blue bar]				
10288c130	Access date - Bay C5 - E/B Slow Lane	0	26-Apr-18 A			◆				
10288c122	Lighting / Conduit installation	18	11-May-18 A	31-May-18	-189	[Blue bar]	[Red bar]			
10288c121	Cable laying / DALI wiring and cable termination	6	25-May-18	31-May-18	-189		[Red bar]			
10288c78	Handover to C19 for remaining works at Bay C4 & C5	34	01-Jun-18	12-Jul-18	-189		[Red bar]			
10288c121	Cable laying / DALI wiring and cable termination (continue)	24	13-Jul-18	09-Aug-18	-189			[Red bar]		
10288c121	T&C and energisation	6	10-Aug-18	16-Aug-18	-189				[Red bar]	
10288c121	LUX measurement	18	10-Aug-18	30-Aug-18	-189				[Red bar]	
<b>Landscape Deck (Bay C5 - E/B Fast Lane)</b>										
10288c130	Hanger bracket / Cable tray / U-channel support for lighting installation	22	26-Apr-18 A	17-May-18 A		[Blue bar]				
10288c140	Access date - Bay C5 - E/B Slow Lane	0	26-Apr-18 A			◆				
10288c130	Lighting / Conduit installation	18	11-May-18 A	31-May-18	-189	[Blue bar]	[Red bar]			
10288c130	Cable laying / DALI wiring and cable termination	6	25-May-18	31-May-18	-189		[Red bar]			
10288c78	Handover to C19 for remaining works at Bay C4 & C5	34	01-Jun-18	12-Jul-18	-189		[Red bar]			
10288c121	Cable laying / DALI wiring and cable termination (continue)	24	13-Jul-18	09-Aug-18	-189			[Red bar]		
10288c130	T&C and energisation	6	10-Aug-18	16-Aug-18	-189				[Red bar]	
10288c140	LUX measurement	18	10-Aug-18	30-Aug-18	-189				[Red bar]	
<b>Landscape Deck (Bay C5 - W/B)</b>										

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING


Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 30 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

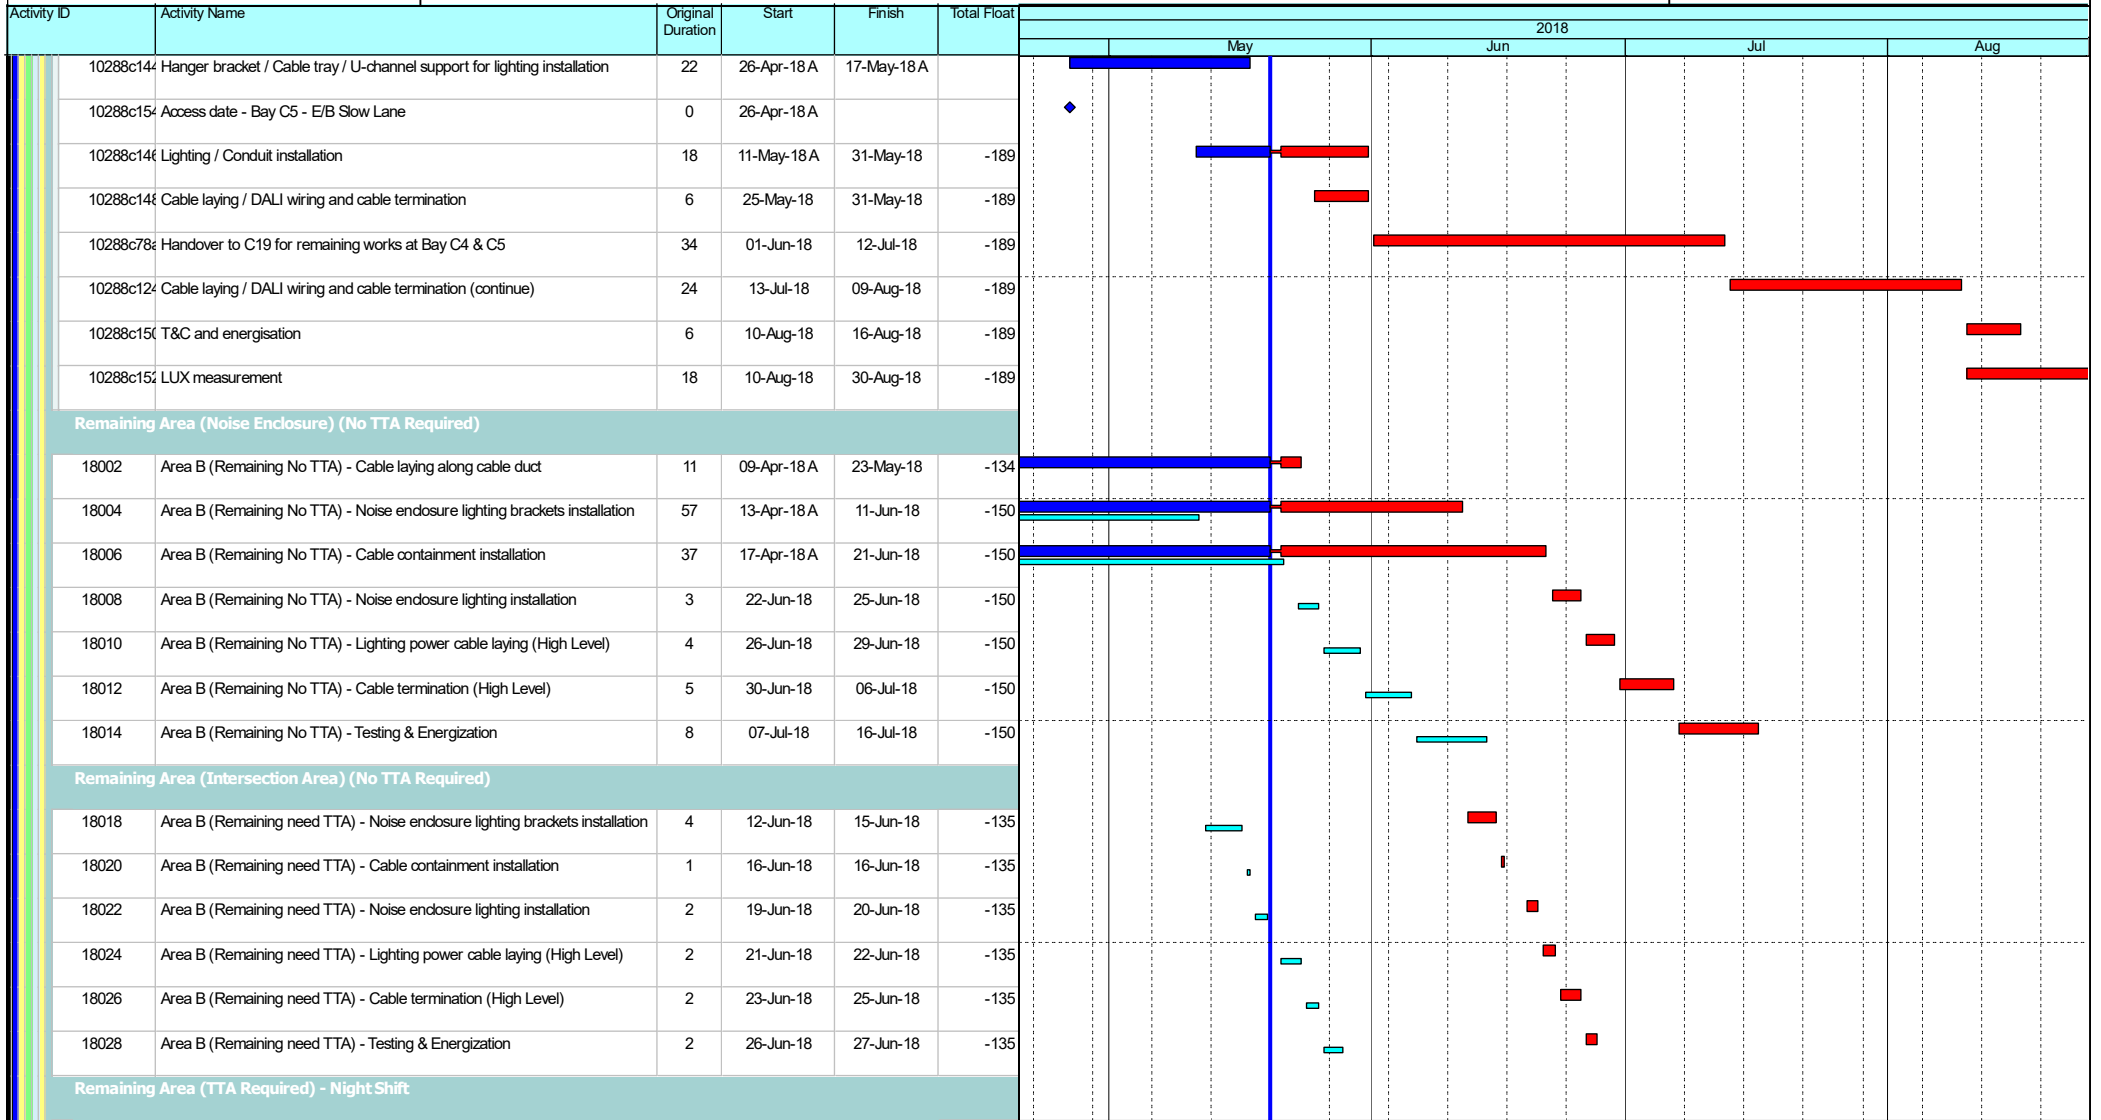

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 31 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

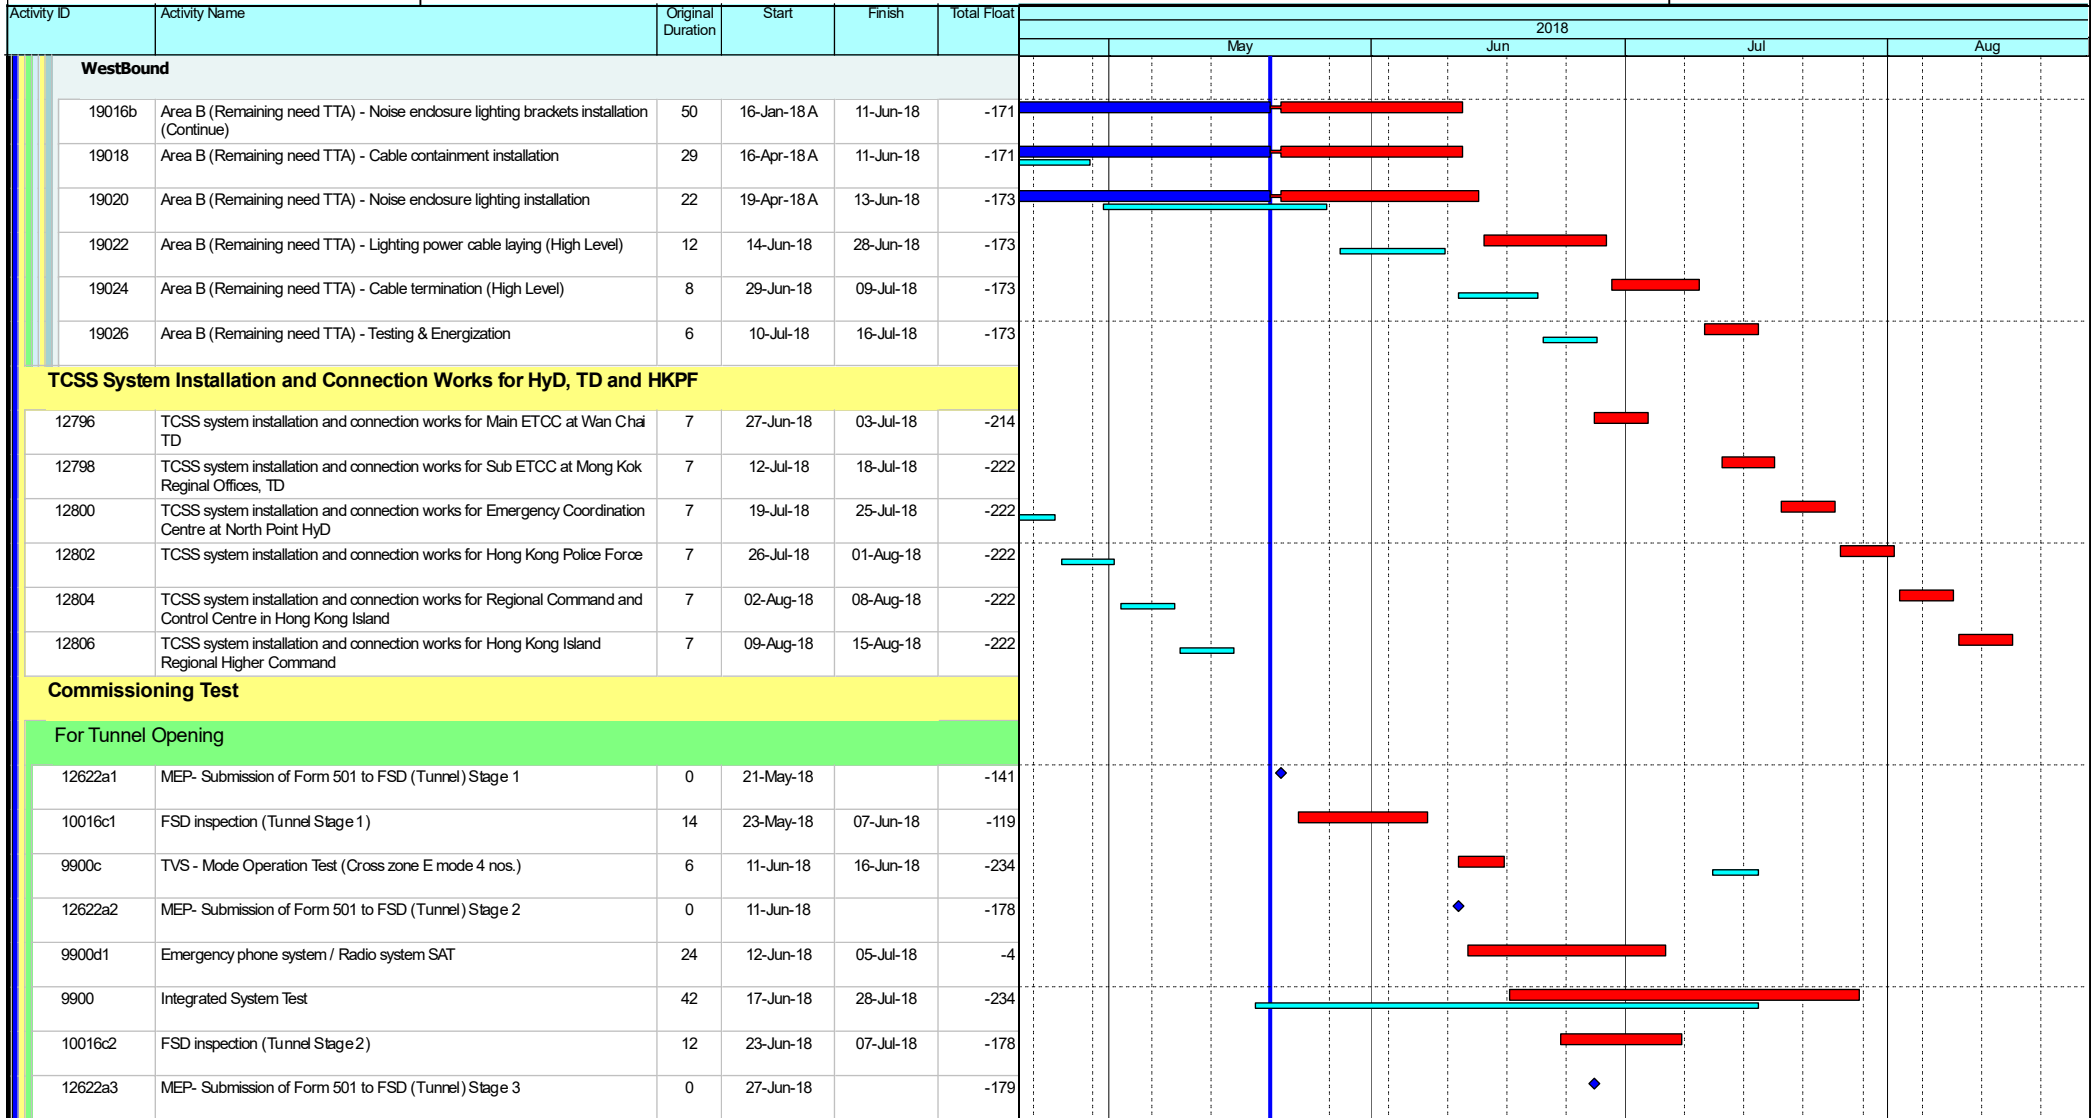

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051  
Baseline: SA01  
Layout: Update Three Month Rolling  
U051  
Page 32 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

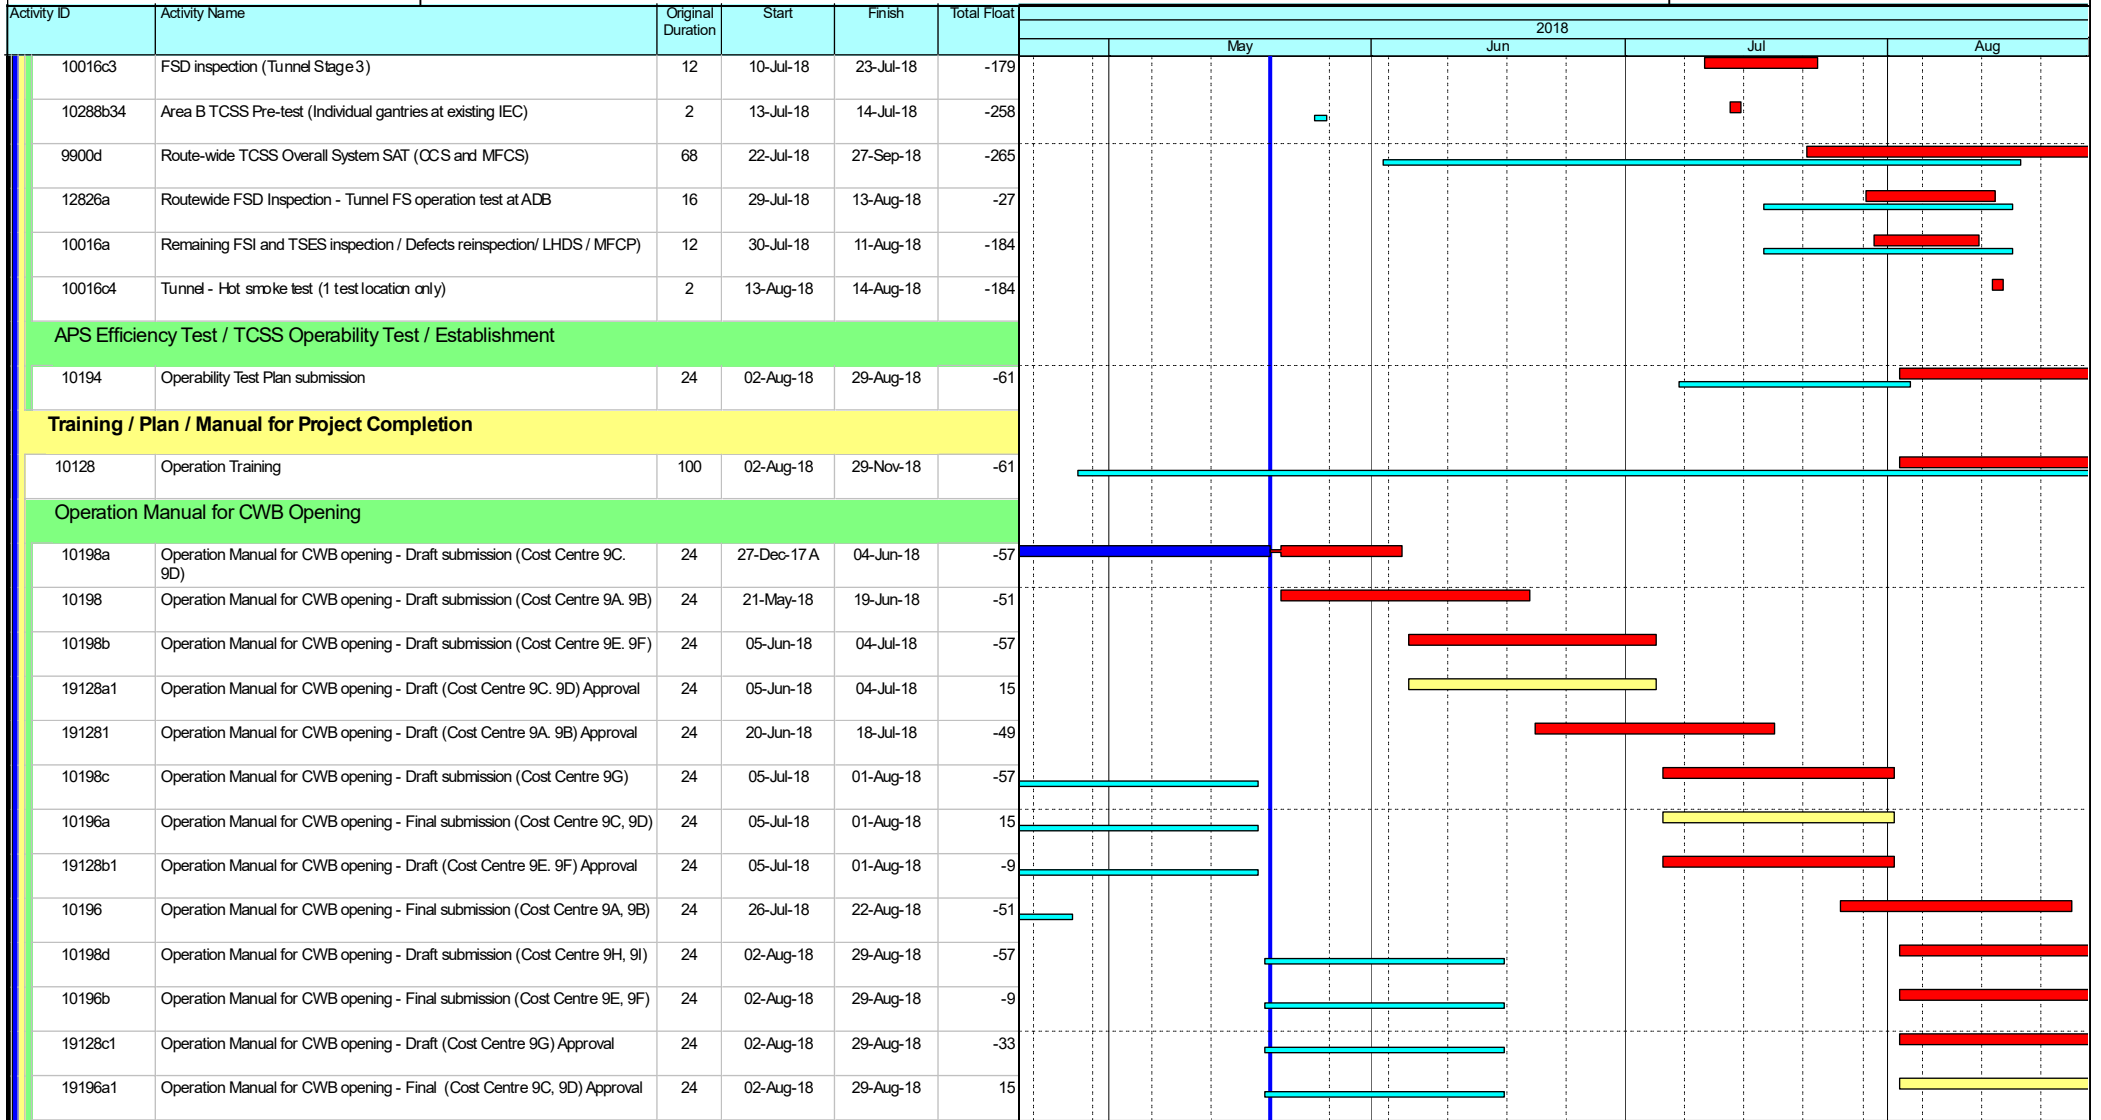

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
Baseline: SA01  
Layout: Update Three Month Rolling  
U051  
Page 33 of 34








Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018																
						May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr					
<b>Training Plan for CWB Opening</b>																						
10206	Training Plan for CWB opening - Draft submission	18	12-Sep-17 A	28-May-18	-69																	
10206a	Training Plan for CWB opening - Draft approval	18	29-May-18	19-Jun-18	-61																	
10208	Training Plan for CWB opening - Final submission	18	20-Jun-18	11-Jul-18	-61																	
10208a	Training Plan for CWB opening - Final approval	18	12-Jul-18	01-Aug-18	-61																	
<b>Training Material for CWB Opening</b>																						
10210	Training Material for CWB opening - Draft submission	18	15-Nov-17 A	28-May-18	-69																	
10210a	Training Material for CWB opening - Draft approval	18	29-May-18	19-Jun-18	-69																	
10212	Training Material for CWB opening - Final submission	18	20-Jun-18	11-Jul-18	-69																	
10212a	Training Material for CWB opening - Final approval	18	12-Jul-18	01-Aug-18	-61																	
<b>Maintenance Manual / Plan</b>																						
10200	Maintenance Plan	18	12-Jul-18	01-Aug-18	-69																	
10220	Maintenance Manual / logbook - Draft submission	18	02-Aug-18	22-Aug-18	-69																	

-  Current Milestone
-  Level of Effort
-  Baseline Milestone
-  Actual Work
-  Critical Remaining Work
-  Remaining Work
-  Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U051  
 Page 34 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW
