

Legend


Original Programme Period
as in version date 11/12/18
Extended Programme Period
as in this version date 21/1/19

Create Date : 21/12/19
Revised Date : 25/12/19
28/12/19
30/12/19
1/2/2019

Remaining Works Programme

項目	工序	Jan-19													Feb-19													Mar-19													Apr-19													May-19																																																																													
		Week 54					Week 55					Week 56					Week 01					Week 02					Week 03					Week 04					Week 05					Week 06																																																																																									
		1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13																																																																																						
1	Removal of Temporary Storage of Backfill material at Portion 5	Portion 5 運泥回填 WCR1 停止運泥因為Close P5 Exit													Portion 5 運泥回填 WCR1																																																																																																																				
2	Seawall 海床														受泥區原海床													填 400 萬方土填新水 (400m)																																																																																																							
3	地面墊仔及 100mm Subbase																																																																																																																																		
4	舊直升機場, 海墘及梯台														舊直升機場 Landing													清場													入機																																																																																										
5	打 D-Wall														打 D-Wall 至 +1.5 (-45M) 回填													掘泥 打 8 區 remaining D-Wall 至 +1.5 (15M) 回填																																																																																																							
6	U Channel & 沙井														Inculvert 埋石渠													北面東段 4 個 catchpit + 3000 渠 (108m) DN8, 1 DN8, 2													北面東段 3 個 catchpit + 3000 渠 DN8, 6													北面東段 DN8, 3																																																																													
7	渠網及 沙井														北面西段 1 個 catchpit + 300, 3750 渠 (56m) DN1, 1													北面中段 3000 渠													北面中段 3750 to																																																																																										
8	IRRIGATION PIPE	VVV542 (21/12/18)													subsoil drainage													approval of design													VVV046 埋管土																																																																																										
9	Fresh Water Main	TTA approved in TMLG Meeting 5/12/18																																																																																																																																	
10	HRR 馬路														AREA ABCD remove PMSMA Relay Area ABCD PMSMA													AREA E remove and relay BC+PMSMA													AREA F remove and relay BC+PMSMA													FOOTPATH ALONG HRR													FOOTPATH																																																																
10.1	HRR FLYOVER REMAINING WORK														VO258 MODIFICATION WORK AT ABUTMENT ROOM													VO253 PROVIDE STAINLESS STEEL LADDER AT ABUTMENT ROOM													place order and delivery																																																																																										
11	還原運泥街 Stage 0.5	EYA																																																																																																																																	
12	博覽道東, WCR1 & WCR3 未完成工作	* Portion 2 Zone 1													* Zone 2a upto end of EYA													* Portion 2 Zone 2b													* Zone 2a remaining area													REMEDIAL TO EXPO DRIVE COVERED WALKWAY													WCR3 填 Sub Base (100mm thk 7000m ²)													Caisson seawall defects													resumption of a monitoring point WCR1-1													海墘圍填如下 COPING (COMMENCEMENT DATE TO BE CONFIRMED)													WCR1&3 MAKE GOOD ARMOUR SLOPE PROFILE												

Remaining Works Programme

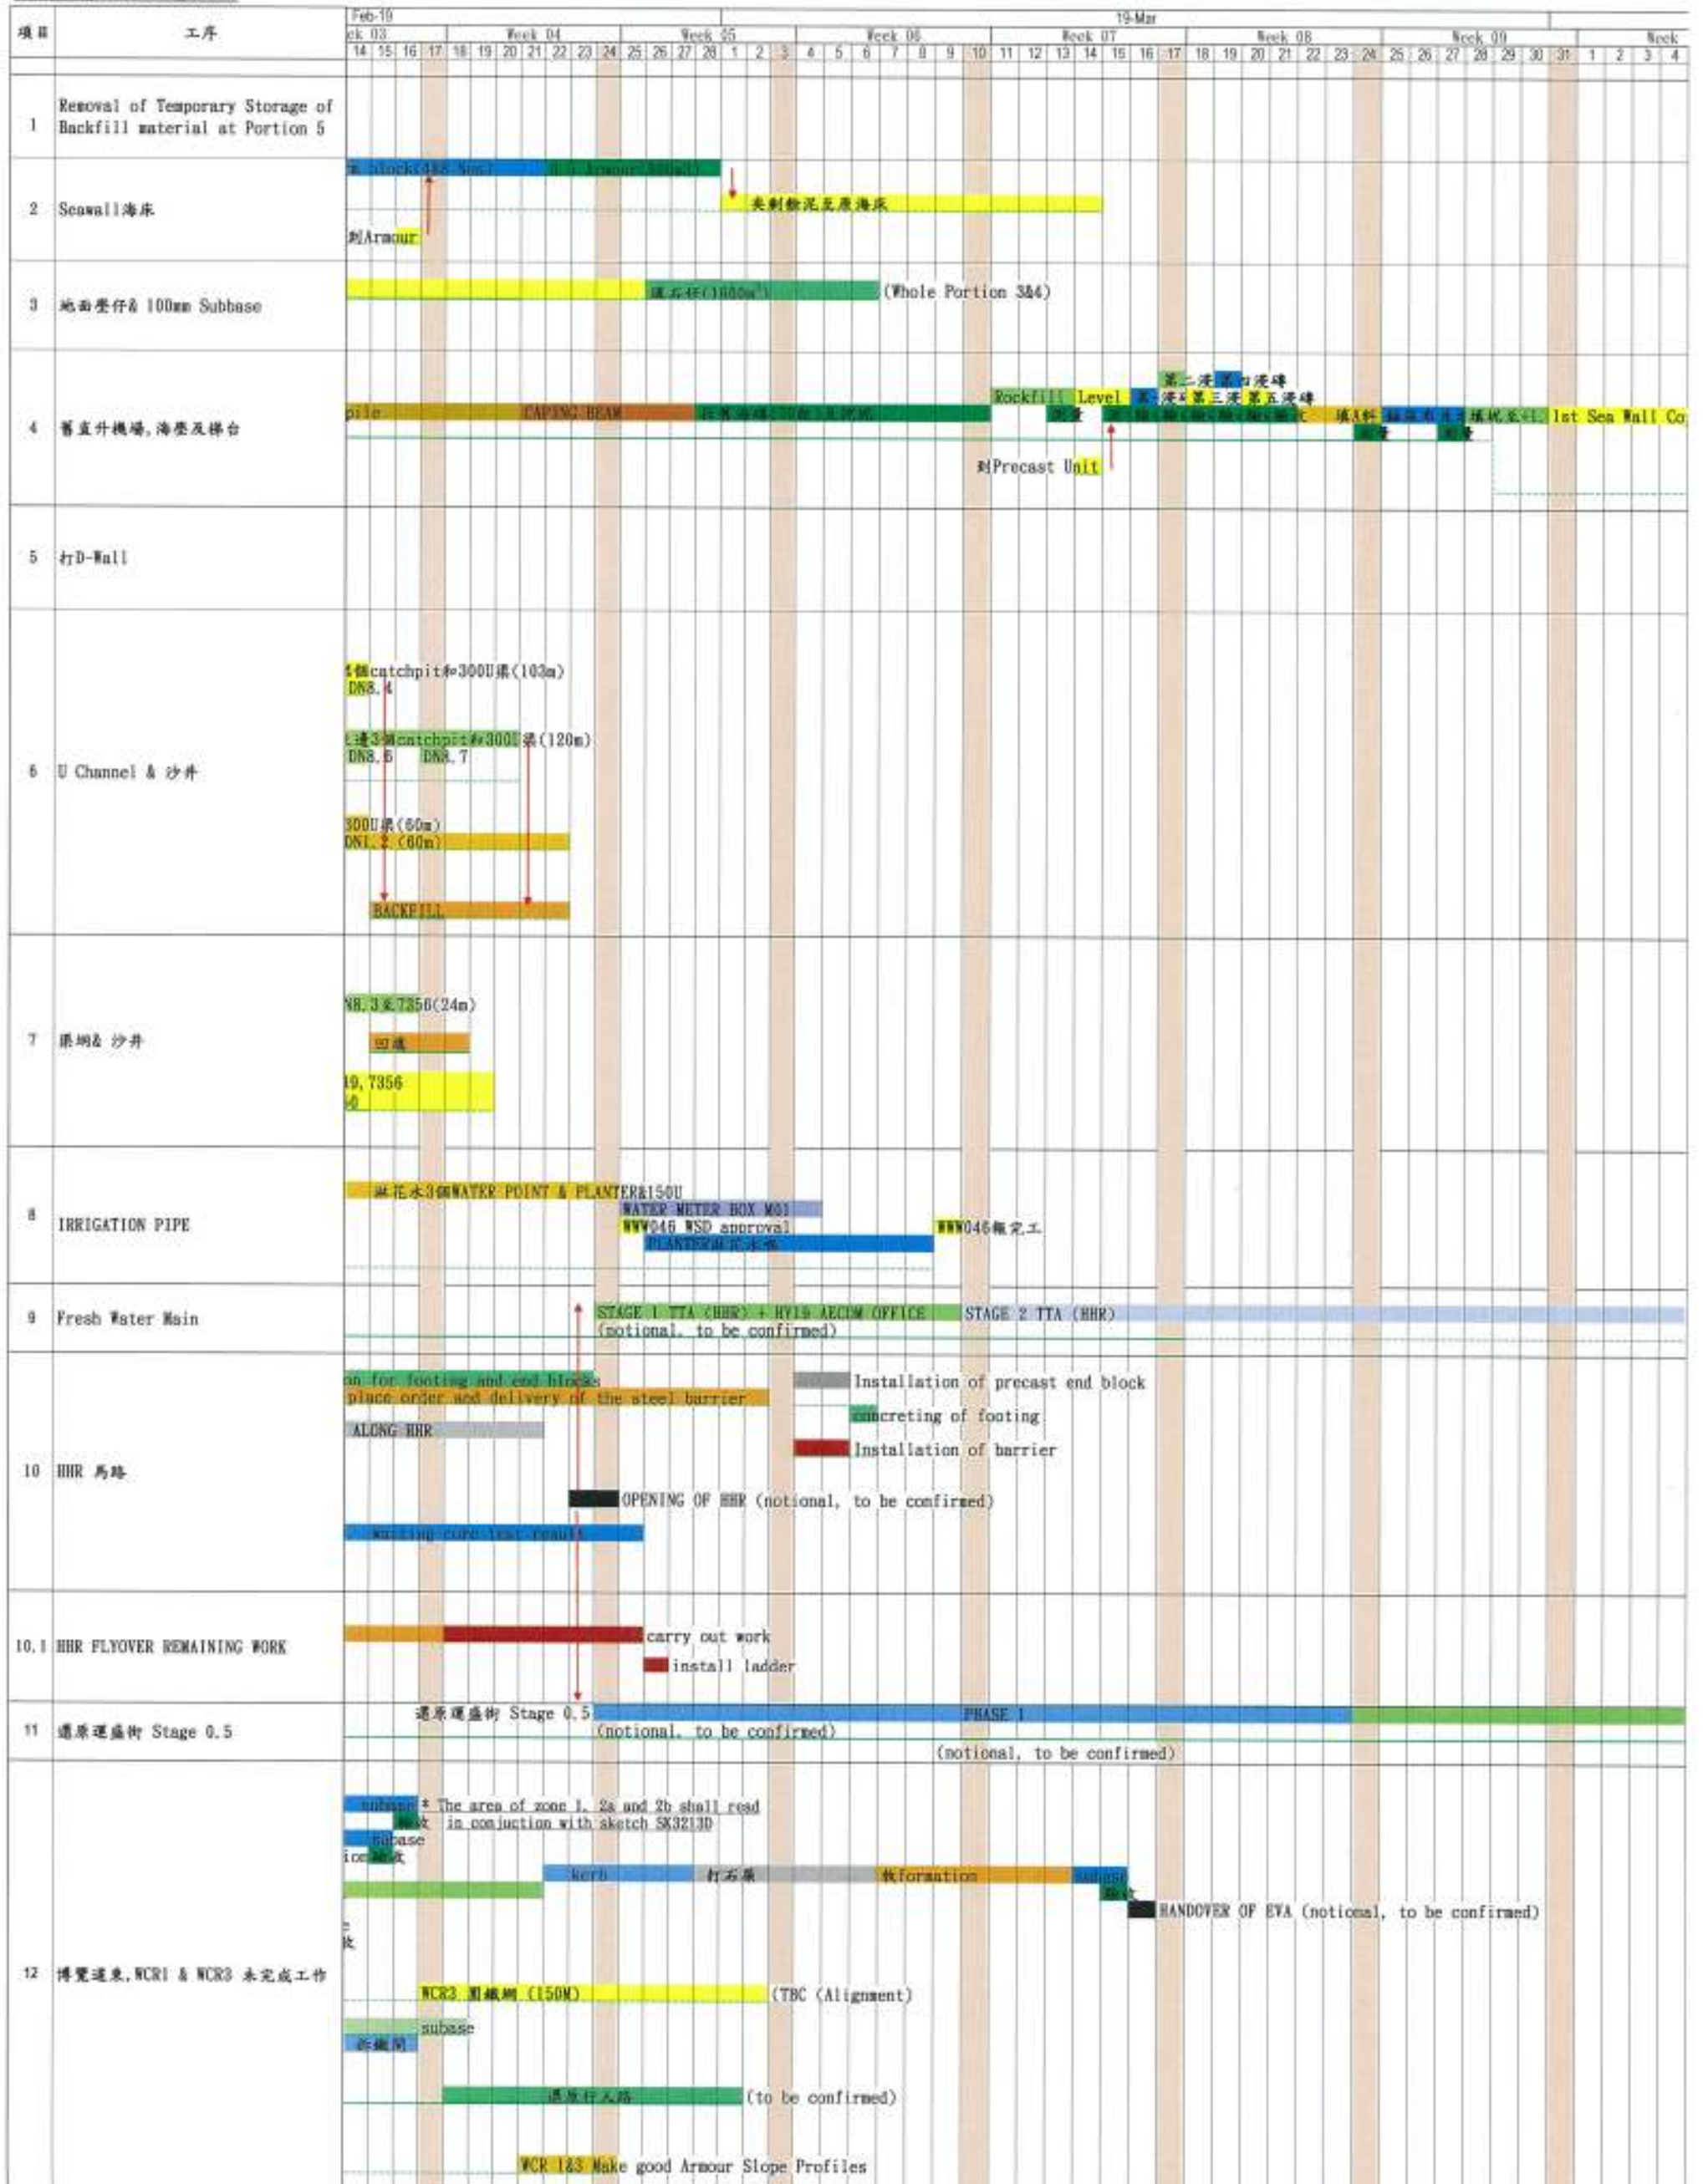

Wan Chai Development Phase II - East
 Central - Wan Chai Bypass at Wan Chai


Contract: HK/2009/02

Remaining Works Programme

項目	工序	June																																			
		Week 18					Week 19					Week 20					Week 21					Week 22															
		27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
1	Removal of Temporary Storage of Backfill material at Portion 5																																				
2	Seawall 海床																																				
3	地面墊仔 100mm Subbase																																				
4	舊直升機塔, 海墜及梯台																																				
5	打D-Wall																																				
6	U Channel & 沙井																																				
7	渠網 & 沙井																																				
8	IRRIGATION PIPE																																				
9	Fresh Water Main																																				
10	HHR 馬路																																				
10.1	HHR FLYOVER REMAINING WORK																																				
11	還原運盛街 Stage 0.5																																				
12	博覽道東, VCR1 & VCR3 未完成工作																																				


**CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019											
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
Promenade Seawall Parapet Construction & EVA																													
SVII12000	Sec VII - Precast parapet	67	18-Nov-17 A	14-May-18	0%																								
SVII12010	Sec VII - Zone CRIII - seawall parapet: Backfilling	14	20-Feb-18	07-Mar-18	0%																								
SVII12120	Sec VII - Zone CRIII - seawall parapet: Construct mass concrete coping	30	08-Mar-18	16-Apr-18	0%																								
SVII12122	Sec VII - Zone CRIII - seawall parapet: reinforced concret coping	17	17-Apr-18	07-May-18	0%																								
SVII12140	Sec VII - Zone CRIII - seawall parapet: construct seawall parapet	30	08-May-18	12-Jun-18	0%																								
SVII12160	Sec VII - CRIII - EVA: watermain	14	13-Jun-18	29-Jun-18	0%																								
SVII12180	Sec VII - CRIII - EVA: U-channel	14	30-Jun-18	17-Jul-18	0%																								
SVII12200	Sec VII - CRIII - EVA: bituminous layer	5	18-Jul-18	23-Jul-18	0%																								
SVII12220	Sec VII - CRIII - EVA: paving block	30	24-Jul-18	27-Aug-18	0%																								
SVII13120	Sec VII - Zone A1, A2 & B - seawall parapet: Construct mass concrete coping	14	28-Dec-17 A	07-Mar-18	68.18%																								
SVII13122	Sec VII - Zone A1, A2 & B - seawall parapet: reinforced concrete coping	18	08-Mar-18	28-Mar-18	0%																								
SVII13140	Sec VII - Zone A1, A2 & B - seawall parapet: Construct seawall parapet	30	09-Apr-18	14-May-18	0%																								
SVII13160	Sec VII - Zone A1, A2 & B - EVA: watermain	14	15-May-18	31-May-18	0%																								
SVII13180	Sec VII - Zone A1, A2 & B - EVA: U-channel	14	01-Jun-18	16-Jun-18	0%																								
SVII13182	Sec VII - Zone A1, A2 & B - EVA: bituminous layer	5	19-Jun-18	23-Jun-18	0%																								
SVII13184	Sec VII - Zone A1, A2 & B - EVA: paving block	30	25-Jun-18	30-Jul-18	0%																								
SVII13200	Sec VII - Zone D - seawall parapet: Remove temporary seawall block	21	07-Mar-18	03-Apr-18	0%																								
SVII13220	Sec VII - Zone D - seawall parapet: Construct mass concrete	30	04-Apr-18	10-May-18	0%																								
SVII13222	Sec VII - Zone D - seawall parapet: reinforced concrete coping	18	11-May-18	01-Jun-18	0%																								
SVII13240	Sec VII - Zone D - seawall parapet: Construct seawall parapet	25	02-Jun-18	03-Jul-18	0%																								
SVII13260	Sec VII - Zone D - EVA : watermain	14	04-Jul-18	19-Jul-18	0%																								
SVII13280	Sec VII - Zone D - EVA : U-channel	14	20-Jul-18	04-Aug-18	0%																								
SVII13300	Sec VII - Zone D - EVA : bituminous layer	5	06-Aug-18	10-Aug-18	0%																								
SVII13320	Sec VII - Zone D - EVA : paving block	30	11-Aug-18	14-Sep-18	0%																								
Promenade Footpath																													
Section 1																													
SVII10440	Sec VII - section 1 footpath - drainage works : connection pipe & U -channel	10	24-May-18	04-Jun-18	0%																								
SVII10445	Sec VII - section 1 footpath - watermain	7	05-Jun-18	12-Jun-18	0%																								
SVII10460	Sec VII - section 1 footpath - lighting	7	13-Jun-18	21-Jun-18	0%																								
SVII10500	Sec VII - section 1 footpath - paving block	21	22-Jun-18	17-Jul-18	0%																								
Section 2																													
SVII12610	Sec VII - section 2 footpath - drainage works : L2202 - L2203A	20	20-Feb-18	14-Mar-18	0%																								
SVII12615	Sec VII - section 2 footpath - watermain	7	15-Mar-18	22-Mar-18	0%																								
SVII12630	Sec VII - section 2 footpath - utilities: TCSS	21	23-Mar-18	20-Apr-18	0%																								
SVII12670	Sec VII - section 2 footpath - paving block	30	21-Apr-18	28-May-18	0%																								
Section 3																													
SVII12850	Sec VII - section 3 footpath - watermain	17	20-Feb-18	10-Mar-18	0%																								
SVII12870	Sec VII - section 3 footpath - utilities (HEC, TCSS, HGC, PCCW)	40	12-Mar-18	02-May-18	0%																								
SVII12875	Sec VII - 3 footpath - drainage works :U chanel	14	03-May-18	18-May-18	0%																								

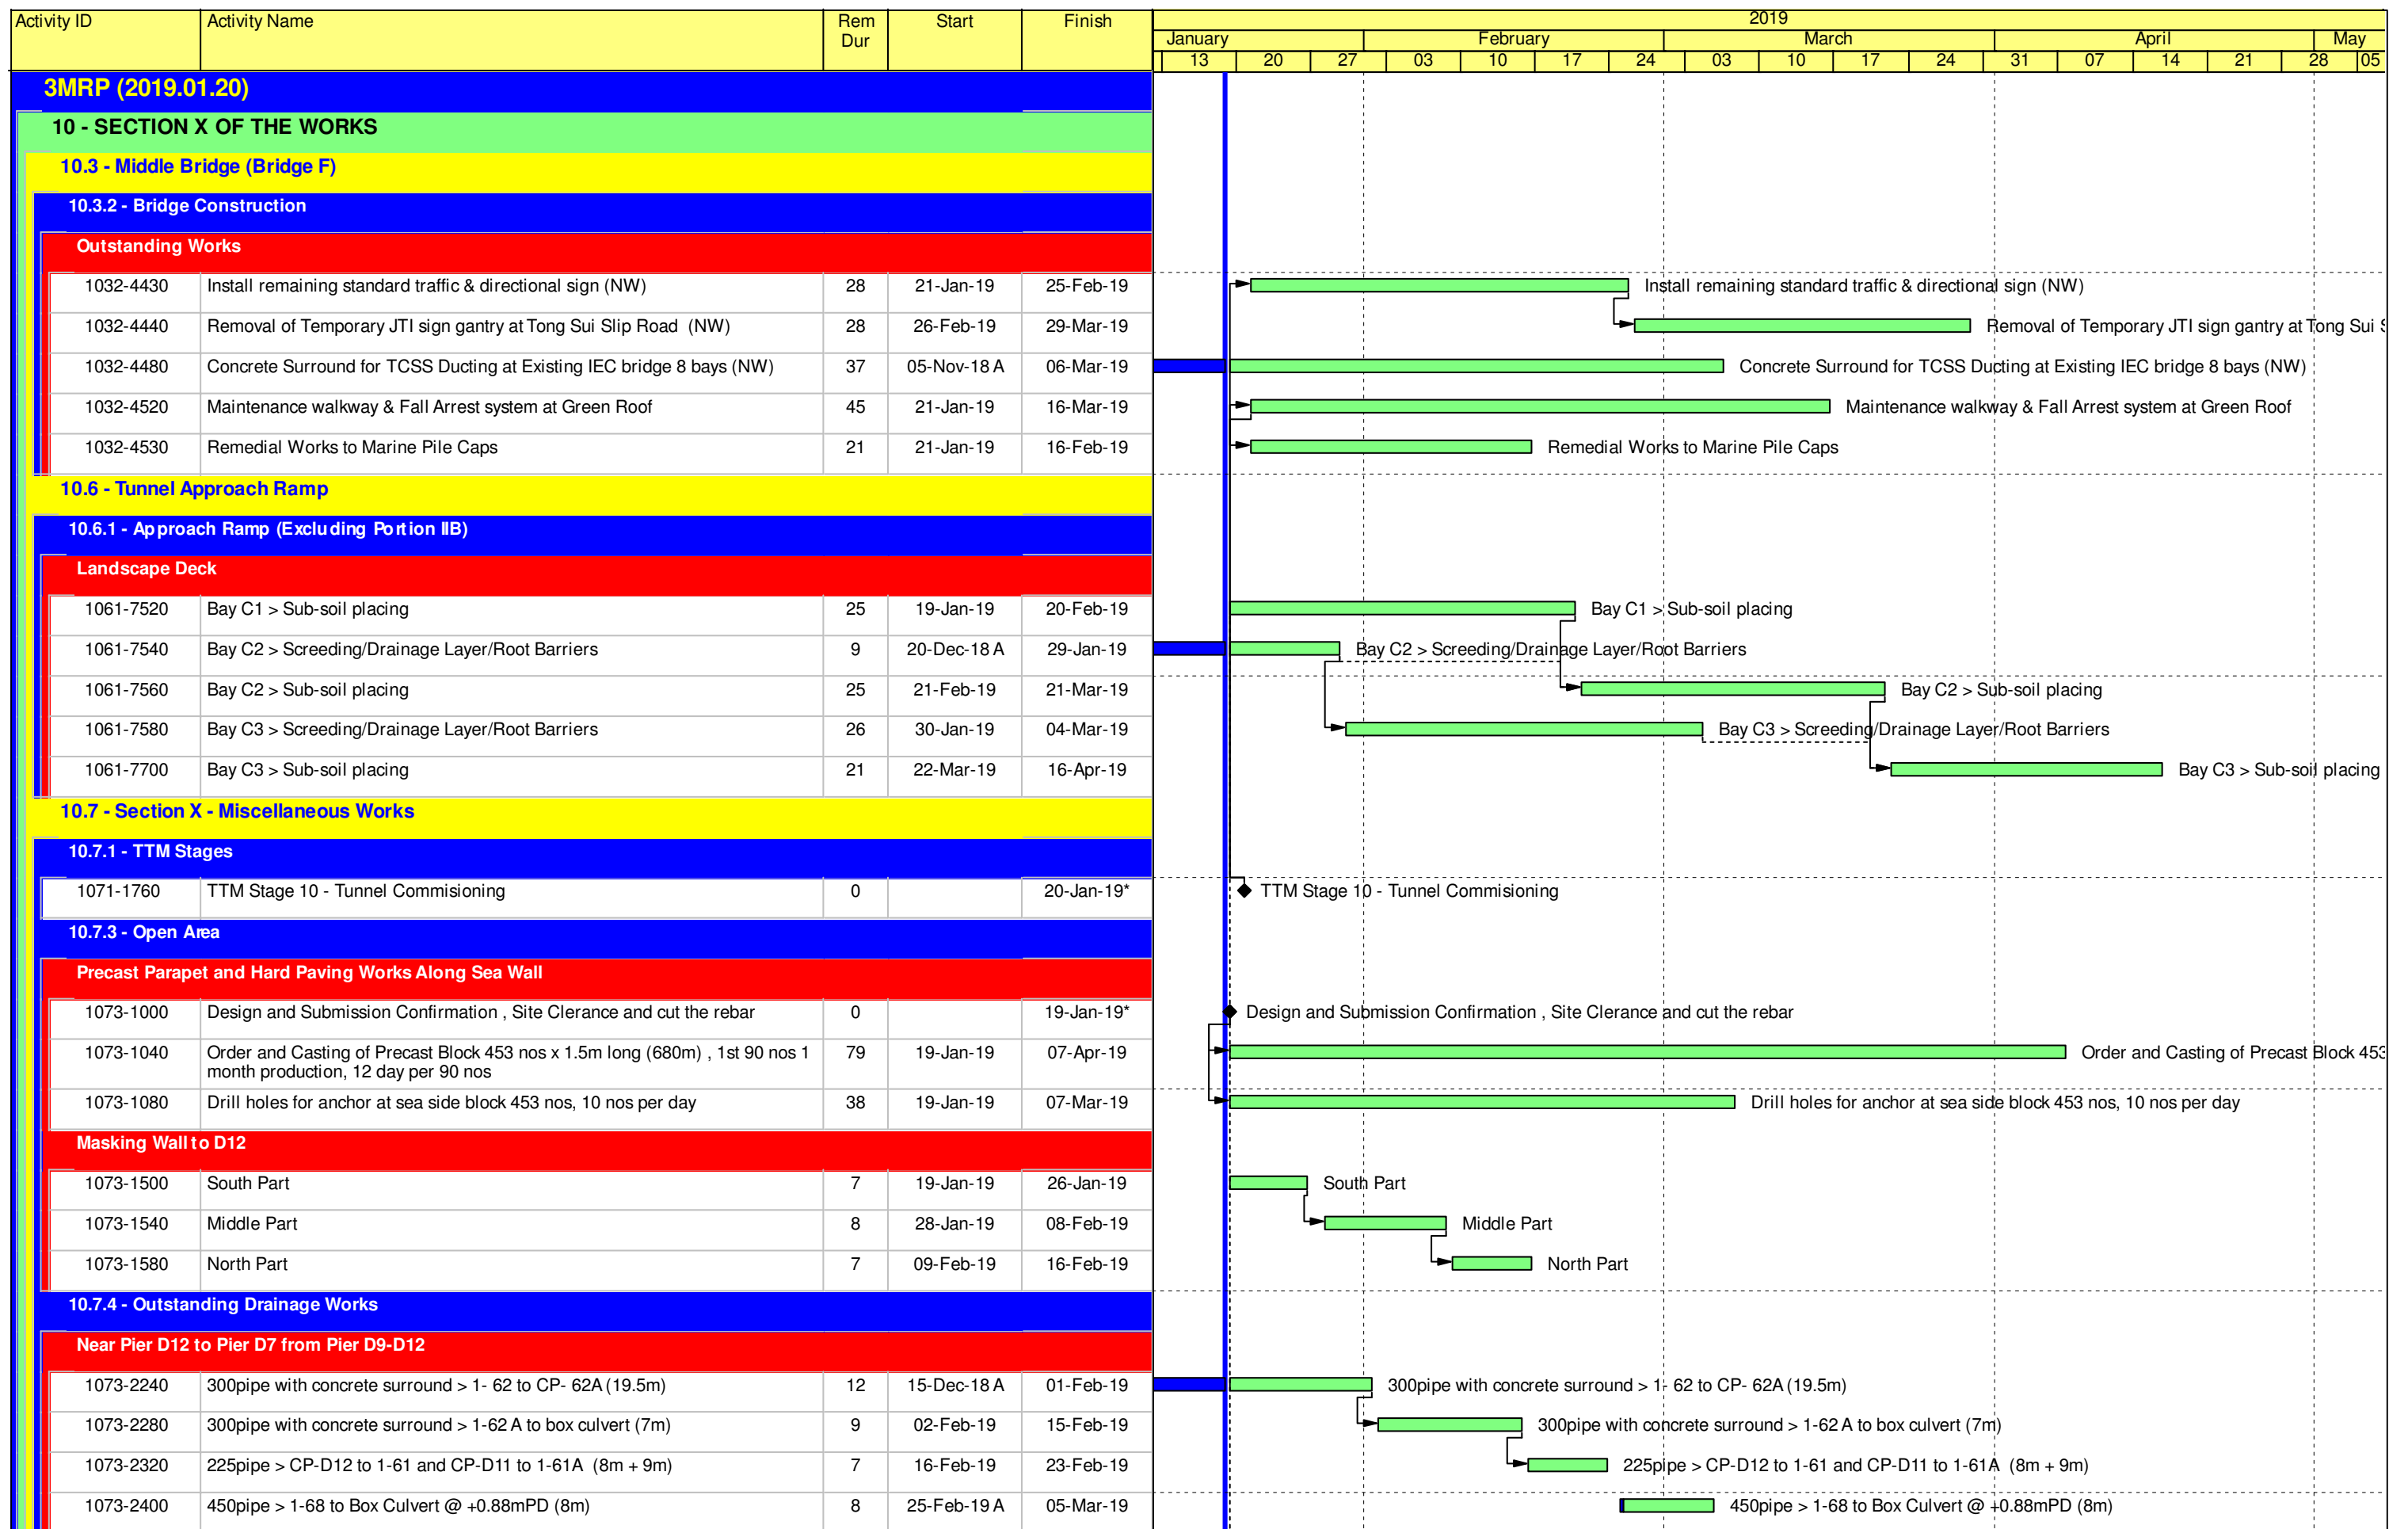


█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Jan.2019 to 20.Apr.2019)

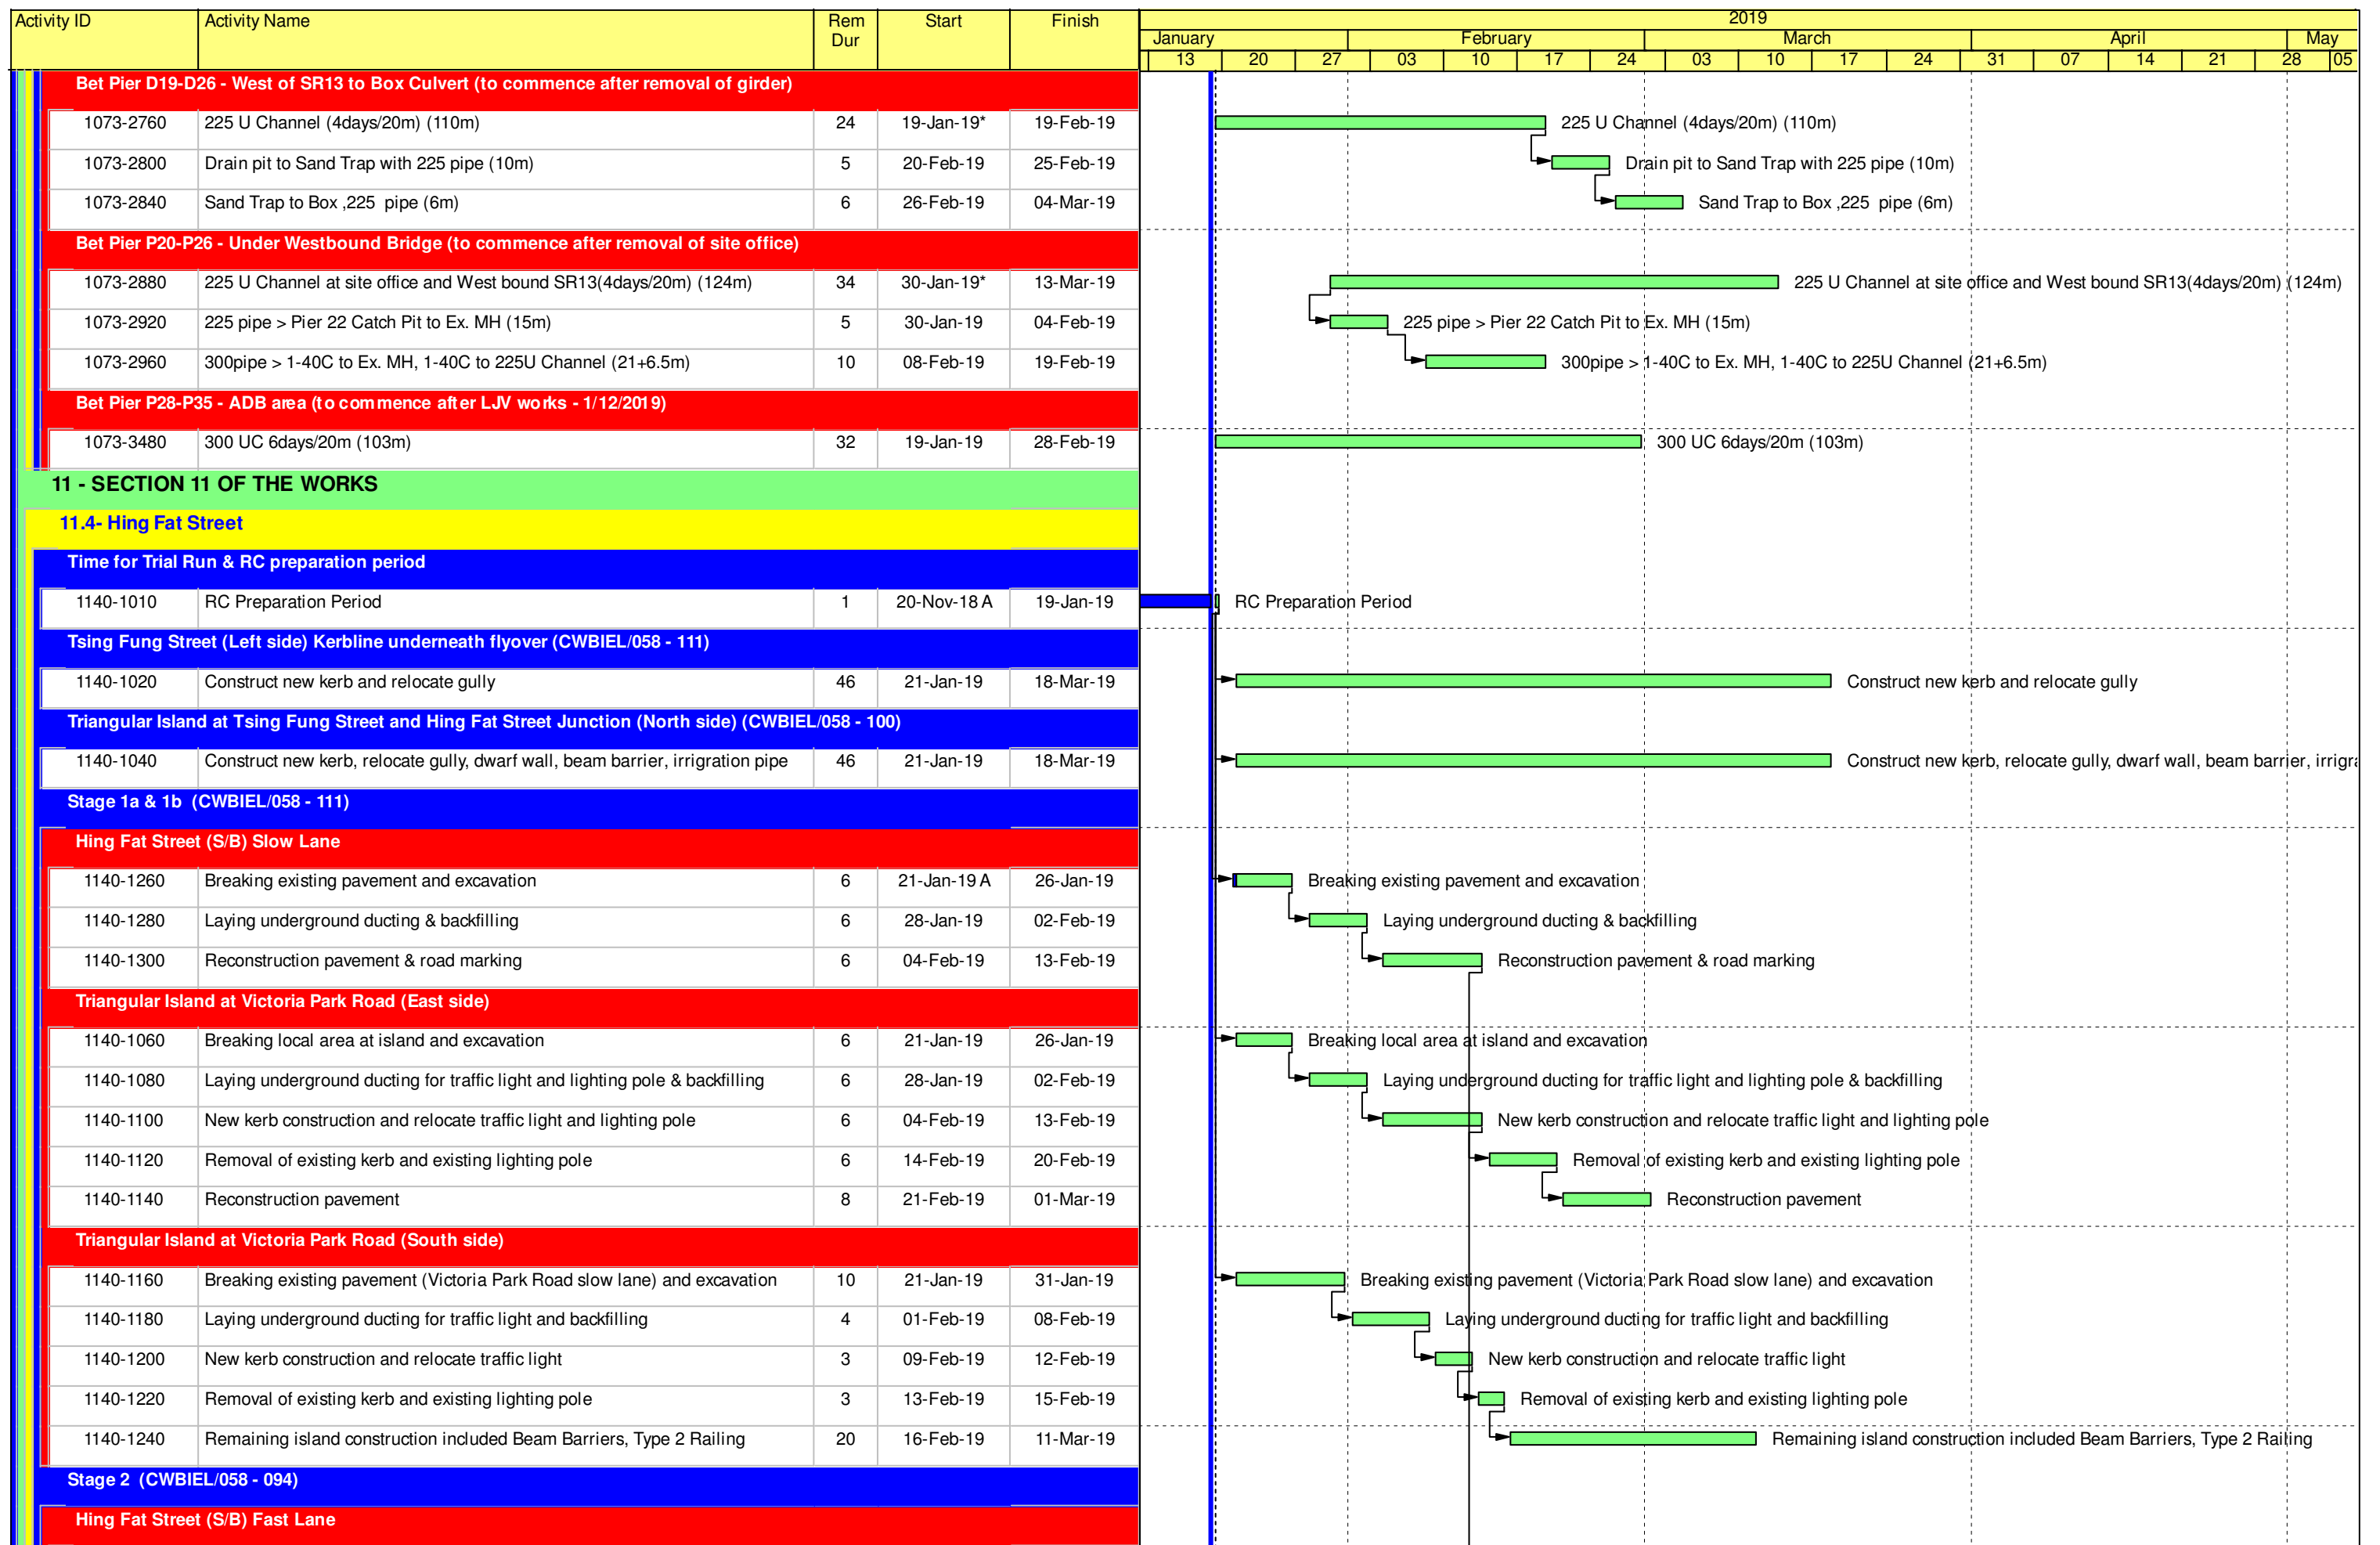

Contract HY/2009/19
Three Months Rolling Programme (20.Jan.2019 to 20.Apr.2019)

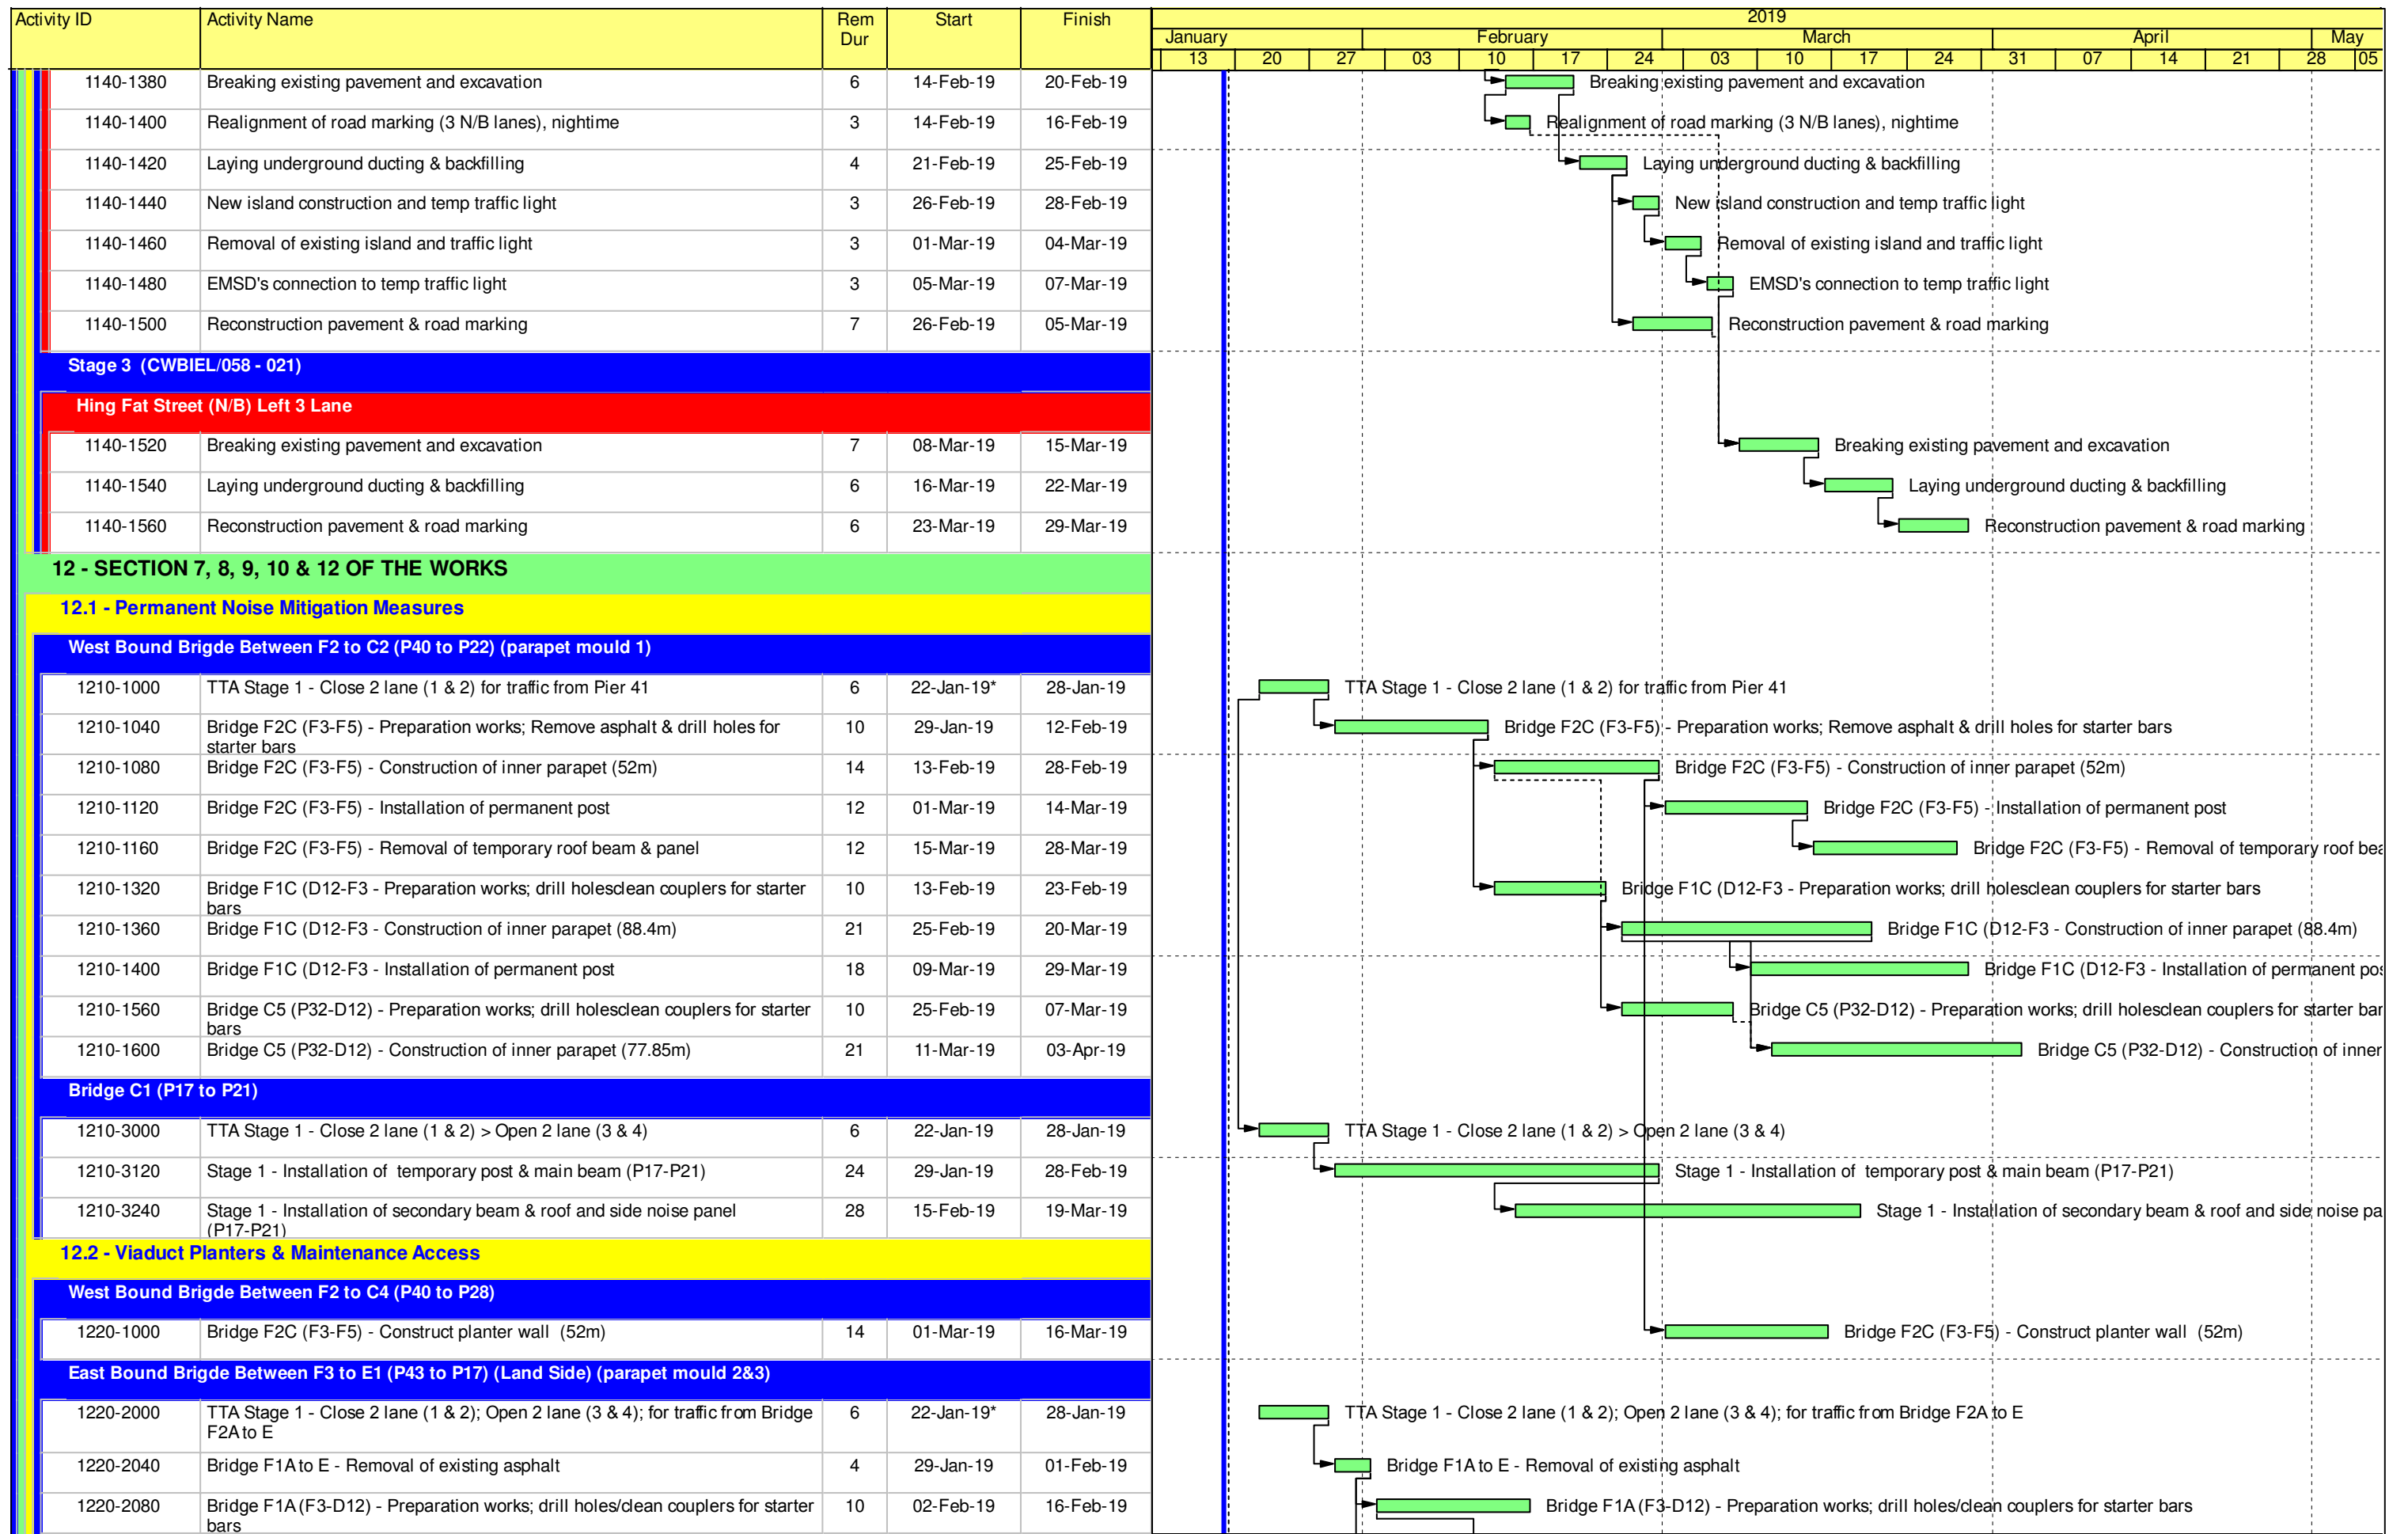

Activity ID	Activity Name	Rem Dur	Start	Finish	2019																
					January			February				March				April				May	
					13	20	27	03	10	17	24	03	10	17	24	31	07	14	21	28	05
1220-2120	Bridge F1A (F3-D12) - Construction of inner parapet (88.4m)	21	13-Feb-19	08-Mar-19																	
1220-2160	Bridge F1A (F3-D12) - Construct planter wall (88.4m)	21	25-Feb-19	20-Mar-19																	
1220-2680	Bridge D2 (D6-D4) - Preparation works; drill holes/clean couplers for starter bars	10	02-Feb-19	16-Feb-19																	
1220-2720	Bridge D2 (D6-D4) - Construction of inner parapet (120m)	21	13-Feb-19	08-Mar-19																	
1220-2760	Bridge D2 (D6-D4) - Construct planter wall (120m)	21	25-Feb-19	20-Mar-19																	
1220-2840	Bridge D1 (D4-D1) - Preparation works; drill holes/clean couplers for starter bars	10	18-Feb-19	28-Feb-19																	
1220-2880	Bridge D1 (D4-D1) - Construction of inner parapet (119m)	21	09-Mar-19	02-Apr-19																	
12.3 - Waterworks																					
1230-1000	Irrigation System - Landscape Deck	121	21-Jan-19	19-Jun-19																	
12.4 - Soft Landscape																					
1240-1000	Top soil & Foothpath at Landscape Deck & green roof	97	23-Mar-19	20-Jul-19																	
15 - SECTION 13A OF THE WORKS																					
15.1 - Soft Landscape																					
1510-1000	Establishment Works at Portion XIII	365	14-May-19	12-May-20																	

- Remaining Level of Effort
- Remaining Work
- Actual Level of Effort
- Critical Remaining Work
- Actual Work
- Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Jan.2019 to 20.Apr.2019)

Activity ID	Activity Name	Original Duration	Start	Finish	2018												2019											
					Dec				Jan				Feb				Mar				Apr				May			
					1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4
Total		2504	21-Mar-13 A	27-Jan-20																								
DWP-08 - (2) - Update Progress As of 20 Dec 18		2504	21-Mar-13 A	27-Jan-20																								
Works in KD9 (Include Re-provisioning Works of KD4,KD5)		341	30-Jan-18 A	27-Jan-19																								
External Works Under KD9		201	30-Jan-18 A	17-Jan-19																								
Zone 4 up to Elderly Facilities		201	30-Jan-18 A	17-Jan-19																								
Elderly Facilities V/039 Received on 22 Jun 2017		201	30-Jan-18 A	17-Jan-19																								
EXW_2270	Facilities fabrication	90	30-Jan-18 A	15-Jan-19	Facilities fabrication																							
EXW_2280	Ground levelling, drainage works and safety met installation	30	16-Nov-18 A	17-Jan-19	Ground levelling, drainage works and safety met installation																							
Additional Walkway & Arbour V/040 Received on 22 Aug 2017		30	03-May-18 A	27-Nov-18 A																								
EXW_2320	Arbour installation and walkway construction	30	03-May-18 A	27-Nov-18 A	Arbour installation and walkway construction																							
Reverting Traffic for IEC,VP Rd & TF St & Seawall Reinstatement (KD9)		341	13-Apr-18 A	27-Jan-19																								
TTA Revert Traffic Back to Original Alignment		251	13-Apr-18 A	25-Dec-18																								
East Bound TTA - IEC East Bound, Victoria Park Road & footpath along Sea Side		146	20-Jun-18 A	07-Dec-18 A																								
TTM Stage 1 - IEC (East Bound)		6	01-Dec-18 A	07-Dec-18 A																								
Reinstatement Existing Structure		6	01-Dec-18 A	07-Dec-18 A																								
EB_1020	Install metal parapet on parapet wall (30m)	6	01-Dec-18 A	07-Dec-18 A	Install metal parapet on parapet wall (30m)																							
TTM Stage 2 - Revert Traffic back to Original Victoria Road		4	01-Dec-18 A	07-Dec-18 A																								
Existing Bridge Parapet Reinstatement		4	01-Dec-18 A	07-Dec-18 A																								
EB_1180	Install metal parapet on parapet wall (40m)	4	01-Dec-18 A	07-Dec-18 A	Install metal parapet on parapet wall (40m)																							
TTM Stage 3 - Reinstatement of Footpath along Seafront		15	20-Jun-18 A	04-Aug-18 A																								
Reinstatement of Existing Utilities at Existing Footpath		2	20-Jun-18 A	20-Jun-18 A																								
EB_1580	Water main Connection by WSD	2	20-Jun-18 A	20-Jun-18 A																								
Reinstatement of Permanent Footpath at Seafront		1	04-Aug-18 A	04-Aug-18 A																								
EB_1650	Pedestrian diversion on Permanent Footpath	1	04-Aug-18 A	04-Aug-18 A	Pedestrian diversion on Permanent Footpath																							
West Bound - IEC West Bound & Tsing fung Street		251	13-Apr-18 A	25-Dec-18																								
TTM Stage 2 - Revert Traffic back to Original Tsing Fung Street		5	29-Dec-18 A	25-Dec-18																								
Existing Bridge Parapet Reinstatement		5	29-Dec-18 A	25-Dec-18																								
IECW_1140	Install metal parapet on parapet wall (60m)	5	29-Dec-18 A	25-Dec-18	Install metal parapet on parapet wall (60m)																							
TTM Stage 3 - Reinstatement of Victoria Park		21	13-Apr-18 A	01-Dec-18 A																								
Reinstatement Works inside Victoria Park		21	13-Apr-18 A	01-Dec-18 A																								
IECW_1470	Slope Reinstatement of Victoria Park	21	13-Apr-18 A	01-Dec-18 A	Slope Reinstatement of Victoria Park																							
Completion of Minor Outstanding / Remaining Works for KD9		230	03-May-18 A	27-Jan-19																								
East Bound - Minor Outstanding Works in Footpath after Substantial Completion of KD9		137	27-Jun-18 A	20-Dec-18 A																								
Minor Reinstatement Works for Existing Sign Gantry		63	19-Jul-18 A	19-Sep-18 A																								
EB_1780	Erect Sign Gantry Steel Supports and Sign Gantry Beam across VPR and IEC E/B	4	19-Jul-18 A	05-Aug-18 A																								
EB_1760	Connection of Public Lighting by HyD (Lighting)	2	14-Sep-18 A	18-Sep-18 A																								
EB_1790	Installation of E & M at Sign Gantry (night work)	1	19-Sep-18 A	19-Sep-18 A																								
Minor Reinstatement Works for Central Median of IEC & Footbridge		6	05-Dec-18 A	20-Dec-18 A																								
EB_1810	Dismantlement of temp directional sign mounted on extg footbridge	1	05-Dec-18 A	05-Dec-18 A	Dismantlement of temp directional sign mounted on extg footbridge																							
EB_1800	Reconstruction of central divider (6m long, night work)	6	17-Dec-18 A	20-Dec-18 A	Reconstruction of central divider (6m long, night work)																							
Minor Reinstatement Works for Footpath		9	27-Sep-18 A	15-Nov-18 A																								
EB_1840	Re-provision of Tree	8	27-Sep-18 A	15-Nov-18 A																								
EB_1830	Reinstatement of District Council Welcome Sign and opening plaque at Planter area	1	03-Oct-18 A	03-Oct-18 A																								



- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Date	Revision	Checked	Approved
20-Dec-18	DWP-08 (2) - 3 Months Rolling	TL	TL

Activity ID	Activity Name	Original Duration	Start	Finish	2018												2019											
					Dec				Jan				Feb				Mar				Apr				May			
					1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4
Minor Reinstatement Works for Bus Stop																												
EB_1870	Relocation of Bus Stop	1	27-Jun-18 A	27-Jun-18 A																								
EB_1880	Reinstate Planter(Previous Temporary Bus Stop)	5	20-Jul-18 A	05-Oct-18 A																								
Minor Reinstatement Works for Loop Detector																												
EB_1900	Construction of concrete plinth and fix counter housing for Loop Detector (ILDS)	3	14-Jul-18 A	14-Jul-18 A																								
EB_1890	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)	1	23-Aug-18 A	24-Aug-18 A																								
West Bound - Completion of Minor Outstanding / Remaining Works for KD9																												
Minor Reinstatement Works for Victoria Park																												
IECW_1500	Re-provision of Tree	32	03-May-18 A	27-Jan-19	Re-provision of Tree																							
IECW_1510	Laying Irrigation Main	10	27-Sep-18 A	30-Dec-18	Laying Irrigation Main																							
IECW_1520	Construct Landscape Footpath and Lightings	7	05-Nov-18 A	27-Dec-18	Construct Landscape Footpath and Lightings																							
Minor Reinstatement Works in IEC West Bound																												
IECW_1640	Erection of new precast concrete panels (12 nos.) at abutment M facing to VPR	2	13-Jul-18 A	17-Jul-18 A																								
IECW_1620	Repairing of concrete defects on extg concrete deck and abutment M	30	15-Oct-18 A	24-Nov-18 A	Repairing of concrete defects on extg concrete deck and abutment M																							
IECW_1610	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)	57	24-Nov-18 A	24-Dec-18 A	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)																							
IECW_1660	Replacement of new rubber seal on extg MJ at IEC W/B and E/B (night work)	4	26-Nov-18 A	31-Dec-18 A	Replacement of new rubber seal on extg MJ at IEC W/B and E/B (night work)																							
IECW_1600	Replacement of new movement joint at IEC W/B (Sun midnight only)	8	27-Dec-18 A	30-Dec-18 A	Replacement of new movement joint at IEC W/B (Sun midnight only)																							
Works in Victoria Park (KD4, KD5, KD9)																												
Re-Provisioning Works																												
Nursery Compound																												
Nursery compound																												
Fire Services																												
VP_NC_2030	FS inspection	14	20-Aug-18 A	27-Sep-18 A																								
Plumbing and Flushing Water Supplies																												
VP_NC_2100	WSD Inspection	14	19-Aug-18 A	19-Aug-18 A																								
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks																												
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)																												
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365	28-Jan-19	27-Jan-20																								
KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH>500mm)																												
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365	28-Jan-19	27-Jan-20																								
KD18 - Section 11: Transplanted Trees DBH>500mm in Portion VA and XII																												
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365	28-Jan-19	27-Jan-20																								
KD10 - Preservation and Protection of Trees																												
PPT_0000	Preservation and Protection of Existing Trees	1088	21-Mar-13 A	28-Jan-19	Preservation and Protection of Existing Trees																							
KD15 & KD8 - Mooring Components Upkeep (CBTS and ATS)																												
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979	15-May-14 A	21-Dec-18	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS																							



- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Date	Revision	Checked	Approved
20-Dec-18	DWP-08 (2) - 3 Months Rolling	TL	TL

Data Date: 20-Jan-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018	2019	2019	2019	2019
							Jan	Feb	Mar	Apr
Update 2019-01-20 CWB(CC) - Commissioning Contract (DWP 4a)										
PRELIMINARIES AND GENERAL REQUIREMENTS										
Salient Key Dates and Milestones										
Contract Key Dates										
KD007	KD7 - Completion of Section 2 of the Works (1771 days) - include EOT No.12 (414 days)	0		20-Jan-19*	-125		▲	◆		
KD008	KD8 - Completion of Section 3 of the Works (1771 days) - include EOT No.12 (414 days)	0		20-Jan-19*	-125		▲	◆		
KD010	KD10 - Completion of Section 5 of the Works (1787 days) - include EOT No.12 (125 days)	0		20-Jan-19*	-125		▲	◆		
Anticipated Completion Dates										
KD11	KD11 - Completion of Section 6 of the Works (1445 days) - include EOT No.12 (149 days)	0		20-Feb-19*	-374			◆		
Possession Dates and Vacation Dates										
PO-IIa	Possession of Portion IIa (Day 1) - WVB below +6.5mPD	1329	28-Feb-14 A	17-Feb-19	-342					
PO-III	Possession of Portion III (Day 120) - CH1805-2600	1209	28-Jun-14 A	17-Feb-19	-342					
PO-Ib	Possession of Portion Ib (Day 242) - CH1580-1805	1087	28-Oct-14 A	17-Feb-19	-342					
PO-IXd	Possession of Portion IXd (Day 266) - CH4600-4860	1063	21-Nov-14 A	17-Feb-19	-342					
PO-XI	Possession of Portion XI (Day 296) - EVS	1033	21-Dec-14 A	17-Feb-19	-154					
PO-IIc	Possession of Portion IIc (Day 336) - CH1360-1580	993	30-Jan-15 A	17-Feb-19	-342					
PO-IIb	Possession of Portion IIb (Day 336) - WVB above +6.5mPD	669	30-Jan-15 A	17-Feb-19	-342					
PO-IXa	Possession of Portion IXa (Day 392) - CH4860-5150	937	27-Mar-15 A	17-Feb-19	-342					
PO-Va	Possession of Portion V (Day 607) - CH2950-3210	722	28-Oct-15 A	17-Feb-19	-342					
PO-VII_a1	Possession of Portion VII (Day 762) - CH3911-4250 (below -6.0mPD)	659	30-Dec-15 A	17-Feb-19	-342					
PO-Vc	Possession of Portion V (Day 607) - CH3210-3250	658	15-Jan-16 A	17-Feb-19	-342					
PO-VIb_b1	Possession of Portion VIb (Day 761) - CH3428-3625 (E/B)	619	18-Feb-16 A	17-Feb-19	-342					
PO-VIb_b2	Possession of Portion VIb (Day 761) - CH3428-3625 (W/B)	568	29-Feb-16 A	17-Feb-19	-342					
PO-Xa_1	Possession of Portion Xa (Day 650) - ADB Southern Portion (AECOM letter ref: 2015007890T)	589	07-Mar-16 A	17-Feb-19	-538					

- ◆ Current Milestone
- Level of Effort
- ▲ Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 59 (January 2019) THREE MONTH ROLLING

Project ID: H2613-U059
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U059
 Page 1 of 8

Date	Revision	Checked	Approv...
20-Dec-18	U058	AT	CW
20-Jan-19	U059	AT	CW

Data Date: 20-Jan-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2019				
						2018	Jan	Feb	Mar	Apr
PO-Xb_1	Possession of Portion Xb (Day 804) - ADB Northern Portion	589	07-Mar-16 A	17-Feb-19	-538					
PO-Vb1	Possession of Portion V (Day 607) - SR3	587	11-Mar-16 A	17-Feb-19	-154					
PO-Ia	Possession of Portion Ia (Day 789) - SCB / SCP1 / SCP2 / Rumsey Street Flyover	600	28-Mar-16 A	17-Feb-19	-526					
PO-VII_a2	Possession of Portion VII (Day 762) - CH3800-3911 (below -6.0mPD)	567	31-Mar-16 A	17-Feb-19	-342					
PO-IXc_1	Possession of Portion IXc (Day 712) - EVB above 3.6mPD - Relinquished on 12 Apr 2016	445	29-Jul-16 A	17-Feb-19	-548					
PO-IXb_1	Possession of Portion IXb (Day 712) - EVB (below +3.6mPD to tunnel top slab) - Relinquished on 12 Apr 2016	445	05-Aug-16 A	17-Feb-19	-548					
PO-VIa_a	Possession of Portion VIa (Day 823) - CH3250-3283	425	15-Aug-16 A	17-Feb-19	-342					
PO-Vb2_a	Possession of Portion V (Day 607) - SR2	456	15-Aug-16 A	17-Feb-19	-342					
PO-VIc_a	Possession of Portion VIc (Day 761) - CH3770-3800 (Access Shaft Opening)	391	23-Sep-16 A	17-Feb-19	-342					
PO-VIb_c	Possession of Portion VIb (Day 761) - CH3625-3770	391	23-Sep-16 A	17-Feb-19	-342					
PO-IVa1	Possession of Portion IVa (Day 930) - CH2600-2720	323	30-Nov-16 A	17-Feb-19	-342					
PO-IVb2	Possession of Portion IVb (Day 930) - MVB (GLD-H)	233	28-Feb-17 A	17-Feb-19	-496					
PO-VIIIa_a	Possession of Portion VIIIa (Day 929) - CH4530-4591 W/B	233	28-Feb-17 A	17-Feb-19	-342					
PO-VIIIa	Possession of Portion VIIIa (Day 929) - CH4250-4600 (Remaining)	241	12-Mar-17 A	17-Feb-19	-342					
PO-VIIIb	Possession of Portion VIIIb (Day 929) - SR8 (CH700-350)	233	12-Mar-17 A	17-Feb-19	-342					
PO-VIIIc	Possession of Portion VIIIc (Day 1039) - SR8 (CH350-310) / SCP4	233	12-Mar-17 A	17-Feb-19	-342					
PO-IVa2_a	Possession of Portion IVa (Day 930) - CH2720-2950	241	12-Mar-17 A	17-Feb-19	-342					
PO-IVb1	Possession of Portion IVb (Day 930) - MVB (GLA-C)	239	14-Mar-17 A	17-Feb-19	-496					
PO-IVa2_b	Possession of Portion IVa (Day 930) - SR1	203	30-Mar-17 A	17-Feb-19	-342					
PO-Vb2_b	Possession of Portion V (Day 607) - SCP3	182	03-Jul-17 A	17-Feb-19	-342					
PO-VIb_a	Possession of Portion VIb (Day 761) - CH3400-3428	80	31-Jul-17 A	17-Feb-19	-342					
PO-VIa_b	Possession of Portion VIa (Day 823) - CH3283-3400	80	31-Jul-17 A	17-Feb-19	-342					
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-Jan-19	10-May-19	-342					
Submissions and Approvals										

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 59 (January 2019) THREE MONTH ROLLING



Project ID: H2613-U059
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U059
 Page 2 of 8

Date	Revision	Checked	Approv...
20-Dec-18	U058	AT	CW
20-Jan-19	U059	AT	CW

Data Date: 20-Jan-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

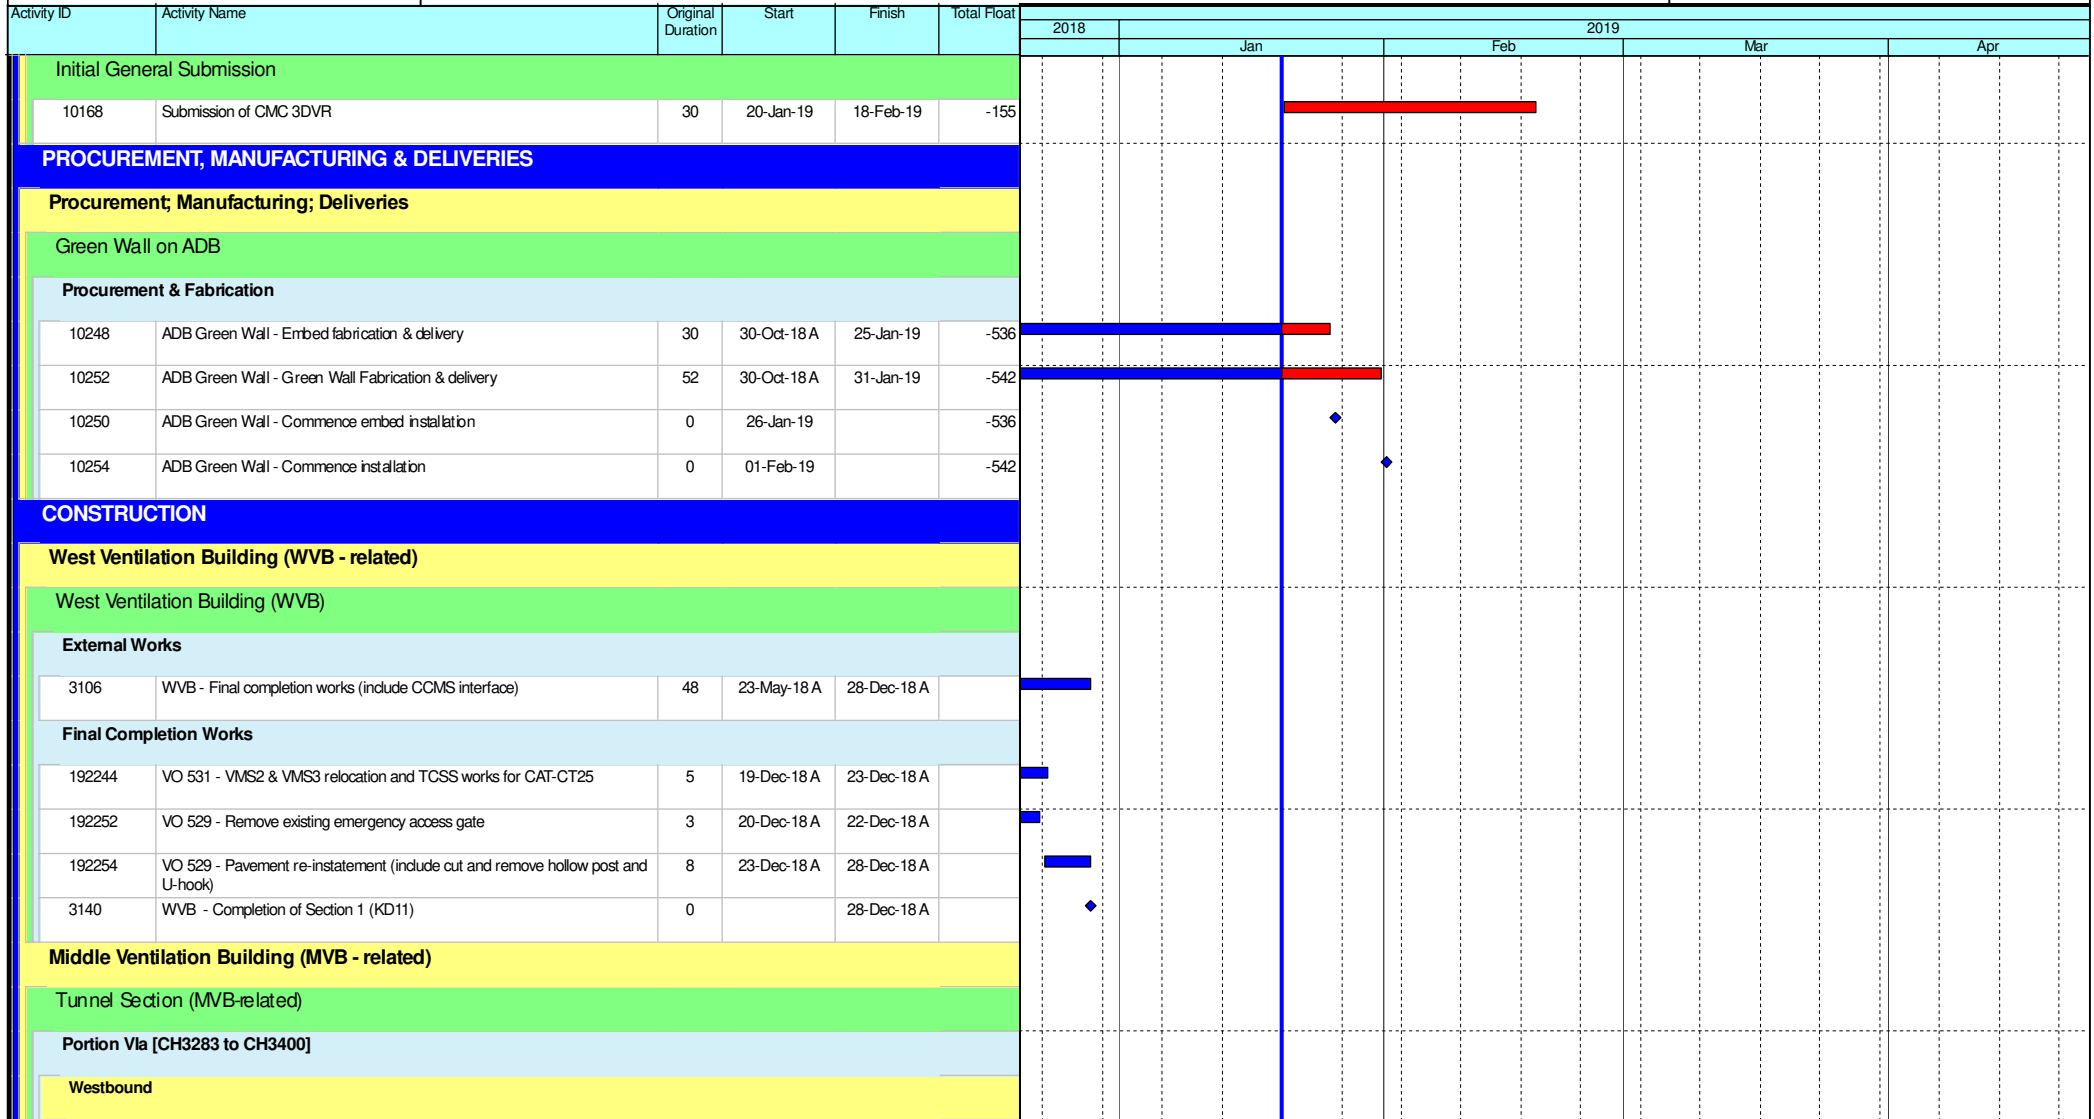

Leighton Contractors (Asia) Limited Programme Update 59 (January 2019) THREE MONTH ROLLING



Project ID: H2613-U059
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U059
 Page 3 of 8

Date	Revision	Checked	Approv...
20-Dec-18	U058	AT	CW
20-Jan-19	U059	AT	CW

Data Date: 20-Jan-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

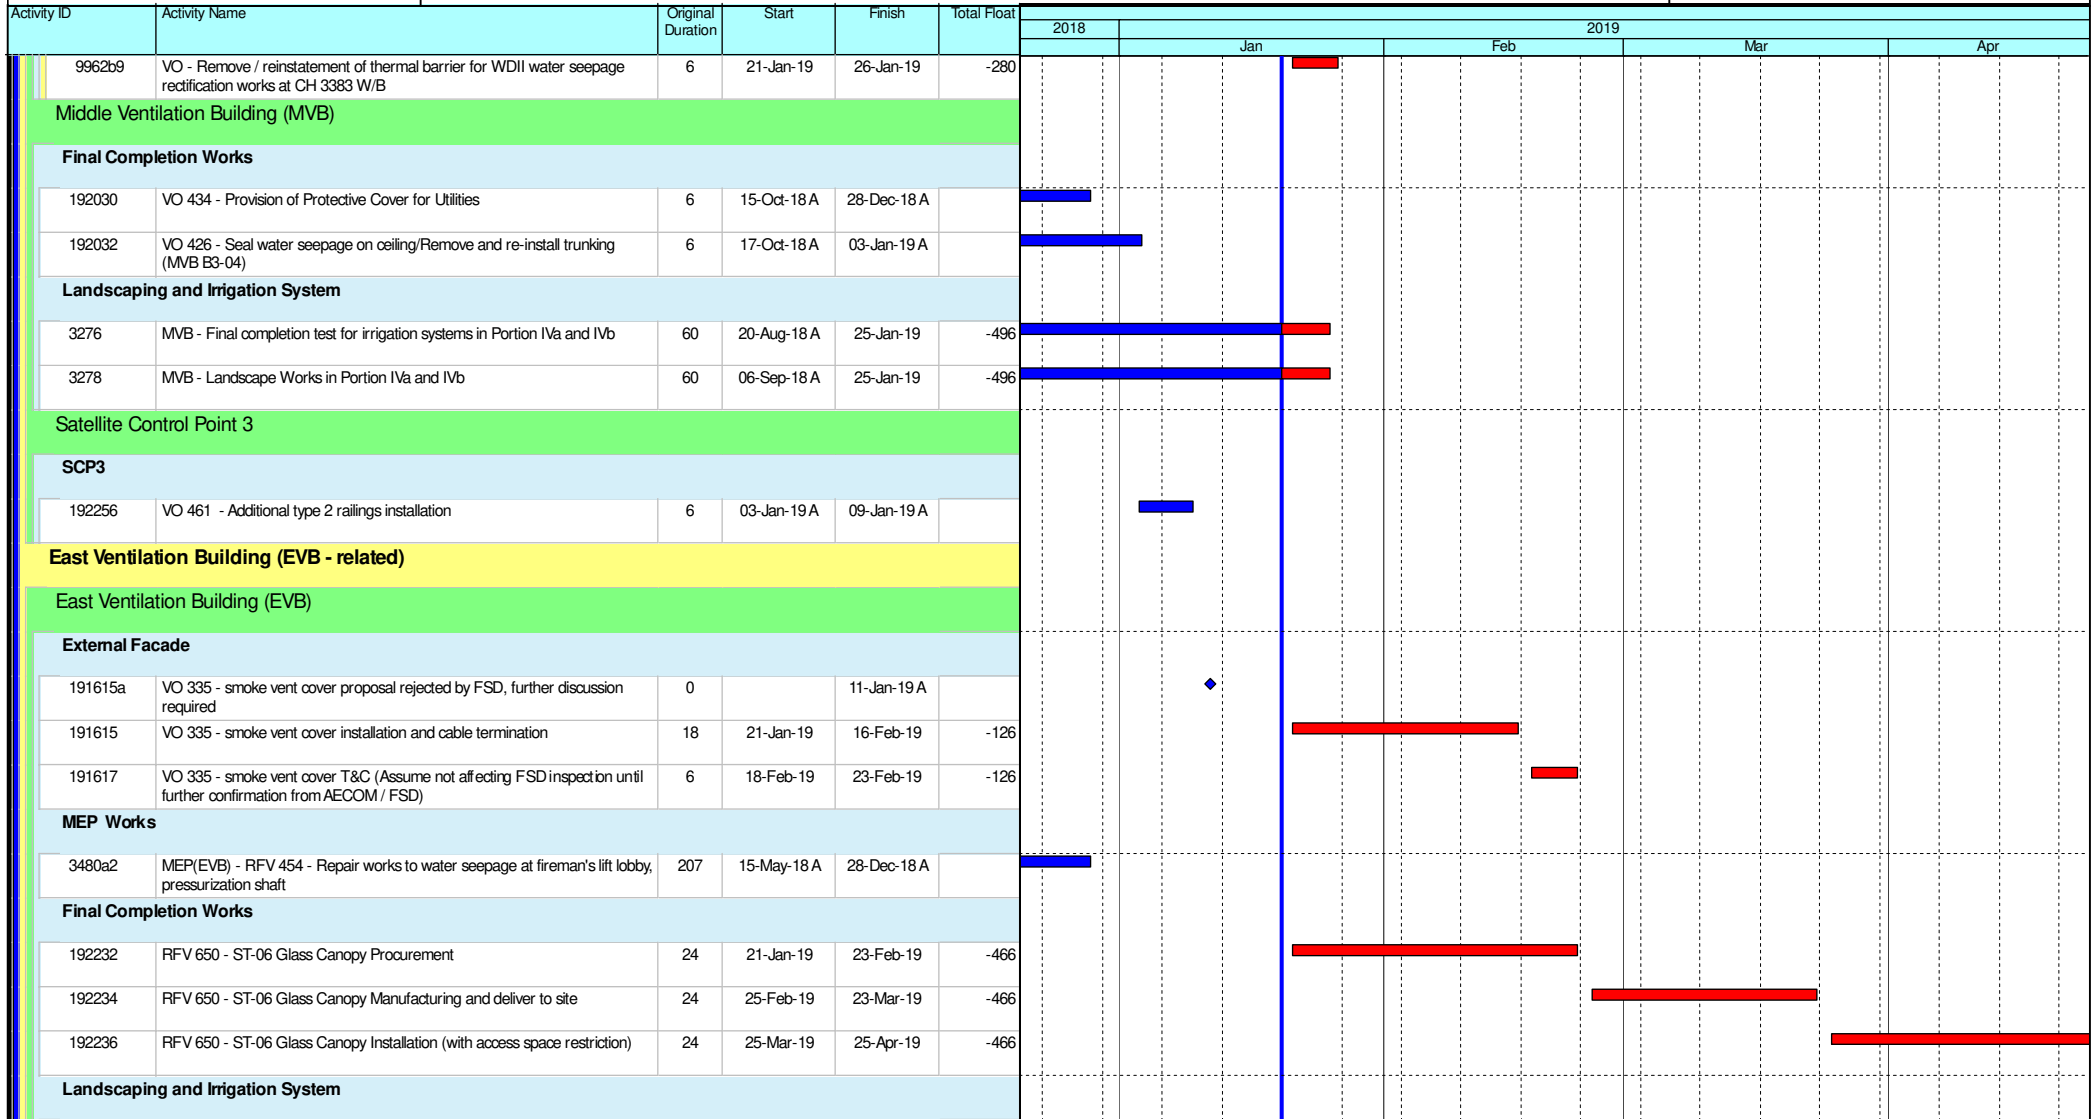

Leighton Contractors (Asia) Limited Programme Update 59 (January 2019) THREE MONTH ROLLING

Project ID: H2613-U059
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U059
 Page 4 of 8

Date	Revision	Checked	Approv...
20-Dec-18	U058	AT	CW
20-Jan-19	U059	AT	CW

Data Date: 20-Jan-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018												2019																																			
						Jan												Feb												Mar												Apr											
3476	EVB - Final completion test for irrigation systems in Portion IXc	52	20-Jan-19	12-Mar-19	-520																																																
191539d	VO 311 - Excavation & Installation of pipes and water points	36	20-Jan-19	24-Feb-19	-562																																																
191539e	VO 311 - WW 046 Part I / II submission and cert	36	20-Jan-19	24-Feb-19	-562																																																
3478	EVB - Landscape Works in Portion IXc	52	26-Jan-19	18-Mar-19	-548																																																
191539f	VO 311 - WW 046 Part IV submission and cert	12	25-Feb-19	08-Mar-19	-562																																																
191539g	VO 311 - Backfill	12	25-Feb-19	08-Mar-19	-562																																																
191539h	VO 311 - Defects & Water test	24	09-Mar-19	01-Apr-19	-562																																																
Tunnel Flexible Pavement (EVB-related)																																																					
192260	VO - Pavement removal / reinstatement for water seepage (CH 5060 W/B)	10	14-Dec-18 A	25-Jan-19	-279																																																
192258	VO - Pavement removal / reinstatement for water seepage (CH 5026-5060 E/B)	15	17-Dec-18 A	02-Feb-19	-286																																																
Administration Building (ADB)																																																					
RC Structures (Portion Xa / Xb)																																																					
13484	ADB - Green Wall	35	01-Feb-19	20-Mar-19	-439																																																
External Works																																																					
13432	ADB - Road and drainage works (EVA)	42	11-Dec-17 A	24-Jan-19	-112																																																
13434	ADB - External concrete pavement (EVA)	24	18-Jan-18 A	28-Jan-19	-109																																																
Final Completion Works																																																					
13466	ADB - Completion of Section 1 (KD06)	0		31-Jan-19	-354																																																
Landscaping and Irrigation System																																																					
13588	ADB - Final completion test for irrigation systems in Portion Xa and Xb	60	18-Sep-18 A	31-Jan-19	-538																																																
13590	ADB - Landscape Works in Portion Xa and Xb	36	01-Feb-19	08-Mar-19	-538																																																
East Ventilation Shaft (EVS)																																																					
External Works																																																					
192228	VO 406 - External wall tiles (CT20) and construct SC2 and CT9	12	21-Jan-19*	02-Feb-19	-406																																																

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 59 (January 2019) THREE MONTH ROLLING

Project ID: H2613-U059
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U059
 Page 5 of 8

Date	Revision	Checked	Approv...
20-Dec-18	U058	AT	CW
20-Jan-19	U059	AT	CW

Data Date: 20-Jan-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018	2019				
							Jan	Feb	Mar	Apr	
External Works											
Rumsey Street Flyover for Pavement & Traffic Barrier											
DS09 Gantry											
192200	DS09 - Procurement and Manufacturing	13	13-Nov-18 A	29-Jan-19	-374						
192198	DS09 - Material delivery to site	6	30-Jan-19	04-Feb-19	-374						
192202	DS09 - Gantry construction	6	05-Feb-19	10-Feb-19	-374						
192204	DS09 - Direction sign installation (include T&C)	10	11-Feb-19	20-Feb-19	-374						
TCSS Sign ADS01											
192214	ADS01 - Lay RB/BC	2	19-Dec-18 A	20-Dec-18 A							
192216	ADS01 - Resurfacing PMFC/WC	2	21-Dec-18 A	22-Dec-18 A							
192218	ADS01 - Erect LCS fascia for ADS01	1	23-Dec-18 A	23-Dec-18 A							
192220	ADS01 - Road marking	1	24-Dec-18 A	24-Dec-18 A							
Tie-in Work and Temporary Arrangement at Connaught Road Elevated Road for CWB Commissioning											
5904e	RS - Install TCSS cable (including T&C)	5	03-Apr-19	09-Apr-19	-163						
Road Pavement Works											
5904f	Mill existing bitumen, clean and apply latex coating	9	21-Feb-19*	01-Mar-19	-204						
5904g	Erect formwork, dowel bar installation and pour concrete (4 bays)	7	28-Feb-19	07-Mar-19	-142						
5904u	Lay base course, cushion layer & modified friction course	3	08-Mar-19	11-Mar-19	-142						
5904w	Road marking and install road stud	3	12-Mar-19	14-Mar-19	-142						
Raising Existing Gully Pots (2 Double Gullies)											
5904h	Expose 2 pairs of gully pots	8	21-Feb-19	01-Mar-19	-134						
5904j	Erect formwork for raising gully pots & pour concrete	3	02-Mar-19	05-Mar-19	-134						
Central Divider Construction (Approx. 100 linear meter)											
5904k	Drill and fix rebar for backing wall	12	21-Feb-19	06-Mar-19	-163						

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 59 (January 2019) THREE MONTH ROLLING

Project ID: H2613-U059
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U059
 Page 6 of 8

Date	Revision	Checked	Approv...
20-Dec-18	U058	AT	CW
20-Jan-19	U059	AT	CW

Data Date: 20-Jan-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2019																
						2018			2019													
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec					
5904m	Install street light cable ducts (2 nos.) inside backing wall	10	25-Feb-19	07-Mar-19	-163																	
5904n	Install precast concrete profile barriers and backing walls (Night Shift)	21	26-Feb-19	21-Mar-19	-163																	
5904p	Lay TCSS ducts (3 nos.) and pour concrete for TCSS ducts	10	22-Mar-19	02-Apr-19	-163																	
Edge Parapet Construction (Approx. 28 linear meter)																						
5904t	Place precast concrete profile barriers (approx. 28 nos.)	2	12-Feb-19*	13-Feb-19	-130																	
5904q	Backing wall construction	6	14-Feb-19	20-Feb-19	-130																	
5904r	Concrete nosing construction	6	14-Feb-19	20-Feb-19	-129																	
Steel Parapet Installation (Approx. 80 linear meter)																						
5904x	Concrete plinth construction	7	14-Feb-19	21-Feb-19	-130																	
5904y	Install steel parapet and grout base plate (approx. 20 nos.)	6	22-Feb-19	28-Feb-19	-130																	
Road Widening (Bridge A / Man Po Street)																						
Construction / Installation Works																						
RW0042	Planter reinstatement (include RFV 474 Lanscape Works)	75	21-Jan-19	29-Apr-19	-177																	
Commissioning Test																						
Handover Tests																						
192112	Run-in test	14	21-Feb-19	06-Mar-19	-171																	
For Tunnel Opening																						
10016b	Ready for Tunnel opening	0		20-Feb-19	-374																	
10016b2	Anticipated tunnel opening	0		20-Feb-19	-218																	
APS Efficiency Test / TCSS Operability Test / Establishment																						
9920	TCSS - Operability Tests for TCSS	61	21-Feb-19	22-Apr-19	-218																	
9910a	APS - Arrangement of the Efficiency Test with TD and the tunnel operator	30	21-Feb-19	22-Mar-19	-218																	
9910b	APS - Record the APS efficiency	10	23-Mar-19	01-Apr-19	-218																	
9910c	APS - Preparation of the test results for ER approval	7	02-Apr-19	08-Apr-19	-218																	

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 59 (January 2019)

THREE MONTH ROLLING



Project ID: H2613-U059
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U059
 Page 7 of 8

Date	Revision	Checked	Approv...
20-Dec-18	U058	AT	CW
20-Jan-19	U059	AT	CW

Data Date: 20-Jan-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

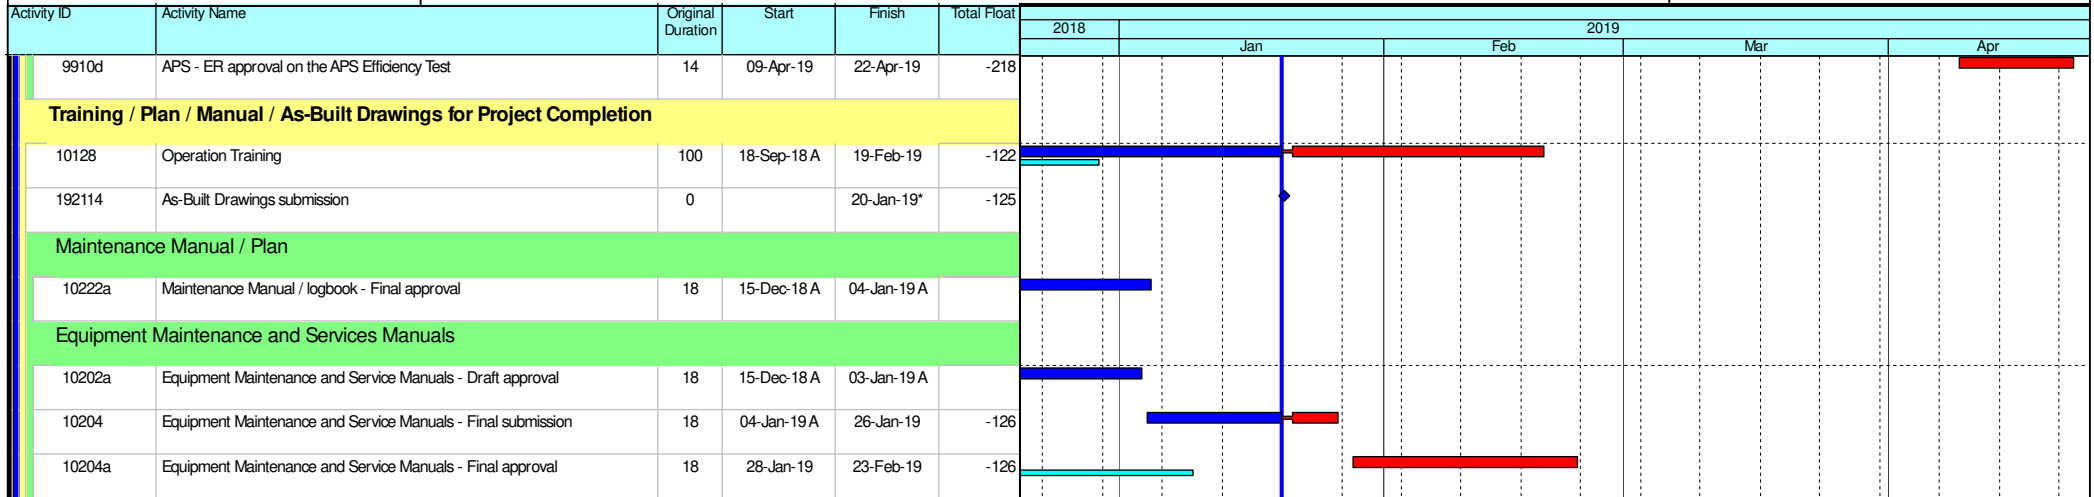

Leighton Contractors (Asia) Limited Programme Update 59 (January 2019) THREE MONTH ROLLING

Project ID: H2613-U059
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U059
 Page 8 of 8

Date	Revision	Checked	Approv...
20-Dec-18	U058	AT	CW
20-Jan-19	U059	AT	CW
