

Legend

Original Programme Period
 as in version date 11/12/18
 Extended Programme Period
 as in this version date 21/1/19

Create Date: 21/12/19
 Revised Date: 25/12/19
 28/12/19
 30/12/19
 1/2/2019

Remaining Works Programme

項目	工序	Jan-19													Feb-19													Mar-19													Apr-19														
		Week 54				Week 55				Week 56					Week 01				Week 02				Week 03					Week 04				Week 05				Week 06																			
		1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13										
1	Removal of Temporary Storage of Backfill material at Portion 5	Portion 5 運泥回填 WCR1 停止運泥因為Close P5 Exit															Portion 5 運泥回填 WCR1																																						
2	Seawall 海床	受泥區原海床															填泥													填泥													填泥												
3	地面墊仔及 100mm Subbase																																																						
4	舊直升機場, 海墘及梯台																舊直升機場Landing													清場													入機												
5	打D-Wall	打D-Wall 至+1.5 (-45M) 回填															打D-Wall remaining D-Wall 至+1.5 (15M) 回填																																						
6	U Channel & 沙井																北面東段4個catchpit+3000渠 (108m) DN8, 1, DN8, 2													北面東段3個catchpit+3000渠 DN8, 6													北面東段DN8, 3												
7	渠網及沙井																北面西段1個catchpit+300, 3750渠 (56m) DN1, 1													北面中段3000渠													北面中段3750 to												
8	IRRIGATION PIPE	subsoil drainage															subsoil drainage													subsoil drainage													subsoil drainage												
9	Fresh Water Main	TTA approved in TMLG Meeting 5/12/18																																																					
10	HRR 馬路	AREA ABCD remove PMSMA															AREA E remove and relay BC+PMSMA													AREA F remove and relay BC+PMSMA																									
10.1	HRR FLYOVER REMAINING WORK	V0258 MODIFICATION WORK AT ABUTMENT ROOM															V0253 PROVIDE STAINLESS STEEL LADDER AT ABUTMENT ROOM																																						
11	還原運泥街 Stage 0.5	EYA																																																					
12	博覽道東, WCR1 & WCR3 未完成工作	* Portion 2 Zone 1 清石渠 打石渠 軟formation															* Zone 2a upto end of EYA 打石渠 軟formation													* Portion 2 Zone 2b 打石渠 軟formation													* Zone 2a remaining area 打石渠												
		REMEDIATION TO EXPO DRIVE COVERED WALKWAY															WCR3 填 Sub Base (100mm thk 7000m ²)													Caisson seawall defects													resumption of a quality control point WCR1												
		海墘填海如下COPING (COMMENCEMENT DATE TO BE CONFIRMED)															WCR1&3 MAKE GOOD ARMOUR SLOPE PROFILE																																						

Wan Chai Development Phase II - East
Central - Wan Chai Bypass at Wan Chai
Contract: HK/2009/02
Remaining Works Programme

項目	工序	June																																			
		Week 18					Week 19					Week 20					Week 21					Week 22															
		27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
1	Removal of Temporary Storage of Backfill material at Portion 5																																				
2	Seawall 海床																																				
3	地面墊仔 100mm Subbase																																				
4	舊直升機塔, 海墜及梯台																																				
5	打D-Wall																																				
6	U Channel & 沙井																																				
7	渠網 & 沙井																																				
8	IRRIGATION PIPE																																				
9	Fresh Water Main																																				
10	HHR 馬路																																				
10.1	HHR FLYOVER REMAINING WORK																																				
11	還原運盛街 Stage 0.5																																				
12	博覽道東, VCR1 & VCR3 未完成工作																																				

CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West

Activity ID		Activity Name		Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019							
								Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
HK/2012/08 Revised Works Programme Rev.12.0(DD 20 November 2017)																											
Key Dates and Milestone Dates																											
Sections of Works Completion (Included Not Granted EOT Entitlement of The Contractor)																											
KD10840	Completion of Section IIIA	0			08-Sep-18*	0%																					
KD10860	Completion of Section IV	0			30-Aug-18*	0%																					
KD10880	Completion of Section V	0			26-Sep-18*	0%																					
KD11010	Completion of Section VII	0			14-Sep-18*	0%																					
KD11020	Completion of Section VIII	0			21-Sep-18*	0%																					
KD11040	Completion of Section IX	0			21-Sep-19*	0%																					
KD11060	Completion of Section X	0			21-Sep-18*	0%																					
Planned Sections of Works Completion																											
KD10080	Planned Section IIIA Completion - Road A2,A4, A5	0			08-Sep-18	0%																					
KD10100	Planned Section IV Completion - Slip Road 3	0			30-Aug-18	0%																					
KD10140	Planned Section V Completion - Remaining At-Grade Road	0			26-Sep-18	0%																					
KD10280	Planned Section VII Completion - Remainder Works	0			14-Sep-18	0%																					
KD10300	Planned Section VIII Completion - Landscape Softwork	0			21-Sep-18	0%																					
KD10320	Planned Section IX Completion - Establishment Works	0			21-Sep-19	0%																					
KD10340	Planned Section X Completion - Tree Protection & Preservation	0			21-Sep-18	0%																					
Dredging and Reclamation																											
Marine Work Construction																											
Zone CRIII																											
Seawall Construction - Zone CRIII																											
Zone CRIII Seawall- 2nd Stage																											
Seawall 2 & 12																											
MAR21371	Zone CRIII - seawall 2 & 12 - Backfilling remaining portion (type A, geotextile and filter)	0			19-Jan-18 A	27-Jan-18 A	100%																				
Zone D																											
Seawall Construction - Zone D																											
Seawall 10 & 11																											
MAR20630	Zone D - Seawall 10 & 11: Install remaining seawall block	14			20-Feb-18*	05-Mar-18	0%																				
MAR20650	Zone D - Seawall 10 & 11: Backfill Type A	7			06-Mar-18	12-Mar-18	0%																				
MAR20670	Zone D - Seawall 10 & 11: Lay geotextile and filter	7			13-Mar-18	19-Mar-18	0%																				
Works for Section Completion																											
Construction																											
Section III A - Road A2, A4 & A5																											
Roadwork & Utilities - Section 1 (L1806 - L1801)																											

Data Date: 20-Feb-18


- ◆ Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Remaining Level of Effort

Updated Works Programme Rev.12
(Ref. to Rev.12 as of 20 February 2018)


Date	Revision	Checked	Approved
20-Feb-18	12		

**CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019											
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
Promenade Seawall Parapet Construction & EVA																													
SVII12000	Sec VII - Precast parapet	67	18-Nov-17 A	14-May-18	0%																								
SVII12010	Sec VII - Zone CRIII - seawall parapet: Backfilling	14	20-Feb-18	07-Mar-18	0%																								
SVII12120	Sec VII - Zone CRIII - seawall parapet: Construct mass concrete coping	30	08-Mar-18	16-Apr-18	0%																								
SVII12122	Sec VII - Zone CRIII - seawall parapet: reinforced concret coping	17	17-Apr-18	07-May-18	0%																								
SVII12140	Sec VII - Zone CRIII - seawall parapet: construct seawall parapet	30	08-May-18	12-Jun-18	0%																								
SVII12160	Sec VII - CRIII - EVA: watermain	14	13-Jun-18	29-Jun-18	0%																								
SVII12180	Sec VII - CRIII - EVA: U-channel	14	30-Jun-18	17-Jul-18	0%																								
SVII12200	Sec VII - CRIII - EVA: bituminous layer	5	18-Jul-18	23-Jul-18	0%																								
SVII12220	Sec VII - CRIII - EVA: paving block	30	24-Jul-18	27-Aug-18	0%																								
SVII13120	Sec VII - Zone A1, A2 & B - seawall parapet: Construct mass concrete coping	14	28-Dec-17 A	07-Mar-18	68.18%																								
SVII13122	Sec VII - Zone A1, A2 & B - seawall parapet: reinforced concrete coping	18	08-Mar-18	28-Mar-18	0%																								
SVII13140	Sec VII - Zone A1, A2 & B - seawall parapet: Construct seawall parapet	30	09-Apr-18	14-May-18	0%																								
SVII13160	Sec VII - Zone A1, A2 & B - EVA: watermain	14	15-May-18	31-May-18	0%																								
SVII13180	Sec VII - Zone A1, A2 & B - EVA: U-channel	14	01-Jun-18	16-Jun-18	0%																								
SVII13182	Sec VII - Zone A1, A2 & B - EVA: bituminous layer	5	19-Jun-18	23-Jun-18	0%																								
SVII13184	Sec VII - Zone A1, A2 & B - EVA: paving block	30	25-Jun-18	30-Jul-18	0%																								
SVII13200	Sec VII - Zone D - seawall parapet: Remove temporary seawall block	21	07-Mar-18	03-Apr-18	0%																								
SVII13220	Sec VII - Zone D - seawall parapet: Construct mass concrete	30	04-Apr-18	10-May-18	0%																								
SVII13222	Sec VII - Zone D - seawall parapet: reinforced concrete coping	18	11-May-18	01-Jun-18	0%																								
SVII13240	Sec VII - Zone D - seawall parapet: Construct seawall parapet	25	02-Jun-18	03-Jul-18	0%																								
SVII13260	Sec VII - Zone D - EVA : watermain	14	04-Jul-18	19-Jul-18	0%																								
SVII13280	Sec VII - Zone D - EVA : U-channel	14	20-Jul-18	04-Aug-18	0%																								
SVII13300	Sec VII - Zone D - EVA : bituminous layer	5	06-Aug-18	10-Aug-18	0%																								
SVII13320	Sec VII - Zone D - EVA : paving block	30	11-Aug-18	14-Sep-18	0%																								
Promenade Footpath																													
Section 1																													
SVII10440	Sec VII - section 1 footpath - drainage works : connection pipe & U-channel	10	24-May-18	04-Jun-18	0%																								
SVII10445	Sec VII - section 1 footpath - watermain	7	05-Jun-18	12-Jun-18	0%																								
SVII10460	Sec VII - section 1 footpath - lighting	7	13-Jun-18	21-Jun-18	0%																								
SVII10500	Sec VII - section 1 footpath - paving block	21	22-Jun-18	17-Jul-18	0%																								
Section 2																													
SVII12610	Sec VII - section 2 footpath - drainage works : L2202 - L2203A	20	20-Feb-18	14-Mar-18	0%																								
SVII12615	Sec VII - section 2 footpath - watermain	7	15-Mar-18	22-Mar-18	0%																								
SVII12630	Sec VII - section 2 footpath - utilities: TCSS	21	23-Mar-18	20-Apr-18	0%																								
SVII12670	Sec VII - section 2 footpath - paving block	30	21-Apr-18	28-May-18	0%																								
Section 3																													
SVII12850	Sec VII - section 3 footpath - watermain	17	20-Feb-18	10-Mar-18	0%																								
SVII12870	Sec VII - section 3 footpath - utilities (HEC, TCSS, HGC, PCCW)	40	12-Mar-18	02-May-18	0%																								
SVII12875	Sec VII - 3 footpath - drainage works :U chanel	14	03-May-18	18-May-18	0%																								

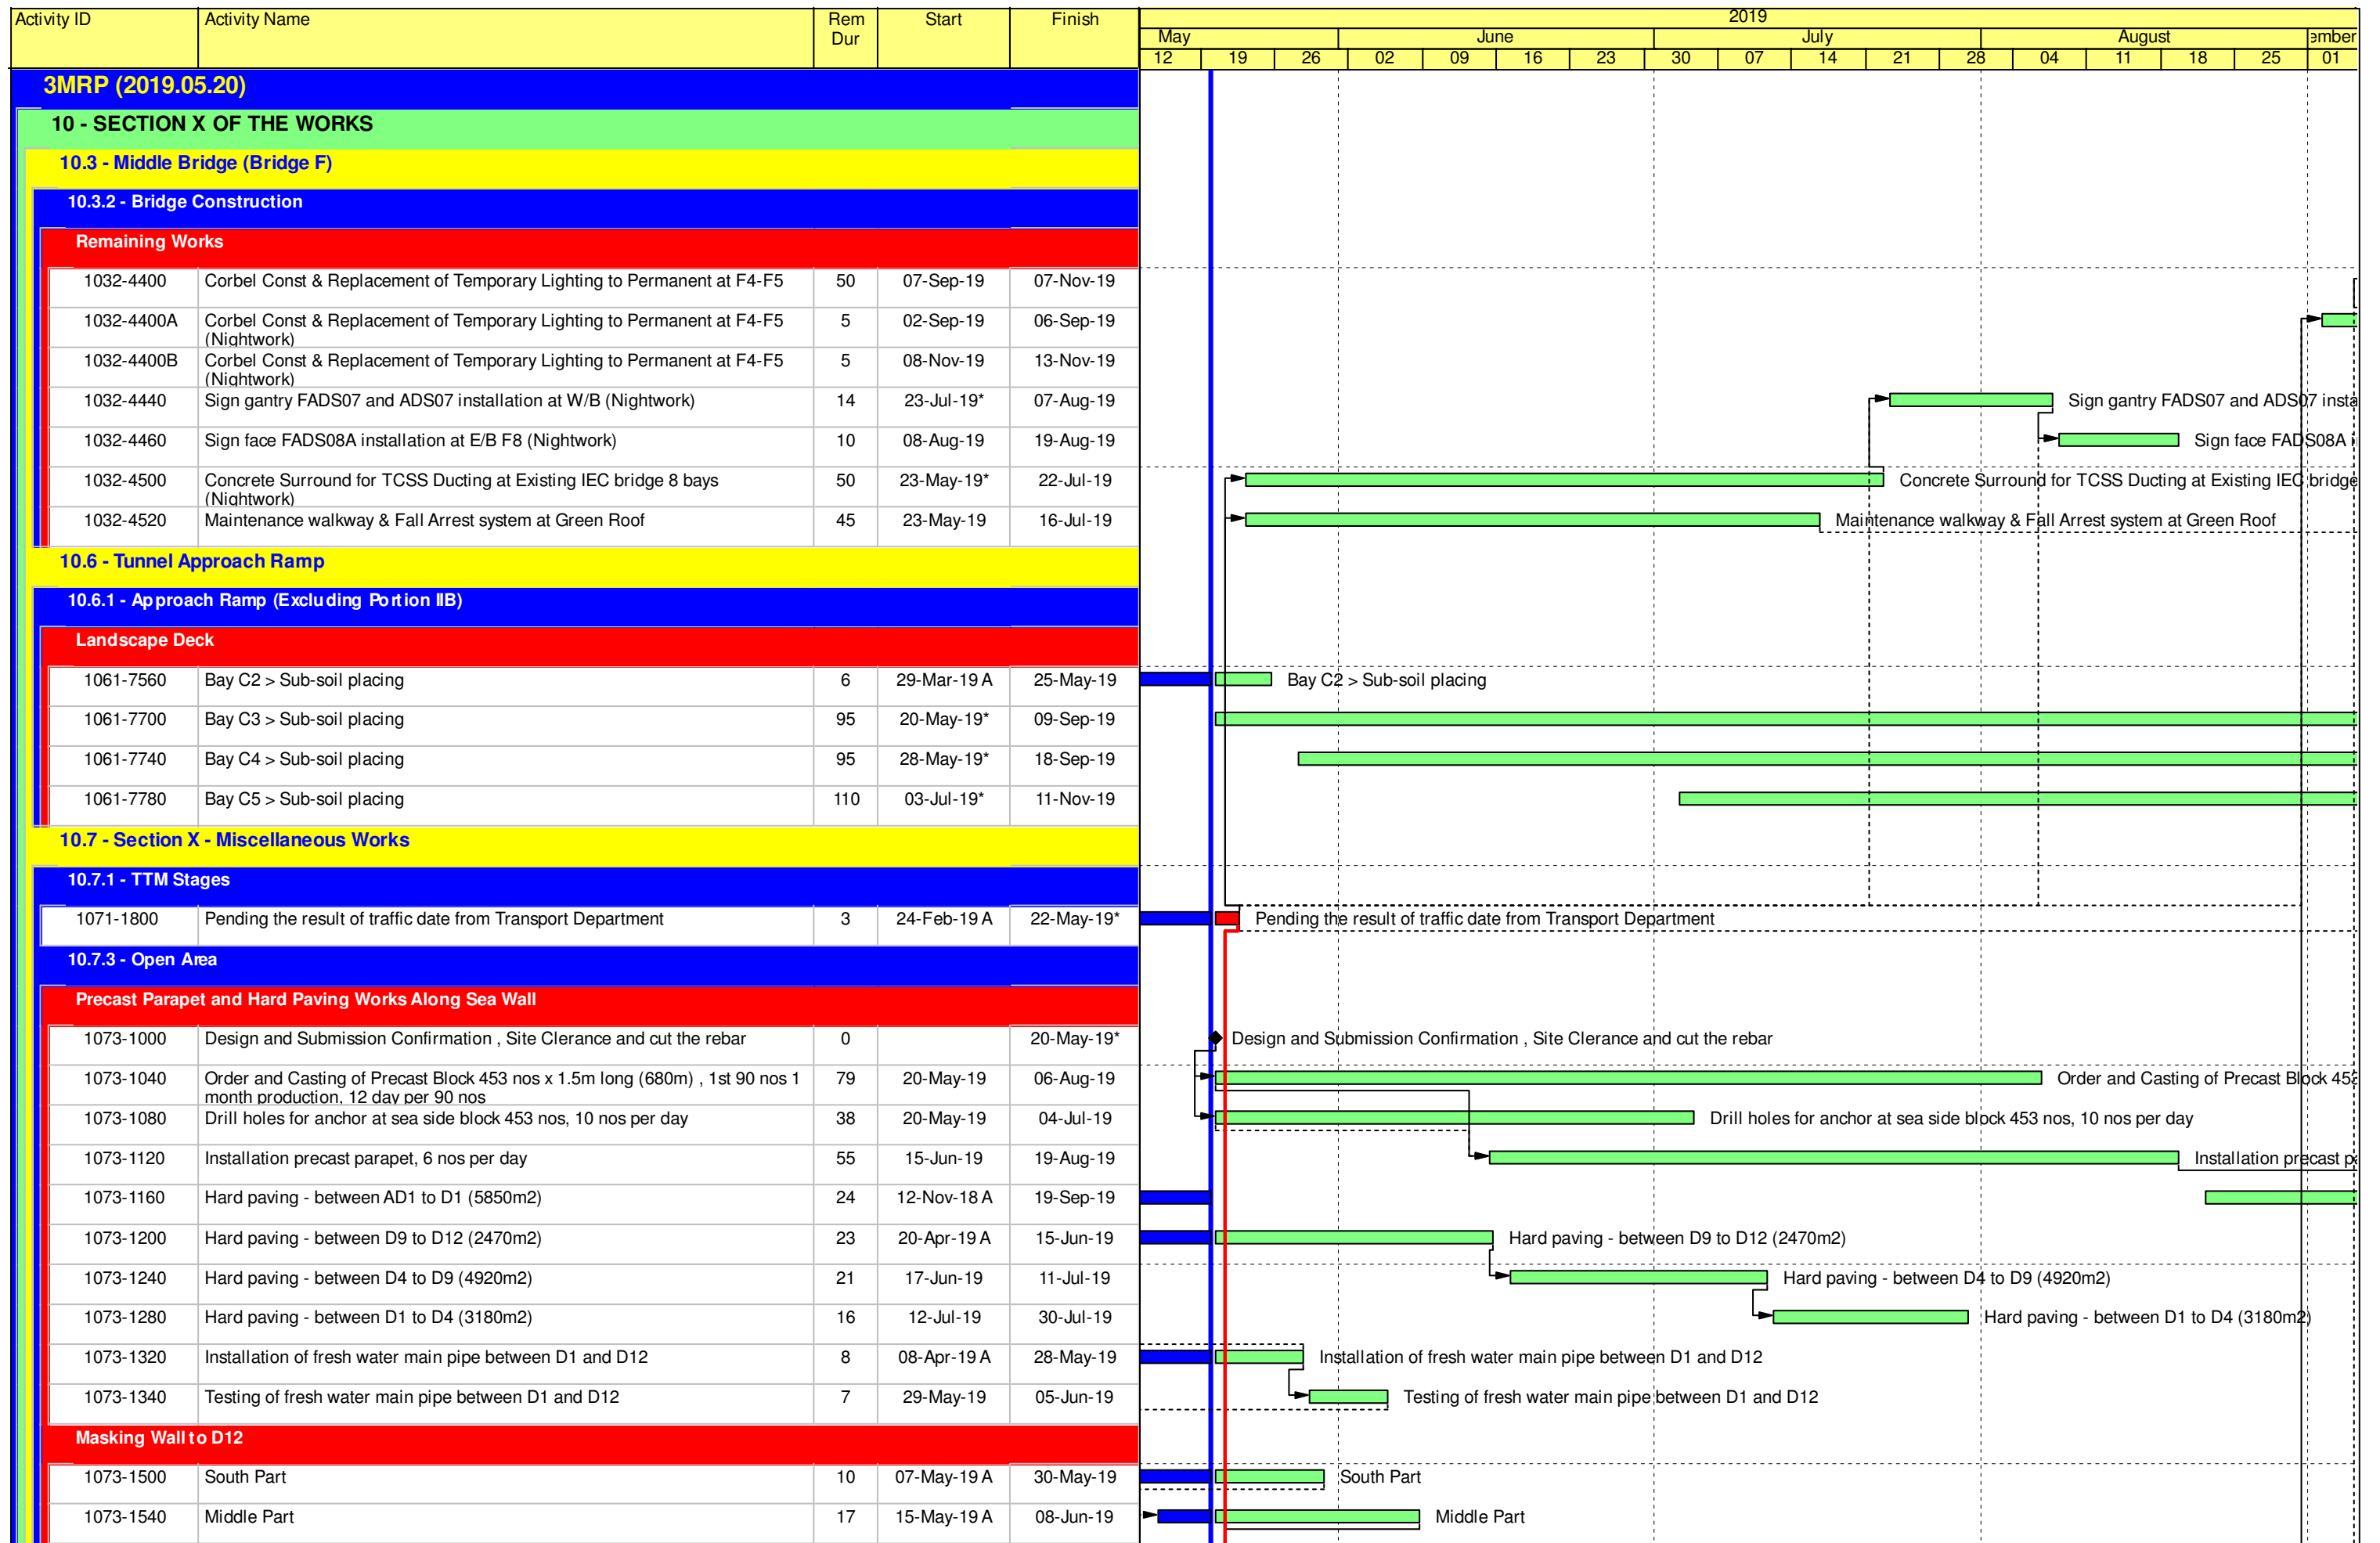


Contract HY/2009/19
Three Months Rolling Programme (20.May.2019 to 20.Aug.2019)

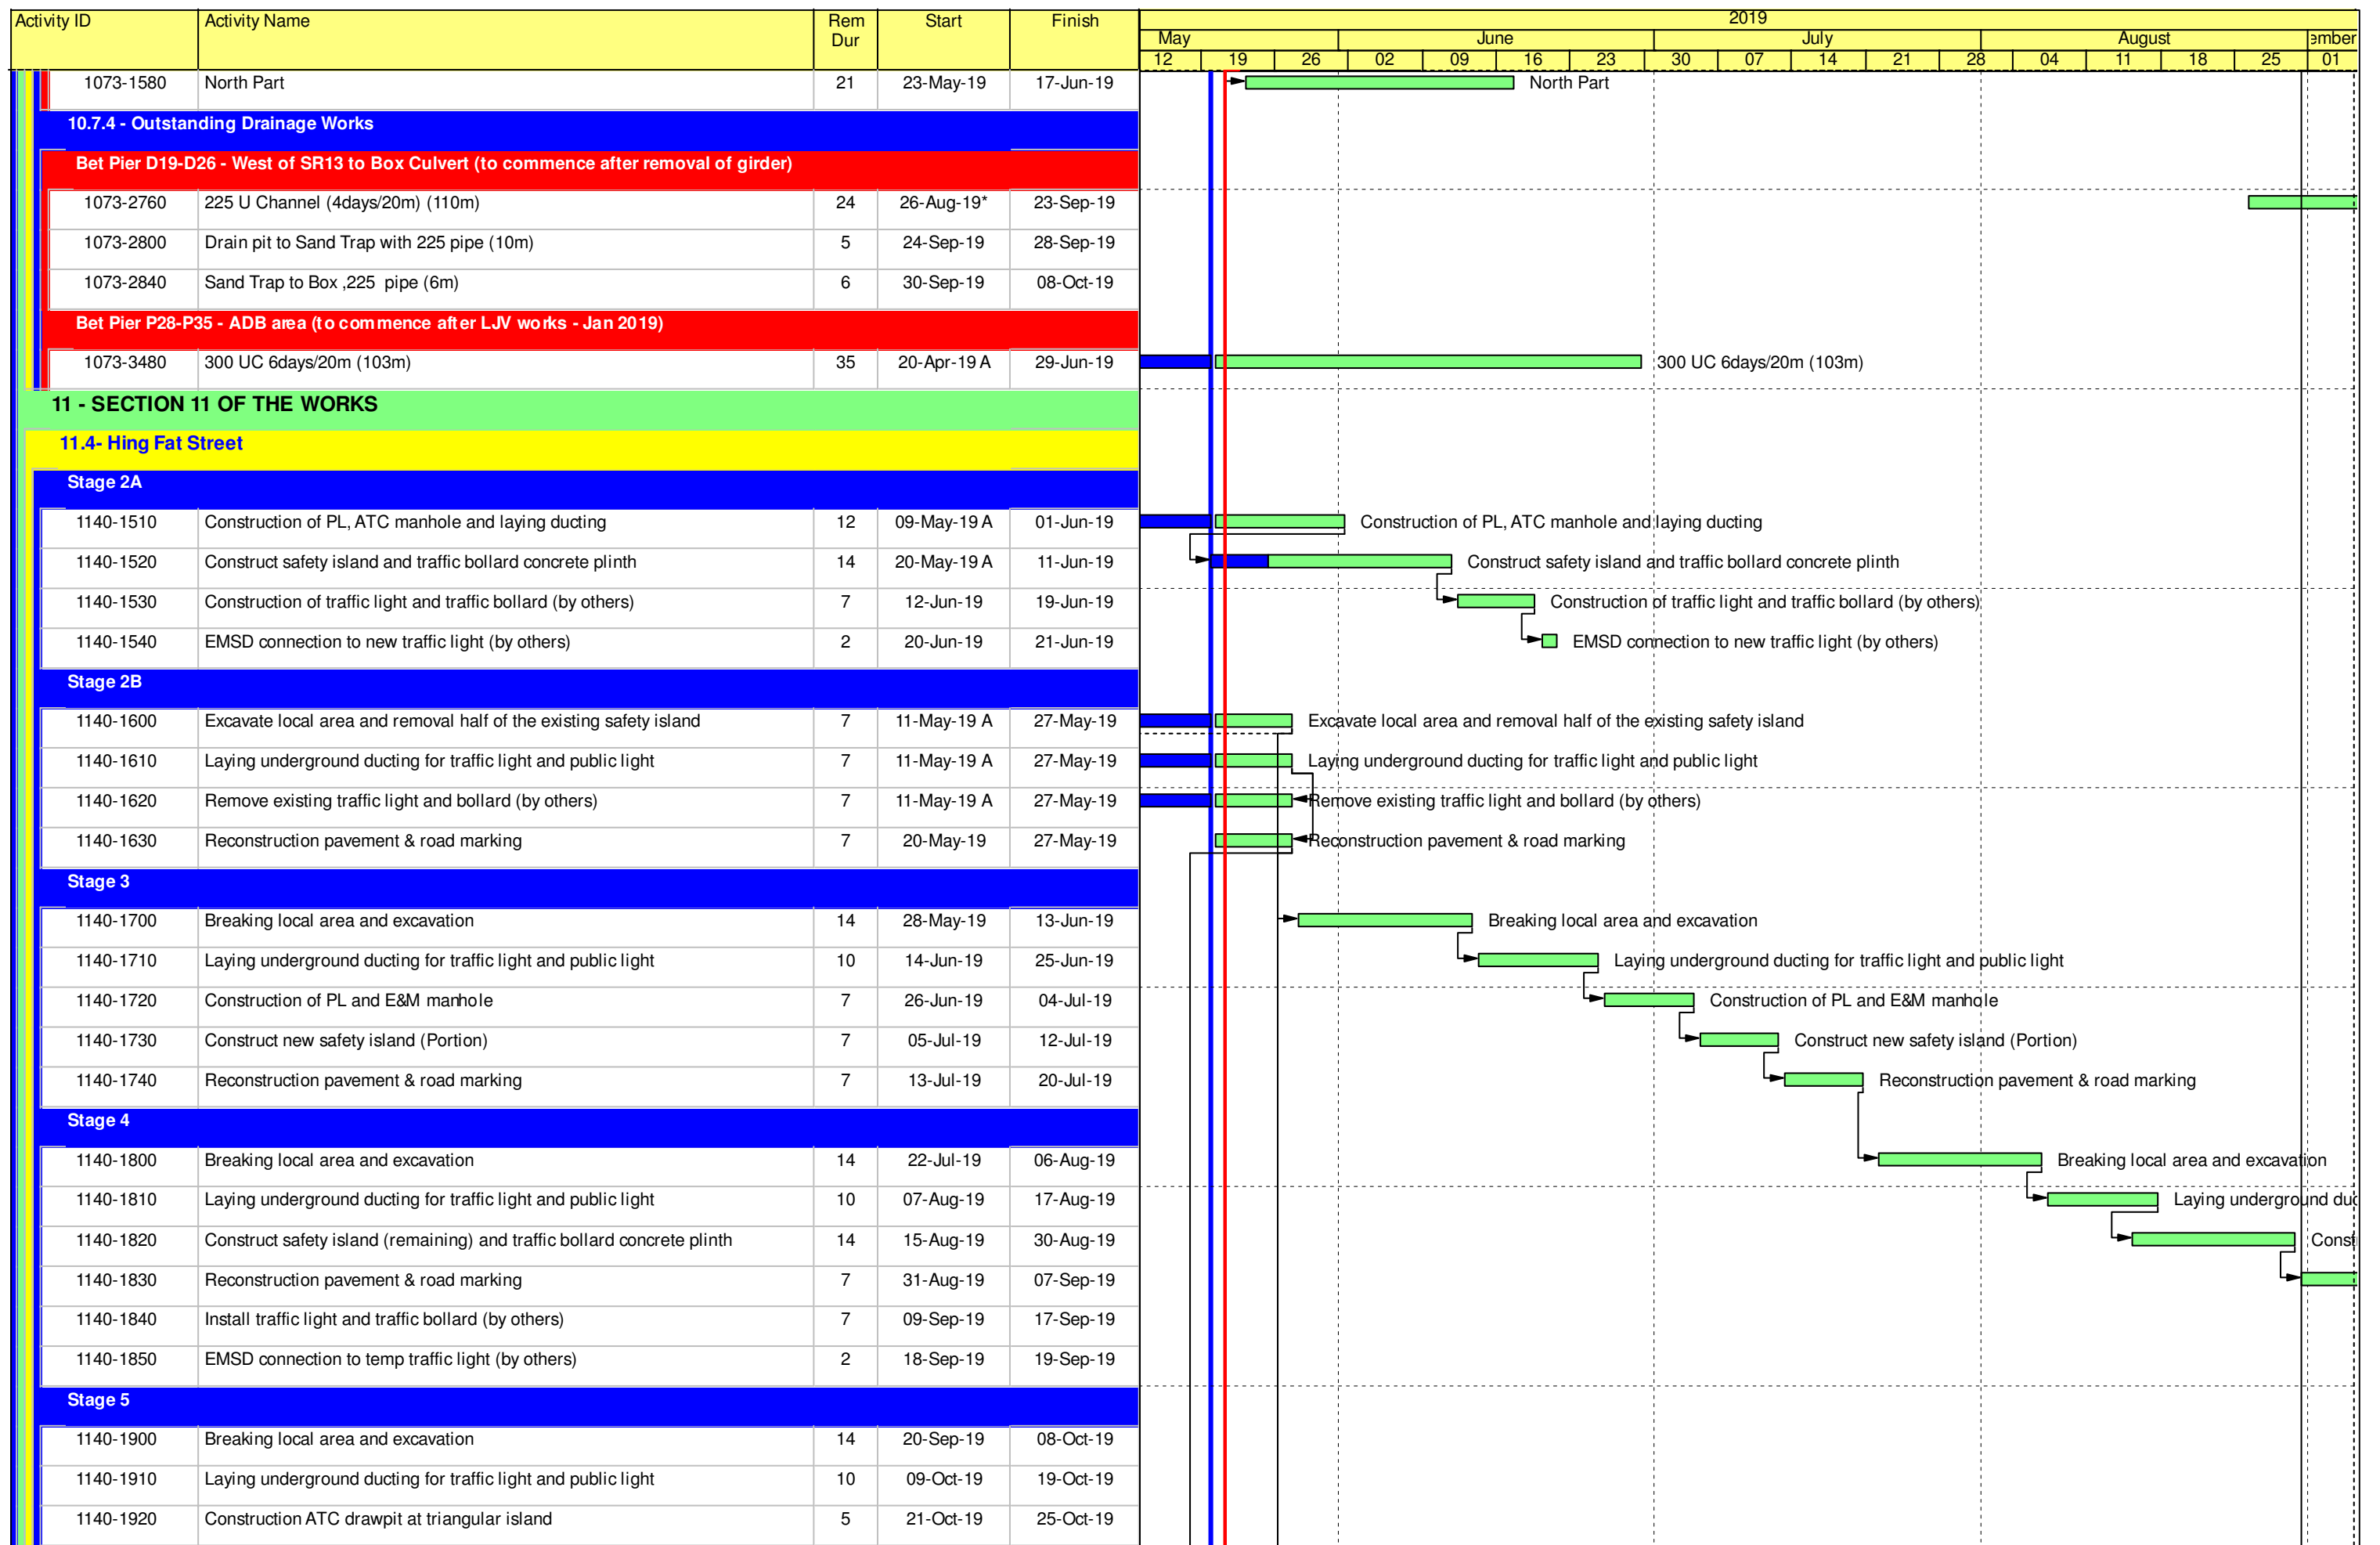


█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.May.2019 to 20.Aug.2019)

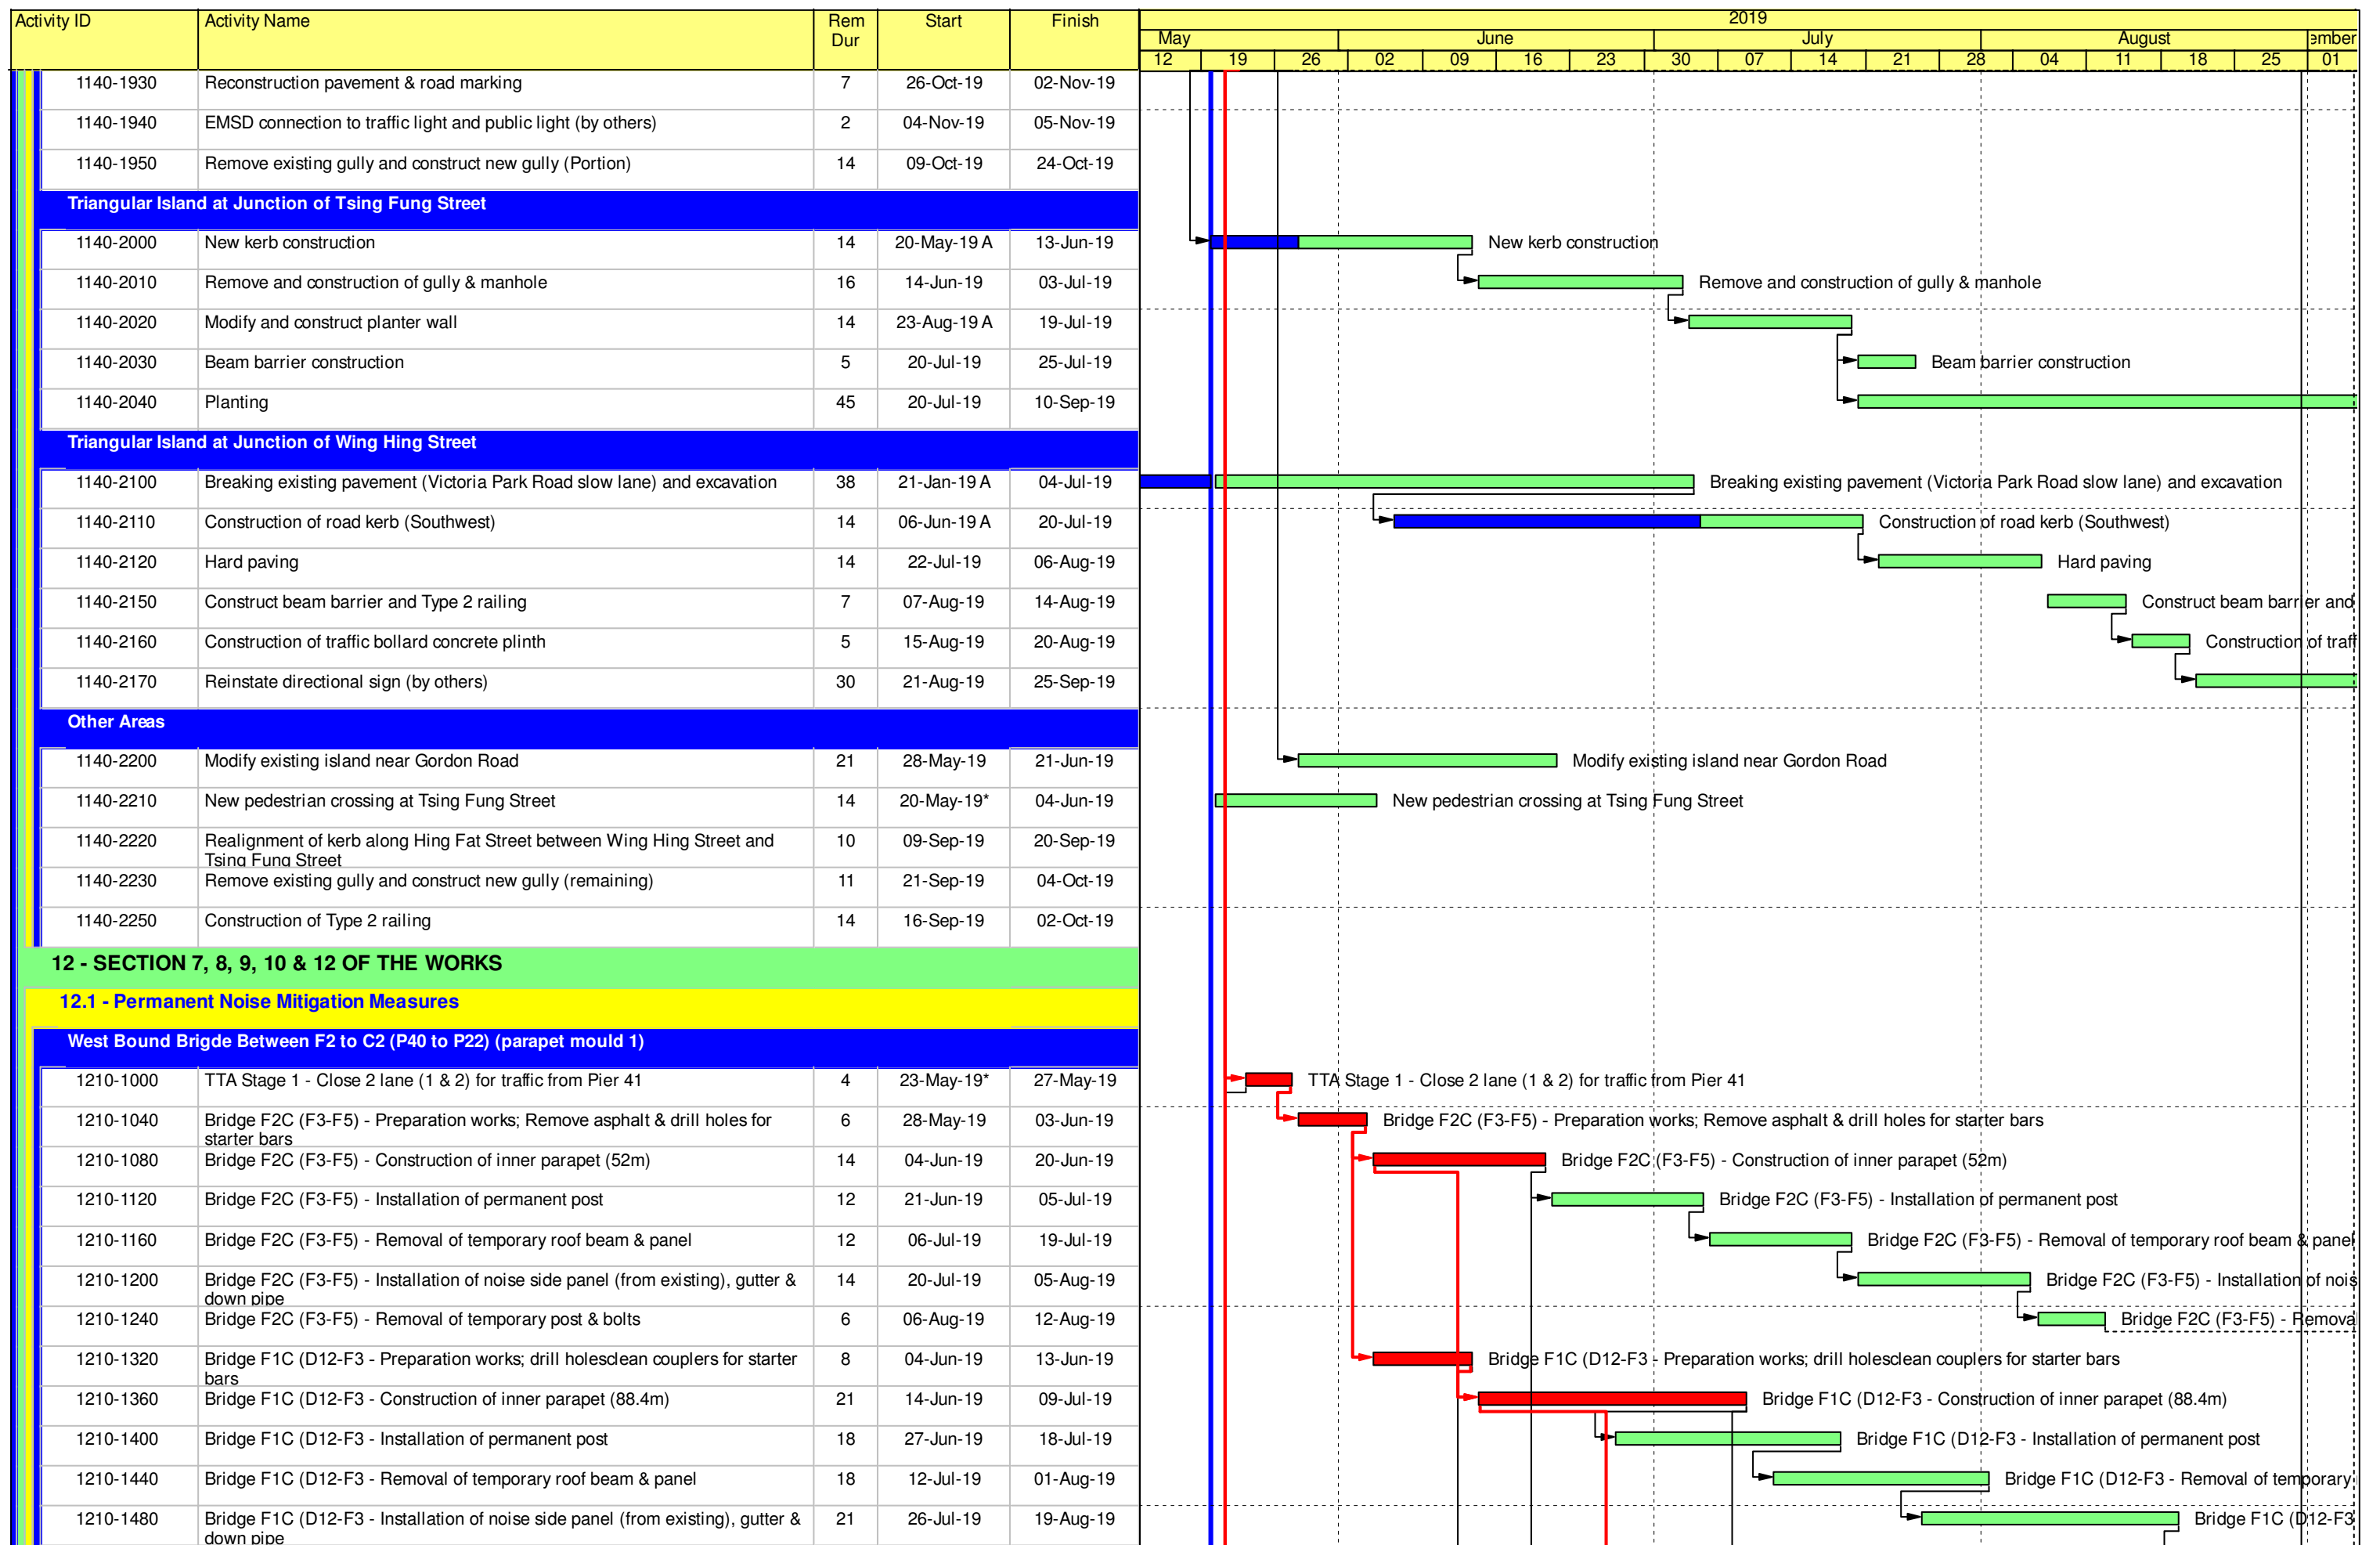


Contract HY/2009/19
Three Months Rolling Programme (20.May.2019 to 20.Aug.2019)

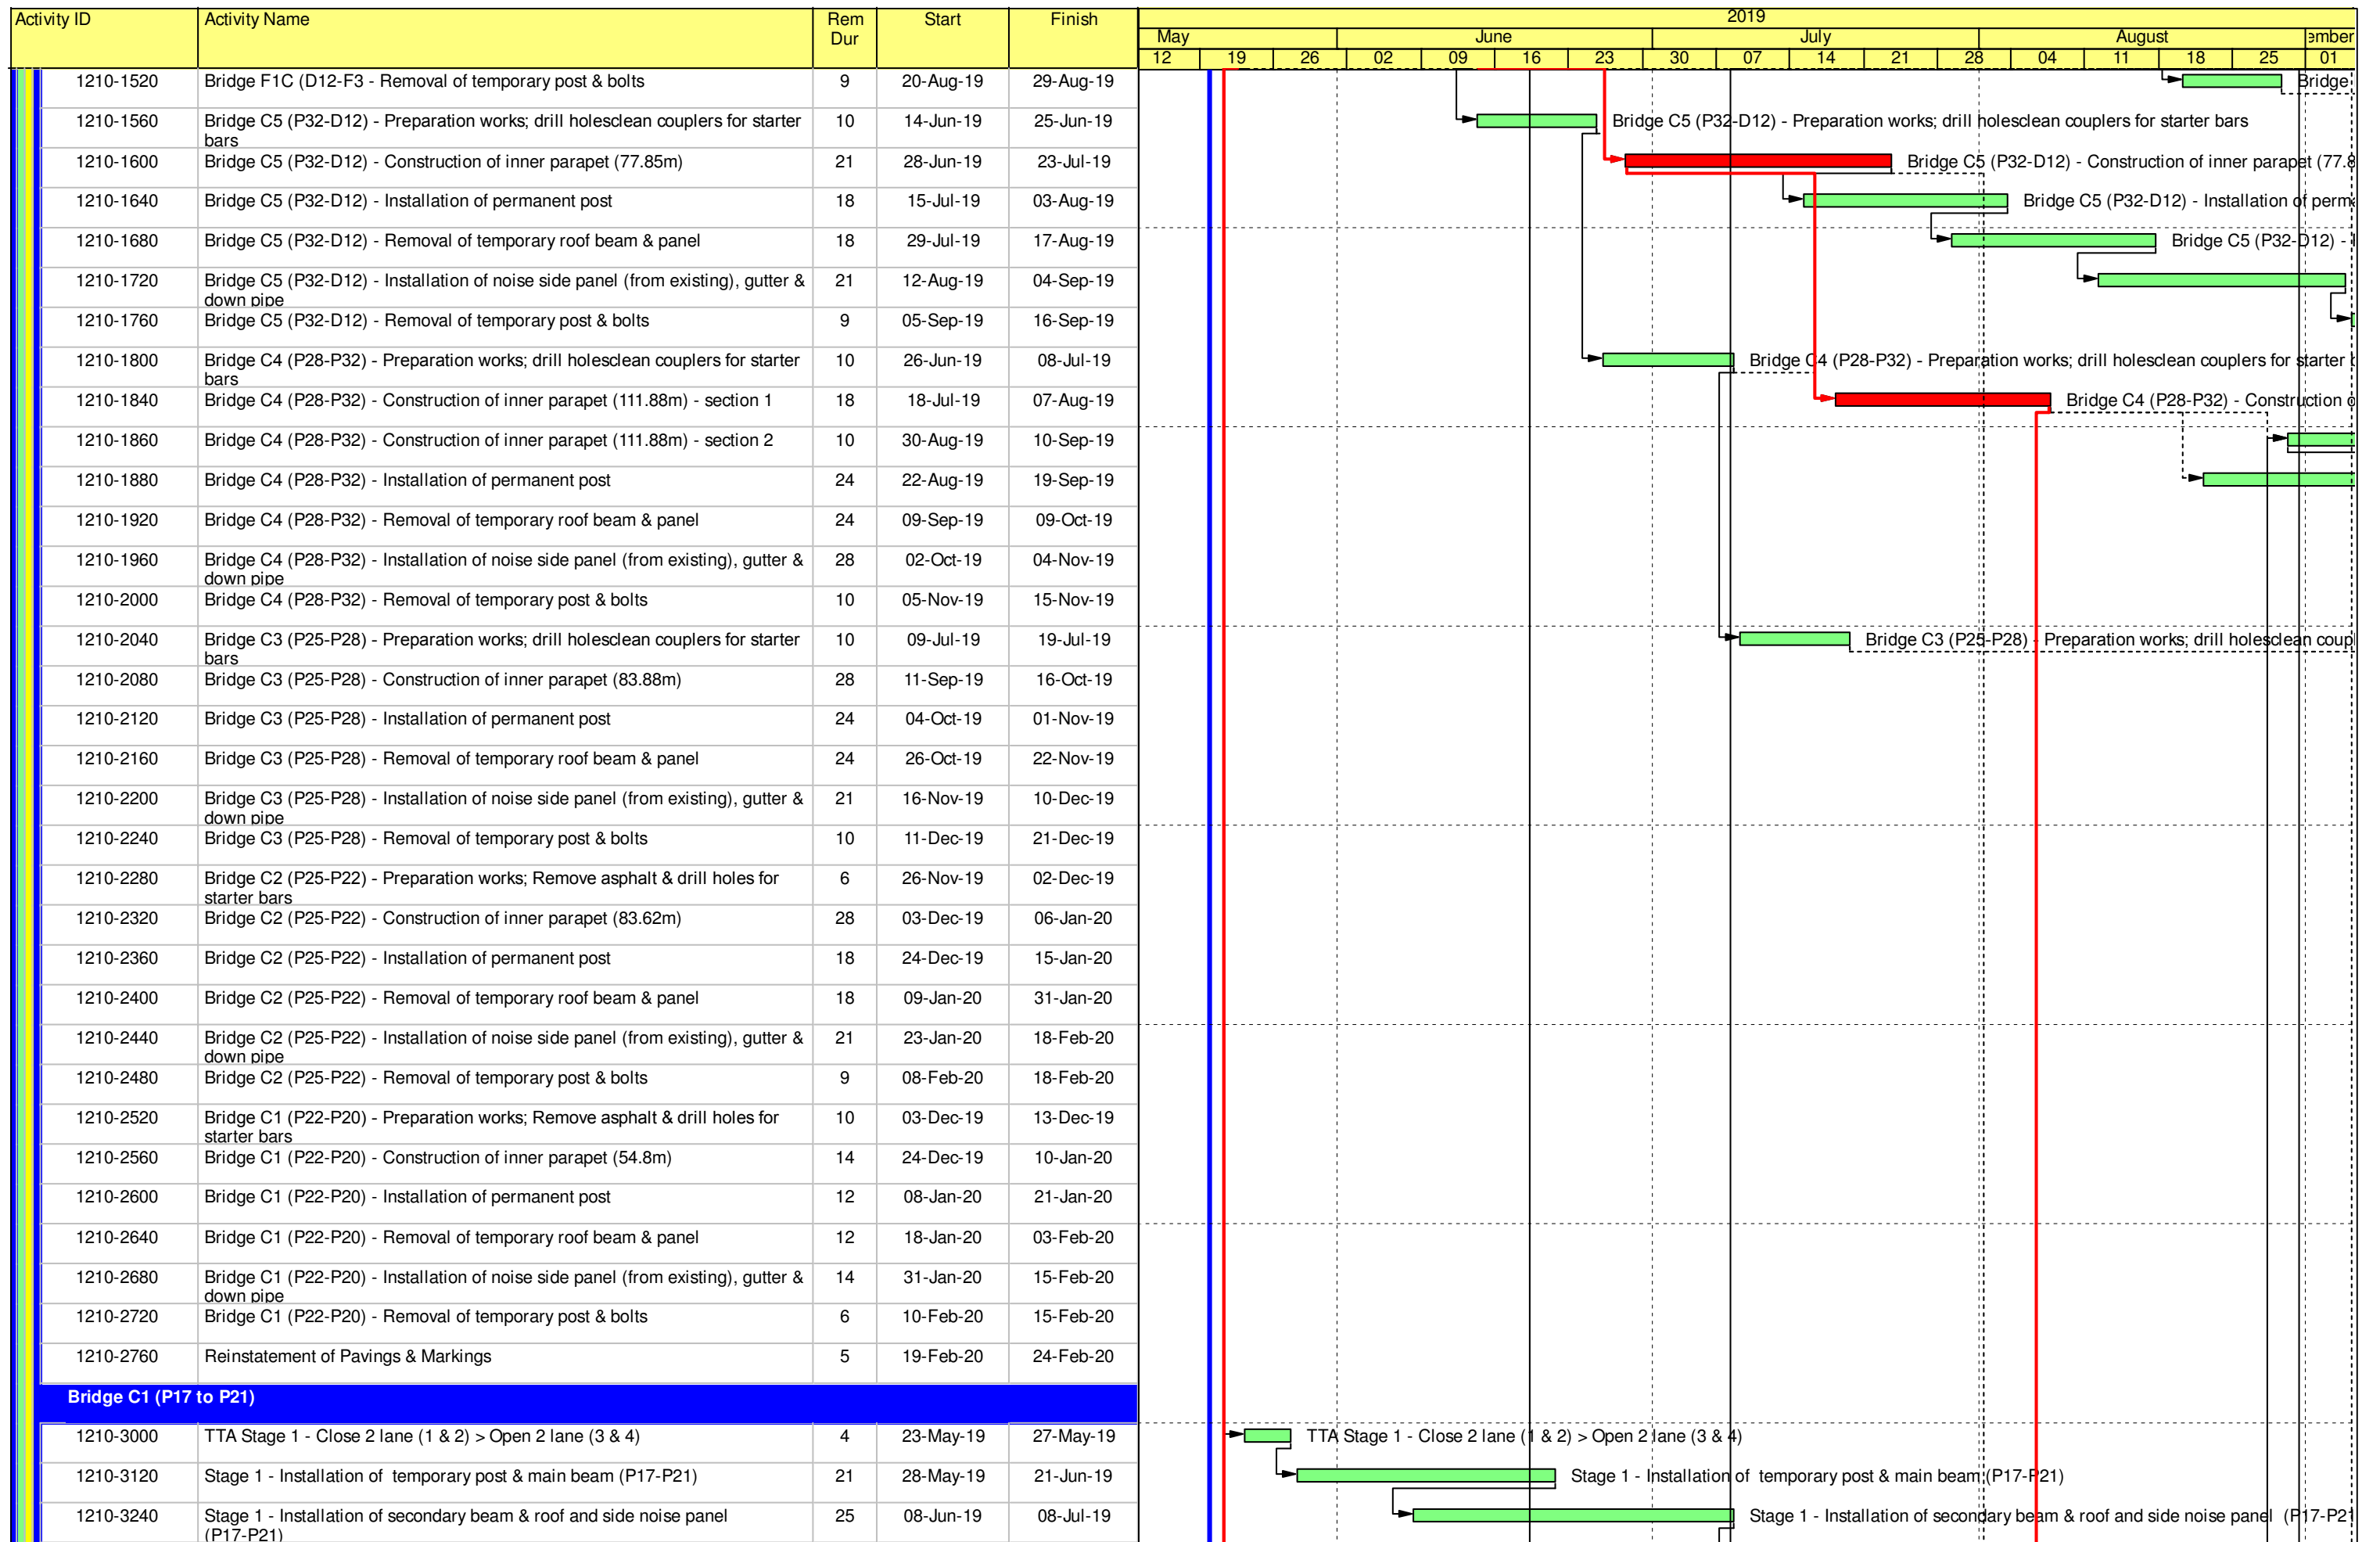


- █ Remaining Level of Effort
- █ Actual Level of Effort
- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work
- ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.May.2019 to 20.Aug.2019)

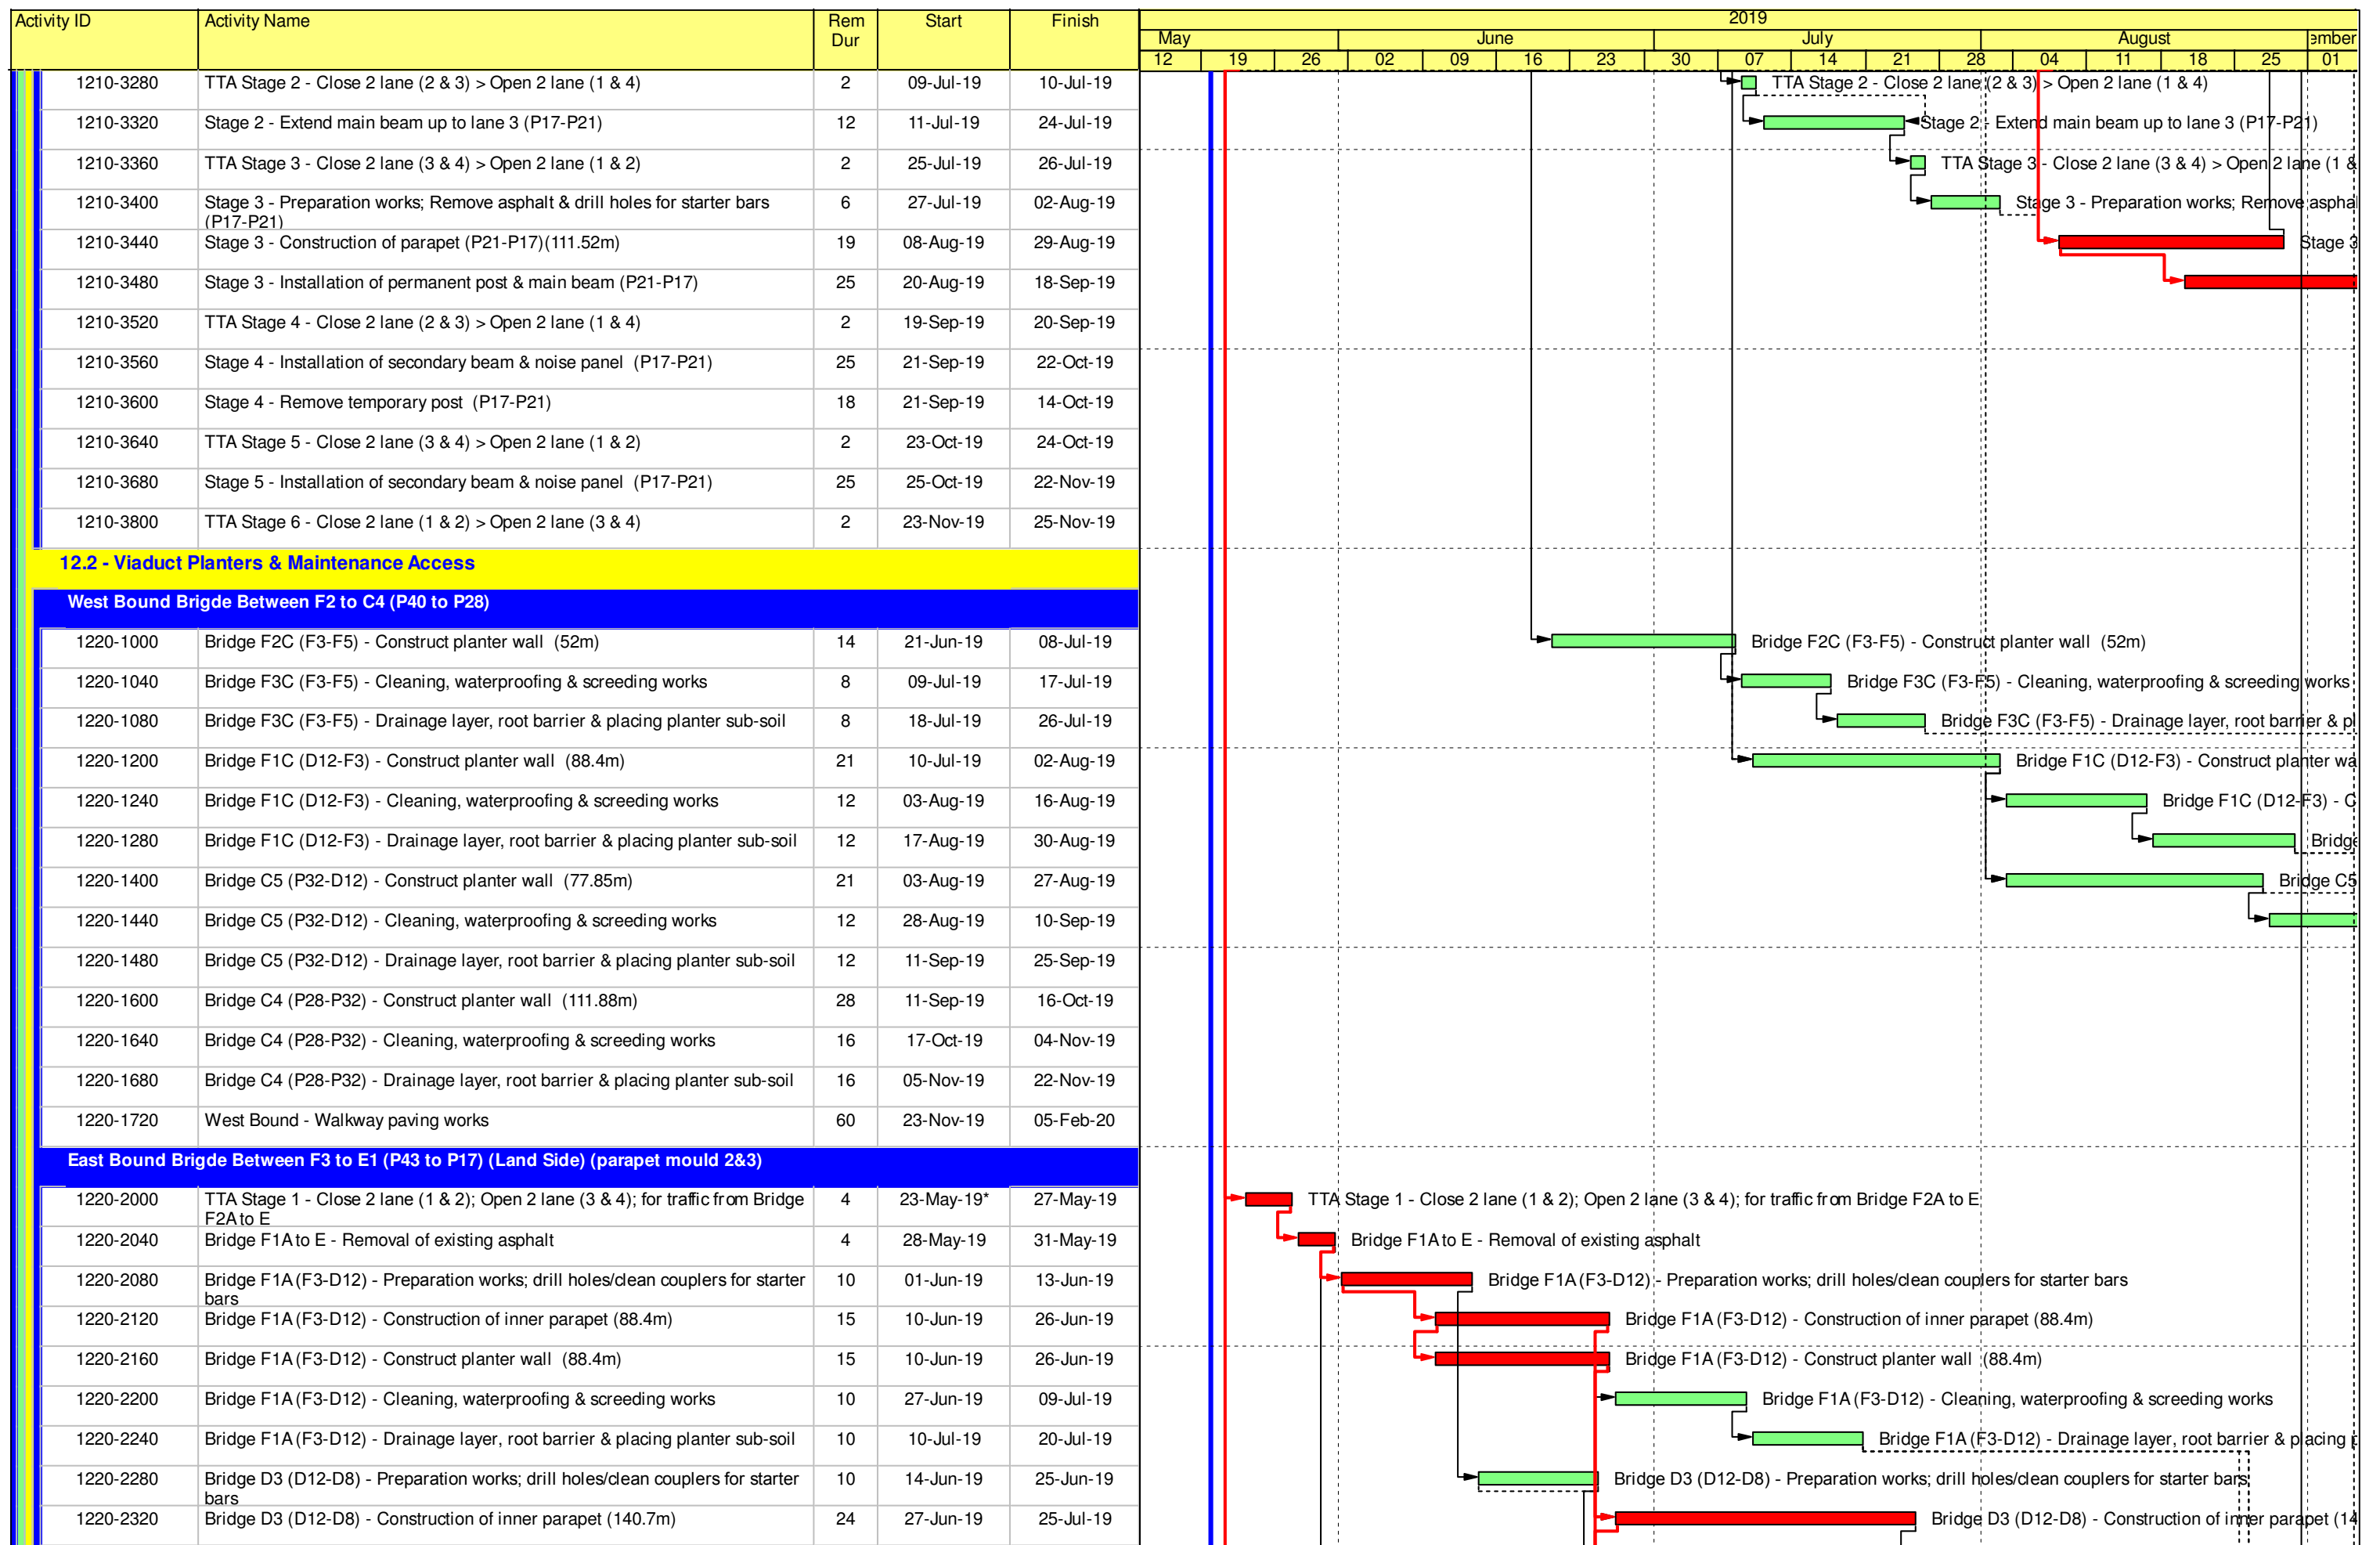

Contract HY/2009/19
Three Months Rolling Programme (20.May.2019 to 20.Aug.2019)

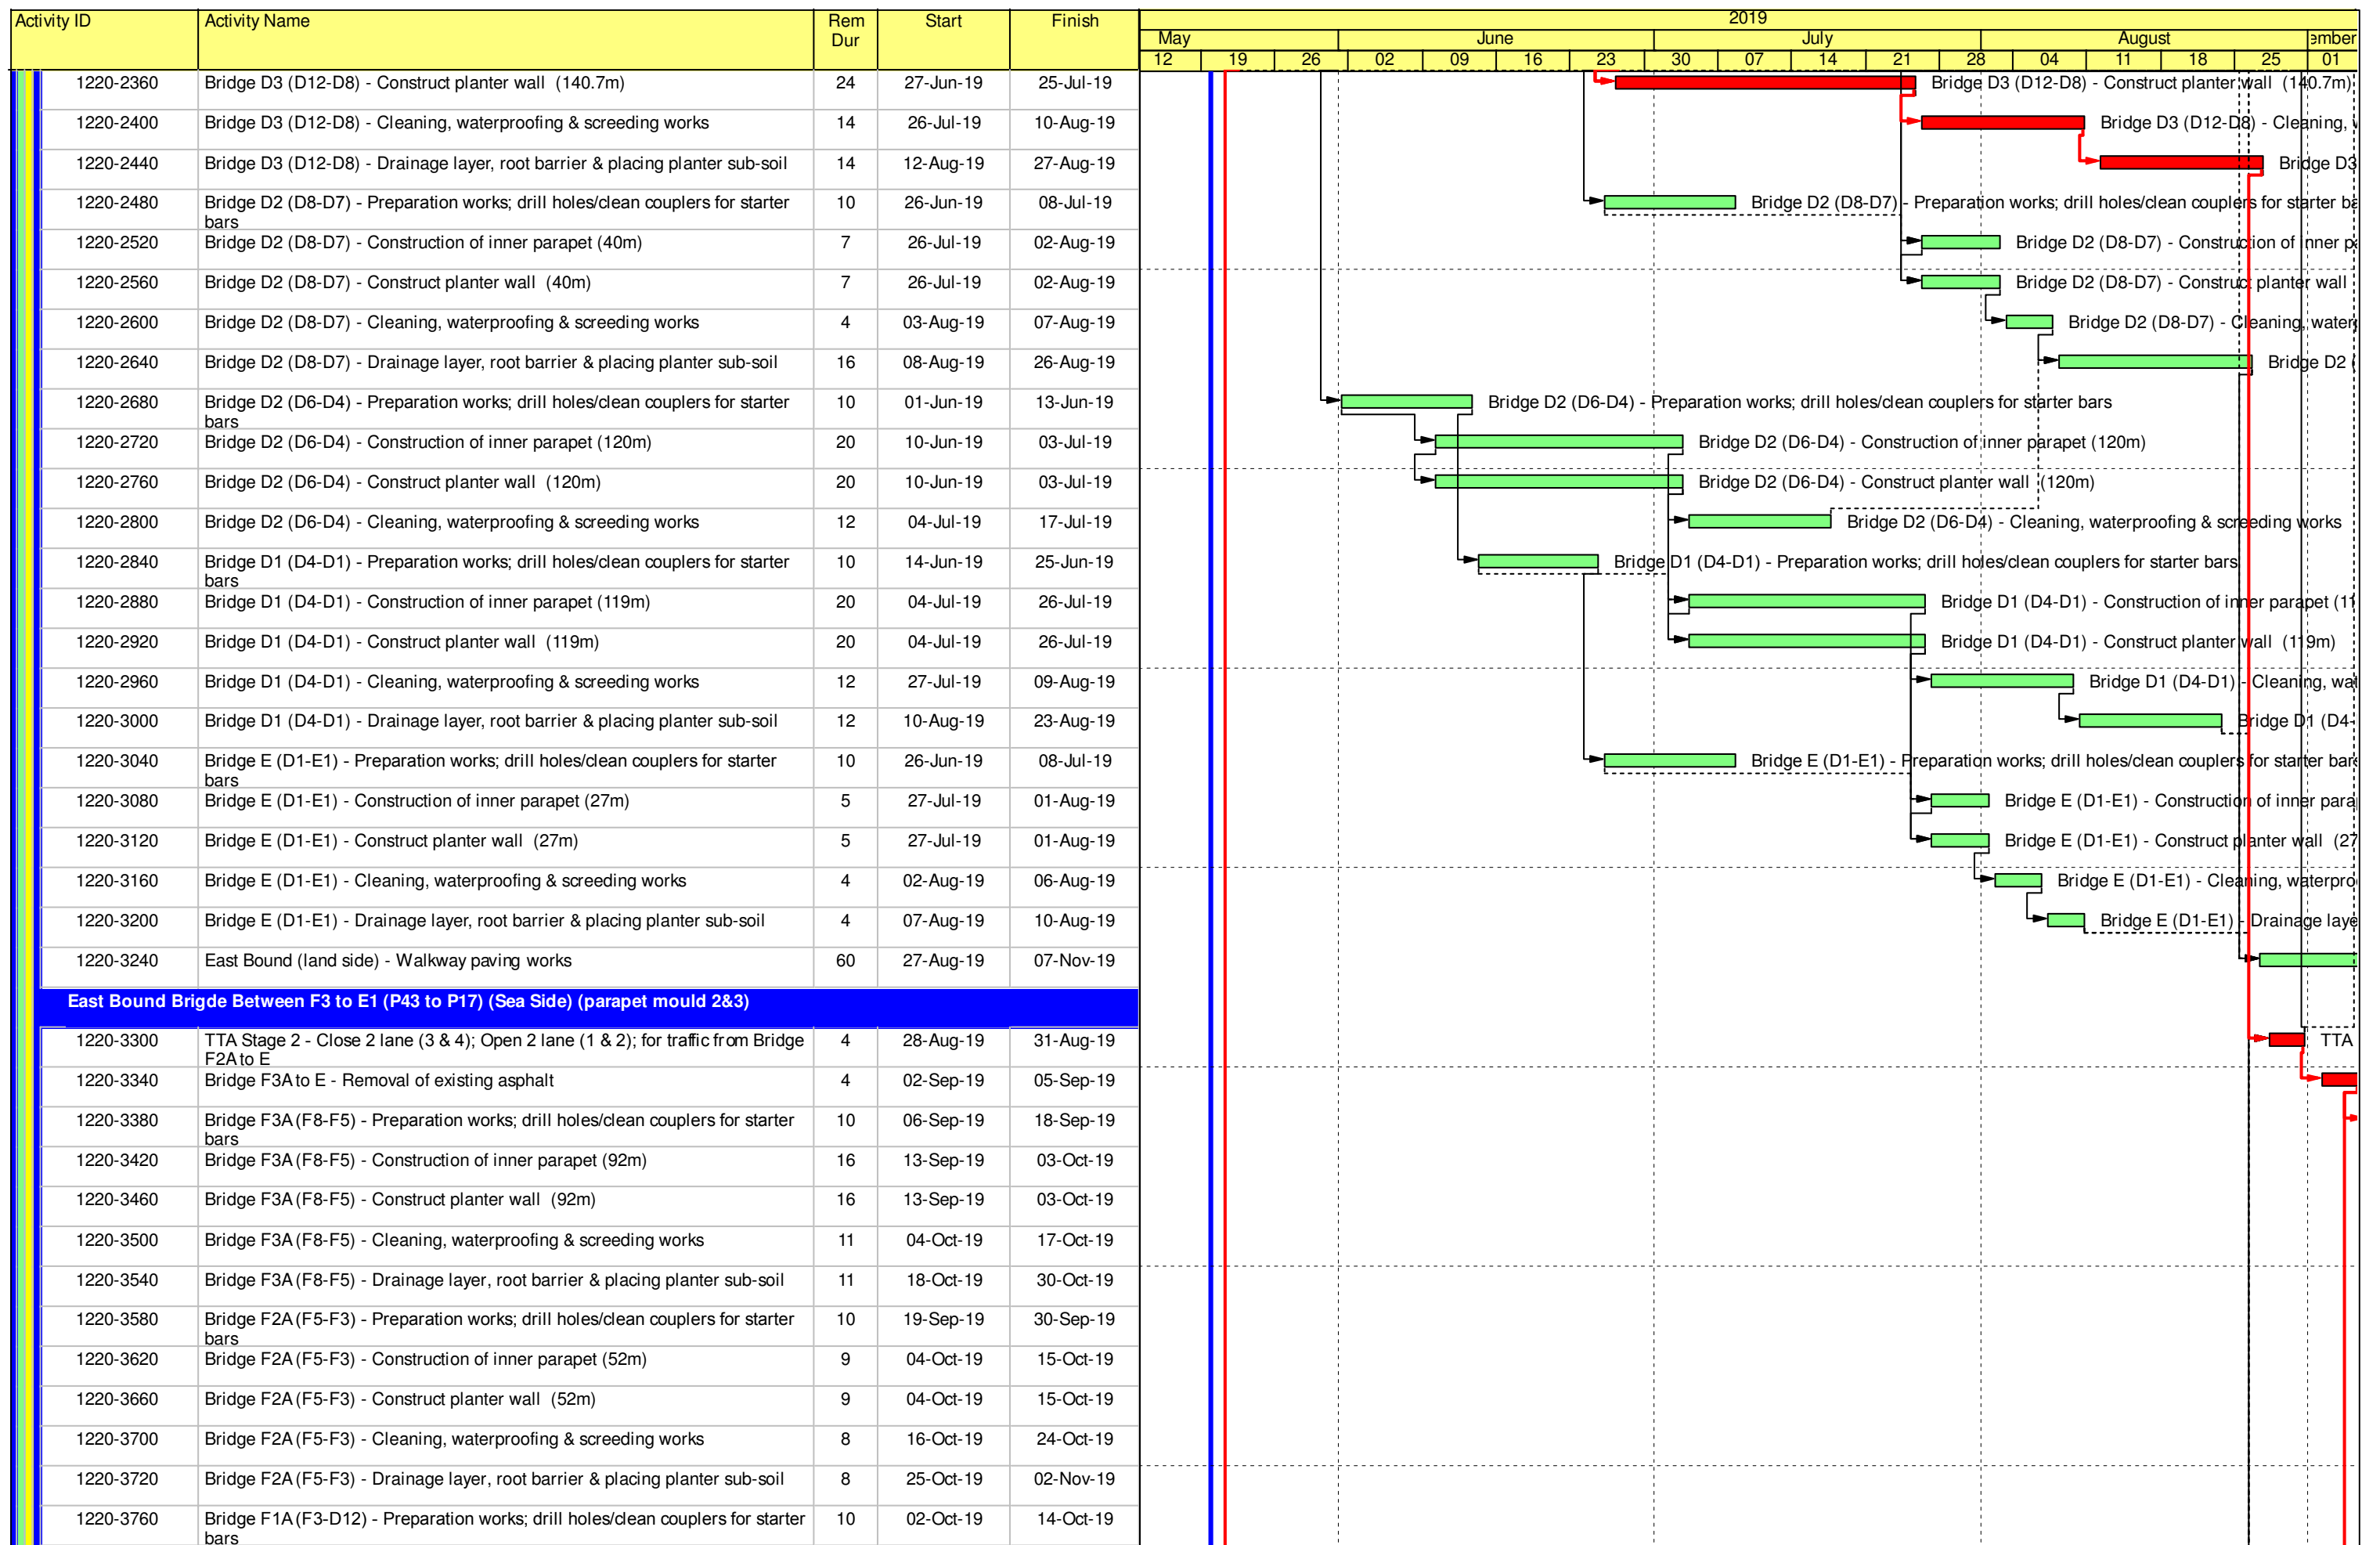


█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.May.2019 to 20.Aug.2019)

Activity ID	Activity Name	Rem Dur	Start	Finish	2019																
					May			June				July				August				September	
					12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	01
1220-3800	Bridge F1A (F3-D12) - Construction of inner parapet (88.4m)	15	16-Oct-19	01-Nov-19																	
1220-3840	Bridge F1A (F3-D12) - Construct planter wall (88.4m)	15	16-Oct-19	01-Nov-19																	
1220-3880	Bridge F1A (F3-D12) - Cleaning, waterproofing & screeding works	10	02-Nov-19	13-Nov-19																	
1220-3920	Bridge F1A (F3-D12) - Drainage layer, root barrier & placing planter sub-soil	10	14-Nov-19	25-Nov-19																	
1220-4020	Bridge D3 (D12-D8) - Preparation works; drill holes/clean couplers for starter bars	10	15-Oct-19	25-Oct-19																	
1220-4060	Bridge D3 (D12-D8) - Construction of inner parapet (140.65m)	24	02-Nov-19	29-Nov-19																	
1220-4100	Bridge D3 (D12-D8) - Construct planter wall (140.65m)	24	02-Nov-19	29-Nov-19																	
1220-4140	Bridge D3 (D12-D8) - Cleaning, waterproofing & screeding works	15	30-Nov-19	17-Dec-19																	
1220-4180	Bridge D3 (D12-D8) - Drainage layer, root barrier & placing planter sub-soil	15	18-Dec-19	06-Jan-20																	
1220-4220	Bridge D2 (D8-D4) - Preparation works; drill holes/clean couplers for starter bars	10	06-Sep-19	18-Sep-19																	
1220-4260	Bridge D2 (D8-D4) - Construction of inner parapet (160m)	28	13-Sep-19	18-Oct-19																	
1220-4300	Bridge D2 (D8-D4) - Construct planter wall (160m)	28	13-Sep-19	18-Oct-19																	
1220-4340	Bridge D2 (D8-D4) - Cleaning, waterproofing & screeding works	16	19-Oct-19	06-Nov-19																	
1220-4380	Bridge D2 (D8-D4) - Drainage layer, root barrier & placing planter sub-soil	16	07-Nov-19	25-Nov-19																	
1220-4420	Bridge D1 (D4-D1) - Preparation works; drill holes/clean couplers for starter bars	10	19-Sep-19	30-Sep-19																	
1220-4460	Bridge D1 (D4-D1) - Construction of inner parapet (119m)	20	19-Oct-19	11-Nov-19																	
1220-4500	Bridge D1 (D4-D1) - Construct planter wall (119m)	20	19-Oct-19	11-Nov-19																	
1220-4540	Bridge D1 (D4-D1) - Cleaning, waterproofing & screeding works	9	12-Nov-19	21-Nov-19																	
1220-4600	Bridge D1 (D4-D1) - Drainage layer, root barrier & placing planter sub-soil	9	22-Nov-19	02-Dec-19																	
1220-4640	Bridge E (D1-E3) - Preparation works; drill holes/clean couplers for starter bars	10	02-Oct-19	14-Oct-19																	
1220-4680	Bridge E (D1-E3) - Construction of inner parapet (77m)	14	12-Nov-19	27-Nov-19																	
1220-4720	Bridge E (D1-E3) - Construct planter wall (77m)	14	12-Nov-19	27-Nov-19																	
1220-4760	Bridge E (D1-E3) - Cleaning, waterproofing & screeding works	12	28-Nov-19	11-Dec-19																	
1220-4800	Bridge E (D1-E3) - Drainage layer, root barrier & placing planter sub-soil	12	12-Dec-19	26-Dec-19																	
1220-4840	East Bound (sea side) - Walkway paving works	60	12-Dec-19	24-Feb-20																	
12.3 - Waterworks																					
1230-1000	Irrigation System - Landscape Deck (C1 to C2)	116	20-May-19	05-Oct-19																	
1230-1010	Irrigation System - Landscape Deck (C3 to C5) & Green Roof	123	10-Sep-19	07-Feb-20																	
1230-1200	Irrigation System (Landscape Deck C1 to C2) - Testing	7	08-Oct-19	15-Oct-19																	
1230-1210	Irrigation System (Landscape Deck C3 to C5 & Green Roof) - Testing	7	08-Feb-20	15-Feb-20																	
1230-1300	Connect to watermain for Water Supply (Landscape Deck C1 to C2) - Works carried out by WSD	7	16-Oct-19	23-Oct-19																	
1230-1310	Connect to watermain for Water Supply (Landscape Deck C3 to C5 & Green Roof) - Works carried out by WSD	7	17-Feb-20	24-Feb-20																	
1230-1500	Irrigation System - Bridge W/B - at III, IVA, VA, X	90	26-Sep-19	13-Jan-20																	
1230-1600	Irrigation System - Bridge E/B (land side) - at IA, III, VI, VIIA	90	28-Aug-19	13-Dec-19																	
1230-1650	Irrigation System - Bridge E/B (sea side) - at IA, III, VI, VIIA	90	30-Oct-19	15-Feb-20																	
1230-1700	Irrigation System (E/B & W/B Bridge) - Testing	7	17-Feb-20	24-Feb-20																	
1230-1800	Connect to watermain for Water Supply (E/B & W/B Bridge) - Works carried out by WSD	7	25-Feb-20	03-Mar-20																	

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.May.2019 to 20.Aug.2019)

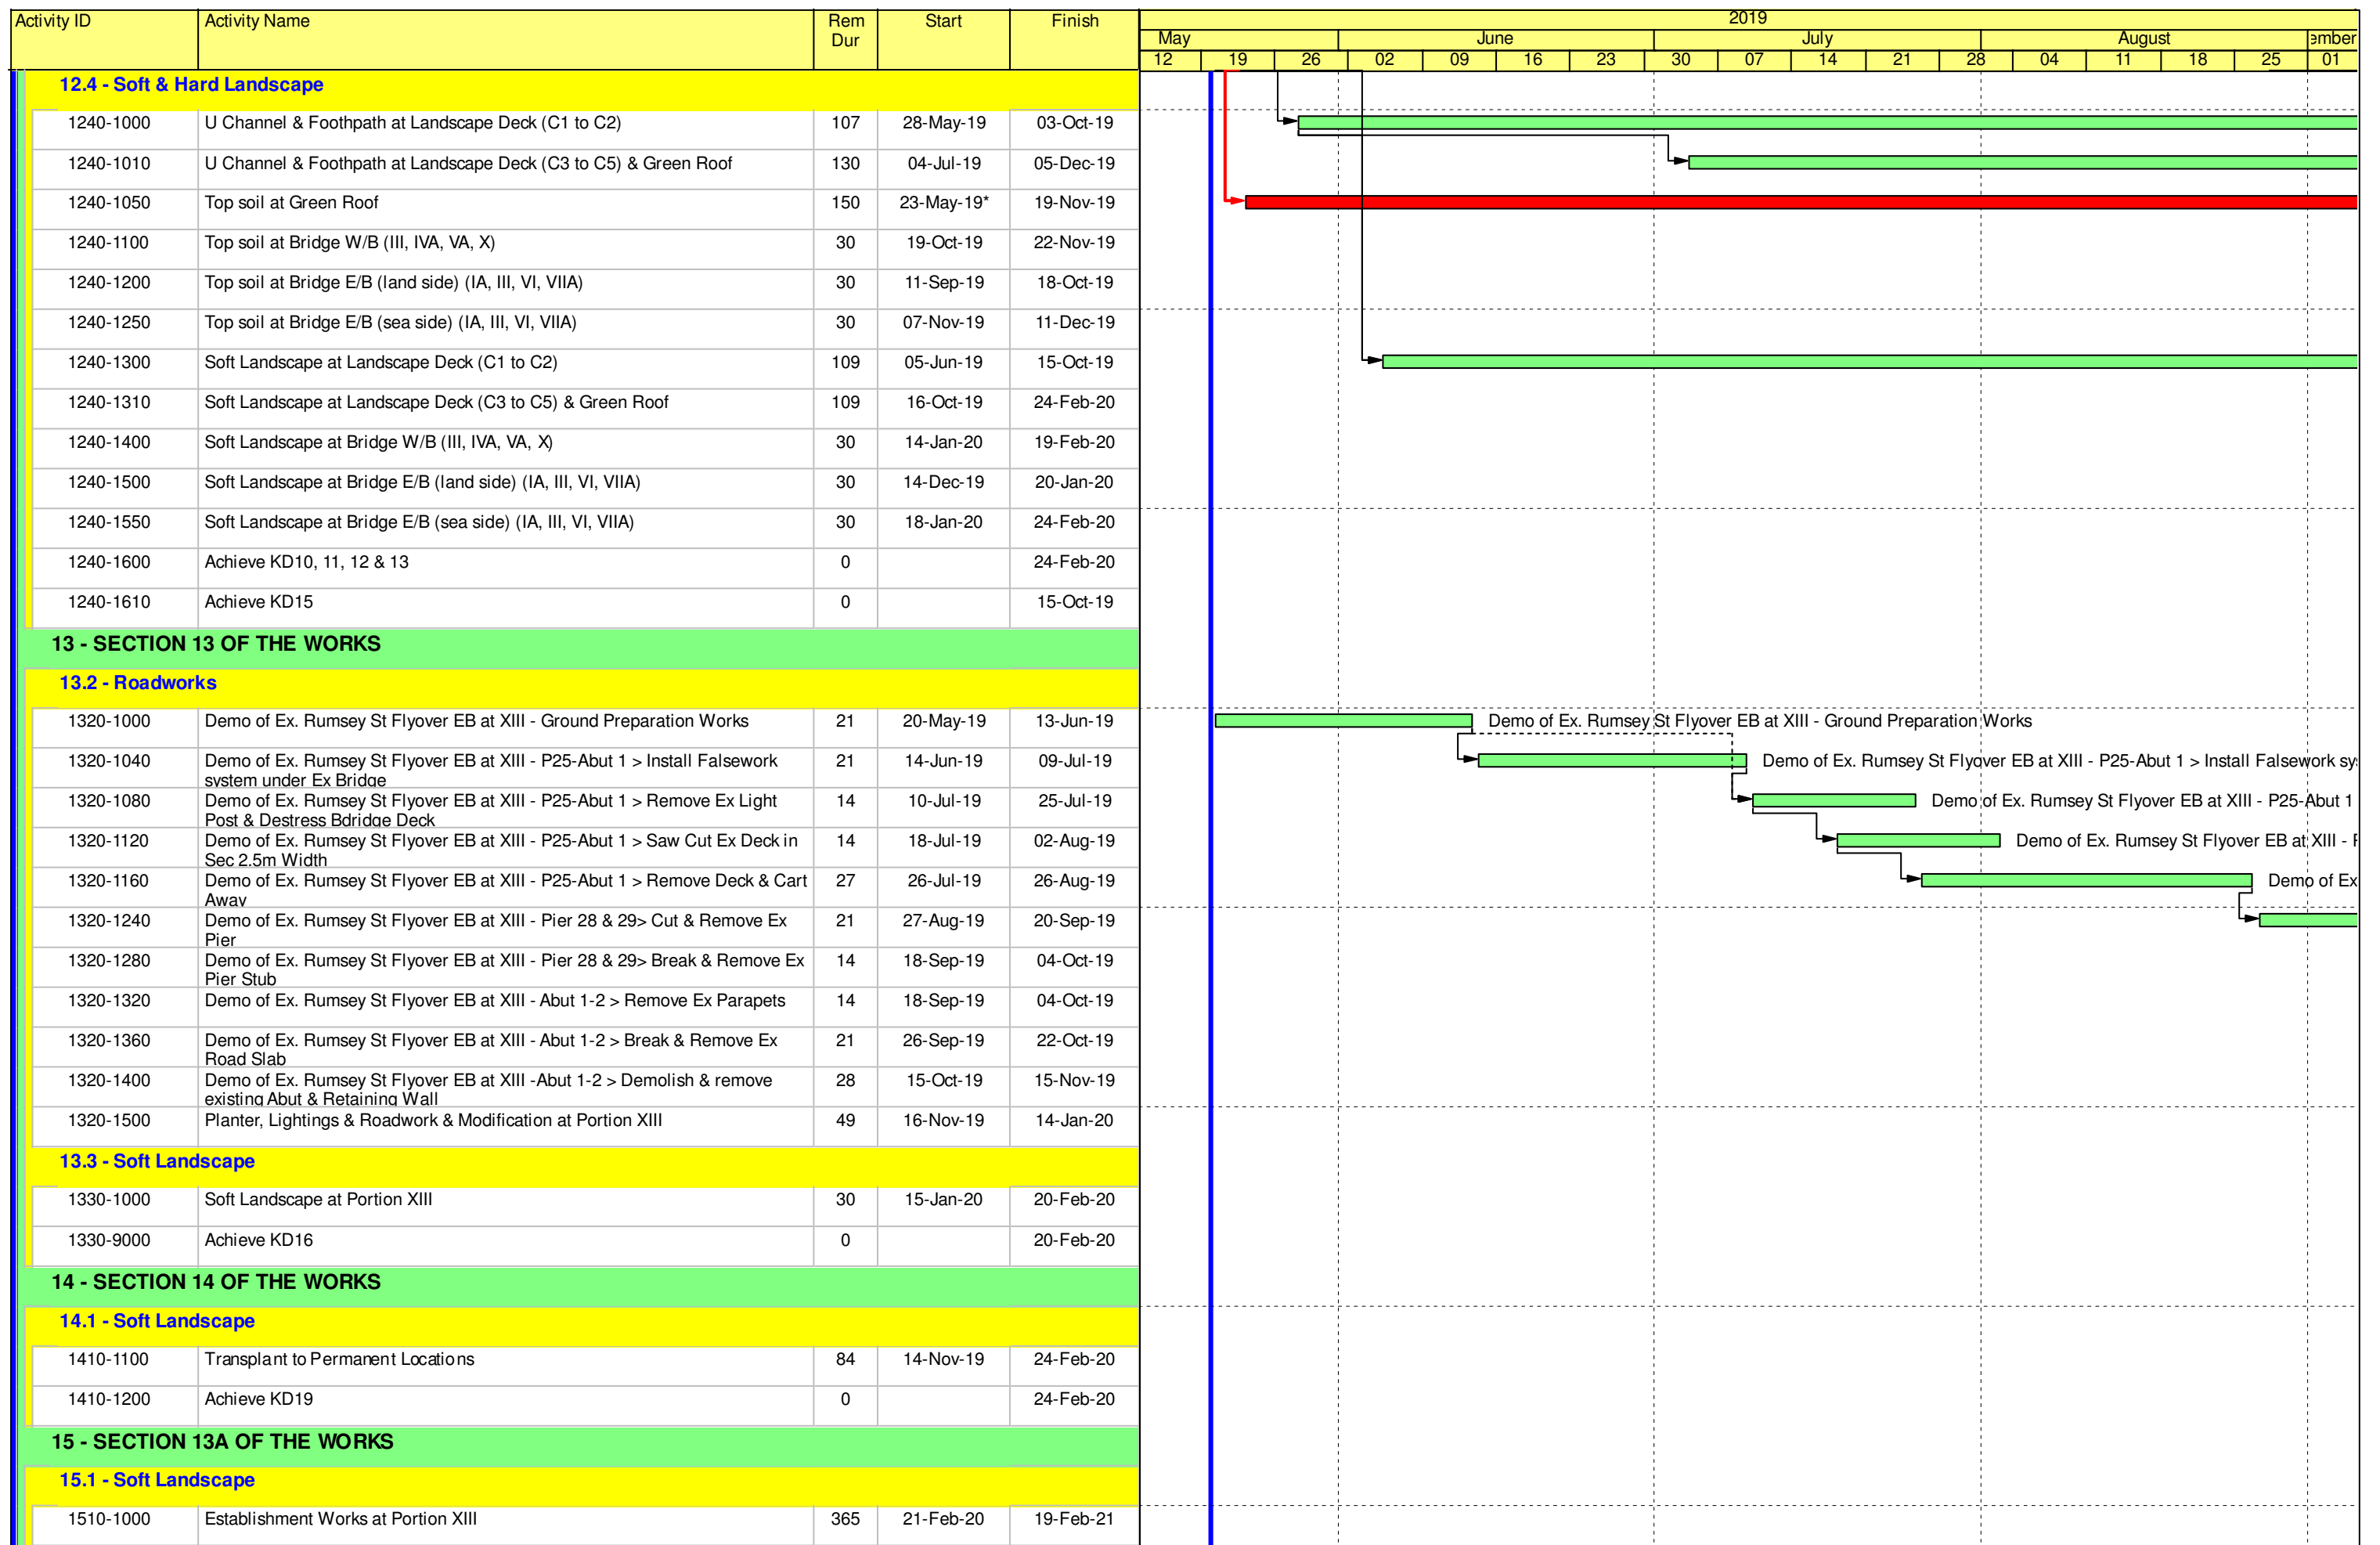

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.May.2019 to 20.Aug.2019)

Activity ID	Activity Name	Rem Dur	Start	Finish	2019																		
					May			June				July				August					September		
					12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	01		
1510-9000	Achieve KD17	0		19-Feb-21																			
16 - SECTION 13B OF THE WORKS																							
16.1 - Soft Landscape																							
1610-1000	Establishment Works at Portion IA	365	25-Feb-20	23-Feb-21																			
1610-1100	Establishment Works at Portion IIA	365	16-Oct-19	14-Oct-20																			
1610-1200	Establishment Works at Portion III	365	25-Feb-20	23-Feb-21																			
1610-1300	Establishment Works at Portion IVA	365	25-Feb-20	23-Feb-21																			
1610-1400	Establishment Works at Portion VA	365	25-Feb-20	23-Feb-21																			
1610-1500	Establishment Works at Portion VC	365	25-Feb-20	23-Feb-21																			
1610-1600	Establishment Works at Portion VI	365	25-Feb-20	23-Feb-21																			
1610-1700	Establishment Works at Portion VIIA	365	25-Feb-20	23-Feb-21																			
1610-1800	Establishment Works at Portion X	365	25-Feb-20	23-Feb-21																			
1610-1900	Establishment Works at Portion XIIA	365	25-Feb-20	23-Feb-21																			
1610-2000	Achieve KD18	0		23-Feb-21																			

■ Remaining Level of Effort ■ Remaining Work
■ Actual Level of Effort ■ Critical Remaining Work
■ Actual Work ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.May.2019 to 20.Aug.2019)

Activity ID	Activity Name	Original Duration	Start	Finish	2019											
					Feb	Mar	Apr	May								
Total		2566d	21-Mar-13 A	29-Mar-20												
DWP-08 - (2) - Update Progress As of 20 Feb 19		2566d	21-Mar-13 A	29-Mar-20												
Works in KD9 (Include Re-provisioning Works of KD4,KD5)		227d	03-May-18 A	30-Mar-19												
External Works Under KD9		30d	16-Nov-18 A	22-Feb-19												
Zone 4 up to Elderly Facilities		30d	16-Nov-18 A	22-Feb-19												
Elderly Facilities V/039 Received on 22 Jun 2017		30d	16-Nov-18 A	22-Feb-19												
EXW_2280	Ground levelling, drainage works and safety met installation	30d	16-Nov-18 A	22-Feb-19	■ Ground levelling, drainage works and safety met installation											
Reverting Traffic for IEC,VP Rd & TF St & Seawall Reinstatement (KD9)		227d	03-May-18 A	30-Mar-19												
TTA Revert Traffic Back to Original Alignment		19d	01-Dec-18 A	31-Dec-18 A												
East Bound TTA - IEC East Bound, Victoria Park Road & footpath along Sea Side		10d	01-Dec-18 A	07-Dec-18 A												
TTM Stage 1 - IEC (East Bound)		6d	01-Dec-18 A	07-Dec-18 A												
Reinstatement Existing Structure		6d	01-Dec-18 A	07-Dec-18 A												
EB_1020	Install metal parapet on parapet wall (30m)	6d	01-Dec-18 A	07-Dec-18 A												
TTM Stage 2 - Revert Traffic back to Original Victoria Road		4d	01-Dec-18 A	07-Dec-18 A												
Existing Bridge Parapet Reinstatement		4d	01-Dec-18 A	07-Dec-18 A												
EB_1180	Install metal parapet on parapet wall (40m)	4d	01-Dec-18 A	07-Dec-18 A												
West Bound - IEC West Bound & Tsing fung Street		5d	29-Dec-18 A	31-Dec-18 A												
TTM Stage 2 - Revert Traffic back to Original Tsing Fung Street		5d	29-Dec-18 A	31-Dec-18 A												
Existing Bridge Parapet Reinstatement		5d	29-Dec-18 A	31-Dec-18 A												
IECW_1140	Install metal parapet on parapet wall (60m)	5d	29-Dec-18 A	31-Dec-18 A												
Completion of Minor Outstanding / Remaining Works for KD9		227d	03-May-18 A	30-Mar-19												
East Bound - Minor Outstanding Works in Footpath after Substantial Completion of KD9		131d	23-Aug-18 A	20-Dec-18 A												
Minor Reinstatement Works for Existing Sign Gantry		3d	14-Sep-18 A	19-Sep-18 A												
EB_1760	Connection of Public Lighting by HyD (Lighting)	2d	14-Sep-18 A	18-Sep-18 A												
EB_1790	Installation of E & M at Sign Gantry (night work)	1d	19-Sep-18 A	19-Sep-18 A												
Minor Reinstatement Works for Central Median of IEC & Footbridge		6d	05-Dec-18 A	20-Dec-18 A												
EB_1810	Dismantlement of temp directional sign mounted on extg footbridge	1d	05-Dec-18 A	05-Dec-18 A												
EB_1800	Reconstruction of central divider (6m long, night work)	6d	17-Dec-18 A	20-Dec-18 A												
Minor Reinstatement Works for Footpath		9d	27-Sep-18 A	15-Nov-18 A												
EB_1840	Re-provision of Tree	8d	27-Sep-18 A	15-Nov-18 A												
EB_1830	Reinstatement of District Council Welcome Sign and opening plaque at Planter area	1d	03-Oct-18 A	03-Oct-18 A												
Minor Reinstatement Works for Loop Detector		1d	23-Aug-18 A	24-Aug-18 A												
EB_1890	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)	1d	23-Aug-18 A	24-Aug-18 A												
West Bound - Completion of Minor Outstanding / Remaining Works for KD9		227d	03-May-18 A	30-Mar-19												
Minor Reinstatement Works for Victoria Park		126d	03-May-18 A	30-Mar-19												
IECW_1500	Re-provision of Tree	32d	03-May-18 A	30-Mar-19	■ Re-provision of Tree											
IECW_1510	Laying Irrigation Main	10d	27-Sep-18 A	12-Jan-19 A												
IECW_1520	Construct Landscape Footpath and Lightings	7d	05-Nov-18 A	16-Jan-19 A	■ Lightings											
Minor Reinstatement Works in IEC West Bound		119d	15-Oct-18 A	31-Dec-18 A												
IECW_1620	Repairing of concrete defects on extg concrete deck and abutment M	30d	15-Oct-18 A	24-Nov-18 A												
IECW_1610	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)	57d	24-Nov-18 A	24-Dec-18 A	■ (Sun midnight only)											
IECW_1660	Replacement of new rubber seal on extg MJ at IEC W/B and E/B (night work)	4d	26-Nov-18 A	31-Dec-18 A	■ work)											
IECW_1600	Replacement of new movement joint at IEC W/B (Sun midnight only)	8d	27-Dec-18 A	30-Dec-18 A												



中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Page 1 of 2
Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel (Slip Road 8 Section) - 3 Months Rolling Programme

Date	Revision	Checked	Approved
20-Feb-19	DWP-08 (2) - 3 Months Rolling	TL	TL

Activity ID	Activity Name	Original Duration	Start	Finish	2019																		
					Feb			Mar			Apr			May									
Works in Victoria Park (KD4, KD5, KD9)																							
Re-Provisioning Works																							
Nursery Compound																							
Nursery compound																							
Fire Sreivces																							
VP_NC_2030	FS inspection	14d	20-Aug-18 A	27-Sep-18 A																			
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks																							
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)																							
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365d	31-Mar-19	29-Mar-20																			
KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH>500mm)																							
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365d	31-Mar-19	29-Mar-20																			
KD18 - Section 11: Transplanted Trees DBH>500mm in Portion VA and XII																							
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365d	31-Mar-19	29-Mar-20																			
KD10 - Preservation and Protection of Trees																							
PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	02-Apr-19																			
KD15 & KD8 - Mooring Components Upkeep (CBTS and ATS)																							
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	21-Feb-19																			

■ Preservation and Protection of Existing Trees

■ Mooring Upkeep at Portion X(10) & XVI(16) - CBTS

Data Date: 20-Apr-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2019											
						Apr			May			Jun			Jul		
Update 2019-04-20 CWB(CC) - Commissioning Contract (DWP 4b)																	
PRELIMINARIES AND GENERAL REQUIREMENTS																	
Salient Key Dates and Milestones																	
Anticipated Completion Dates																	
KD11	KD11 - Completion of Section 6 of the Works (1445 days) - include EOT No.12 (149 days)	0		01-May-19*	-444	◆											
KD07	KD07 - Completion of Section 2 of the Works (1771 days) - include EOT No.12 (414 days)	0		19-Jun-19*	-276	◆											
KD09	KD09 - Completion of Section 4 of the Works (1445 days) - include EOT No.12 (149 days)	0		19-Jul-19*	-671	◆											
Possession Dates and Vacation Dates																	
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-Apr-19	08-Aug-19	-432	—											
Submissions and Approvals																	
Initial General Submission																	
10168	Submission of CMC 3DVR	30	20-Apr-19	19-May-19	-245	—											
PROCUREMENT, MANUFACTURING & DELIVERIES																	
Procurement; Manufacturing; Deliveries																	
Green Wall on ADB																	
Procurement & Fabrication																	
10248	ADB Green Wall - Embed fabrication & delivery	30	30-Oct-18 A	25-Apr-19	-626	—											
10252	ADB Green Wall - Green Wall Fabrication & delivery	52	30-Oct-18 A	19-May-19	-650	—											
10250	ADB Green Wall - Commence embed installation	0	26-Apr-19		-626	◆											
10254	ADB Green Wall - Commence installation	0	20-May-19		-650	◆											
CONSTRUCTION																	
East Ventilation Building (EVb - related)																	
East Ventilation Building (EVb)																	
Final Completion Works																	

◆	Current Milestone	—	Remaining Work
—	Level of Effort	—	Project Baseline
△	Baseline Milestone	—	
—	Actual Work	—	
—	Critical Remaining Work	—	

Leighton Contractors (Asia) Limited

Programme Update 62 (April 2019)

THREE MONTH ROLLING



Project ID: H2613-U062
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U062
 Page 1 of 3

Date	Revision	Checked	Approv...
20-Mar-19	U061	AT	CW
20-Apr-19	U062	AT	CW

Data Date: 20-Apr-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

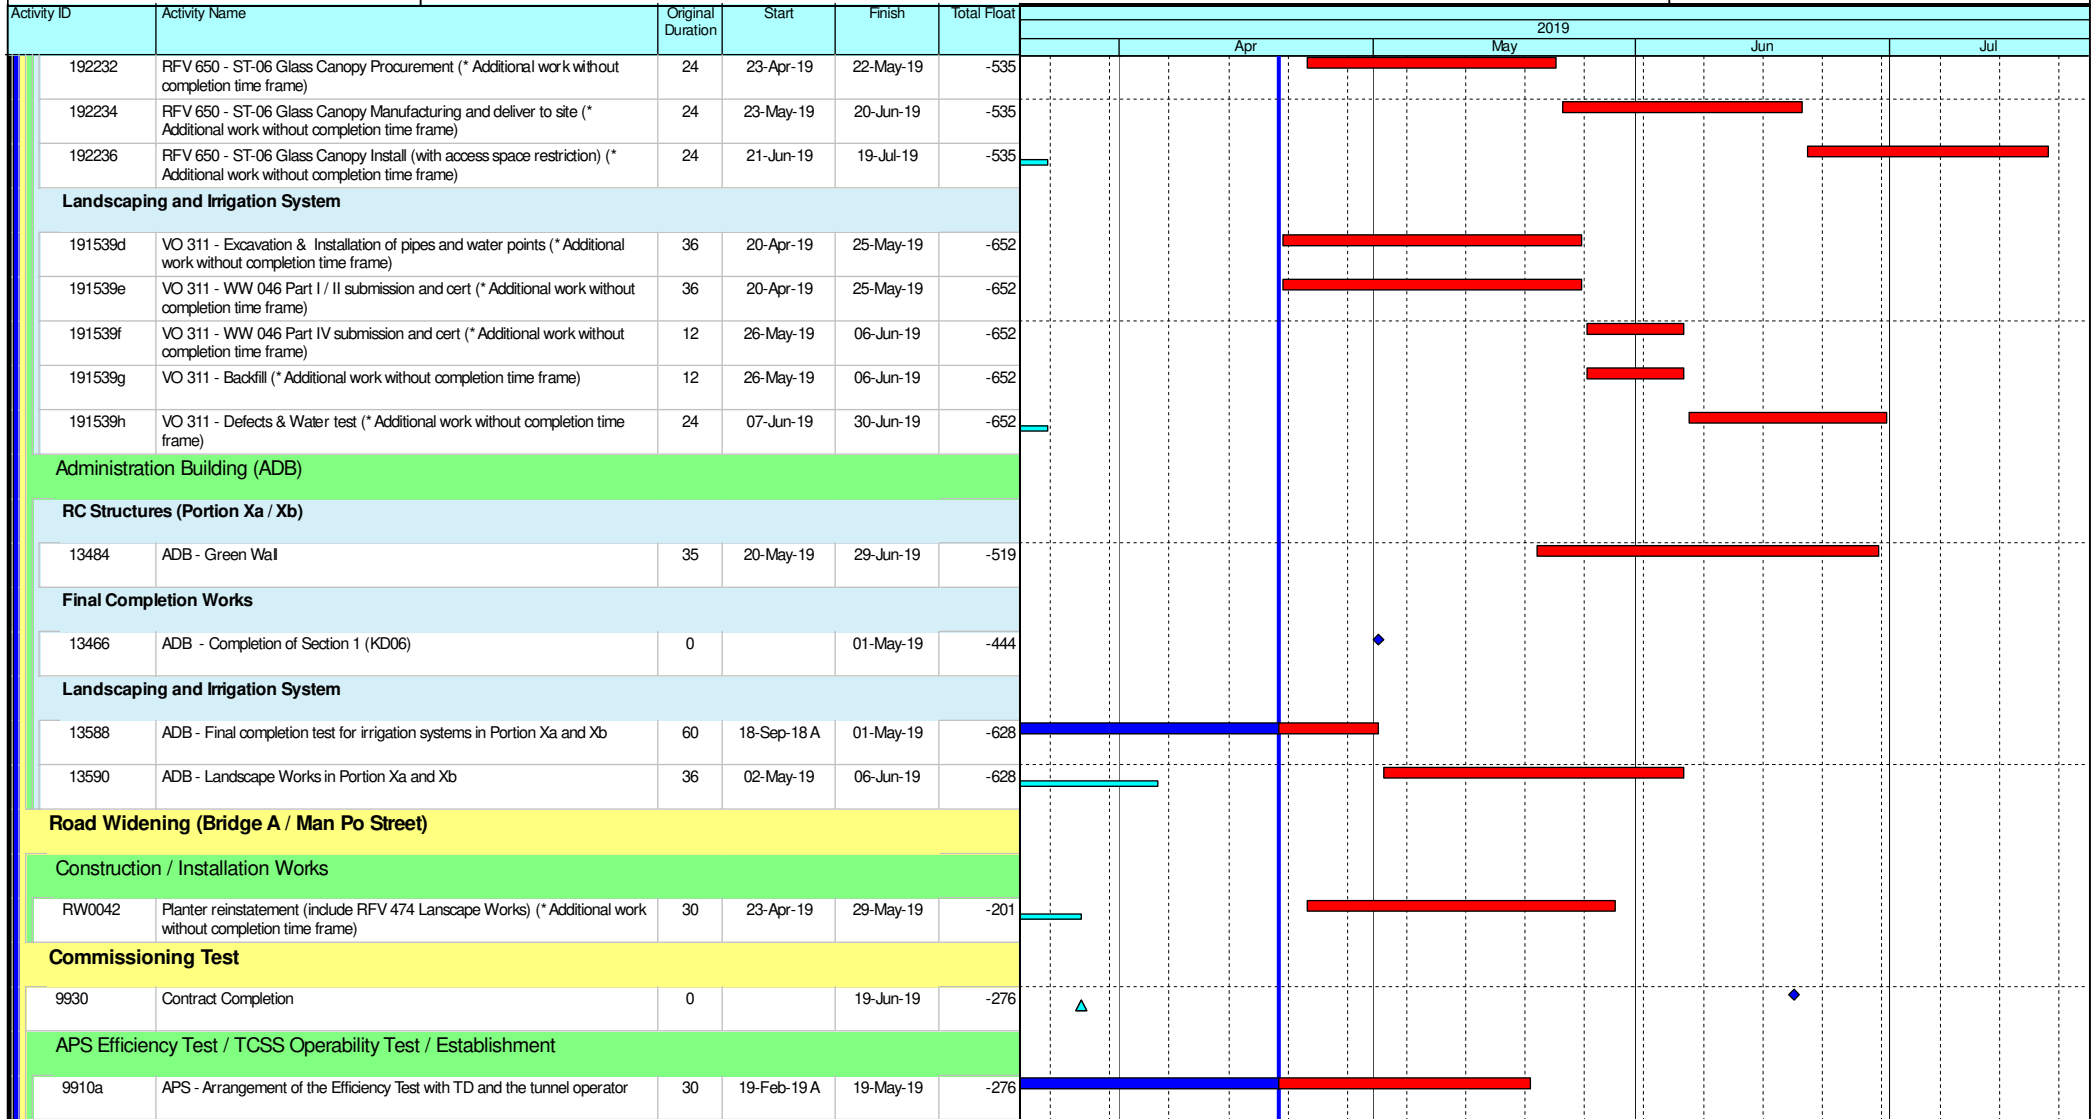

Leighton Contractors (Asia) Limited Programme Update 62 (April 2019) THREE MONTH ROLLING

Project ID: H2613-U062
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U062
 Page 2 of 3








Date	Revision	Checked	Approv...
20-Mar-19	U061	AT	CW
20-Apr-19	U062	AT	CW

Data Date: 20-Apr-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2019			
						Apr	May	Jun	Jul
10218	TCSS - Test results documentation (after TCSS operability tests completion)	0		20-Apr-19	-215				
10224	TCSS - List of all consumables (after TCSS operability tests completion)	0		20-Apr-19	-215				
9910b	APS - Record the APS efficiency	10	20-May-19	29-May-19	-276				
9910c	APS - Preparation of the test results for ER approval	7	30-May-19	05-Jun-19	-276				
9910d	APS - ER approval on the APS Efficiency Test	14	06-Jun-19	19-Jun-19	-276				
Training / Plan / Manual / As-Built Drawings for Project Completion									
192114	As-Built Drawings submission	0		20-Apr-19*	-215				

-  Current Milestone
-  Level of Effort
-  Baseline Milestone
-  Actual Work
-  Critical Remaining Work
-  Remaining Work
-  Project Baseline

Leighton Contractors (Asia) Limited Programme Update 62 (April 2019) THREE MONTH ROLLING

Project ID: H2613-U062
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U062
 Page 3 of 3

Date	Revision	Checked	Approv...
20-Mar-19	U061	AT	CW
20-Apr-19	U062	AT	CW
