

CONTRACTOR'S SUBMISSION

Contract No. HK/2009/02 Wan Chai Development Phase II Central – Wan Chai Bypass at Wan Chai East

То	: AECOM Asia Co. Ltd. Attn : Ms Gloria Tang
CS Title CS Ref.	: Three-Month Rolling Programme (Version Date: 1 February 2019) : CWCRGLJV/573/CS/PR/S-0295 Revision K
Status	☑-1 st submission date : 9 February 2018
Type of Submission	: □Design □Drawings □Method Statement □Materials □QA / QC □Safety □Environ. ☑Programme / Progress □Survey □Others
Specification Ref.	: <u>N.A.</u>
Drawing Ref.	: <u>N.A.</u>
Submission Details	: ☑Please refer to attachment ☑Please see below
Version) with minor re	ner submit the Three-Month Rolling Programme Version Date: 1 February 2019 (Excel vision of the construction of subbase at Portion 5 to suit the latest information of delivery of Lunar New Year for your information and comments.
Purpose of Submission	n :☑For review and approval □For record purposes
Remarks:	
From : Chun W Name : Paul Yu Title : Project N Signature :	o – CRGL Joint Venture fanager
Date :	February 2019 PY/DY/JS/JN Originator : Jeffrey Ng

c.c. AACL – HO

Issue 02

Wan Chai Development Phase II - East

Create Date: 21/1/2019 Leaend Revised Date: 25/1/2019 Original Programme Period 28/1/2019 as in version date 11/12/18 30/1/2019 1/2/2019

Extendedl Programme Period as in this version date 21/1/19

Central - Wan Chai Bypass at Wan Chai **Contract: HK/2009/02**

Remaining Works Programme
 Week
 54
 Week
 55
 Week
 56
 Week
 01
 Week
 02


 1
 2
 3
 4
 5
 6
 7
 8
 9
 10
 11
 12
 13
 14
 15
 16
 17
 18
 19
 20
 21
 22
 23
 24
 25
 26
 27
 28
 29
 30
 31
 1
 2
 3
 4
 5
 6
 7
 8
 工序 9 10 11 12 13 Portion 5 運掘回填 WCRI 停止運泥因為Close P5 Exit Portion 5 運坭回填 WCR1 Removal of Temporary Storage of Backfill material at Portion 5 2 Seawall海床 做學仔 3 地面壆仔& 100mm Subbase 蕭直升機場Landing 清場 4 舊直升機場,海壆及梯台 5 打D-Wall 掘泥 打B區remaining D-Wall至+1.5 (15M) 北面東段4個catchpit和300U渠 (103m) 北面東段 DN8.3 DN8. 1 DN8. 2 Culvert東邊3個catchpit和300U渠 Culvert 1 DN8.5 6 U Channel & 沙井 北面西段1個catchpit和300,375U渠(56m) 北面中段: 375U to rea 7(2個catchpit和300/450U渠) BACKFILL 225垌由DN8.6至7349 225垌由D 7 渠垌& 沙井 225垌由7356和7349至BCO CCTV 7352, 7340, 7328, 7327 試棄 7353,7339, C1.3 CCTV 734 試氣 735 wsD approval of design WWW542 (21/12/18) WWW046報開工 IRRIGATION PIPE TTA approved in TMLG Meeting 5/12/18 9 Fresh Water Main FOOTPATH ALONG HHR FOOTPATH AREA ABCD remove PMSMA Relay Area ABCD PMSMA

AREA E remove and relay BC+PMSMA wait 10 HHR 馬路 AREA F remove and relay BC+PMSMA REMEDIAL TO CONCRETE LAYBY remdeial to concrete layby VO258 MODIFICATION WORK AT ABUTMENT ROOM 10.1 HHR FLYOVER REMAINING WORK VO253 PROVIDE STAINLESS STEEL LADDER AT ABUTMENT ROOM * Portion 2 Zone 1 清濁 打路面石原 * Zone 2a upto end of EVA 升井蓋 載.formation subase 打石屎 執formation * Zone 2a remaining area * Portion 2 Zone 2b 打石屎 執formation REMEDIAL TO EXPO DRIVE COVERED WALKWAY 12 博覽道東, WCR1 & WCR3 未完成工作 subase 拆沈載池 Caisson seawall defects ng point WCR3-1 海龍明珠如下COPING (COMMENCEMENT DATE TO BE CONFIRMED) WCR1&3 MAKE GOOD ARMOUR SLOPE PROFILE



Wan Chai Development Phase II - East Central - Wan Chai Bypass at Wan Chai Contract: HK/2009/02

Remaining Works Programme

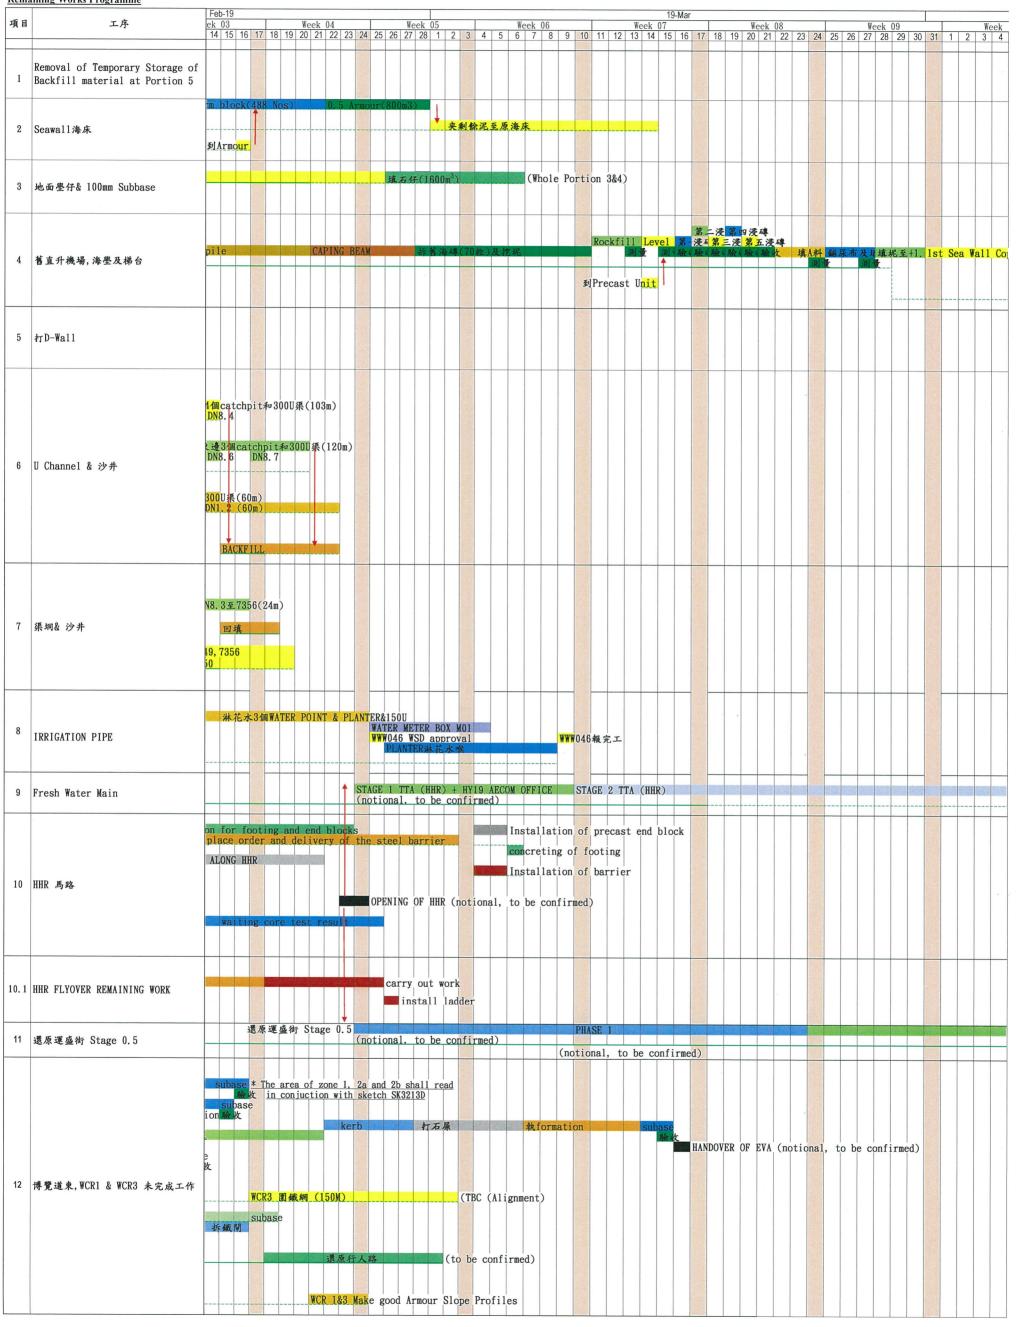



Wan Chai Development Phase II - East Central - Wan Chai Bypass at Wan Chai Contract: HK/2009/02

Kem	aining Works Programme	_														_		_																			
項目	工序	10	6	7 8	9	Wee	k 11	2 13)-Apr 15 16	We	ek 12	2 19 20	0 21	22	23 24	Veek 1	3 26 2	27 28	29	30 1	Week 1	4 3 4	4 5	6	We 7 8	ek 15) 11	12 1	3 14	Week	16	18 1	9 20	21 22	Week 2 23	17	25 26
1	Removal of Temporary Storage of Backfill material at Portion 5																																				
2	Seawall海床																																				
3	地面坐仔& 100mm Subbase																																				
4	舊直升機場,海壆及梯台	oing <mark>2nd</mark>	Copi	ing		樓梯		落分	回 Filte	cut 填至	麦Fen pipe p +2.8 透原	oile	原石 Beam	屎地	台															3							
5	打D-Wall																																				
6	U Channel & 沙井																																				
7	渠坰& 沙井																																				
8	IRRIGATION PIPE																																				
9	Fresh Water Main												_																								
10	HHR 馬路																																				
10.1	HHR FLYOVER REMAINING WORK																																				
11	透原運盛街 Stage 0.5	PHAS	SE 2																P	HASE	3																
12	博覽道東, WCR1 & WCR3 未完成工作																																				



Wan Chai Development Phase II - East Central - Wan Chai Bypass at Wan Chai Contract: HK/2009/02

Remaining Works Programme

						Т													Ju	ıne													
項目	工序	27	28	We 29	30 3	8 31	1	2 3	3 4	4 5	Week 6	19	8	9	10	11	Week	20 3 14			17	18	Week	21	22	23	24	25	W 26	eek 27	22	29	30
1	Removal of Temporary Storage of Backfill material at Portion 5																																
2	Seawall海床																																
3	地面學仔& 100mm Subbase																																
4	舊直升機場,海壆及梯台																																
5	≱τD-Wall																																
6	U Channel & 沙井																																
7	渠坰& 沙井																								v								
8	IRRIGATION PIPE																																
9	Fresh Water Main				_																												
10	HHR 馬路																																
10.1	HHR FLYOVER REMAINING WORK																																
11	遷原運盛街 Stage 0.5				_																		_										
12	博覽道東, WCR1 & WCR3 未完成工作																																


Page 1 of 4 CEDD CONTRACT HK/2009/02 3 MONTHS ROLLING PROGRAMME OF WORKS PROGRAMME REVIEWED 8 AUG 2018 (DD 7-9-18) **EXCAVATION TWCR4 AND CONSTRUCTION OF WCR4 EXCAVATE TWCR4 AND INSTALL SEAWALL** 10 10 30-Oct-18 08-Nov-18 32 HK Working Day TRANSPORT OF P5 FILL MATERIAL TRANSPORT OF P5 FILL MATERIAL TO P34 MARINE EXCAVATION WEST SIDE EXC FOR G400 (1600M3) & 0.5TARMOUR WEST SIDE EXC FOR G400 (1600M3) 8 0.5TARMOUR, WEST SIDE EXC FOR G400 (1600M 20 07-Sep-18* 26-Sep-18 7-Day Workweek-ARRIVAL OF G400 A1040 ARRIVAL OF G400 17-Sep-18 17-Sep-18 143 7-Day Workweek-1 1<mark>→∎</mark> ARRIVAL OF ARMOUR A1050 ARRIVAL OF ARMOUR 134 21-Sep-18 22-Sep-18 HK Working Day **CUTTING D-WALL** EAST SIDE CORE HOLES 01-Sep-18 A 07-Sep-18 7-Day Workweek-EAST SIDE CORE HOLES WEST SIDE CORE HOLES A1090 WEST SIDE CORE HOLES 05-Sep-18 A 5 12-Sep-18 16 7-Day Workweek-20 VERTICAL CUT A1100 05-Sep-18 A 11-Sep-18 13 7-Day Workweek-1 HÓRIZONTÁL CUT A1110 HORIZONTAL CUT 20 20 07-Sep-18 26-Sep-18 7-Day Workweek-A1120 REMOVAL OF D-WALL 20 20 07-Sep-18 26-Sep-18 7-Day Workweek-1 **INSTALL SEAWALL** MANUFACTURE OF SEAWALL BLOCK MANUFACTURE OF SEAWALL BLOCK 27-Jul-18 A MANUFACTURE OF SEAWALL BLOCK A1125 43 19-Oct-18 40 86 7-Day Workweek-1 MANUFACTURE OF FACING STONE A1127 MANUFACTURE OF FACING STONE 15 15 20-Oct-18 03-Nov-18 103 7-Day Workweek-1 1ST DELIVERY 1 1ST DELIVERY A1130 13-Sep-18* 19 13-Sep-18 7-Day Workweek-A1140 2ND DELIVERY 06-Oct-18* 06-Oct-18 7-Day Workweek-1 2ND DELIVERY 3RD DELIVERY A1150 3RD DELIVERY 17 12-Oct-18* 12-Oct-18 7-Day Workweek-A1160 4TH DELIVERY 4TH DEL VERY 19-Oct-18* 19-Oct-18 7-Day Workweek-► 5TH DELIVERY A1170 5TH DELIVERY 27-Oct-18* 27-Oct-18 7-Day Workweek-6TH DELIVERY 6TH DELIVERY 02-Nov-18* 7-Day Workweek-►1 7TH DELWERY Δ1190 7TH DELIVERY 09-Nov-18* 09-Nov-18 7-Day Workweek-1 A1200 8TH DELIVERY 14 + 8TH DELIVERY 15-Nov-18* 15-Nov-18 7-Day Workweek-1 INSTALL AST SIDE SEAWALL BLOC MOUNTING ROCK BEDDING MOUNTING ROCK BEDDING 19-Sep-18 24-Sep-18 A1210 7-Day Workweek-LEVELLING LEVELLING 25-Sep-18 27-Sep-18 19 7-Day Workweek-1 — ■ M9 BLOCK A1230 M9 BLOCK 28-Sep-18 29-Sep-18 19 7-Day Workweek-LEVELLING LEVELLING A1240 30-Sep-18 04-Oct-18 7-Day Workweek-1 IST LAYER OF BLOCK A1250 1ST LAYER OF BLOCK 05-Oct-18 08-Oct-18 19 7-Day Workweek-2ND LAYER 2ND LAYER 09-Oct-18 11-Oct-18 7-Day Workweek-1 →□ βRD LAYER A1270 3RD LAYER 3 12-Oct-18 14-Oct-18 19 7-Day Workweek-A1280 4TH LAYER 19 4TH LAYER 15-Oct-18 17-Oct-18 7-Day Workweek-► 5TH LAYEI A1290 5TH LAYER 18-Oct-18 20-Oct-18 7-Day Workweek-1 6TH LAYER 6TH LAYER A1300 3 19 7-Day Workweek-21-Oct-18 23-Oct-18 TYPE A A1310 TYPE A 27-Oct-18 7-Day Workweek-1 24-Oct-18 GEOTEXTILE AND FILTER GEOTEXTILE AND FILTER A1320 4 28-Oct-18 31-Oct-18 19 7-Day Workweek-7-Day Workweek-A1330 B/F SOIL (5000m3) 01-Nov-18 08-Nov-18 19 B/F SOIL (5000m3) PLACE CONC CUBES AND PLACE CONC CUBES AND PARTLY B/F TO +3.5mPD (1000m3) A1340 09-Nov-18 14-Nov-18 19 7-Day Workweek-INSTALL WEST SIDE SEAWALL BLOCK MOUNTING ROCK BEDDING TYPE 12A & 12B MOUNTING ROCK BEDDING TYPE 12A & 12B, MOUNTING ROCK BEDD A1370 15 15 27-Sep-18 11-Oct-18 0 7-Day Workweek-1 A1380 LEVELLING 12-Oct-18 15-Oct-18 📺 LEVĖLLING, LEVELLING 7-Day Workweek-M9 BLOCK, M9 BLÖCK A1390 M9 BLOCK 16-Oct-18 18-Oct-18 7-Day Workweek-1 LEVELLING, LEVELLING LEVELLING A1400 19-Oct-18 25-Oct-18 7-Day Workweek-A1410 1ST LAYER OF BLOCK 7-Day Workweek-1ST LAYER OF BLOCK, 1ST LAYER OF BLOCI 26-Oct-18 31-Oct-18 2ND LAYER, 2ND LAYER A1420 2ND LAYER 01-Nov-18 05-Nov-18 7-Day Workweek-A1430 3RD LAYER, 3RD LAYER 3RD LAYER 06-Nov-18 7-Day Workweek-1 4TH LAYER, 4TH LAYER A1440 4TH LAYER 11-Nov-18 15-Nov-18 7-Day Workweek-5TH LAYER, 5TH LA A1450 5TH LAYER 16-Nov-18 7-Day Workweek-1 6TH LAYER, 6TH A1460 6TH LAYER 3 20-Nov-18 22-Nov-18 7-Day Workweek-TYPEA, TY TYPE A 23-Nov-18 7-Day Workweek-A1480 FILTER 27-Nov-18 30-Nov-18 7-Day Workweek-1 FILTER A1490 B/F TO +2.8mPD 6 01-Dec-18 06-Dec-18 7-Day Workweek-Revision Checked Approved Milestone **CHUN WO - CRGL** CEDD CONTRACT NO. HK/2009/02 Critical Milestones **JOINT VENTURE** WD II - Central Wanchai Bypass at Wan Chai East (Contract 2)


Current Works
Critical Works

Remaining Level of..

3-MONTH ROLLING PROGRAMME (data date 07-Sep-18)

Date	Revision	Checked	Approved

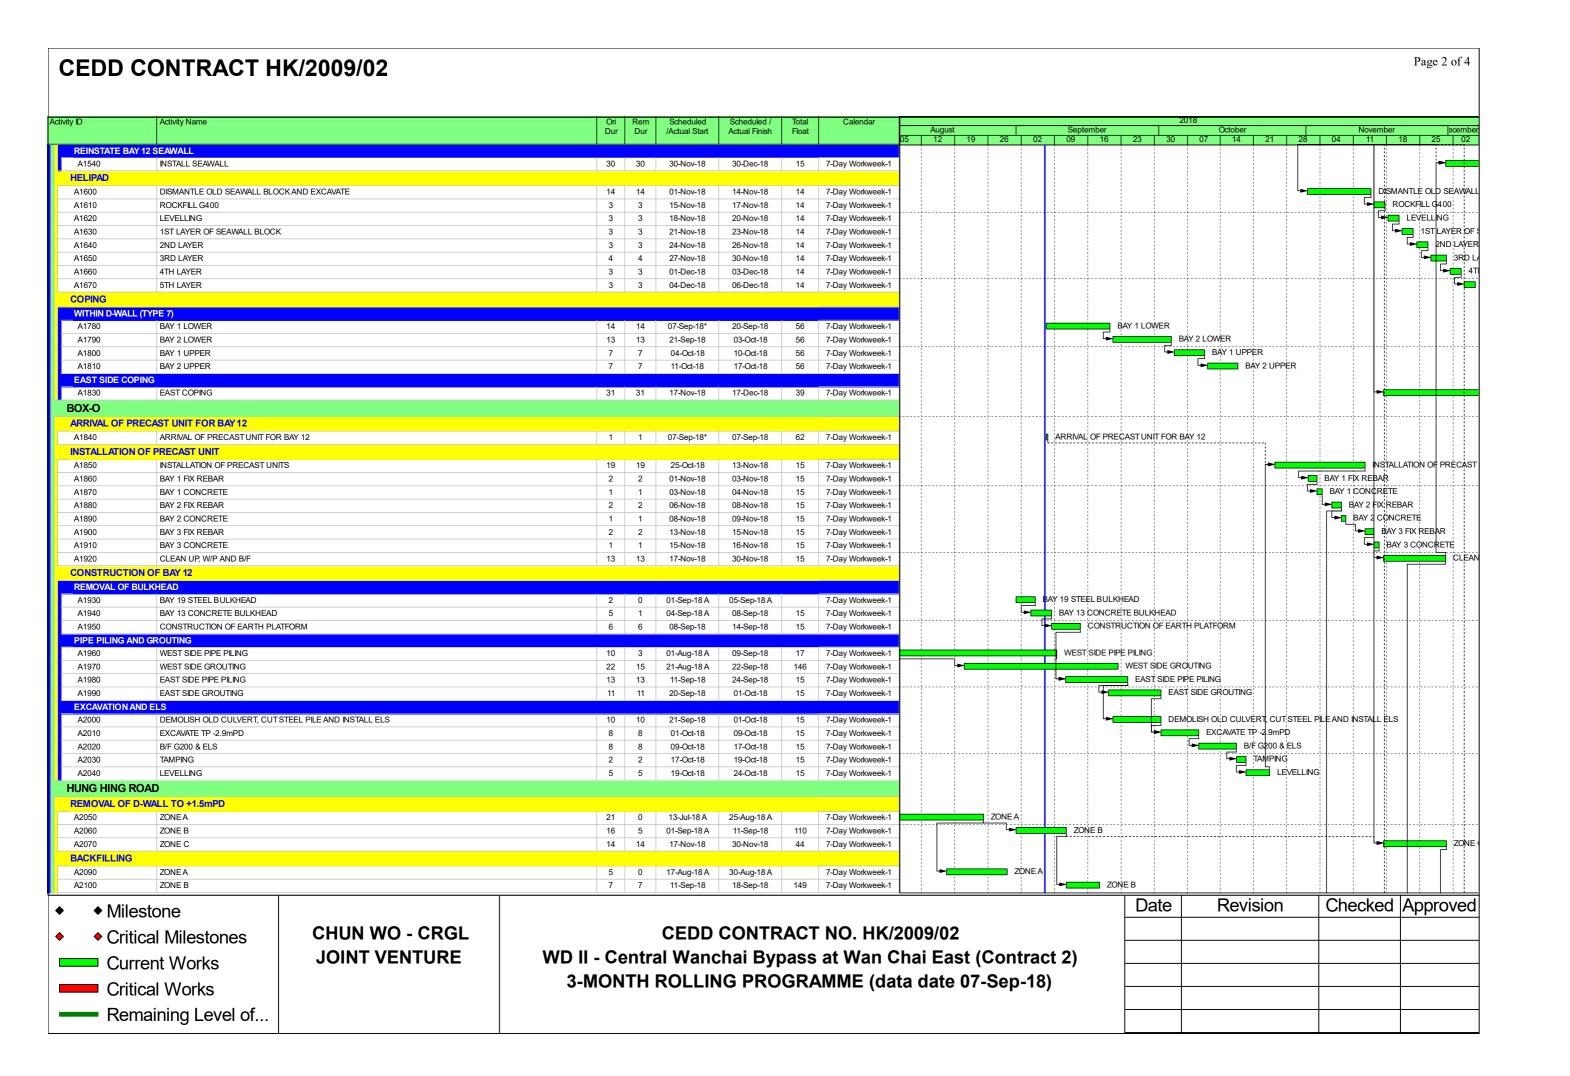

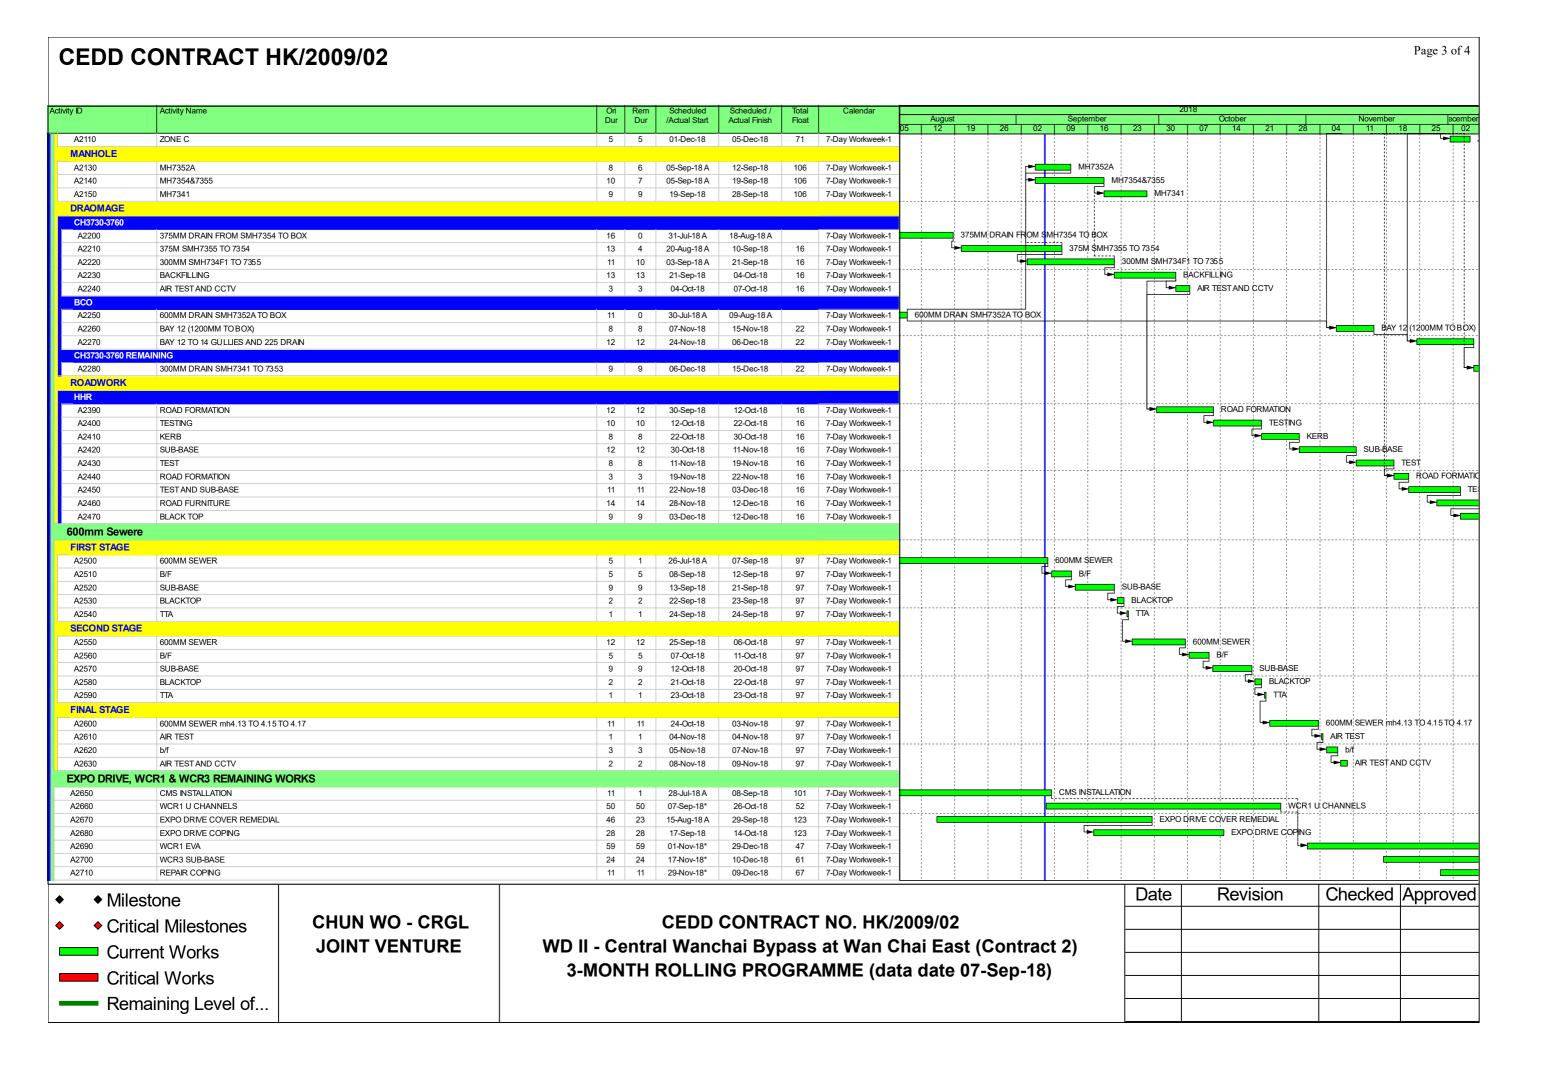

CEDD CONTRACT HK/2009/02	
LCEDIJ CONTRACT OR/2009/02	

Page 4 of 4

Activity ID	Activity Name	Ori	Rem	Scheduled	Scheduled /	Total	Calendar									20)18								
		Dur	Dur	/Actual Start	Actual Finish	Float			August				Septe	mber				October				November		ece	iber
								05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18 2	25	2
A2720	WCR1&3 ARMOUR SLOPE PROFILE	31	31	01-Dec-18*	31-Dec-18	45	7-Day Workweek-1																	-	_
A2740	REINSTATE WCR3 EXIT	23	23	24-Sep-18*	16-Oct-18	121	7-Day Workweek-1	1										RE	NSTATE \	WCR3 EX	ķπ		į		
A2750	WCR3 FENCING	23	23	09-Nov-18*	01-Dec-18	75	7-Day Workweek-1	1													_	-	_	\	VCR

◆ Milestone
 Critical Milestones
Current Works
Critical Works
Remaining Level of

CHUN WO - CRGL JOINT VENTURE CEDD CONTRACT NO. HK/2009/02 WD II - Central Wanchai Bypass at Wan Chai East (Contract 2) 3-MONTH ROLLING PROGRAMME (data date 07-Sep-18)

Date	Revision	Checked	Approved

	14.88.9								Centr	Wan	Chai	Devel	No. H opmer pass a	nt Ph	ase II	i Wes	t							Pa	ge:1/7		
tivity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	Jan	Feb	Mar	Apr	May	Jun 2	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	2019 Jun	Jul	Aug	Sep	Oct /
	Revised Works Programme Rev.12.0(DD 20 No	ovember 20	017)																			,	Jun	oui	Aug	Зер	Oct P
	nd Milestone Dates Vorks Completion (Included Not Granted EOT Enti																										
KD10840	Completion of Section IIIA	trement of	ne Contracto		201																						
KD10860	Complection of Section IV	0		08-Sep-18*	0%									•													
KD10880	Completion of Section V	0		30-Aug-18* 26-Sep-18*	0%																						
KD11010	Completion of Section VII	0			0%									_													
KD11020	Completion of Section VIII	0		14-Sep-18* 21-Sep-18*	0%									·_										•			
KD11040	Completion of Section IX	0		21-Sep-19*	0%									•													
KD11060	Completion of Section X	0		21-Sep-19*	0%									_												•	
	tions of Works Completion			21 Sep 16	0 70				ļ					•													
KD10080	Planned Section IIIA Completion - Road A2,A4, A5	0		08-Sep-18	0%									_													
KD10100	Planned Section IV Completion - Slip Road 3	0		30-Aug-18	0%									Ť													
KD10140	Planned Section V Completion - Remaining At-Grade Road	0		26-Sep-18	0%									_													
KD10280	Planned Section VII Completion - Remainder Works	0		14-Sep-18	0%																						
KD10300	Planned Section VIII Completion - Landscape Softwork	0		21-Sep-18	0%			-																			
KD10320	Planned Section IX Completion - Establishment Works	0		21-Sep-19	0%																						
KD10340	Planned Section X Completion - Tree Protection & Preservation	0		21-Sep-18	0%									•												•	
Dredging and	d Reclamation																										
Marine Work	Construction																										
Zone CRIII																											
Seawall Cons	truction - Zone CRIII																										
	eawall- 2nd Stage																										
Seawalf 2 &																											
MAR21371	Zone CRIII - seawall 2 & 12 - Backfilling remaining portion (type A, geotextile and filter)	0	19-Jan-18 A	27-Jan-18 A	100%																						
Zone D																											
	truction - Zone D																										
Seawall 10 &																											
MAR20630	Zone D - Seawall 10 & 11: Install remaining seawall block	14	20-Feb-18*	05-Mar-18	0%																						
MAR20650	Zone D - Seawall 10 & 11: Backfill Type A	7	06-Mar-18	12-Mar-18	0%																						
MAR20670	Zone D - Seawall 10 & 11: Lay geotextile and filter	7	13-Mar-18	19-Mar-18	0%																						
	ction Completion																										
Construction	Road A2, A4 & A5																										
NOGUWOFK &	Utilities - Section 1 (L1806 - L1801)																										
ata Date: 0-Feb-18	Current Milestone Actual Work Critical Remaining Work Remaining Work Remaining Level of Effort				Up (Ref	dated to R	d Wo	orks 2 as	Progr of 20	amm Febr	ne Re urary	v.12 2018	3)						Dat 20-Feb		Revision 2	Chec	cked		Approv	ed	


Page: 2/7

vity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity %							2018											2019	63233			
SIIIA10279c	Sec III A - section 1 carriageway - sewerage pipe from M/H	0	02-Jan-18 A	03-Feb-18 A	Complete 100%	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	
SIIIA10293	Sc to F8B (night time): construct sewerage pipe Sec III A - section 1 carriageway - sewerage pipe from M/H	6	05-Feb-18 A																								
	F8B - F8A (night time)	0		26-Feb-18	0%																						
SIIIA10294	Sec III A - section 1 carriageway - sewerage pipe from M/H F8A - F8	8	17-Jan-18 A	28-Feb-18	27.27%	100000																					
SIIIA10295	Sec III A - carriageway - works prrior TTA stage 5: excavation and duct laying of TCSS and public lighting	7	18-Jan-18 A	27-Feb-18	0%																						
SIIIA10298	Sec III A - section 1 carriageway - works prrior TTA stage 5: road kerb	5	28-Feb-18	05-Mar-18	0%																						
SIIIA10301	Sec III A - section 1 carriageway - works prrior TTA stage 5: road formation	2	06-Mar-18	07-Mar-18	0%			1																			
SIIIA10302	Sec III A - section 1 carriageway - works prrior TTA stage	5	08-Mar-18	13-Mar-18	0%			•																			
SIIIA10303	5: laying asphalt Sec III A - section 1 carriageway - works prrior TTA stage	3	14-Mar-18	16-Mar-18	0%																						
SIIIA10310	5: road marking & preparation works Sec III A - section 1 carriageway - TTA stage 5:	1	17-Mar-18	17-Mar-18	0%			1																			
SIIIA10310a	Implementation of TTA Stage 5 Sec III A - section 1 carriageway - TTA stage 5: remaining	12	19-Mar-18	04-Apr-18	0%																						
SIIIA10310b	sewerage pipe for M/H F8A - M/H F8 Sec III A - section 1 carriageway - TTA stage 5: remaining	18	06-Apr-18	26-Apr-18	0%																ļļ			ļ			
SIIIA10310c	sewerage pipe for M/H F8A - M/H F8B Sec III A - section 1 carriageway - TTA stage 5: SR1	5	19-Mar-18	23-Mar-18	0%																						
	at-grade road- remove sheetpile at U-trough west	21						_																			
SIIIA10310d	at-grade road -remove temp. road access bay 5 of SR1	21	24-Mar-18	21-Apr-18	0%																						
SIIIA10310e	at-grade road -construct upstand wall above Dwall	25	23-Apr-18	23-May-18	0%				-																		
SIIIA10310f	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - roadside barrier	14	24-May-18	08-Jun-18	0%					_																	
SIIIA10310g	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - road formation	7	09-Jun-18	16-Jun-18	0%						-																
SIIIA10310h	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - laying asphalt with transition slab	14	19-Jun-18	05-Jul-18	0%																						
SIIIA10312	Sec III A - roadwork and utitites section 1 carriageway - Drainage works (L2202 - L2201)	15	19-Mar-18	09-Apr-18	0%																						
SIIIA10312a	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L1805 - L1801)	15	10-Apr-18	26-Apr-18	0%																						
SIIIA10312b	Sec III A - roadwork and utilities section 1 carriageway -	12	27-Apr-18	11-May-18	0%				1																		
SIIIA10313	Drainage works (L1805-1807) Sec III A - roadwork and utilities section 1 carriageway -	14	07-May-18	23-May-18	0%			1	-						†												
SIIIA10320	gully pipe (L1807 - L1801) Sec III A - roadwork and utilities section 1 carriageway -	7	24-May-18	31-May-18	0%					-																	
SIIIA10340	fresh watermain Sec III A - roadwork and utities section 1 carriageway -	14	01-Jun-18	16-Jun-18	0%	1																					
SIIIA10360	utilities: HEC (80m) along carriageway Sec III A - roadwork and utilities section 1 carriageway -	14	19-Jun-18	05-Jul-18	0%																						
SIIIA10400	road kerb & formation Sec III A - roadwork and utilities section 1 carriageway -	7	06-Jul-18	13-Jul-18	0%																						
SIIIA10420	black top Sec III A - Implementation of TTA Stage 7P (Closure of	1	14-Jul-18	14-Jul-18	0%																						
	U-turn at Expo Drive)	10										_															
SIIIA10440	Sec III A - roadwork and utitites section 1 carriageway : breaking existing asphalt	10	16-Jul-18	26-Jul-18	0%																						
SIIIA10460	Sec III A - roadwork and utilities section 1 carriageway: road kerb and formation	14	27-Jul-18	11-Aug-18	0%							•															
SIIIA10480	Sec III A - roadwork and utilities section 1 carriageway : black top	10	13-Aug-18	23-Aug-18	0%								1000														
SIIIA10500	Sec III A - roadwork and utilities section 1 carriageway : roadmarking and road furniture	14	24-Aug-18	08-Sep-18	0%																						
Roadwork &	Utilities - Section 2 (L1810 - L1807)																				İ						
SIIIA12590	Sec III A - roadwork and utilities section 2 carriageway - black top	0	20-Jan-18 A	27-Jan-18 A	100%																						
Roadwork &	Utilities - Section 3 (L1808 - L1102)																										
SIIIA12770	Sec III A - roadwork and utilities section 3 carriageway - utilities: HEC ducting (60m) & crossroad duct (PCCW & HGC)	0	20-Jan-18 A	07-Feb-18 A	100%																						
SIIIA12790	Sec III A - roadwork and utilities section 3 carriageway -	17	08-Feb-18 A	10-Mar-18	0%		-																				
SIIIA12810	road kerb & formation Sec III A - roadwork and utilities section 3 carriageway -	7	12-Mar-18	19-Mar-18	0%								<u>.</u>										į				-
Roadwork &	black top Utilities - Section 6 (L1102 - L1411)																										
SIIIA13399	Sec III A - roadwork and utilities section 6 carriageway -	0	12-Jan-18 A	26-Jan-18 A	100%																						
SIIIA13444	gully pipe (L1101 -L1102) Sec III A - roadwork and utilities section 6 carriageway -	0	27-Jan-18 A	03-Feb-18 A	100%																						
	watermain (road crossing)	13						1																			
SIIIA13445	Sec III A - roadwork and utilities section 6 carriageway - utilities: crossed duct(HEC , HGC, PCCW)	13	05-Feb-18 A	06-Mar-18	0%			1																			

Page: 3 / 7

ity ID	LA officials Alarma	Domeining Dur	Early Chart		1 1-5-2-0/	
ity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019 2019
SIIIA13450	Sec III A - roadwork and utilities section 6 carriageway - road kerb & formation	18	07-Mar-18	27-Mar-18	0%	
SIIIA13470	Sec III A - roadwork and utilities section 6 carriageway - black top	7	28-Mar-18	09-Apr-18	0%	
SIIIA13570	Achievement of Section IIIA of the Works	0		08-Sep-18	0%	
Section V - Re	emaining At-Grade Road & Road P2					
Roadwork &	Utilities					
Section 1 (L1	504 - L1900)					
SV12456	Sec V-Roadwork & Utilities Section 1 - implementation of	0	20-Feb-18*	20-Feb-18	0%	
SV12460	TTA stage 5E (closure of slow lane at northbound of Expo Sec V - Roadwork & Utilities Section 1 - drinage works	15	20-Feb-18	08-Mar-18	0%	
SV12462	(L1902 - L1900) Sec V - Roadwork & Utilities Section 1 - gully pipe (L1902 -	6	09-Mar-18	15-Mar-18	0%	
SV12464	L1900) Sec V - Roadwork & Utilities Section 1 - temp. reinstatement	14	16-Mar-18	04-Apr-18	0%	
SV12466	to match with existing Expo Drive Sec V - Section 1 - Modification to 2nd stage ITA (V.O. 50) :	1	14-Jul-18	14-Jul-18	0%	
SV12468	closure of northbound and maintain one lane at southbound Sec V - Roadwork & Utilities Section 1 Carriageway -	7	16-Jul-18	23-Jul-18	0%	
SV12490	breaking existing asphalt Sec V - Roadwork & Utilities Section 1 Carriageway - Road	10	24-Jul-18	03-Aug-18	0%	
SV12520	kerb & formation Sec V - Roadwork & Utilities Section 1 Carriageway - Black	7	04-Aug-18	11-Aug-18	0%	
SV12522	Sec V - Section 1 - Implementation of TTA for road closure	3	13-Aug-18	15-Aug-18	0%	
SV12524	of northbound and southbound of Expo Drive Sec V - Section 1 - Northbound & Southbound of Expo Drive :	14	16-Aug-18	31-Aug-18	0%	
SV12526	breaking asphalt Sec V - Section 1 - Northbound & Southbound of Expo Drive:	14	01-Sep-18	17-Sep-18	0%	
SV12528	road kerb & formation Sec V - Section 1 - Northbound & Southbound of Expo Drive : black top	7	18-Sep-18	26-Sep-18	0%	
SV12570	Sec V - Roadwork & Utilities Section 1 footpath - utilities: TCSS	12	29-Dec-17 A	05-Mar-18	60%	
SV12580	Sec V - Roadwork & Utilities Section 1 footpath - paving block	29	06-Mar-18	12-Apr-18	0%	
Section 2 (L	1510 - L1504)					
SV12624	Sec V - Roadwork & Utilities Section 1 Carriageway - road kerb & formation	0	04-Jan-18 A	30-Jan-18 A	100%	
SV12626	Sec V - Roadwork & Utilities Section 1 Carriageway - black top	13	31-Jan-18 A	06-Mar-18	0%	
SV12692	Sec V - Roadwork & Utilities Section 2 footpath - U channel	11	17-Jan-18 A	03-Mar-18	21.43%	
SV12695	Sec V - Roadwork & Utilities Section 2 footpath - Watermain	13	05-Mar-18	19-Mar-18	0%	
SV12700	Sec V - Roadwork & Utilities Section 2 footpath - utilities: TCSS	16	20-Mar-18	11-Apr-18	0%	
SV12740	Sec V - Roadwork & Utilities Section 2 footpath - paving block	18	12-Apr-18	03-May-18	0%	
Section 3 (C	ulvert L - L1510)					
SIV12860	Sec V - Roadwork & Utilities Section 3 footpath - Utilities: TCSS, HGC, PCCW)	30	16-Jan-18 A	26-Mar-18	11.76%	
SIV12880	Sec V - Roadwork & Utilities Section 3 footpath - Paving block	21	27-Mar-18	24-Apr-18	0%	
Section 4 (Ki	L106 - Culvert L)					
SIV12282	Sec V - Roadwork & Utilities Section 4 Carriageway - Drainage Works (L1311 - Culvert L, L1201 - Culvert L)	10	20-Feb-18	02-Mar-18	0%	
SIV12300	Sec V - Roadwork & Utilities Section 4 Carriageway - Gully pipe (L1301 - Culvert L, L1201 - Culvert L)	7	03-Mar-18	10-Mar-18	0%	
SIV12302	Sec V - Roadwork & Utilities Section 4 Carriageway - watermain	6	12-Mar-18	17-Mar-18	0%	
SIV12305	Sec V - Roadwork & Utilities Section 4 Carriageway - utilities : cross road duct	7	19-Mar-18	26-Mar-18	0%	
SIV12310	Sec V - Roadwork & Utilities Section 4 Carriageway - Road kerb & formation : between culvert K and culvert L	15	27-Mar-18	17-Apr-18	0%	
SIV12320	Sec V - Roadwork & Utilities Section 4 Carriageway - Black top: between culvert K and culvert L	10	18-Apr-18	28-Apr-18	0%	
SIV12340	Sec V - Roadwork & Utilities Section 4 Carriageway - Black top: at west of culvert K	7	20-Feb-18	27-Feb-18	0%	
SIV12422	Sec V - Roadwork & Utilities Section 4 footpath - Utilities : TCSS	20	20-Feb-18	14-Mar-18	0%	
SIV12440	Sec V - Roadwork & Utilities Section 4 footpath - Utilities : HGC & PCCW	8	15-Mar-18	23-Mar-18	0%	


Page: 4 / 7

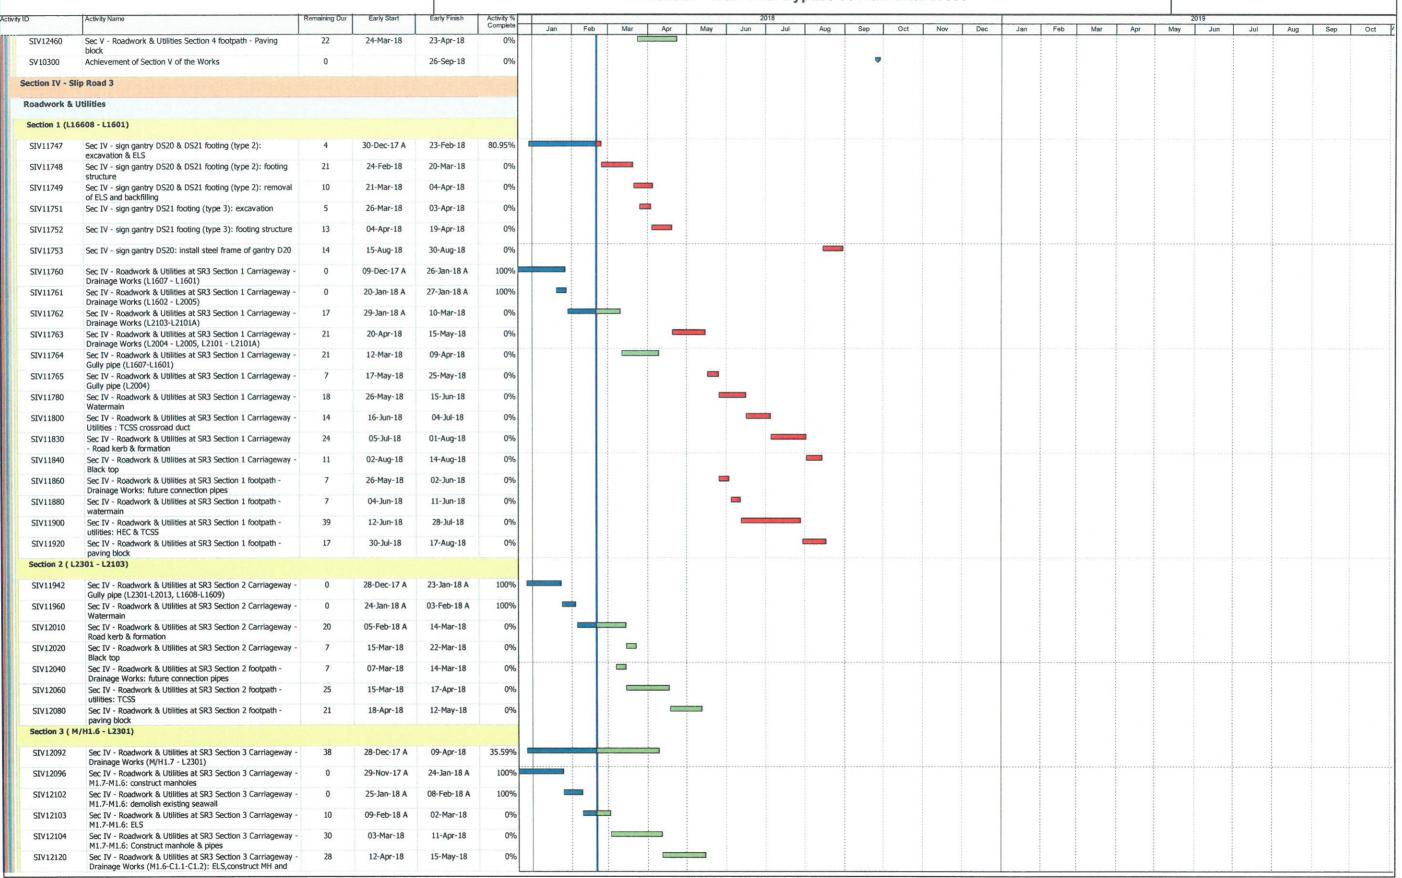


Page	:5/7	


vity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete							2018		2007									2019				
	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	6	16-May-18	23-May-18	O%	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	_	Jun	Jul	Aug	Sep	Oct
	Drainage Works (M1.6-C1.1-C1.2): Backfilling & shift lane Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	5	24-May-18	29-May-18	0%						1																
SIV12140	Drainage Works (M1.6-C1.1-C1.2): Construct MH C1.2 Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	32	10-Apr-18	17-May-18	0%																						
	Gully pipe (M/H 1.7 - L2301) Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	14	18-May-18	04-Jun-18	0%																						
	Road kerb Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	10	05-Jun-18	15-Jun-18	0%																						
	formation Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	7	16-Jun-18	25-Jun-18	0%																						
	Black top Sec IV - Roadwork & Utilities at SR3 Section 3 footpath -	21									1																
	Utilities: TCSS	21	10-May-18	04-Jun-18	0%																						
	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - U channel	10	05-Jun-18	15-Jun-18	0%																						
	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - Paving block	25	16-Jun-18	17-Jul-18	0%																						
SIV12222	Achievement of Section IV of the Works	0		30-Aug-18	0%								•														
Section VII - Re	mainder Works					1																		÷	·	ļ	
Road & Draina	ge Works (Culvert L - M/H1.7, Adjacent to SR3)																										
	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - Drainage Works (Culvert L -MH1.7)	48	08-Jan-18 A	20-Apr-18	18.64%																						
SVII11620	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway :	3	21-Apr-18	24-Apr-18	0%															1 4 4 6 6							
SVII11640	traffic diversion at Lung King Street Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway -	27	25-Apr-18	28-May-18	0%																	1 0 0 1 1					
SVII11650	Gully pipe (Culvert L -MH1.7) Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway -	7	29-May-18	05-Jun-18	0%					1											ļ						
SVII11654	TCSS duct Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway -	14	06-Jun-18	22-Jun-18	0%																						
SVII11660	road kerb & formation Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway -	6	23-Jun-18	29-Jun-18	0%																						
	Black top Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - U	14	29-May-18	13-Jun-18	0%																						
	channel Sec IV - Roadwork & Utilities at SR3 Section 4 footpath -	14	14-Jun-18	30-Jun-18	0%																						
	utilities: TCSS Sec IV - Roadwork & Utilities at SR3 Section 4 footpath -	14	03-Jul-18	18-Jul-18	0%																						
	paving block RW5 Construction			10 30 10	0.0																						
	Sec VII - Retaining Wall RW5 (bay 1) - construct base slab	22	20-Mar-18	10 4 10	000																						
	and wall Sec VII - Retaining wall RW5 (bay 2) - construct base slab			18-Apr-18	0%																						
	and wall	22	19-Apr-18	15-May-18	0%																						
	Sec VII - Retaining wall RW5 (bay 3) - construct base slab and wall	22	20-Mar-18	18-Apr-18	0%																						
	Sec VII - Retaining wall RW5 (bay 4) - construct base slab and wall	22	19-Apr-18	15-May-18	0%																						
SVII10860	Sec VII - Retaining wall RW5 - curing, removal formwork	8	16-May-18	25-May-18	0%																						
Landing Steps (Construction																										
Landing Steps	BSW13																										
	Sec VII - Landing steps (BSW13) - install vertical fender / step fender	15	15-May-18	01-Jun-18	0%						1																
	Sec VII - Landing steps (BSW13) - install s.s. handrail / tactile / sign board / bollard	25	02-Jun-18	03-Jul-18	0%	1						1											į į				
Landing Steps																											
SVII10980	Sec VII - Landing steps (BSW4) - install vertical fender / step fender	15	20-Jun-18	07-Jul-18	0%							-															
	Sec VII - Landing steps (BSW4) - install s.s. handrail / tactile	25	09-Jul-18	06-Aug-18	0%								-														
Landing Steps	/ sign board / bollard BSW5																										
SVII11060	Sec VII - Landing steps (BSW5) - install vertical fender / step	15	25-Jul-18	10-Aug-18	0%	ļ																			ļ		
	fender Sec VII - Landing steps (BSW5) - install s.s. handrail / tactile	25	11-Aug-18	08-Sep-18	0%																						
	/ sign board / bollard			- 50p 40	0,70																						
	Sec VII - Landing steps (BSW9) - install vertical fender / step	15	13-Jun-18	30-Jun-18	0%																						
	fender																										
	Sec VII - Landing steps (BSW9) - install s.s. handrail / tactile / sign board / bollard	25	03-Jul-18	31-Jul-18	0%																						


Page		6	1	7	
------	--	---	---	---	--

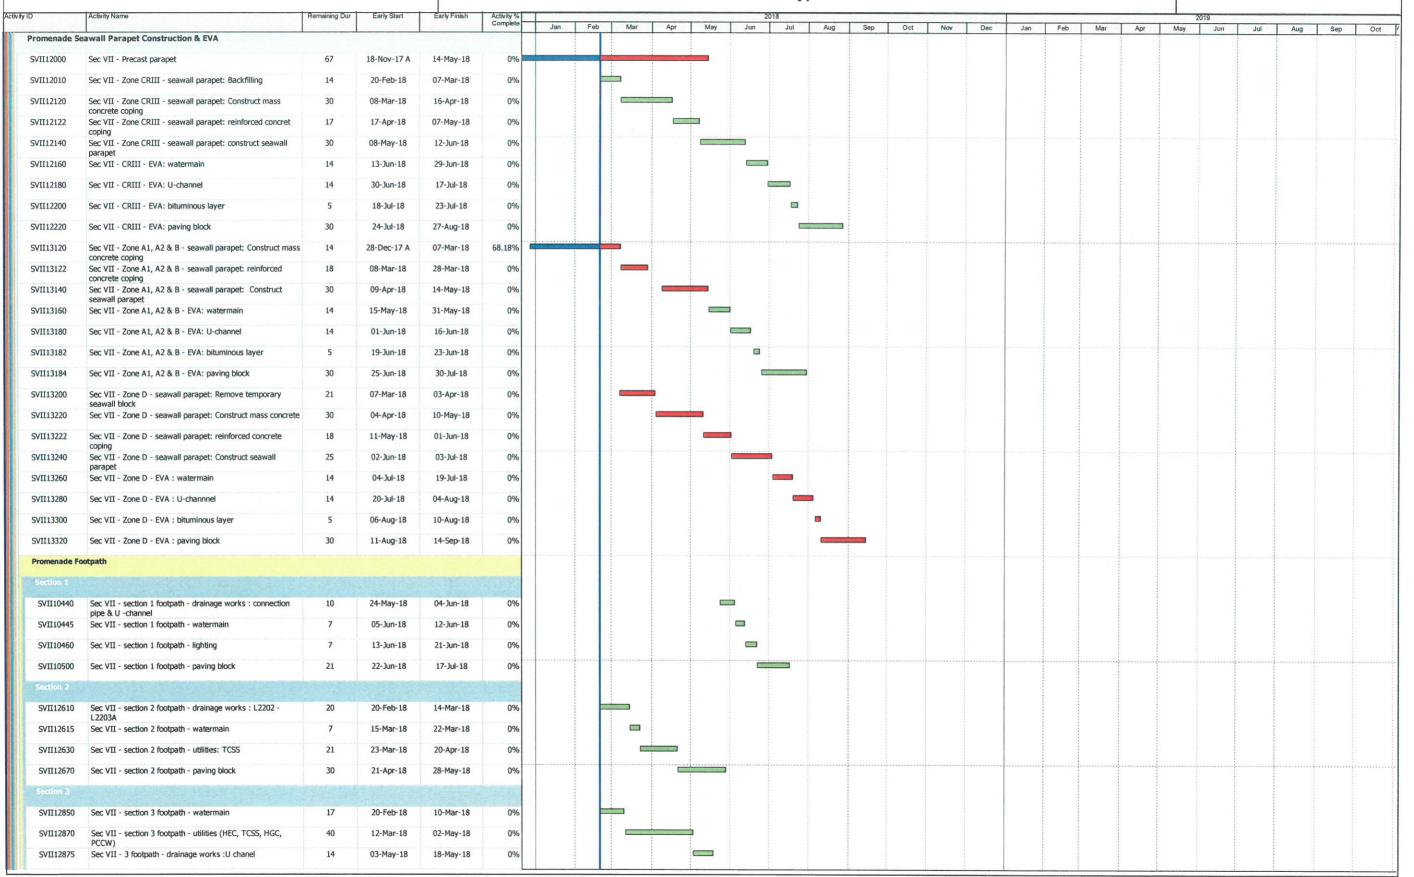



Page: 7/7

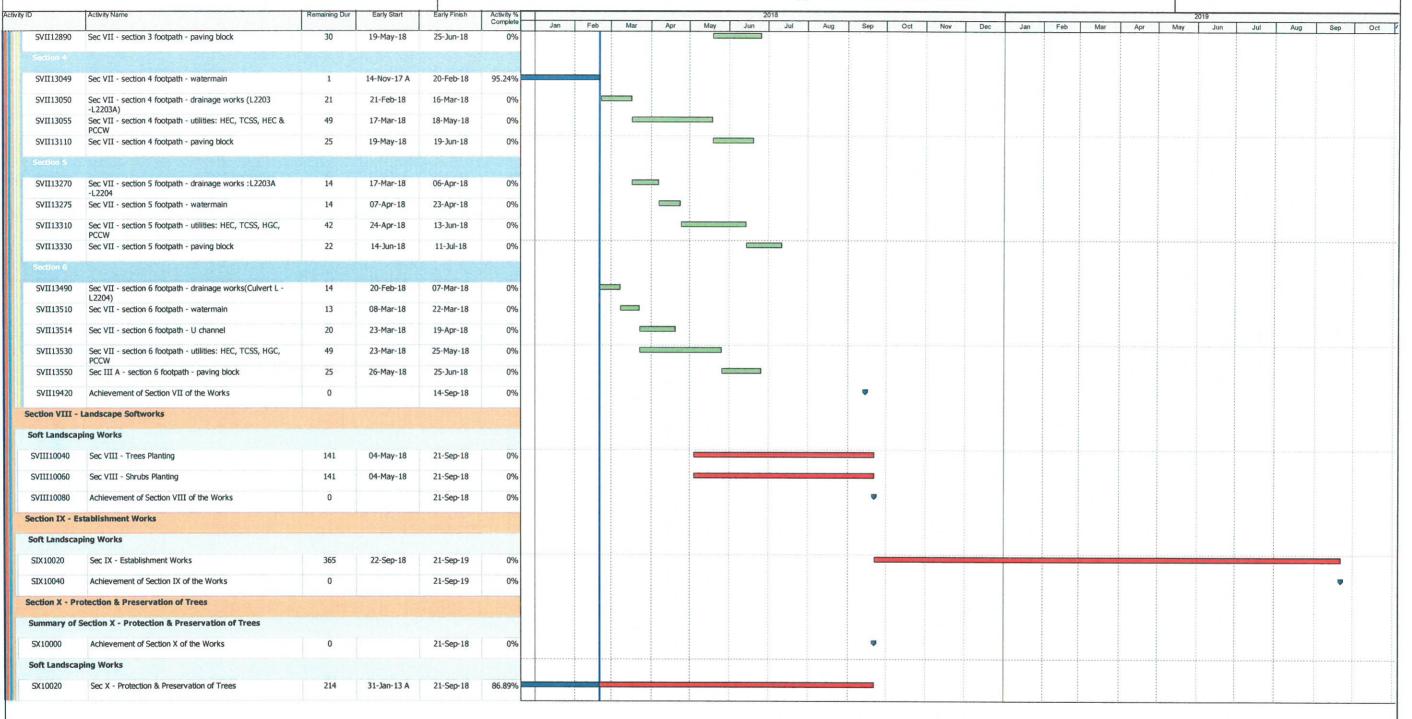


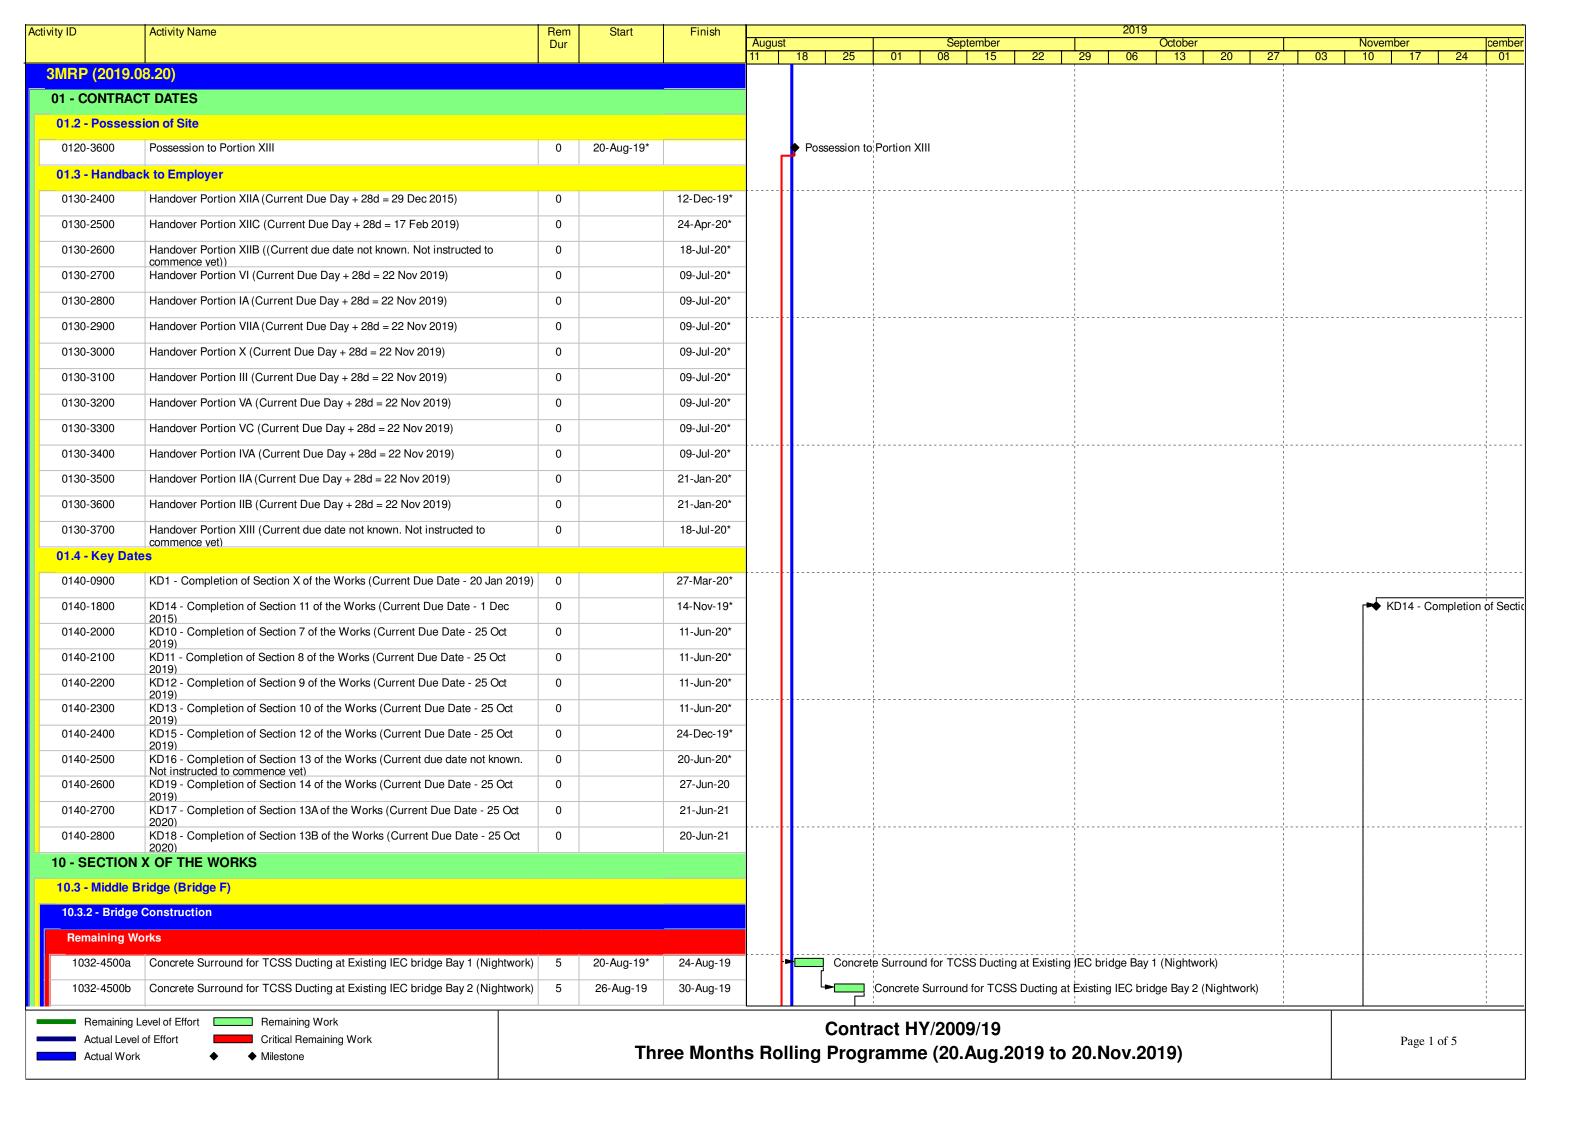


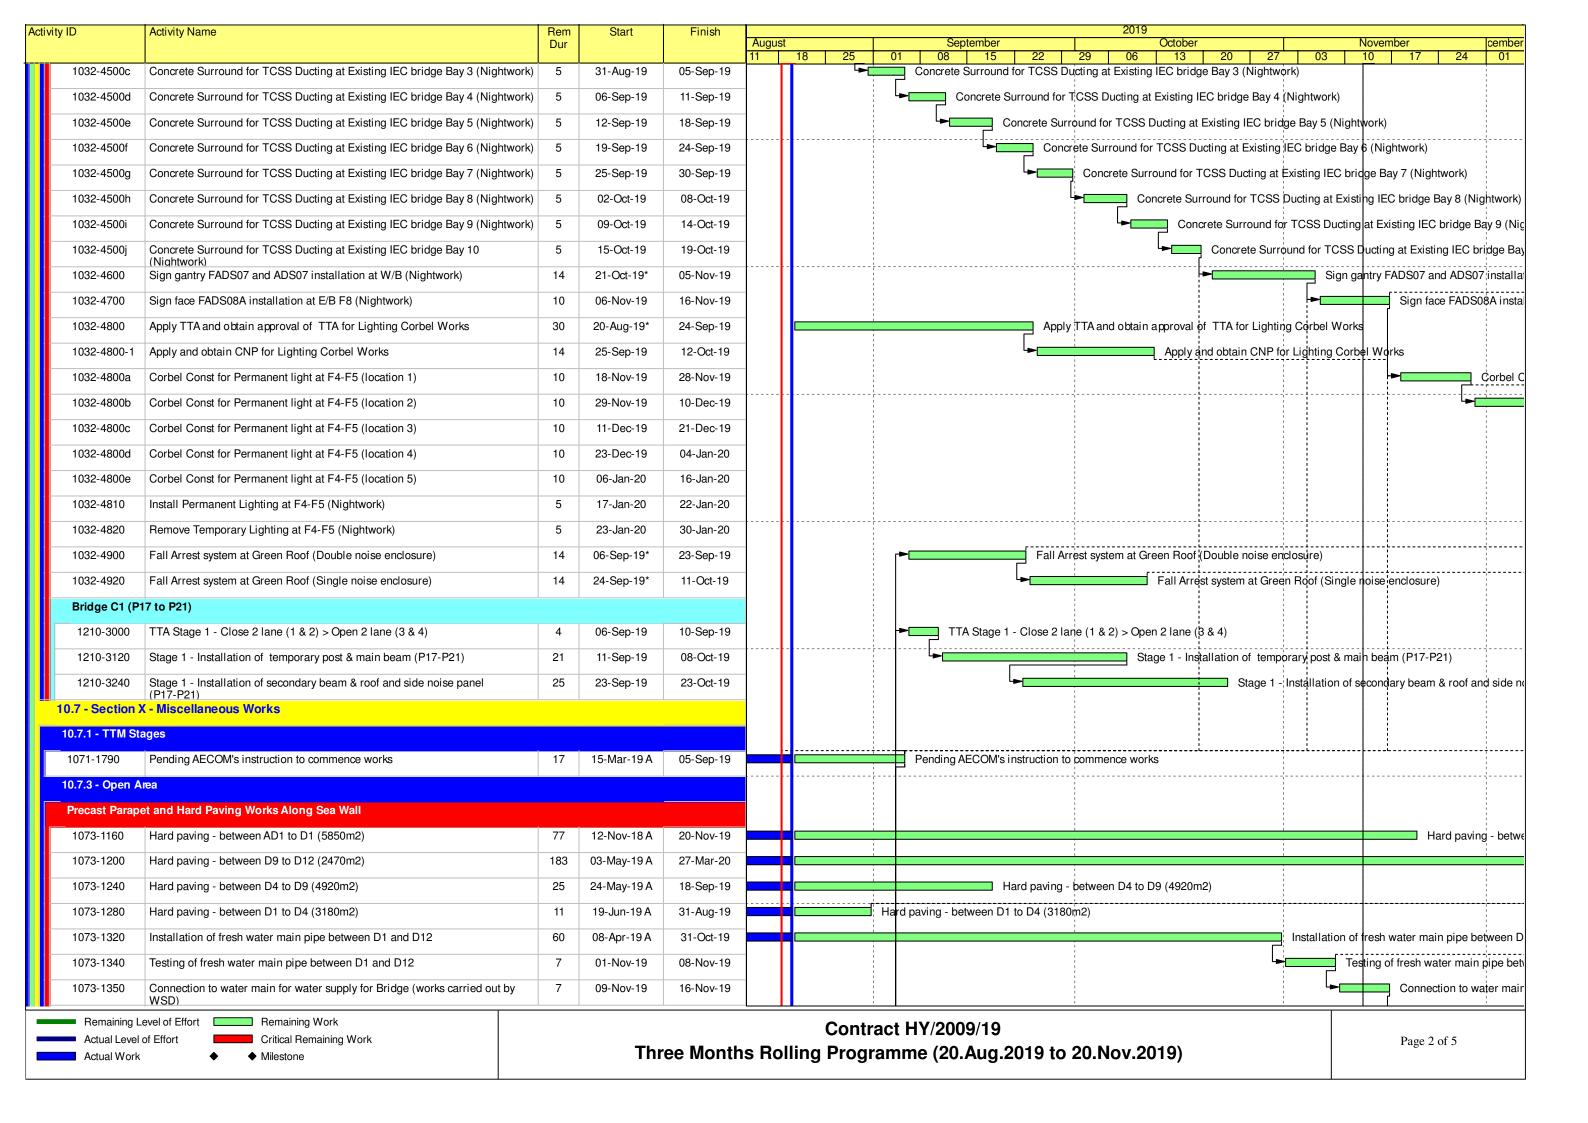

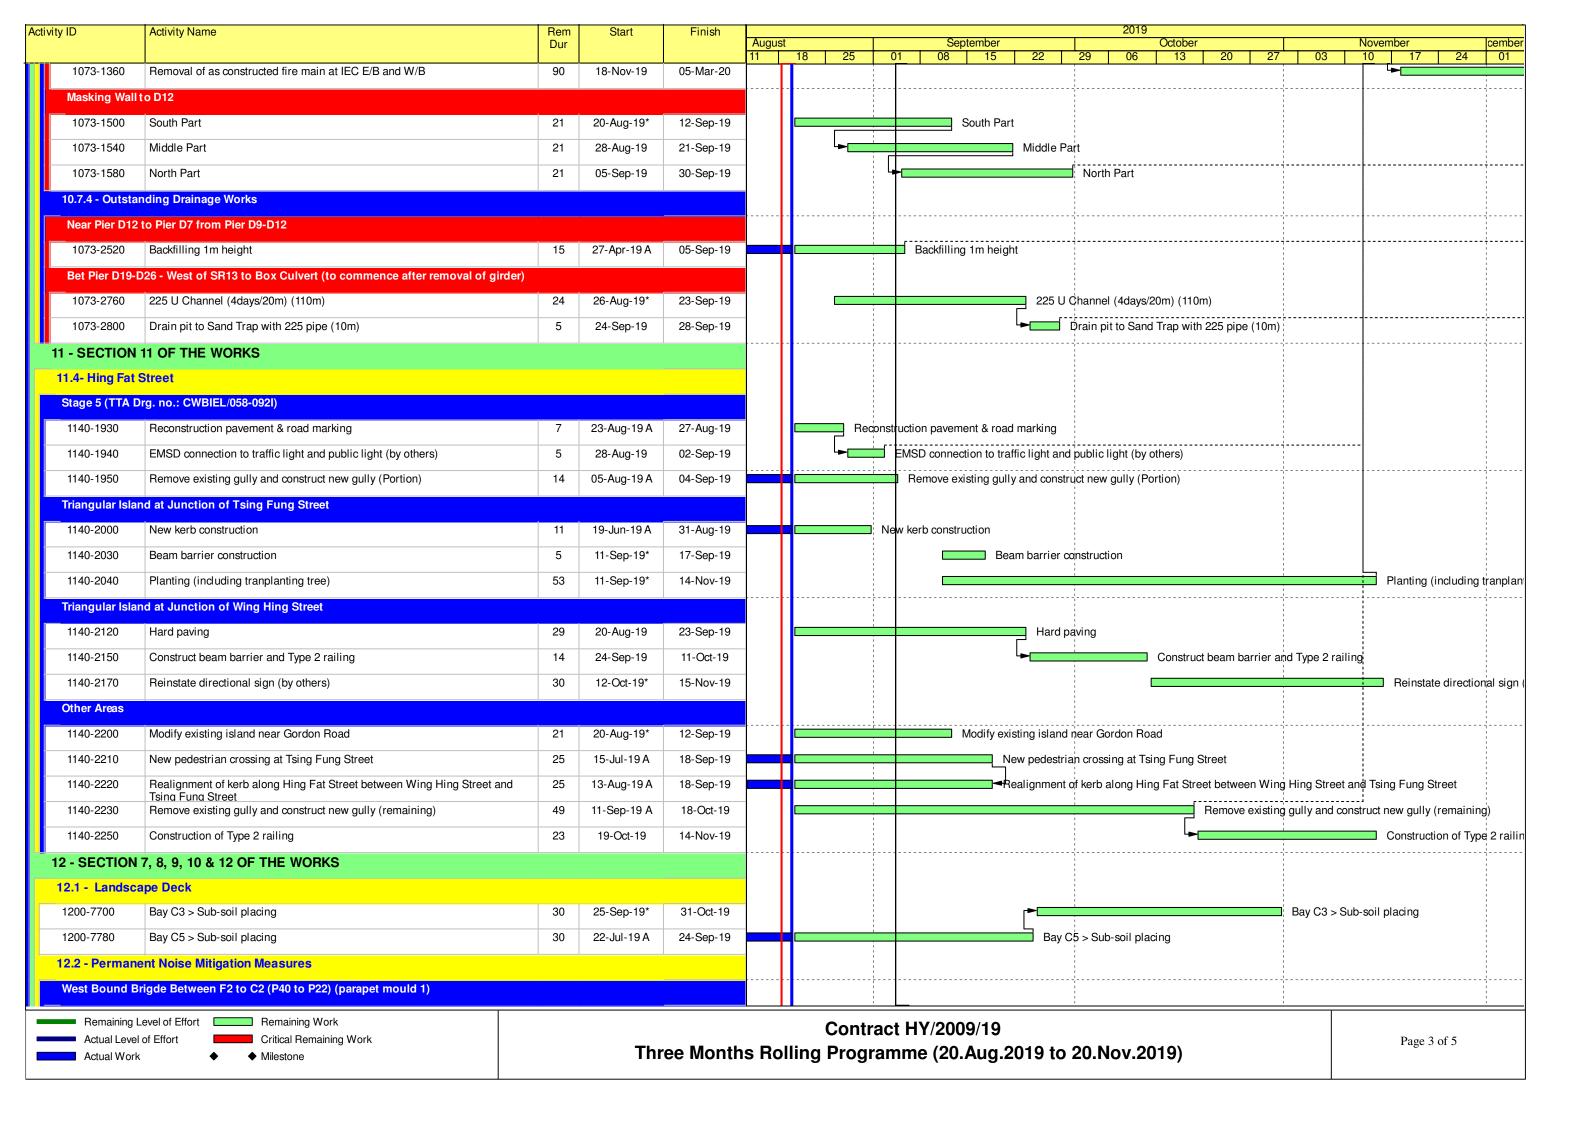


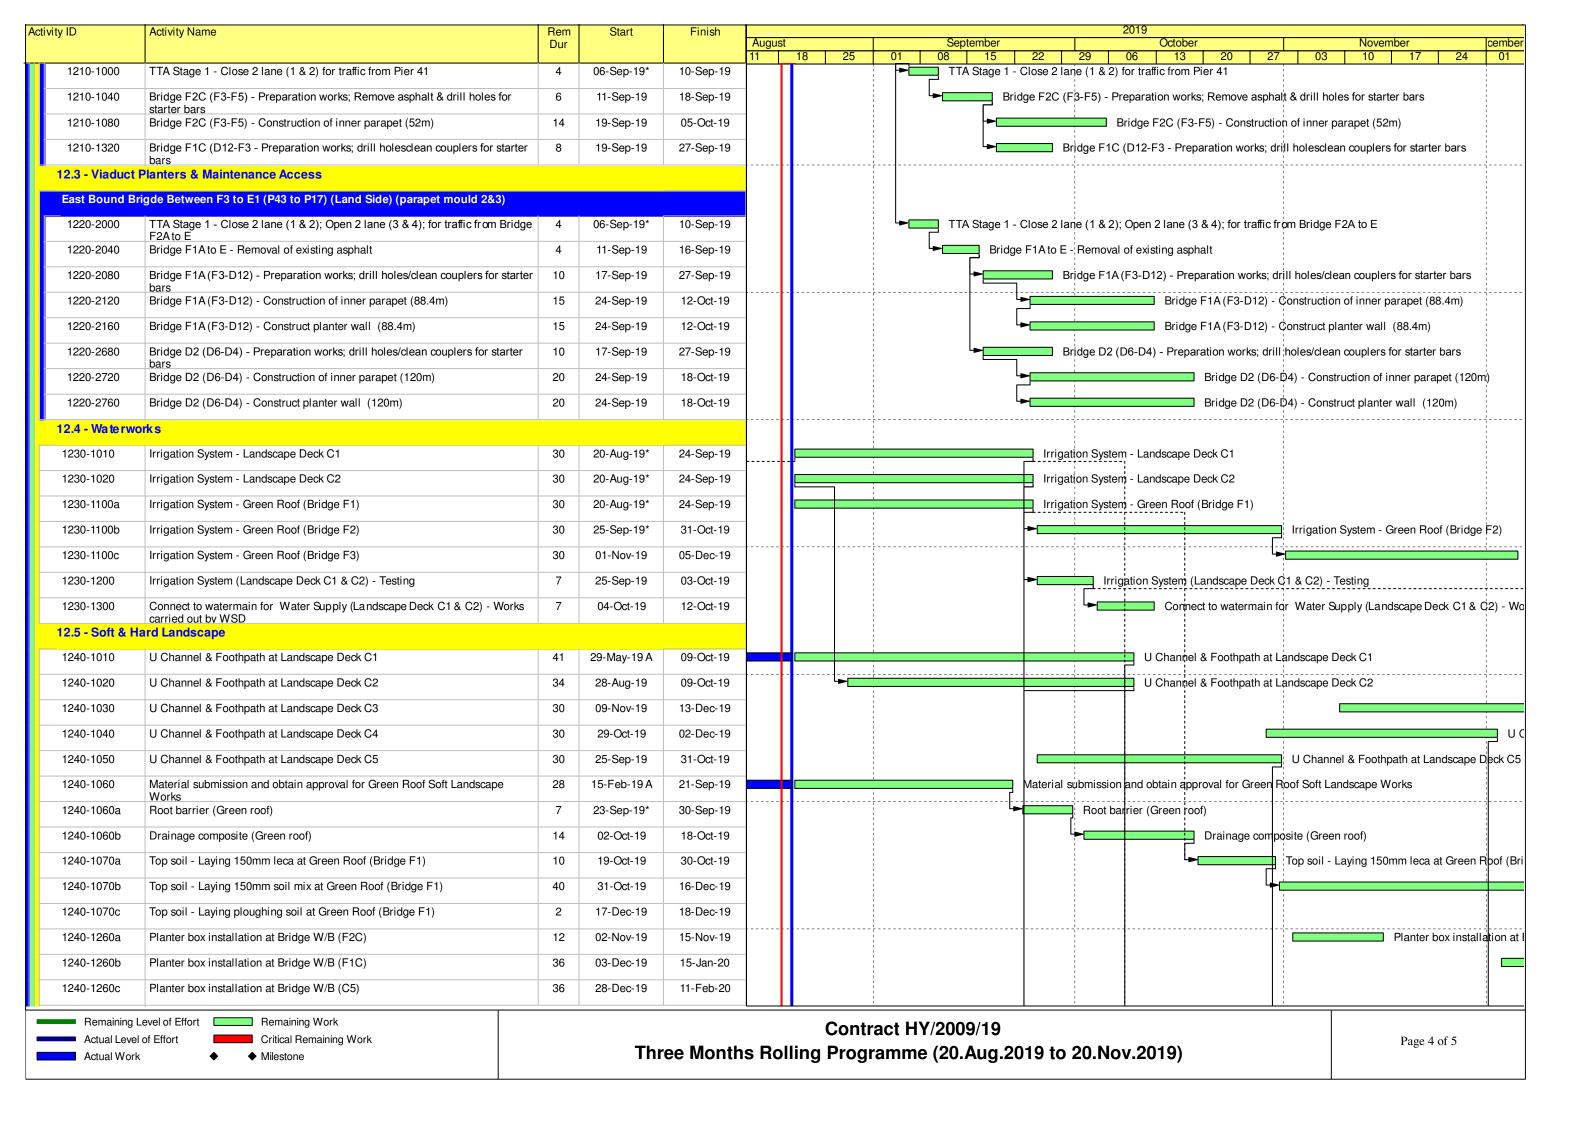

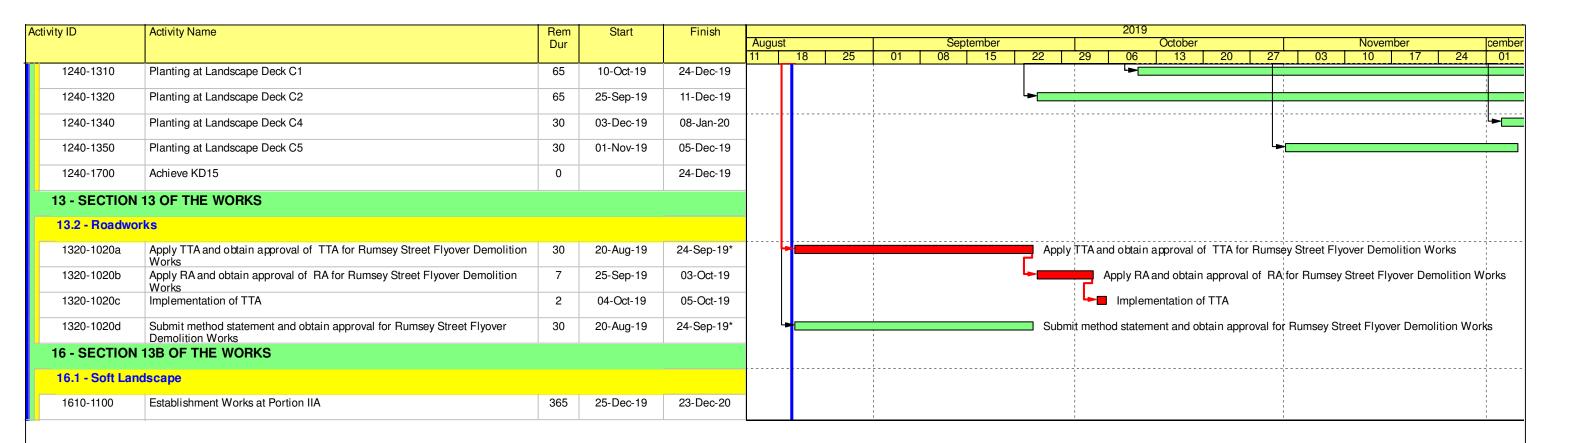

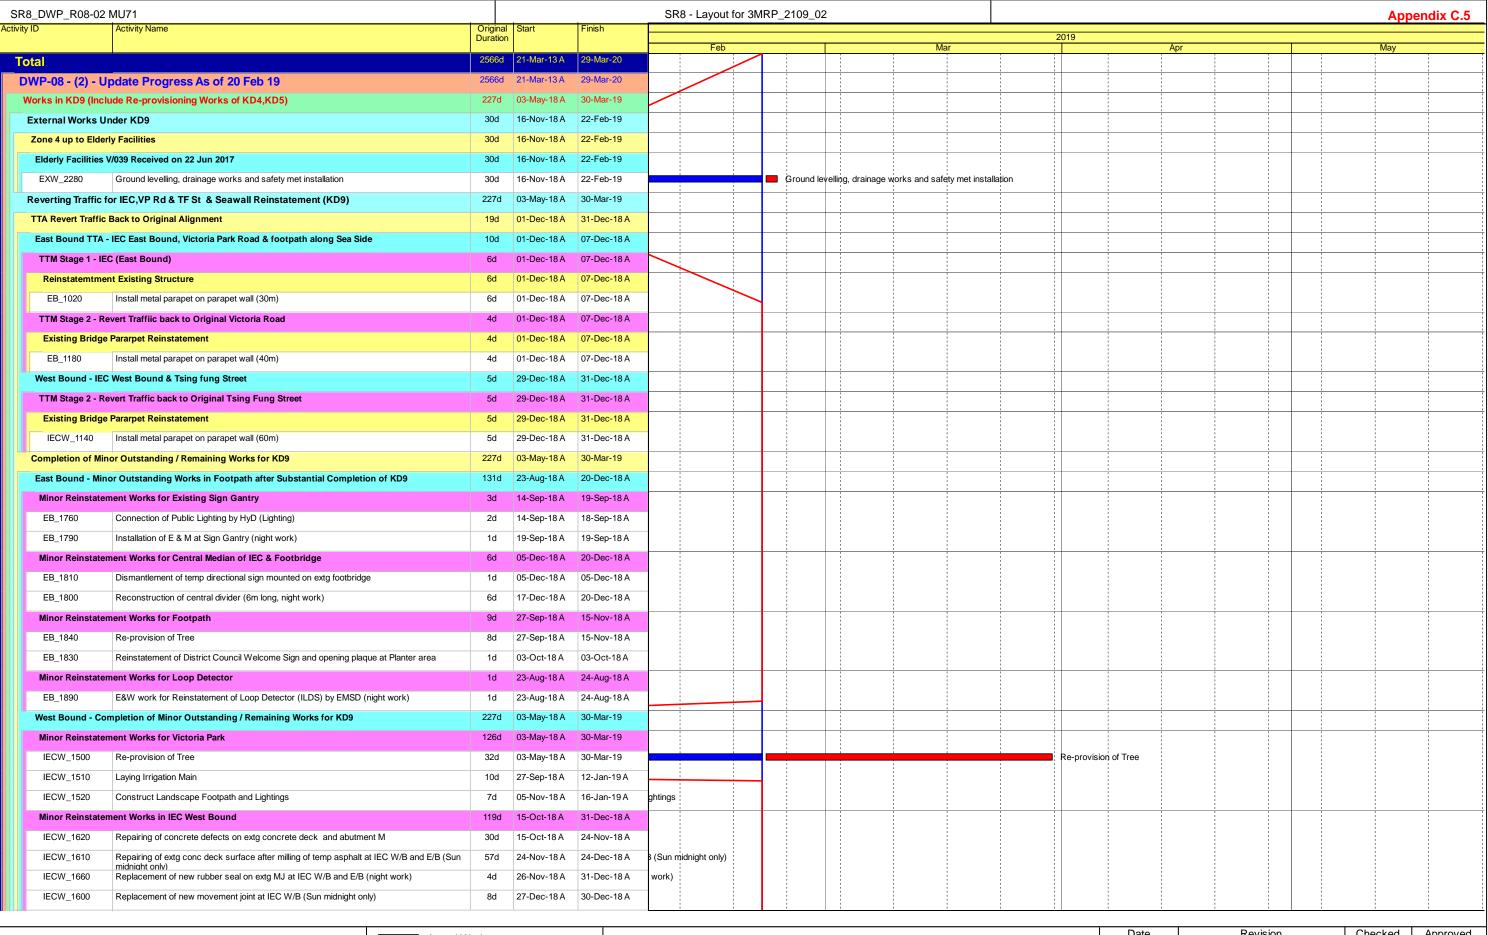






Page 1 of 2

Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel (Slip Road 8 Section) - 3 Months Rolling Progamme

Date	Revision	Checked	Approved
eb-19	DWP-08 (2) - 3 Months Rolling	TL	TL

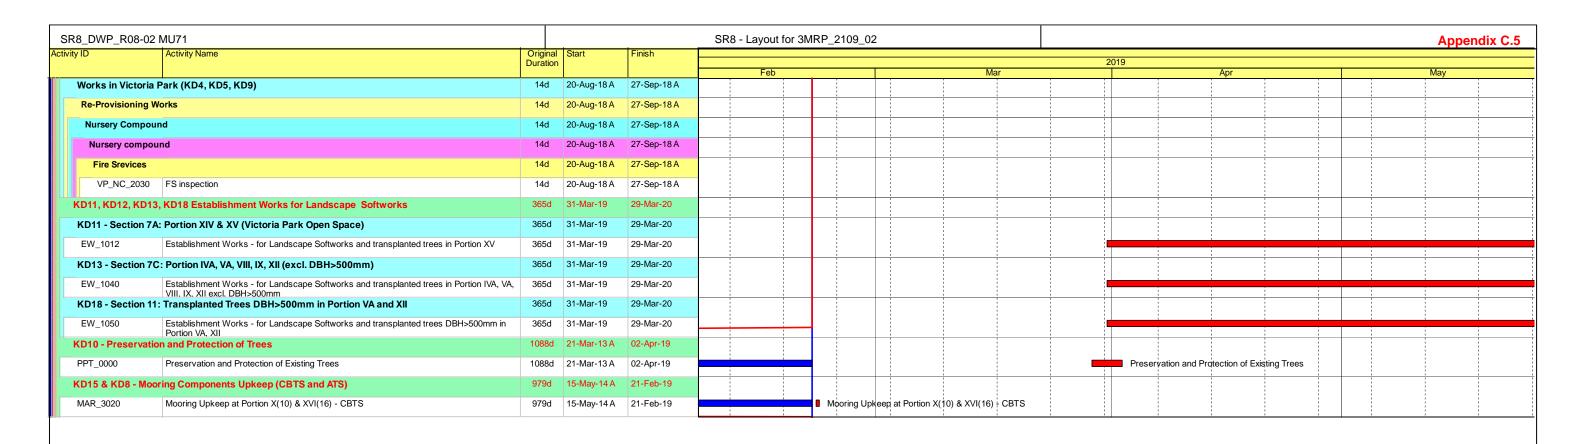



Page 2 of 2

Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel (Slip Road 8 Section) - 3 Months Rolling Progamme

Date	Revision	Checked	Approved
:0-Feb-19	DWP-08 (2) - 3 Months Rolling	TL	TL

SR8_DWP_R08-02 MU77					SR8 - Layout for 3MRP_2109_	08	Appendix						
ctivity ID	Activity Name	Original Duration		Finish			2019						
					Aug	Sep		Oct	Nov				
Total		385	21-Mar-19 A	02-Apr-20									
DWP-08 - (2)	- Update Progress As of 20 Aug 19	385	21-Mar-19 A	02-Apr-20									
KD11, KD12, KD	013, KD18 Establishment Works for Landscape Softworks	385	21-Mar-19 A	02-Apr-20									
KD11 - Section	n 7A: Portion XIV & XV (Victoria Park Open Space)	365	21-Mar-19 A	29-Jan-20									
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365	21-Mar-19 A	29-Jan-20									
KD13 - Section	n 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH>500mm)	365	21-Mar-19 A	02-Apr-20									
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365	21-Mar-19 A	02-Apr-20									
KD18 - Section	n 11: Transplanted Trees DBH>500mm in Portion VA and XII	365	21-Mar-19 A	02-Apr-20									
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365	21-Mar-19 A	02-Apr-20									

Actual Work

Remaining Work


Critical Remaining Work


Milestone

Page 1 of 1

Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel (Slip Road 8 Section) - 3 Months Rolling Progamme

Date	Revision	Checked	Approved
0-Aug-19	DWP-08 (2) - 3 Months Rolling	TL	TL

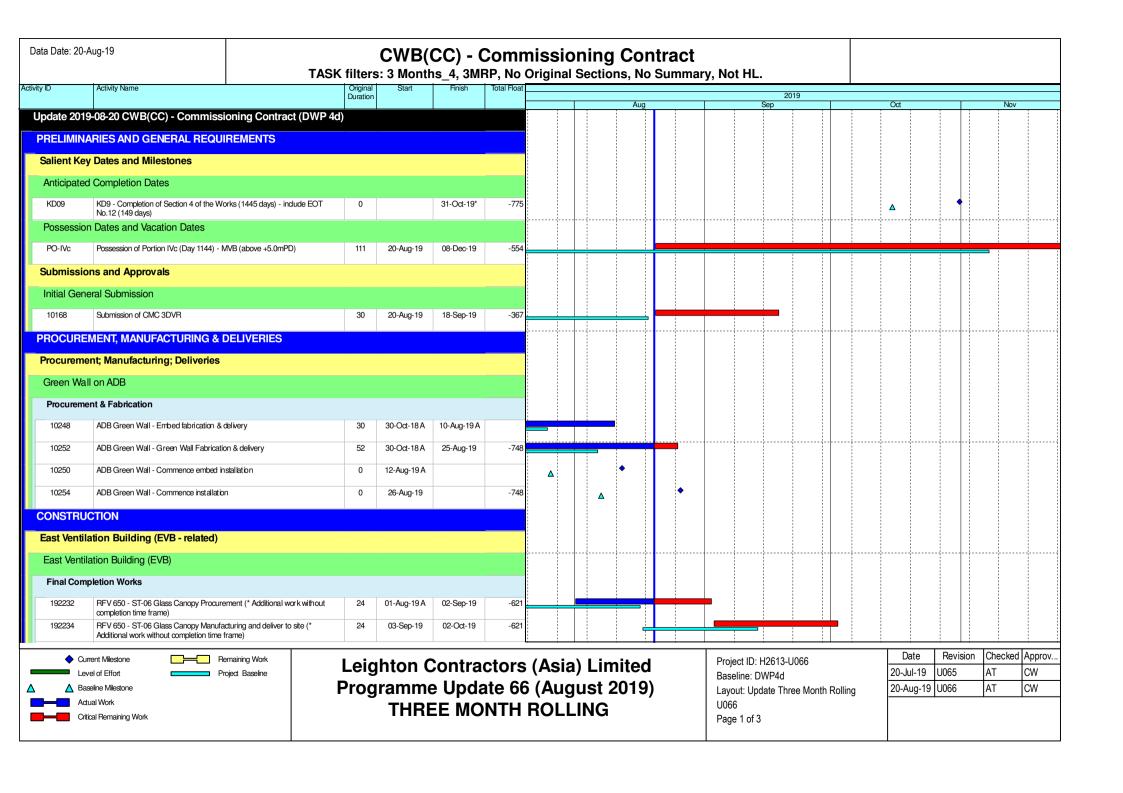

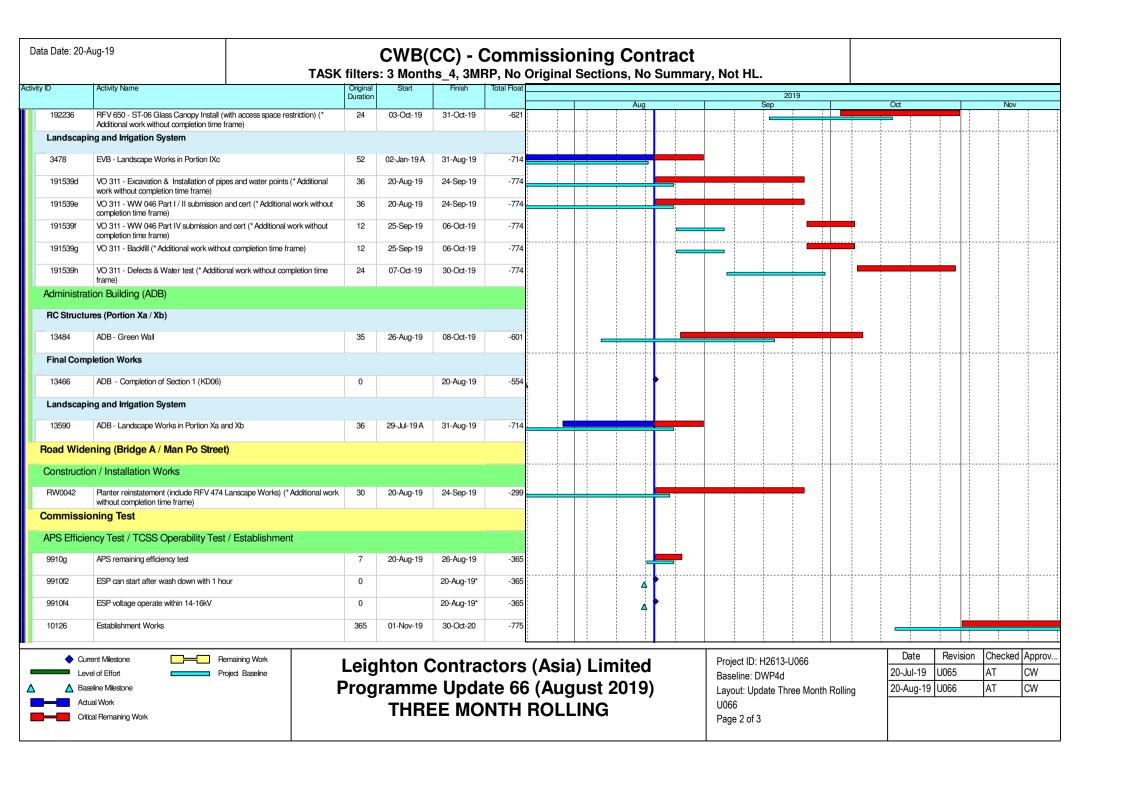

Data Date: 20-Aug-19

CWB(CC) - Commissioning Contract

Activity ID	Activity Name	Original	Start	Finish	Total Float																
-		Duration											2019								
								A	ug			Sep				Oct				Nov	
Training / Plan / Manual / As-Built Drawings for Project Completion																					
	,					1		-		1 1		1	-				1 1				- 11
192114	As Duilt Drawings automission	0		20-Aug-19*	-337	1	1			1		1	1		1	1	1 1				1
192114	As-Built Drawings submission	U		20-Aug-19	-337	ķ į			1	1 1	i			i I							- 11
						1		!				!		:L	!		. 1 1				
10226	Routine Maintenance Records / Maintenance Monthly Report	0	01-Nov-19		-410	i i	1			1 1		i		1	- 1		1 1	>			- 11
,						1				1	- 1	1	1	1	1	; A	1 1	1.1			- 11
						:	- 1		- ;	-		i	- 1		i	- 1	1 1				- 1



Leighton Contractors (Asia) Limited Programme Update 66 (August 2019) THREE MONTH ROLLING Project ID: H2613-U066
Baseline: DWP4d
Layout: Update Three Month Rolling

Layout. Opuate	THIER MOHULI KO
U066	
Page 3 of 3	

Date	Revision	Checked	Approv
20-Jul-19	U065	AT	CW
20-Aug-19	U066	AT	CW
