


Programme for Outstanding and Defective Works

ID	Task Name	Duration	Start	Finish	2019																															
					July 2019							August 2019							September 2019							October 2019										
					14	17	20	23	26	29	1	4	7	10	13	16	19	22	25	28	31	3	6	9	12	15	18	21	24	27	30	3	6	9	12	15
1	15. Reinstatement of Hung Hing Road and Wan Shing Street in Accordance to Hung Hing Road Traffic Diversion Reinstatement Stage 0.5 Scheme Under VO No. 257 on Hung Hing Road	248 days	Fri 1/3/19	Sun 3/11/19																																
2	Phase 1 (Completed)	41 days	Fri 1/3/19	Wed 10/4/19																																
55	Phase 2 (Completed)	41 days	Tue 2/4/19	Sun 12/5/19																																
169	Yacht Club (40m Long)	43 days	Fri 15/3/19	Fri 26/4/19																																
182	Triangle Island (40m Long)	28 days	Fri 31/5/19	Thu 27/6/19																																
194	Phase 3	144 days	Thu 13/6/19	Sun 3/11/19																																
195	Advacne Work	35 days	Thu 13/6/19	Wed 17/7/19																																
200	Construction of Road Kerb and Pavement (Portion 5)	23 days	Thu 18/7/19	Fri 9/8/19																																
201	TTA Implementation	1 day	Thu 18/7/19	Thu 18/7/19																																
202	Demolition of Concrete and Asphalt Pavement	4 days	Fri 19/7/19	Mon 22/7/19																																
203	Removal of Steel Plate	4 days	Tue 23/7/19	Fri 26/7/19																																
204	Installation of Kerb	2 days	Sat 27/7/19	Sun 28/7/19																																
205	Subbase Levelling	1 day	Mon 29/7/19	Mon 29/7/19																																
206	SRT for Sub-base	5 days	Tue 30/7/19	Sat 3/8/19																																
207	Concrete Laying	1 day	Sun 4/8/19	Sun 4/8/19																																
208	Concrete Curing	3 days	Mon 5/8/19	Wed 7/8/19																																
209	Existing Asphalt Patch Up Work at Water Ponding Area (Photo 3, 4 & 5, Figure 211) (Concurrent with ID 669)	2 days	Thu 8/8/19	Fri 9/8/19																																
210	Demolition of water ponding area	1 day	Thu 8/8/19	Thu 8/8/19																																
211	Patching Up with Asphalt layer	1 day	Fri 9/8/19	Fri 9/8/19																																
212	Construction of Road Kerb and Pavement (Portion 4)	30 days	Fri 2/8/19	Sat 31/8/19																																
213	TTA Implementation	1 day	Sat 10/8/19	Sat 10/8/19																																
214	Demolition of Concrete and Asphalt Pavement	4 days	Sun 11/8/19	Wed 14/8/19																																
215	Removal of Steel Plate	4 days	Thu 15/8/19	Sun 18/8/19																																
216	Installation of Kerb	1 day	Mon 19/8/19	Mon 19/8/19																																
217	Subbase Levelling	1 day	Tue 20/8/19	Tue 20/8/19																																
218	SRT for Sub-base	5 days	Wed 21/8/19	Sun 25/8/19																																
219	Concrete Laying	1 day	Mon 26/8/19	Mon 26/8/19																																
220	Concrete Curing	3 days	Tue 27/8/19	Thu 29/8/19																																
221	Existing Asphalt Patch Up Work at Water Ponding Area (Photo 1, Figure 212)	2 days	Fri 30/8/19	Sat 31/8/19																																
224	Repaving Works at Yacht Club (Photo 2, Figure 216-1), Same as	30 days	Fri 2/8/19	Sat 31/8/19																																
231	Construction of Trial Pit and Installation of decking (Portion 3)	21 days	Mon 2/9/19	Sun 22/9/19																																
232	TTA Implementation	1 day	Mon 2/9/19	Mon 2/9/19																																
233	Demolition of Concrete and Asphalt Pavement	4 days	Tue 3/9/19	Fri 6/9/19																																
234	Removal of Steel Plate and installation of ELS for waterpipe	4 days	Sat 7/9/19	Tue 10/9/19																																
235	Kerb Installation and installation of decking	2 days	Wed 11/9/19	Thu 12/9/19																																
236	Subbase Levelling	1 day	Fri 13/9/19	Fri 13/9/19																																
237	SRT for Sub-base	5 days	Sat 14/9/19	Wed 18/9/19																																
238	Concrete Laying	1 day	Thu 19/9/19	Thu 19/9/19																																
239	Concrete Curing	3 days	Fri 20/9/19	Sun 22/9/19																																
240	Construction of Road Kerb and Pavement (Portion 2)	21 days	Mon 23/9/19	Sun 13/10/19																																
249	Construction of Road Kerb and Pavement (Portion 1)	21 days	Mon 14/10/19	Sun 3/11/19																																
258	Phase 3.5 (Remaining Works for HHR0.5 Scheme & Cable Duct Laying)	69 days	Tue 14/5/19	Sun 21/7/19																																
259	Construction of Footpath at HHR (Up Birdge)	11 days	Fri 31/5/19	Mon 10/6/19																																

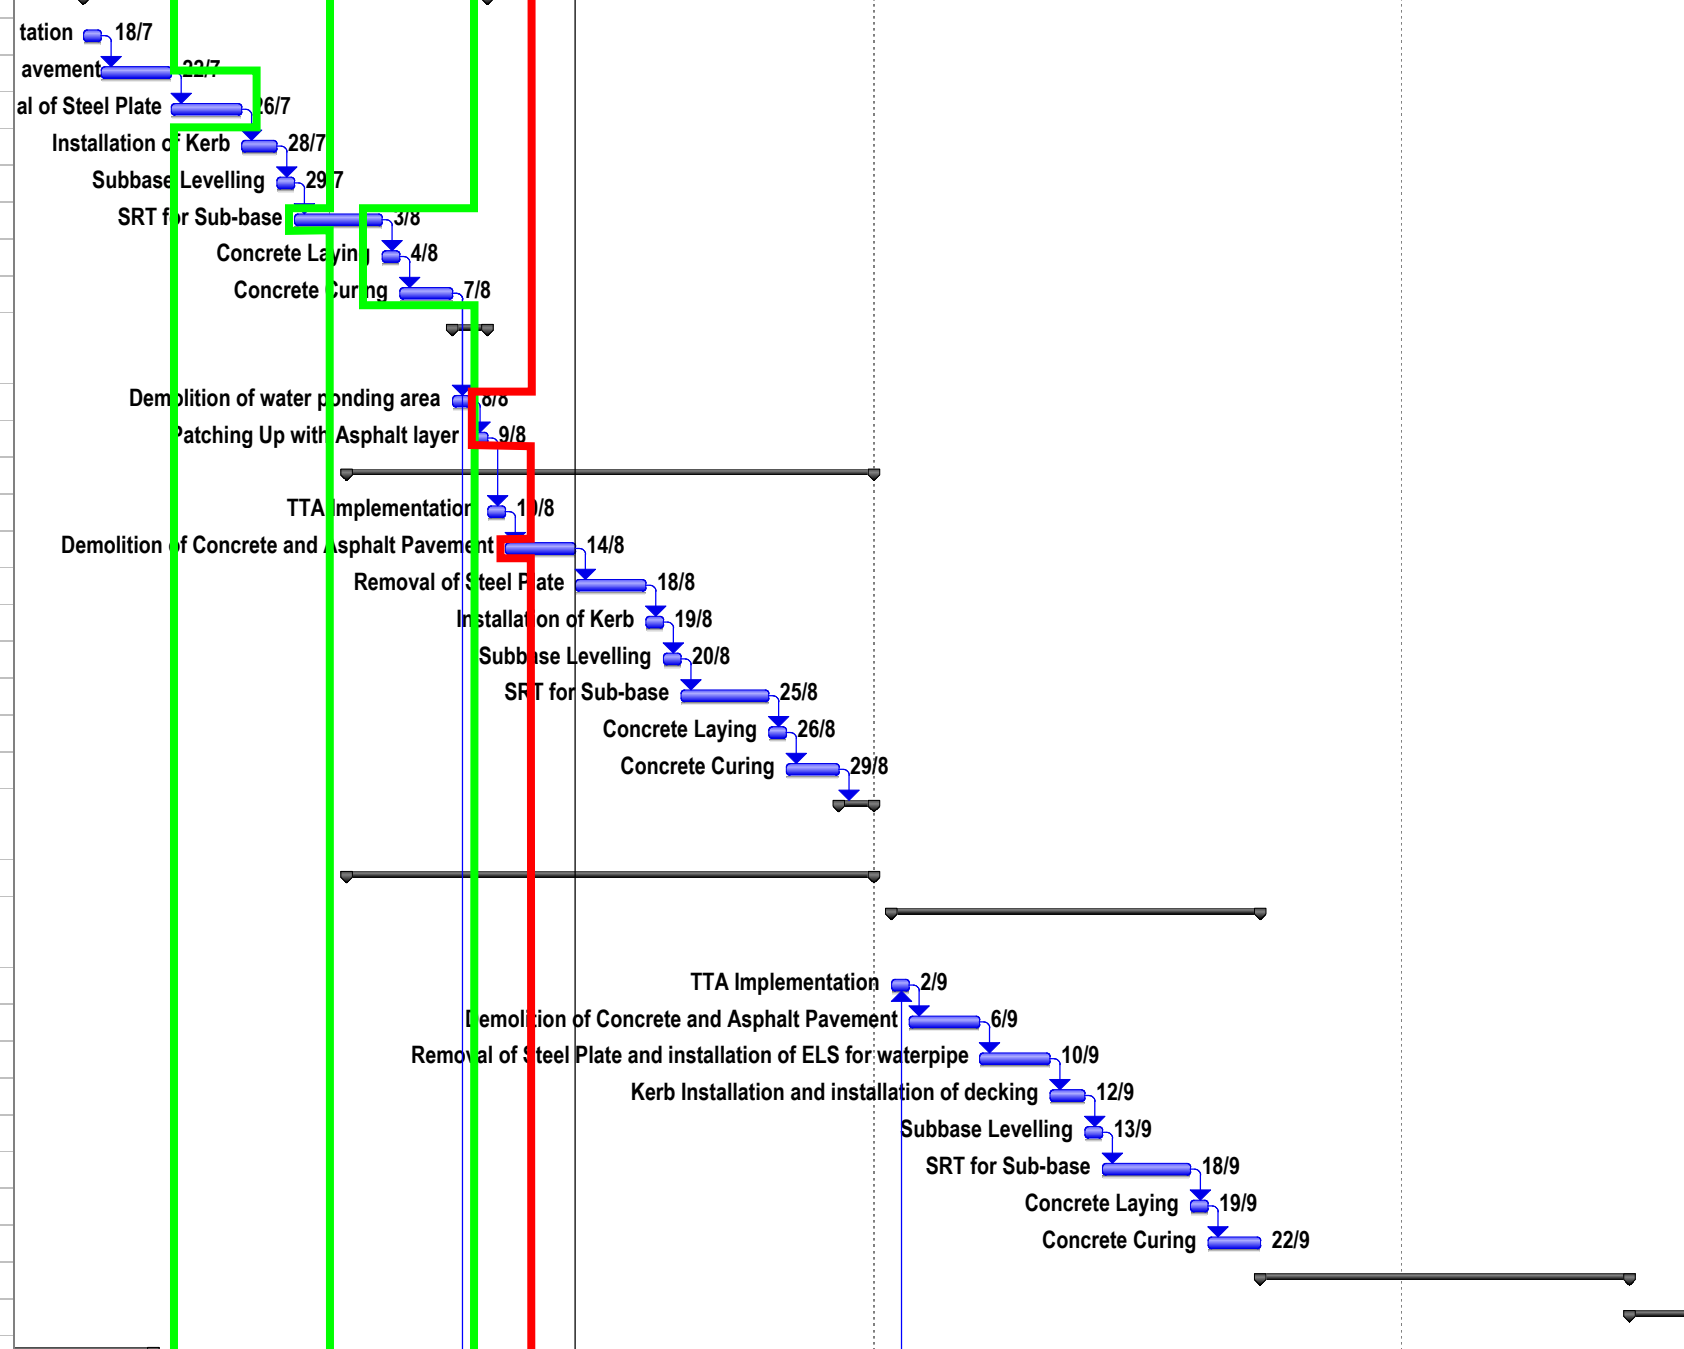

Task Milestone Rolled Up Task Rolled Up Progress External Tasks Group By Summary

Progress Summary Rolled Up Milestone Split Project Summary Deadline

Programme for Outstanding and Defective Works

ID	Task Name	Duration	Start	Finish	Qtr 3, 2019																														
					July 2019							August 2019							September 2019							October 2019									
387	Backfilling of Subbase Level and SRT	8 days	Tue 30/7/19	Tue 6/8/19	g of Subbase Level and SRT																														
388	RB Laying	1 day	Wed 7/8/19	Wed 7/8/19	RB Laying																														
389	BC Laying	1 day	Thu 8/8/19	Thu 8/8/19	BC Laying																														
390	WC Laying	1 day	Fri 9/8/19	Fri 9/8/19	WC Laying																														
391	Construction of Cross road duct (Opposite to SPCA)	85 days	Fri 17/5/19	Fri 9/8/19																															
392	Endorsement of TTA Drawing (Notional)	57 days	Fri 17/5/19	Fri 12/7/19	2/7																														
393	Application Road Work Advise	7 days	Sat 13/7/19	Fri 19/7/19	19/7																														
394	TTA Implementation	1 day	Sat 20/7/19	Sat 20/7/19	20/7																														
395	Demolition and Removal of Asphalt and Concrete Surface	5 days	Sun 21/7/19	Thu 25/7/19	25/7																														
396	Excavation for PVC duct laying	3 days	Fri 26/7/19	Sun 28/7/19	28/7																														
397	Duct Laying	2 days	Mon 29/7/19	Tue 30/7/19	30/7																														
398	Backfilling to Formaiton Level	1 day	Wed 31/7/19	Wed 31/7/19	31/7																														
399	Backfilling of Subbase Level and SRT	7 days	Thu 1/8/19	Wed 7/8/19	7/8																														
400	RB Laying	1 day	Thu 8/8/19	Thu 8/8/19	8/8																														
401	BC Laying	1 day	Fri 9/8/19	Fri 9/8/19	9/8																														
402	Construction of cross road duct (Bus Lane)	73 days	Fri 31/5/19	Sun 11/8/19																															
403	Endorsement of TTA Drawing	22 days	Fri 31/5/19	Fri 21/6/19																															
404	Application Road Work Advise	7 days	Sat 22/6/19	Fri 28/6/19																															
405	Cross road duct at Bus Lane (Northern Portion)	19 days	Fri 5/7/19	Tue 23/7/19																															
406	TTA Implementation	1 day	Fri 5/7/19	Fri 5/7/19																															
407	Demolition and Removal of Asphalt Surface	2 days	Sat 6/7/19	Sun 7/7/19																															
408	Excavation for PVC duct laying	3 days	Mon 8/7/19	Wed 10/7/19																															
409	Duct Laying	1 day	Thu 11/7/19	Thu 11/7/19																															
410	Backfilling to Formaiton Level	1 day	Fri 12/7/19	Fri 12/7/19																															
411	Backfilling of Subbase Level and SRT	8 days	Sat 13/7/19	Sat 20/7/19	20/7																														
412	RB Laying	1 day	Sun 21/7/19	Sun 21/7/19	21/7																														
413	BC Laying	1 day	Mon 22/7/19	Mon 22/7/19	22/7																														
414	WC Laying	1 day	Tue 23/7/19	Tue 23/7/19	23/7																														
415	Cross road duct at Bus Lane (Southern Portion)	19 days	Wed 24/7/19	Sun 11/8/19																															
416	TTA Implementation	1 day	Wed 24/7/19	Wed 24/7/19	24/7																														
417	Demolition and Removal of Asphalt Surface	2 days	Thu 25/7/19	Fri 26/7/19	26/7																														
418	Excavation for PVC duct laying	3 days	Sat 27/7/19	Mon 29/7/19	29/7																														
419	Duct Laying	1 day	Tue 30/7/19	Tue 30/7/19	30/7																														
420	Backfilling to Formaiton Level	1 day	Wed 31/7/19	Wed 31/7/19	31/7																														
421	Backfilling of Subbase Level and SRT	8 days	Thu 1/8/19	Thu 8/8/19	8/8																														
422	Road Base Laying	1 day	Fri 9/8/19	Fri 9/8/19	9/8																														
423	BC Laying	1 day	Sat 10/8/19	Sat 10/8/19	10/8																														
424	WC Laying	1 day	Sun 11/8/19	Sun 11/8/19	11/8																														
425	Construction of Cross road duct (EVA Access)	115 days	Fri 17/5/19	Sun 8/9/19																															
426	Endorsement of TTA Drawing	22 days	Fri 17/5/19	Fri 7/6/19																															
427	Application Road Work Advise	7 days	Sat 8/6/19	Fri 14/6/19																															
428	Seeking Permission from FSD for Enclosure of EVA access	27 days	Sat 8/6/19	Thu 4/7/19																															
429	Run-in at EVA (Eastern Portion)	16 days	Thu 8/8/19	Fri 23/8/19																															
430	TTA Implementation	1 day	Thu 8/8/19	Thu 8/8/19	8/8																														
431	Demolition and Removal of Asphalt Surface	1 day	Fri 9/8/19	Fri 9/8/19	9/8																														
432	Excavation for PVC duct laying	1 day	Sat 10/8/19	Sat 10/8/19	10/8																														
433	Duct Laying	1 day	Sun 11/8/19	Sun 11/8/19	11/8																														
434	Backfilling to Formaiton Level	1 day	Mon 12/8/19	Mon 12/8/19	12/8																														

Task Milestone Rolled Up Task Rolled Up Progress External Tasks Group By Summary


Progress Summary Rolled Up Milestone Split Project Summary Deadline



Programme for Outstanding and Defective Works

ID	Task Name	Duration	Start	Finish	Qtr 3, 2019																															
					July 2019							August 2019							September 2019							October 2019										
					14	17	20	23	26	29	1	4	7	10	13	16	19	22	25	28	31	3	6	9	12	15	18	21	24	27	30	3	6	9	12	15
435	Backfilling of Subbase Level and SRT	8 days	Tue 13/8/19	Tue 20/8/19	Backfilling of Subbase Level and SRT																															
436	RB Laying	1 day	Wed 21/8/19	Wed 21/8/19	RB Laying																															
437	BC Laying	1 day	Thu 22/8/19	Thu 22/8/19	BC Laying																															
438	WC Laying	1 day	Fri 23/8/19	Fri 23/8/19	WC Laying																															
439	Run-in at EVA (Western Portion)	16 days	Sat 24/8/19	Sun 8/9/19	Run-in at EVA (Western Portion)																															
440	TTA Implementation	1 day	Sat 24/8/19	Sat 24/8/19	TTA Implementation																															
441	Demolition and Removal of Asphalt Surface	1 day	Sun 25/8/19	Sun 25/8/19	Demolition and Removal of Asphalt Surface																															
442	Excavation for PVC duct laying	1 day	Mon 26/8/19	Mon 26/8/19	Excavation for PVC duct laying																															
443	Duct Laying	1 day	Tue 27/8/19	Tue 27/8/19	Duct Laying																															
444	Backfilling to Formaiton Level	1 day	Wed 28/8/19	Wed 28/8/19	Backfilling to Formaiton Level																															
445	Backfilling of Subbase Level and SRT	8 days	Thu 29/8/19	Thu 5/9/19	Backfilling of Subbase Level and SRT																															
446	RB Laying	1 day	Fri 6/9/19	Fri 6/9/19	RB Laying																															
447	BC Laying	1 day	Sat 7/9/19	Sat 7/9/19	BC Laying																															
448	WC Laying	1 day	Sun 8/9/19	Sun 8/9/19	WC Laying																															
449	Construction of Lighting Cable Duct (Yacht Club)	10 days	Mon 4/11/19	Wed 13/11/19	Construction of Lighting Cable Duct (Yacht Club)																															
450	TTA Implementation	1 day	Mon 4/11/19	Mon 4/11/19	TTA Implementation																															
451	Demolition of Concrete Pavement	2 days	Tue 5/11/19	Wed 6/11/19	Demolition of Concrete Pavement																															
452	PVC Duct Laying	1 day	Thu 7/11/19	Thu 7/11/19	PVC Duct Laying																															
453	Backfilling of Trench	1 day	Fri 8/11/19	Fri 8/11/19	Backfilling of Trench																															
454	Subbase Laying and SRT	4 days	Sat 9/11/19	Tue 12/11/19	Subbase Laying and SRT																															
455	Concrete Laying	1 day	Wed 13/11/19	Wed 13/11/19	Concrete Laying																															
456	Installation of Lamp Post (West of Triangular Island) (8 nos.)	26 days	Sat 10/8/19	Wed 4/9/19	Installation of Lamp Post (West of Triangular Island) (8 nos.)																															
457	Inspection of laid cable duct by Hyd	7 days	Sat 10/8/19	Fri 16/8/19	Inspection of laid cable duct by Hyd																															
458	Preparation work by Hyd Lighting Division for instllation of Lamp Post (8 nos.)	14 days	Sat 17/8/19	Fri 30/8/19	Preparation work by Hyd Lighting Division for instllation of Lamp Post (8 nos.)																															
459	Installation of Lamp Post (2 nos./day)	5 days	Sat 31/8/19	Wed 4/9/19	Installation of Lamp Post (2 nos./day)																															
460	Installation of Lamp Post (East of Triangular Island to Yacht Club) (6 nos.)	26 days	Thu 14/11/19	Mon 9/12/19	Installation of Lamp Post (East of Triangular Island to Yacht Club) (6 nos.)																															
461	Inspection of laid cable duct Hyd	7 days	Thu 14/11/19	Wed 20/11/19	Inspection of laid cable duct Hyd																															
462	Preparation work by HyD Lighting Division for instllation of Lamp Post (6 nos.)	14 days	Thu 21/11/19	Wed 4/12/19	Preparation work by HyD Lighting Division for instllation of Lamp Post (6 nos.)																															
463	Installation of Lamp Post (2 nos./day)	5 days	Thu 5/12/19	Mon 9/12/19	Installation of Lamp Post (2 nos./day)																															
464	Construction Directional Sign at Triangle Island	213 days	Tue 14/5/19	Thu 12/12/19	Construction Directional Sign at Triangle Island																															
465	Advance Work	211 days	Tue 14/5/19	Tue 10/12/19	Advance Work																															
466	Submit shop drawing of traffic sign and frame to AECOM	0 days	Tue 14/5/19	Tue 14/5/19	Submit shop drawing of traffic sign and frame to AECOM																															
467	Approval of shop drawing of traffic sign and frame by AECOM	14 days	Tue 14/5/19	Mon 27/5/19	Approval of shop drawing of traffic sign and frame by AECOM																															
468	Procurement of traffic sign and frame	30 days	Tue 28/5/19	Wed 26/6/19	Procurement of traffic sign and frame																															
469	Delivery of traffic sign and frame	0 days	Wed 26/6/19	Wed 26/6/19	Delivery of traffic sign and frame																															
470	Design of footing	7 days	Thu 6/6/19	Thu 13/6/19	Design of footing																															
471	Obtain ICE certificate for footing	1 day	Thu 13/6/19	Fri 14/6/19	Obtain ICE certificate for footing																															
472	Submission to AECOM	0 days	Fri 14/6/19	Fri 14/6/19	Submission to AECOM																															
473	Approval of footing design	180 days	Fri 14/6/19	Tue 10/12/19	Approval of footing design																															
474	Site Work	168 days	Fri 28/6/19	Thu 12/12/19	Site Work																															

Task Milestone Rolled Up Task Rolled Up Progress External Tasks Group By Summary

Progress Summary Rolled Up Milestone Split Project Summary Deadline

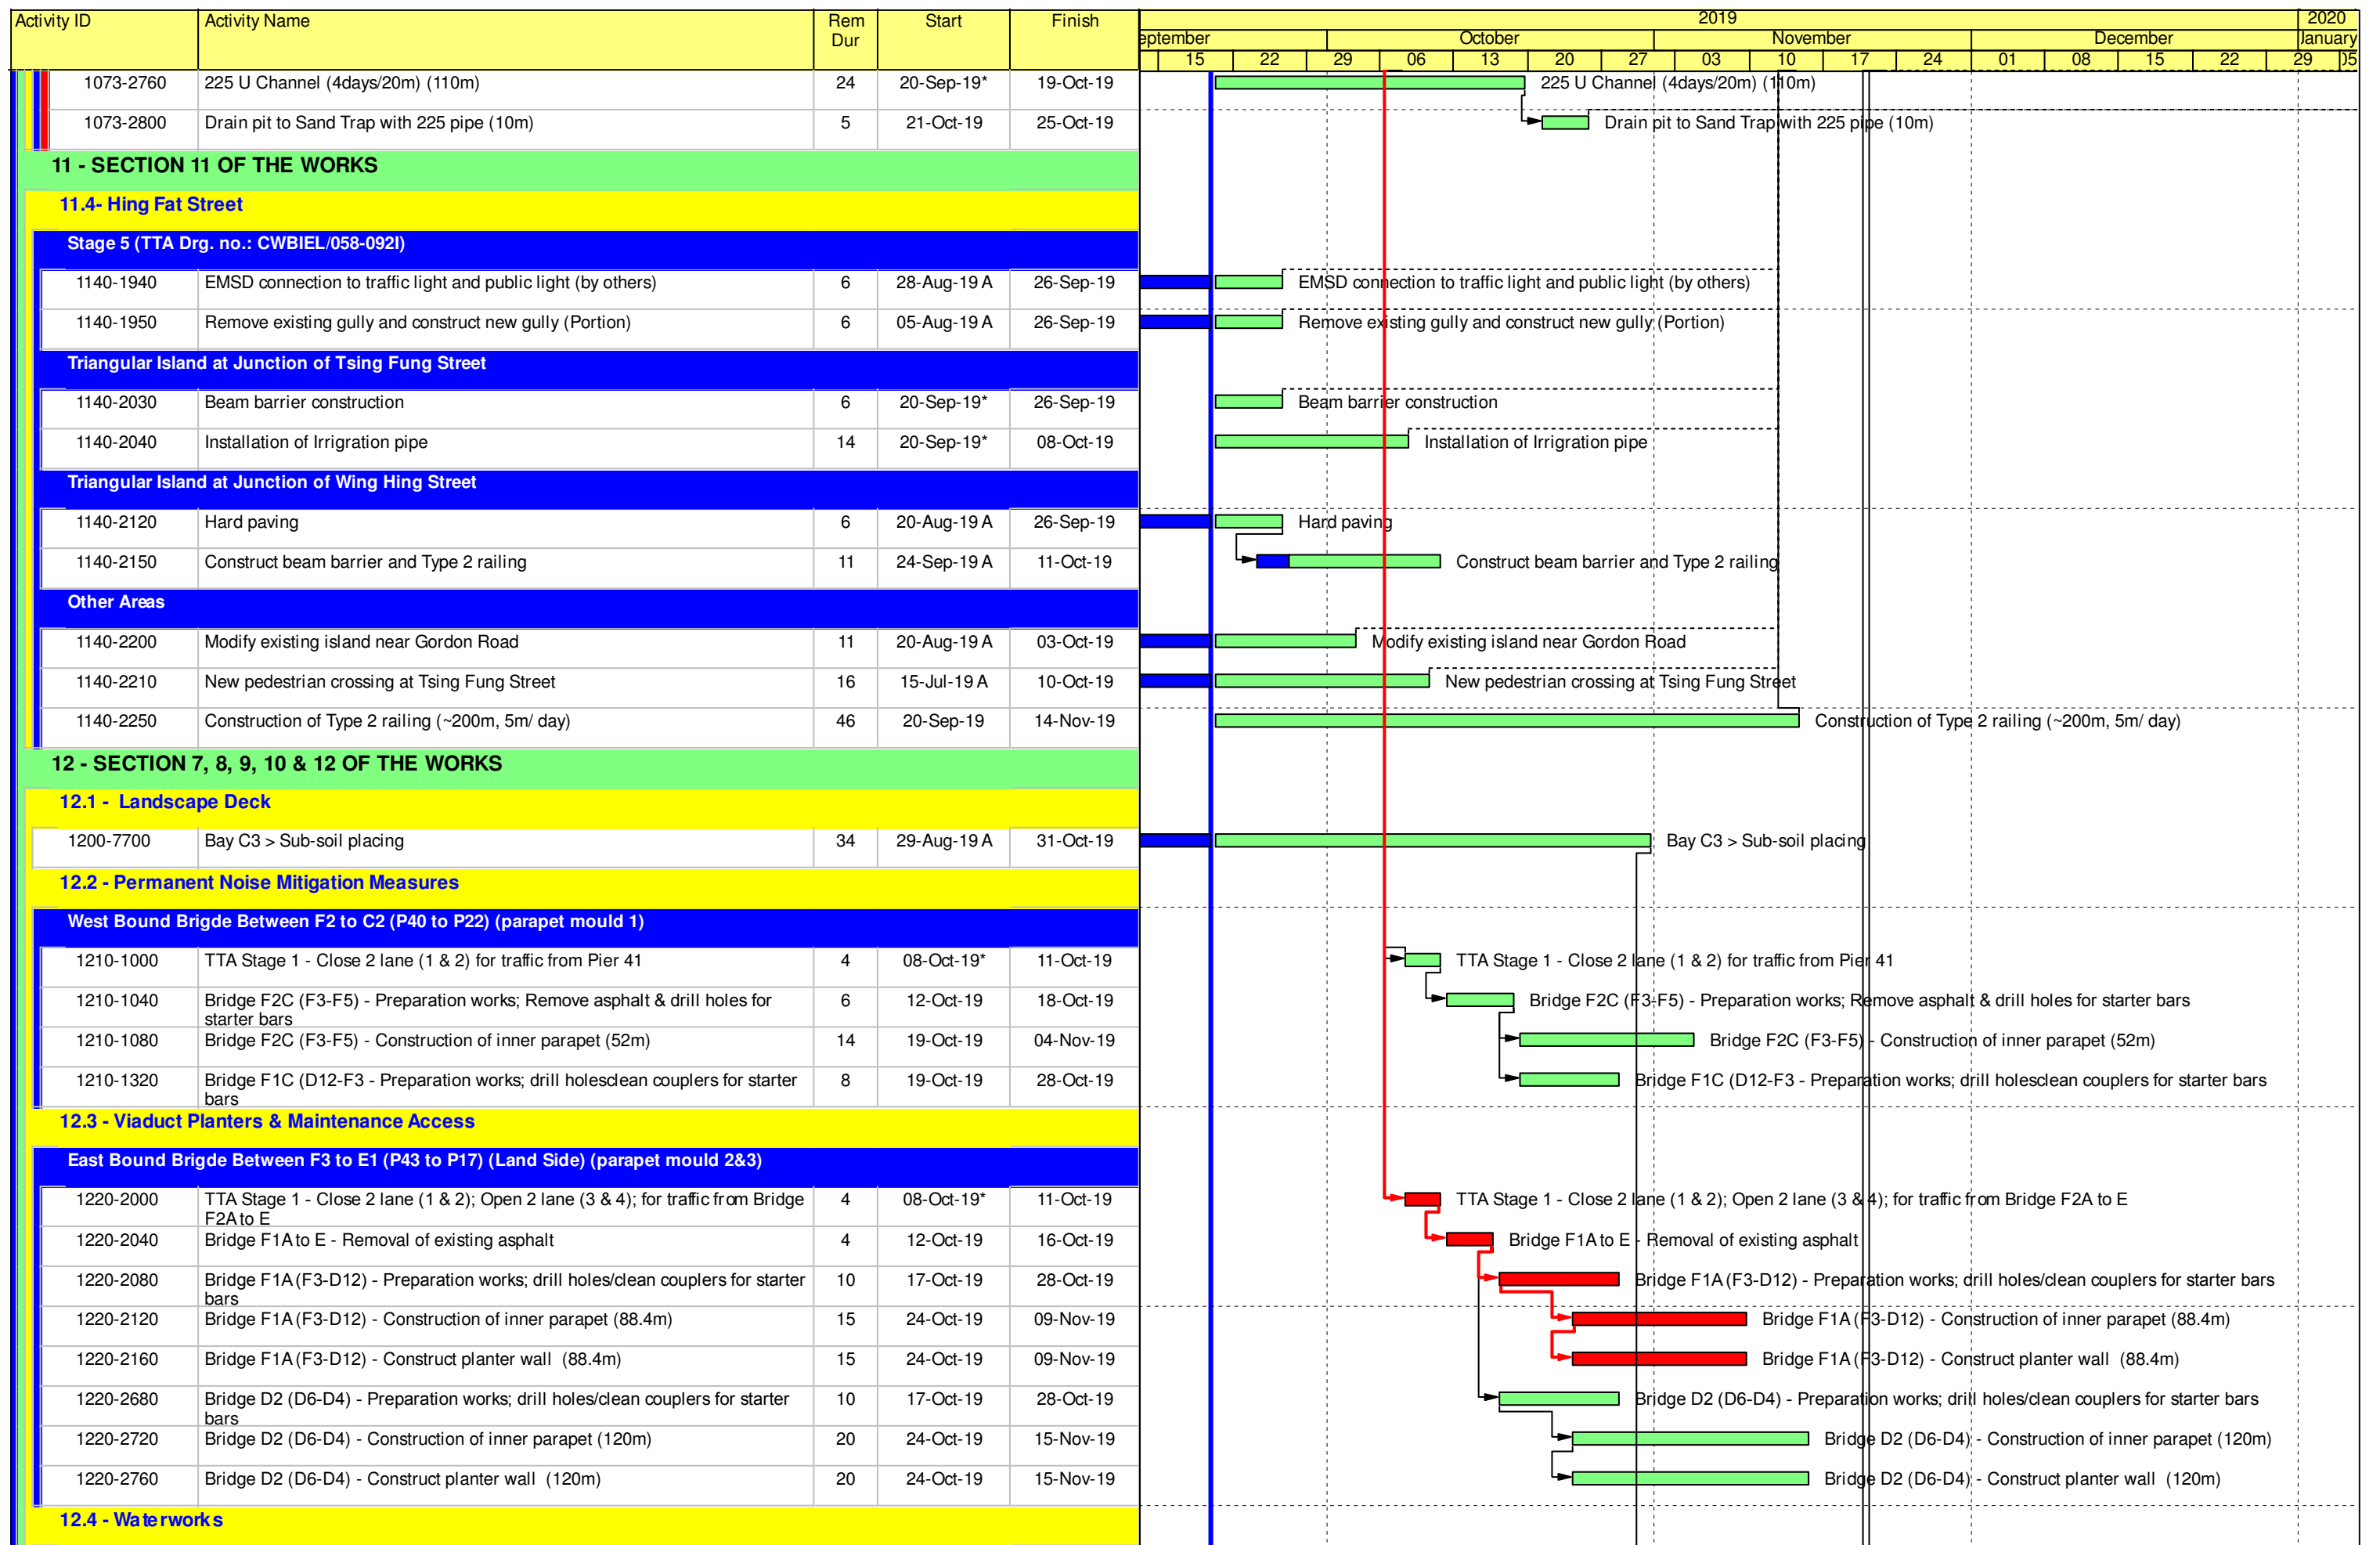

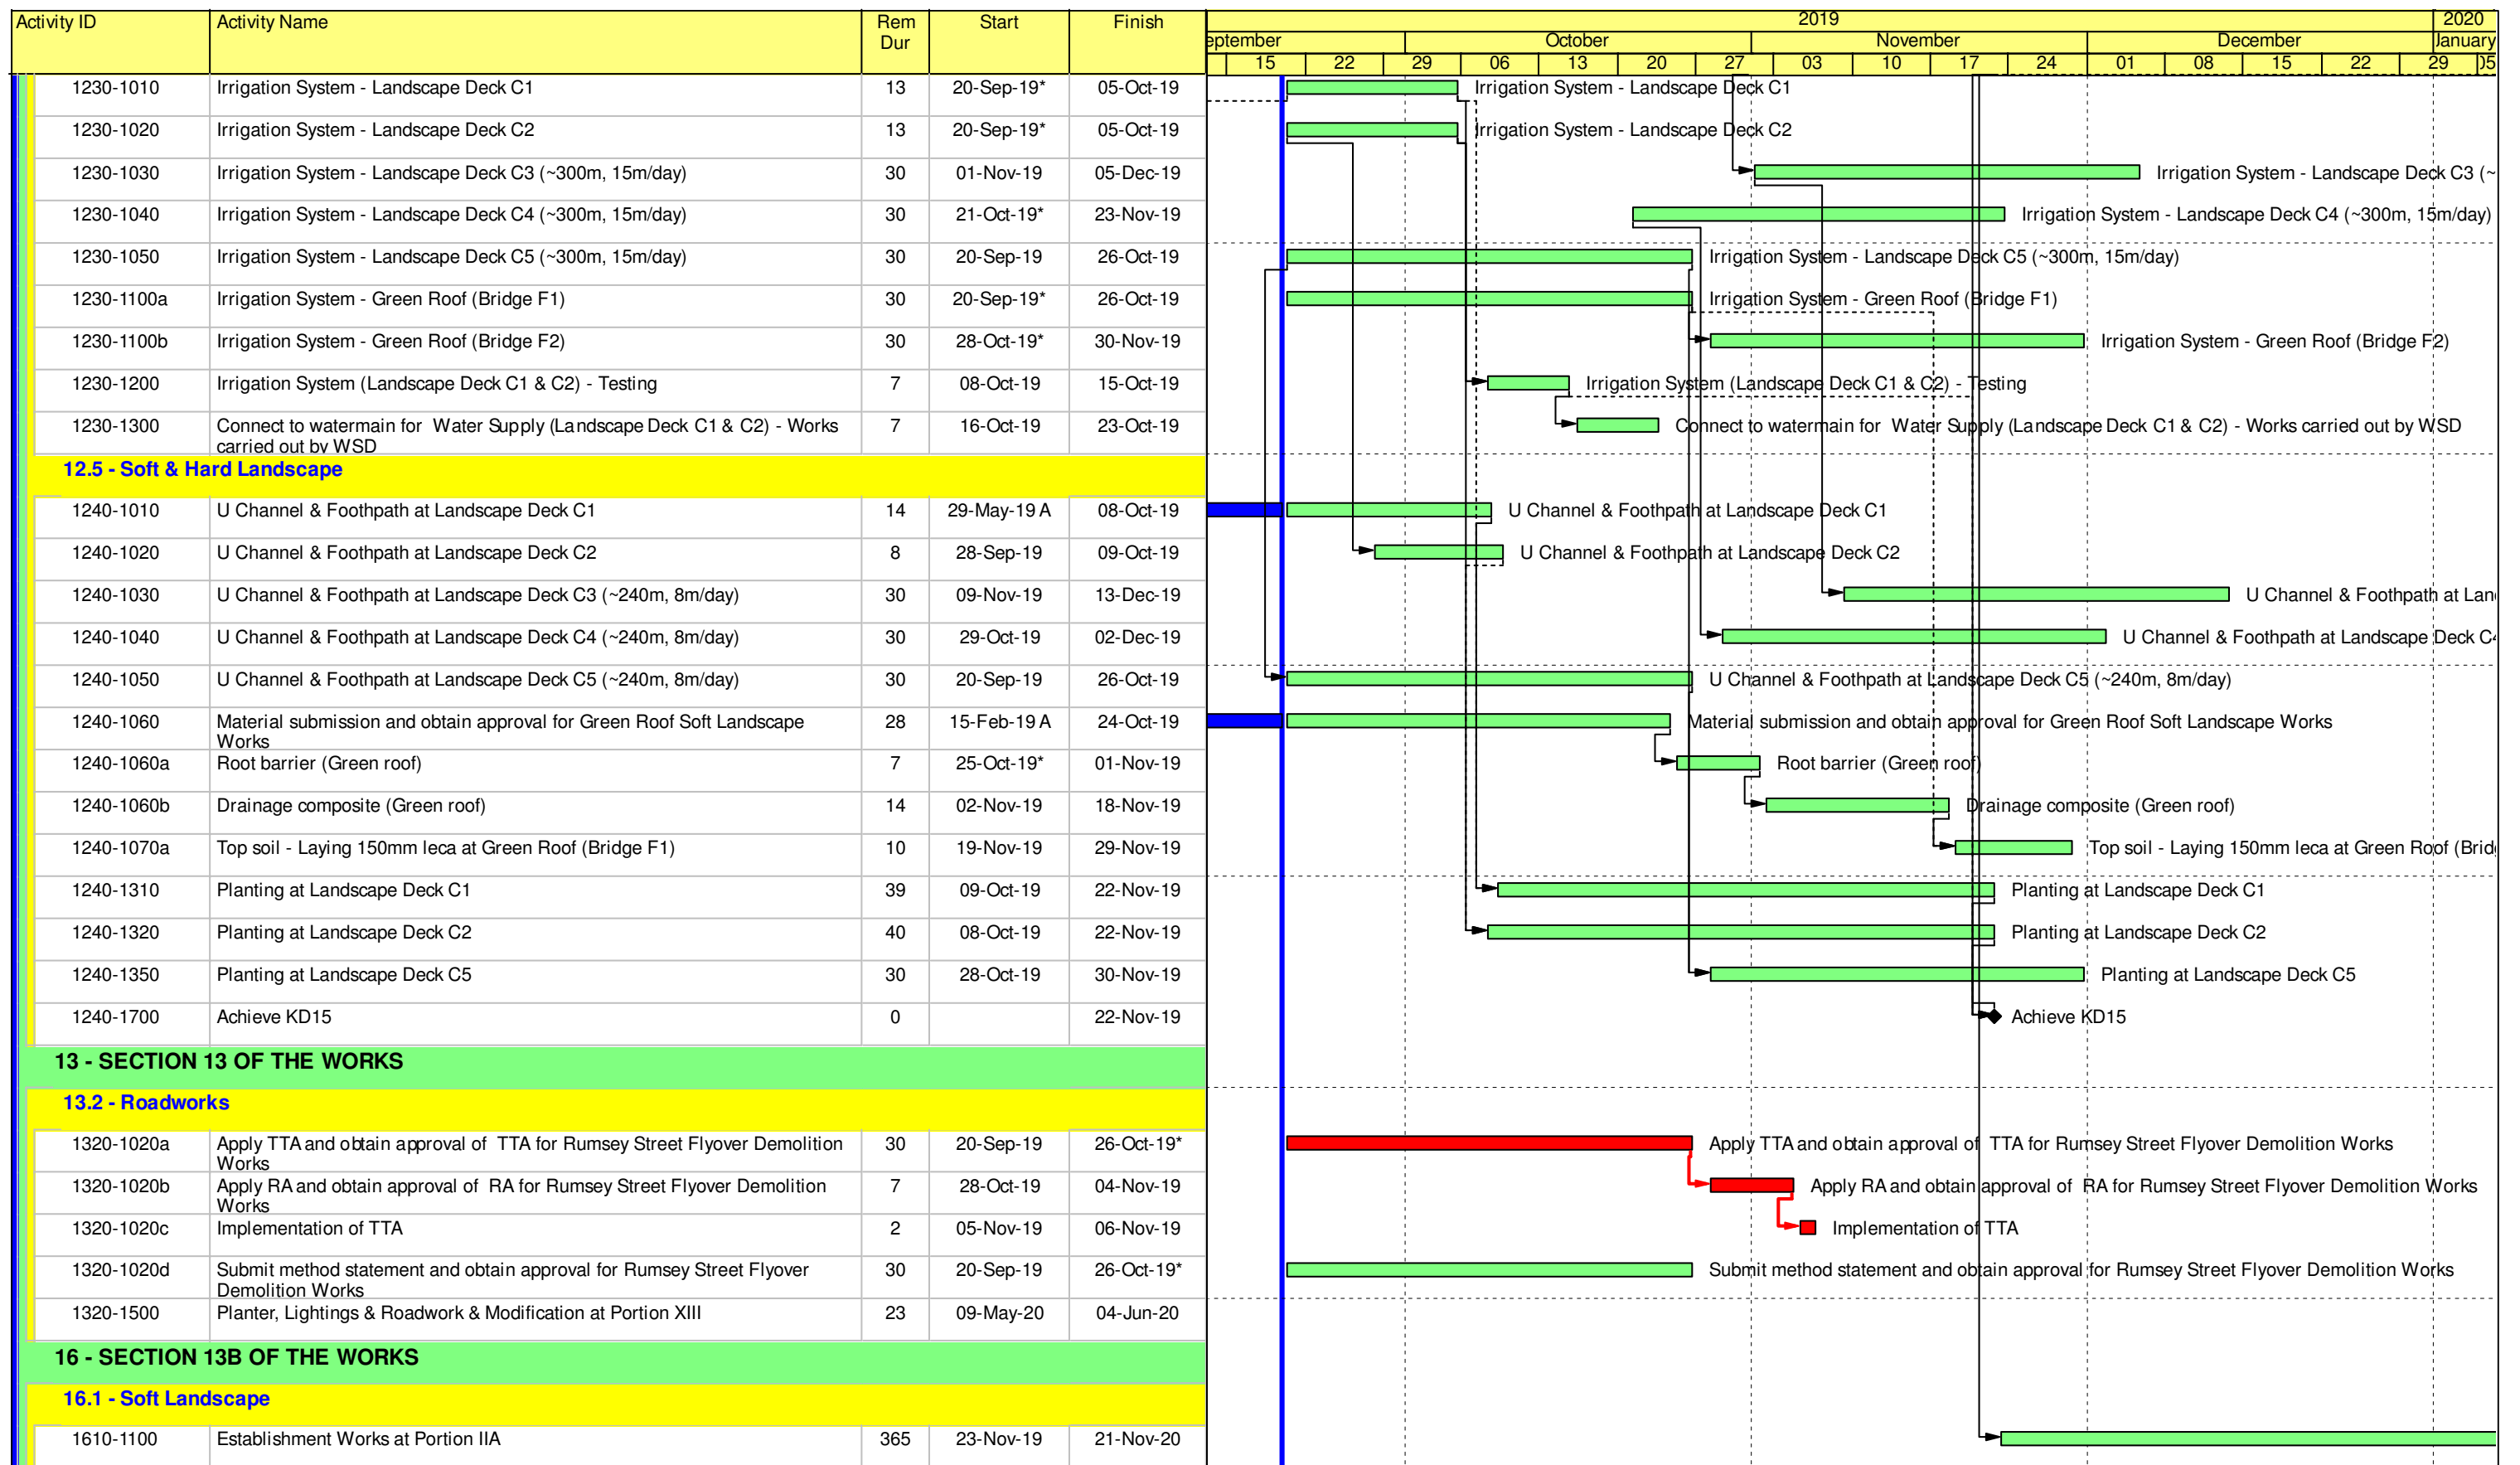

Activity ID	Activity Name	Original Duration	Start	Finish	2019															
					Aug			Sep			Oct			Nov						
Total		385	21-Mar-19 A	02-Apr-20																
DWP-08 - (2) - Update Progress As of 20 Aug 19		385	21-Mar-19 A	02-Apr-20																
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks		385	21-Mar-19 A	02-Apr-20																
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)		365	21-Mar-19 A	29-Jan-20																
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365	21-Mar-19 A	29-Jan-20																
KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH>500mm)		365	21-Mar-19 A	02-Apr-20																
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365	21-Mar-19 A	02-Apr-20																
KD18 - Section 11: Transplanted Trees DBH>500mm in Portion VA and XII		365	21-Mar-19 A	02-Apr-20																
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365	21-Mar-19 A	02-Apr-20																

■ Actual Work
■ Remaining Work
■ Critical Remaining Work
◆ Milestone

Page 1 of 1
 Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel (Slip Road 8 Section) - 3 Months Rolling Programme

Date	Revision	Checked	Approved
20-Aug-19	DWP-08 (2) - 3 Months Rolling	TL	TL



Data Date: 20-Sep-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2019			
						Sep	Oct	Nov	Dec
Update 2019-09-20 CWB(CC) - Commissioning Contract (DWP 4d)									
PRELIMINARIES AND GENERAL REQUIREMENTS									
Salient Key Dates and Milestones									
Anticipated Completion Dates									
KD09	KD9 - Completion of Section 4 of the Works (1445 days) - include EOT No.12 (149 days)	0		30-Nov-19*	-805		▲		◆
Possession Dates and Vacation Dates									
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-Sep-19	08-Jan-20	-585	[Red bar from Sep to Nov]			
Submissions and Approvals									
Initial General Submission									
10168	Submission of CMC 3DVR	30	20-Sep-19	19-Oct-19	-398	[Red bar from Sep to Oct]			
PROCUREMENT, MANUFACTURING & DELIVERIES									
Procurement; Manufacturing; Deliveries									
Green Wall on ADB									
Procurement & Fabrication									
10252	ADB Green Wall - Green Wall Fabrication & delivery	52	30-Oct-18 A	25-Sep-19	-779	[Blue bar from Sep to Oct]			
10254	ADB Green Wall - Commence installation	0	26-Sep-19		-779		◆		
CONSTRUCTION									
Middle Ventilation Building (MVB - related)									
Middle Ventilation Building (MVB)									
Smoke Extraction Louvre									
192324	MVB - ICE certification	12	17-Aug-19 A	30-Aug-19 A		[Blue bar from Aug to Sep]			
192326	MVB - Purchasing & material testing of steel materials & aluminum panels	34	17-Aug-19 A	26-Sep-19	-337	[Blue bar from Aug to Sep]			
192328	MVB - Fabrication & MOS of steel materials & aluminum panels	45	26-Aug-19 A	19-Oct-19	-319	[Blue bar from Sep to Oct]			
192330	MVB - Louvre installation	30	05-Oct-19	09-Nov-19	-337		[Red bar from Oct to Nov]		

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 67 (September 2019)

THREE MONTH ROLLING



Project ID: H2613-U067
 Baseline: DWP4d
 Layout: Update Three Month Rolling
 U067
 Page 1 of 5

Date	Revision	Checked	Approv...
20-Aug-19	U066	AT	CW
20-Sep-19	U067	AT	CW

Data Date: 20-Sep-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

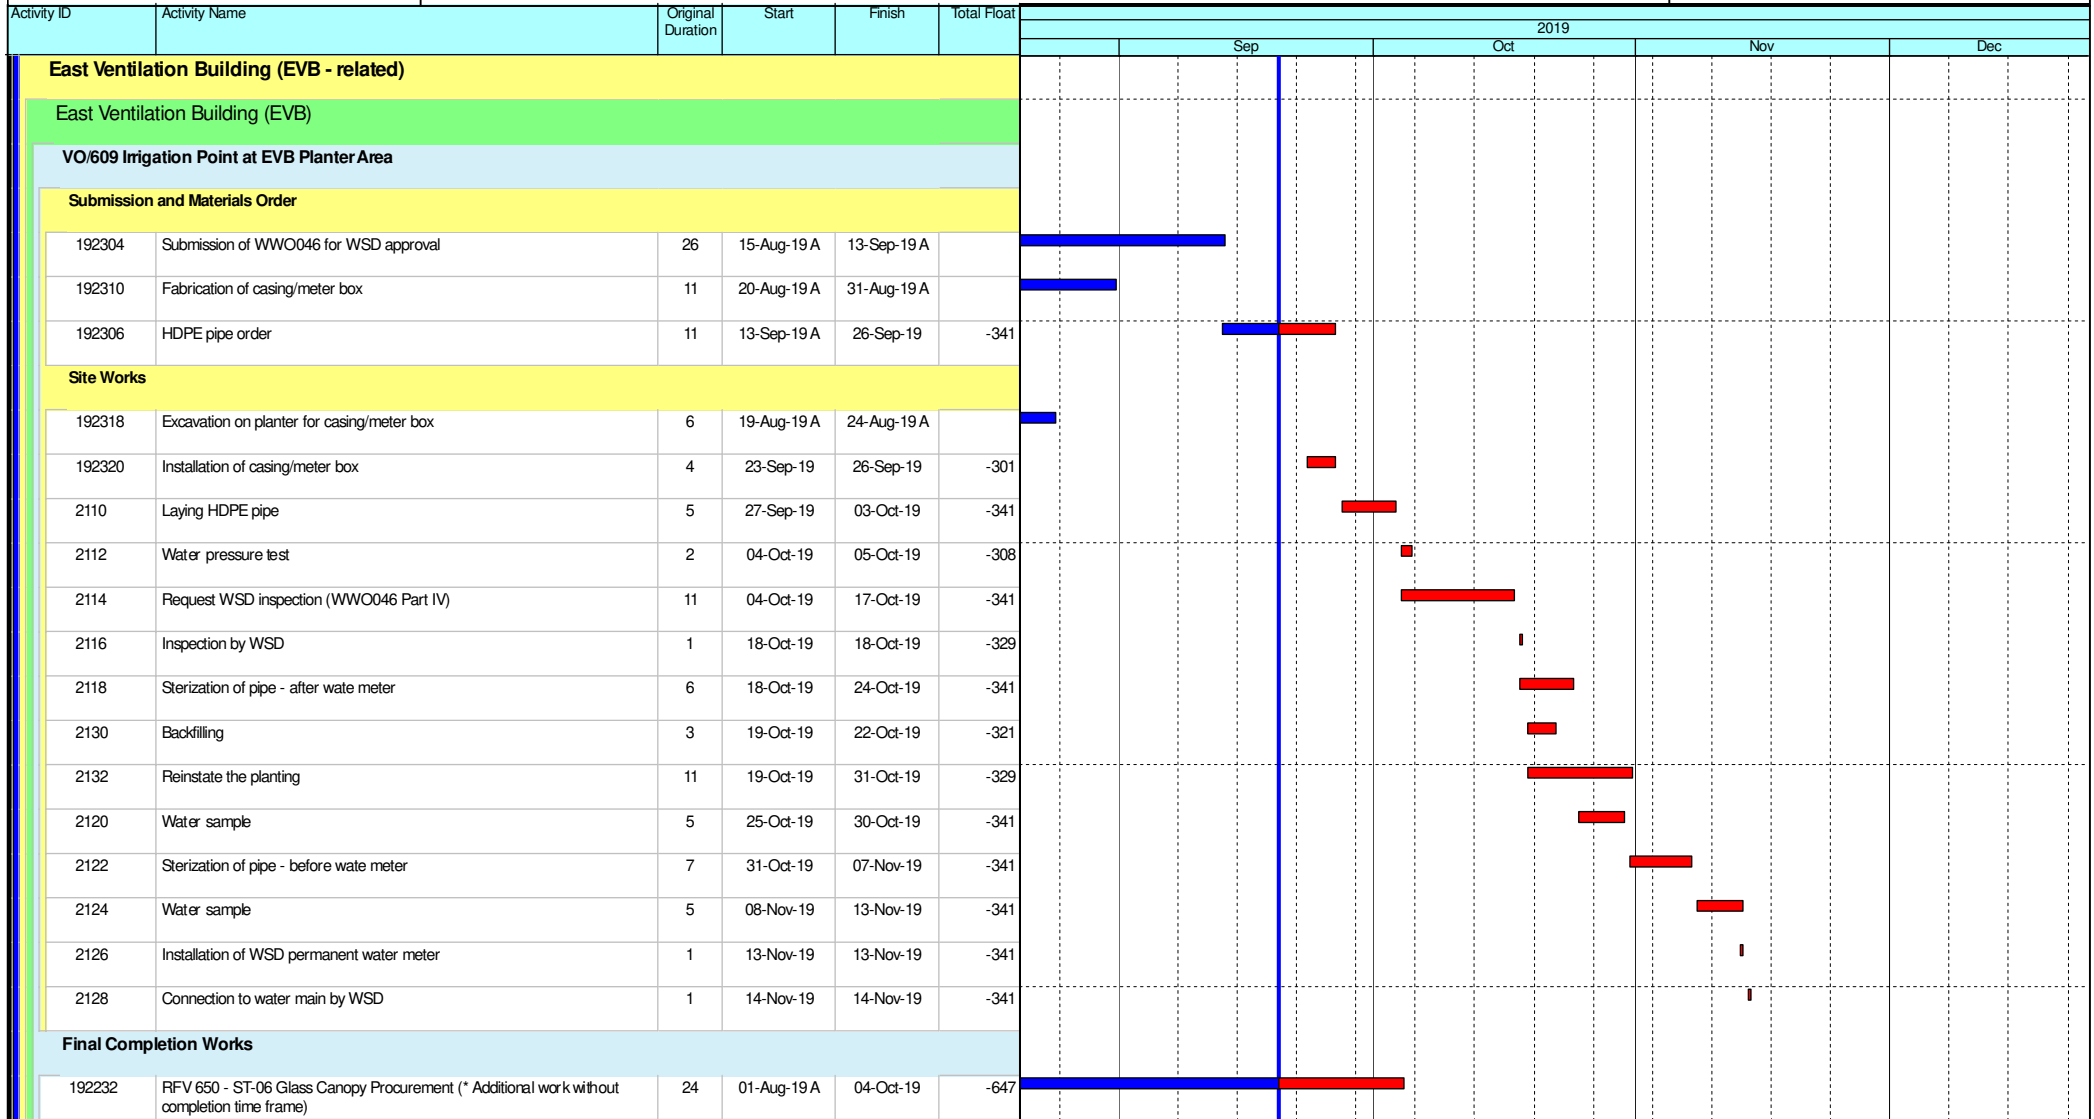

Leighton Contractors (Asia) Limited Programme Update 67 (September 2019) THREE MONTH ROLLING



Project ID: H2613-U067
 Baseline: DWP4d
 Layout: Update Three Month Rolling
 U067
 Page 2 of 5

Date	Revision	Checked	Approv...
20-Aug-19	U066	AT	CW
20-Sep-19	U067	AT	CW

Data Date: 20-Sep-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

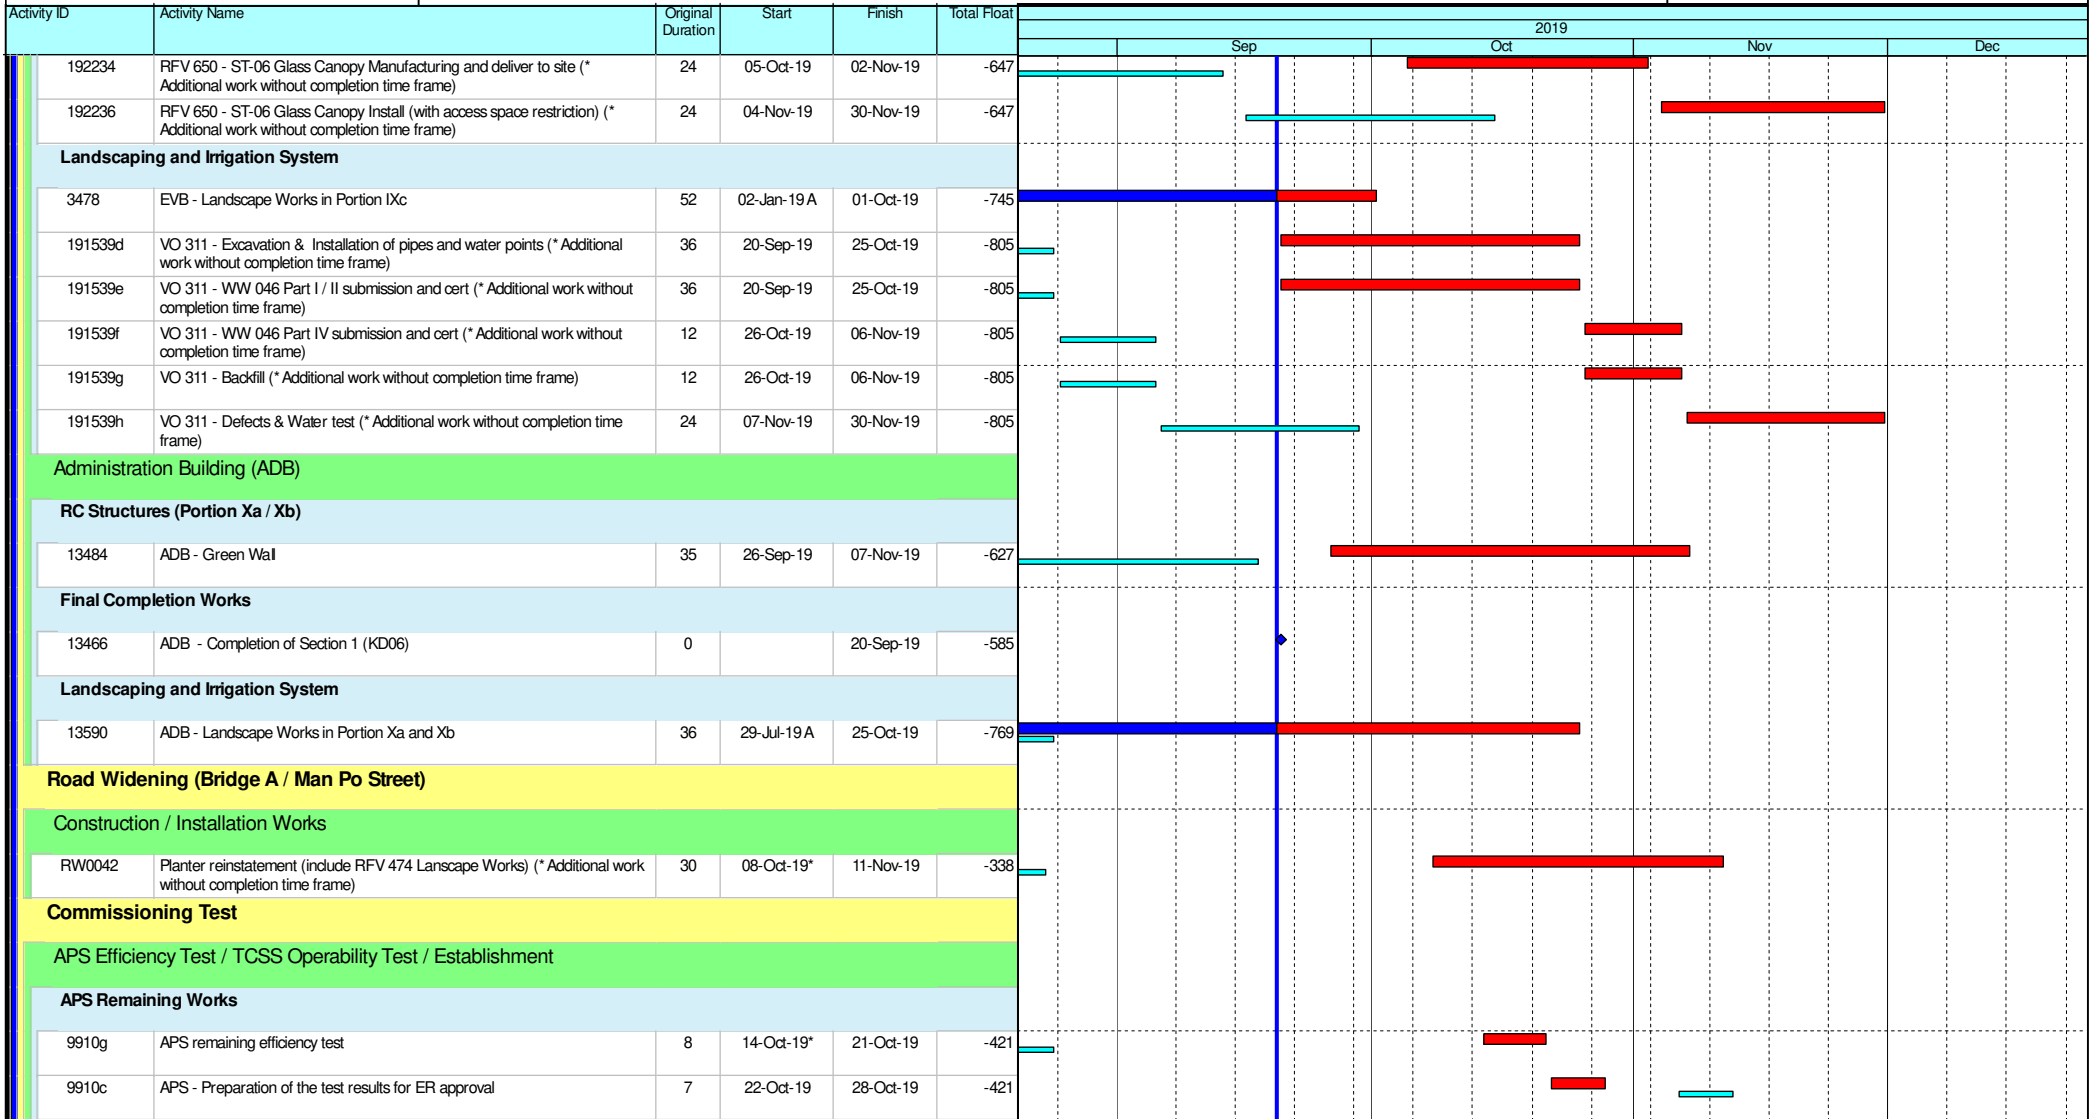

Leighton Contractors (Asia) Limited Programme Update 67 (September 2019) THREE MONTH ROLLING

Project ID: H2613-U067
 Baseline: DWP4d
 Layout: Update Three Month Rolling
 U067
 Page 3 of 5

Date	Revision	Checked	Approv...
20-Aug-19	U066	AT	CW
20-Sep-19	U067	AT	CW

Data Date: 20-Sep-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2019			
						Sep	Oct	Nov	Dec
9910d	APS - ER approval on the APS Efficiency Test	14	29-Oct-19	11-Nov-19	-421				
10126	Establishment Works	365	01-Dec-19	29-Nov-20	-805				
ESP failed to start after washdoen within 1 hour									
192266	Continuous trial run on MVB-APS-004, 002, 003 (can restart right after washdown without fault)	30	12-Sep-19 A	30-Sep-19	-379				
192270	Continuous trial run on MVB-APS-001b, 001c (Rectify and look for root cause)	24	12-Sep-19 A	30-Sep-19	-379				
192272	WVB-APS-001 (Rectify works)	10	12-Sep-19 A	30-Sep-19	-379				
192264	Continuous trial run on MVB-APS-001 (Rectify & located 2 rows of faulty modules)	24	13-Sep-19 A	26-Sep-19	-375				
192268	Continuous trial run on EVB-APS-001a (can restart right after washdown without fault)	30	17-Sep-19 A	27-Sep-19	-376				
192274	Monitor the wash down ESP start up performance	7	24-Sep-19*	30-Sep-19	-379				
Adjust ESP operation voltage (16kV average ionizer / 7kV average collector)									
192278	Adjust voltage per FAT test results WVB	3	05-Sep-19 A	07-Sep-19 A					
192280	Adjust voltage per FAT test results MVB	4	10-Sep-19 A	13-Sep-19 A					
192282	Adjust voltage per FAT test results EVB	2	12-Sep-19 A	13-Sep-19 A					
Roller curtain "failed to open" signal in WVB									
192284	Filtrontec investigate the root cause and advise solution	1	22-Aug-19 A	22-Aug-19 A					
192286	Filtrontec to fix the faulty roller curtain	2	15-Sep-19 A	16-Sep-19 A					
192288	Filtrontec / LJV monitor performance	14	17-Sep-19 A	30-Sep-19	-379				
AMS tripped the APS Plant due to Spike Pollutant Values									
192290	Filtrontec (VLA) check and examine the the AMS in MVB-001	7	17-Sep-19 A	23-Sep-19	-372				
192292	Filtrontec (VLA) reprogramme the AMS in MVB-002	7	17-Sep-19 A	23-Sep-19	-372				
192294	Filtrontec (VLA) reprogramme the AMS in MVB-003	7	17-Sep-19 A	23-Sep-19	-372				
192296	Filtrontec (VLA) reprogramme the AMS in EVB	7	17-Sep-19 A	23-Sep-19	-379				
192298	Monitor and observe the AMS performance	7	24-Sep-19	30-Sep-19	-379				
Training / Plan / Manual / As-Built Drawings for Project Completion									

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 67 (September 2019) THREE MONTH ROLLING

Project ID: H2613-U067
 Baseline: DWP4d
 Layout: Update Three Month Rolling
 U067
 Page 4 of 5








Date	Revision	Checked	Approv...
20-Aug-19	U066	AT	CW
20-Sep-19	U067	AT	CW

Data Date: 20-Sep-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2019																
						Sep			Oct			Nov			Dec							
192114	As-Built Drawings submission complete	0		02-Nov-19*	-412																	
10226	Routine Maintenance Records / Maintenance Monthly Report	0	01-Dec-19		-440																	

-  Current Milestone
-  Level of Effort
-  Baseline Milestone
-  Actual Work
-  Critical Remaining Work
-  Remaining Work
-  Project Baseline

Leighton Contractors (Asia) Limited Programme Update 67 (September 2019) THREE MONTH ROLLING

Project ID: H2613-U067
 Baseline: DWP4d
 Layout: Update Three Month Rolling
 U067
 Page 5 of 5

Date	Revision	Checked	Approv...
20-Aug-19	U066	AT	CW
20-Sep-19	U067	AT	CW
