


























**CEDD Contract No. HK/2012/08**  
**Wan Chai Development Phase II**  
**Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019							
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
<b>Promenade Seawall Parapet Construction &amp; EVA</b>																									
SVII12000	Sec VII - Precast parapet	67	18-Nov-17 A	14-May-18	0%																				
SVII12010	Sec VII - Zone CRIII - seawall parapet: Backfilling	14	20-Feb-18	07-Mar-18	0%																				
SVII12120	Sec VII - Zone CRIII - seawall parapet: Construct mass concrete coping	30	08-Mar-18	16-Apr-18	0%																				
SVII12122	Sec VII - Zone CRIII - seawall parapet: reinforced concret coping	17	17-Apr-18	07-May-18	0%																				
SVII12140	Sec VII - Zone CRIII - seawall parapet: construct seawall parapet	30	08-May-18	12-Jun-18	0%																				
SVII12160	Sec VII - CRIII - EVA: watermain	14	13-Jun-18	29-Jun-18	0%																				
SVII12180	Sec VII - CRIII - EVA: U-channel	14	30-Jun-18	17-Jul-18	0%																				
SVII12200	Sec VII - CRIII - EVA: bituminous layer	5	18-Jul-18	23-Jul-18	0%																				
SVII12220	Sec VII - CRIII - EVA: paving block	30	24-Jul-18	27-Aug-18	0%																				
SVII13120	Sec VII - Zone A1, A2 & B - seawall parapet: Construct mass concrete coping	14	28-Dec-17 A	07-Mar-18	68.18%																				
SVII13122	Sec VII - Zone A1, A2 & B - seawall parapet: reinforced concrete coping	18	08-Mar-18	28-Mar-18	0%																				
SVII13140	Sec VII - Zone A1, A2 & B - seawall parapet: Construct seawall parapet	30	09-Apr-18	14-May-18	0%																				
SVII13160	Sec VII - Zone A1, A2 & B - EVA: watermain	14	15-May-18	31-May-18	0%																				
SVII13180	Sec VII - Zone A1, A2 & B - EVA: U-channel	14	01-Jun-18	16-Jun-18	0%																				
SVII13182	Sec VII - Zone A1, A2 & B - EVA: bituminous layer	5	19-Jun-18	23-Jun-18	0%																				
SVII13184	Sec VII - Zone A1, A2 & B - EVA: paving block	30	25-Jun-18	30-Jul-18	0%																				
SVII13200	Sec VII - Zone D - seawall parapet: Remove temporary seawall block	21	07-Mar-18	03-Apr-18	0%																				
SVII13220	Sec VII - Zone D - seawall parapet: Construct mass concrete	30	04-Apr-18	10-May-18	0%																				
SVII13222	Sec VII - Zone D - seawall parapet: reinforced concrete coping	18	11-May-18	01-Jun-18	0%																				
SVII13240	Sec VII - Zone D - seawall parapet: Construct seawall parapet	25	02-Jun-18	03-Jul-18	0%																				
SVII13260	Sec VII - Zone D - EVA : watermain	14	04-Jul-18	19-Jul-18	0%																				
SVII13280	Sec VII - Zone D - EVA : U-channel	14	20-Jul-18	04-Aug-18	0%																				
SVII13300	Sec VII - Zone D - EVA : bituminous layer	5	06-Aug-18	10-Aug-18	0%																				
SVII13320	Sec VII - Zone D - EVA : paving block	30	11-Aug-18	14-Sep-18	0%																				
<b>Promenade Footpath</b>																									
<b>Section 1</b>																									
SVII10440	Sec VII - section 1 footpath - drainage works : connection pipe & U -channel	10	24-May-18	04-Jun-18	0%																				
SVII10445	Sec VII - section 1 footpath - watermain	7	05-Jun-18	12-Jun-18	0%																				
SVII10460	Sec VII - section 1 footpath - lighting	7	13-Jun-18	21-Jun-18	0%																				
SVII10500	Sec VII - section 1 footpath - paving block	21	22-Jun-18	17-Jul-18	0%																				
<b>Section 2</b>																									
SVII12610	Sec VII - section 2 footpath - drainage works : L2202 - L2203A	20	20-Feb-18	14-Mar-18	0%																				
SVII12615	Sec VII - section 2 footpath - watermain	7	15-Mar-18	22-Mar-18	0%																				
SVII12630	Sec VII - section 2 footpath - utilities: TCSS	21	23-Mar-18	20-Apr-18	0%																				
SVII12670	Sec VII - section 2 footpath - paving block	30	21-Apr-18	28-May-18	0%																				
<b>Section 3</b>																									
SVII12850	Sec VII - section 3 footpath - watermain	17	20-Feb-18	10-Mar-18	0%																				
SVII12870	Sec VII - section 3 footpath - utilities (HEC, TCSS, HGC, PCCW)	40	12-Mar-18	02-May-18	0%																				
SVII12875	Sec VII - 3 footpath - drainage works :U chanel	14	03-May-18	18-May-18	0%																				








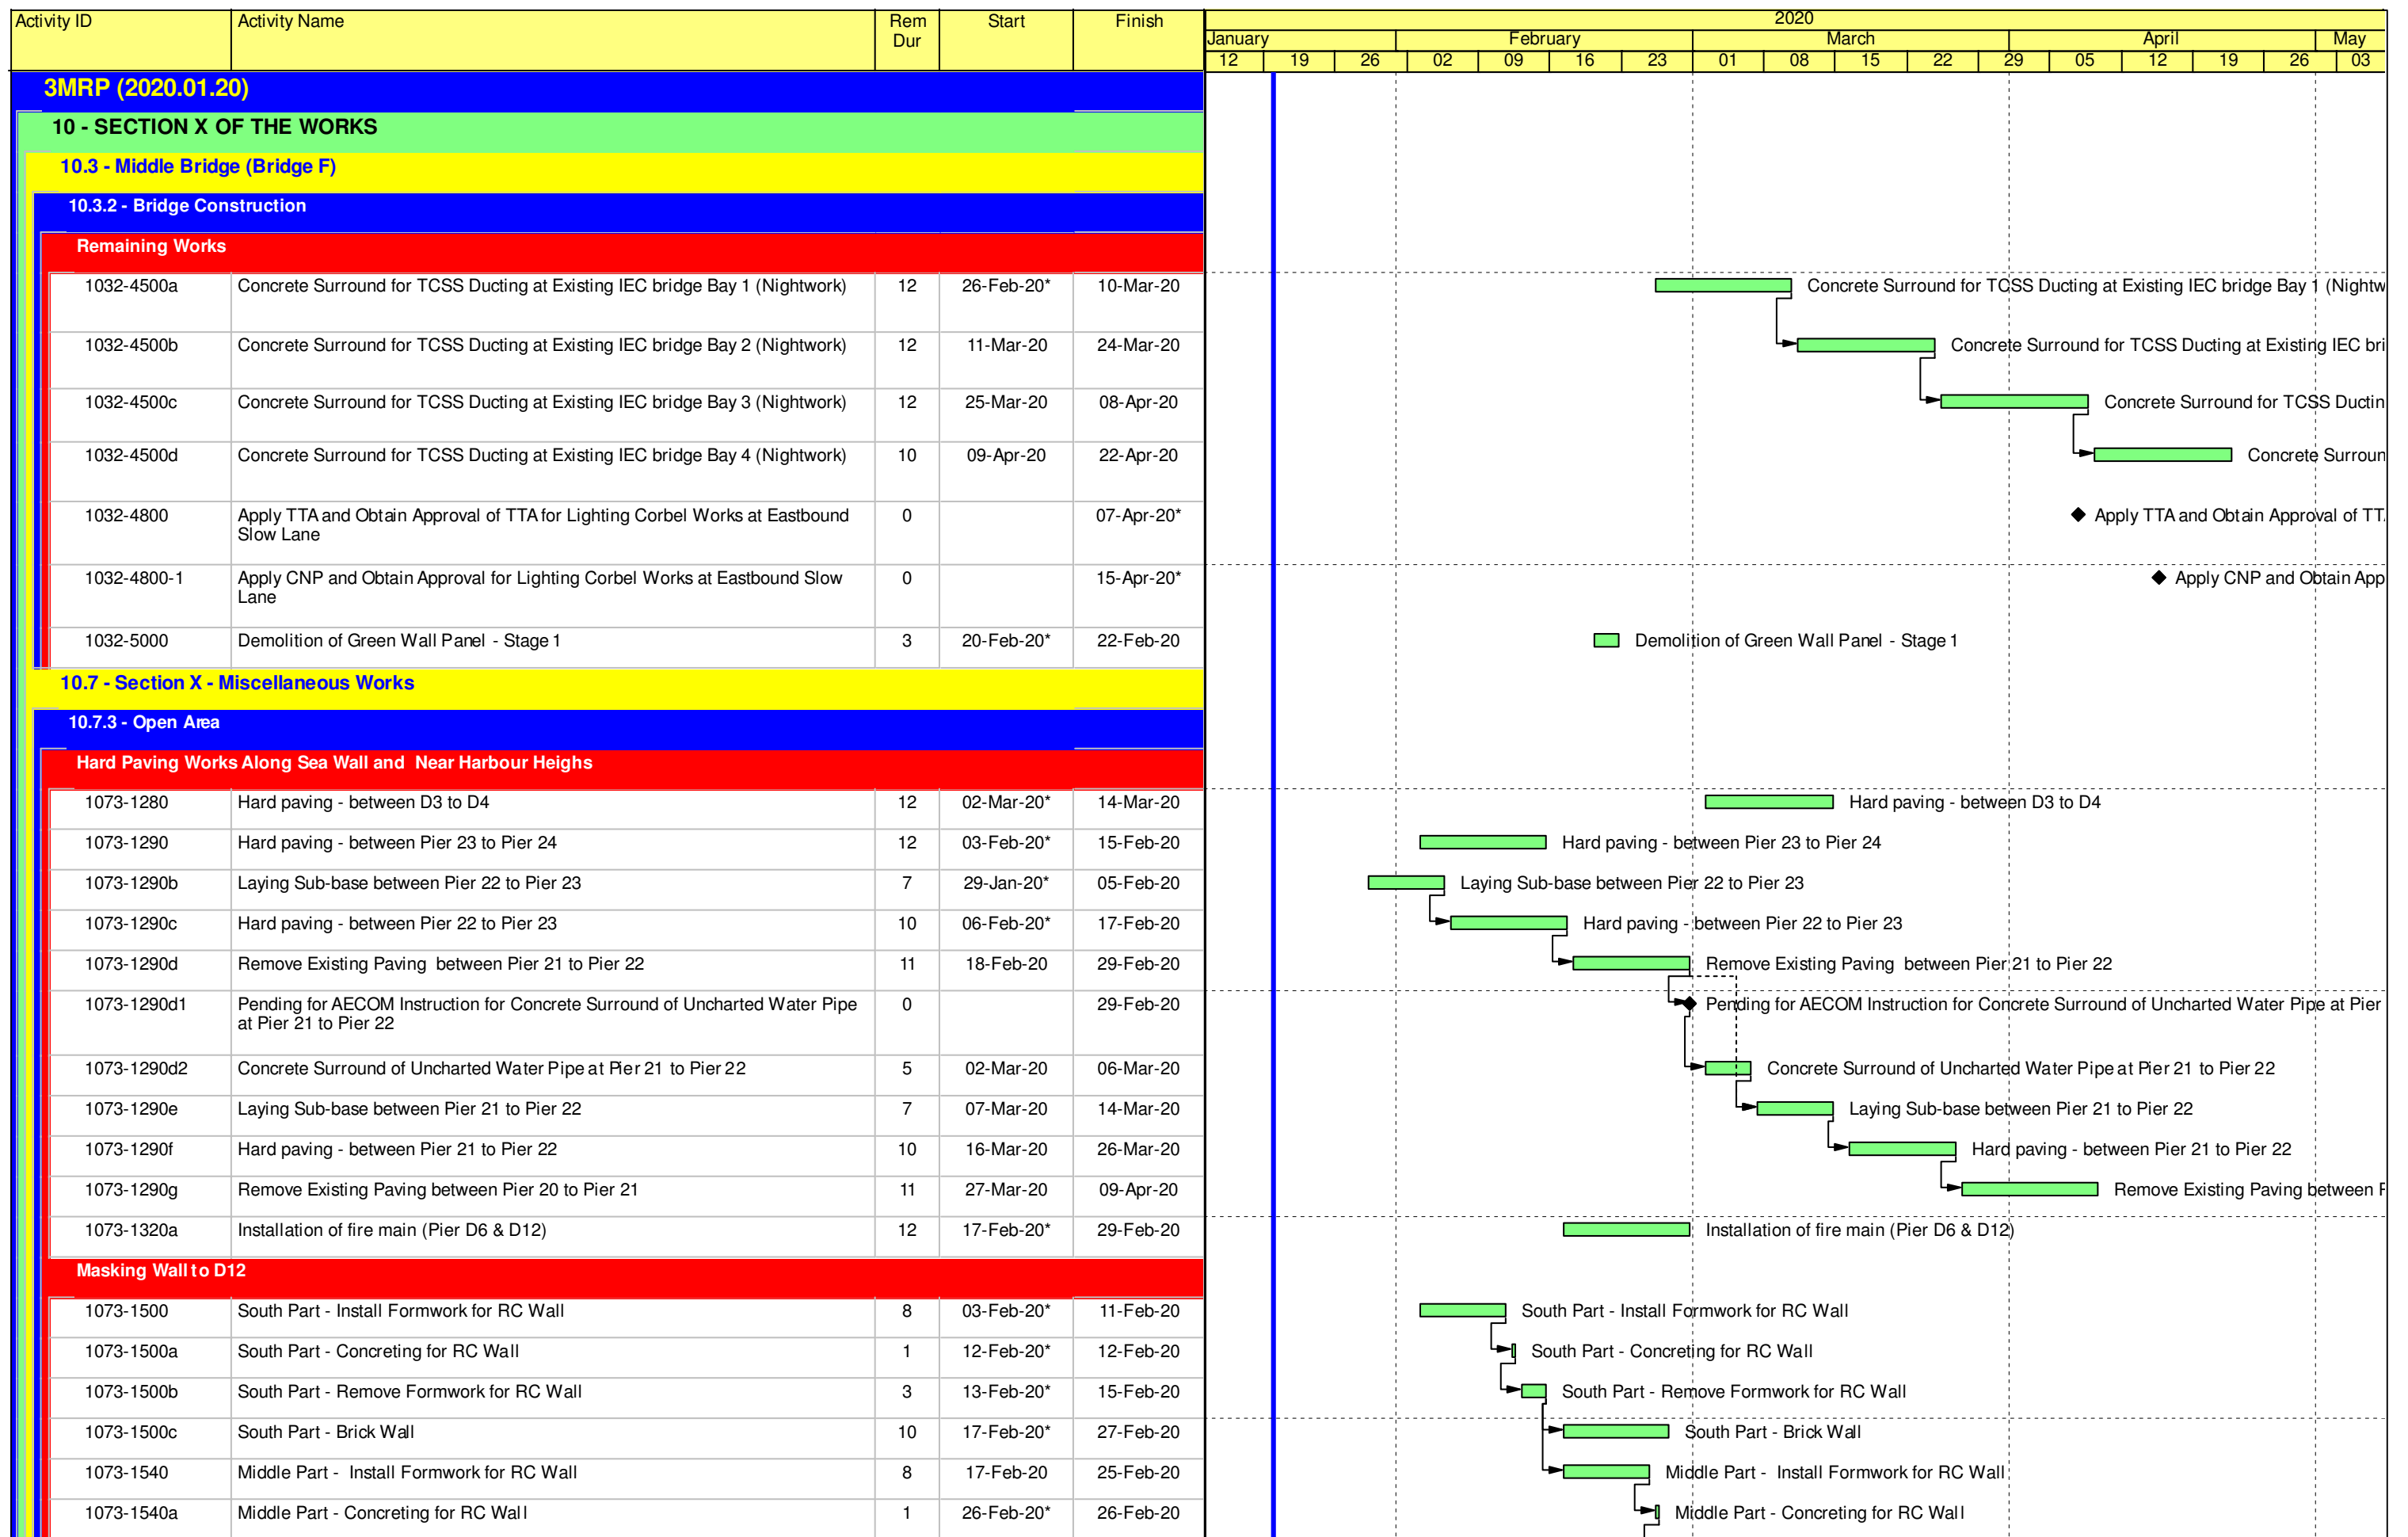

█ Remaining Level of Effort    █ Remaining Work  
█ Actual Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Jan.2020 to 20.Apr.2020)**



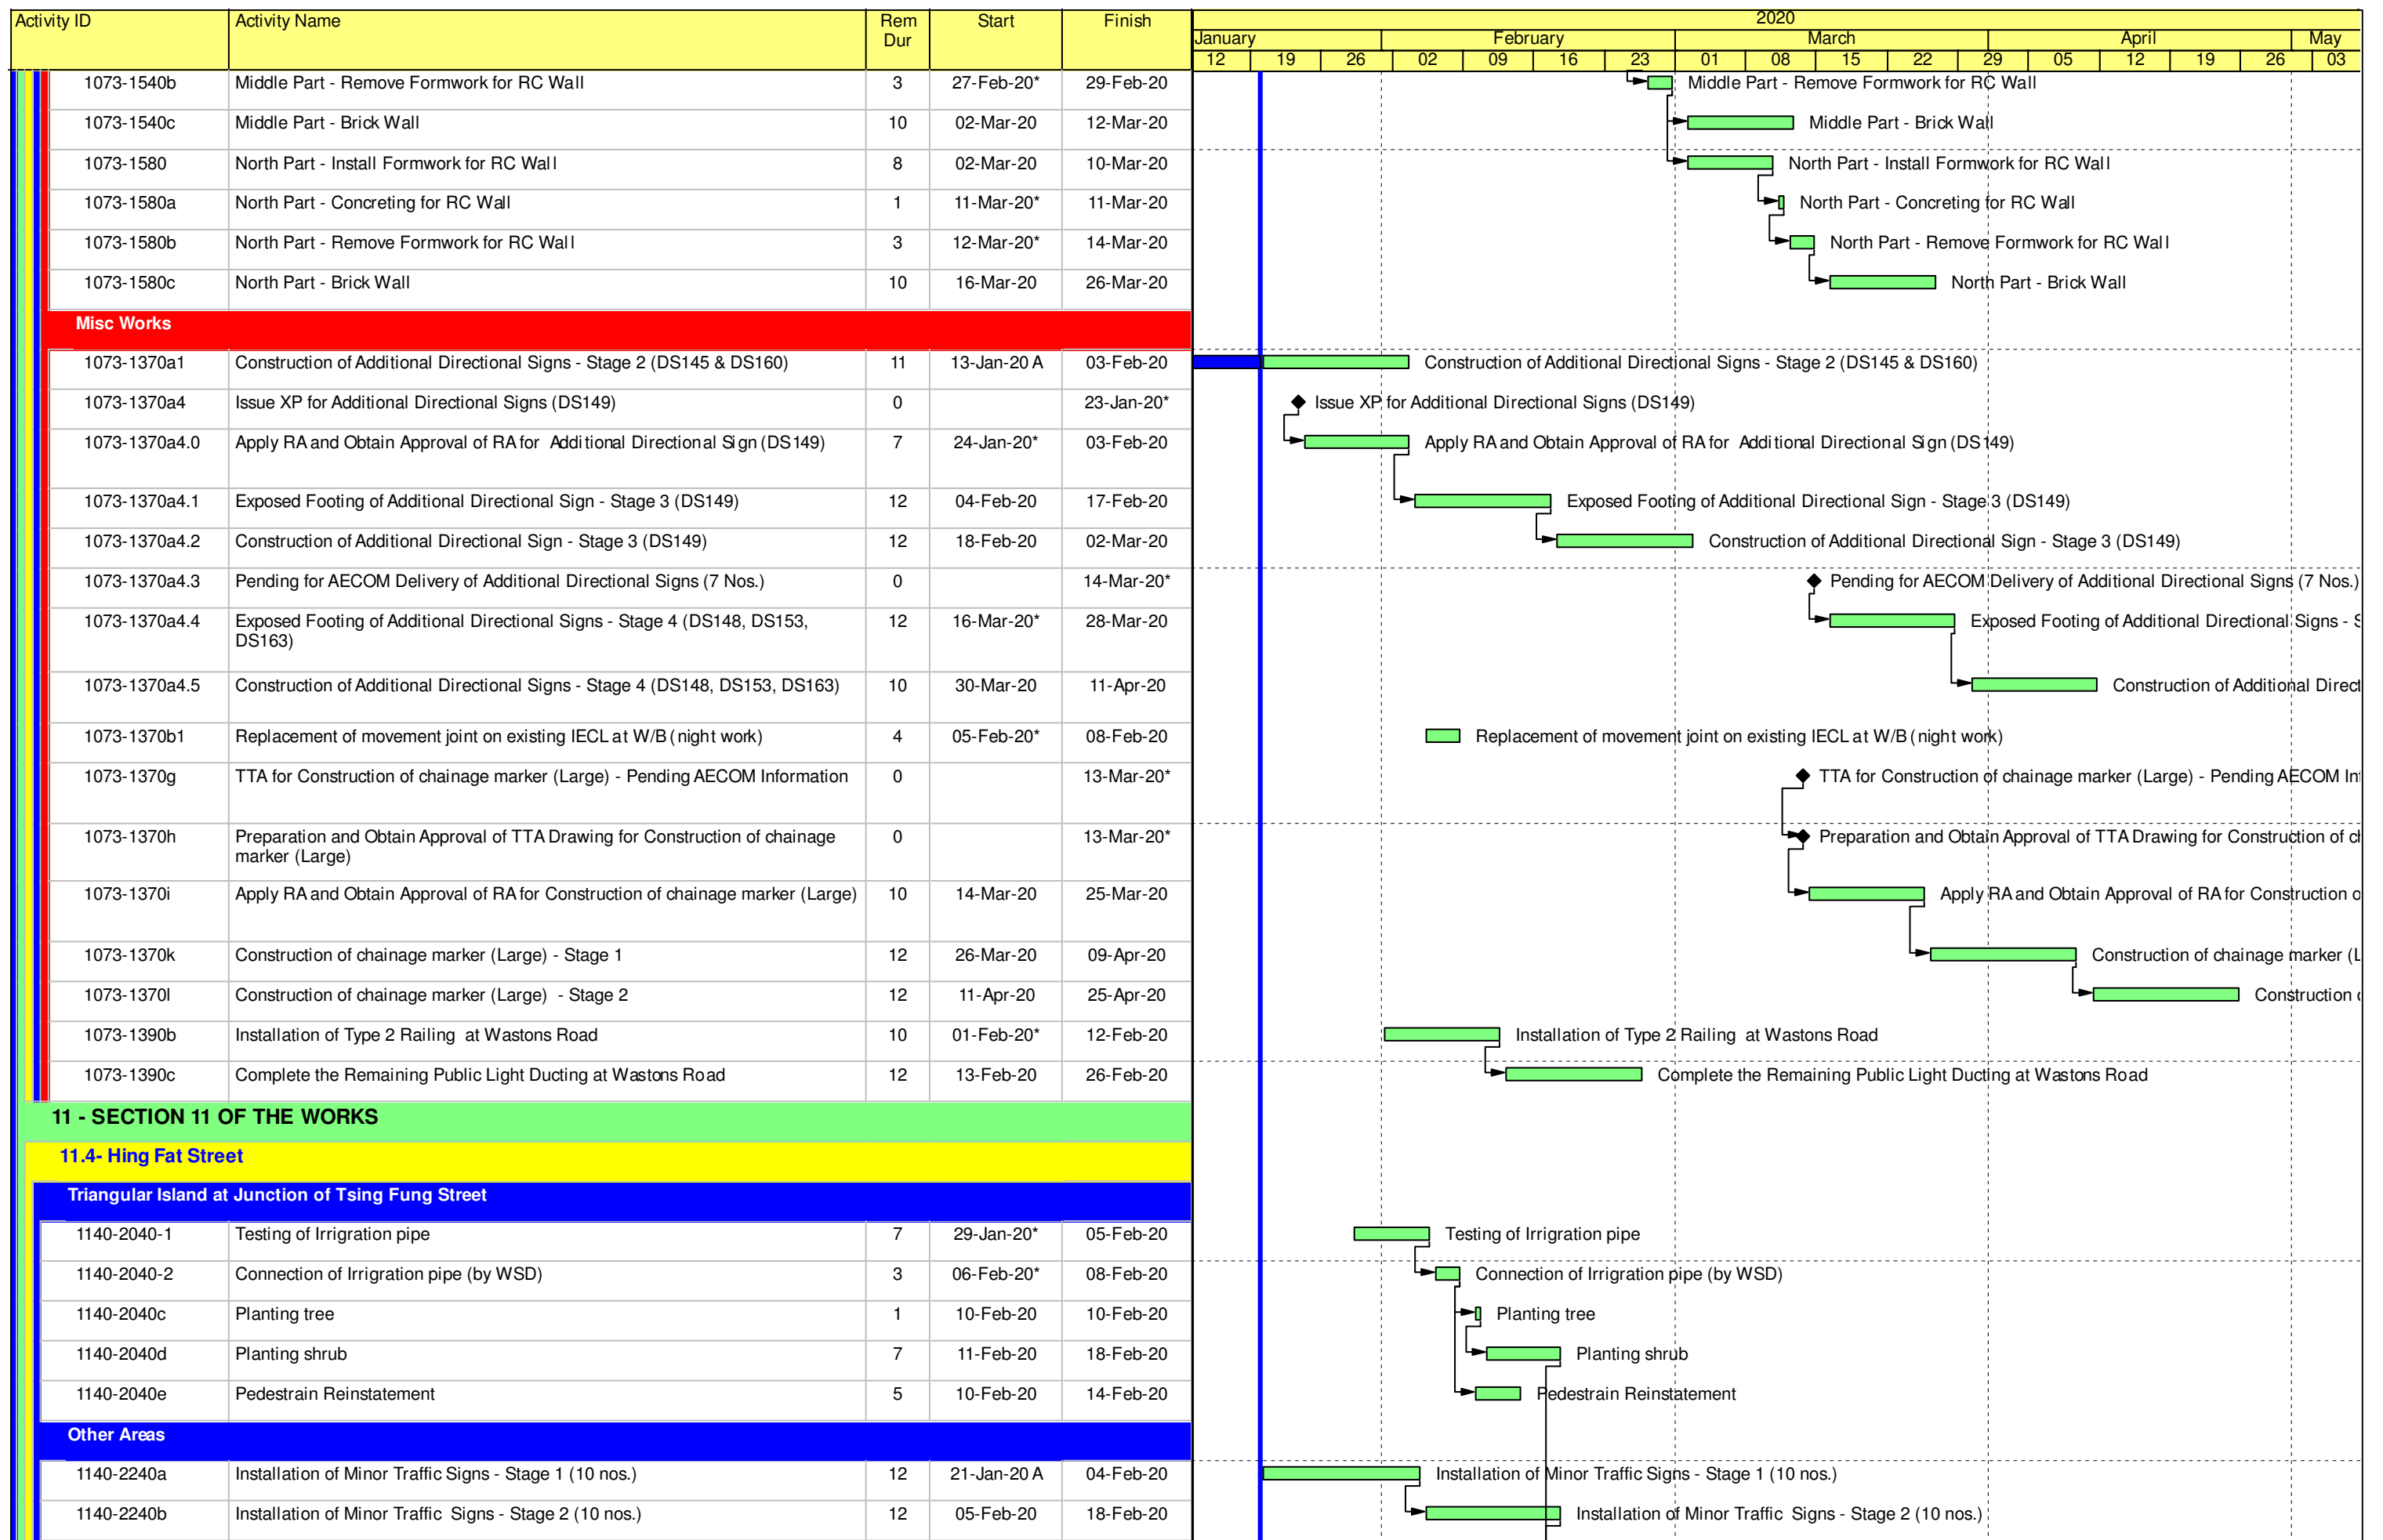

█ Remaining Level of Effort    █ Remaining Work  
█ Actual Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Jan.2020 to 20.Apr.2020)**



Activity ID	Activity Name	Rem Dur	Start	Finish	2020																		
					January			February			March			April			May						
					12	19	26	02	09	16	23	01	08	15	22	29	05	12	19	26	03		
1140-2240c	Installation of Minor Traffic Signs - Stage 3 (10 nos.)	12	19-Feb-20	03-Mar-20	Installation of Minor Traffic Signs - Stage 3 (10 nos.)																		
1140-2250c	Construction of Type 2 railing (5 Bays) - Junction of Hing Fat St & Tsing Fung St	12	21-Jan-20 A	04-Feb-20	Construction of Type 2 railing (5 Bays) - Junction of Hing Fat St & Tsing Fung St																		
1140-2270	Road resurfacing at Hing Fat Street - Stage 1 (4 TTA Schemes - Night Work)	11	19-Feb-20*	02-Mar-20	Road resurfacing at Hing Fat Street - Stage 1 (4 TTA Schemes - Night Work)																		
1140-2270a	Renew on CNP and Obtain Approval for CNP	0		02-Mar-20*	Renew on CNP and Obtain Approval for CNP																		
1140-2270b	Road resurfacing at Hing Fat Street - Stage 2 (4 TTA Schemes - Night Work)	12	03-Mar-20	16-Mar-20	Road resurfacing at Hing Fat Street - Stage 2 (4 TTA Schemes - Night Work)																		
1140-2270c	Road resurfacing at Hing Fat Street - Stage 3 (4 TTA Schemes - Night Work)	12	17-Mar-20	30-Mar-20	Road resurfacing at Hing Fat Street - Stage 3 (4 TTA Schemes - Night Work)																		
1140-2270d	Road resurfacing at Hing Fat Street - Stage 4 (4 TTA Schemes - Night Work)	12	31-Mar-20	16-Apr-20	Road resurfacing at Hing Fat Street - Stage 4 (4 TTA Schemes - Night Work)																		

**12 - SECTION 7, 8, 9, 10 & 12 OF THE WORKS**

**12.1 - Landscape Deck**

1200-7820a	Reinstatement of wall opening at Landscape deck C1 / Tunnel Eastern Portal	3	17-Jan-20 A	22-Jan-20
1200-7830	Formation Level for Footpath near C1 at SR13	10	23-Jan-20	05-Feb-20
1200-7830a	Construct Footpath near C1 at SR13	12	06-Feb-20	19-Feb-20
1200-7830b	Cultivation for D4-D5	12	20-Feb-20	04-Mar-20
1200-7830c	Planting Soil for D4-D5	12	05-Mar-20	18-Mar-20
1200-7830d	Cultivation for D5-D6	12	19-Mar-20	01-Apr-20
1200-7830e	Planting Soil for D5-D6	12	02-Apr-20	18-Apr-20
1200-7830f	Cultivation for D6-D7	12	20-Apr-20	04-May-20

**12.2 - THE WORKS along IECL**

**12.2.1 - Noise Enclosure and Inner Parapet along IECL Westbound**

**West Bound Brigde Between F2 to C2 (P40 to P22) (parapet mould 1)**

A12750	Pending of AECOM Instruction for Inner Parapet at Pier 20 to Pier 40	0		20-Apr-20*
--------	--	---	--	------------

**Pier 17 - Pier 26 (Section 8)**

**Pier 22 - Pier 23**

**Construction of Noise Enclosure**

A11350	Installation of permanent vertical PMMA panel (Night works)	12	12-Feb-20*	23-Feb-20
--------	---	----	------------	-----------

**Pier 21 - Pier 22**

**Southern**

**Construction of Noise Enclosure**


A12320	Installation of permanent roof PMMA panel - Stage 1 (Night works)	12	24-Feb-20*	06-Mar-20
A12320a	Installation of permanent roof PMMA panel- Stage 2 (Night works)	12	07-Mar-20*	18-Mar-20

**Pier 20 - Pier 21**

**Northern**

A12760	TTA (P17-P21) (Fast Lane)	0		18-Feb-20*
A12770	Apply RA and Obtain Approval of RA for Construction Inner Parapet	7	19-Feb-20	25-Feb-20
A12780	Apply CNP and Obtain Approval of CNP for Construction Inner Parapet	14	24-Jan-20*	06-Feb-20

**Construction of Inner Parapet**

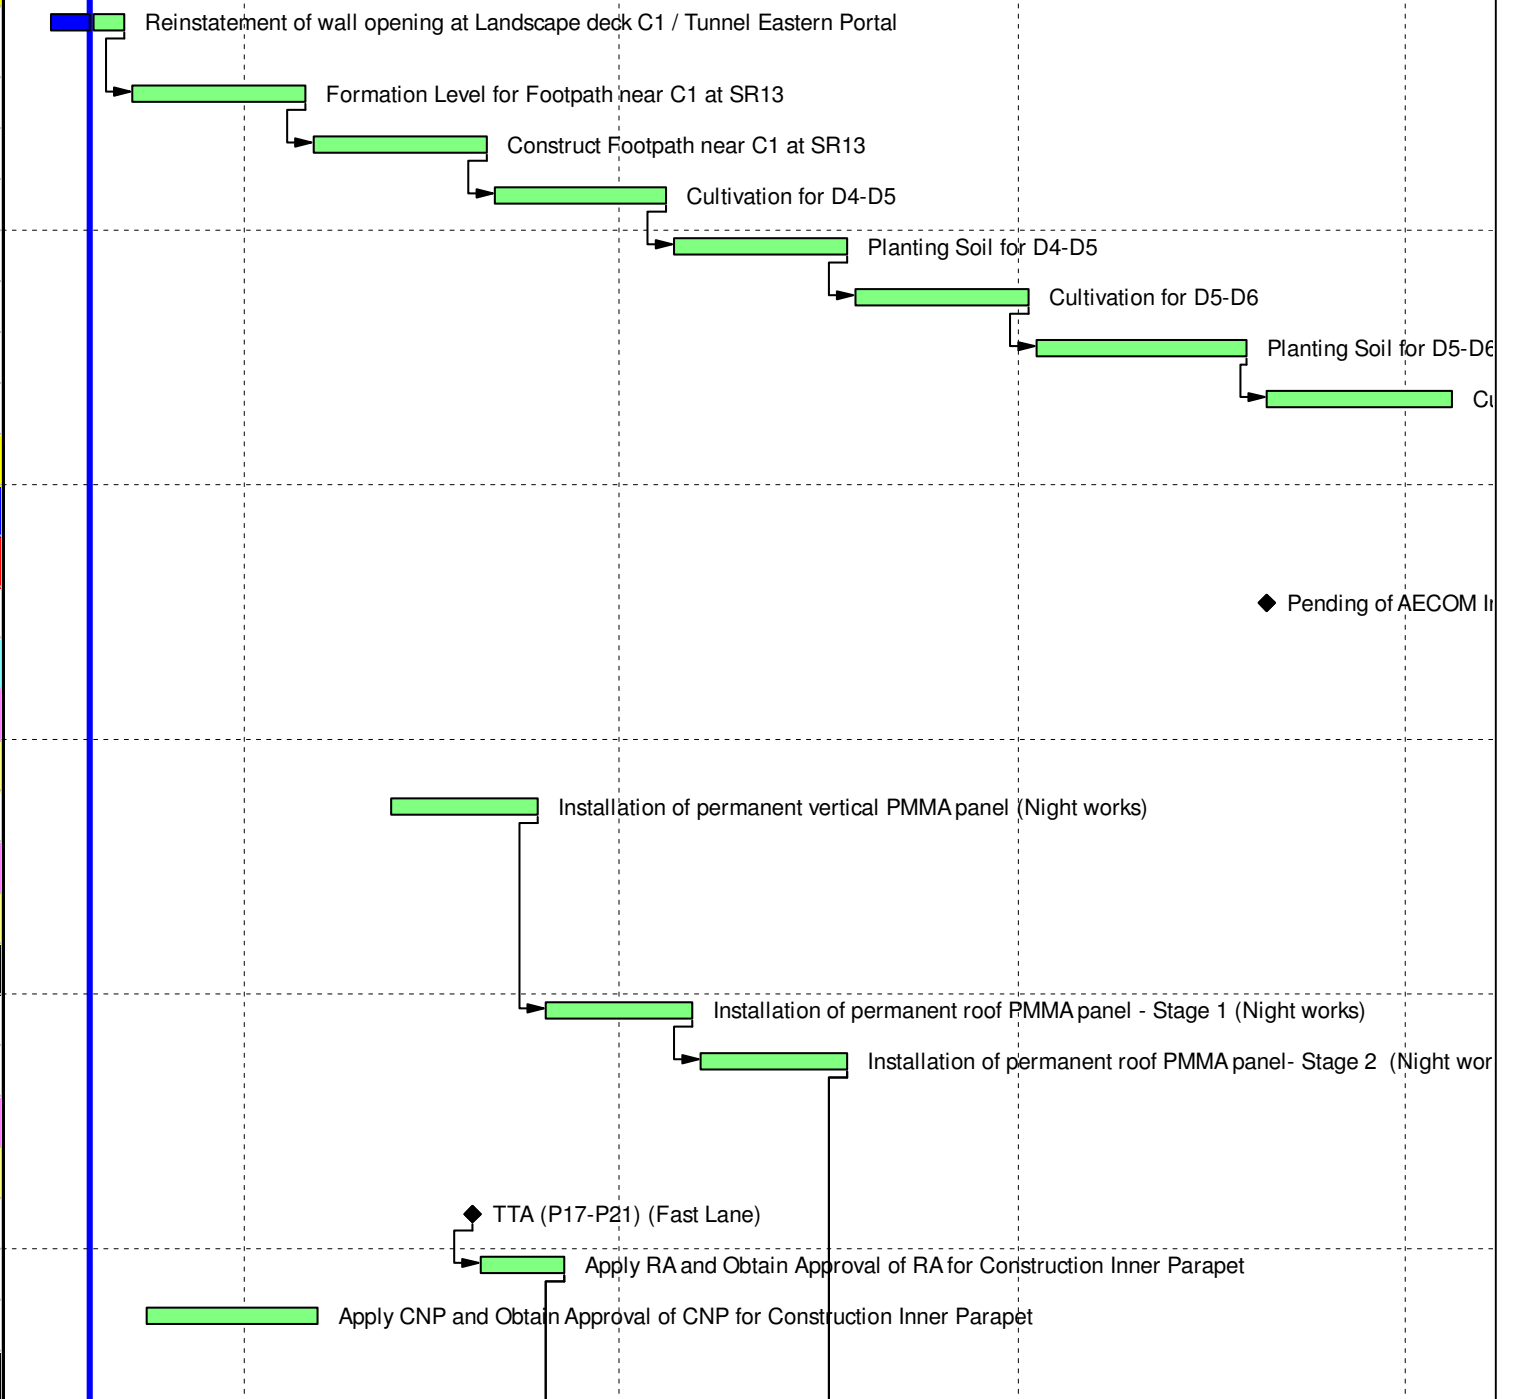


Remaining Level of Effort	Remaining Work
Actual Level of Effort	Critical Remaining Work
Actual Work	Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Jan.2020 to 20.Apr.2020)**







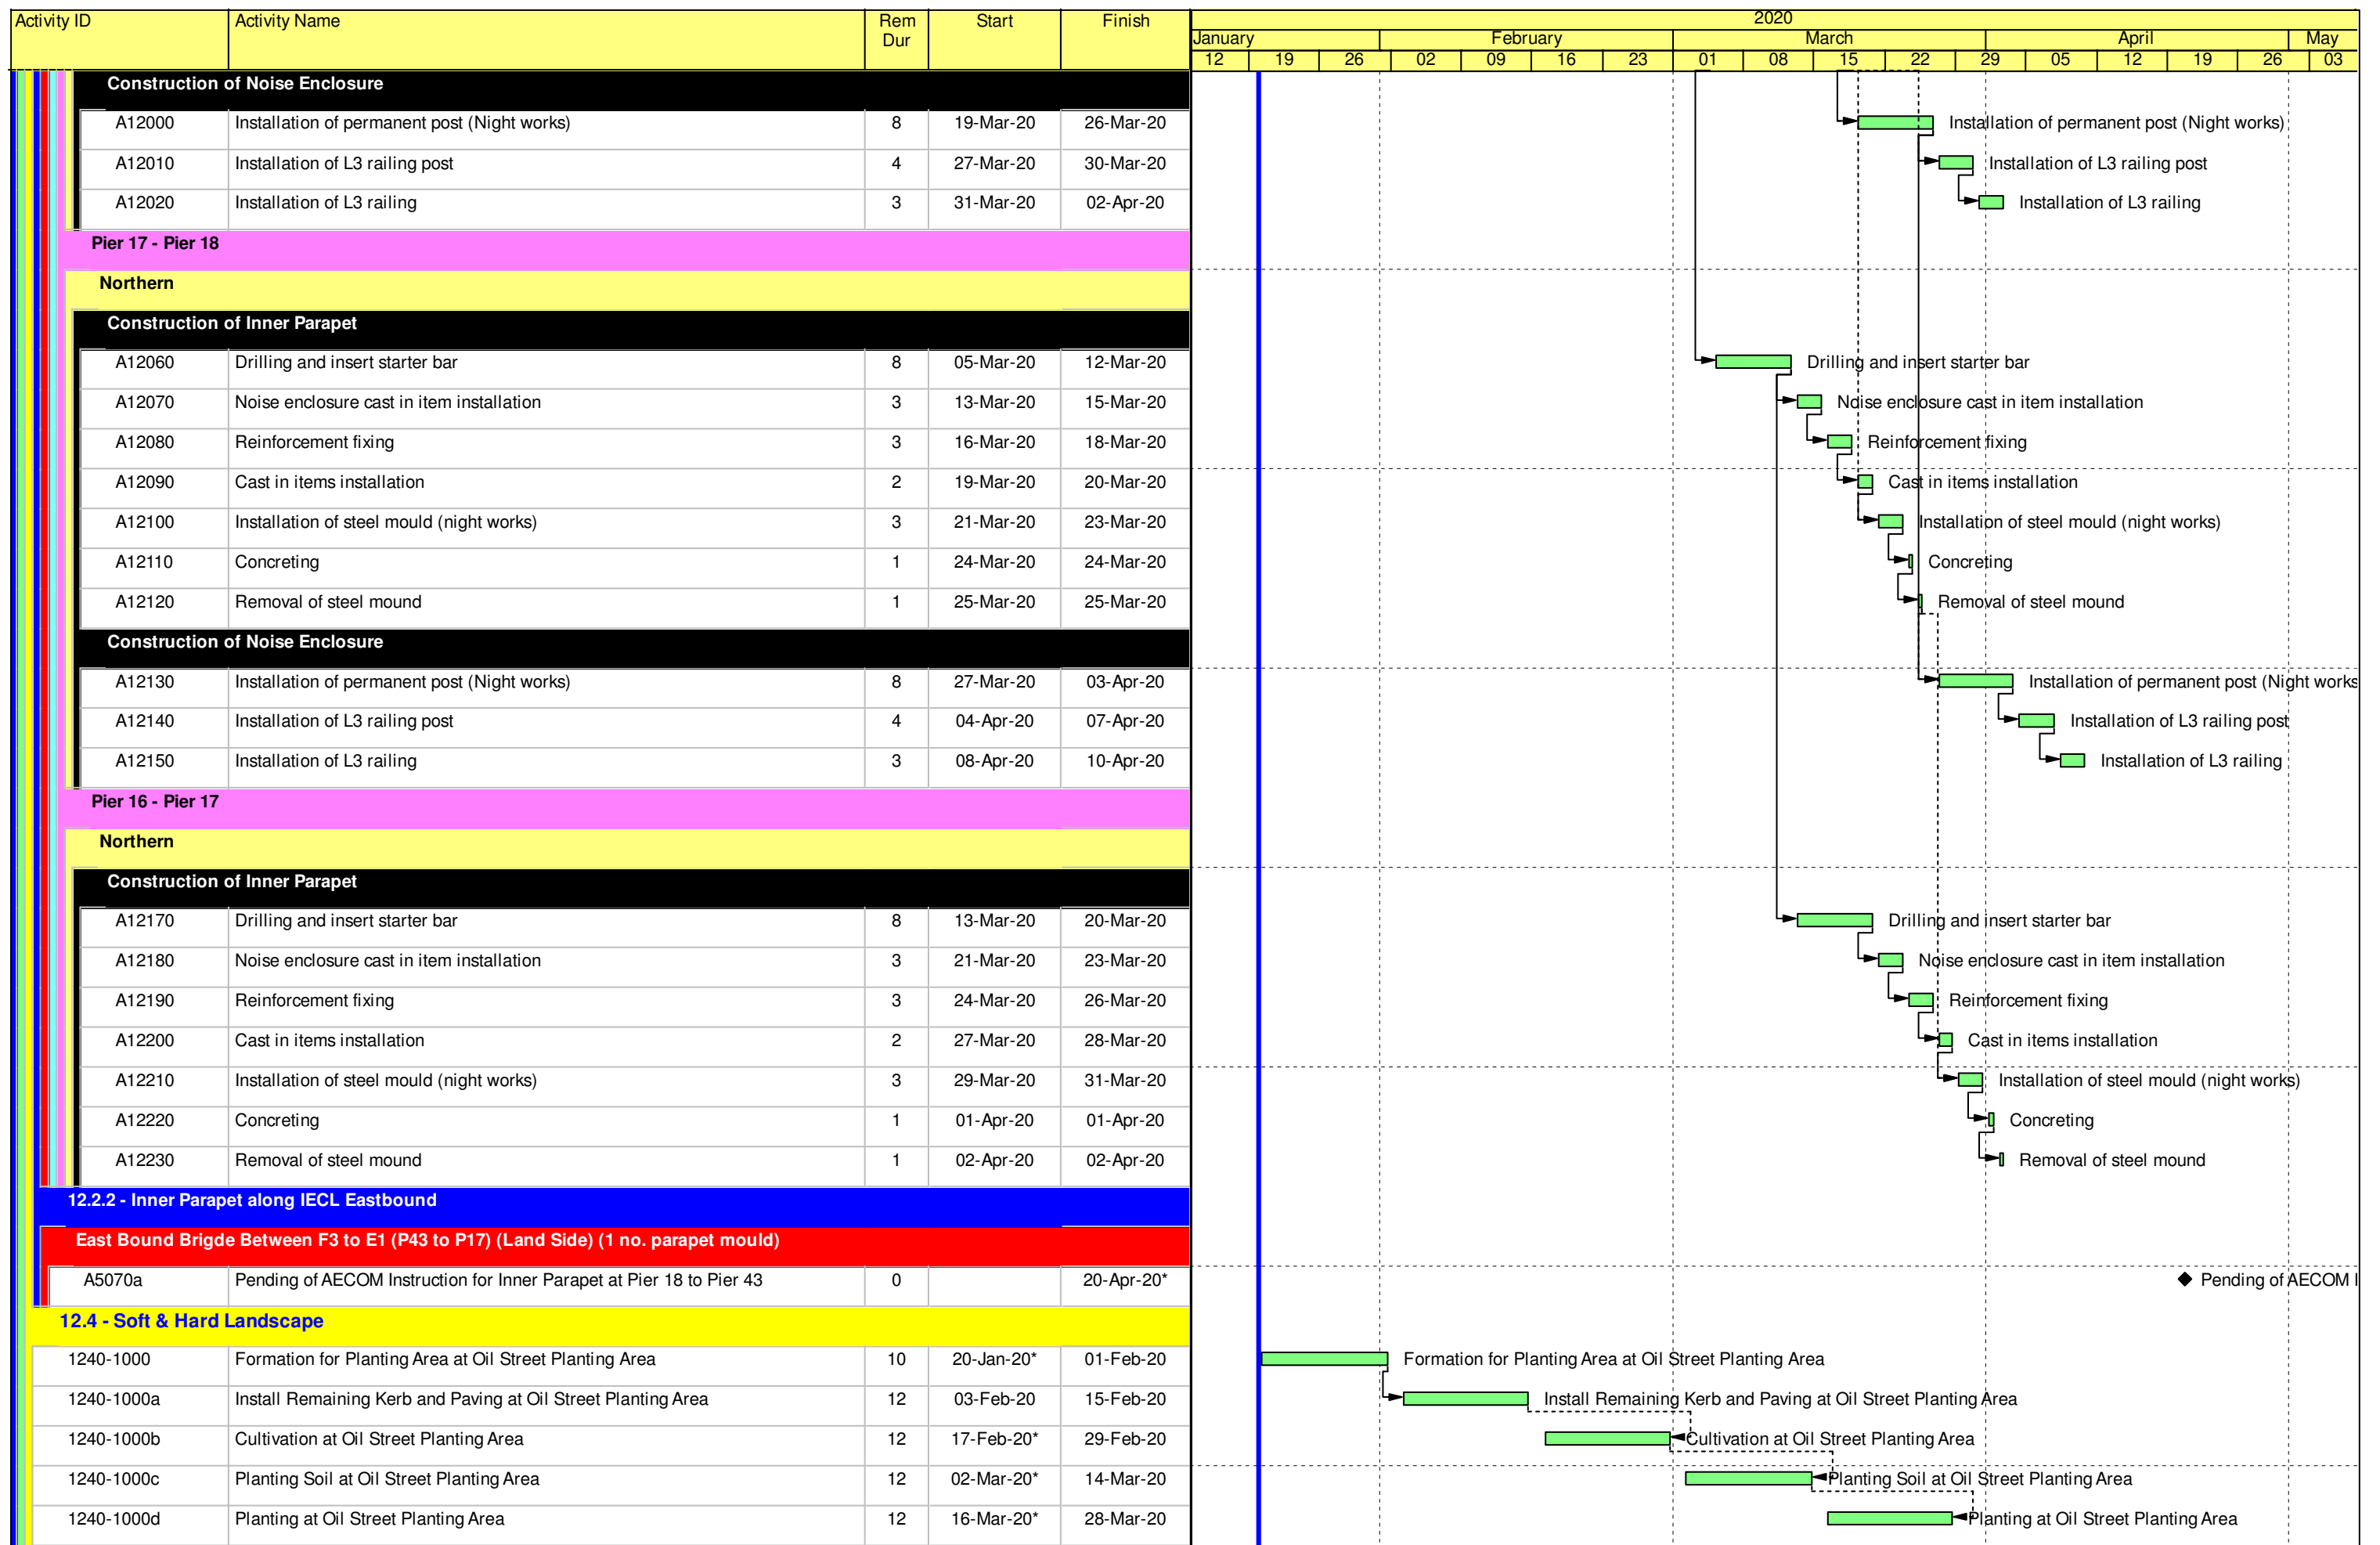

█ Remaining Level of Effort    █ Remaining Work  
█ Actual Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Jan.2020 to 20.Apr.2020)**





Activity ID	Activity Name	Rem Dur	Start	Finish	2020																
					January			February				March				April			May		
					12	19	26	02	09	16	23	01	08	15	22	29	05	12	19	26	03
1240-1040a	Laying Subbase for Footpath at Landscape Deck C5	12	17-Jan-20 A	04-Feb-20	Laying Subbase for Footpath at Landscape Deck C5																
1240-1040b	Laying Concrete Paver for Footpath at Landscape Deck C5	12	05-Feb-20	18-Feb-20	Laying Concrete Paver for Footpath at Landscape Deck C5																
1240-1060a2	Root barrier (Green roof) Stage 1 - 3 Bays	11	20-Jan-20 A	03-Feb-20	Root barrier (Green roof) Stage 1 - 3 Bays																
1240-1060a3	Root barrier (Green roof) Stage 2 - 3 Bays	12	04-Feb-20*	17-Feb-20	Root barrier (Green roof) Stage 2 - 3 Bays																
1240-1060b	Pending for AECOM instruction for Green Roof	0		20-Mar-20*	Pending for AECOM instruction for Green Roof																
1240-1060b1	Drainage composite (Green roof) Stage 1 - 2 Bays	12	20-Mar-20	02-Apr-20	Drainage composite (Green roof) Stage 1 - 2 Bays																
1240-1060b2	Drainage composite (Green roof) Stage 2 - 2 Bays	12	03-Apr-20	20-Apr-20	Drainage composite (Green roof) Stage 2 - 2 Bays																
1240-1330	Planting at Landscape Deck C3	12	19-Feb-20*	03-Mar-20	Planting at Landscape Deck C3																
1240-1340	Planting at Landscape Deck C4	12	05-Feb-20*	18-Feb-20	Planting at Landscape Deck C4																
1240-1350	Planting at Landscape Deck C5	12	19-Feb-20*	03-Mar-20	Planting at Landscape Deck C5																
<b>13 - SECTION 13 OF THE WORKS</b>																					
<b>13.2 - Roadworks</b>																					
1320-1010	Issue XP for Rumsey Street Flyover Construct Meter Box Works by AECOM	0		23-Jan-20*	Issue XP for Rumsey Street Flyover Construct Meter Box Works by AECOM																
1320-1010a	Issue XP for Rumsey Street Flyover Modification Works by AECOM	0		05-Feb-20*	Issue XP for Rumsey Street Flyover Modification Works by AECOM																
1320-1010b	Apply RA and obtain approval of RA for Rumsey Street Flyover construct meter box works	6	24-Jan-20*	01-Feb-20	Apply RA and obtain approval of RA for Rumsey Street Flyover construct meter box works																
1320-1010c	Excavation of Meter Box location	7	06-Feb-20	13-Feb-20	Excavation of Meter Box location																
1320-1010d	Connection of Meter box (by other) - stage 1	10	14-Feb-20	25-Feb-20	Connection of Meter box (by other) - stage 1																
1320-1010e	Connection of Meter box (by other) - stage 2	10	26-Feb-20	07-Mar-20	Connection of Meter box (by other) - stage 2																
1320-1020	Preparation of method statement for Rumsey Street Flyover Modification Works	10	29-Jan-20*	08-Feb-20	Preparation of method statement for Rumsey Street Flyover Modification Works																
1320-1020a	Obtain approval of MS for Rumsey Street Flyover Modification Works	12	10-Feb-20	22-Feb-20	Obtain approval of MS for Rumsey Street Flyover Modification Works																
1320-1030	Preparation and Obtain approval of TTA for Rumsey Street Flyover Modification Works	0		05-Feb-20*	Preparation and Obtain approval of TTA for Rumsey Street Flyover Modification Works																
1320-1030a	Apply RA and obtain approval of RA for Rumsey Street Flyover Modification Works	7	06-Feb-20	13-Feb-20	Apply RA and obtain approval of RA for Rumsey Street Flyover Modification Works																
1320-1030b	Implementation of TTA	2	14-Feb-20	15-Feb-20	Implementation of TTA																
1320-1040	Trim off Existing Parapet (Type 1 Enlarged Parapet) - Stage 1	12	09-Mar-20	21-Mar-20	Trim off Existing Parapet (Type 1 Enlarged Parapet) - Stage 1																
1320-1040a	Trim off Existing Parapet (Type 1 Enlarged Parapet) - Stage 2	12	23-Mar-20	06-Apr-20	Trim off Existing Parapet (Type 1 Enlarged Parapet) - Stage 2																
1320-1040b	Trim off Existing Parapet (Type 1 Enlarged Parapet) - Stage 3	12	07-Apr-20	22-Apr-20	Trim off Existing Parapet (Type 1 Enlarged Parapet) - Stage 3																
<b>16 - SECTION 13B OF THE WORKS</b>																					
<b>16.1 - Soft Landscape</b>																					
1610-1100	Establishment Works at Portion IIA	365	20-Jan-20	18-Jan-21	Establishment Works at Portion IIA																

█ Remaining Level of Effort    █ Remaining Work  
█ Actual Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Jan.2020 to 20.Apr.2020)**



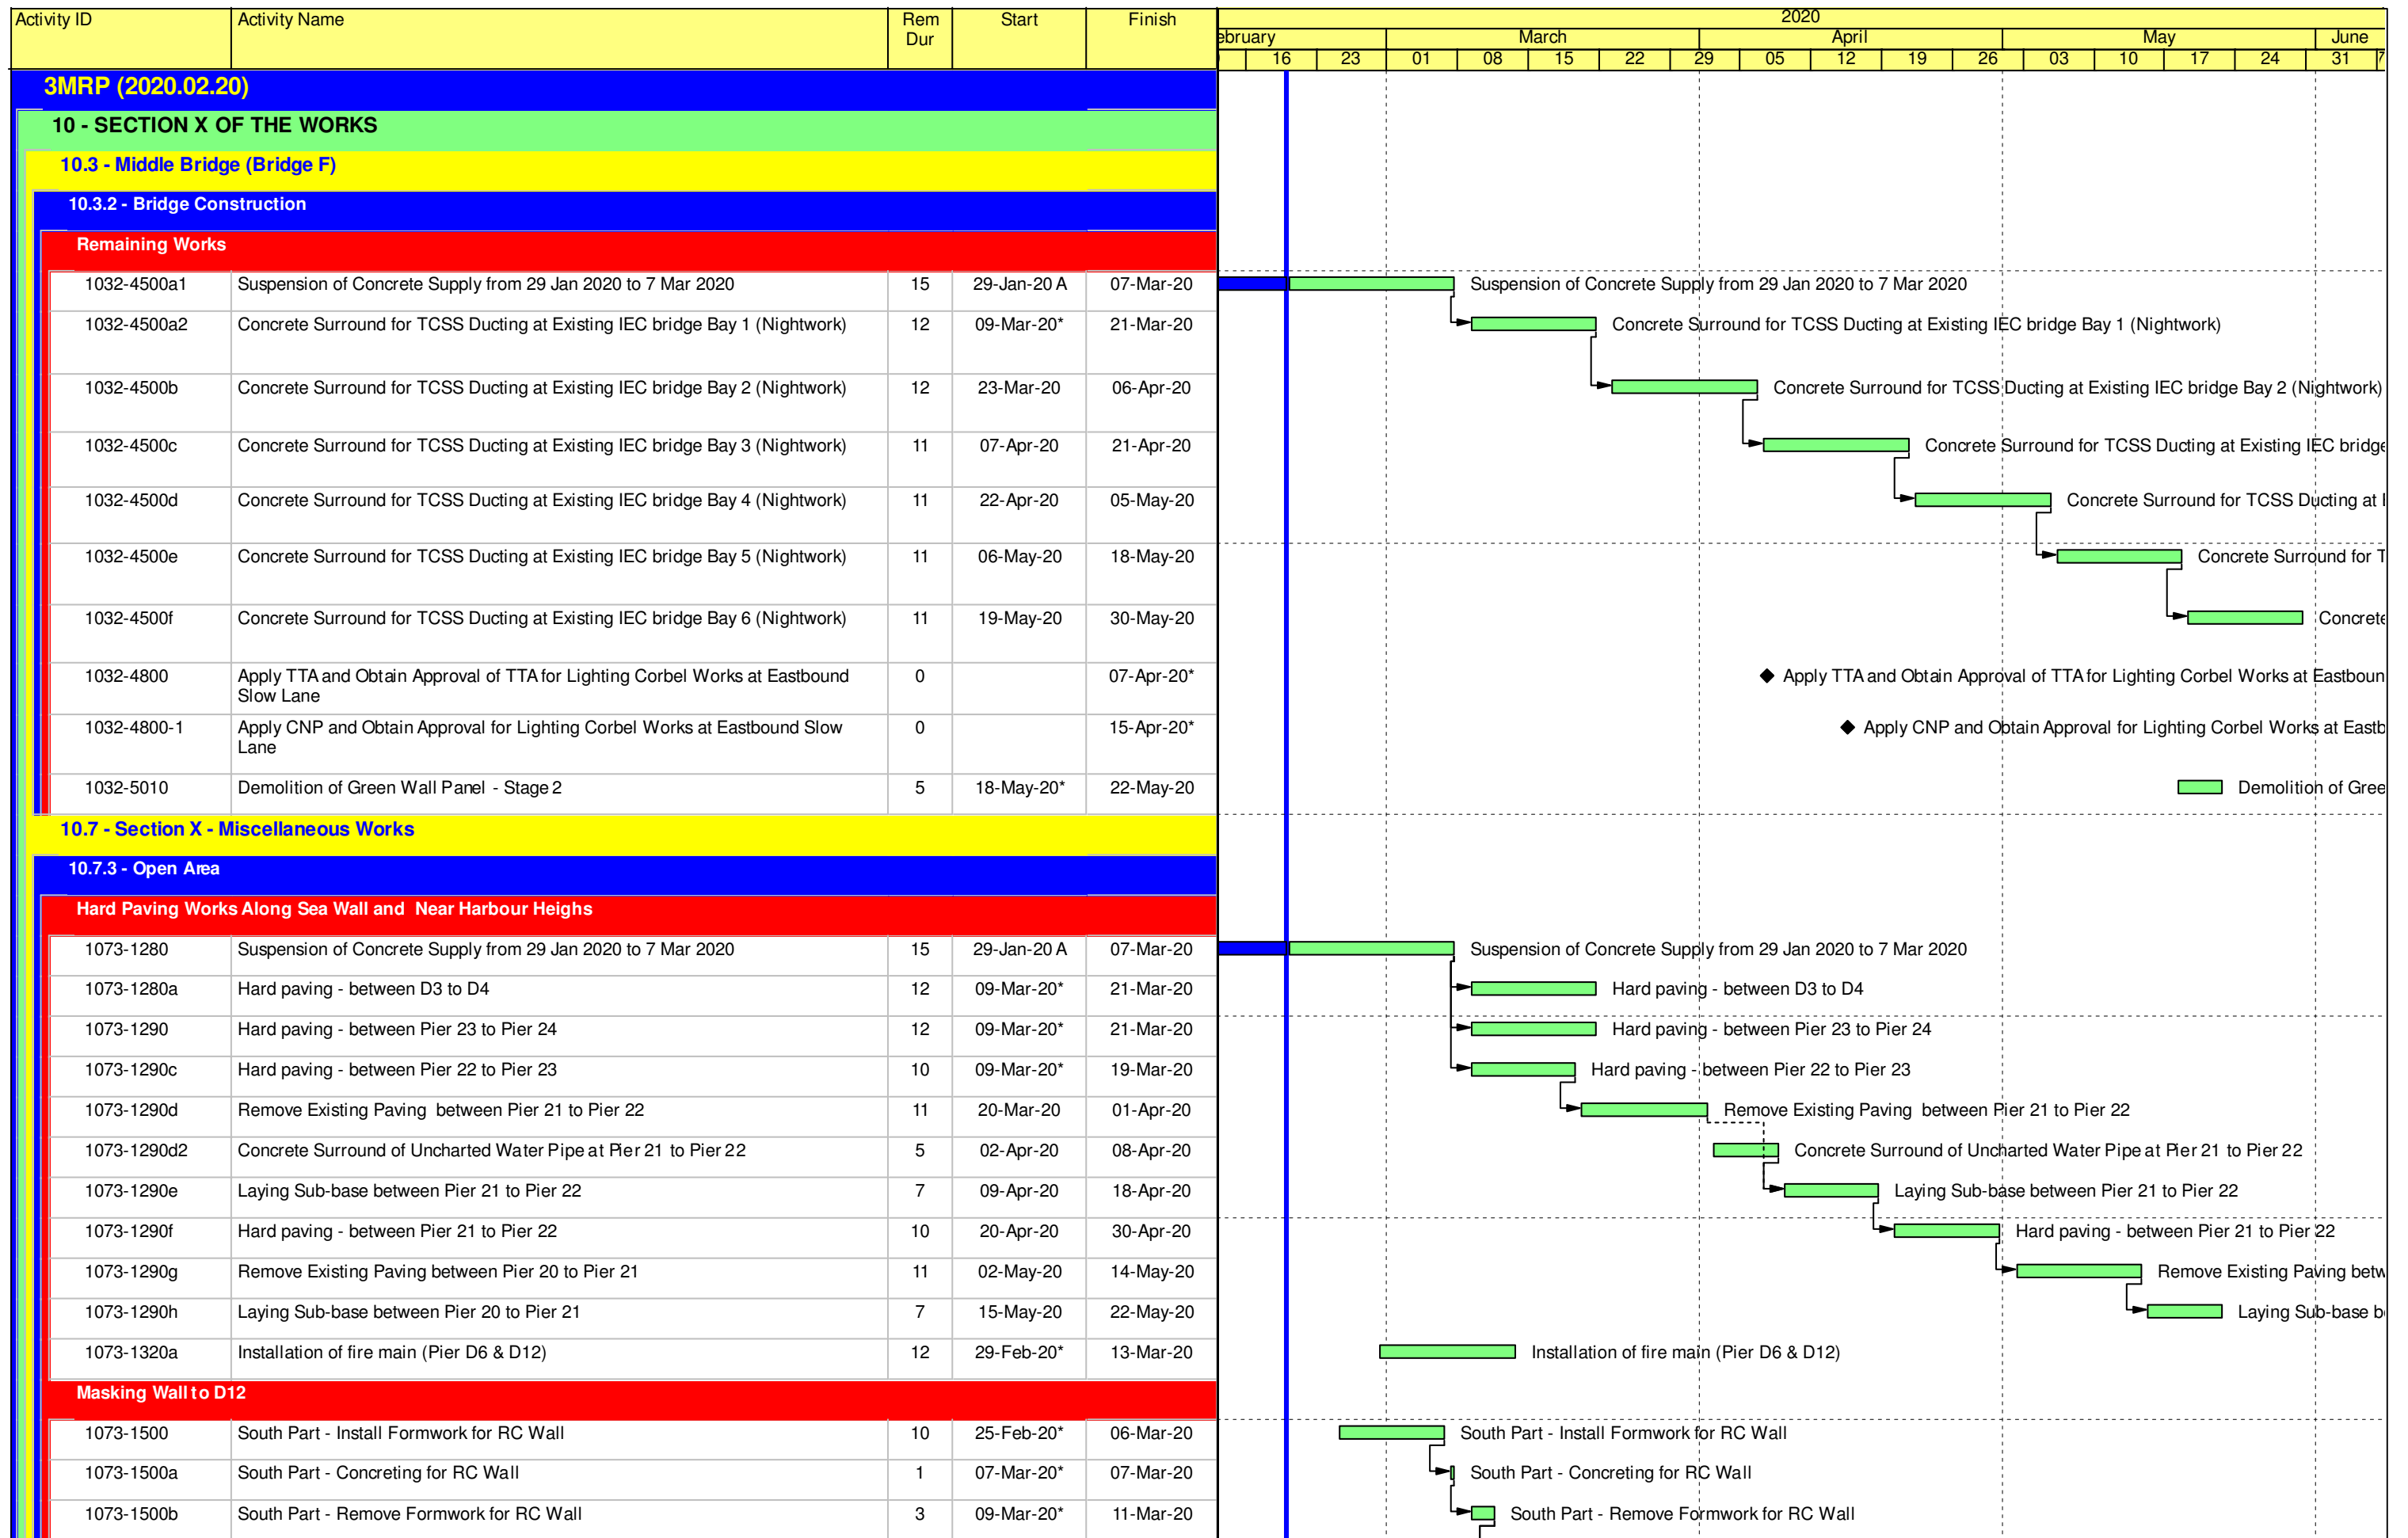


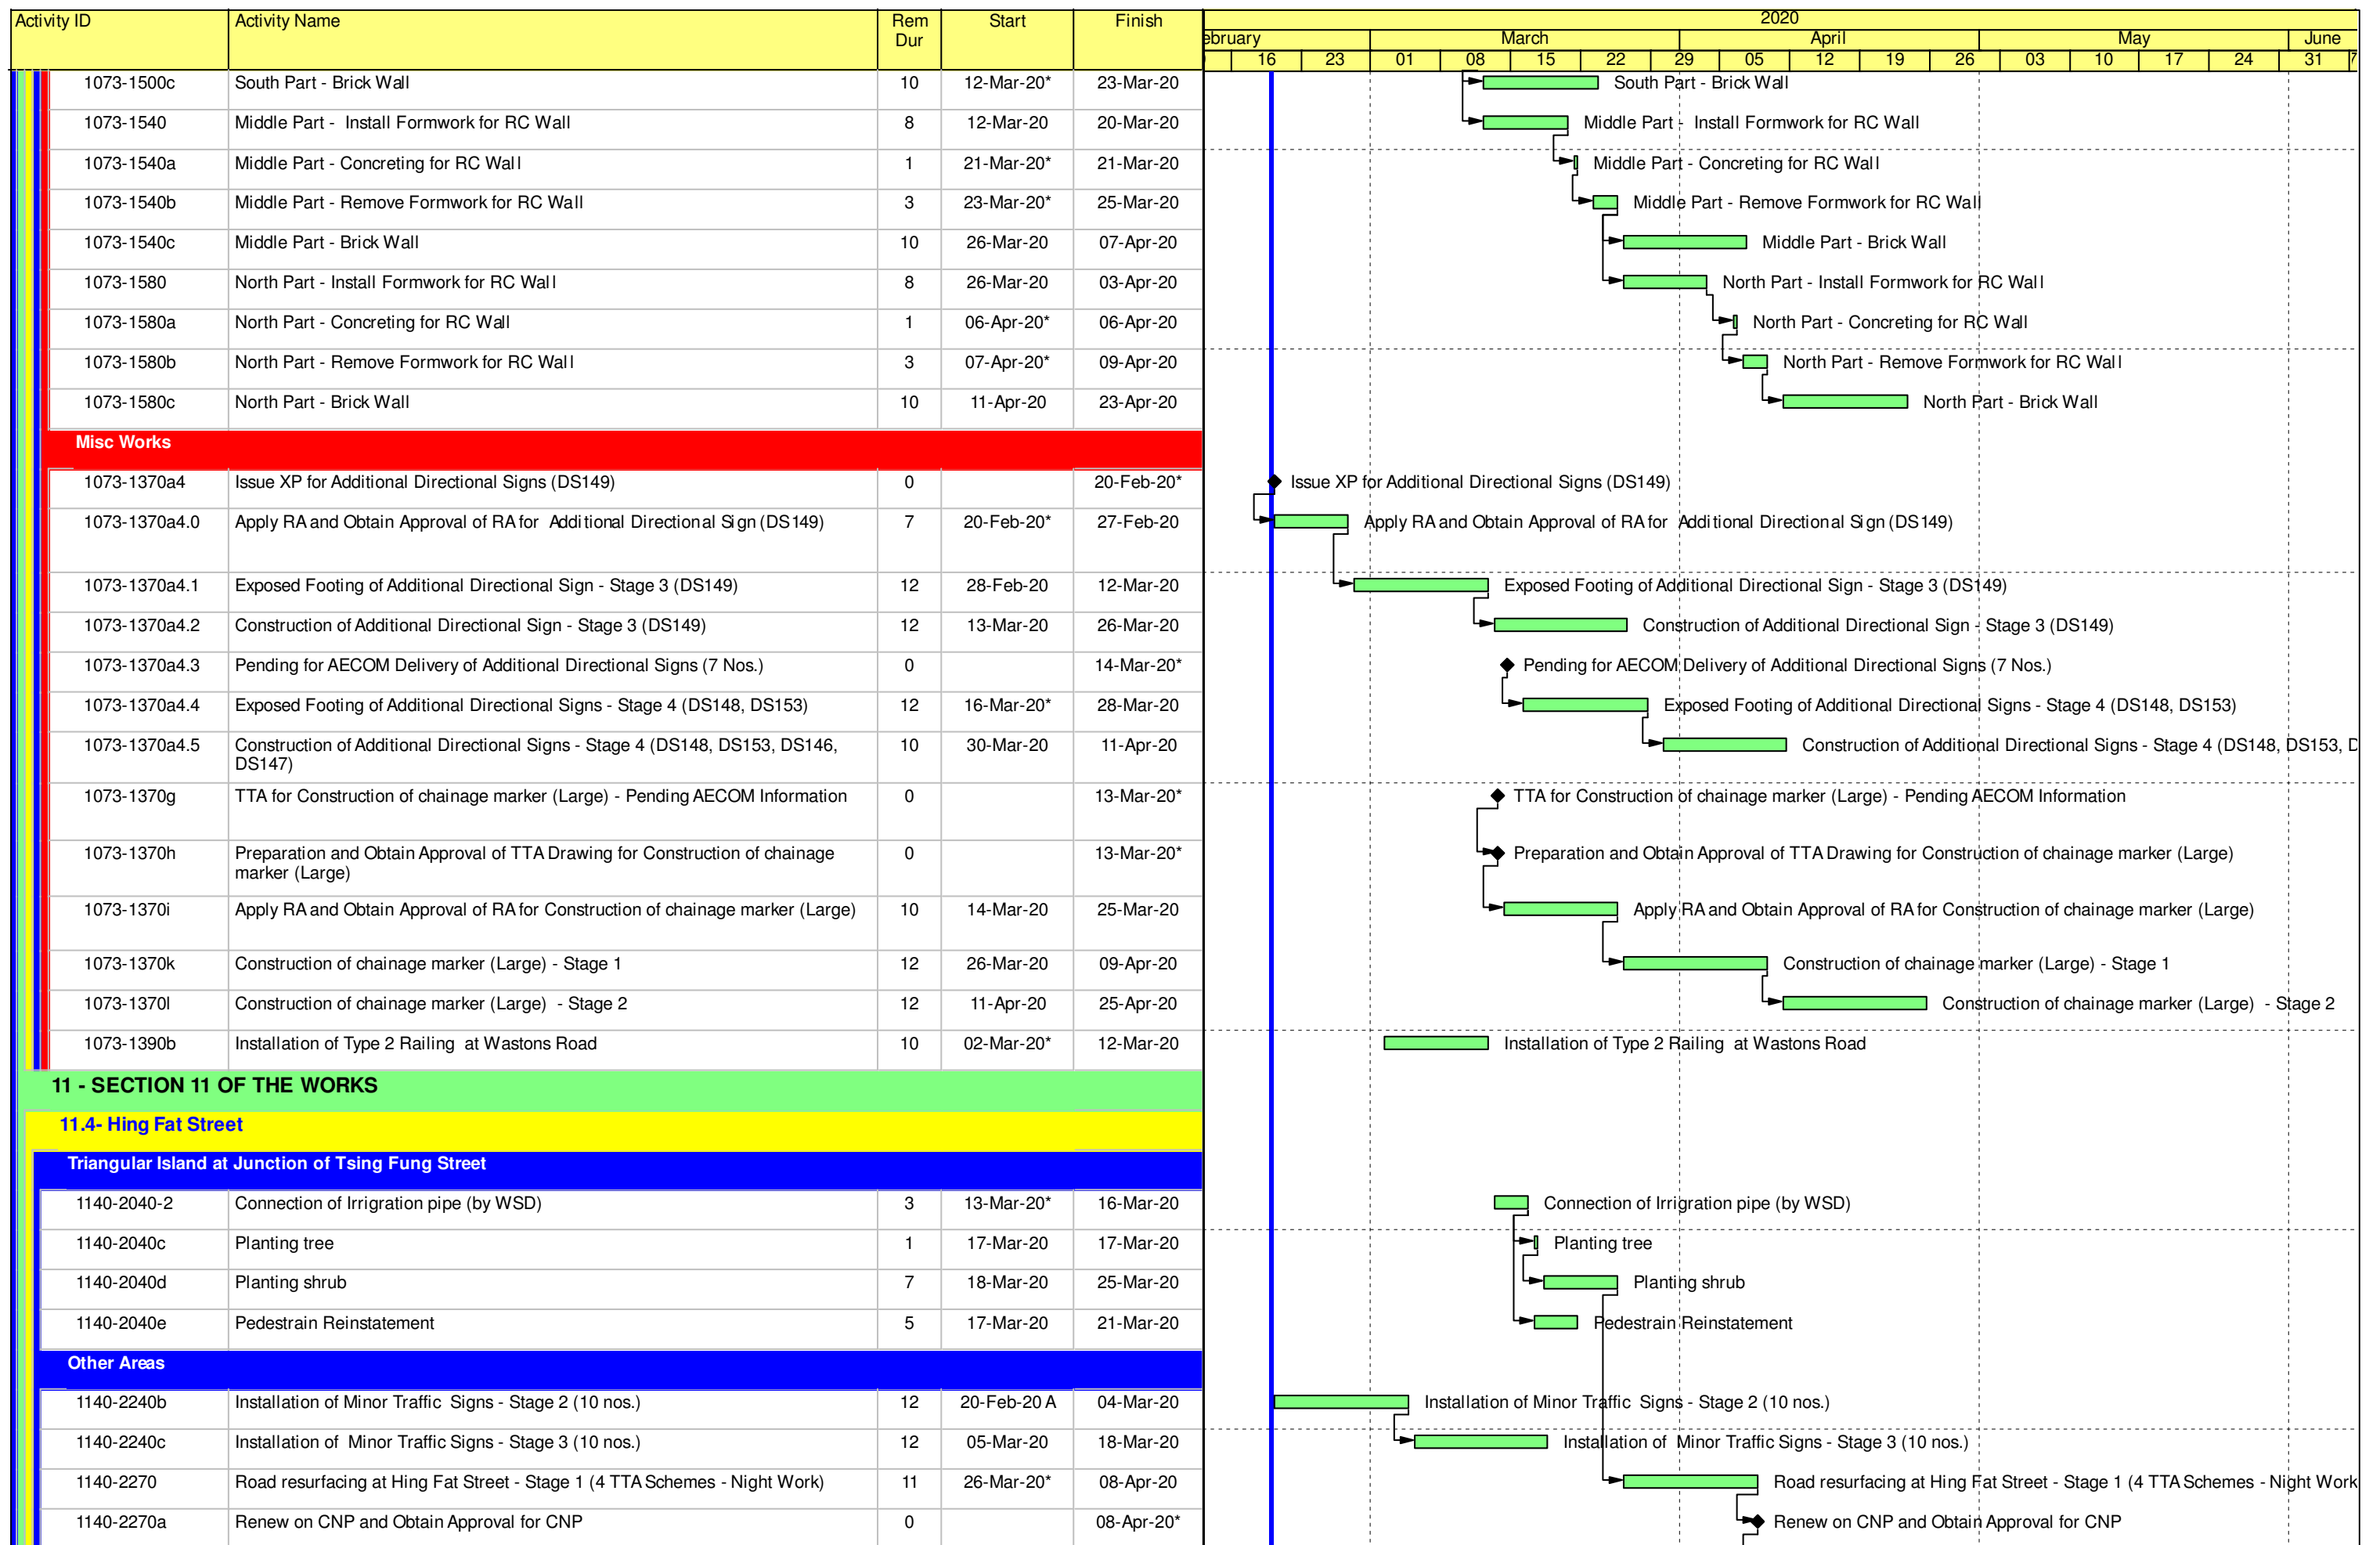

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Feb.2020 to 20.May.2020)**






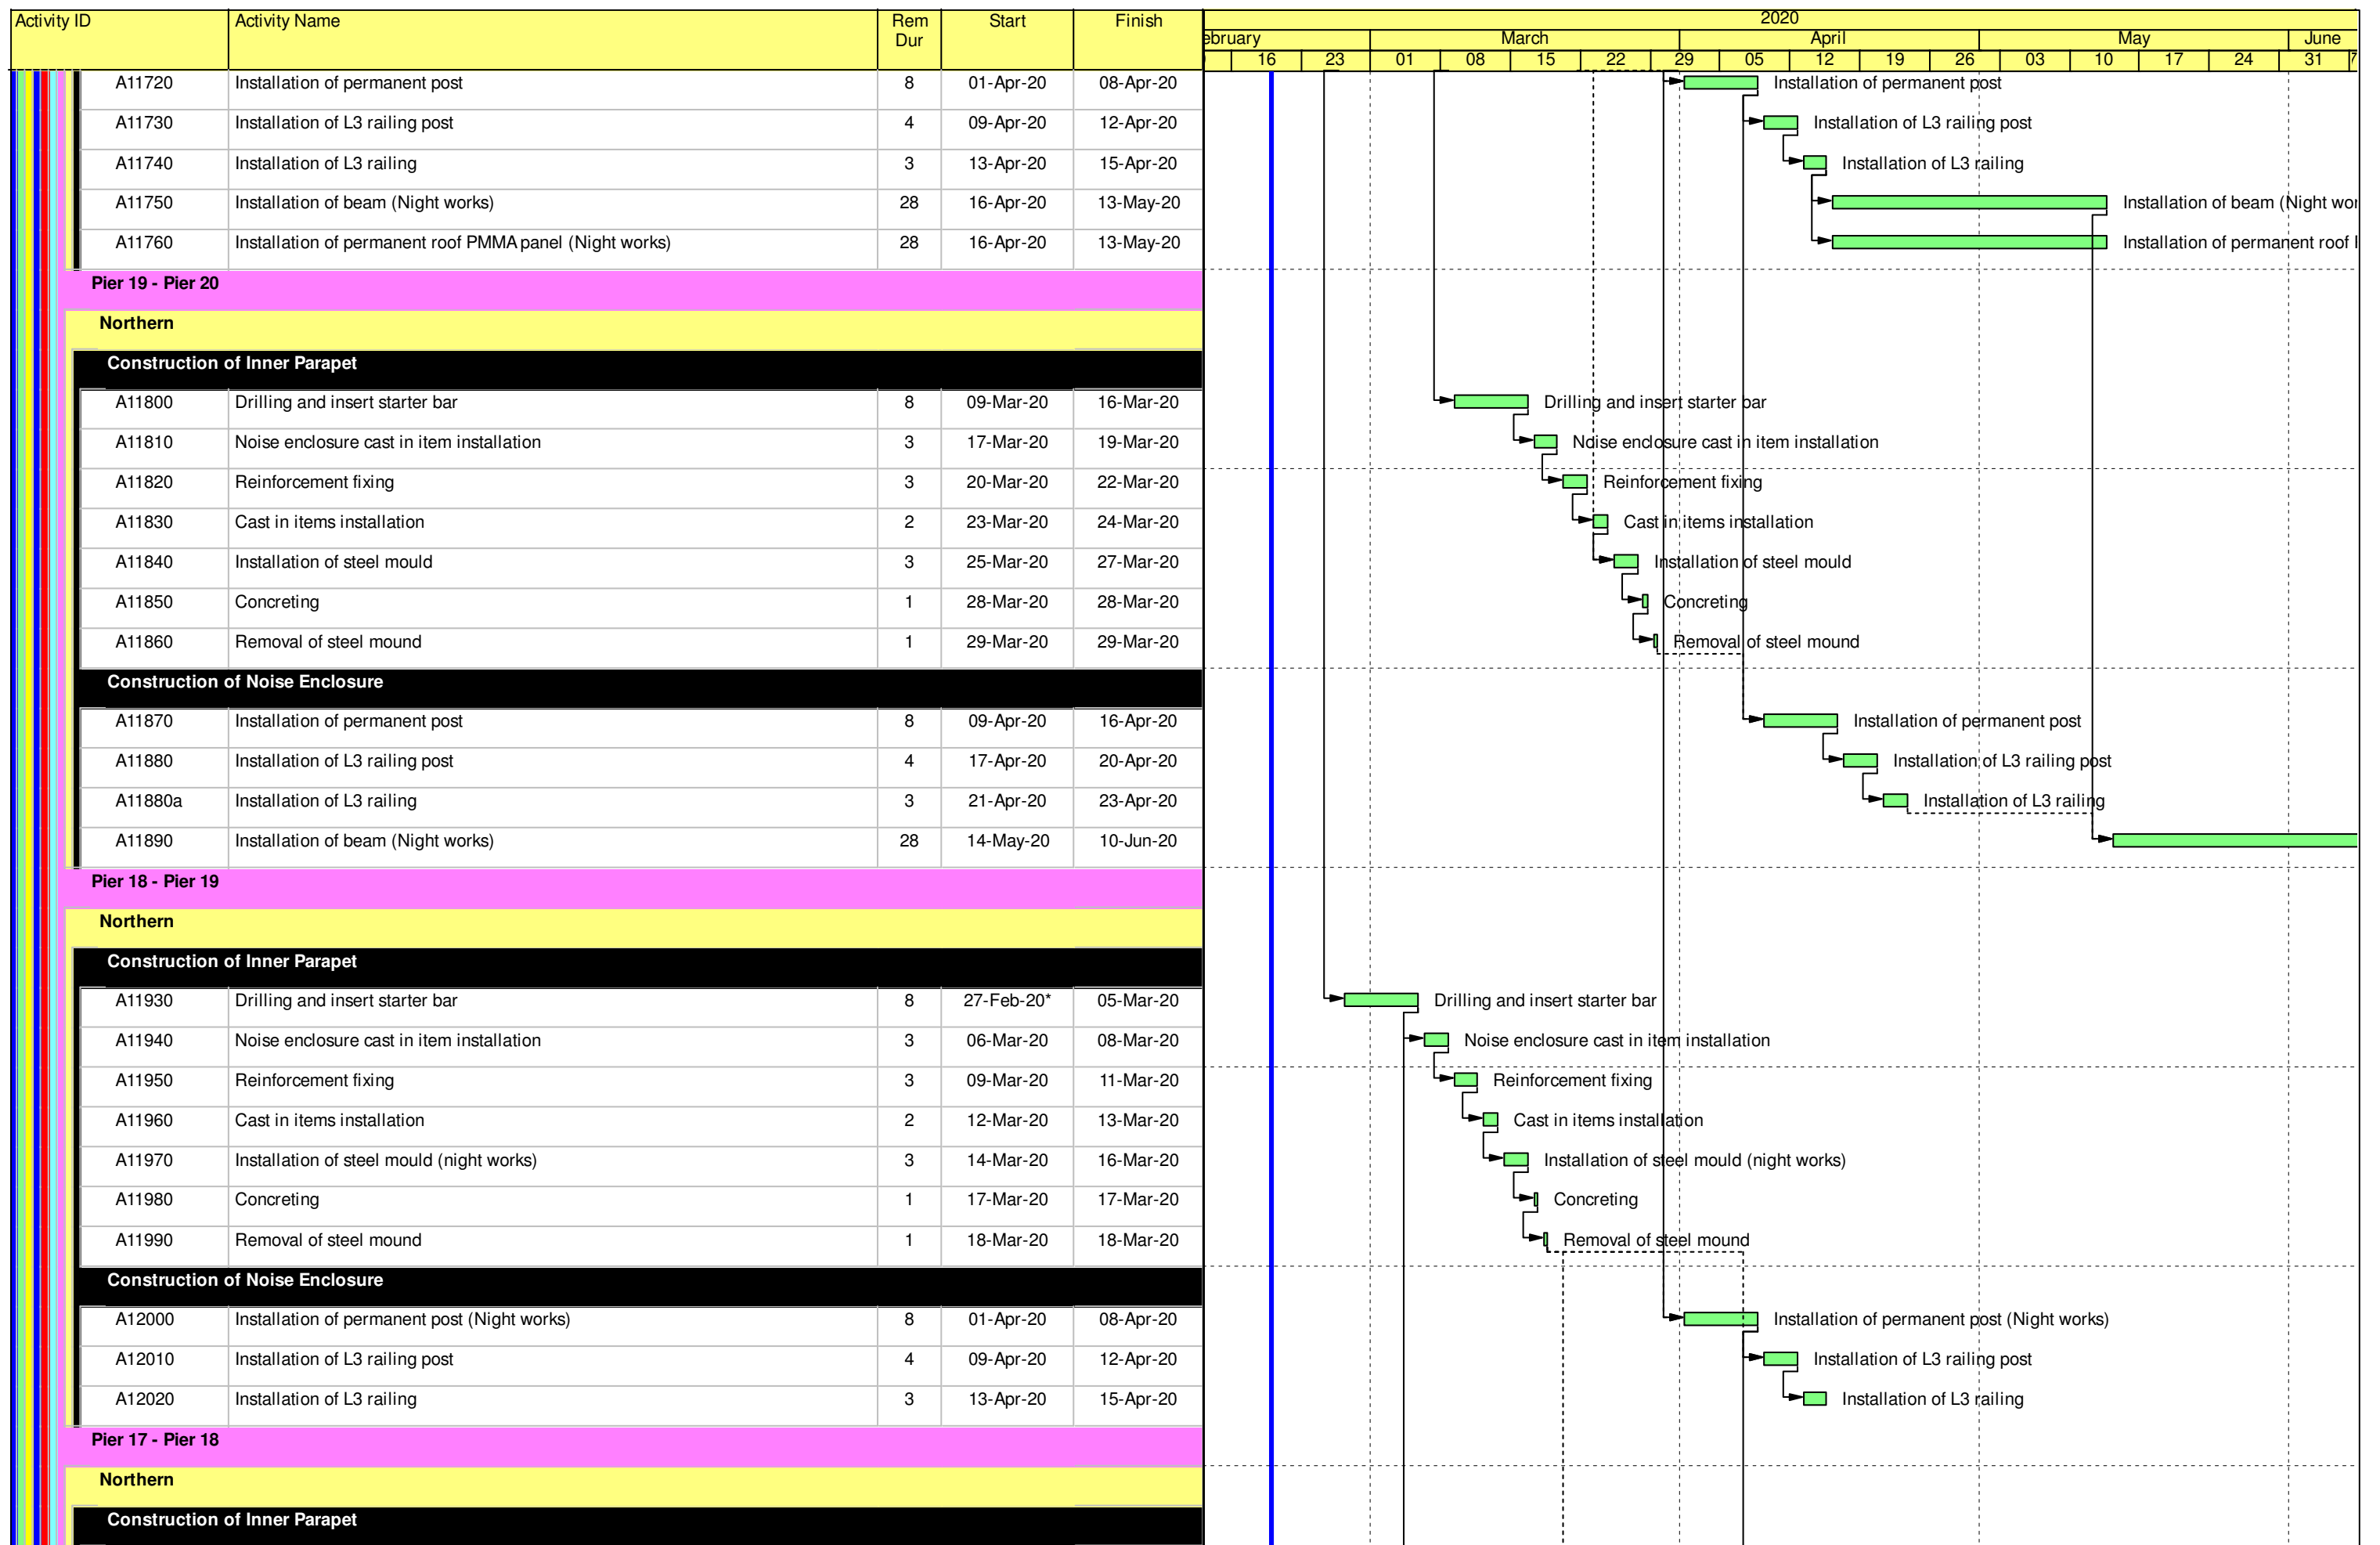

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Feb.2020 to 20.May.2020)**





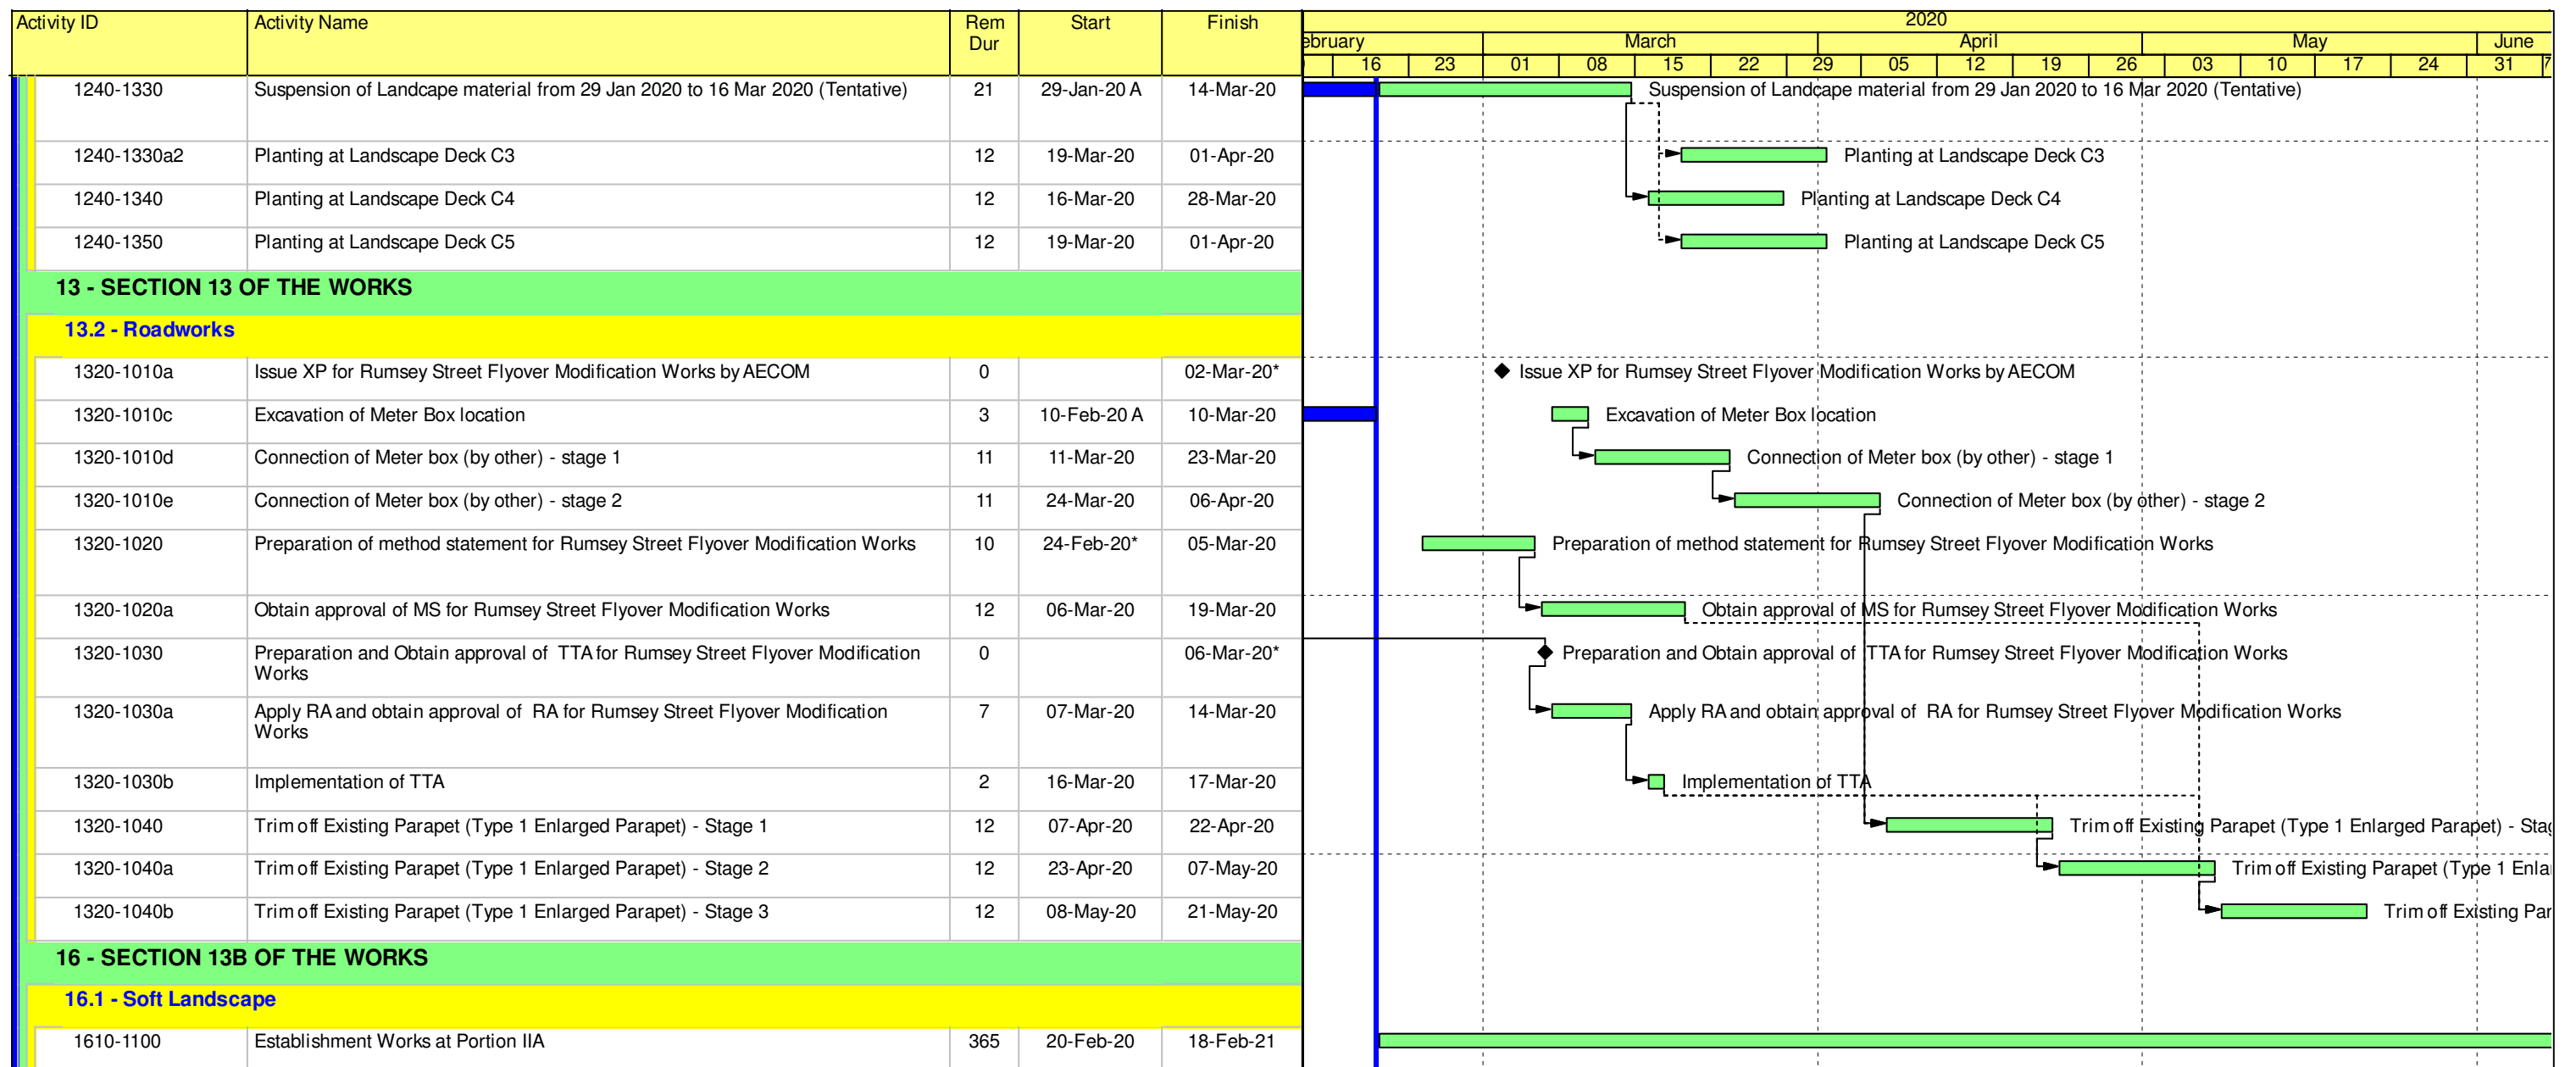

█ Remaining Level of Effort    █ Remaining Work  
█ Actual Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone



Activity ID	Activity Name	Original Duration	Start	Finish	2020															
					Jan	Feb	Mar	Apr												
<b>Total</b>		385.0	31-Mar-19 A	03-May-20																
<b>DWP-08 - (2) - Update Progress As of 20 Jan 20</b>		385.0	31-Mar-19 A	03-May-20																
<b>KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks</b>		385.0	31-Mar-19 A	03-May-20																
<b>KD11 - Section 7A: Portion XIV &amp; XV (Victoria Park Open Space)</b>		365.0	31-Mar-19 A	29-Feb-20																
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365.0	31-Mar-19 A	29-Feb-20																Establishment Works - for Landscape Softworks and transplanted trees in Portion XV
<b>KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH&gt;500mm)</b>		365.0	20-Apr-19 A	03-May-20																
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365.0	20-Apr-19 A	03-May-20																
<b>KD18 - Section 11: Transplanted Trees DBH&gt;500mm in Portion VA and XII</b>		365.0	20-Apr-19 A	03-May-20																
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365.0	20-Apr-19 A	03-May-20																



- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Date	Revision	Checked	Approved
20-Jan-20	DWP-08 (2) - 3 Months Rolling	TL	TL

Data Date: 20-Feb-20

# CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

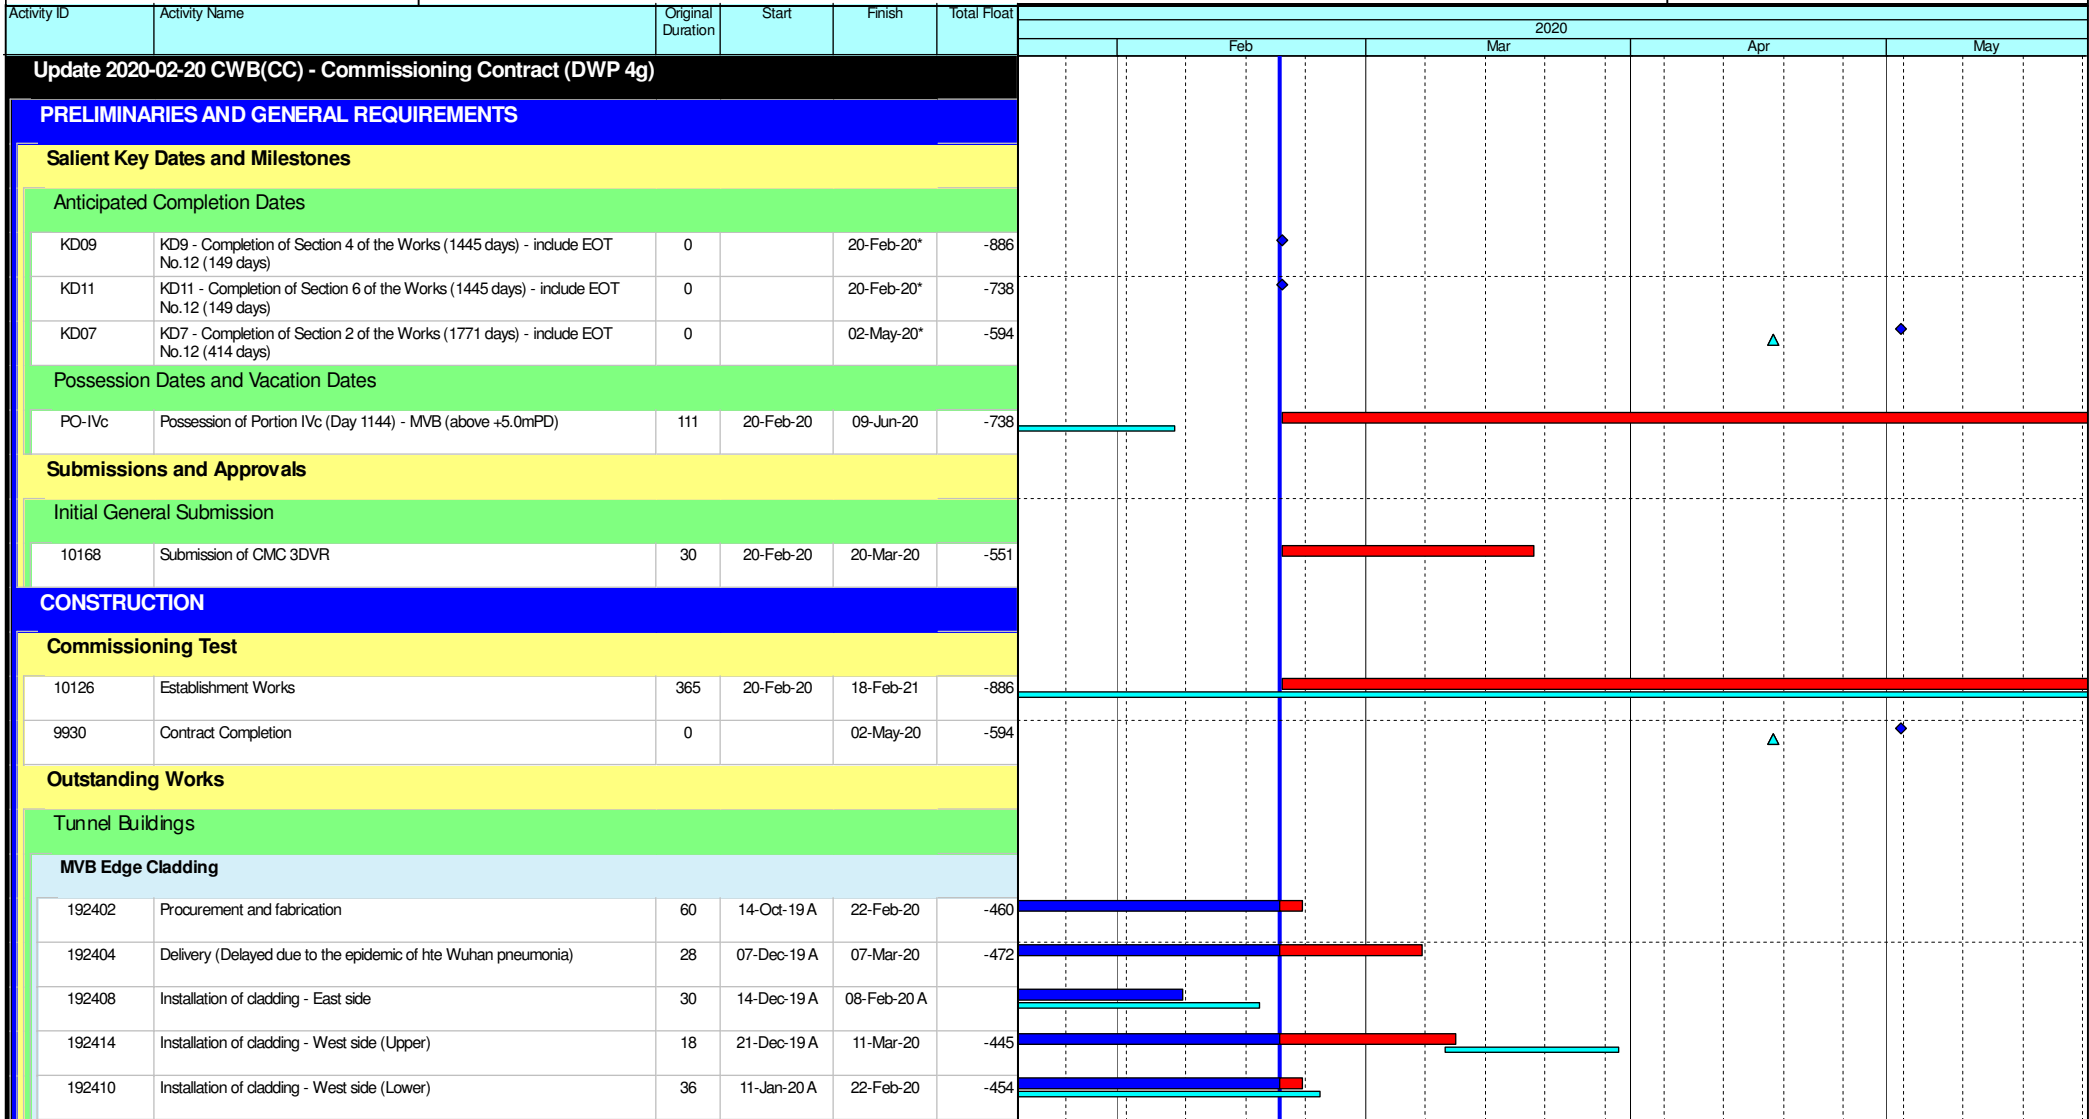

## Leighton Contractors (Asia) Limited Programme Update 72 (February 2020) THREE MONTH ROLLING

Project ID: H2613-U072  
 Baseline: DWP4g  
 Layout: Update Three Month Rolling  
 U072  
 Page 1 of 2



Date	Revision	Checked	Approv...
20-Jan-2...	U071	AT	CW
20-Feb-2...	U072	AT	CW



Data Date: 20-Feb-20

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

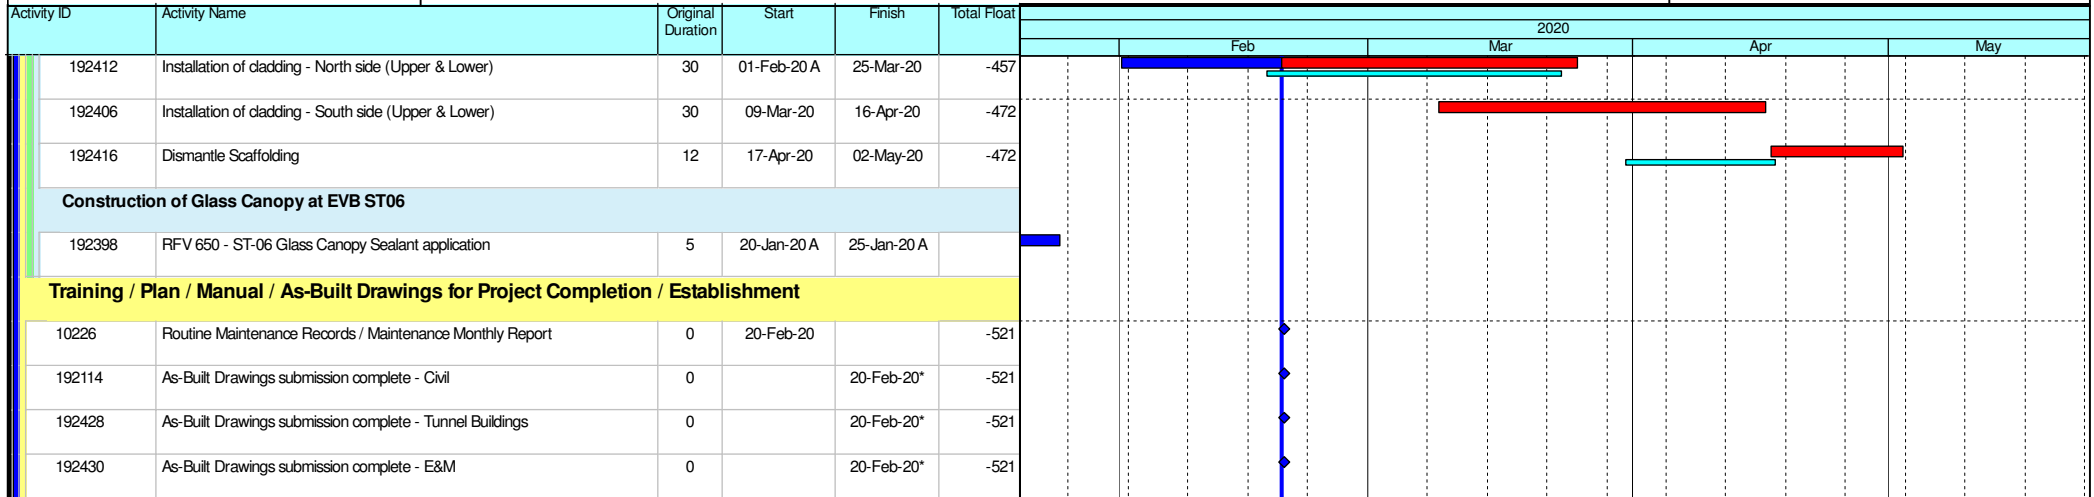

### Leighton Contractors (Asia) Limited Programme Update 72 (February 2020) THREE MONTH ROLLING

Project ID: H2613-U072  
 Baseline: DWP4g  
 Layout: Update Three Month Rolling  
 U072  
 Page 2 of 2

Date	Revision	Checked	Approv...
20-Jan-2...	U071	AT	CW
20-Feb-2...	U072	AT	CW
