

# Programme for Outstanding and Defective Works

CSF: PR/S-0336 REV D  
APPENDIX A

ID	Task Name	Duration	Start	Finish	Finish (Programme dd 25 June 2019)	Qtr 3, 2019							Qtr 4, 2019																				
						July 28	29	30	31	August 32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52	1		
1	1. Site Formation Drainage Works, K1 Kerb with Subbase Pavement and Chain Link Fences/Access Gates in WCR1 to WCR4	315 days	20 February 2019	31 December 2019	31 December 2019	→																											
15	2. Rectification of Caisson Seawalls and Installation of Corrosion Monitoring System (CMS) of Caisson Seawalls in WCR1 and WCR3	136 days	20 February 2019	05 July 2019	05 July 2019	05/07																											
32	3. Rectification of 0.5T Rock Armour and Seabed Level (High Spot to be Trimmed) in WCR3	85 days	08 June 2019	31 August 2019	31 August 2019	→ 31/08																											
43	4. Rectification of Grade 400 Rockfill and 0.5T Rock Armour in WCR1	68 days	14 June 2019	20 August 2019	04 August 2019	→ 20/08																											
52	5. Construction of EVA for Ferry Pier in WCR1 (Completed)	0 days	22 January 2019	22 January 2019	22 January 2019																												
53	6. Construction of Road Improvement Works and Reconstruction of Hung Hing Road under VO254 (Footpath Pavement, Roadside Barrier, Irrigation System, Road Lighting System), and Reinstatement of Associated Existing Footpath on Hung Hing Road	302 days	02 October 2018	30 July 2019	30 July 2019	→ 30/07																											
78	7. Blockwork Seawalls (Construction of Remaining Seawall Coping) in WCR4 (Completed)	0 days	09 January 2019	09 January 2019	09 January 2019																												
80	8. Completion of Remaining Grade 400 for Seawalls in WCR4 (Completed)	77 days	26 February 2019	13 May 2019	13 May 2019																												
94	9. Completion of Remaining Backfilling Works in WCR4 (Completed)	0 days	19 February 2019	19 February 2019	19 February 2019																												
95	10. Reinstatement of Existing Seabed Level in TWCR4 (Completed)	145 days	03 April 2019	25 August 2019	25 August 2019	→ 25/08																											
113	11. Construction of Landing Steps (Type 10 and Type 11 Seawalls) in Ex-Helipad	170 days	03 March 2019	19 August 2019	19 August 2019	→ 19/08																											
205	12. Reinstatement of Existing Seawall at Box Culvert O Temporary Diversion in Ex-PWCA Basin (Completed)	0 days	14 January 2019	14 January 2019	14 January 2019																												
207	13. Reinstatement of Existing Pavement and Drainage System in Ex-Helipad	79 days	02 June 2019	19 August 2019	19 August 2019	→ 19/08																											
248	14. Rectification of Granite Facing Stone on Existing Seawall in WCR4 and Ex-PWCA Basin (70nos.)	28 days	17 July 2019	13 August 2019	13 August 2019	→ 13/08																											
252	15. Reinstatement of Hung Hing Road and Wan Shing Street in Accordance to Hung Hing Road Traffic Diversion Reinstatement Stage 0.5 Scheme Under VO No. 257 on Hung Hing Road	248 days	01 March 2019	03 November 2019	26 October 2019	→ 03/11																											
576	16. Reinstatement of LCSD Sitting Out Area underneath Hung Hing Road Flyover on Hung Hing Road	17 days	08 May 2019	24 May 2019	24 May 2019																												
582	17. Completion of Notice Submission of CWXP No. C000266 on Hung Hing Road, Wan Shing Street and Expo Drive East (Notional)	0 days	20 September 2019	20 September 2019	20 September 2019	→ 20/09																											
584	18. Completion of Notice Submission of XP No. 1202793 on Expo Drive East	0 days	20 April 2019	20 April 2019	20 April 2019																												
585	19. Modification Work inside Room of Hung Hing Road Flyover (Completed)	9 days	21 March 2019	29 March 2019	29 March 2019																												
590	20. Ladder Installation Inside Room of Hung Hing Road (Completed)	9 days	21 March 2019	29 March 2019	29 March 2019																												
595	21. Defective Works of the Reinstatement of Hung Hing Road Flyover, such as Painting of Wall of Flyover, Touch-up Rust of Steel Door and Steel Vehicular Parapet and etc. (Completed)	34 days	24 March 2019	26 April 2019	26 April 2019																												
601	22. Establishment Period for 8nos. (6nos.) of Trees Being Transplanted Back Underneath Hung Hing Road Flyover	366 days	11 June 2019	10 June 2020	10 June 2020	→																											
604	23. Construction of Watermain Across Hung Hing Road	128 days	30 August 2019	04 January 2020	27 December 2019	→																											
643	24. Repaving Work at Hung Hing Road and Wan Shing Street	199 days	21 June 2019	05 January 2020	29 December 2019	→																											
672	25. Rectification Works of Temporary Covered Walkway	90 days	27 May 2019	24 August 2019	12 August 2019	→ 24/08																											
726	26. Tree Transplanting	541 days	14 May 2019	04 November 2020	04 November 2020	→																											
771	27. Reprovision of Public Lighting and Directional Sign at Hung Hing Road and Wan Shing Street	213 days	14 May 2019	12 December 2019	12 December 2019	→ 12/12																											

aTask Baseline Milestone Project Summary Deadline Finish-only   
 Critical Split Baseline Milestone Summary Group By Summary Start-only

**CEDD Contract No. HK/2012/08  
Wan Chai Development Phase II  
Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019							
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
<b>HK/2012/08 Revised Works Programme Rev.12.0(DD 20 November 2017)</b>																									
<b>Key Dates and Milestone Dates</b>																									
<b>Sections of Works Completion (Included Not Granted EOT Entitlement of The Contractor)</b>																									
KD10840	Completion of Section IIIA	0		08-Sep-18*	0%																				
KD10860	Completion of Section IV	0		30-Aug-18*	0%																				
KD10880	Completion of Section V	0		26-Sep-18*	0%																				
KD11010	Completion of Section VII	0		14-Sep-18*	0%																				
KD11020	Completion of Section VIII	0		21-Sep-18*	0%																				
KD11040	Completion of Section IX	0		21-Sep-19*	0%																				
KD11060	Completion of Section X	0		21-Sep-18*	0%																				
<b>Planned Sections of Works Completion</b>																									
KD10080	Planned Section IIIA Completion - Road A2,A4, A5	0		08-Sep-18	0%																				
KD10100	Planned Section IV Completion - Slip Road 3	0		30-Aug-18	0%																				
KD10140	Planned Section V Completion - Remaining At-Grade Road	0		26-Sep-18	0%																				
KD10280	Planned Section VII Completion - Remainder Works	0		14-Sep-18	0%																				
KD10300	Planned Section VIII Completion - Landscape Softwork	0		21-Sep-18	0%																				
KD10320	Planned Section IX Completion - Establishment Works	0		21-Sep-19	0%																				
KD10340	Planned Section X Completion - Tree Protection & Preservation	0		21-Sep-18	0%																				
<b>Dredging and Reclamation</b>																									
<b>Marine Work Construction</b>																									
<b>Zone CRIII</b>																									
<b>Seawall Construction - Zone CRIII</b>																									
<b>Zone CRIII Seawall- 2nd Stage</b>																									
<b>Seawall 2 &amp; 12</b>																									
MAR21371	Zone CRIII - seawall 2 & 12 - Backfilling remaining portion (type A, geotextile and filter)	0	19-Jan-18 A	27-Jan-18 A	100%	■																			
<b>Zone D</b>																									
<b>Seawall Construction - Zone D</b>																									
<b>Seawall 10 &amp; 11</b>																									
MAR20630	Zone D - Seawall 10 & 11: Install remaining seawall block	14	20-Feb-18*	05-Mar-18	0%		■																		
MAR20650	Zone D - Seawall 10 & 11: Backfill Type A	7	06-Mar-18	12-Mar-18	0%			■																	
MAR20670	Zone D - Seawall 10 & 11: Lay geotextile and filter	7	13-Mar-18	19-Mar-18	0%			■																	
<b>Works for Section Completion</b>																									
<b>Construction</b>																									
<b>Section III A - Road A2, A4 &amp; A5</b>																									
<b>Roadwork &amp; Utilities - Section 1 (L1806 - L1801)</b>																									

Data Date: 20-Feb-18

- ◆ Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Remaining Level of Effort

**Updated Works Programme Rev.12  
(Ref. to Rev.12 as of 20 February 2018)**

Date	Revision	Checked	Approved
20-Feb-18	12		










**CEDD Contract No. HK/2012/08**  
**Wan Chai Development Phase II**  
**Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019					
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
<b>Promenade Seawall Parapet Construction &amp; EVA</b>																							
SVII12000	Sec VII - Precast parapet	67	18-Nov-17 A	14-May-18	0%																		
SVII12010	Sec VII - Zone CRIII - seawall parapet: Backfilling	14	20-Feb-18	07-Mar-18	0%																		
SVII12120	Sec VII - Zone CRIII - seawall parapet: Construct mass concrete coping	30	08-Mar-18	16-Apr-18	0%																		
SVII12122	Sec VII - Zone CRIII - seawall parapet: reinforced concret coping	17	17-Apr-18	07-May-18	0%																		
SVII12140	Sec VII - Zone CRIII - seawall parapet: construct seawall parapet	30	08-May-18	12-Jun-18	0%																		
SVII12160	Sec VII - CRIII - EVA: watermain	14	13-Jun-18	29-Jun-18	0%																		
SVII12180	Sec VII - CRIII - EVA: U-channel	14	30-Jun-18	17-Jul-18	0%																		
SVII12200	Sec VII - CRIII - EVA: bituminous layer	5	18-Jul-18	23-Jul-18	0%																		
SVII12220	Sec VII - CRIII - EVA: paving block	30	24-Jul-18	27-Aug-18	0%																		
SVII13120	Sec VII - Zone A1, A2 & B - seawall parapet: Construct mass concrete coping	14	28-Dec-17 A	07-Mar-18	68.18%																		
SVII13122	Sec VII - Zone A1, A2 & B - seawall parapet: reinforced concrete coping	18	08-Mar-18	28-Mar-18	0%																		
SVII13140	Sec VII - Zone A1, A2 & B - seawall parapet: Construct seawall parapet	30	09-Apr-18	14-May-18	0%																		
SVII13160	Sec VII - Zone A1, A2 & B - EVA: watermain	14	15-May-18	31-May-18	0%																		
SVII13180	Sec VII - Zone A1, A2 & B - EVA: U-channel	14	01-Jun-18	16-Jun-18	0%																		
SVII13182	Sec VII - Zone A1, A2 & B - EVA: bituminous layer	5	19-Jun-18	23-Jun-18	0%																		
SVII13184	Sec VII - Zone A1, A2 & B - EVA: paving block	30	25-Jun-18	30-Jul-18	0%																		
SVII13200	Sec VII - Zone D - seawall parapet: Remove temporary seawall block	21	07-Mar-18	03-Apr-18	0%																		
SVII13220	Sec VII - Zone D - seawall parapet: Construct mass concrete	30	04-Apr-18	10-May-18	0%																		
SVII13222	Sec VII - Zone D - seawall parapet: reinforced concrete coping	18	11-May-18	01-Jun-18	0%																		
SVII13240	Sec VII - Zone D - seawall parapet: Construct seawall parapet	25	02-Jun-18	03-Jul-18	0%																		
SVII13260	Sec VII - Zone D - EVA : watermain	14	04-Jul-18	19-Jul-18	0%																		
SVII13280	Sec VII - Zone D - EVA : U-channel	14	20-Jul-18	04-Aug-18	0%																		
SVII13300	Sec VII - Zone D - EVA : bituminous layer	5	06-Aug-18	10-Aug-18	0%																		
SVII13320	Sec VII - Zone D - EVA : paving block	30	11-Aug-18	14-Sep-18	0%																		
<b>Promenade Footpath</b>																							
<b>Section 1</b>																							
SVII10440	Sec VII - section 1 footpath - drainage works : connection pipe & U -channel	10	24-May-18	04-Jun-18	0%																		
SVII10445	Sec VII - section 1 footpath - watermain	7	05-Jun-18	12-Jun-18	0%																		
SVII10460	Sec VII - section 1 footpath - lighting	7	13-Jun-18	21-Jun-18	0%																		
SVII10500	Sec VII - section 1 footpath - paving block	21	22-Jun-18	17-Jul-18	0%																		
<b>Section 2</b>																							
SVII12610	Sec VII - section 2 footpath - drainage works : L2202 - L2203A	20	20-Feb-18	14-Mar-18	0%																		
SVII12615	Sec VII - section 2 footpath - watermain	7	15-Mar-18	22-Mar-18	0%																		
SVII12630	Sec VII - section 2 footpath - utilities: TCSS	21	23-Mar-18	20-Apr-18	0%																		
SVII12670	Sec VII - section 2 footpath - paving block	30	21-Apr-18	28-May-18	0%																		
<b>Section 3</b>																							
SVII12850	Sec VII - section 3 footpath - watermain	17	20-Feb-18	10-Mar-18	0%																		
SVII12870	Sec VII - section 3 footpath - utilities (HEC, TCSS, HGC, PCCW)	40	12-Mar-18	02-May-18	0%																		
SVII12875	Sec VII - 3 footpath - drainage works :U chanel	14	03-May-18	18-May-18	0%																		





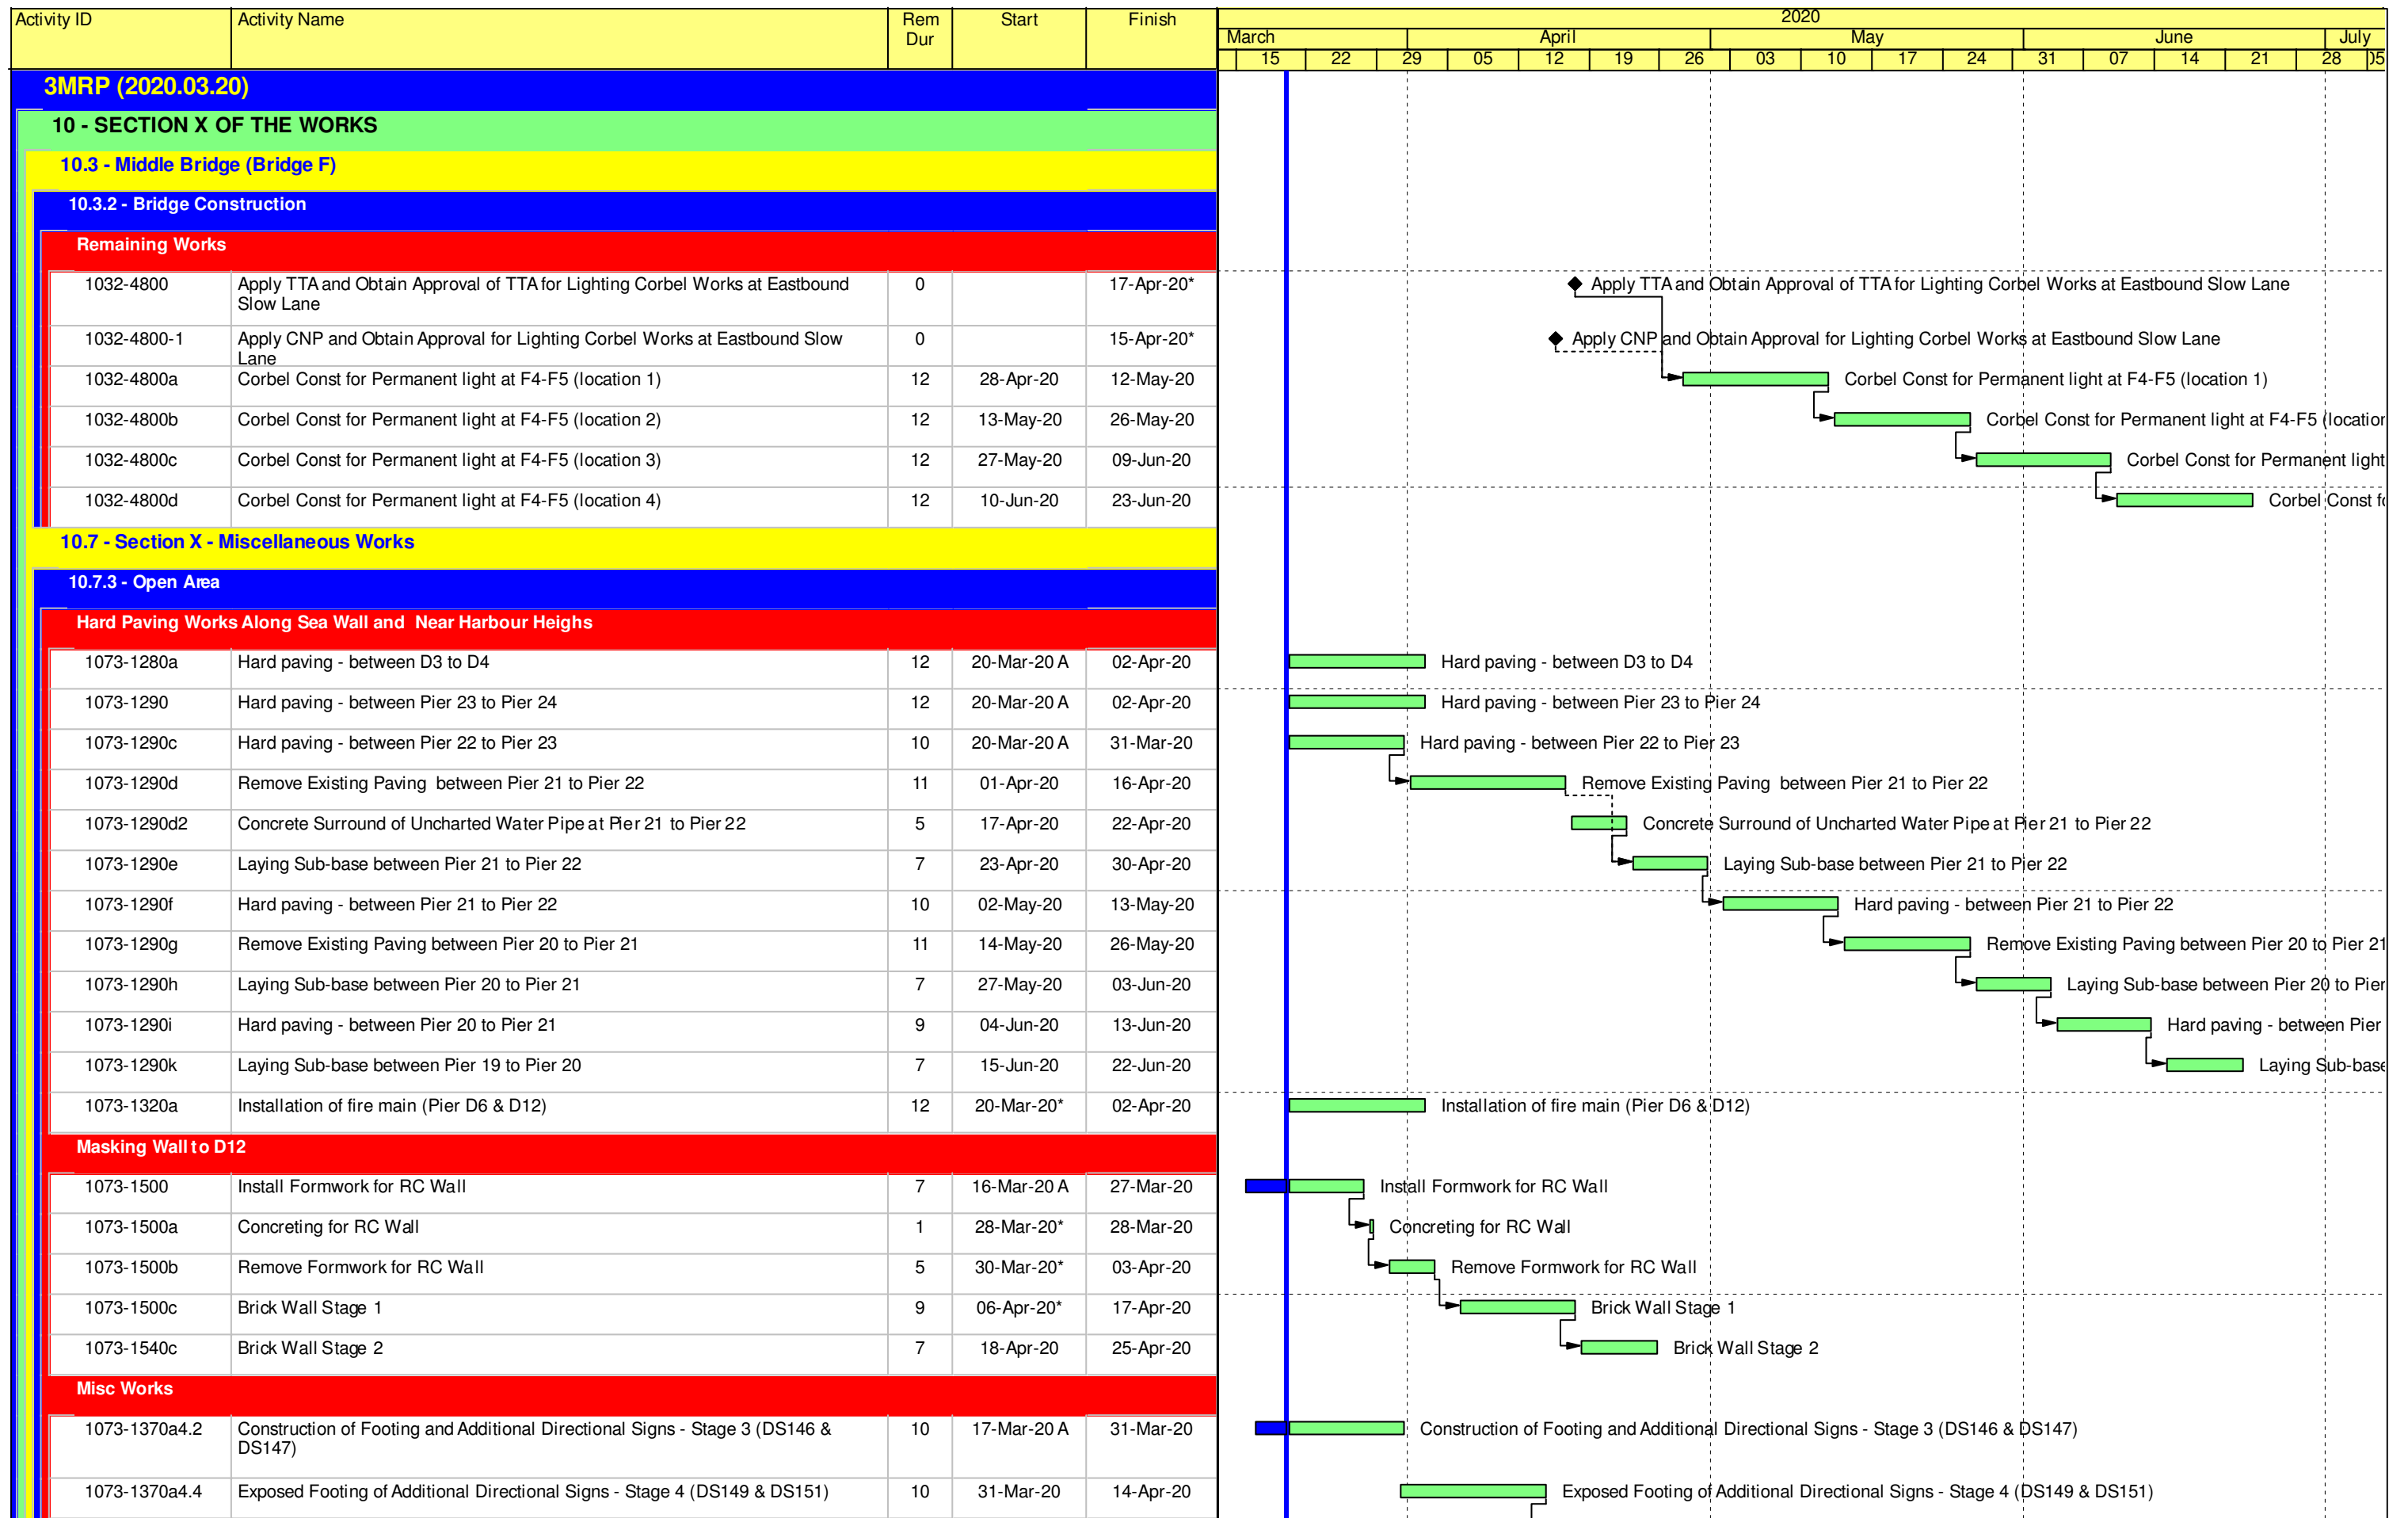

█ Remaining Level of Effort    █ Remaining Work  
█ Actual Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Mar.2020 to 20.Jun.2020)**

Activity ID	Activity Name	Rem Dur	Start	Finish	2020																		
					March			April				May				June				July			
					15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	05		
1073-1370a4.5	Construction of Footing of Additional Directional Signs - Stage 4 (DS149 & DS151)	12	15-Apr-20	28-Apr-20																			
1073-1370a4.6	Erection of Additional Directional Signs - Stage 4 (DS149 & DS151)	8	29-Apr-20	08-May-20																			
1073-1370a4.7	Pending for XP of Additional Directional Signs (DS148 & DS153)	0		27-Mar-20*																			
1073-1370a4.8	Exposed Footing of Additional Directional Signs - Stage 5 (DS148 & DS153)	10	28-Mar-20	09-Apr-20																			
1073-1370a4.9	Construction of Footing of Additional Directional Signs - Stage 5 (DS148 & DS153)	12	11-Apr-20	25-Apr-20																			
1073-1370a4.90	Erection of Additional Directional Signs - Stage 5 (DS148 & DS153)	8	27-Apr-20	06-May-20																			
1073-1370a4.91	Erection of Additional Directional Signs - Stage 6 (DS160 & DS161)	9	02-Apr-20*	15-Apr-20																			
1073-1370a4.92	Erection of Additional Directional Signs - Stage 7 (DS162)	12	16-Apr-20	29-Apr-20																			
1073-1370g	Application of CNP for Construction of chainage marker (Large)	0		07-Apr-20*																			
1073-1370h	Apply TDN for Construction of chainage marker (Large)	12	11-Apr-20	25-Apr-20*																			
1073-1370i	Apply RA and Obtain Approval of RA for Construction of chainage marker (Large)	8	27-Apr-20	06-May-20																			
1073-1370k	Construction of chainage marker (Large) - Stage 1	12	07-May-20	20-May-20																			
1073-1370l	Construction of chainage marker (Large) - Stage 2	12	21-May-20	03-Jun-20																			
1073-1370m	Construction of chainage marker (Large) - Stage 3	12	04-Jun-20*	17-Jun-20																			

**11 - SECTION 11 OF THE WORKS**

**11.4- Hing Fat Street**

**Other Areas**

1140-2240c	Installation of Minor Traffic Signs - Stage 3 (10 nos.)	12	25-Mar-20	08-Apr-20																
1140-2270	Pending for AECOM instruction on hold of resurfacing work in Progress Meeting	0		24-Apr-20*																
1140-2270a	Road resurfacing at Hing Fat Street - Stage 1 (4 TTA Schemes - Night Work)	12	25-Apr-20	09-May-20																
1140-2270b	Road resurfacing at Hing Fat Street - Stage 2 (4 TTA Schemes - Night Work)	12	11-May-20	23-May-20																
1140-2270c	Road resurfacing at Hing Fat Street - Stage 3 (4 TTA Schemes - Night Work)	12	25-May-20	06-Jun-20																
1140-2270d	Road resurfacing at Hing Fat Street - Stage 4 (4 TTA Schemes - Night Work)	12	08-Jun-20	20-Jun-20																

**12 - SECTION 7, 8, 9, 10 & 12 OF THE WORKS**

**12.1 - Landscape Deck**

1200-7830a2	Construct Footpath near C1 at SR13 Stage 2	12	20-Mar-20 A	02-Apr-20																
1200-7830b	Cultivation for D4-D5	9	03-Apr-20	16-Apr-20																
1200-7830c	Planting Soil for D4-D5	12	17-Apr-20	30-Apr-20																
1200-7830d	Cultivation for D5-D6	12	02-May-20	15-May-20																
1200-7830e	Planting Soil for D5-D6	12	16-May-20	29-May-20																
1200-7830f	Cultivation for D6-D7	12	30-May-20	12-Jun-20																
1200-7830g	Planting Soil for D6-D7	12	13-Jun-20	27-Jun-20																


**12.2 - THE WORKS along IECL**

**12.2.1 - Noise Enclosure and Inner Parapet along IECL Westbound**


**West Bound Brigde Between F2 to C2 (P40 to P22) (parapet mould 1)**



**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Mar.2020 to 20.Jun.2020)**

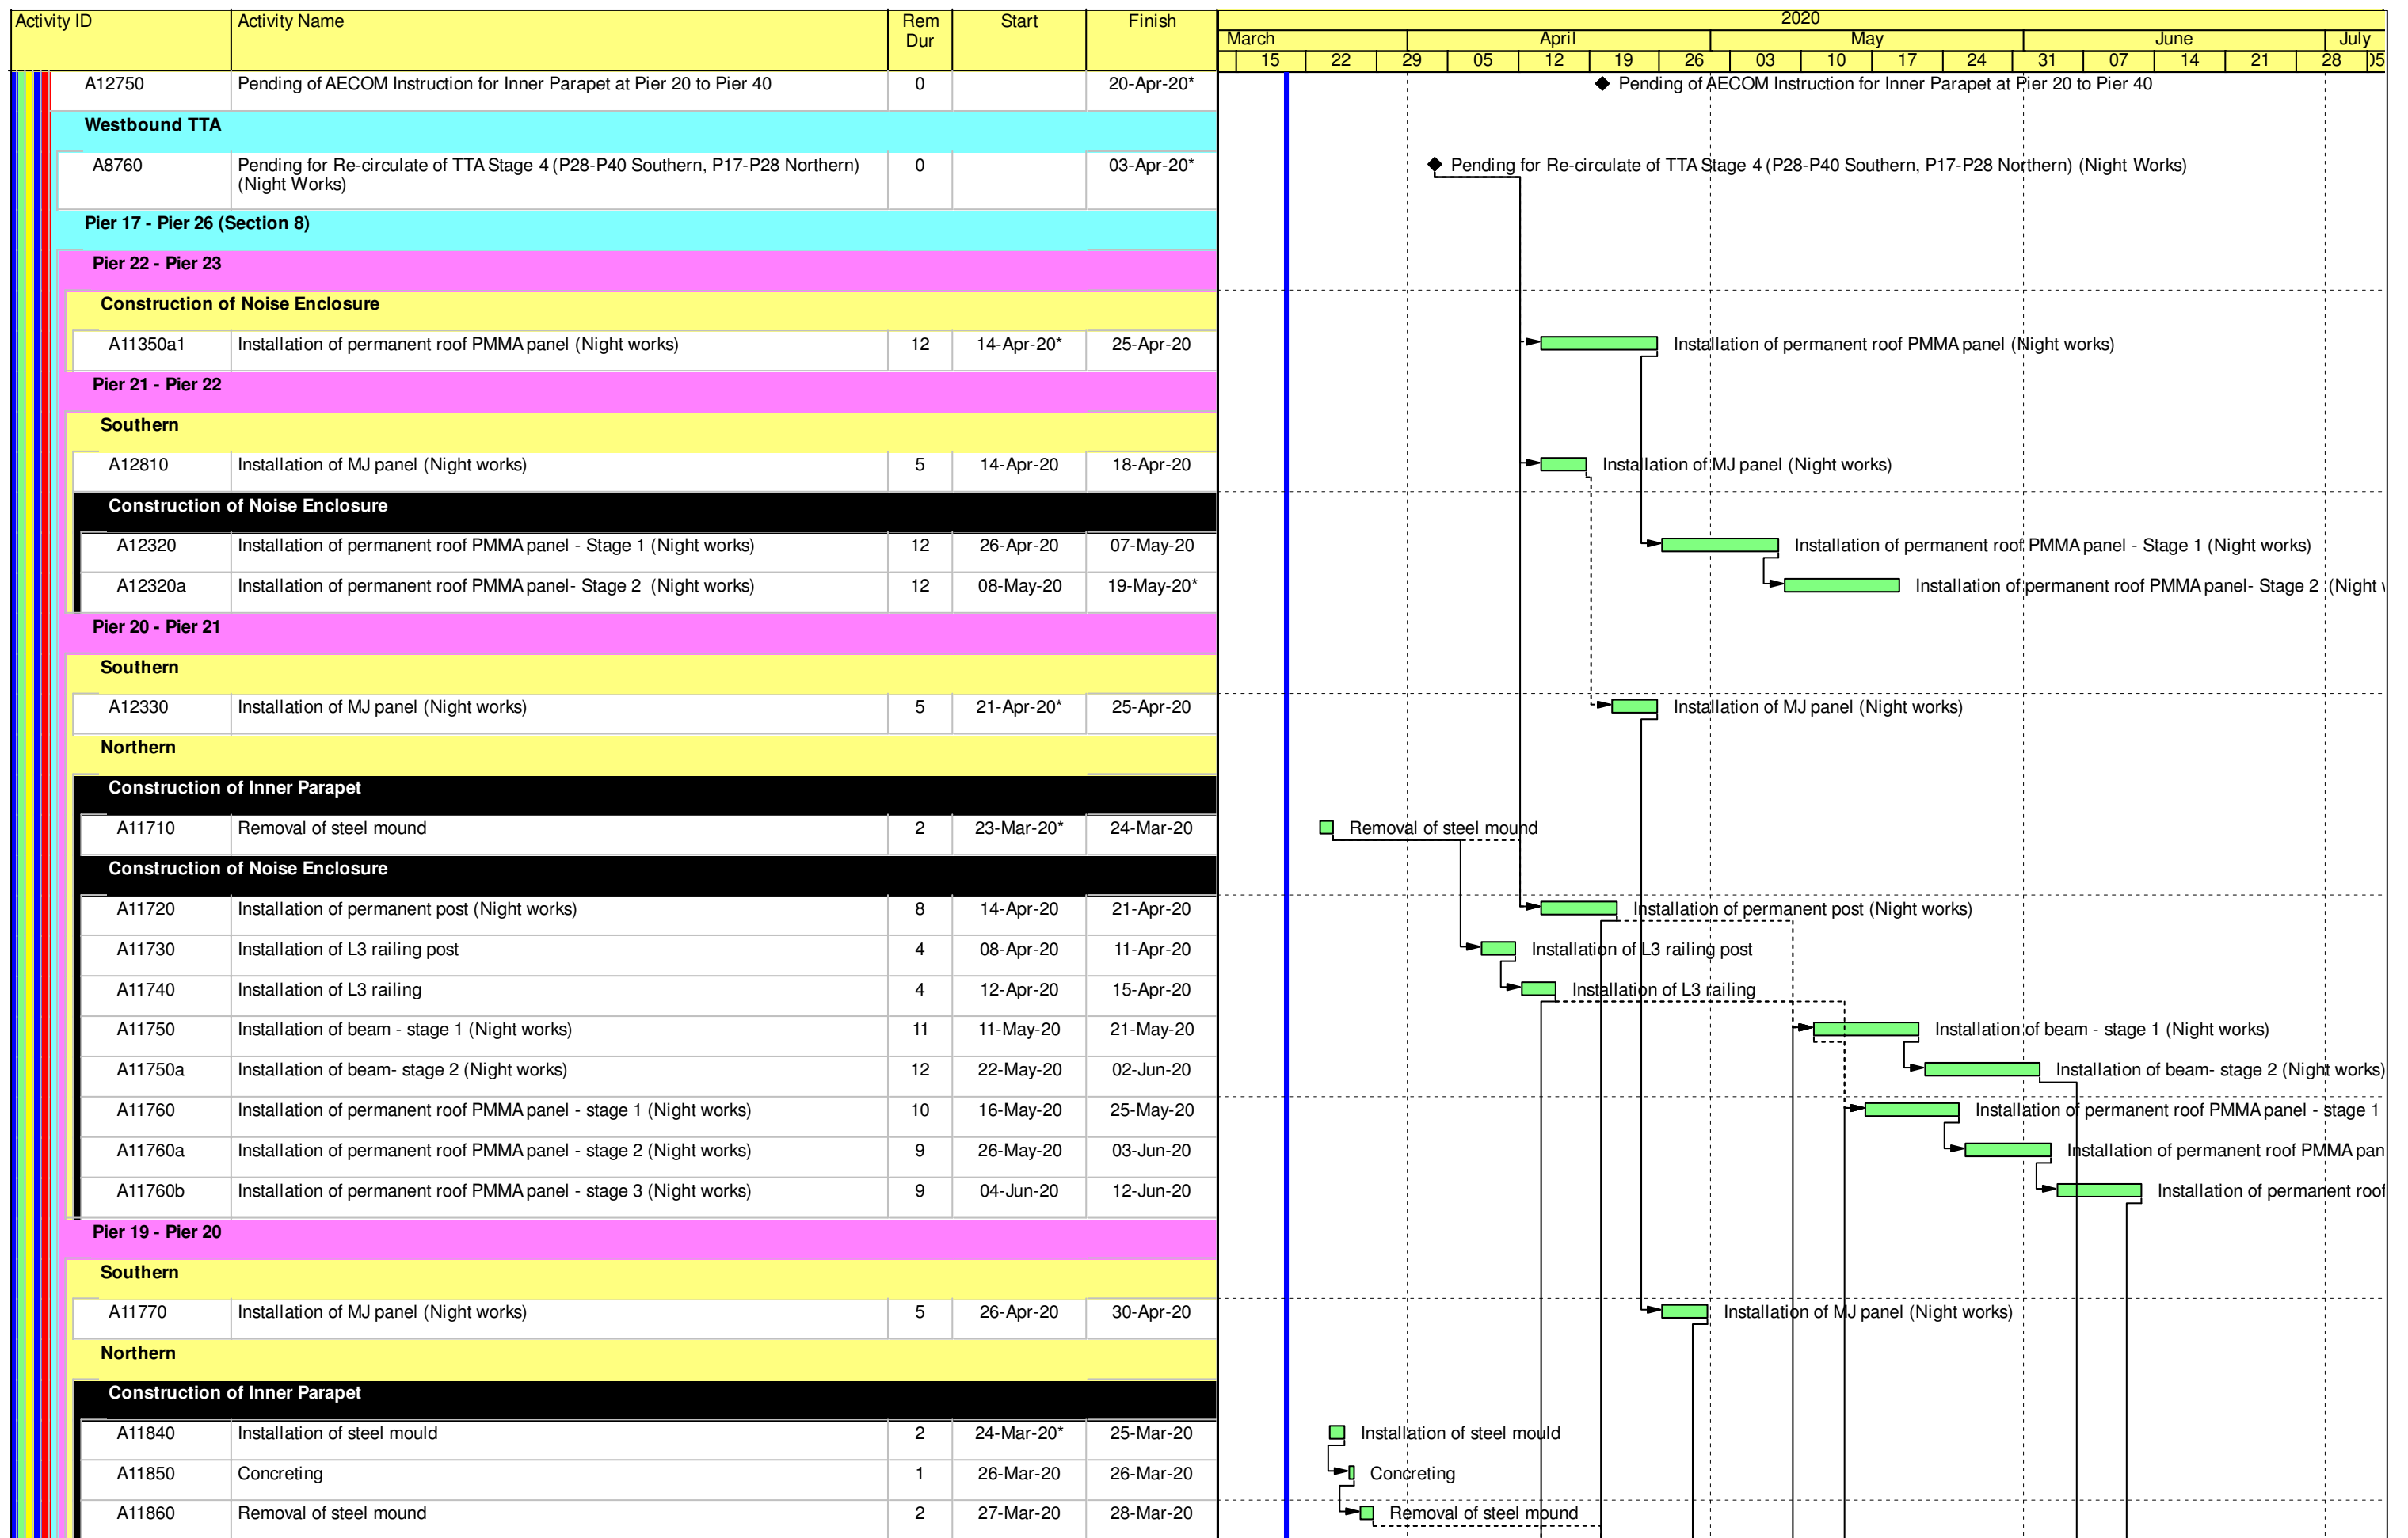


**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Mar.2020 to 20.Jun.2020)**

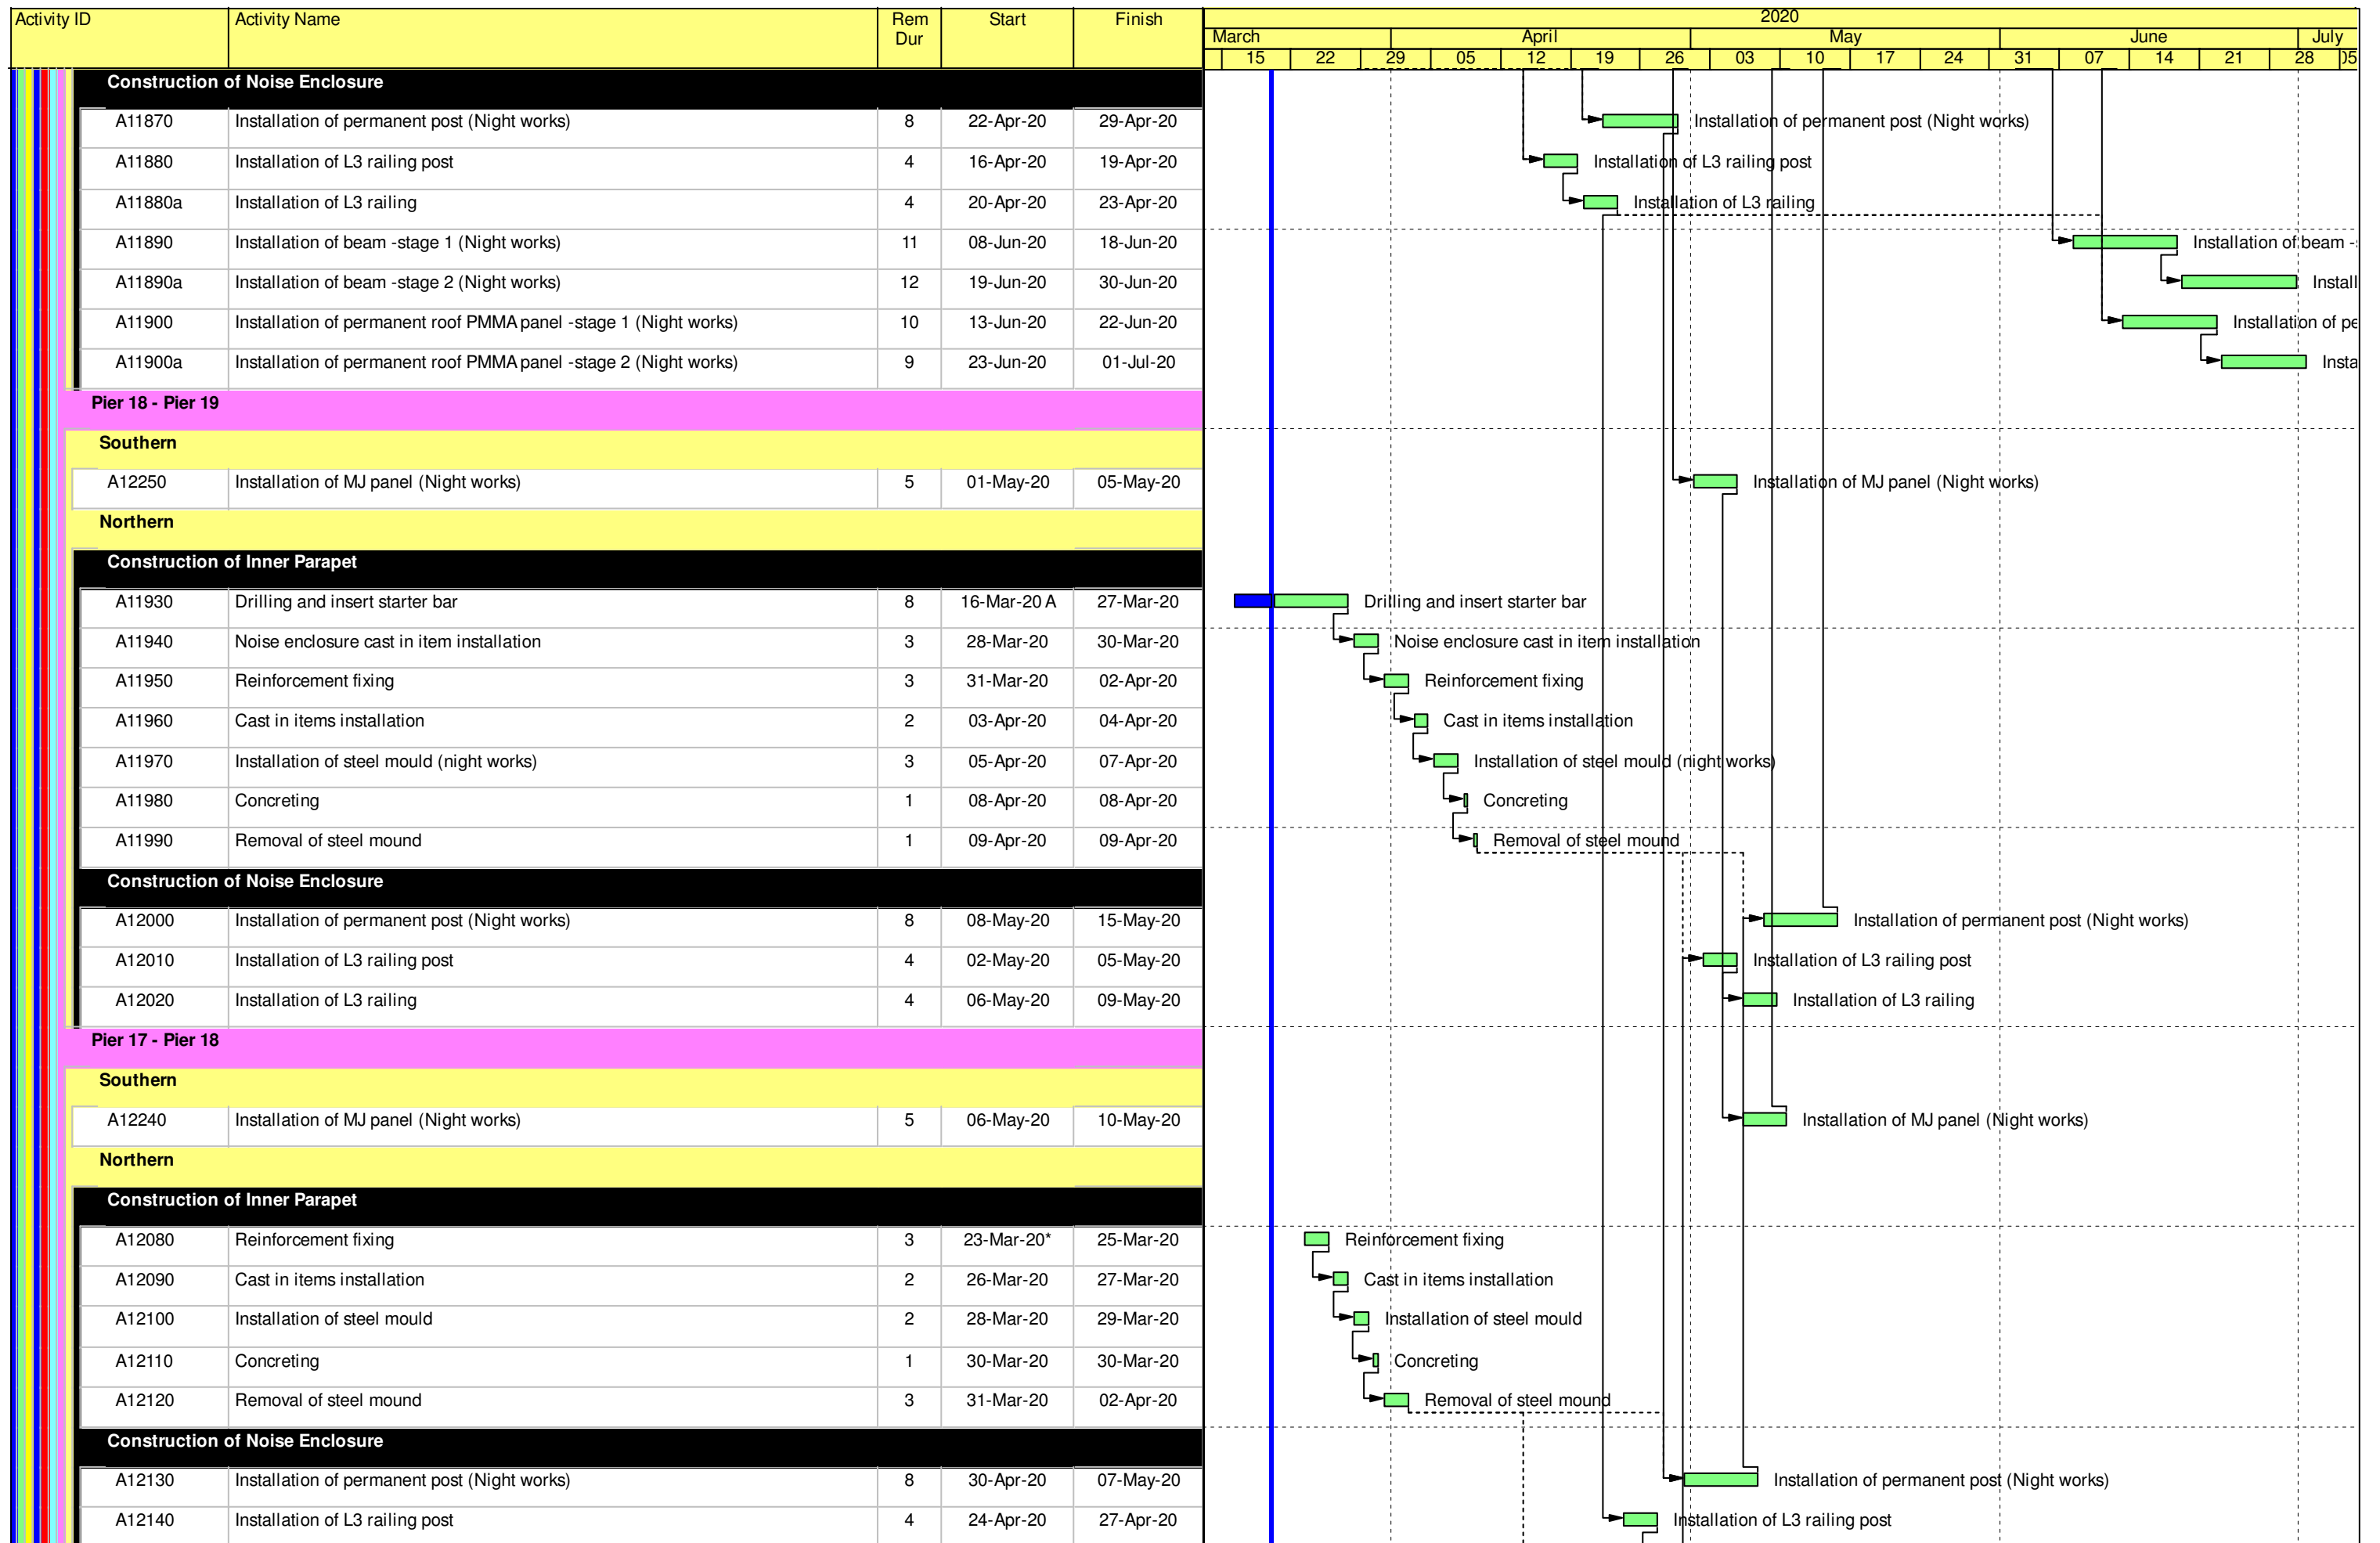

■ Remaining Level of Effort    ■ Remaining Work  
■ Actual Level of Effort    ■ Critical Remaining Work  
■ Actual Work    ◆ ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Mar.2020 to 20.Jun.2020)**

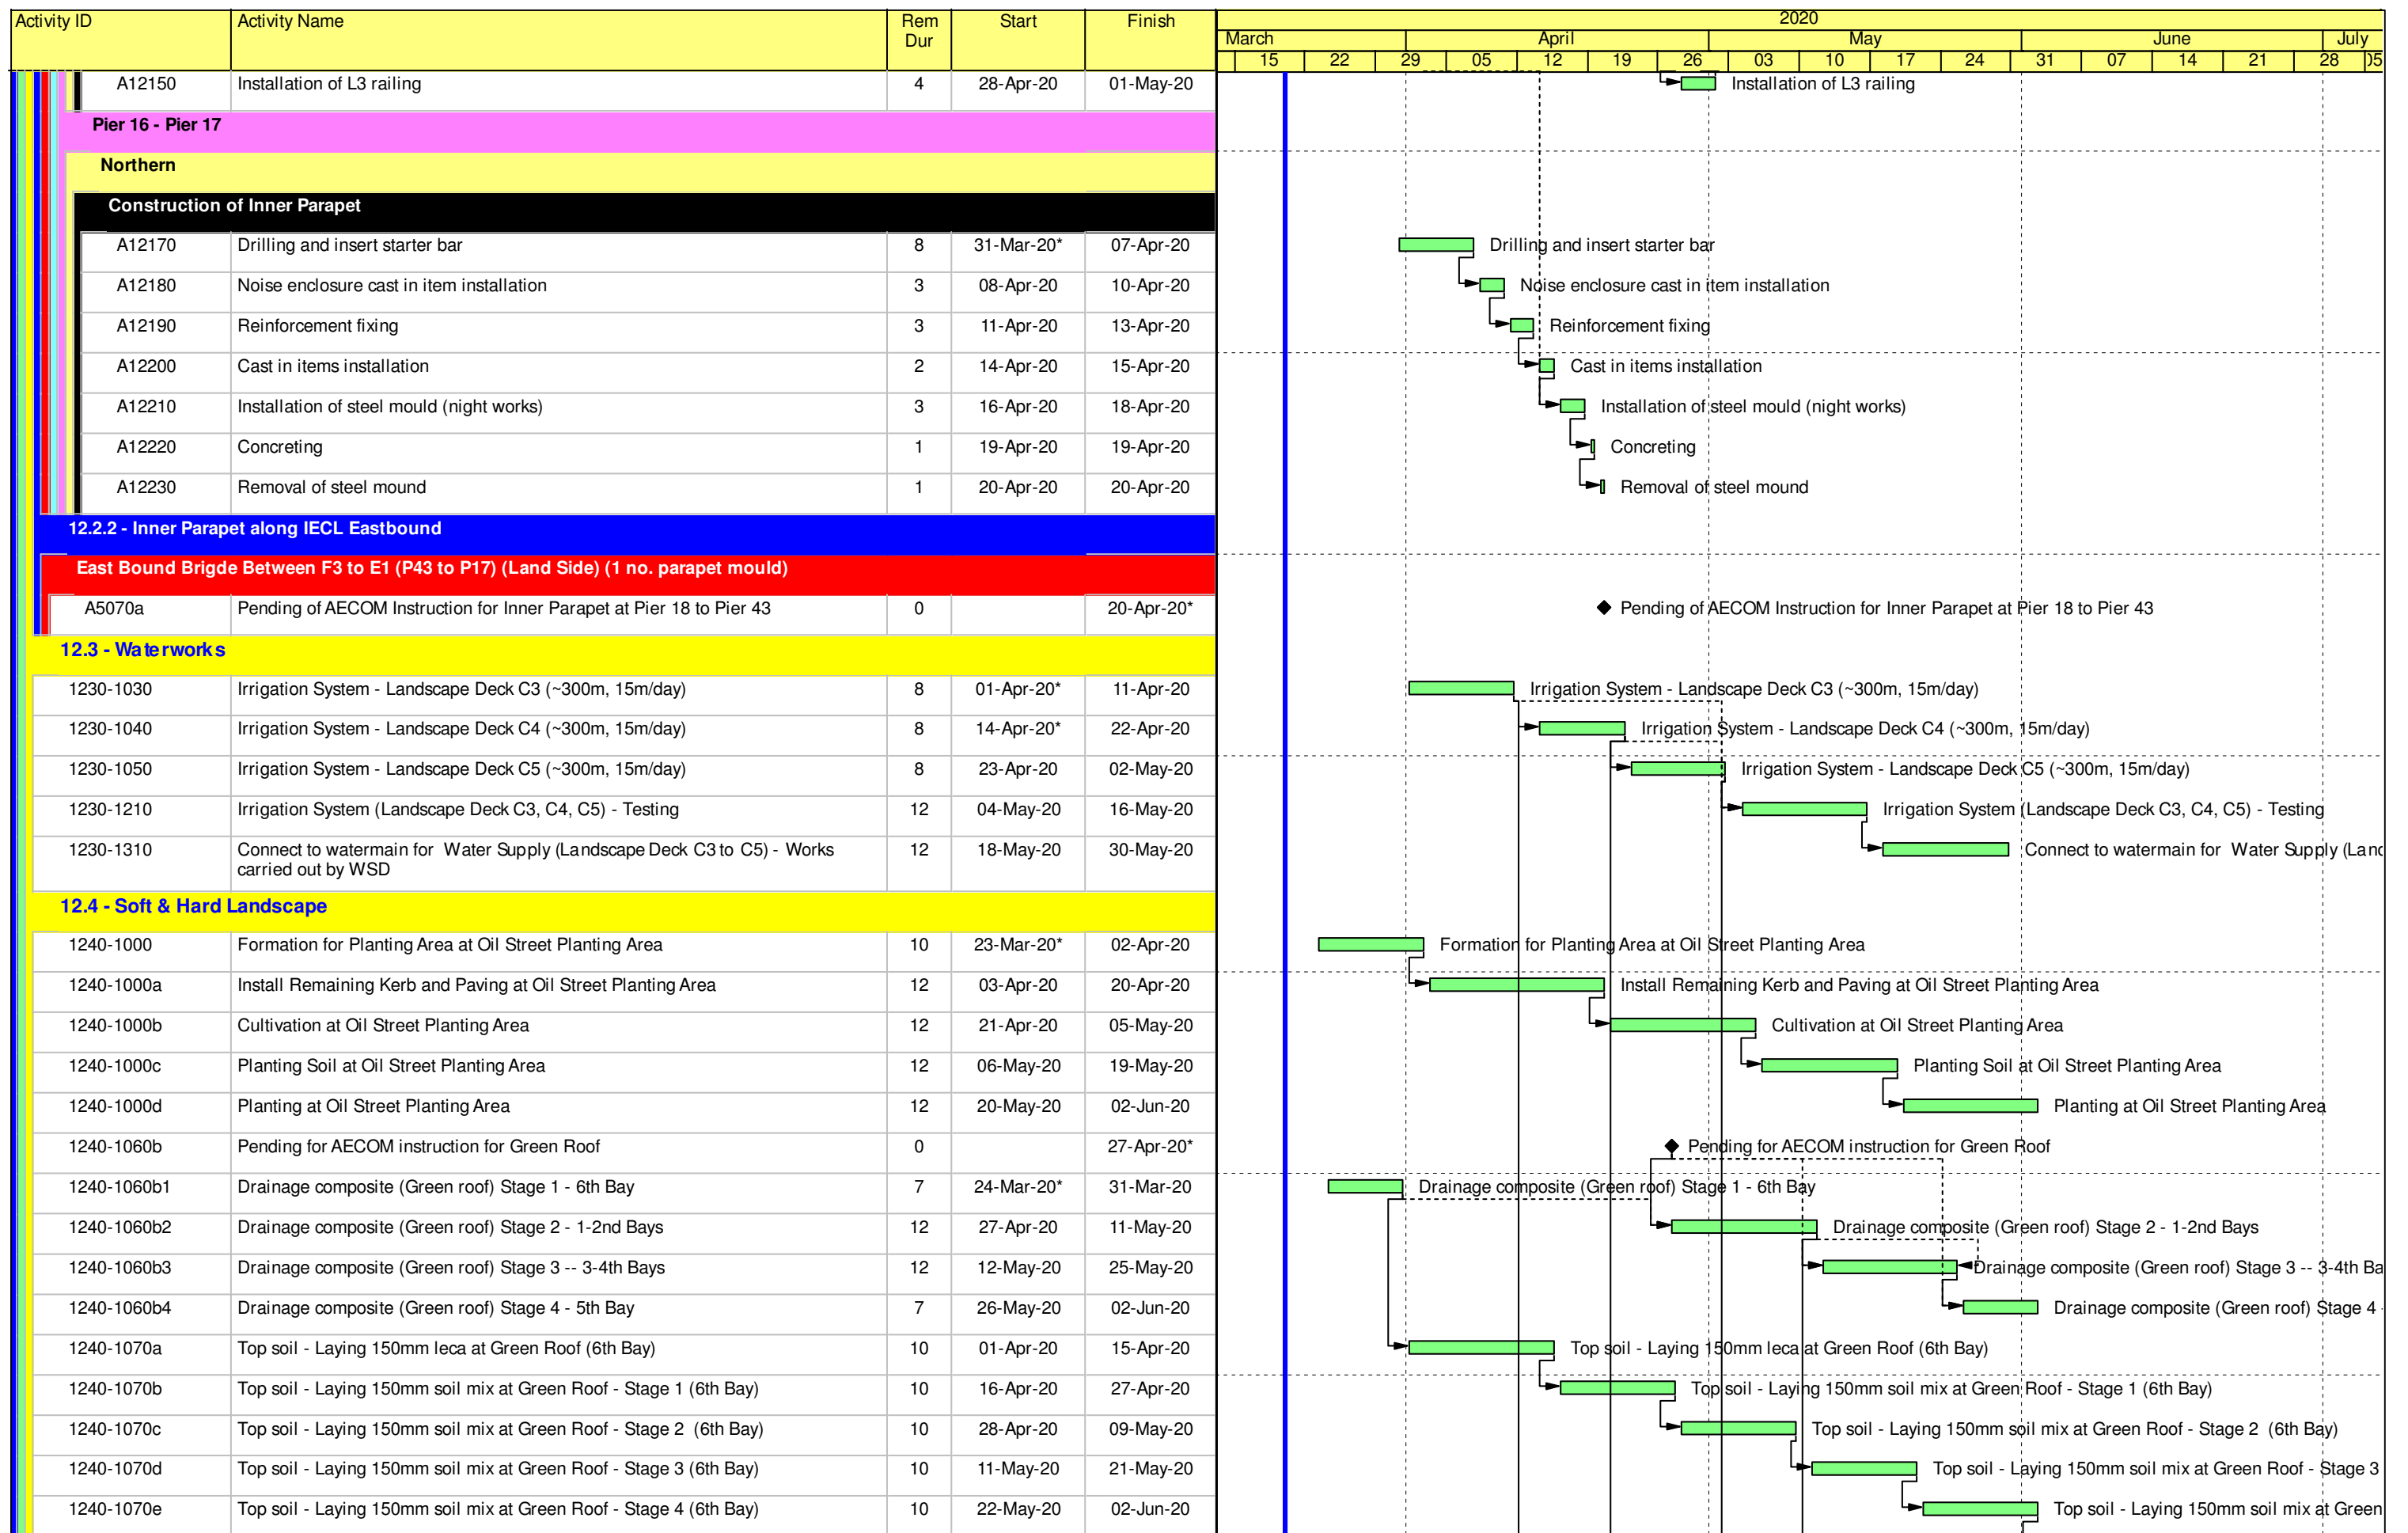

■ Remaining Level of Effort    ■ Remaining Work  
■ Actual Level of Effort    ■ Critical Remaining Work  
■ Actual Work    ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Mar.2020 to 20.Jun.2020)**

Activity ID	Activity Name	Rem Dur	Start	Finish	2020																
					March			April				May			June			July			
					15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	05
1240-1070x	Top soil - Laying ploughing soil at Green Roof (6th Bay)	2	03-Jun-20	04-Jun-20																	
1240-1080a	Top soil - Laying 150mm leca at Green Roof (1-2nd Bays)	10	12-May-20	22-May-20																	
1240-1080b	Top soil - Laying 150mm soil mix at Green Roof - Stage 1 (1-2nd Bays)	10	23-May-20	03-Jun-20																	
1240-1080c	Top soil - Laying 150mm soil mix at Green Roof - Stage 2 (1-2nd Bays)	10	04-Jun-20	15-Jun-20																	
1240-1080d	Top soil - Laying 150mm soil mix at Green Roof - Stage 3 (1-2nd Bays)	10	16-Jun-20	27-Jun-20																	
1240-1100a	Maintenance walkway at Green Roof (6th Bay)	12	05-Jun-20	18-Jun-20																	
1240-1330a2	Planting at Landscape Deck C3	12	14-Apr-20	27-Apr-20																	
1240-1340	Planting at Landscape Deck C4	12	23-Apr-20	07-May-20																	
1240-1350	Planting at Landscape Deck C5	12	04-May-20	16-May-20																	
1240-1360a	Planting at Green Roof (6th Bay)	12	19-Jun-20	04-Jul-20																	
<b>13 - SECTION 13 OF THE WORKS</b>																					
<b>13.2 - Roadworks</b>																					
1320-1010a	Issue XP for Rumsey Street Flyover Modification Works by AECOM	0		06-Apr-20*																	
1320-1010e	Connection of Meter box (by other) - stage 2	5	18-Mar-20 A	02-Apr-20																	
1320-1020	Preparation of method statement for Rumsey Street Flyover Modification Works	6	20-Mar-20 A	26-Mar-20																	
1320-1020a	Obtain approval of MS for Rumsey Street Flyover Modification Works	12	27-Mar-20	11-Apr-20																	
1320-1030	Preparation and Obtain approval of TTA for Rumsey Street Flyover Modification Works	0		27-Mar-20*																	
1320-1030a	Apply RA and obtain approval of RA for Rumsey Street Flyover Modification Works	7	28-Mar-20	06-Apr-20																	
1320-1030b	Implementation of TTA	2	07-Apr-20	08-Apr-20																	
1320-1040	Trim off Existing Parapet (Type 1 Enlarged Parapet) - Stage 1	12	14-Apr-20	27-Apr-20																	
1320-1040a	Trim off Existing Parapet (Type 1 Enlarged Parapet) - Stage 2	12	28-Apr-20	12-May-20																	
1320-1040b	Trim off Existing Parapet (Type 1 Enlarged Parapet) - Stage 3	12	13-May-20	26-May-20																	
1320-1040c	Construct Type 1 Enlarged Parapet - Stage 1	11	27-May-20	08-Jun-20																	
1320-1040d	Construct Type 1 Enlarged Parapet - Stage 2	11	09-Jun-20	20-Jun-20																	
<b>16 - SECTION 13B OF THE WORKS</b>																					
<b>16.1 - Soft Landscape</b>																					
1610-1100	Establishment Works at Portion IIA	365	20-Mar-20	19-Mar-21																	

Activity ID	Activity Name	Original Duration	Start	Finish	2020																	
					Jan	Feb	Mar	Apr														
<b>Total</b>		385.0	31-Mar-19 A	03-May-20																		
<b>DWP-08 - (2) - Update Progress As of 20 Jan 20</b>		385.0	31-Mar-19 A	03-May-20																		
<b>KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks</b>		385.0	31-Mar-19 A	03-May-20																		
<b>KD11 - Section 7A: Portion XIV &amp; XV (Victoria Park Open Space)</b>		365.0	31-Mar-19 A	29-Feb-20																		
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365.0	31-Mar-19 A	29-Feb-20																		
<b>KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH&gt;500mm)</b>		365.0	20-Apr-19 A	03-May-20																		
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365.0	20-Apr-19 A	03-May-20																		
<b>KD18 - Section 11: Transplanted Trees DBH&gt;500mm in Portion VA and XII</b>		365.0	20-Apr-19 A	03-May-20																		
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365.0	20-Apr-19 A	03-May-20																		

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Page 1 of 1  
 Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel (Slip Road 8 Section) - 3 Months Rolling Programme

Date	Revision	Checked	Approved
20-Jan-20	DWP-08 (2) - 3 Months Rolling	TL	TL




Data Date: 20-Apr-20

# CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
<b>Update 2020-04-20 CWB(CC) - Commissioning Contract (DWP 4g)</b>					
<b>PRELIMINARIES AND GENERAL REQUIREMENTS</b>					
<b>Salient Key Dates and Milestones</b>					
<b>Anticipated Completion Dates</b>					
KD09	KD9 - Completion of Section 4 of the Works (1445 days) - include EOT No.12 (149 days)	0		20-Apr-20*	-946
KD11	KD11 - Completion of Section 6 of the Works (1445 days) - include EOT No.12 (149 days)	0		20-Apr-20*	-798
KD07	KD7 - Completion of Section 2 of the Works (1771 days) - include EOT No.12 (414 days)	0		23-May-20*	-615
<b>Possession Dates and Vacation Dates</b>					
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-Apr-20	08-Aug-20	-798
<b>Submissions and Approvals</b>					
<b>Initial General Submission</b>					
10168	Submission of CMC 3DVR	30	20-Apr-20	19-May-20	-611
<b>CONSTRUCTION</b>					
<b>Commissioning Test</b>					
10126	Establishment Works	365	20-Apr-20	19-Apr-21	-946
9930	Contract Completion	0		23-May-20	-615
<b>Outstanding Works</b>					
<b>Tunnel Buildings</b>					
<b>MVB Edge Cladding</b>					
192414	Installation of cladding - West side (Upper)	18	21-Dec-19 A	30-Mar-20 A	
192410	Installation of cladding - West side (Lower)	36	11-Jan-20 A	04-Apr-20 A	
192412	Installation of cladding - North side (Upper & Lower)	30	01-Feb-20 A	24-Apr-20	-479
192406	Installation of cladding - South side (Upper & Lower)	30	04-Apr-20 A	09-May-20	-490
192416	Dismantle Scaffolding	12	11-May-20	23-May-20	-490

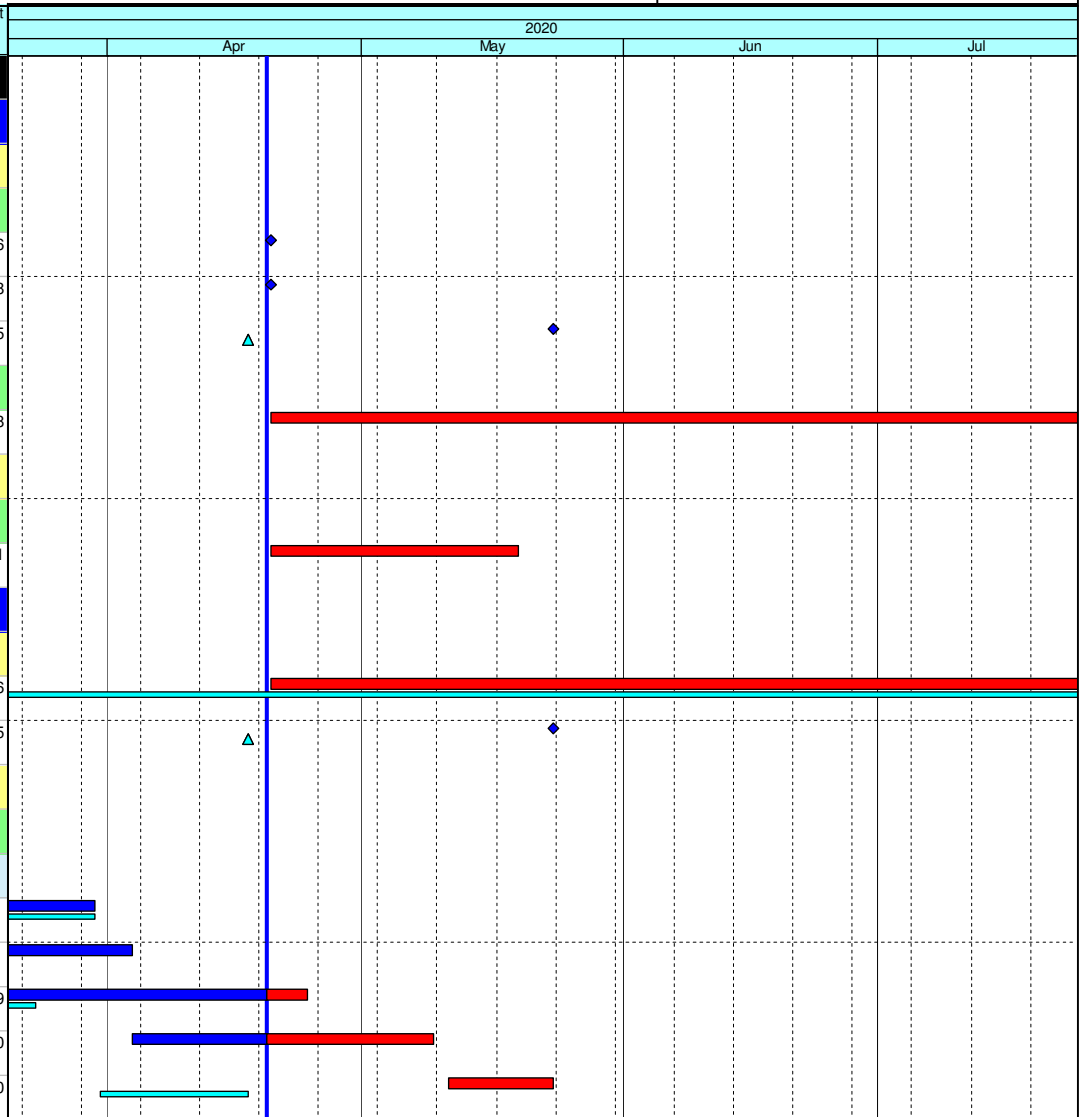

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Project Baseline
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline
- ▲ Baseline Milestone

## Leighton Contractors (Asia) Limited

### Programme Update 4(April 2020)

# THREE MONTH ROLLING

Project ID: H2613-U074  
 Baseline: DWP4g  
 Layout: Update Three Month Rolling  
 U074\_1  
 Page 1 of 2

Date	Revision	Checked	Approv...
20-Mar-2...	U073	AT	CW
20-Apr-2...	U074	AT	CW



Data Date: 20-Apr-20

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2020																
						Apr			May			Jun			Jul							
<b>Training / Plan / Manual / As-Built Drawings for Project Completion / Establishment</b>																						
10226	Routine Maintenance Records / Maintenance Monthly Report	0	20-Apr-20		-581																	

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 4(April 2020) THREE MONTH ROLLING

Project ID: H2613-U074  
 Baseline: DWP4g  
 Layout: Update Three Month Rolling  
 U074\_1  
 Page 2 of 2

Date	Revision	Checked	Approv...
20-Mar-2...	U073	AT	CW
20-Apr-2...	U074	AT	CW
