



Activity ID	Activity Name	Original Duration	Start	Finish	2020															
					Jan	Feb	Mar	Apr												
<b>Total</b>		385.0	31-Mar-19 A	03-May-20																
<b>DWP-08 - (2) - Update Progress As of 20 Jan 20</b>		385.0	31-Mar-19 A	03-May-20																
<b>KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks</b>		385.0	31-Mar-19 A	03-May-20																
<b>KD11 - Section 7A: Portion XIV &amp; XV (Victoria Park Open Space)</b>		365.0	31-Mar-19 A	29-Feb-20																
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365.0	31-Mar-19 A	29-Feb-20																Establishment Works - for Landscape Softworks and transplanted trees in Portion XV
<b>KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH&gt;500mm)</b>		365.0	20-Apr-19 A	03-May-20																
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365.0	20-Apr-19 A	03-May-20																
<b>KD18 - Section 11: Transplanted Trees DBH&gt;500mm in Portion VA and XII</b>		365.0	20-Apr-19 A	03-May-20																
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365.0	20-Apr-19 A	03-May-20																

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Page 1 of 1  
 Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel (Slip Road 8 Section) - 3 Months Rolling Programme

Date	Revision	Checked	Approved
20-Jan-20	DWP-08 (2) - 3 Months Rolling	TL	TL





Activity ID	Activity Name	Rem Dur	Start	Finish	2020																		
					July			August				September				October				ember			
					12	19	26	02	09	16	23	30	06	13	20	27	04	11	18	25	01		
<b>3MRP (2020.07.20)</b>																							
<b>10 - SECTION X OF THE WORKS</b>																							
<b>10.3 - Middle Bridge (Bridge F)</b>																							
<b>10.3.2 - Bridge Construction</b>																							
<b>Remaining Works</b>																							
1032-4800-2b	Temp work design for Lighting Corbel Work - stage 3	12	20-Jul-20*	01-Aug-20	Temp work design for Lighting Corbel Work - stage 3																		
1032-4800-2c	Temp work design for Lighting Corbel Work - stage 4	12	03-Aug-20	15-Aug-20	Temp work design for Lighting Corbel Work - stage 4																		
1032-4800-3	Approval of Temp work design for Lighting Corbel Work	8	17-Aug-20	25-Aug-20	Approval of Temp work design for Lighting Corbel Work																		
1032-4800a	Corbel Const for Permanent light at F4-F5 (location 1)	12	26-Aug-20	08-Sep-20	Corbel Const for Permanent light at F4-F5 (location 1)																		
1032-4800b	Corbel Const for Permanent light at F4-F5 (location 2)	12	09-Sep-20	22-Sep-20	Corbel Const for Permanent light at F4-F5 (location 2)																		
1032-4800c	Corbel Const for Permanent light at F4-F5 (location 3)	12	23-Sep-20	08-Oct-20	Corbel Const for Permanent light at F4-F5 (location 3)																		
1032-4800d	Corbel Const for Permanent light at F4-F5 (location 4)	12	09-Oct-20	22-Oct-20	Corbel Const for Permanent light at F4-F5 (location 4)																		
<b>10.7 - Section X - Miscellaneous Works</b>																							
<b>10.7.3 - Open Area</b>																							
<b>Hard Paving Works Along Sea Wall and Near Harbour Heighs</b>																							
1073-1290g	Hard paving - between D12 Stage 2	12	20-Jul-20 A	01-Aug-20	Hard paving - between D12 Stage 2																		
1073-1290g1	Hard paving - between D12 Stage 3	12	03-Aug-20	15-Aug-20	Hard paving - between D12 Stage 3																		
1073-1290h	Hard paving - between D11	12	17-Aug-20	29-Aug-20	Hard paving - between D11																		
1073-1290i	Hard paving - between D10	12	31-Aug-20	12-Sep-20	Hard paving - between D10																		
1073-1290k	Hard paving - between D9	12	14-Sep-20	26-Sep-20	Hard paving - between D9																		
1073-1290l	Hard paving - between Pier 24 to Pier 25 Stage 1	12	20-Jul-20 A	01-Aug-20	Hard paving - between Pier 24 to Pier 25 Stage 1																		
1073-1290m	Hard paving - between Pier 24 to Pier 25 Stage 2	12	03-Aug-20	15-Aug-20	Hard paving - between Pier 24 to Pier 25 Stage 2																		
1073-1290n	Hard paving - between Pier 24 to Pier 25 Stage 3	12	17-Aug-20	29-Aug-20	Hard paving - between Pier 24 to Pier 25 Stage 3																		
1073-1290o	Hard paving - between Pier 24 to Pier 25 Stage 4	12	31-Aug-20	12-Sep-20	Hard paving - between Pier 24 to Pier 25 Stage 4																		
1073-1290p	Hard paving - between Pier 24 to Pier 25 Stage 5	12	14-Sep-20	26-Sep-20	Hard paving - between Pier 24 to Pier 25 Stage 5																		
1073-1290q	Hard paving - between Pier 20 to Pier 23 Stage 1	12	28-Sep-20	13-Oct-20	Hard paving - between Pier 20 to Pier 23 Stage 1																		
1073-1290r	Hard paving - between Pier 20 to Pier 23 Stage 2	12	14-Oct-20	28-Oct-20	Hard paving - between Pier 20 to Pier 23 Stage 2																		
<b>Misc Works</b>																							
1073-1370a4.6b	Erection of Additional Directional Signs - Stage 4B (DS146, 153 & 162)	12	20-Jul-20 A	01-Aug-20	Erection of Additional Directional Signs - Stage 4B (DS146, 153 & 162)																		
1073-1410e	Modification of seawall top surface - Stage 6	12	20-Jul-20 A	01-Aug-20	Modification of seawall top surface - Stage 6																		
1073-1410f	Modification of seawall top surface - Stage 7	12	03-Aug-20	15-Aug-20	Modification of seawall top surface - Stage 7																		
1073-1410g	Modification of seawall top surface - Stage 8	12	17-Aug-20	29-Aug-20	Modification of seawall top surface - Stage 8																		
1073-1410h	Modification of seawall top surface - Stage 9	12	31-Aug-20	12-Sep-20	Modification of seawall top surface - Stage 9																		
1073-1410i	Modification of seawall top surface - Stage 10	12	14-Sep-20	26-Sep-20	Modification of seawall top surface - Stage 10																		
1073-1410j	Modification of seawall top surface - Stage 11	12	28-Sep-20	13-Oct-20	Modification of seawall top surface - Stage 11																		
1073-1410k	Modification of seawall top surface - Stage 12	12	14-Oct-20	28-Oct-20	Modification of seawall top surface - Stage 12																		
<b>11 - SECTION 11 OF THE WORKS</b>																							
<b>11.4- Hing Fat Street</b>																							
<b>Other Areas</b>																							
1140-2270c	Road resurfacing at Hing Fat Street - Part 1 Stage 3 (TTA Schemes - Night Work)	12	21-Jul-20*	03-Aug-20	Road resurfacing at Hing Fat Street - Part 1 Stage 3 (TTA Schemes - Night Work)																		

█ Remaining Level of Effort    █ Remaining Work    ◆ Milestone  
█ Actual Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Baseline Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Jul.2020 to 20.Oct.2020)**



Activity ID	Activity Name	Rem Dur	Start	Finish	2020																		
					July			August				September				October				November			
					12	19	26	02	09	16	23	30	06	13	20	27	04	11	18	25	01		
<b>Northern</b>																							
<b>Construction of Noise Enclosure</b>																							
A12010a	Measurement of As-built of L3 Post and Fabrication of L3 Railing Beam	12	31-Jul-20	13-Aug-20	Measurement of As-built of L3 Post and Fabrication of L3 Railing Beam																		
A12020	Installation of L3 railing beam	4	22-Aug-20	25-Aug-20	Installation of L3 railing beam																		
A12030a	Installation of beam - Stage 2 (Night works)	12	25-Jul-20*	05-Aug-20	Installation of beam - Stage 2 (Night works)																		
A12790	Installation of permanent roof PMMA panel -stage 1 (Night works)	11	19-Sep-20	29-Sep-20	Installation of permanent roof PMMA panel -stage 1 (Night works)																		
A12790a	Installation of permanent roof PMMA panel -stage 2 (Night works)	11	30-Sep-20	10-Oct-20	Installation of permanent roof PMMA panel -stage 2 (Night works)																		
A12790b	Installation of permanent roof PMMA panel -stage 3 (Night works)	11	11-Oct-20	21-Oct-20	Installation of permanent roof PMMA panel -stage 3 (Night works)																		
<b>Pier 17 - Pier 18</b>																							
<b>Northern</b>																							
<b>Construction of Noise Enclosure</b>																							
A12140a	Measurement of As-built of L3 Post and Fabrication of L3 Railing Beam	12	31-Jul-20	13-Aug-20	Measurement of As-built of L3 Post and Fabrication of L3 Railing Beam																		
A12150	Installation of L3 railing beam	4	26-Aug-20	29-Aug-20	Installation of L3 railing beam																		
A12800	Installation of permanent roof PMMA panel -stage 1 (Night works)	11	17-Aug-20*	27-Aug-20	Installation of permanent roof PMMA panel -stage 1 (Night works)																		
A12800a	Installation of permanent roof PMMA panel -stage 2 (Night works)	11	28-Aug-20	07-Sep-20	Installation of permanent roof PMMA panel -stage 2 (Night works)																		
A12800b	Installation of permanent roof PMMA panel -stage 3 (Night works)	11	08-Sep-20	18-Sep-20	Installation of permanent roof PMMA panel -stage 3 (Night works)																		
<b>Pier 16 - Pier 17</b>																							
<b>Northern</b>																							
<b>Construction of Inner Parapet</b>																							
A12170	Drilling and insert rebar with chemical adhesive for existing parapet	8	10-Aug-20*	17-Aug-20	Drilling and insert rebar with chemical adhesive for existing parapet																		
A12180	Form of CJ for existing Parapet	6	18-Aug-20	23-Aug-20	Form of CJ for existing Parapet																		
A12190	Reinforcement fixing for precast parapet	6	24-Aug-20	29-Aug-20	Reinforcement fixing for precast parapet																		
A12200	concreting for precast parapet	2	30-Aug-20	31-Aug-20	concreting for precast parapet																		
A12210	Installation of precast parapet	4	01-Sep-20	04-Sep-20	Installation of precast parapet																		
A12220	Rebar fixing between precast parapet and existing parapet	5	05-Sep-20	09-Sep-20	Rebar fixing between precast parapet and existing parapet																		
A12230	Concreting	1	10-Sep-20	10-Sep-20	Concreting																		
<b>12.3 - Waterworks</b>																							
1230-1050	Irrigation System for Landscape Deck - New Pipe at Oil Street	8	10-Aug-20*	18-Aug-20	Irrigation System for Landscape Deck - New Pipe at Oil Street																		
1230-1050a	Irrigation System for Landscape Deck - Pressure Test	12	19-Aug-20	01-Sep-20	Irrigation System for Landscape Deck - Pressure Test																		
1230-1050b	Irrigation System for Landscape Deck - Connection by WSD	12	02-Sep-20	15-Sep-20	Irrigation System for Landscape Deck - Connection by WSD																		
1230-1050c	Irrigation System for Landscape Deck - Auto Irrigation System Stage 1	12	16-Sep-20	29-Sep-20	Irrigation System for Landscape Deck - Auto Irrigation System Stage 1																		
1230-1050d	Irrigation System for Landscape Deck - Auto Irrigation System Stage 2	12	30-Sep-20	15-Oct-20	Irrigation System for Landscape Deck - Auto Irrigation System Stage 2																		
1230-1100b	Irrigation System for Green Roof - Bay 1-2	12	17-Aug-20*	29-Aug-20	Irrigation System for Green Roof - Bay 1-2																		
1230-1100c	Irrigation System for Green Roof - Bay 3	12	31-Aug-20	12-Sep-20	Irrigation System for Green Roof - Bay 3																		
1230-1100d	Irrigation System for Green Roof - Bay 4	12	14-Sep-20	26-Sep-20	Irrigation System for Green Roof - Bay 4																		
1230-1100e	Irrigation System for Green Roof - Bay 5-6	12	28-Sep-20	13-Oct-20	Irrigation System for Green Roof - Bay 5-6																		
1230-1100f	Irrigation System for Green Roof - Pressure Test	12	14-Oct-20	28-Oct-20	Irrigation System for Green Roof - Pressure Test																		
1230-2100a	Installation of Fire Main Stage 1	12	20-Jul-20*	01-Aug-20	Installation of Fire Main Stage 1																		
1230-2100b	Installation of Fire Main Stage 2	12	03-Aug-20	15-Aug-20	Installation of Fire Main Stage 2																		
1230-2100c	Additional 80PE (VO) Stage 1	12	17-Aug-20*	29-Aug-20	Additional 80PE (VO) Stage 1																		
1230-2100d	Additional 80PE (VO) Stage 2	12	31-Aug-20	12-Sep-20	Additional 80PE (VO) Stage 2																		

█ Remaining Level of Effort    █ Remaining Work    ◆ Milestone  
█ Actual Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Baseline Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Jul.2020 to 20.Oct.2020)**

Activity ID	Activity Name	Rem Dur	Start	Finish	2020																		
					July			August				September				October				November			
					12	19	26	02	09	16	23	30	06	13	20	27	04	11	18	25	01		
1230-2100e	Pressure Test for Fire Main	12	14-Sep-20	26-Sep-20																			
A12930	Connection of Fire Main by WSD at Oil Street and Watson Road	12	28-Sep-20	13-Oct-20																			
A12940	Connection of Fire Main by WSD at D12	12	14-Oct-20	28-Oct-20																			
<b>12.4 - Soft &amp; Hard Landscape</b>																							
1240-1000a	Install Remaining Kerb and Paving at Oil Street Planting Area	12	19-Aug-20*	01-Sep-20																			
1240-1000b	Cultivation at Oil Street Planting Area	12	02-Sep-20	15-Sep-20																			
1240-1000d	Planting at Oil Street Planting Area	12	16-Sep-20	29-Sep-20																			
1240-1060c	Lifting Leca to Green Roof Stage 1	12	20-Jul-20 A	01-Aug-20																			
1240-1060d	Lifting Leca to Green Roof Stage 2	12	03-Aug-20*	15-Aug-20																			
1240-1060e	Lifting Leca to Green Roof Stage 3	12	17-Aug-20*	29-Aug-20																			
1240-1060f	Lifting Leca to Green Roof Stage 4	12	31-Aug-20*	12-Sep-20																			
1240-1060g	Lifting Leca to Green Roof Stage 5	12	14-Sep-20*	26-Sep-20																			
1240-1070a	Gree Roof - Leca for Bay 6 Stage 1	12	28-Sep-20*	13-Oct-20																			
1240-1070a1	Gree Roof - Leca for Bay 6 Stage 2	12	14-Oct-20*	28-Oct-20																			
1240-1100a	Gree Roof - Maintenance walkwayfor Bay 6 Stage 1	12	27-Aug-20*	09-Sep-20																			
1240-1100b	Gree Roof - Maintenance walkwayfor Bay 6 Stage 2	12	10-Sep-20	23-Sep-20																			
1240-1100c	Gree Roof - Maintenance walkwayfor Bay 6 Stage 3	12	24-Sep-20	09-Oct-20																			
1240-1100d	Gree Roof - Maintenance walkwayfor Bay 6 Stage 4	12	10-Oct-20	23-Oct-20																			
<b>13 - SECTION 13 OF THE WORKS</b>																							
<b>13.2 - Roadworks</b>																							
1320-1040a	Enlarge Type 1 parapet and 3nos. lighting corbels on Eastbound North side Stage 2	12	20-Jul-20 A	01-Aug-20																			
1320-1040b	Enlarge Type 1 parapet and 3nos. lighting corbels on Eastbound North side Stage 3	12	03-Aug-20	15-Aug-20																			
1320-1040c	Enlarge Type 1 parapet and 3nos. lighting corbels on Eastbound North side Stage 4	12	17-Aug-20	29-Aug-20																			
1320-1040d	Enlarge Type 1 parapet and 3nos. lighting corbels on Eastbound North side Stage 5	12	31-Aug-20	12-Sep-20																			
1320-1040e	Enlarge Type 1 parapet and 3nos. lighting corbels on Eastbound North side Stage 6	10	14-Sep-20	24-Sep-20																			
1320-1050b	Enlarge Type 2 parapet on Eastbound North side Stage 3	12	20-Jul-20	01-Aug-20																			
1320-1050c	Enlarge Type 2 parapet on Eastbound North side Stage 4	12	03-Aug-20	15-Aug-20																			
1320-1060	Construct Lighting corbel on Type 2 parapet, EB North side (3nos.) Stage 1	12	03-Aug-20*	15-Aug-20																			
1320-1060a	Construct Lighting corbel on Type 2 parapet, EB North side (3nos.) Stage 2	12	17-Aug-20	29-Aug-20																			
1320-1060b	Construct Lighting corbel on Type 2 parapet, EB North side (3nos.) Stage 3	12	31-Aug-20	12-Sep-20																			
1320-1060c	Construct Lighting corbel on Type 2 parapet, EB North side (3nos.) Stage 4	7	14-Sep-20	21-Sep-20																			
1320-1070	Demolish existing Westbound steel parapet & construct new steel parapet Stage 1	12	10-Aug-20*	22-Aug-20																			
1320-1070a	Demolish existing Westbound steel parapet & construct new steel parapet Stage 2	12	24-Aug-20	05-Sep-20																			
1320-1070b	Demolish existing Westbound steel parapet & construct new steel parapet Stage 3	12	07-Sep-20	19-Sep-20																			
1320-1080	Construction new steel parapet and traffic sign Stage 1	12	07-Sep-20*	19-Sep-20																			
1320-1090	Enlarge Type 3 parapet Stage 1	12	01-Sep-20*	14-Sep-20																			

█ Remaining Level of Effort    █ Remaining Work    ◆ Milestone  
█ Actual Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Baseline Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Jul.2020 to 20.Oct.2020)**



Activity ID	Activity Name	Rem Dur	Start	Finish	2020																
					August			September				October				November				December	
					16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	
<b>3MRP 2020.08.20</b>																					
<b>10 - SECTION X OF THE WORKS</b>																					
<b>10.3 - Middle Bridge (Bridge F)</b>																					
<b>10.3.2 - Bridge Construction</b>																					
<b>Remaining Works</b>																					
1032-4800-3	Approval of Temp work design for Lighting Corbel Work	12	17-Aug-20 A	02-Sep-20	Approval of Temp work design for Lighting Corbel Work																
1032-4800a	Corbel Const for Permanent light at F4-F5 (location 1)	12	03-Sep-20	16-Sep-20	Corbel Const for Permanent light at F4-F5 (location 1)																
1032-4800b	Corbel Const for Permanent light at F4-F5 (location 2)	12	17-Sep-20	30-Sep-20	Corbel Const for Permanent light at F4-F5 (location 2)																
1032-4800c	Corbel Const for Permanent light at F4-F5 (location 3)	12	03-Oct-20	16-Oct-20	Corbel Const for Permanent light at F4-F5 (location 3)																
1032-4800d	Corbel Const for Permanent light at F4-F5 (location 4)	12	17-Oct-20	31-Oct-20	Corbel Const for Permanent light at F4-F5 (location 4)																
1032-4800e	Corbel Const for Permanent light at F4-F5 (location 5)	12	02-Nov-20	14-Nov-20	Corbel Const for Permanent light at F4-F5 (location 5)																
<b>10.7 - Section X - Miscellaneous Works</b>																					
<b>10.7.3 - Open Area</b>																					
<b>Hard Paving Works Along Sea Wall and Near Harbour Heighs</b>																					
1073-1290n	Hard paving - between Pier 24 to Pier 25 Stage 3	12	17-Aug-20 A	02-Sep-20	Hard paving - between Pier 24 to Pier 25 Stage 3																
1073-1290o	Hard paving - between Pier 24 to Pier 25 Stage 4	12	03-Sep-20	16-Sep-20	Hard paving - between Pier 24 to Pier 25 Stage 4																
1073-1290p	Hard paving - between Pier 24 to Pier 25 Stage 5	12	17-Sep-20	30-Sep-20	Hard paving - between Pier 24 to Pier 25 Stage 5																
1073-1290q	Hard paving - between Pier 20 to Pier 23 Stage 1	12	21-Aug-20*	03-Sep-20	Hard paving - between Pier 20 to Pier 23 Stage 1																
1073-1290r	Hard paving - between Pier 20 to Pier 23 Stage 2	12	04-Sep-20	17-Sep-20	Hard paving - between Pier 20 to Pier 23 Stage 2																
1073-1290s	Hard paving - between Pier 20 to Pier 23 Stage 3	12	18-Sep-20	03-Oct-20	Hard paving - between Pier 20 to Pier 23 Stage 3																
1073-1290t	Hard paving - between Pier 20 to Pier 23 Stage 4	12	05-Oct-20	17-Oct-20	Hard paving - between Pier 20 to Pier 23 Stage 4																
1073-1290u	Hard paving - between Pier 20 to Pier 23 Stage 5	12	19-Oct-20	02-Nov-20	Hard paving - between Pier 20 to Pier 23 Stage 5																
1073-1300	Hard paving - between Watson Rd to Pier 21 Stage 1	12	07-Sep-20*	19-Sep-20	Hard paving - between Watson Rd to Pier 21 Stage 1																
1073-1300a	Hard paving - between Watson Rd to Pier 21 Stage 2	12	21-Sep-20	06-Oct-20	Hard paving - between Watson Rd to Pier 21 Stage 2																
1073-1300b	Hard paving - between Watson Rd to Pier 21 Stage 3	12	07-Oct-20	20-Oct-20	Hard paving - between Watson Rd to Pier 21 Stage 3																
1073-1300c	Hard paving - between Watson Rd to Pier 21 Stage 4	12	21-Oct-20	04-Nov-20	Hard paving - between Watson Rd to Pier 21 Stage 4																
1073-1300d	Hard paving - between Watson Rd to Pier 21 Stage 5	12	05-Nov-20	18-Nov-20	Hard paving - between Watson Rd to Pier 21 Stage 5																
1073-1300e	Hard paving - between Watson Rd to Pier 21 Stage 6	12	19-Nov-20	02-Dec-20	Hard paving - between Watson Rd to Pier 21 Stage 6																
<b>Misc Works</b>																					
1073-1410g	Modification of seawall top surface - Stage 8	12	17-Aug-20 A	02-Sep-20	Modification of seawall top surface - Stage 8																
1073-1410h	Modification of seawall top surface - Stage 9	12	03-Sep-20	16-Sep-20	Modification of seawall top surface - Stage 9																
1073-1410i	Modification of seawall top surface - Stage 10	12	17-Sep-20	30-Sep-20	Modification of seawall top surface - Stage 10																
1073-1410j	Modification of seawall top surface - Stage 11	12	03-Oct-20	16-Oct-20	Modification of seawall top surface - Stage 11																
1073-1410k	Modification of seawall top surface - Stage 12	12	17-Oct-20	31-Oct-20	Modification of seawall top surface - Stage 12																
1073-1410l	Modification of seawall top surface - Stage 13	12	02-Nov-20	14-Nov-20	Modification of seawall top surface - Stage 13																
1073-1410m	Modification of seawall top surface - Stage 14	12	16-Nov-20	28-Nov-20	Modification of seawall top surface - Stage 14																
<b>11 - SECTION 11 OF THE WORKS</b>																					
<b>11.4- Hing Fat Street</b>																					
<b>Other Areas</b>																					
1140-2270e	Road resurfacing at Hing Fat Street - Part 1 Stage 5 (TTA Schemes - Night Work)	12	18-Aug-20 A	02-Sep-20	Road resurfacing at Hing Fat Street - Part 1 Stage 5 (TTA Schemes - Night Work)																

█ Remaining Level of Effort    █ Remaining Work    ◆ Milestone  
█ Actual Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Baseline Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Aug.2020 to 20.Nov.2020)**














Data Date: 20-Jul-20

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
<b>Update 2020-06-20 CWB(CC) - Commissioning Contract (DWP 4g)</b>					
<b>PRELIMINARIES AND GENERAL REQUIREMENTS</b>					
<b>Salient Key Dates and Milestones</b>					
<b>Anticipated Completion Dates</b>					
KD09	KD9 - Completion of Section 4 of the Works (1445 days) - include EOT No.12 (149 days)	0		20-Jul-20*	-1037
KD11	KD11 - Completion of Section 6 of the Works (1445 days) - include EOT No.12 (149 days)	0		20-Jul-20*	-889
KD07	KD7 - Completion of Section 2 of the Works (1771 days) - include EOT No.12 (414 days)	0		18-Aug-20*	-702
<b>Possession Dates and Vacation Dates</b>					
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-Jul-20	07-Nov-20	-889
<b>Submissions and Approvals</b>					
<b>Initial General Submission</b>					
10168	Submission of CMC 3DVR	30	20-Jul-20	18-Aug-20	-702
<b>CONSTRUCTION</b>					
<b>Commissioning Test</b>					
10126	Establishment Works	365	20-Jul-20	19-Jul-21	-1037
9930	Contract Completion	0		18-Aug-20	-702
<b>Training / Plan / Manual / As-Built Drawings for Project Completion / Establishment</b>					
10226	Routine Maintenance Records / Maintenance Monthly Report	0	20-Jul-20		-672

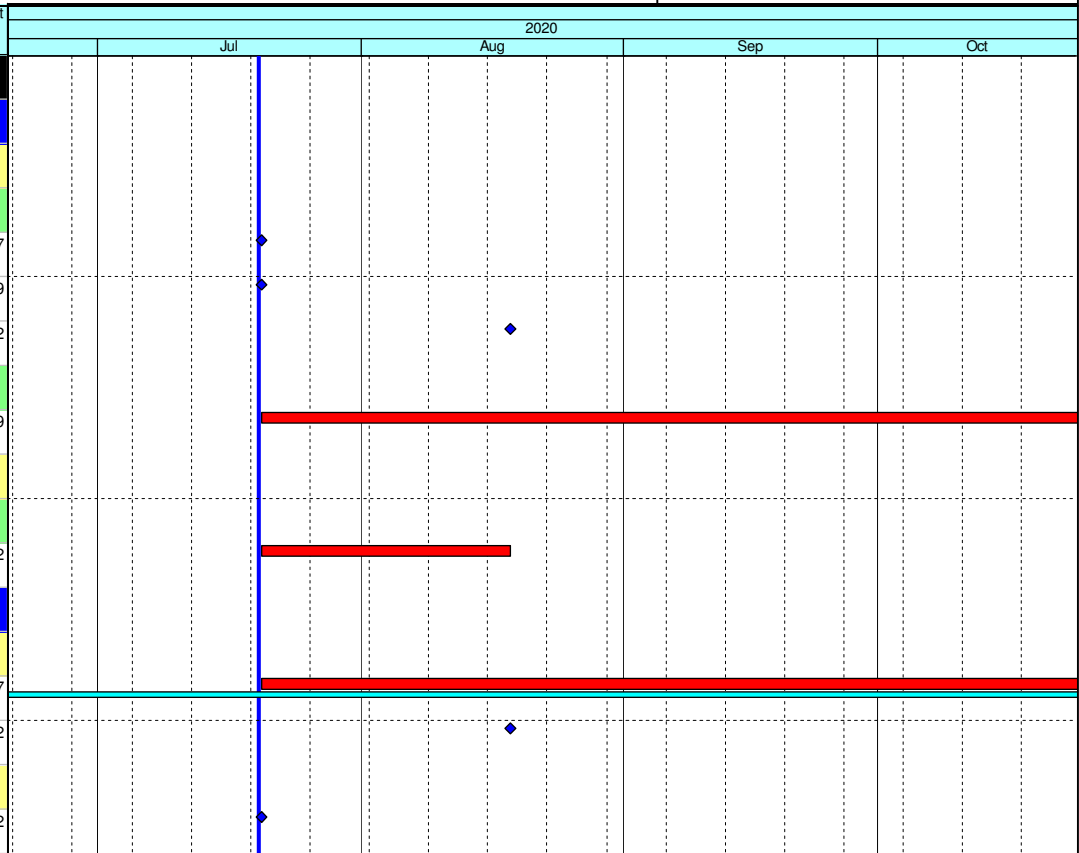

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 77 (July 2020) THREE MONTH ROLLING

Project ID: H2613-U077  
 Baseline: DWP4g  
 Layout: Update Three Month Rolling  
 U077  
 Page 1 of 1

Date	Revision	Checked	Approv...
20-Jun-20...	U076	AT	CW
20-Jul-20...	U077	AT	CW
