

Programme for Outstanding and Defective Works

CSF: PR/S-0336 REV D
APPENDIX A

ID	Task Name	Duration	Start	Finish	Finish (Programme dd 25 June 2019)	Qtr 3, 2019							Qtr 4, 2019						
						July	August	September	October	November	December	1							
1	1. Site Formation Drainage Works, K1 Kerb with Subbase Pavement and Chain Link Fences/Access Gates in WCR1 to WCR4	315 days	20 February 2019	31 December 2019	31 December 2019	[Timeline bar from 20 Feb 2019 to 31 Dec 2019]													
15	2. Rectification of Caisson Seawalls and Installation of Corrosion Monitoring System (CMS) of Caisson Seawalls in WCR1 and WCR3	136 days	20 February 2019	05 July 2019	05 July 2019	[Timeline bar from 20 Feb 2019 to 05 Jul 2019]													
32	3. Rectification of 0.5T Rock Armour and Seabed Level (High Spot to be Trimmed) in WCR3	85 days	08 June 2019	31 August 2019	31 August 2019	[Timeline bar from 08 Jun 2019 to 31 Aug 2019]													
43	4. Rectification of Grade 400 Rockfill and 0.5T Rock Armour in WCR1	68 days	14 June 2019	20 August 2019	04 August 2019	[Timeline bar from 14 Jun 2019 to 04 Aug 2019]													
52	5. Construction of EVA for Ferry Pier in WCR1 (Completed)	0 days	22 January 2019	22 January 2019	22 January 2019	[Timeline bar from 22 Jan 2019 to 22 Jan 2019]													
53	6. Construction of Road Improvement Works and Reconstruction of Hung Hing Road under VO254 (Footpath Pavement, Roadside Barrier, Irrigation System, Road Lighting System), and Reinstatement of Associated Existing Footpath on Hung Hing Road	302 days	02 October 2018	30 July 2019	30 July 2019	[Timeline bar from 02 Oct 2018 to 30 Jul 2019]													
78	7. Blockwork Seawalls (Construction of Remaining Seawall Coping) in WCR4 (Completed)	0 days	09 January 2019	09 January 2019	09 January 2019	[Timeline bar from 09 Jan 2019 to 09 Jan 2019]													
80	8. Completion of Remaining Grade 400 for Seawalls in WCR4 (Completed)	77 days	26 February 2019	13 May 2019	13 May 2019	[Timeline bar from 26 Feb 2019 to 13 May 2019]													
94	9. Completion of Remaining Backfilling Works in WCR4 (Completed)	0 days	19 February 2019	19 February 2019	19 February 2019	[Timeline bar from 19 Feb 2019 to 19 Feb 2019]													
95	10. Reinstatement of Existing Seabed Level in TWCR4 (Completed)	145 days	03 April 2019	25 August 2019	25 August 2019	[Timeline bar from 03 Apr 2019 to 25 Aug 2019]													
113	11. Construction of Landing Steps (Type 10 and Type 11 Seawalls) in Ex-Helipad	170 days	03 March 2019	19 August 2019	19 August 2019	[Timeline bar from 03 Mar 2019 to 19 Aug 2019]													
205	12. Reinstatement of Existing Seawall at Box Culvert O Temporary Diversion in Ex-PWCA Basin (Completed)	0 days	14 January 2019	14 January 2019	14 January 2019	[Timeline bar from 14 Jan 2019 to 14 Jan 2019]													
207	13. Reinstatement of Existing Pavement and Drainage System in Ex-Helipad	79 days	02 June 2019	19 August 2019	19 August 2019	[Timeline bar from 02 Jun 2019 to 19 Aug 2019]													
248	14. Rectification of Granite Facing Stone on Existing Seawall in WCR4 and Ex-PWCA Basin (70nos.)	28 days	17 July 2019	13 August 2019	13 August 2019	[Timeline bar from 17 Jul 2019 to 13 Aug 2019]													
252	15. Reinstatement of Hung Hing Road and Wan Shing Street in Accordance to Hung Hing Road Traffic Diversion Reinstatement Stage 0.5 Scheme Under VO No. 257 on Hung Hing Road	248 days	01 March 2019	03 November 2019	26 October 2019	[Timeline bar from 01 Mar 2019 to 03 Nov 2019]													
576	16. Reinstatement of LCSD Sitting Out Area underneath Hung Hing Road Flyover on Hung Hing Road	17 days	08 May 2019	24 May 2019	24 May 2019	[Timeline bar from 08 May 2019 to 24 May 2019]													
582	17. Completion of Notice Submission of CWXP No. C000266 on Hung Hing Road, Wan Shing Street and Expo Drive East (Notional)	0 days	20 September 2019	20 September 2019	20 September 2019	[Timeline bar from 20 Sep 2019 to 20 Sep 2019]													
584	18. Completion of Notice Submission of XP No. 1202793 on Expo Drive East	0 days	20 April 2019	20 April 2019	20 April 2019	[Timeline bar from 20 Apr 2019 to 20 Apr 2019]													
585	19. Modification Work inside Room of Hung Hing Road Flyover (Completed)	9 days	21 March 2019	29 March 2019	29 March 2019	[Timeline bar from 21 Mar 2019 to 29 Mar 2019]													
590	20. Ladder Installation Inside Room of Hung Hing Road (Completed)	9 days	21 March 2019	29 March 2019	29 March 2019	[Timeline bar from 21 Mar 2019 to 29 Mar 2019]													
595	21. Defective Works of the Reinstatement of Hung Hing Road Flyover, such as Painting of Wall of Flyover, Touch-up Rust of Steel Door and Steel Vehicular Parapet and etc. (Completed)	34 days	24 March 2019	26 April 2019	26 April 2019	[Timeline bar from 24 Mar 2019 to 26 Apr 2019]													
601	22. Establishment Period for 8nos. (6nos.) of Trees Being Transplanted Back Underneath Hung Hing Road Flyover	366 days	11 June 2019	10 June 2020	10 June 2020	[Timeline bar from 11 Jun 2019 to 10 Jun 2020]													
604	23. Construction of Watermain Across Hung Hing Road	128 days	30 August 2019	04 January 2020	27 December 2019	[Timeline bar from 30 Aug 2019 to 04 Jan 2020]													
643	24. Repaving Work at Hung Hing Road and Wan Shing Street	199 days	21 June 2019	05 January 2020	29 December 2019	[Timeline bar from 21 Jun 2019 to 05 Jan 2020]													
672	25. Rectification Works of Temporary Covered Walkway	90 days	27 May 2019	24 August 2019	12 August 2019	[Timeline bar from 27 May 2019 to 24 Aug 2019]													
726	26. Tree Transplanting	541 days	14 May 2019	04 November 2020	04 November 2020	[Timeline bar from 14 May 2019 to 04 Nov 2020]													
771	27. Reprovision of Public Lighting and Directional Sign at Hung Hing Road and Wan Shing Street	213 days	14 May 2019	12 December 2019	12 December 2019	[Timeline bar from 14 May 2019 to 12 Dec 2019]													

Task Baseline Milestone Project Summary Deadline Finish-only
Critical Split Baseline Milestone Summary Group By Summary Start-only

Activity ID	Activity Name	Original Duration	Start	Finish	2020																		
					Jan	Feb	Mar	Apr															
Total		385.0	31-Mar-19 A	03-May-20																			
DWP-08 - (2) - Update Progress As of 20 Jan 20		385.0	31-Mar-19 A	03-May-20																			
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks		385.0	31-Mar-19 A	03-May-20																			
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)		365.0	31-Mar-19 A	29-Feb-20																			
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365.0	31-Mar-19 A	29-Feb-20																			
KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH>500mm)		365.0	20-Apr-19 A	03-May-20																			
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365.0	20-Apr-19 A	03-May-20																			
KD18 - Section 11: Transplanted Trees DBH>500mm in Portion VA and XII		365.0	20-Apr-19 A	03-May-20																			
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365.0	20-Apr-19 A	03-May-20																			

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Page 1 of 1
 Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel (Slip Road 8 Section) - 3 Months Rolling Programme

Date	Revision	Checked	Approved
20-Jan-20	DWP-08 (2) - 3 Months Rolling	TL	TL



Activity ID	Activity Name	Rem Dur	Start	Finish	2020							2021							
					November			December				January				February			March
					15	22	29	06	13	20	27	03	10	17	24	31	07	14	21
3MRP 2020.11.20																			
10 - SECTION X OF THE WORKS																			
10.3 - Middle Bridge (Bridge F)																			
10.3.2 - Bridge Construction																			
Remaining Works																			
1032-4800-3	Approval of Temp work design for Lighting Corbel Work	9	17-Aug-20 A	30-Nov-20	Approval of Temp work design for Lighting Corbel Work														
1032-4800a	Corbel Const for Permanent light at F4-F5 (location 1)	12	01-Dec-20	14-Dec-20	Corbel Const for Permanent light at F4-F5 (location 1)														
1032-4800b	Corbel Const for Permanent light at F4-F5 (location 2)	11	15-Dec-20	28-Dec-20	Corbel Const for Permanent light at F4-F5 (location 2)														
1032-4800c	Corbel Const for Permanent light at F4-F5 (location 3)	11	29-Dec-20	11-Jan-21	Corbel Const for Permanent light at F4-F5 (location 3)														
1032-4800d	Corbel Const for Permanent light at F4-F5 (location 4)	12	12-Jan-21	25-Jan-21	Corbel Const for Permanent light at F4-F5 (location 4)														
1032-4800e	Corbel Const for Permanent light at F4-F5 (location 5)	12	26-Jan-21	08-Feb-21	Corbel Const for Permanent light at F4-F5														
10.7 - Section X - Miscellaneous Works																			
10.7.3 - Open Area																			
Hard Paving Works Along Sea Wall and Near Harbour Heighs																			
1073-1290p4	Hard paving - between Pier 24 to Pier 25 Stage 9	7	14-Nov-20 A	27-Nov-20	Hard paving - between Pier 24 to Pier 25 Stage 9														
1073-1290p5	Hard paving - between Pier 24 to Pier 25 Stage 10	12	28-Nov-20	11-Dec-20	Hard paving - between Pier 24 to Pier 25 Stage 10														
1073-1290r	Hard paving - between Pier 20 to Pier 23 Stage 2	1	07-Oct-20 A	20-Nov-20	Hard paving - between Pier 20 to Pier 23 Stage 2														
1073-1290s	Hard paving - between Pier 20 to Pier 23 Stage 3	12	21-Nov-20	04-Dec-20	Hard paving - between Pier 20 to Pier 23 Stage 3														
1073-1290t	Hard paving - between Pier 20 to Pier 23 Stage 4	12	05-Dec-20	18-Dec-20	Hard paving - between Pier 20 to Pier 23 Stage 4														
1073-1290u	Hard paving - between Pier 20 to Pier 23 Stage 5	10	19-Dec-20	31-Dec-20	Hard paving - between Pier 20 to Pier 23 Stage 5														
1073-1300a	Hard paving - between Watson Rd to Pier 21 Stage 2	1	07-Oct-20 A	20-Nov-20	Hard paving - between Watson Rd to Pier 21 Stage 2														
1073-1300b	Hard paving - between Watson Rd to Pier 21 Stage 3	12	02-Jan-21	15-Jan-21	Hard paving - between Watson Rd to Pier 21 Stage 3														
1073-1300c	Hard paving - between Watson Rd to Pier 21 Stage 4	12	16-Jan-21	29-Jan-21	Hard paving - between Watson Rd to Pier 21 Stage 4														
1073-1300d	Hard paving - between Watson Rd to Pier 21 Stage 5	12	30-Jan-21	16-Feb-21	Hard paving - between Watson Rd to Pier 21 Stage 5														
1073-1300e	Hard paving - between Watson Rd to Pier 21 Stage 6	12	17-Feb-21	02-Mar-21	Hard paving - between Watson Rd to Pier 21 Stage 6														
1073-1300f	Hard paving - between Watson Rd to Pier 21 Stage 7	12	03-Mar-21	16-Mar-21	Hard paving - between Watson Rd to Pier 21 Stage 7														
Misc Works																			
1073-1410m	Modification of seawall top surface - Stage 14	11	19-Nov-20 A	02-Dec-20	Modification of seawall top surface - Stage 14														
1073-1410n	Modification of seawall top surface - Stage 15	12	03-Dec-20	16-Dec-20	Modification of seawall top surface - Stage 15														
1073-1410o	Modification of seawall top surface - Stage 16	11	17-Dec-20	30-Dec-20	Modification of seawall top surface - Stage 16														
1073-1410p	Modification of seawall top surface - Stage 17	11	31-Dec-20	13-Jan-21	Modification of seawall top surface - Stage 17														
1073-1410q	Modification of seawall top surface - Stage 18	12	14-Jan-21	27-Jan-21	Modification of seawall top surface - Stage 18														
1073-1410t	Modification of seawall top surface - Stage 19	12	28-Jan-21	10-Feb-21	Modification of seawall top surface - Stage 19														
11 - SECTION 11 OF THE WORKS																			
11.4- Hing Fat Street																			
Other Areas																			
1140-2280c	Further Improvement of Hing Fat Street Stage 4	9	17-Nov-20 A	30-Nov-20	Further Improvement of Hing Fat Street Stage 4														
1140-2280d	Further Improvement of Hing Fat Street Stage 5	12	01-Dec-20	14-Dec-20	Further Improvement of Hing Fat Street Stage 5														
1140-2280e	Further Improvement of Hing Fat Street Stage 6	11	15-Dec-20	28-Dec-20	Further Improvement of Hing Fat Street Stage 6														
1140-2280f	Further Improvement of Hing Fat Street Stage 7	11	29-Dec-20	11-Jan-21	Further Improvement of Hing Fat Street Stage 7														
1140-2280g	Further Improvement of Hing Fat Street Stage 8	12	12-Jan-21	25-Jan-21	Further Improvement of Hing Fat Street Stage 8														

Remaining Level of Effort	Remaining Work	Milestone
Actual Level of Effort	Critical Remaining Work	Baseline Milestone
Actual Work		

Contract HY/2009/19
Three Months Rolling Programme (20.Nov.2020 to 20.Feb.2021)

Activity ID	Activity Name	Rem Dur	Start	Finish	2020							2021							
					November			December				January			February				March
					15	22	29	06	13	20	27	03	10	17	24	31	07	14	21
12 - SECTION 7, 8, 9, 10 & 12 OF THE WORKS																			
12.1 - Landscape Deck																			
1200-7830I	Planting for D4	9	16-Oct-20 A	30-Nov-20	Planting for D4														
12.2 - THE WORKS along IECL																			
12.2.1 - Noise Enclosure and Inner Parapet along IECL Westbound																			
West Bound Brigade Between F2 to C2 (P40 to P22) (parapet mould 1)																			
Pier 17 - Pier 26 (Section 8)																			
Pier 20 - Pier 21																			
Northern																			
Construction of Noise Enclosure																			
A11760a	Installation of permanent roof PMMA panel - stage 2 (Night works)	10	19-Dec-20	28-Dec-20	Installation of permanent roof PMMA panel - stage 2 (Night works)														
A11760b	Installation of permanent roof PMMA panel - stage 3 (Night works)	10	29-Dec-20	07-Jan-21	Installation of permanent roof PMMA panel - stage 3 (Night works)														
Pier 19 - Pier 20																			
Southern																			
Construction of Noise Enclosure																			
A11790	Installation of permanent roof PMMA panel (Night works)	12	08-Dec-20	19-Dec-20	Installation of permanent roof PMMA panel (Night works)														
Northern																			
Construction of Noise Enclosure																			
A11900b	Installation of permanent roof PMMA panel - stage 3 (Night works)	9	10-Dec-20	18-Dec-20	Installation of permanent roof PMMA panel - stage 3 (Night works)														
Pier 17 - Pier 18																			
Northern																			
Construction of Noise Enclosure																			
A12800a	Installation of permanent roof PMMA panel - stage 2 (Night works)	10	17-Sep-20 A	29-Nov-20	Installation of permanent roof PMMA panel - stage 2 (Night works)														
A12800b	Installation of permanent roof PMMA panel - stage 3 (Night works)	10	30-Nov-20	09-Dec-20	Installation of permanent roof PMMA panel - stage 3 (Night works)														
12.3 - Waterworks																			
1230-1050a	Irrigation System for Landscape Deck - New Pipe at Oil Street Stage 2	1	07-Oct-20 A	20-Nov-20	Irrigation System for Landscape Deck - New Pipe at Oil Street Stage 2														
1230-1050a1	Irrigation System for Landscape Deck - New Pipe at Oil Street Stage 3	8	21-Nov-20	30-Nov-20	Irrigation System for Landscape Deck - New Pipe at Oil Street Stage 3														
1230-1050b	Irrigation System for Landscape Deck - Pressure Test	12	01-Dec-20	14-Dec-20	Irrigation System for Landscape Deck - Pressure Test														
1230-1050c	Irrigation System for Landscape Deck - Connection by WSD	12	15-Dec-20	29-Dec-20	Irrigation System for Landscape Deck - Connection by WSD														
1230-1050e	Irrigation System for Landscape Deck - Auto Irrigation System Stage 2	1	07-Oct-20 A	20-Nov-20	Irrigation System for Landscape Deck - Auto Irrigation System Stage 2														
1230-1050g	Irrigation System for Landscape Deck - Auto Irrigation System Stage 3	12	21-Nov-20	04-Dec-20	Irrigation System for Landscape Deck - Auto Irrigation System Stage 3														
1230-1050h	Irrigation System for Landscape Deck - Auto Irrigation System Stage 4	9	05-Dec-20	15-Dec-20	Irrigation System for Landscape Deck - Auto Irrigation System Stage 4														
1230-1100b	Irrigation System for Green Roof - Bay 1-2	12	15-Dec-20*	29-Dec-20	Irrigation System for Green Roof - Bay 1-2														
1230-1100c	Irrigation System for Green Roof - Bay 3	12	30-Dec-20	13-Jan-21	Irrigation System for Green Roof - Bay 3														
1230-1100d	Irrigation System for Green Roof - Bay 4	12	14-Jan-21	27-Jan-21	Irrigation System for Green Roof - Bay 4														
1230-1100e	Irrigation System for Green Roof - Bay 5-6	12	28-Jan-21	10-Feb-21	Irrigation System for Green Roof - Bay 5-6														
1230-2100h	Pressure Test for Fire Main	8	16-Nov-20 A	28-Nov-20	Pressure Test for Fire Main														
A12930	Connection of Fire Main by WSD at Oil Street and Watson Road	12	30-Nov-20	12-Dec-20	Connection of Fire Main by WSD at Oil Street and Watson Road														
A12940	Connection of Fire Main by WSD at D12	12	14-Dec-20	28-Dec-20	Connection of Fire Main by WSD at D12														
A12950	Connection of Fire Main by WSD at Pier 28 Stage 1	12	29-Dec-20	12-Jan-21	Connection of Fire Main by WSD at Pier 28 Stage 1														
A12960	Connection of Fire Main by WSD at Pier 28 Stage 2	12	13-Jan-21	26-Jan-21	Connection of Fire Main by WSD at Pier 28 Stage 2														

█ Remaining Level of Effort █ Remaining Work ◆ Milestone
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Baseline Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Nov.2020 to 20.Feb.2021)

Activity ID	Activity Name	Rem Dur	Start	Finish	2021																
					January			February			March				April				May		
					0	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02
3MRP 2021.1.20																					
10 - SECTION X OF THE WORKS																					
10.3 - Middle Bridge (Bridge F)																					
10.3.2 - Bridge Construction																					
Remaining Works																					
1032-4800a	Corbel Const for Permanent light at F4-F5 (location 1)	12	28-Jan-21	10-Feb-21	Corbel Const for Permanent light at F4-F5 (location 1)																
1032-4800b	Corbel Const for Permanent light at F4-F5 (location 2)	11	11-Feb-21	26-Feb-21	Corbel Const for Permanent light at F4-F5 (location 2)																
1032-4800c	Corbel Const for Permanent light at F4-F5 (location 3)	11	27-Feb-21	11-Mar-21	Corbel Const for Permanent light at F4-F5 (location 3)																
1032-4800d	Corbel Const for Permanent light at F4-F5 (location 4)	12	12-Mar-21	25-Mar-21	Corbel Const for Permanent light at F4-F5 (location 4)																
1032-4800e	Corbel Const for Permanent light at F4-F5 (location 5)	12	26-Mar-21	10-Apr-21	Corbel Const for Permanent light at F4-F5																
1032-4801-3	TCSS concreting (Stage 4)	7	20-Jan-21 A	27-Jan-21	TCSS concreting (Stage 4)																
10.7 - Section X - Miscellaneous Works																					
10.7.3 - Open Area																					
Hard Paving Works Along Sea Wall and Near Harbour Heighs																					
1073-1290w	Hard paving & Channel - between Pier 20 to Pier 23 Stage 7	9	16-Jan-21 A	29-Jan-21	Hard paving & Channel - between Pier 20 to Pier 23 Stage 7																
1073-1290x	Hard paving & Channel - between Pier 20 to Pier 23 Stage 8	12	30-Jan-21	16-Feb-21	Hard paving & Channel - between Pier 20 to Pier 23 Stage 8																
1073-1290y	Hard paving & Channel - between Pier 20 to Pier 23 Stage 9	10	17-Feb-21	27-Feb-21	Hard paving & Channel - between Pier 20 to Pier 23 Stage 9																
1073-1300c	Hard paving - between Watson Rd to Pier 21 Stage 4	9	16-Jan-21 A	29-Jan-21	Hard paving - between Watson Rd to Pier 21 Stage 4																
1073-1300d	Hard paving - between Watson Rd to Pier 21 Stage 5	12	30-Jan-21	16-Feb-21	Hard paving - between Watson Rd to Pier 21 Stage 5																
1073-1300e	Hard paving - between Watson Rd to Pier 21 Stage 6	12	17-Feb-21	02-Mar-21	Hard paving - between Watson Rd to Pier 21 Stage 6																
1073-1300f	Hard paving - between Watson Rd to Pier 21 Stage 7	12	03-Mar-21	16-Mar-21	Hard paving - between Watson Rd to Pier 21 Stage 7																
Misc Works																					
1073-1410q	Modification of seawall top surface - Stage 18	7	14-Jan-21 A	27-Jan-21	Modification of seawall top surface - Stage 18																
1073-1410r	Modification of seawall top surface - Stage 19	12	28-Jan-21	10-Feb-21	Modification of seawall top surface - Stage 19																
1073-1410s	Modification of seawall top surface - Stage 20	12	11-Feb-21	27-Feb-21	Modification of seawall top surface - Stage 20																
1073-1410t	Modification of seawall top surface - Stage 21	12	01-Mar-21	13-Mar-21	Modification of seawall top surface - Stage 21																
1073-1410u	Modification of seawall top surface - Stage 22	12	15-Mar-21	27-Mar-21	Modification of seawall top surface - Stage 22																
11 - SECTION 11 OF THE WORKS																					
11.4- Hing Fat Street																					
Other Areas																					
1140-2280d1	Further Improvement of Hing Fat Street Stage 4 (Part 2)	9	20-Jan-21 A	29-Jan-21	Further Improvement of Hing Fat Street Stage 4 (Part 2)																
1140-2280e	Further Improvement of Hing Fat Street Stage 5	9	30-Jan-21	09-Feb-21	Further Improvement of Hing Fat Street Stage 5																
1140-2280f	Further Improvement of Hing Fat Street Stage 6 (Part 1)	9	10-Feb-21	23-Feb-21	Further Improvement of Hing Fat Street Stage 6 (Part 1)																
1140-2280f1	Further Improvement of Hing Fat Street Stage 6 (Part 2)	12	24-Feb-21	09-Mar-21	Further Improvement of Hing Fat Street Stage 6 (Part 2)																
1140-2280g	Further Improvement of Hing Fat Street Stage 7 (Part 1)	12	10-Mar-21	23-Mar-21	Further Improvement of Hing Fat Street Stage 7 (Part 1)																
1140-2280g1	Further Improvement of Hing Fat Street Stage 7 (Part 2)	7	24-Mar-21	31-Mar-21	Further Improvement of Hing Fat Street Stage 7 (Part 2)																
1140-2290	Remaining works on footpath	8	01-Apr-21	12-Apr-21	Remaining works on footpath																
1140-2300	Resurfacing of HFS (Works on Sunday only, 10 Sundays)	65	01-Apr-21	19-Jun-21																	
12 - SECTION 7, 8, 9, 10 & 12 OF THE WORKS																					
12.3 - Waterworks																					
1230-1050a2	Irrigation System for Landscape Deck - New Pipe at Oil Street Stage 4	4	20-Jan-21 A	23-Jan-21	Irrigation System for Landscape Deck - New Pipe at Oil Street Stage 4																

	Remaining Level of Effort		Remaining Work		Milestone
	Actual Level of Effort		Critical Remaining Work		Baseline Milestone
	Actual Work				

Contract HY/2009/19
Three Months Rolling Programme (20.Jan.2021 to 20.Apr.2021)

Activity ID	Activity Name	Rem Dur	Start	Finish	2021																		
					January				February				March				April				May		
					0	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02		
1320-1800	Modification of Type 2 parapet at westbound (Part 1)	12	10-Feb-21	26-Feb-21																			
1320-1800-1	Modification of Type 2 parapet at westbound (Part 2)	12	27-Feb-21	12-Mar-21																			
1320-1800-2	Modification of Type 2 parapet at westbound (Part 3)	13	13-Mar-21	27-Mar-21																			
1320-1900	Drainage works at westbound (Part 1)	12	10-Feb-21	26-Feb-21																			
1320-1900-1	Drainage works at westbound (Part 2)	12	27-Feb-21	12-Mar-21																			
1320-1900-2	Drainage works at westbound (Part 3)	13	13-Mar-21	27-Mar-21																			
1320-2000	Replacement of MJ, resurfacing & road on wetbound	6	29-Mar-21	06-Apr-21																			
13.3 - Soft Landscape																							
1330-1000	Soft Landscape at Portion XIII	12	02-Feb-21*	18-Feb-21																			
17 - VO Additional Works																							
Quick-win Promenade at Open Area																							
1075-1200	Site establishment and demolish existing on grade slab	0	14-Dec-20 A	26-Dec-20 A																			
1075-1300-1	Construct Kids Land and City Hangout (Part 1)	12	28-Dec-20 A	02-Feb-21																			
1075-1300-2	Construct Kids Land and City Hangout (Part 2)	12	03-Feb-21	19-Feb-21																			
1075-1300-3	Construct Kids Land and City Hangout (Part 3)	12	20-Feb-21	05-Mar-21																			
1075-1300-4	Construct Kids Land and City Hangout (Part 4)	12	06-Mar-21	19-Mar-21																			
1075-1300-5	Construct Kids Land and City Hangout (Part 5)	12	20-Mar-21	03-Apr-21																			
1075-1300-6	Construct Kids Land and City Hangout (Part 6)	12	06-Apr-21	19-Apr-21																			
1075-1400-1	Construct Sunset Gallery (Part 1)	12	12-Apr-21	24-Apr-21																			
1075-1500-1	Construct entrance area (Part 1)	12	14-Jan-21 A	02-Feb-21																			
1075-1500-2	Construct entrance area (Part 2)	12	03-Feb-21	19-Feb-21																			
1075-1500-3	Construct entrance area (Part 3)	12	20-Feb-21	05-Mar-21																			
1075-1500-4	Construct entrance area (Part 4)	12	06-Mar-21	19-Mar-21																			
1075-1700-1	Plumbing & Drainage Installation (Part 1)	12	05-Feb-21 A	02-Feb-21																			
1075-1700-2	Plumbing & Drainage Installation (Part 2)	12	03-Feb-21	19-Feb-21																			
1075-1700-3	Plumbing & Drainage Installation (Part 3)	12	20-Feb-21	05-Mar-21																			
1075-1700-4	Plumbing & Drainage Installation (Part 4)	12	06-Mar-21	19-Mar-21																			
Downstream Road Marking (Drafted VO 332)																							
1074-2800-3	Banner installation and road marking modification (Part 3)	12	20-Jan-21 A	02-Feb-21																			
1074-2800-4	Banner installation and road marking modification (Part 4)	12	03-Feb-21	19-Feb-21																			
Further Modification Works on IEC																							
IEC Eastbound																							
1074-1100-4	Fabrication of L3 Railing for Fast Lane Part 1	14	21-Jan-21 A	04-Feb-21																			
1074-1100-5	Fabrication of L3 Railing for Fast Lane Part 2	18	05-Feb-21	01-Mar-21																			
1074-1100-6	Installation of L3 Railing at Fast Lane	14	02-Mar-21	17-Mar-21																			
1074-1200-1	Pavement for Fast Lane Bottom Layer (include testing time)	6	22-Jan-21*	28-Jan-21																			
1074-1200-2	Pavement for Fast Lane Top Layer (include testing time)	12	29-Jan-21	11-Feb-21																			
1074-1200-3	Road Marking and Shifting TTA to Seaside	2	18-Mar-21	19-Mar-21																			
1074-1300-B1	Construction of enlarge seaside parapet E3 to E2	12	20-Jan-21	02-Feb-21																			
1074-1300-B2	Construction of enlarge seaside parapet E2 to E1	12	03-Feb-21	19-Feb-21																			
1074-1300-B3	Construction of enlarge seaside parapet E1 to D1	12	20-Feb-21	05-Mar-21																			

█ Remaining Level of Effort █ Remaining Work ◆ Milestone
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Baseline Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Jan.2021 to 20.Apr.2021)

Activity ID	Activity Name	Rem Dur	Start	Finish	2021																			
					January					February					March					April				
					0	7	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	
1074-1300-B4	Construction of enlarge seaside parapet D1 to D2	12	06-Mar-21	19-Mar-21																		Construction of enlarge seaside parapet D1 to D2		
1074-1300-C1	Construction of enlarge seaside parapet to D12 to F1A (Part 1)	12	20-Mar-21	03-Apr-21																		Construction of enlarge seaside parapet to D12 to F1A		
1074-1300-C1a	Construction of enlarge seaside parapet to D12 to F1A (Part 2)	4	06-Apr-21	09-Apr-21																		Construction of enlarge seaside parapet to D12 to F1A		
1074-1300-C2	Construction of enlarge seaside parapet to D11 to D12 (Part 1)	12	10-Apr-21	23-Apr-21																		Construction of enlarge seaside parapet to D11 to D12		
1074-1300-C2a	Construction of enlarge seaside parapet to D11 to D12 (Part 2)	4	24-Apr-21	28-Apr-21																		Construction of enlarge seaside parapet to D11 to D12		
1074-1300-C3	Construction of enlarge seaside parapet to D10 to D11 (Part 1)	12	29-Apr-21	13-May-21																		Construction of enlarge seaside parapet to D10 to D11		
1074-1300-C3a	Construction of enlarge seaside parapet to D10 to D11 (Part 2)	4	14-May-21	18-May-21																		Construction of enlarge seaside parapet to D10 to D11		
1074-1300-D1	Construction of enlarge seaside parapet to D4 to D5 (Part 1)	12	20-Mar-21	03-Apr-21																		Construction of enlarge seaside parapet to D4 to D5		
1074-1300-D1a	Construction of enlarge seaside parapet to D4 to D5 (Part 2)	4	06-Apr-21	09-Apr-21																		Construction of enlarge seaside parapet to D4 to D5		
1074-1300-D2	Construction of enlarge seaside parapet to D5 to D6 (Part 1)	12	10-Apr-21	23-Apr-21																		Construction of enlarge seaside parapet to D5 to D6		
1074-1300-D2a	Construction of enlarge seaside parapet to D5 to D6 (Part 2)	4	24-Apr-21	28-Apr-21																		Construction of enlarge seaside parapet to D5 to D6		
1074-1300-D3	Construction of enlarge seaside parapet to D6 to D7 (Part 1)	12	29-Apr-21	13-May-21																		Construction of enlarge seaside parapet to D6 to D7		
1074-1300-D3a	Construction of enlarge seaside parapet to D6 to D7 (Part 2)	4	14-May-21	18-May-21																		Construction of enlarge seaside parapet to D6 to D7		
1074-1400-1	Installation of L3 Post at Slow Lane	14	19-May-21	03-Jun-21																				
1074-1400-2	Survey for L3 Post and Preparation of Shop Drawing for L3 Railing at Slow Lane	5	04-Jun-21	09-Jun-21																				
1074-1400-3	Fabrication of L3 Railing for Slow Lane Part 1	13	10-Jun-21	25-Jun-21																				
1074-1400-4	Fabrication of L3 Railing for Slow Lane Part 2	13	26-Jun-21	12-Jul-21																				
1074-1400-5	Installation of L3 Railing at Slow Lane E3 to D8	9	13-Jul-21	22-Jul-21																				
1074-1400-6	Installation of L3 Railing at Slow Lane D8 to F8	5	23-Jul-21	28-Jul-21																				
1074-1500	Fabrication of directional signage (FADS08A) Part 1	12	20-Mar-21*	03-Apr-21																		Fabrication of directional signage (FADS08A) Part 1		
1074-1500-1	Fabrication of directional signage (FADS08A) Part 2	12	06-Apr-21	19-Apr-21																		Fabrication of directional signage (FADS08A) Part 2		
1074-1500-2	Installation of directional signage (FADS08A) Part 1	12	20-Apr-21	04-May-21																		Installation of directional signage (FADS08A) Part 1		
1074-1500-3	Installation of directional signage (FADS08A) Part 2	12	05-May-21	18-May-21																		Installation of directional signage (FADS08A) Part 2		
1074-1500A	Installation of directional signage (ADS08B) Part 1	12	14-May-21	27-May-21																		Installation of directional signage (ADS08B) Part 1		
1074-1500A-1	Installation of directional signage (ADS08B) Part 2	12	28-May-21	10-Jun-21																		Installation of directional signage (ADS08B) Part 2		
IEC Westbound																								
1074-1700-1	Installation of Water Logging Bracket Part 2	5	12-Jan-21 A	25-Jan-21																		Installation of Water Logging Bracket Part 2		
1074-1700-2	Installation of Water Logging Bracket Part 3	12	26-Jan-21	08-Feb-21																		Installation of Water Logging Bracket Part 3		
1074-1700-3	Installation of Water Logging Bracket Part 4	12	09-Feb-21	25-Feb-21																		Installation of Water Logging Bracket Part 4		
1074-1700-4	Installation of Water Logging Bracket Part 5	12	26-Feb-21	11-Mar-21																		Installation of Water Logging Bracket Part 5		
1074-1700-5	Installation of Water Logging Bracket Part 6	12	12-Mar-21	25-Mar-21																		Installation of Water Logging Bracket Part 6		
1074-1700-6	Installation of Water Logging Bracket Part 7	12	26-Mar-21	10-Apr-21																		Installation of Water Logging Bracket Part 7		
1074-1800-3	Scaffolding for Noise Enclosure Modification Part 3	12	20-Jan-21 A	02-Feb-21																		Scaffolding for Noise Enclosure Modification Part 3		
1074-1800-4	Scaffolding for Noise Enclosure Modification Part 4	12	03-Feb-21	19-Feb-21																		Scaffolding for Noise Enclosure Modification Part 4		
1074-1800-5	Scaffolding for Noise Enclosure Modification Part 5	12	20-Feb-21	05-Mar-21																		Scaffolding for Noise Enclosure Modification Part 5		
1074-1800-6	Scaffolding for Noise Enclosure Modification Part 6	12	06-Mar-21	19-Mar-21																		Scaffolding for Noise Enclosure Modification Part 6		
1074-1800-7	Scaffolding for Noise Enclosure Modification Part 7	10	20-Mar-21	31-Mar-21																		Scaffolding for Noise Enclosure Modification Part 7		
1074-1900-2	Torque Test for Interim Post of Noise Enclosure Outer Side Part 2	12	17-Apr-21	30-Apr-21																		Torque Test for Interim Post of Noise Enclosure Outer Side Part 2		
1074-2000-1	Modification of gutter and downpipe for noise enclosure Stage 1	12	03-Feb-21	19-Feb-21																		Modification of gutter and downpipe for noise enclosure Stage 1		
1074-2000-2	Modification of gutter and downpipe for noise enclosure Stage 2	12	20-Feb-21	05-Mar-21																		Modification of gutter and downpipe for noise enclosure Stage 2		
1074-2000-3	Modification of gutter and downpipe for noise enclosure Stage 3	12	06-Mar-21	19-Mar-21																		Modification of gutter and downpipe for noise enclosure Stage 3		

	Remaining Level of Effort		Remaining Work		Milestone
	Actual Level of Effort		Critical Remaining Work		Baseline Milestone
	Actual Work				


Contract HY/2009/19
Three Months Rolling Programme (20.Jan.2021 to 20.Apr.2021)

Data Date: 20-Jul-20

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
Update 2020-06-20 CWB(CC) - Commissioning Contract (DWP 4g)					
PRELIMINARIES AND GENERAL REQUIREMENTS					
Salient Key Dates and Milestones					
Anticipated Completion Dates					
KD09	KD9 - Completion of Section 4 of the Works (1445 days) - include EOT No.12 (149 days)	0		20-Jul-20*	-1037
KD11	KD11 - Completion of Section 6 of the Works (1445 days) - include EOT No.12 (149 days)	0		20-Jul-20*	-889
KD07	KD7 - Completion of Section 2 of the Works (1771 days) - include EOT No.12 (414 days)	0		18-Aug-20*	-702
Possession Dates and Vacation Dates					
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-Jul-20	07-Nov-20	-889
Submissions and Approvals					
Initial General Submission					
10168	Submission of CMC 3DVR	30	20-Jul-20	18-Aug-20	-702
CONSTRUCTION					
Commissioning Test					
10126	Establishment Works	365	20-Jul-20	19-Jul-21	-1037
9930	Contract Completion	0		18-Aug-20	-702
Training / Plan / Manual / As-Built Drawings for Project Completion / Establishment					
10226	Routine Maintenance Records / Maintenance Monthly Report	0	20-Jul-20		-672

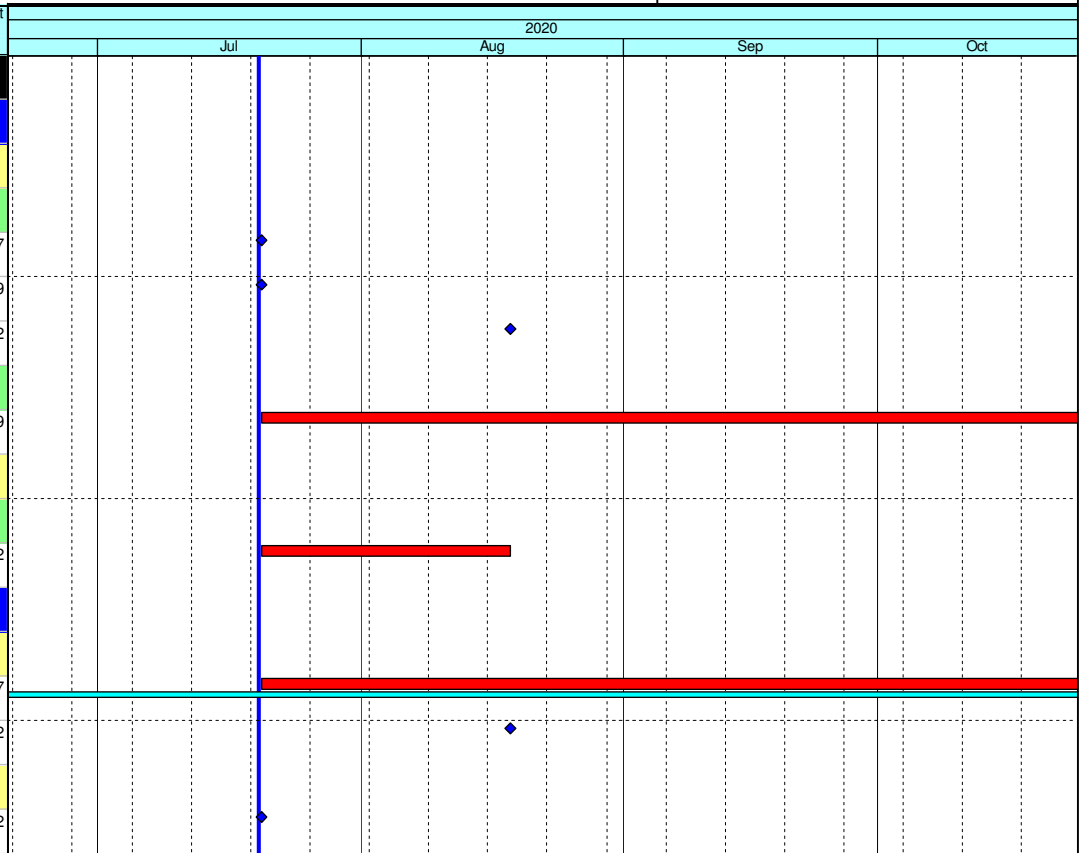

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 83 (January 2021) THREE MONTH ROLLING

Project ID: H2613-U077
 Baseline: DWP4g
 Layout: Update Three Month Rolling
 U077
 Page 1 of 1

Date	Revision	Checked	Approv...
20-Jun-20...	U076	AT	CW
20-Jul-20...	U077	AT	CW
