

Programme for Outstanding and Defective Works

CSF: PR/S-0336 REV D
APPENDIX A

ID	Task Name	Duration	Start	Finish	Finish (Programme dd 25 June 2019)	Qtr 3, 2019							Qtr 4, 2019																					
						July	August	September	October	November	December	January	February	March	April																			
						28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52	1			
1	1. Site Formation Drainage Works, K1 Kerb with Subbase Pavement and Chain Link Fences/Access Gates in WCR1 to WCR4	315 days	20 February 2019	31 December 2019	31 December 2019	→																												
15	2. Rectification of Caisson Seawalls and Installation of Corrosion Monitoring System (CMS) of Caisson Seawalls in WCR1 and WCR3	136 days	20 February 2019	05 July 2019	05 July 2019	05/07																												
32	3. Rectification of 0.5T Rock Armour and Seabed Level (High Spot to be Trimmed) in WCR3	85 days	08 June 2019	31 August 2019	31 August 2019	→ 31/08																												
43	4. Rectification of Grade 400 Rockfill and 0.5T Rock Armour in WCR1	68 days	14 June 2019	20 August 2019	04 August 2019	→ 20/08																												
52	5. Construction of EVA for Ferry Pier in WCR1 (Completed)	0 days	22 January 2019	22 January 2019	22 January 2019																													
53	6. Construction of Road Improvement Works and Reconstruction of Hung Hing Road under VO254 (Footpath Pavement, Roadside Barrier, Irrigation System, Road Lighting System), and Reinstatement of Associated Existing Footpath on Hung Hing Road	302 days	02 October 2018	30 July 2019	30 July 2019	→ 30/07																												
78	7. Blockwork Seawalls (Construction of Remaining Seawall Coping) in WCR4 (Completed)	0 days	09 January 2019	09 January 2019	09 January 2019																													
80	8. Completion of Remaining Grade 400 for Seawalls in WCR4 (Completed)	77 days	26 February 2019	13 May 2019	13 May 2019																													
94	9. Completion of Remaining Backfilling Works in WCR4 (Completed)	0 days	19 February 2019	19 February 2019	19 February 2019																													
95	10. Reinstatement of Existing Seabed Level in TWCR4 (Completed)	145 days	03 April 2019	25 August 2019	25 August 2019	→ 25/08																												
113	11. Construction of Landing Steps (Type 10 and Type 11 Seawalls) in Ex-Helipad	170 days	03 March 2019	19 August 2019	19 August 2019	→ 19/08																												
205	12. Reinstatement of Existing Seawall at Box Culvert O Temporary Diversion in Ex-PWCA Basin (Completed)	0 days	14 January 2019	14 January 2019	14 January 2019																													
207	13. Reinstatement of Existing Pavement and Drainage System in Ex-Helipad	79 days	02 June 2019	19 August 2019	19 August 2019	→ 19/08																												
248	14. Rectification of Granite Facing Stone on Existing Seawall in WCR4 and Ex-PWCA Basin (70nos.)	28 days	17 July 2019	13 August 2019	13 August 2019	→ 13/08																												
252	15. Reinstatement of Hung Hing Road and Wan Shing Street in Accordance to Hung Hing Road Traffic Diversion Reinstatement Stage 0.5 Scheme Under VO No. 257 on Hung Hing Road	248 days	01 March 2019	03 November 2019	26 October 2019	→ 03/11																												
576	16. Reinstatement of LCSD Sitting Out Area underneath Hung Hing Road Flyover on Hung Hing Road	17 days	08 May 2019	24 May 2019	24 May 2019																													
582	17. Completion of Notice Submission of CWXP No. C000266 on Hung Hing Road, Wan Shing Street and Expo Drive East (Notional)	0 days	20 September 2019	20 September 2019	20 September 2019	→ 20/09																												
584	18. Completion of Notice Submission of XP No. 1202793 on Expo Drive East	0 days	20 April 2019	20 April 2019	20 April 2019																													
585	19. Modification Work inside Room of Hung Hing Road Flyover (Completed)	9 days	21 March 2019	29 March 2019	29 March 2019																													
590	20. Ladder Installation Inside Room of Hung Hing Road (Completed)	9 days	21 March 2019	29 March 2019	29 March 2019																													
595	21. Defective Works of the Reinstatement of Hung Hing Road Flyover, such as Painting of Wall of Flyover, Touch-up Rust of Steel Door and Steel Vehicular Parapet and etc. (Completed)	34 days	24 March 2019	26 April 2019	26 April 2019																													
601	22. Establishment Period for 8nos. (6nos.) of Trees Being Transplanted Back Underneath Hung Hing Road Flyover	366 days	11 June 2019	10 June 2020	10 June 2020	→																												
604	23. Construction of Watermain Across Hung Hing Road	128 days	30 August 2019	04 January 2020	27 December 2019	→																												
643	24. Repaving Work at Hung Hing Road and Wan Shing Street	199 days	21 June 2019	05 January 2020	29 December 2019	→																												
672	25. Rectification Works of Temporary Covered Walkway	90 days	27 May 2019	24 August 2019	12 August 2019	→ 24/08																												
726	26. Tree Transplanting	541 days	14 May 2019	04 November 2020	04 November 2020	→																												
771	27. Reprovision of Public Lighting and Directional Sign at Hung Hing Road and Wan Shing Street	213 days	14 May 2019	12 December 2019	12 December 2019	→ 12/12																												

Task Baseline Milestone Project Summary Deadline Finish-only
Critical Split Baseline Milestone Summary Group By Summary Start-only

Activity ID	Activity Name	Original Duration	Start	Finish	2020																		
					Jan	Feb	Mar	Apr															
Total		385.0	31-Mar-19 A	03-May-20																			
DWP-08 - (2) - Update Progress As of 20 Jan 20		385.0	31-Mar-19 A	03-May-20																			
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks		385.0	31-Mar-19 A	03-May-20																			
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)		365.0	31-Mar-19 A	29-Feb-20																			
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365.0	31-Mar-19 A	29-Feb-20																			
KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH>500mm)		365.0	20-Apr-19 A	03-May-20																			
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365.0	20-Apr-19 A	03-May-20																			
KD18 - Section 11: Transplanted Trees DBH>500mm in Portion VA and XII		365.0	20-Apr-19 A	03-May-20																			
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365.0	20-Apr-19 A	03-May-20																			

- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone


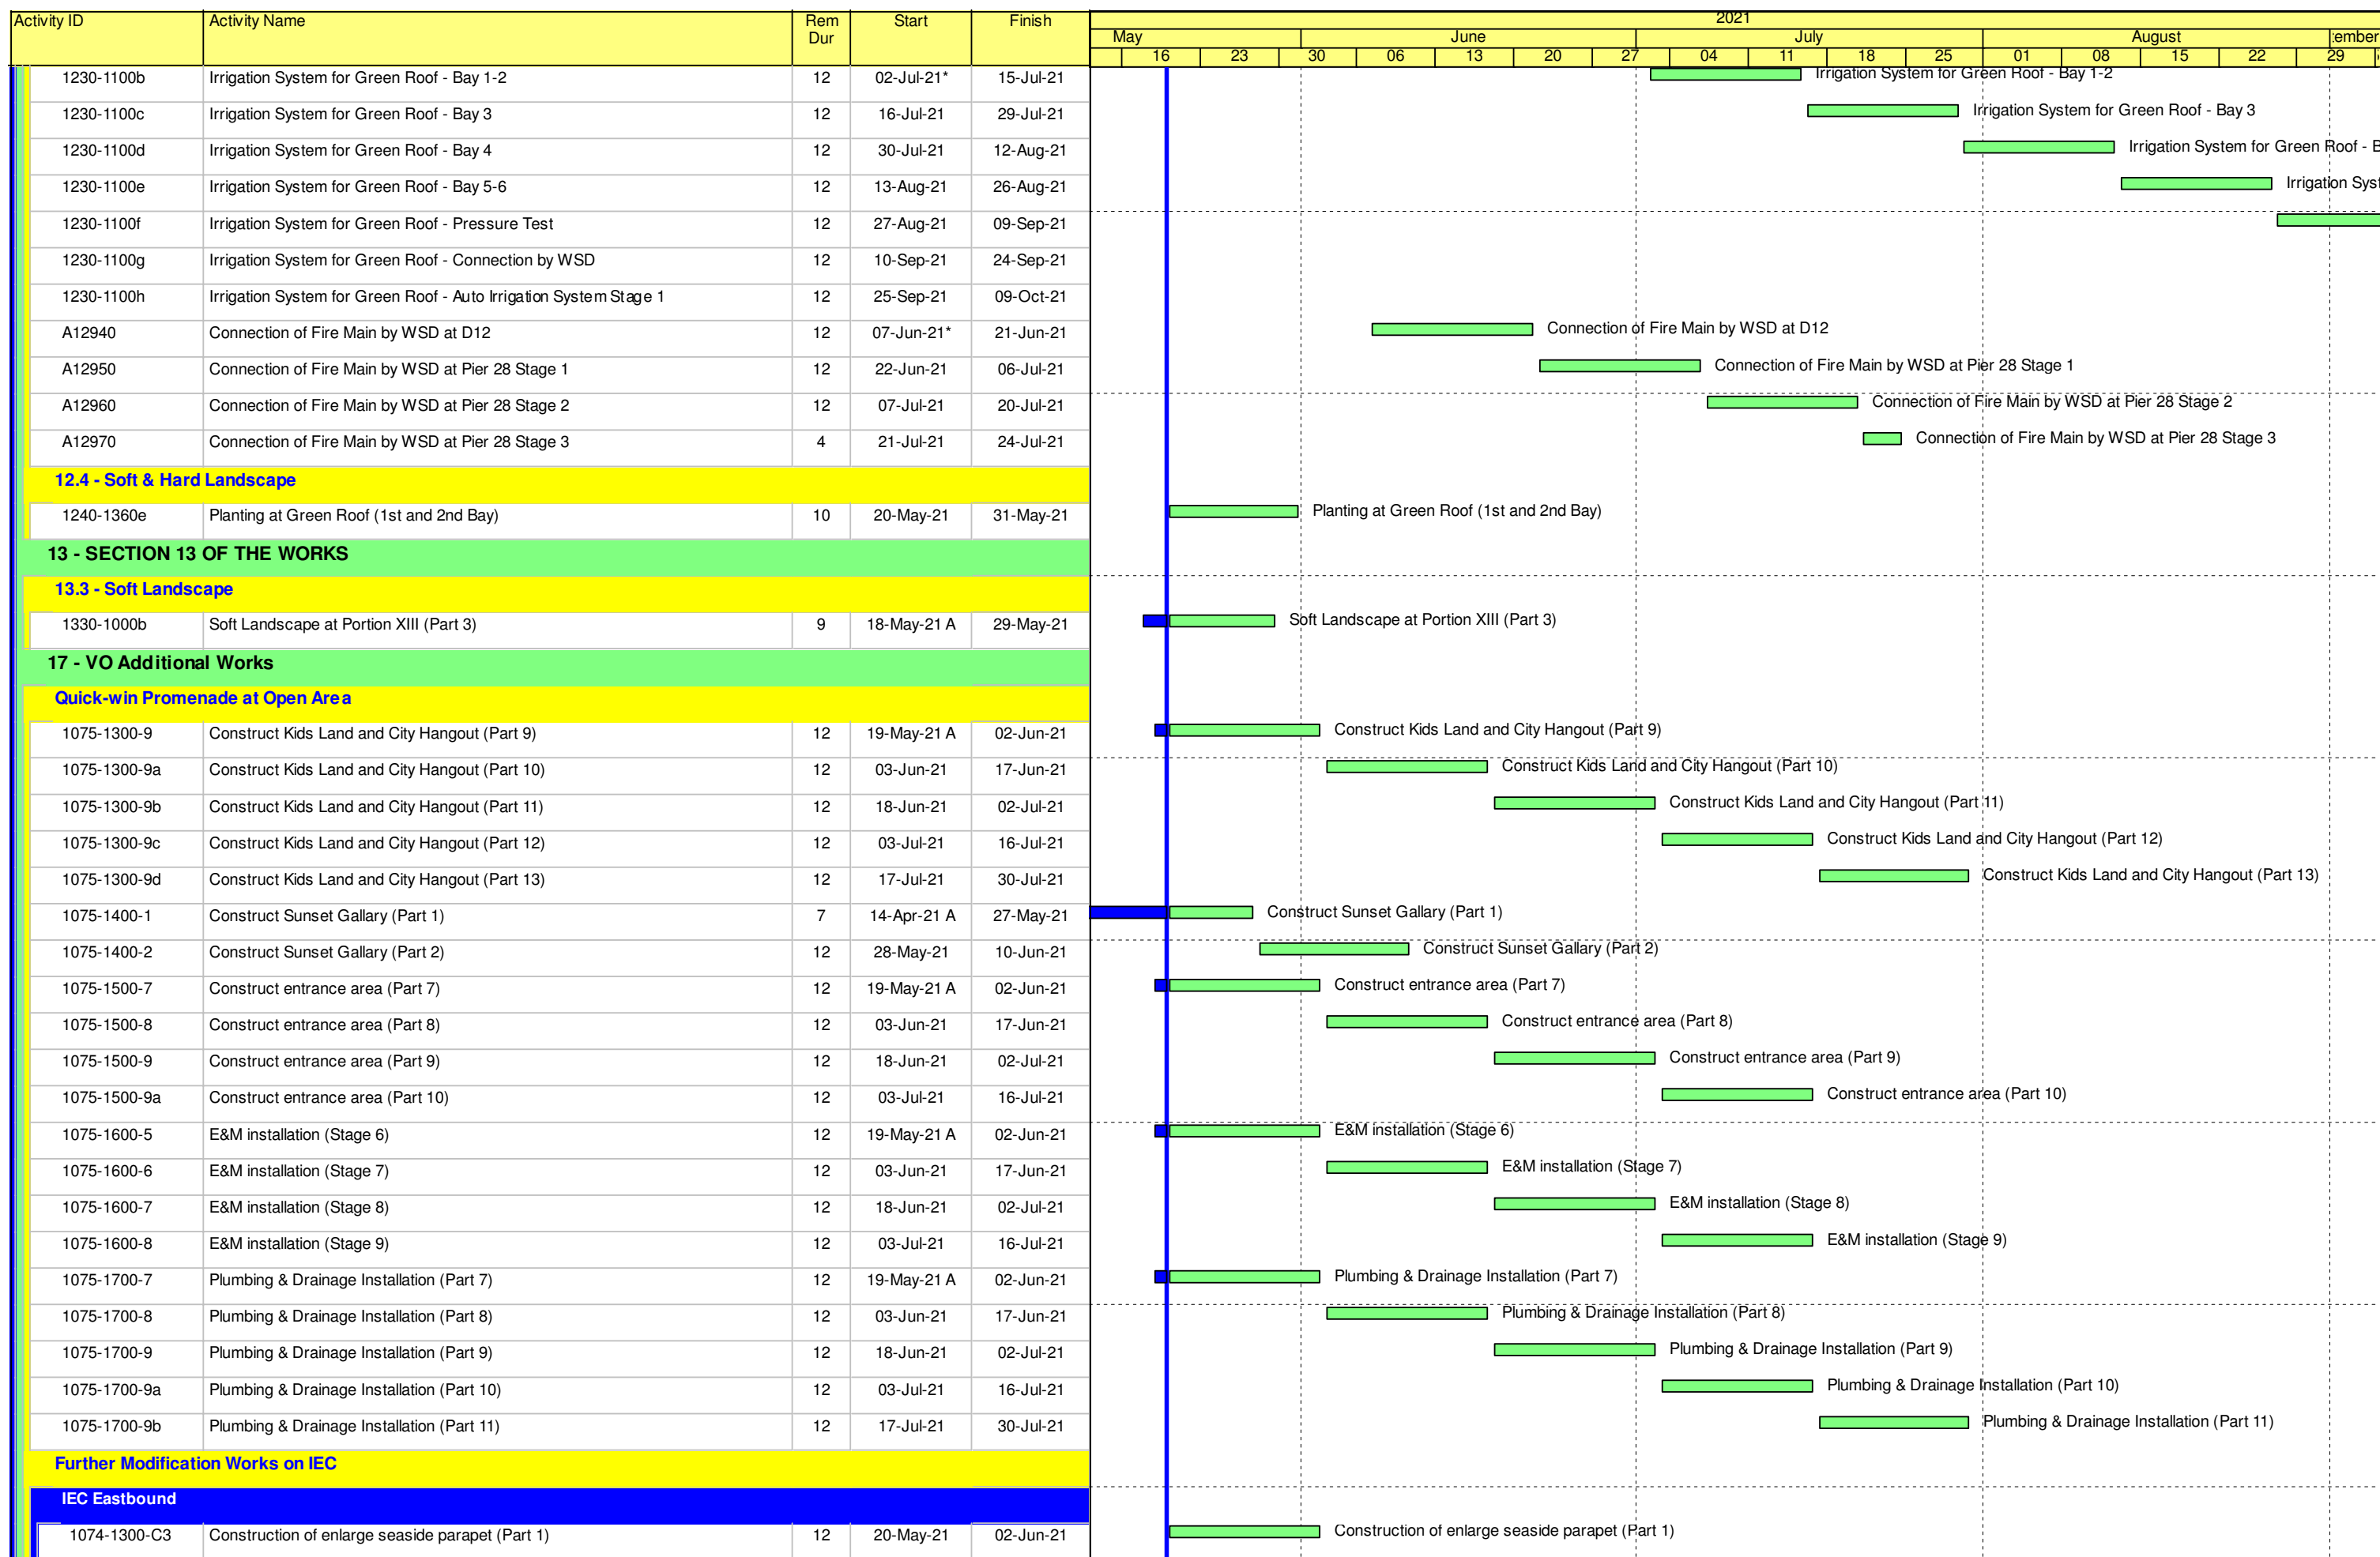
Page 1 of 1
 Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel (Slip Road 8 Section) - 3 Months Rolling Programme

Date	Revision	Checked	Approved
20-Jan-20	DWP-08 (2) - 3 Months Rolling	TL	TL






Activity ID	Activity Name	Rem Dur	Start	Finish	2021																
					May			June				July				August				September	
					16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	
3MRP 2021.5.20																					
10 - SECTION X OF THE WORKS																					
10.3 - Middle Bridge (Bridge F)																					
10.3.2 - Bridge Construction																					
Remaining Works																					
1032-4800d	Corbel Const for Permanent light at F4-F5 (location 4)	9	17-May-21 A	29-May-21	Corbel Const for Permanent light at F4-F5 (location 4)																
1032-4800e	Corbel Const for Permanent light at F4-F5 (location 5)	12	31-May-21	12-Jun-21	Corbel Const for Permanent light at F4-F5 (location 5)																
10.7 - Section X - Miscellaneous Works																					
10.7.3 - Open Area																					
Hard Paving Works Along Sea Wall and Near Harbour Heighs																					
1073-1290Z5	Hard paving & Channel - between Pier 20 to Pier 23 Stage 15	12	17-May-21 A	02-Jun-21	Hard paving & Channel - between Pier 20 to Pier 23 Stage 15																
1073-1290Z6	Hard paving & Channel - between Pier 20 to Pier 23 Stage 16	12	03-Jun-21	17-Jun-21	Hard paving & Channel - between Pier 20 to Pier 23 Stage 16																
Misc Works																					
1073-1410y	Modification of seawall top surface - Stage 26	3	10-May-21 A	22-May-21	Modification of seawall top surface - Stage 26																
1073-1410z	Modification of seawall top surface - Stage 27	10	24-May-21	03-Jun-21	Modification of seawall top surface - Stage 27																
11 - SECTION 11 OF THE WORKS																					
11.4- Hing Fat Street																					
Other Areas																					
1140-2290	Remaining works on footpath	9	16-Apr-21 A	29-May-21	Remaining works on footpath																
1140-2300	Resurfacing of HFS (Works on Sunday only, 10 Sundays)	43	04-Apr-21 A	10-Jul-21	Resurfacing of HFS (Works on Sunday only, 10 Sundays)																
12 - SECTION 7, 8, 9, 10 & 12 OF THE WORKS																					
12.2 - THE WORKS along IECL																					
12.2.1 - Noise Enclosure and Inner Parapet along IECL Westbound																					
A12980	Resurfacing works (Part 1)	12	02-Aug-21	14-Aug-21	Resurfacing works (Part 1)																
A12990	Resurfacing works (Part 2)	12	16-Aug-21	28-Aug-21	Resurfacing works (Part 2)																
A13000	Resurfacing works (Part 3)	12	30-Aug-21	11-Sep-21	Resurfacing works (Part 3)																
A13010	Resurfacing works (Part 4)	12	13-Sep-21	27-Sep-21	Resurfacing works (Part 4)																
A13020	Resurfacing works (Part 5)	12	28-Sep-21	12-Oct-21	Resurfacing works (Part 5)																
A13090	Resurfacing works (Part 6)	12	13-Oct-21	27-Oct-21	Resurfacing works (Part 6)																
12.2.2 - Inner Parapet along IECL Eastbound																					
A13030	Resurfacing (Part 1)	12	02-Aug-21	14-Aug-21	Resurfacing (Part 1)																
A13040	Resurfacing (Part 2)	12	16-Aug-21	28-Aug-21	Resurfacing (Part 2)																
A13050	Resurfacing (Part 3)	12	30-Aug-21	11-Sep-21	Resurfacing (Part 3)																
A13060	Resurfacing (Part 4)	12	13-Sep-21	27-Sep-21	Resurfacing (Part 4)																
A13070	Resurfacing (Part 5)	12	28-Sep-21	12-Oct-21	Resurfacing (Part 5)																
A13080	Resurfacing (Part 6)	12	13-Oct-21	27-Oct-21	Resurfacing (Part 6)																
12.3 - Waterworks																					
1230-1050c	Irrigation System for Landscape Deck - Connection by WSD	12	07-Jun-21*	21-Jun-21	Irrigation System for Landscape Deck - Connection by WSD																
1230-1050k	Irrigation System for Landscape Deck - Auto Irrigation System Stage 7	12	14-Apr-21 A	02-Jun-21	Irrigation System for Landscape Deck - Auto Irrigation System Stage 7																
1230-1050l	Irrigation System for Landscape Deck - Auto Irrigation System Stage 8	12	03-Jun-21	17-Jun-21	Irrigation System for Landscape Deck - Auto Irrigation System Stage 8																
1230-1050m	Irrigation System for Landscape Deck - Auto Irrigation System Stage 9	12	18-Jun-21	02-Jul-21	Irrigation System for Landscape Deck - Auto Irrigation System Stage 9																

█ Remaining Level of Effort █ Remaining Work ◆ Milestone
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Baseline Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Apr.2021 to 20.Jul.2021)



Activity ID	Activity Name	Rem Dur	Start	Finish	2021																		
					May			June					July					August				September	
					16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29			
1074-1300-C3a	Construction of enlarge seaside parapet (Part 2)	12	03-Jun-21	17-Jun-21																			
1074-1400-1	Installation of L3 Post at Slow Lane	12	18-Jun-21	02-Jul-21																			
1074-1400-2	Survey for L3 Post and Preparation of Shop Drawing for L3 Railing at Slow Lane	5	03-Jul-21	08-Jul-21																			
1074-1400-3	Fabrication of L3 Railing for Slow Lane	9	09-Jul-21	19-Jul-21																			
1074-1400-5	Installation of L3 Railing at Slow Lane E3 to F8	11	20-Jul-21	31-Jul-21																			
1074-1500	Fabrication of directional signage (FADS08A) Part 1 (pending approval)	10	12-Jun-21	24-Jun-21																			
1074-1500-1	Fabrication of directional signage (FADS08A) Part 2	10	25-Jun-21	07-Jul-21																			
1074-1500-2	Installation of directional signage (FADS08A) Part 1	10	08-Jul-21	19-Jul-21																			
1074-1500-3	Installation of directional signage (FADS08A) Part 2	10	20-Jul-21	30-Jul-21																			
1074-1500A	Installation of directional signage (ADS08B) Part 1 (pending approval)	12	18-Jun-21	02-Jul-21																			
1074-1500A-1	Installation of directional signage (ADS08B) Part 2	12	03-Jul-21	16-Jul-21																			
1074-1500A-2	Installation of directional signage (ADS08B) Part 3	12	17-Jul-21	30-Jul-21																			
IEC Westbound																							
1074-1700-7a	Gully and cover plate after water logging (part 1)	12	20-May-21	02-Jun-21																			
1074-1700-7b	Gully and cover plate after water logging (part 2)	12	03-Jun-21	17-Jun-21																			
1074-1700-7c	Gully and cover plate after water logging (part 3)	12	18-Jun-21	02-Jul-21																			
1074-1700-7d	Gully and cover plate after water logging (part 4)	12	03-Jul-21	16-Jul-21																			
1074-1700-7e	Gully and cover plate after water logging (part 5)	12	17-Jul-21	30-Jul-21																			
1074-2000-4	Modification of gutter and downpipe for noise enclosure Stage 4	5	12-Apr-21 A	25-May-21																			
1074-2000-5	Modification of gutter and downpipe for noise enclosure Stage 5	12	26-May-21	08-Jun-21																			
1074-2000-6	Modification of gutter and downpipe for noise enclosure Stage 6	10	09-Jun-21	21-Jun-21																			
1074-2100-6	Modification existing drainage from Pier 29 to 40 Part 3-4	12	18-May-21 A	02-Jun-21																			
1074-2100-7	Modification existing drainage from Pier 29 to 40 Part 3-5	12	03-Jun-21	17-Jun-21																			
1074-2100-8	Modification existing drainage from Pier 29 to 40 Part 3-6	11	18-Jun-21	30-Jun-21																			
1074-2200	Abandon existing gullies (remaining 23 nos)	11	18-Jun-21	30-Jun-21																			
1074-2300-2	Fabrication of L3 Railing for Slow Lane Part 1	13	20-May-21	03-Jun-21																			
1074-2300-3	Fabrication of L3 Railing for Slow Lane Part 2	13	04-Jun-21	19-Jun-21																			
1074-2300-4	Installation of L3 Railing at Slow Lane	14	21-Jun-21	07-Jul-21																			
1074-2500	Design of fall arrest and maintenance walkway	22	02-Jan-21 A	15-Jun-21																			
1074-2500-1	Fabrication of fall arrest and maintenance walkway	17	16-Jun-21	06-Jul-21																			
1074-2500-3	Installation of fall arrest and maintenance walkway Part 1	12	07-Jul-21	20-Jul-21																			
1074-2500-4	Installation of fall arrest and maintenance walkway Part 2	10	21-Jul-21	31-Jul-21																			
1074-2600-2	Design Approval of directional signage (FADS07, ADS07)	15	12-Feb-21 A	05-Jun-21																			
1074-2600-3	Fabrication of directional signage (FADS07, ADS07) Part 1	12	07-Jun-21	21-Jun-21																			
1074-2600-4	Fabrication of directional signage (FADS07, ADS07) Part 2	12	22-Jun-21	06-Jul-21																			
1074-2600-5	Installation of directional signage (FADS07, ADS07) Part 1	12	07-Jul-21	20-Jul-21																			
1074-2600-6	Installation of directional signage (FADS07, ADS07) Part 2	10	21-Jul-21	31-Jul-21																			
1074-2700-1	Design of MJ of Noise Enclosure for Pier 40 Part 2	10	20-May-21	31-May-21																			
1074-2800a-1	Fabrication of MJ of Noise Enclosure for Pier 35 and 40 Part 1	17	22-May-21	10-Jun-21																			
1074-2800a-2	Fabrication of MJ of Noise Enclosure for Pier 35 and 40 Part 2	12	11-Jun-21	25-Jun-21																			
1074-2800a-3	Installation of MJ of Noise Enclosure for Pier 35 and 40 Part 1	12	26-Jun-21	10-Jul-21																			

 Remaining Level of Effort	 Remaining Work	 Milestone
 Actual Level of Effort	 Critical Remaining Work	 Baseline Milestone
 Actual Work		

Contract HY/2009/19
Three Months Rolling Programme (20.Apr.2021 to 20.Jul.2021)

Activity ID	Activity Name	Rem Dur	Start	Finish	2021																				
					May			June				July				August				September					
					16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29					
1074-2800a-4	Installation of MJ of Noise Enclosure for Pier 35 and 40 Part 2	12	12-Jul-21	24-Jul-21																		Installation of MJ of Noise Enclosure for Pier 35 and 40 Part 2			
1074-2800a-5	Installation of MJ of Noise Enclosure for Pier 35 and 40 Part 3	6	26-Jul-21	31-Jul-21																		Installation of MJ of Noise Enclosure for Pier 35 and 40			

 Remaining Level of Effort
 Remaining Work
 Milestone
 Milestone
 Actual Level of Effort
 Critical Remaining Work
 Actual Work
 Baseline Milestone
 Baseline Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Apr.2021 to 20.Jul.2021)
