

**CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2018			
					Apr	May	Jun	Jul
HK/ 2012/ 08 Revised Works Programme Rev.12.0(DD 20 November 2017)								
Dredging and Reclamation								
Marine Work Construction								
Zone D								
Seawall Construction - Zone D								
Seawall 10 & 11								
MAR20630	Zone D - Seawall 10 & 11: Install remaining seawall block	14	04-Apr-18*	17-Apr-18				
MAR20650	Zone D - Seawall 10 & 11: Backfill Type A	7	18-Apr-18	24-Apr-18				
MAR20670	Zone D - Seawall 10 & 11: Lay geotextile and filter	7	25-Apr-18	01-May-18				
Works for Section Completion								
Construction								
Section III A - Road A2, A4 & A5								
Roadwork & Utilities - Section 1 (L1806 - L1801)								
SIIA10310b	Sec III A - section 1 carriageway - TTA stage 5: remaining sewerage pipe for M/H F8A - M/H F8B	18	20-Mar-18	13-Apr-18				
SIIA10310e	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - construct upstand wall above Dwall	25	10-Apr-18	09-May-18				
SIIA10310f	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - roadside barrier	14	10-May-18	26-May-18				
SIIA10310g	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - road formation	7	28-May-18	04-Jun-18				
SIIA10310h	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - laying asphalt with transition slab	14	05-Jun-18	21-Jun-18				
SIIA10312a	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L1805 - L1801)	15	23-Mar-18	13-Apr-18				
SIIA10312b	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L1805-1807)	12	14-Apr-18	27-Apr-18				
SIIA10313	Sec III A - roadwork and utilities section 1 carriageway - gully pipe (L1807 - L1801)	14	23-Apr-18	09-May-18				
SIIA10320	Sec III A - roadwork and utilities section 1 carriageway - fresh watermain	7	10-May-18	17-May-18				
SIIA10340	Sec III A - roadwork and utilities section 1 carriageway - utilities: HEC (80m) along carriageway	14	18-May-18	04-Jun-18				
SIIA10360	Sec III A - roadwork and utilities section 1 carriageway - road kerb & formation	14	05-Jun-18	21-Jun-18				
Roadwork & Utilities - Section 6 (L1102 - L1411)								
SIIA13470	Sec III A - roadwork and utilities section 6 carriageway - black top	7	28-Mar-18	09-Apr-18				
Section V - Remaining At-Grade Road & Road P2								
Roadwork & Utilities								
Section 2 (L1510 - L1504)								
SV12700	Sec V - Roadwork & Utilities Section 2 footpath - utilities: TCSS	16	20-Mar-18	11-Apr-18				
SV12740	Sec V - Roadwork & Utilities Section 2 footpath - paving block	18	12-Apr-18	03-May-18				
Section 3 (Culvert L - L1510)								
SIV12880	Sec V - Roadwork & Utilities Section 3 footpath - Paving block	21	27-Mar-18	24-Apr-18				
Section IV - Slip Road 3								
Roadwork & Utilities								

Data Date: 20-Feb-18	<ul style="list-style-type: none"> ◆ Current Milestone ■ Actual Work ■ Critical Remaining Work ■ Remaining Work ▬ Remaining Level of Effort
-------------------------	---

**3 Months Rolling Programme for Non-CRIII Area (April 2018 - June 2018)
(Ref. to Works Programme Rev.12)**


Date	Revision	Checked	Approved
13-Mar-18	12		

**CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2018			
					Apr	May	Jun	Jul
Section 1 (L16608 - L1601)								
SIV11749	Sec IV - sign gantry DS20 & DS21 footing (type 2): removal of ELS and backfilling	10	21-Mar-18	04-Apr-18	█			
SIV11751	Sec IV - sign gantry DS21 footing (type 3): excavation	5	26-Mar-18	03-Apr-18	█			
SIV11752	Sec IV - sign gantry DS21 footing (type 3): footing structure	13	04-Apr-18	19-Apr-18	█			
SIV11763	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Drainage Works (L2004 - L2005, L2101 - L2101A)	21	20-Apr-18	15-May-18	█			
SIV11765	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Gully pipe (L2004)	7	17-May-18	25-May-18		█		
SIV11780	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Watermain	18	26-May-18	15-Jun-18			█	
SIV11800	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Utilities : TCSS crossroad duct	14	16-Jun-18	04-Jul-18				█
SIV11860	Sec IV - Roadwork & Utilities at SR3 Section 1 footpath - Drainage Works: future connection pipes	7	26-May-18	02-Jun-18			█	
SIV11880	Sec IV - Roadwork & Utilities at SR3 Section 1 footpath - watermain	7	04-Jun-18	11-Jun-18			█	
SIV11900	Sec IV - Roadwork & Utilities at SR3 Section 1 footpath - utilities: HEC & TCSS	39	12-Jun-18	28-Jul-18				█
Section 2 (L2301 - L2103)								
SIV12080	Sec IV - Roadwork & Utilities at SR3 Section 2 footpath - paving block	21	18-Apr-18	12-May-18	█			
Section 3 (M/ H1.6 - L2301)								
SIV12120	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Drainage Works (M1.6-C1.1-C1.2): ELS,construct MH and	28	12-Apr-18	15-May-18	█			
SIV12121	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Drainage Works (M1.6-C1.1-C1.2): Backfilling & shift lane	6	16-May-18	23-May-18		█		
SIV12122	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Drainage Works (M1.6-C1.1-C1.2): Construct MH C1.2	5	24-May-18	29-May-18			█	
SIV12140	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Gully pipe (M/H 1.7 - L2301)	32	10-Apr-18	17-May-18	█			
SIV12150	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Road kerb	14	18-May-18	04-Jun-18		█		
SIV12155	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - formation	10	05-Jun-18	15-Jun-18			█	
SIV12160	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Black top	7	16-Jun-18	25-Jun-18				█
SIV12170	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - Utilities: TCSS	21	10-May-18	04-Jun-18		█		
SIV12180	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - U channel	10	05-Jun-18	15-Jun-18			█	
SIV12220	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - Paving block	25	16-Jun-18	17-Jul-18				█
Section VII - Remainder Works								
Road & Drainage Works (Culvert L - M/ H1.7, Adjacent to SR3)								
SVII11620	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway : traffic diversion at Lung King Street	3	21-Apr-18	24-Apr-18	█			
SVII11640	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - Gully pipe (Culvert L -MH1.7)	27	25-Apr-18	28-May-18	█			
SVII11650	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - TCSS duct	7	29-May-18	05-Jun-18			█	
SVII11654	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - road kerb & formation	14	06-Jun-18	22-Jun-18			█	
SVII11680	Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - U channel	14	29-May-18	13-Jun-18			█	
SVII11700	Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - utilities: TCSS	14	14-Jun-18	30-Jun-18				█
Retaining Wall RW5 Construction								
SVII10660	Sec VII - Retaining Wall RW5 (bay 1) - construct base slab and wall	22	02-May-18	28-May-18		█		
SVII10680	Sec VII - Retaining wall RW5 (bay 2) - construct base slab and wall	22	29-May-18	23-Jun-18			█	
SVII10800	Sec VII - Retaining wall RW5 (bay 3) - construct base slab and wall	22	02-May-18	28-May-18		█		
SVII10820	Sec VII - Retaining wall RW5 (bay 4) - construct base slab and wall	22	29-May-18	23-Jun-18			█	
Landing Steps Construction								
Landing Steps BSW13								
SVII10900	Sec VII - Landing steps (BSW13) - install vertical fender / step fender	15	31-May-18	16-Jun-18			█	

**CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West**


Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2018				
					Apr	May	Jun	Jul	
SVII10920	Sec VII - Landing steps (BSW13) - install s.s. handrail / tactile / sign board / bollard	25	19-Jun-18	18-Jul-18					
Promenade Seawall Parapet Construction & EVA									
SVII13122	Sec VII - Zone A1, A2 & B - seawall parapet: reinforced concrete coping	18	29-Mar-18	23-Apr-18					
SVII13140	Sec VII - Zone A1, A2 & B - seawall parapet: Construct seawall parapet	30	24-Apr-18	30-May-18					
SVII13160	Sec VII - Zone A1, A2 & B - EVA: watermain	14	31-May-18	15-Jun-18					
SVII13180	Sec VII - Zone A1, A2 & B - EVA: U-channel	14	16-Jun-18	04-Jul-18					
SVII13200	Sec VII - Zone D - seawall parapet: Remove temporary seawall block	21	21-Mar-18*	18-Apr-18					
SVII13220	Sec VII - Zone D - seawall parapet: Construct mass concrete	30	19-Apr-18	25-May-18					
SVII13222	Sec VII - Zone D - seawall parapet: reinforced concrete coping	18	26-May-18	15-Jun-18					
SVII13240	Sec VII - Zone D - seawall parapet: Construct seawall parapet	25	16-Jun-18	17-Jul-18					
Promenade Footpath									
Section 1									
SVII10440	Sec VII - section 1 footpath - drainage works : connection pipe & U -channel	10	10-May-18	21-May-18					
SVII10445	Sec VII - section 1 footpath - watermain	7	23-May-18	30-May-18					
SVII10460	Sec VII - section 1 footpath - lighting	7	31-May-18	07-Jun-18					
Section 2									
SVII12615	Sec VII - section 2 footpath - watermain	7	12-Apr-18	19-Apr-18					
SVII12630	Sec VII - section 2 footpath - utilities: TCSS	21	20-Apr-18	15-May-18					
SVII12670	Sec VII - section 2 footpath - paving block	30	16-May-18	21-Jun-18					
Section 3									
SVII12850	Sec VII - section 3 footpath - watermain	17	26-Mar-18*	18-Apr-18					
SVII12870	Sec VII - section 3 footpath - utilities (HEC, TCSS, HGC, PCCW)	40	19-Apr-18	06-Jun-18					
SVII12875	Sec VII - 3 footpath - drainage works :U chanel	14	07-Jun-18	23-Jun-18					
Section 4									
SVII13110	Sec VII - section 4 footpath - paving block	25	19-May-18	19-Jun-18					
Section 5									
SVII13275	Sec VII - section 5 footpath - watermain	14	07-Apr-18	23-Apr-18					
SVII13310	Sec VII - section 5 footpath - utilities: HEC, TCSS, HGC, PCCW	42	24-Apr-18	13-Jun-18					
SVII13330	Sec VII - section 5 footpath - paving block	22	14-Jun-18	11-Jul-18					
Section 6									
SVII13510	Sec VII - section 6 footpath - watermain	13	29-Mar-18	17-Apr-18					
SVII13514	Sec VII - section 6 footpath - U channel	20	18-Apr-18	11-May-18					
SVII13530	Sec VII - section 6 footpath - utilities: HEC, TCSS, HGC, PCCW	49	18-Apr-18	15-Jun-18					
SVII13550	Sec III A - section 6 footpath - paving block	25	16-Jun-18	17-Jul-18					
Section VIII - Landscape Softworks									
Soft Landscaping Works									
SVIII10040	Sec VIII - Trees Planting	141	03-Jun-18	21-Oct-18					
SVIII10060	Sec VIII - Shrubs Planting	141	03-Jun-18	21-Oct-18					

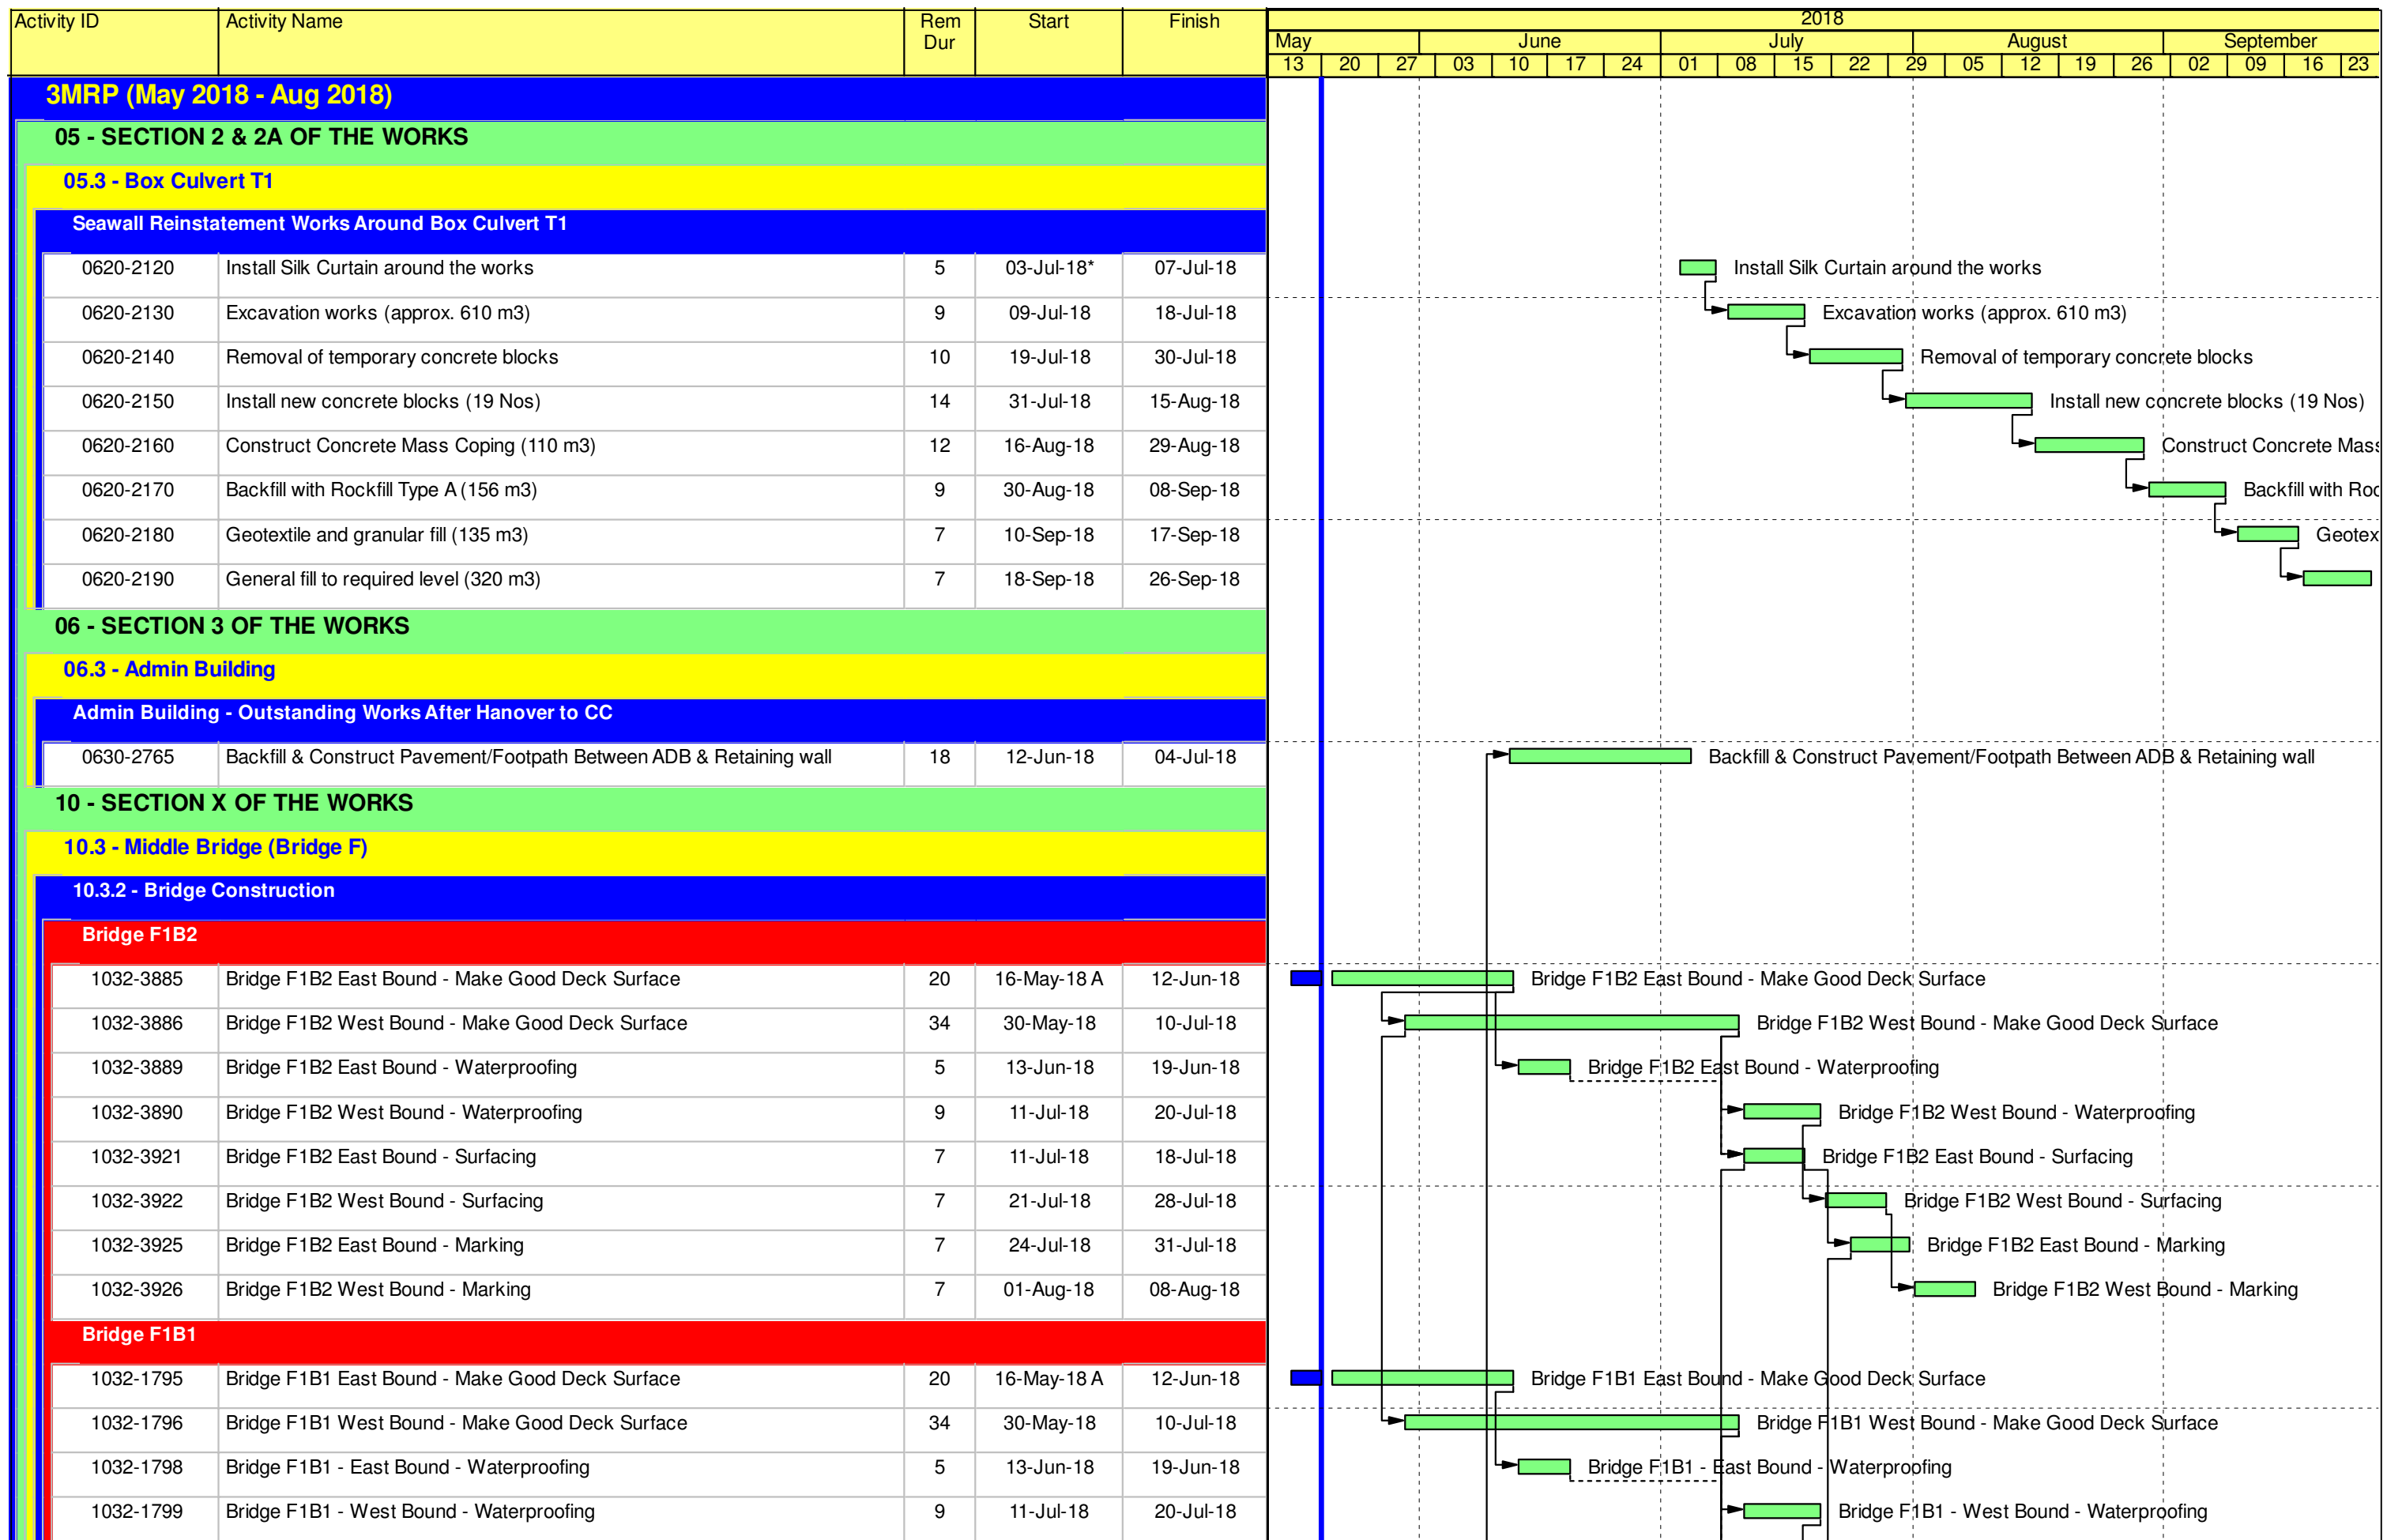

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.May.2018 to 31.Aug.2018)

Activity ID	Activity Name	Rem Dur	Start	Finish	2018																				
					May			June			July			August			September								
					13	20	27	03	10	17	24	01	08	15	22	29	05	12	19	26	02	09	16	23	
1032-1821	Bridge F1B1 - East Bound - Surfacing	7	11-Jul-18	18-Jul-18																					
1032-1822	Bridge F1B1 - West Bound - Surfacing	7	21-Jul-18	28-Jul-18																					
1032-1823	Bridge F1B1 - East Bound - Marking	7	24-Jul-18	31-Jul-18																					
1032-1824	Bridge F1B1 - West Bound - Marking	7	01-Aug-18	08-Aug-18																					
All Middle Bridge F (Common)																									
1032-4357.1	(Green Roof @ F1) - Bondec Installation	10	21-May-18	31-May-18																					
1032-4357.2	(Green Roof @ F1) - Screeding	12	01-Jun-18	14-Jun-18																					
1032-4357.3	(Green Roof @ F1) - Down Pipe & Drainage system	16	21-May-18	07-Jun-18																					
1032-4359	(Green Roof @ F2) - Vertical Steel Plate Installation	23	21-May-18	15-Jun-18																					
1032-4359.1	(Green Roof @ F2) - Bondec Installation	12	16-Jun-18	30-Jun-18																					
1032-4359.2	(Green Roof @ F2) - Screeding	12	03-Jul-18	16-Jul-18																					
1032-4359.3	(Green Roof @ F2) - Down Pipe & Drainage system	18	16-Jun-18	09-Jul-18																					
1032-4360	(Green Roof @ F3 - Excl above live traffic) - Vertical Steel Plate Installation	25	16-Jun-18	17-Jul-18																					
1032-4360.1	(Green Roof @ F3 - Excl above live traffic) - Bondec Installation	12	18-Jul-18	31-Jul-18																					
1032-4360.2	(Green Roof @ F3 - Excl above live traffic) - Screeding	12	01-Aug-18	14-Aug-18																					
1032-4360.3	(Green Roof @ F3 - Down Pipe & Drainage system	20	18-Jul-18	09-Aug-18																					
1032-4363	(Green Roof @ F3-above live traffic)(Sun/PH-after CC works) (15/7, 22/7, 29/7) - Vertical Plate Installation	15	15-Jul-18*	29-Jul-18																					
1032-4363.1	(Green Roof @ F3-above live traffic)(Sun/PH-after CC works) (5/8) - Bondec Installation	1	05-Aug-18	05-Aug-18																					
1032-4363.2	(Green Roof @ F3-above live traffic)(Sun/PH-after CC works) (12/8, 19/8) - Screeding	8	12-Aug-18	19-Aug-18																					
Other Misc/Add'l Works																									
1032-4370	EB - Removal of Temporary Post for Noise Enclosure (Sunday/PH - Parallel to CC works) (3/6, 10/6 & 17/6)	15	03-Jun-18*	17-Jun-18																					
1032-4371	EB - Construct F1 nosing	6	12-Jun-18	19-Jun-18																					
1032-4372	EB - Make Good Deck Surface to Receive Waterproofing after removal of post	6	19-Jun-18	25-Jun-18																					
1032-4373	EB - Waterproofing Works	3	26-Jun-18	28-Jun-18																					
1032-4374	EB - Lay Bitumen & Marking (Sunday/PH) (26/8, 2/9) 18/6,24/6,1/7,2/7,8/7 by CC, 15/7,22/7,29/7,5/8,12/8,14/8 for Green R	8	26-Aug-18*	02-Sep-18																					
1032-4378	WB - Removal of Temporary Post for Noise Enclosure (F1/F2/F3) (NW-after CC night works)	19	22-Jul-18*	09-Aug-18																					
1032-4379	WB - Make Good Deck Surface to Receive Waterproofing after removal of post	17	28-Jul-18	16-Aug-18																					
1032-4380	WB - Waterproofing Works	13	06-Aug-18	20-Aug-18																					
1032-4381	WB - Lay Bitumen & Marking (Sunday/PH) (9/9, 16/9) (28/8, 2/9 Conflict with EB)	8	09-Sep-18*	16-Sep-18																					
1032-4382	WB - Install Crash Cushion (2 months lead time) - will arrive on site by early Aug	2	13-Aug-18*	14-Aug-18																					




Contract HY/2009/19
Three Months Rolling Programme (20.May.2018 to 31.Aug.2018)

Activity ID	Activity Name	Rem Dur	Start	Finish	2018																			
					May			June				July				August				September				
					13	20	27	03	10	17	24	01	08	15	22	29	05	12	19	26	02	09	16	23
A1420	Vertical Water Proofing & Backfilling	6	25-May-18	31-May-18																				
Phase II - Landscape Deck Bay C1 (3)																								
Wall - Upper Portion																								
A1575	Remove Waling & Reinstall Boxing out for struts	4	24-May-18	28-May-18																				
A1580	Vertical Water Proofing & Backfilling	6	29-May-18	04-Jun-18																				
Phase II - Landscape Deck Bay C1 (4)																								
Wall - Upper Portion																								
A1745	Remove Waling & Reinstall Boxing out for struts	4	24-May-18	28-May-18																				
A1750	Vertical Water Proofing & Backfilling	6	31-May-18	06-Jun-18																				
Phase II - Landscape Deck Bay C1 (5)																								
Wall - Upper Portion																								
A1905	Remove Waling & Reinstall Boxing out for struts	4	26-May-18	30-May-18																				
A1910	Vertical Water Proofing & Backfilling	6	31-May-18	06-Jun-18																				
Landscape Deck																								
1062-1274	Bay C1 > Staircase No. 1	10	16-Jun-18	28-Jun-18																				
1062-1275	Bay C1 > Re-instatement of temporary opening at OHVD slab (waiting confirmation w/ CC for access date)	15	30-May-18*	15-Jun-18																				
Road Works																								
1062-1276	Re-instatement of De-watering Well	14	01-Jun-18*	16-Jun-18																				
1062-1277	Re-instatement of Temporary Sump Pit	7	19-Jun-18	26-Jun-18																				
1062-1278	Masking at D-wall side wall at Bay C1-5 (2 pours/face)(waiting confirmation w/ CC for access date)	18	30-May-18*	20-Jun-18																				
1062-1300	Road Drainage & Downpipe (within Portion IIB)	24	31-May-18	28-Jun-18																				
1062-1320	Remaining Profile Barrier (within Portion IIB)	15	02-May-18 A	06-Jun-18																				
1062-1340	Signage GT3	7	17-May-18 A	28-May-18																				
1062-1345	Signage VMS 2,3 & 4 (Post Drill Bolt)	14	29-May-18	13-Jun-18																				
1062-1380	Road Surfacing & Marking (within Portion IIB) (after CC installation works)	6	31-Jul-18*	06-Aug-18																				
1062-1385	Construct Noise Panel Trough A (within Portion IIB)	9	20-Jul-18	30-Jul-18																				
10.6.3 - Slip Road 13																								
1061-6992	Slip Road 13 (South 1) Drainage & Road Formation - adjacent to ADB	13	16-Apr-18 A	04-Jun-18																				
1062-1283	Slip Road 13 (South 2 - Adj to Car Park) Breaking Ex. Concrete & Drainage Works & other Under Ground Civil Provisions	21	24-May-18	16-Jun-18																				
1062-1284	Slip Road 13 (South 2 - Adj to Car Park) Backfilling & Compaction	12	19-Jun-18	03-Jul-18																				
1062-1287	Slip Road 13 (South 2 - Adj to Car Park) Road Curve & Other Misc Works	8	04-Jul-18	12-Jul-18																				

█ Remaining Level of Effort Remaining Work
 Actual Level of Effort Critical Remaining Work
 Actual Work ◆ ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.May.2018 to 31.Aug.2018)

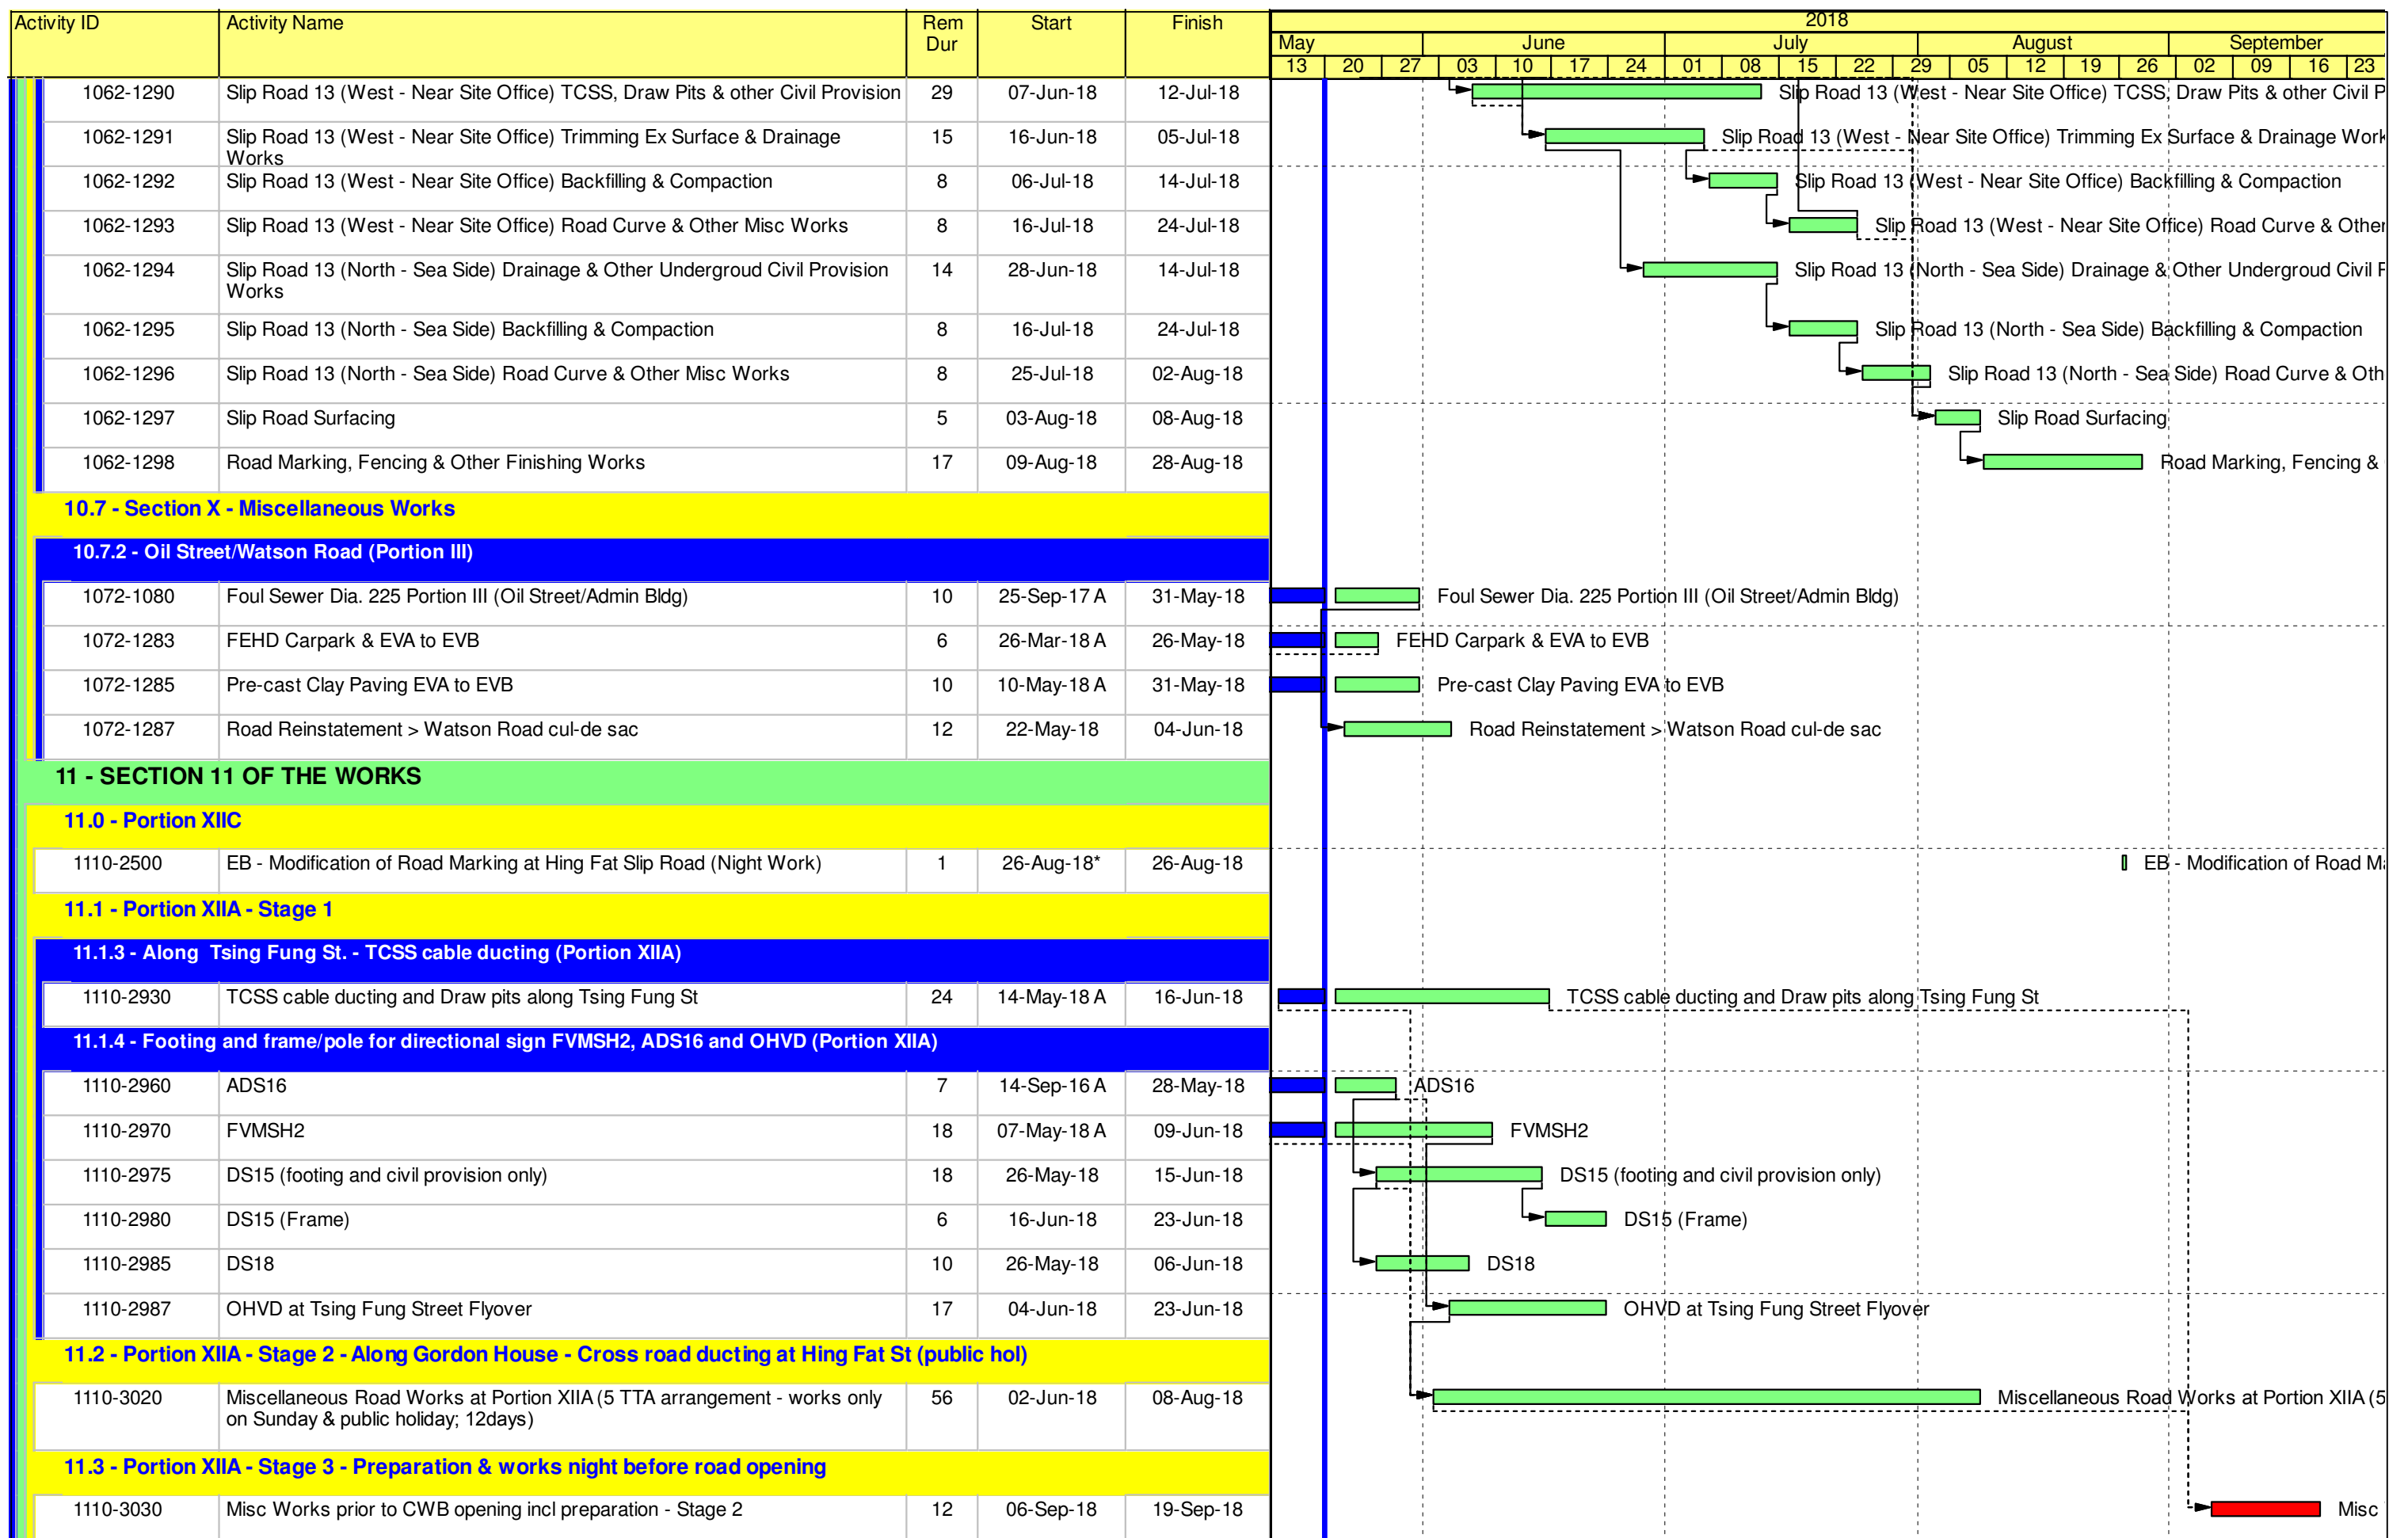

Contract HY/2009/19
Three Months Rolling Programme (20.May.2018 to 31.Aug.2018)

Activity ID	Activity Name	Original Duration	Start	Finish	2018											
					Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
Total		2356d	21-Mar-13 A	01-Sep-19												
DWP-08 - (2) - Update Progress As of 20 Jun 18		2356d	21-Mar-13 A	01-Sep-19												
Works in KD9 (Include Re-provisioning Works of KD4,KD5)		247d	30-Jan-18 A	23-Sep-18												
External Works Under KD9		151d	30-Jan-18 A	17-Sep-18												
Zone 1		60d	18-Apr-18 A	27-May-18 A												
Drainage Alignment Confirmation for MH72, 73, 74 due to Tree T1106		60d	18-Apr-18 A	27-May-18 A												
EXW_1155	Confirmation, TTA application and construction of re-routing of drainage works near RW8E side	60d	18-Apr-18 A	27-May-18 A	TTA application and construction of re-routing of drainage works near RW8E side											
Zone 4 up to Elderly Facilities		125d	30-Jan-18 A	17-Sep-18												
Elderly Facilities V/039 Received on 22 Jun 2017		100d	30-Jan-18 A	17-Sep-18												
EXW_2270	Facilities fabrication	90d	30-Jan-18 A	13-Aug-18	Facilities fabrication											
EXW_2280	Ground levelling, drainage works and safety met installation	30d	14-Aug-18	17-Sep-18	Ground levelling											
Additional Walkway & Arbour V/040 Received on 22 Aug 2017		93d	28-Mar-18 A	28-Jul-18												
EXW_2310	Assiciated drainage works for the walkway	20d	28-Mar-18 A	23-May-18 A	Works for the walkway											
EXW_2320	Arbour installation and walkway construction	30d	03-May-18 A	28-Jul-18	Arbour installation and walkway construction											
Reverting Traffic for IEC,VP Rd & TF St & Seawall Reinstatement (KD9)		164d	26-Mar-18 A	23-Sep-18												
TTA Revert Traffic Back to Original Alignment		105d	26-Mar-18 A	28-Jul-18												
East Bound TTA - IEC East Bound, Victoria Park Road & footpath along Sea Side		93d	28-Mar-18 A	28-Jul-18												
TTM Stage 1 - IEC (East Bound)		6d	21-Jun-18	26-Jun-18												
Reinstatement Existing Structure		6d	21-Jun-18	26-Jun-18												
EB_1020	Install metal parapet on parapet wall (30m)	6d	21-Jun-18	26-Jun-18	Install metal parapet on parapet wall (30m)											
TTM Stage 2 - Revert Traffic back to Original Victoria Road		4d	27-Jun-18	30-Jun-18												
Existing Bridge Parapet Reinstatement		4d	27-Jun-18	30-Jun-18												
EB_1180	Install metal parapet on parapet wall (40m)	4d	27-Jun-18	30-Jun-18	Install metal parapet on parapet wall (40m)											
TTM Stage 3 - Reinstatement of Footpath along Seafront		93d	28-Mar-18 A	28-Jul-18												
Reinstatement of Existing Utilities at Existing Footpath		86d	28-Mar-18 A	24-Jul-18												
EB_1600	Lay HGC, PCCW, Whart T&T and NWT telecom ducts and construct drawpits	10d	28-Mar-18 A	24-Jul-18	Lay HGC, PCCW, Whart T&T and NWT telecom ducts and construct drawpits											
EB_1620	Reinstate permanent water main	5d	18-Apr-18 A	17-Jul-18	Reinstate permanent water main											
EB_1580	Water main Connection by WSD	2d	20-Jun-18 A	20-Jun-18 A	Water main Connection by WSD											
Reinstatement of Permanent Footpath at Seafront		49d	27-May-18 A	26-Jul-18												
EB_1630	Backfilling Subbase	3d	27-May-18 A	29-May-18 A	Subbase											
EB_1640	Concreting of Permanent Footpath	4d	29-May-18 A	25-Jul-18	Concreting of Permanent Footpath											
EB_1650	Pedestrian diversion on Permanent Footpath	1d	26-Jul-18	26-Jul-18	Pedestrian diversion on Permanent Footpath											
Reinstatement Works in Traffic Deck Part B		3d	07-May-18 A	28-Jul-18												
EB_1700	Backfill Type B Material up to 2m below F.F.L (Compaction by proof rolling method of 0.2m each layer)	3d	07-May-18 A	28-Jul-18	Backfill Type B Material up to 2m below F.F.L (Compaction by proof rolling method of 0.2m each layer)											
West Bound - IEC West Bound & Tsing fung Street		74d	26-Mar-18 A	06-Jul-18												
TTM Stage 2 - Revert Traffic back to Original Tsing Fung Street		5d	21-Jun-18	25-Jun-18												
Existing Bridge Parapet Reinstatement		5d	21-Jun-18	25-Jun-18												
IECW_1140	Install metal parapet on parapet wall (60m)	5d	21-Jun-18	25-Jun-18	Install metal parapet on parapet wall (60m)											
TTM Stage 3 - Reinstatement of Victoria Park		21d	26-Mar-18 A	06-Jul-18												
Reinstatement Works inside Victoria Park		21d	26-Mar-18 A	06-Jul-18												
IECW_1470	Slope Reinstatement of Victoria Park	21d	26-Mar-18 A	06-Jul-18	Slope Reinstatement of Victoria Park											
Completion of Minor Outstanding / Remaining Works for KD9		110d	18-May-18 A	23-Sep-18												
East Bound - Minor Outstanding Works in Footpath after Substantial Completion of KD9		88d	18-May-18 A	01-Sep-18												

中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work
- ◆ Milestone

Page 1 of 3

Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip Road 8 Section) - 3 Months Rolling Programme

Date	Revision	Checked	Approved
20-Jun-18	DWP-08 (2) - 3 Months Rolling	TL	TL

Activity ID	Activity Name	Original Duration	Start	Finish	2018			
					Jun	Jul	Aug	Sep
Minor Reinstatement Works for Existing Sign Gantry								
EB_1750	Laying Public Lighting duct	3d	30-May-18 A	25-Aug-18	Laying Public Lighting duct			
EB_1780	Erect Sign Gantry Steel Supports and Sign Gantry Beam across VPR and IEC E/B	4d	29-Jul-18	01-Aug-18	Erect Sign Gantry Steel Supports and Sign Gantry Beam across VPR and IEC E/B			
EB_1790	Installation of E & M at Sign Gantry (night work)	1d	02-Aug-18	02-Aug-18	Installation of E & M at Sign Gantry (night work)			
EB_1760	Connection of Public Lighting by HyD (Lighting)	2d	26-Aug-18	27-Aug-18	Connection of Public Lighting by HyD (Lighting)			
Minor Reinstatement Works for Central Median of IEC & Footbridge								
EB_1800	Reconstruction of central divider (6m long, night work)	6d	02-Aug-18	07-Aug-18	Reconstruction of central divider (6m long, night work)			
EB_1810	Dismantlement of temp directional sign mounted on extg footbridge	1d	03-Aug-18	03-Aug-18	Dismantlement of temp directional sign mounted on extg footbridge			
Minor Reinstatement Works for Footpath								
EB_1820	Place kerblines along VPR footpath	3d	18-May-18 A	23-Aug-18	Place kerblines along VPR footpath			
EB_1850	Backfilling subbase material	2d	27-May-18 A	29-May-18 A	subbase material			
EB_1830	Reinstatement of District Council Welcome Sign and opening plaque at Planter area	1d	24-Aug-18	24-Aug-18	Reinstatement of District Council Welcome Sign and opening			
EB_1840	Re-provision of Tree	8d	25-Aug-18	01-Sep-18	Re-provision of Tree			
Minor Reinstatement Works for Bus Stop								
EB_1860	Reinstatement of Permanent Bus Stop	5d	23-May-18 A	26-Jun-18 A	Reinstatement of Permanent Bus Stop			
EB_1870	Relocation of Bus Stop	1d	27-Jun-18 A	27-Jun-18 A	Relocation of Bus Stop			
EB_1880	Reinstate Planter(Previous Temporary Bus Stop)	5d	25-Aug-18	29-Aug-18	Reinstate Planter(Previous Temporary Bus Stop)			
Minor Reinstatement Works for Loop Detector								
EB_1900	Construction of concrete plinth and fix counter housing for Loop Detector (ILDS)	3d	04-Aug-18	06-Aug-18	Construction of concrete plinth and fix counter housing for Loop Detector (ILDS)			
EB_1890	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)	1d	07-Aug-18	07-Aug-18	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)			
West Bound - Completion of Minor Outstanding / Remaining Works for KD9								
Minor Reinstatement Works for Victoria Park								
IECW_1500	Re-provision of Tree	32d	07-Jul-18	07-Aug-18	Re-provision of Tree			
IECW_1510	Laying Irrigation Main	10d	22-Jul-18	31-Jul-18	Laying Irrigation Main			
IECW_1520	Construct Landscape Footpath and Lightings	7d	06-Aug-18	12-Aug-18	Construct Landscape Footpath and Lightings			
Minor Reinstatement Works in IEC West Bound								
IECW_1600	Replacement of new movement joint at IEC W/B (Sun midnight only)	8d	21-Jun-18	28-Jun-18	Replacement of new movement joint at IEC W/B (Sun midnight only)			
IECW_1610	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)	57d	29-Jun-18	24-Aug-18	Repairing of extg conc deck surface after milling of temp asp			
IECW_1640	Erection of new precast concrete panels (12 nos.) at abutment M facing to VPR	2d	25-Aug-18	26-Aug-18	Erection of new precast concrete panels (12 nos.) at abu			
IECW_1620	Repairing of concrete defects on extg concrete deck and abutment M	30d	25-Aug-18	23-Sep-18	Re			
Works in Victoria Park (KD4, KD5, KD9)								
Re-Provisioning Works								
Nursery Compound								
Nursery compound								
ABWF								
Metal Fence								
VP_NC_1820	Installation	30d	05-Apr-18 A	07-Aug-18	Installation			
Fire Services								
VP_NC_2030	FS inspection	14d	21-Jun-18	07-Jul-18	FS inspection			
Plumbing and Flushing Water Supplies								
VP_NC_2100	WSD Inspection	14d	21-Jun-18	07-Jul-18	WSD Inspection			
External Works Aside Nursery Compound								
External Works Around Nursery Compound								

Activity ID	Activity Name	Original Duration	Start	Finish	2018											
					Jun			Jul			Aug			Sep		
					1	2	3	1	2	3	1	2	3	1	2	3
VP_NC_2250	Reinstatement of Existing Boundary Fence Wall Around Nursery Compound	45d	01-Mar-18 A	26-May-18 A	Existing Boundary Fence Wall Around Nursery Compound											
VP_NC_2260	EVA Construction	15d	28-May-18 A	14-Jul-18	EVA Construction											
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks		390d	08-Aug-18	01-Sep-19												
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)		365d	08-Aug-18	07-Aug-19												
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365d	08-Aug-18	07-Aug-19												
KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH>500mm)		365d	02-Sep-18	01-Sep-19												
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365d	02-Sep-18	01-Sep-19												
KD18 - Section 11: Transplanted Trees DBH>500mm in Portion VA and XII		365d	08-Aug-18	07-Aug-19												
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365d	08-Aug-18	07-Aug-19												
KD10 - Preservation and Protection of Trees		1088d	21-Mar-13 A	27-Sep-18												
PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	27-Sep-18												
KD15 & KD8 - Mooring Components Upkeep (CBTS and ATS)		979d	15-May-14 A	21-Jun-18												
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	21-Jun-18	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS											
