

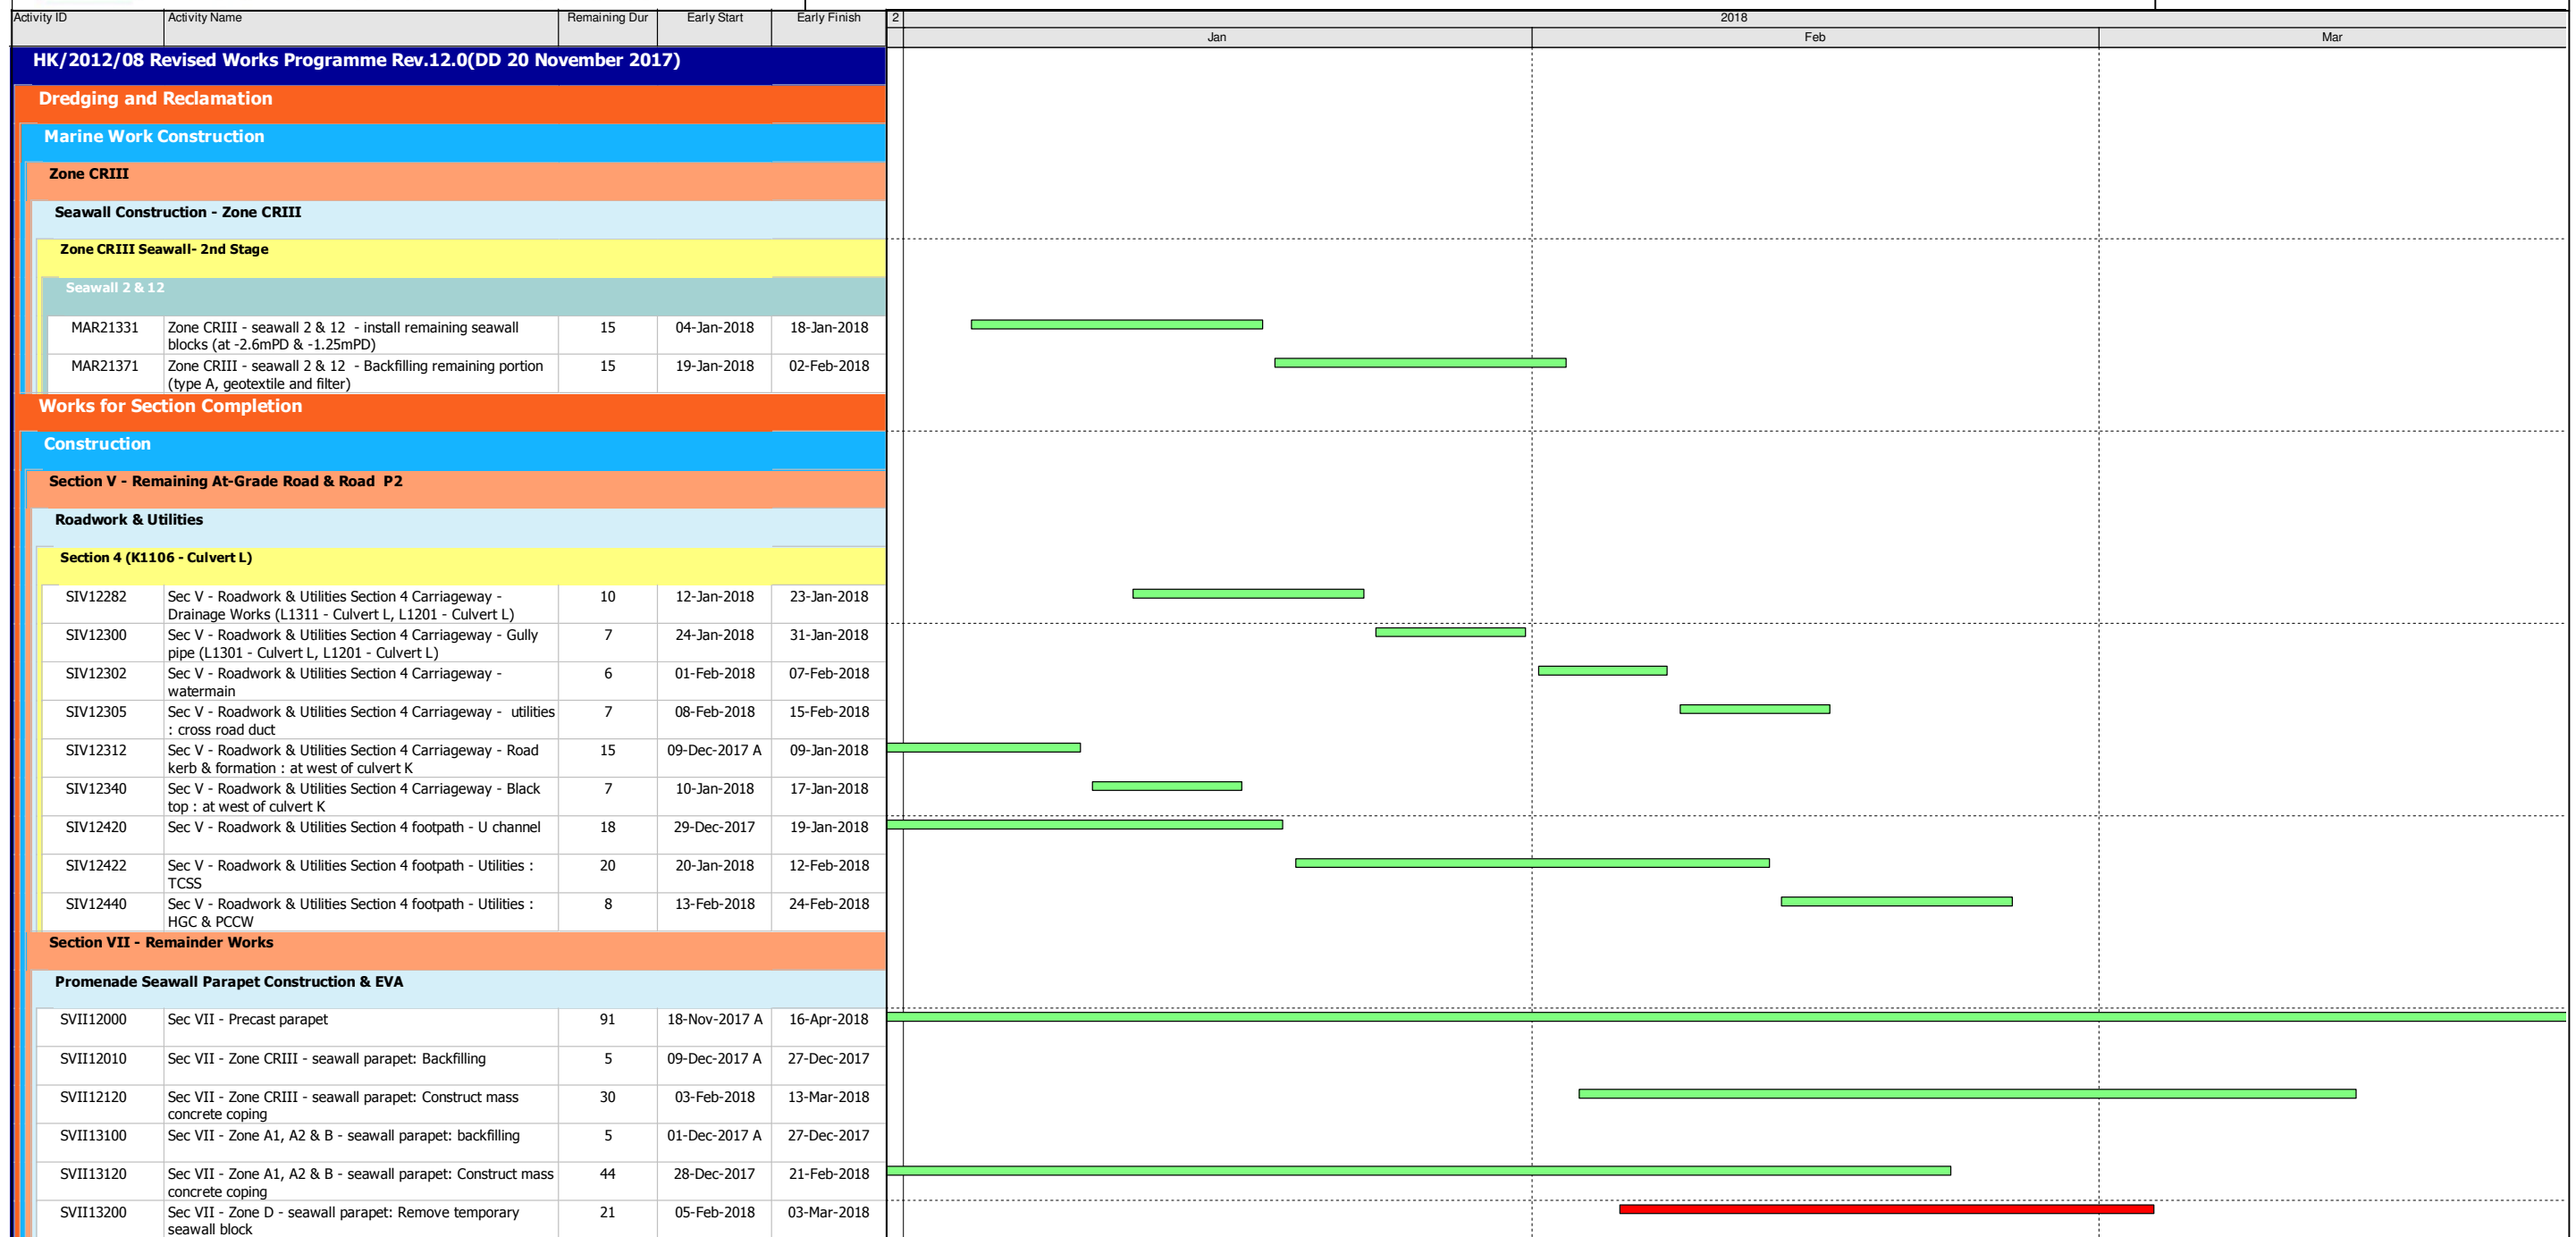


Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2017			2018
					Oct	Nov	Dec	Jan
<b>HK/2012/08 Revised Works Programme Rev.11.1(DD 30 Jun 2017)</b>								
<b>Dredging and Reclamation</b>								
<b>Marine Work Construction</b>								
<b>Zone CR111</b>								
<b>Seawall Construction - Zone CR111</b>								
<b>Zone CR111 Seawall- 2nd Stage</b>								
Seawall 2 & 12								
MAR21331	Zone CR111 - seawall 2 & 12 - install remaining seawall blocks (at -2.6mPD & -1.25mPD)	15	01-Oct-17	15-Oct-17				
MAR21371	Zone CR111 - seawall 2 & 12 - Backfilling remaining portion (type A, geotextile and filter)	15	16-Oct-17	30-Oct-17				
<b>Works for Section Completion</b>								
<b>Construction</b>								
<b>CWB Tunnel &amp; Slip Road Structures and Facilities</b>								
<b>CWB CR111 &amp; A1</b>								
<b>CWB CR111 - ELS &amp; Tunnel Structure</b>								
<b>CWB CR111 - Other Works</b>								
SIIA11204	Sec II A - CWB CR111: Reinstatement of culvert K - Bay 15: Construct Roof Slab	44	13-Oct-17	25-Nov-17				
SIIA11251	Sec II A - CWB CR111: Reinstatement of temporary openings at culvert K bay 20B	14	14-Nov-17	27-Nov-17				
SIIA11205	Sec II A - CWB CR111: Reinstatement of culvert K - Bay 15: Remove formwork & backfilling	25	26-Nov-17	20-Dec-17				
SIIA11685	Sec II A - CWB CR111: Reinstatement cooling mains - 2nd stage: Install cooling mains (DN700, DN800, DN900 & )	54	07-Nov-17	30-Dec-17				
SIIA11248	Sec II A - CWB CR111: Install & test stop log at culvert K bay 21	20	25-Oct-17*	13-Nov-17				
<b>Section V - Remaining At-Grade Road; Remove 2nd Stage ITA</b>								
<b>Roadwork &amp; Utilities</b>								
<b>Section 4 (K1106 - Culvert L)</b>								
SIV12305	Sec V - Roadwork & Utilities Section 4 Carriageway - Utilities : crossroad duct	14	05-Dec-17	20-Dec-17				
SIV12300	Sec V - Roadwork & Utilities Section 4 Carriageway - Gully pipe (K1106-Culvert K, K1201-Culvert K, L1201, L1301)	35	24-Oct-17	04-Dec-17				
SIV12360	Sec V - Roadwork & Utilities Section 4 Carriageway - watermain	15	21-Dec-17	10-Jan-18				
SIV12440	Sec V - Roadwork & Utilities Section 4 footpath - Utilities : HGC & PCCW	8	21-Dec-17	02-Jan-18				

Data Date: 30-Jun-17	Current Milestone
	Actual Work
	Critical Remaining Work
	Remaining Work
	Remaining Level of Effort

**3 Months Rolling Programme for CR111 Area ( Oct 2017 - Dec 2017)**  
**(Ref. to Works Programme Rev.11.1)**

Date	Revision	Checked	Approved
03-Oct-17	11.1		





Data Date: 20-Dec-2017	<ul style="list-style-type: none"> <li><span style="color: blue;">◆</span> Current Milestone</li> <li><span style="color: blue;">■</span> Actual Work</li> <li><span style="color: red;">■</span> Critical Remaining Work</li> <li><span style="color: green;">■</span> Remaining Work</li> <li><span style="color: green;">▬</span> Remaining Level of Effort</li> </ul>
---------------------------	---

**3 Months Rolling Programme for CRIII Area (January 2018 - March 2018)**  
(Ref. to Revised Works Programme Rev.12)

Date	Revision	Checked	Approved
20-Dec-2017	12		

**HY/2009/18 Central - Wan Chai Bypass - Central Interchange**

2017				
	September	October	November	December
<b>Road P1</b>				
Installation of irrigation pipes at P1 Road				
Reinstatement of planter at P1 Road				
<b>LEGEND:</b>	<b>Three Month Rolling Programme</b>			Update on 26.11.2017
 Actual Works				
 Remaining Works				
