

**CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019							
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
HK/2012/08 Revised Works Programme Rev.12.0(DD 20 November 2017)																									
Key Dates and Milestone Dates																									
Sections of Works Completion (Included Not Granted EOT Entitlement of The Contractor)																									
KD10840	Completion of Section IIIA	0		08-Sep-18*	0%																				
KD10860	Completion of Section IV	0		30-Aug-18*	0%																				
KD10880	Completion of Section V	0		26-Sep-18*	0%																				
KD11010	Completion of Section VII	0		14-Sep-18*	0%																				
KD11020	Completion of Section VIII	0		21-Sep-18*	0%																				
KD11040	Completion of Section IX	0		21-Sep-19*	0%																				
KD11060	Completion of Section X	0		21-Sep-18*	0%																				
Planned Sections of Works Completion																									
KD10080	Planned Section IIIA Completion - Road A2,A4, A5	0		08-Sep-18	0%																				
KD10100	Planned Section IV Completion - Slip Road 3	0		30-Aug-18	0%																				
KD10140	Planned Section V Completion - Remaining At-Grade Road	0		26-Sep-18	0%																				
KD10280	Planned Section VII Completion - Remainder Works	0		14-Sep-18	0%																				
KD10300	Planned Section VIII Completion - Landscape Softwork	0		21-Sep-18	0%																				
KD10320	Planned Section IX Completion - Establishment Works	0		21-Sep-19	0%																				
KD10340	Planned Section X Completion - Tree Protection & Preservation	0		21-Sep-18	0%																				
Dredging and Reclamation																									
Marine Work Construction																									
Zone CRIII																									
Seawall Construction - Zone CRIII																									
Zone CRIII Seawall- 2nd Stage																									
Seawall 2 & 12																									
MAR21371	Zone CRIII - seawall 2 & 12 - Backfilling remaining portion (type A, geotextile and filter)	0	19-Jan-18 A	27-Jan-18 A	100%	■																			
Zone D																									
Seawall Construction - Zone D																									
Seawall 10 & 11																									
MAR20630	Zone D - Seawall 10 & 11: Install remaining seawall block	14	20-Feb-18*	05-Mar-18	0%		■																		
MAR20650	Zone D - Seawall 10 & 11: Backfill Type A	7	06-Mar-18	12-Mar-18	0%			■																	
MAR20670	Zone D - Seawall 10 & 11: Lay geotextile and filter	7	13-Mar-18	19-Mar-18	0%			■																	
Works for Section Completion																									
Construction																									
Section III A - Road A2, A4 & A5																									
Roadwork & Utilities - Section 1 (L1806 - L1801)																									

Data Date: 20-Feb-18


- ◆ Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Remaining Level of Effort

**Updated Works Programme Rev.12
(Ref. to Rev.12 as of 20 February 2018)**

Date	Revision	Checked	Approved
20-Feb-18	12		

**CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019											
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
Promenade Seawall Parapet Construction & EVA																													
SVII12000	Sec VII - Precast parapet	67	18-Nov-17 A	14-May-18	0%																								
SVII12010	Sec VII - Zone CRIII - seawall parapet: Backfilling	14	20-Feb-18	07-Mar-18	0%																								
SVII12120	Sec VII - Zone CRIII - seawall parapet: Construct mass concrete coping	30	08-Mar-18	16-Apr-18	0%																								
SVII12122	Sec VII - Zone CRIII - seawall parapet: reinforced concret coping	17	17-Apr-18	07-May-18	0%																								
SVII12140	Sec VII - Zone CRIII - seawall parapet: construct seawall parapet	30	08-May-18	12-Jun-18	0%																								
SVII12160	Sec VII - CRIII - EVA: watermain	14	13-Jun-18	29-Jun-18	0%																								
SVII12180	Sec VII - CRIII - EVA: U-channel	14	30-Jun-18	17-Jul-18	0%																								
SVII12200	Sec VII - CRIII - EVA: bituminous layer	5	18-Jul-18	23-Jul-18	0%																								
SVII12220	Sec VII - CRIII - EVA: paving block	30	24-Jul-18	27-Aug-18	0%																								
SVII13120	Sec VII - Zone A1, A2 & B - seawall parapet: Construct mass concrete coping	14	28-Dec-17 A	07-Mar-18	68.18%																								
SVII13122	Sec VII - Zone A1, A2 & B - seawall parapet: reinforced concrete coping	18	08-Mar-18	28-Mar-18	0%																								
SVII13140	Sec VII - Zone A1, A2 & B - seawall parapet: Construct seawall parapet	30	09-Apr-18	14-May-18	0%																								
SVII13160	Sec VII - Zone A1, A2 & B - EVA: watermain	14	15-May-18	31-May-18	0%																								
SVII13180	Sec VII - Zone A1, A2 & B - EVA: U-channel	14	01-Jun-18	16-Jun-18	0%																								
SVII13182	Sec VII - Zone A1, A2 & B - EVA: bituminous layer	5	19-Jun-18	23-Jun-18	0%																								
SVII13184	Sec VII - Zone A1, A2 & B - EVA: paving block	30	25-Jun-18	30-Jul-18	0%																								
SVII13200	Sec VII - Zone D - seawall parapet: Remove temporary seawall block	21	07-Mar-18	03-Apr-18	0%																								
SVII13220	Sec VII - Zone D - seawall parapet: Construct mass concrete	30	04-Apr-18	10-May-18	0%																								
SVII13222	Sec VII - Zone D - seawall parapet: reinforced concrete coping	18	11-May-18	01-Jun-18	0%																								
SVII13240	Sec VII - Zone D - seawall parapet: Construct seawall parapet	25	02-Jun-18	03-Jul-18	0%																								
SVII13260	Sec VII - Zone D - EVA : watermain	14	04-Jul-18	19-Jul-18	0%																								
SVII13280	Sec VII - Zone D - EVA : U-channel	14	20-Jul-18	04-Aug-18	0%																								
SVII13300	Sec VII - Zone D - EVA : bituminous layer	5	06-Aug-18	10-Aug-18	0%																								
SVII13320	Sec VII - Zone D - EVA : paving block	30	11-Aug-18	14-Sep-18	0%																								
Promenade Footpath																													
Section 1																													
SVII10440	Sec VII - section 1 footpath - drainage works : connection pipe & U -channel	10	24-May-18	04-Jun-18	0%																								
SVII10445	Sec VII - section 1 footpath - watermain	7	05-Jun-18	12-Jun-18	0%																								
SVII10460	Sec VII - section 1 footpath - lighting	7	13-Jun-18	21-Jun-18	0%																								
SVII10500	Sec VII - section 1 footpath - paving block	21	22-Jun-18	17-Jul-18	0%																								
Section 2																													
SVII12610	Sec VII - section 2 footpath - drainage works : L2202 - L2203A	20	20-Feb-18	14-Mar-18	0%																								
SVII12615	Sec VII - section 2 footpath - watermain	7	15-Mar-18	22-Mar-18	0%																								
SVII12630	Sec VII - section 2 footpath - utilities: TCSS	21	23-Mar-18	20-Apr-18	0%																								
SVII12670	Sec VII - section 2 footpath - paving block	30	21-Apr-18	28-May-18	0%																								
Section 3																													
SVII12850	Sec VII - section 3 footpath - watermain	17	20-Feb-18	10-Mar-18	0%																								
SVII12870	Sec VII - section 3 footpath - utilities (HEC, TCSS, HGC, PCCW)	40	12-Mar-18	02-May-18	0%																								
SVII12875	Sec VII - 3 footpath - drainage works :U chanel	14	03-May-18	18-May-18	0%																								

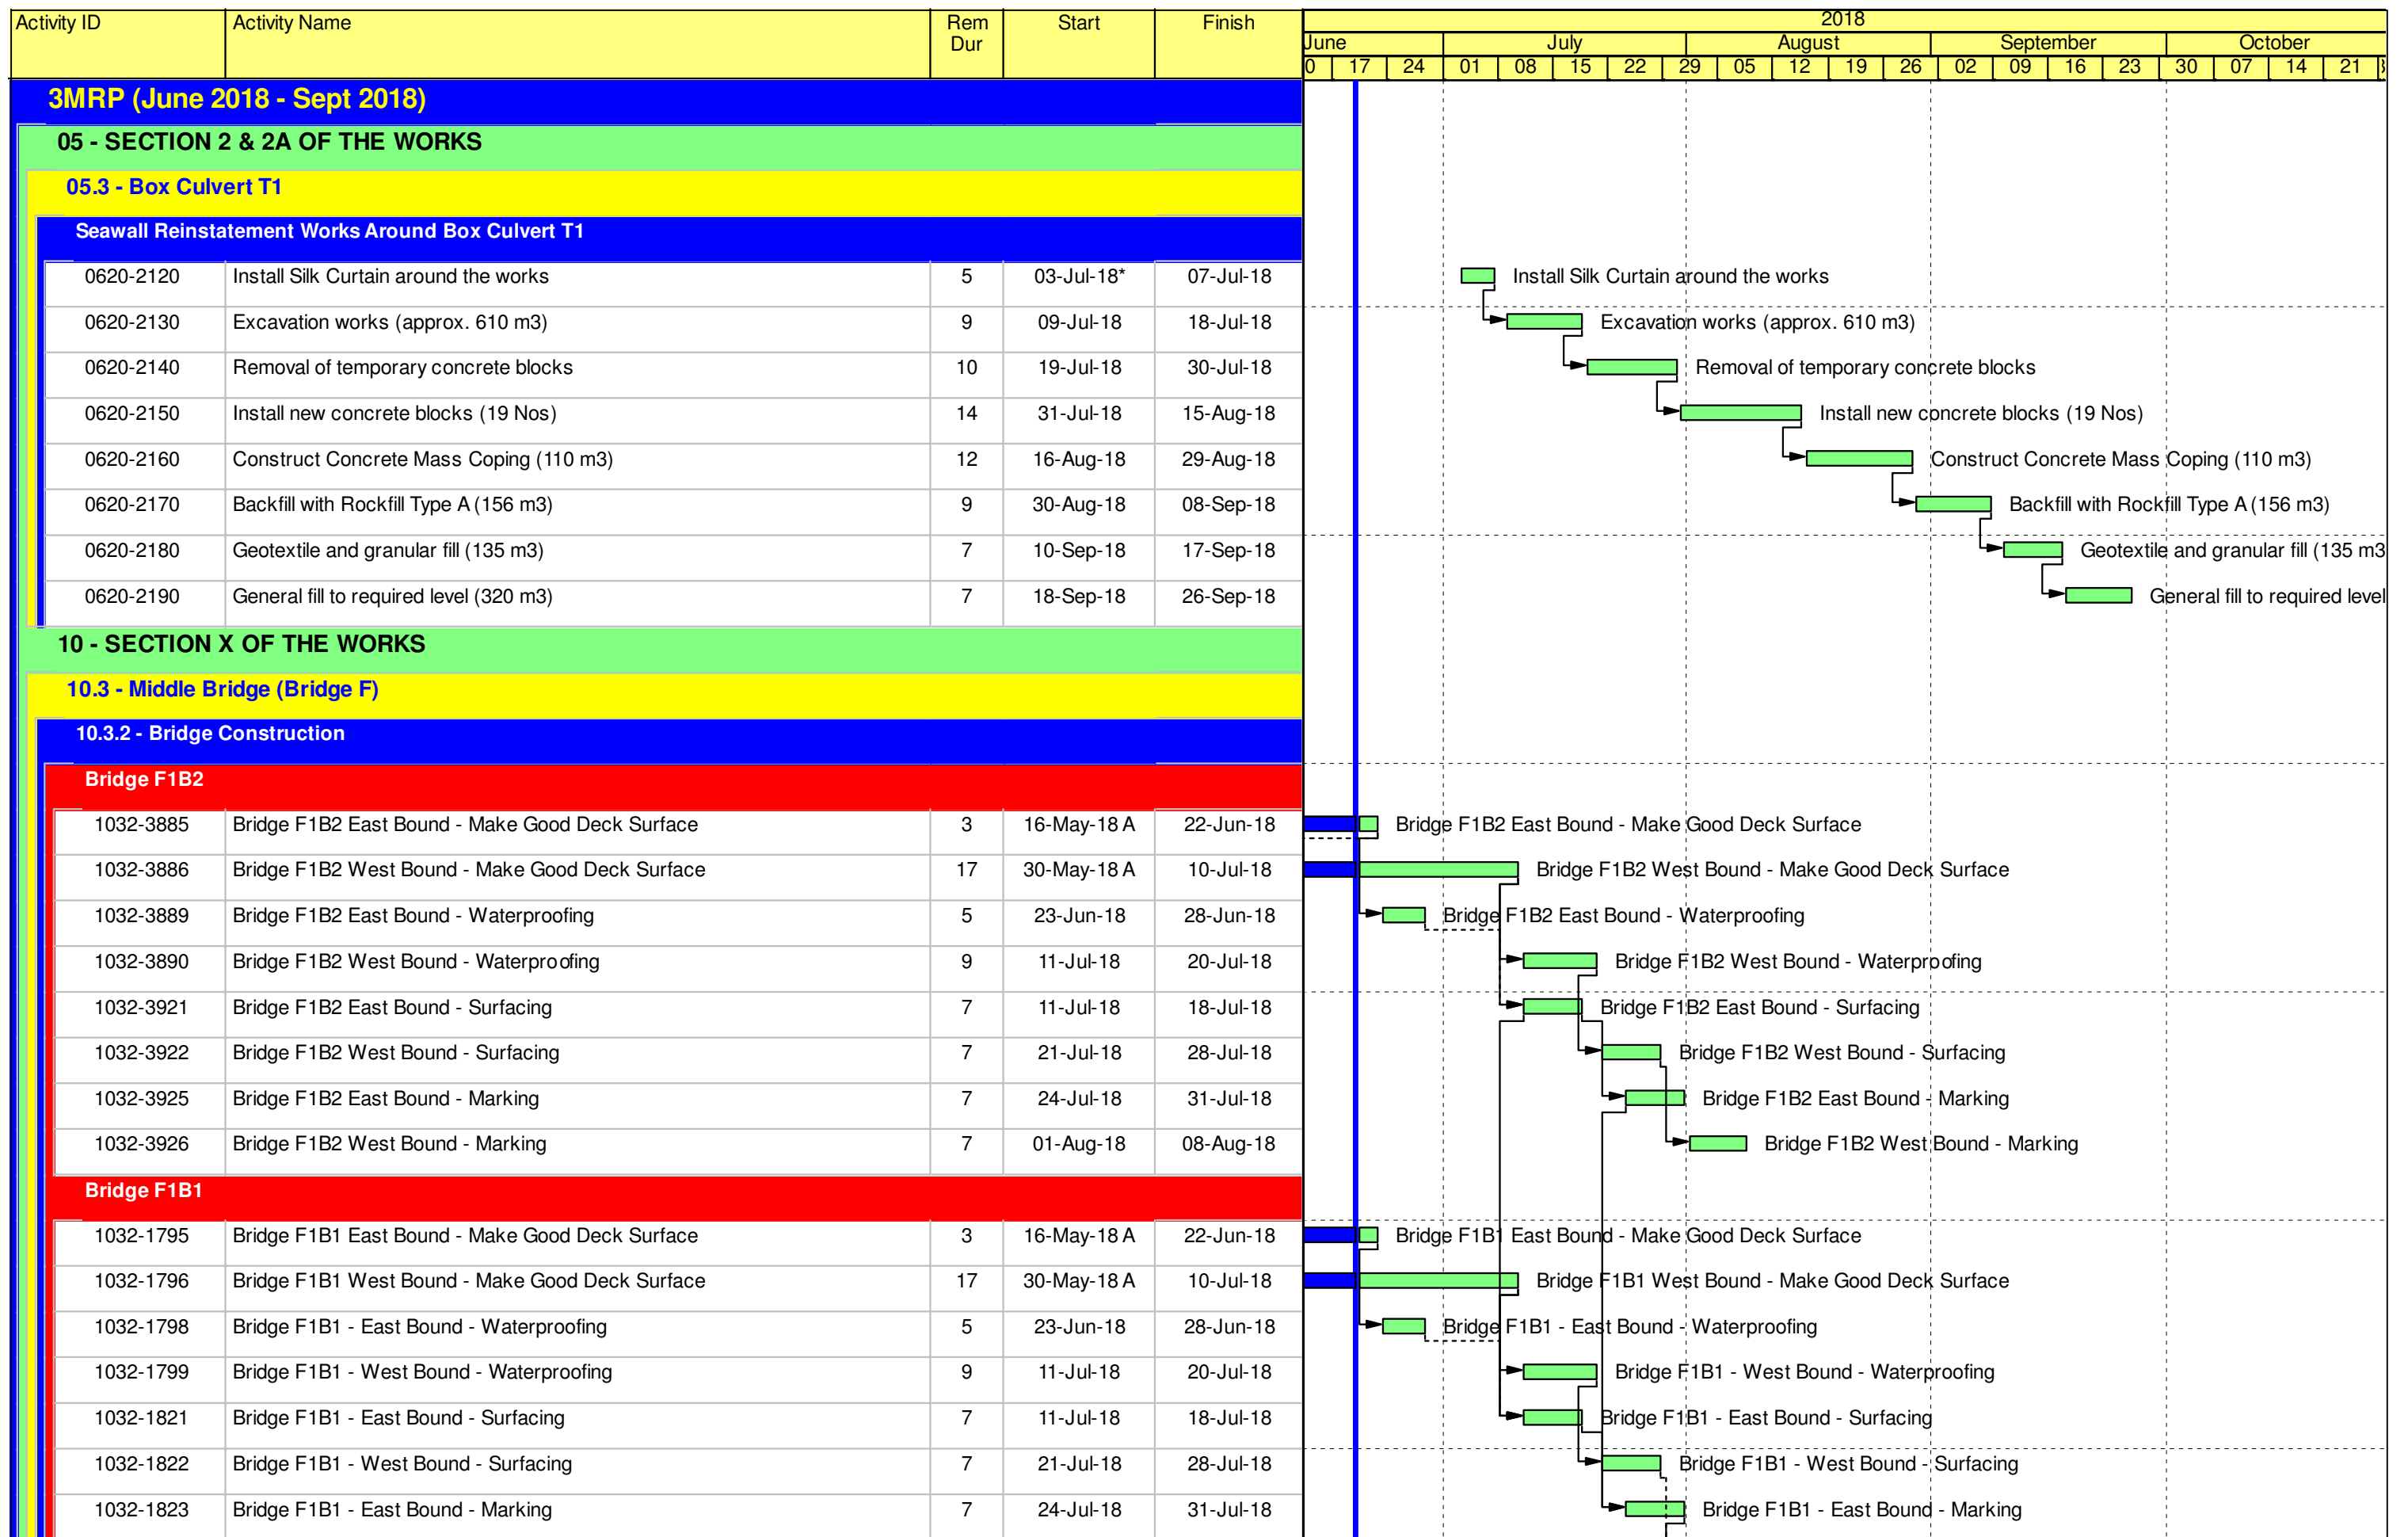

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.June.2018 to 20.Sept.2018)

Activity ID	Activity Name	Rem Dur	Start	Finish	2018																			
					June			July				August				September				October				
					0	17	24	01	08	15	22	29	05	12	19	26	02	09	16	23	30	07	14	21
1062-1291	Slip Road 13 (West - Near Site Office) Trimming Ex Surface & Drainage Works	13	07-Jun-18 A	05-Jul-18	Slip Road 13 (West - Near Site Office) Trimming Ex Surface & Drainage Works																			
1062-1292	Slip Road 13 (West - Near Site Office) Backfilling & Compaction	8	06-Jul-18	14-Jul-18	Slip Road 13 (West - Near Site Office) Backfilling & Compaction																			
1062-1293	Slip Road 13 (West - Near Site Office) Road Kerb & Other Misc Works	8	16-Jul-18	24-Jul-18	Slip Road 13 (West - Near Site Office) Road Kerb & Other Misc Works																			
1062-1294	Slip Road 13 (North - Sea Side) Drainage & Other Underground Civil Provision Works	14	25-Jun-18	11-Jul-18	Slip Road 13 (North - Sea Side) Drainage & Other Underground Civil Provision Works																			
1062-1295	Slip Road 13 (North - Sea Side) Backfilling & Compaction	8	12-Jul-18	20-Jul-18	Slip Road 13 (North - Sea Side) Backfilling & Compaction																			
1062-1296	Slip Road 13 (North - Sea Side) Road Kerb & Other Misc Works	8	21-Jul-18	30-Jul-18	Slip Road 13 (North - Sea Side) Road Kerb & Other Misc Works																			
1062-1297	Slip Road Surfacing	5	31-Jul-18	04-Aug-18	Slip Road Surfacing																			
1062-1298	Road Marking, Fencing & Other Finishing Works	17	06-Aug-18	24-Aug-18	Road Marking, Fencing & Other Finishing Works																			
10.7 - Section X - Miscellaneous Works																								
10.7.2 - Oil Street/Watson Road (Portion III)																								
1072-1285	Pre-cast Clay Paving EVA to EVB (remaining paver to arrive on site by mid Aug)	57	10-May-18 A	25-Aug-18	Pre-cast Clay Paving EVA to EVB (remaining paver to arrive on site by mid Aug)																			
1072-1287	Road Reinstatement > Watson Road cul-de sac	12	22-May-18 A	04-Jul-18	Road Reinstatement > Watson Road cul-de sac																			
11 - SECTION 11 OF THE WORKS																								
11.0 - Portion XIIC																								
1110-2500	EB - Modification of Road Marking at Hing Fat Slip Road (Night Work)	1	26-Aug-18*	26-Aug-18	EB - Modification of Road Marking at Hing Fat Slip Road																			
11.1 - Portion XIIA - Stage 1																								
11.1.4 - Footing and frame/pole for directional sign FVMSh2, ADS16 and OHVD (Portion XIIA)																								
1110-2970	FVMSh2	18	07-May-18 A	11-Jul-18	FVMSh2																			
1110-2980	DS15 (Frame)	6	19-Jun-18 A	26-Jun-18	DS15 (Frame)																			
1110-2985	DS18	10	20-Jun-18	30-Jun-18	DS18																			
1110-2987	OHVD at Tsing Fung Street Flyover	17	05-Jul-18*	24-Jul-18	OHVD at Tsing Fung Street Flyover																			
11.2 - Portion XIIA - Stage 2 - Along Gordon House - Cross road ducting at Hing Fat St (public hol)																								
1110-3020	Miscellaneous Road Works at Portion XIIA (5 TTA arrangement - works only on Sunday & public holiday; 12days)	56	04-Jul-18	06-Sep-18	Miscellaneous Road Works at Portion XIIA (5 TTA arrangement - works only on Sunday & public holiday; 12days)																			
11.3 - Portion XIIA - Stage 3 - Preparation & works night before road opening																								
1110-3030	Misc Works prior to CWB opening incl preparation - Stage 2	12	06-Sep-18	19-Sep-18	Misc Works prior to CWB opening																			

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.June.2018 to 20.Sept.2018)

Activity ID	Activity Name	Original Duration	Start	Finish	2018			
					Jun	Jul	Aug	Sep
Total		2356d	21-Mar-13 A	01-Sep-19				
DWP-08 - (2) - Update Progress As of 20 Jun 18		2356d	21-Mar-13 A	01-Sep-19				
Works in KD9 (Include Re-provisioning Works of KD4,KD5)		247d	30-Jan-18 A	23-Sep-18				
External Works Under KD9		151d	30-Jan-18 A	17-Sep-18				
Zone 1		60d	18-Apr-18 A	27-May-18 A				
Drainage Alignment Confirmation for MH72, 73, 74 due to Tree T1106		60d	18-Apr-18 A	27-May-18 A				
EXW_1155	Confirmation, TTA application and construction of re-routing of drainage works near RW8E side	60d	18-Apr-18 A	27-May-18 A	TTA application and construction of re-routing of drainage works near RW8E side			
Zone 4 up to Elderly Facilities		125d	30-Jan-18 A	17-Sep-18				
Elderly Facilities V/039 Received on 22 Jun 2017		100d	30-Jan-18 A	17-Sep-18				
EXW_2270	Facilities fabrication	90d	30-Jan-18 A	13-Aug-18	Facilities fabrication			
EXW_2280	Ground levelling, drainage works and safety met installation	30d	14-Aug-18	17-Sep-18	Ground levelling			
Additional Walkway & Arbour V/040 Received on 22 Aug 2017		93d	28-Mar-18 A	28-Jul-18				
EXW_2310	Associated drainage works for the walkway	20d	28-Mar-18 A	23-May-18 A	Works for the walkway			
EXW_2320	Arbour installation and walkway construction	30d	03-May-18 A	28-Jul-18	Arbour installation and walkway construction			
Reverting Traffic for IEC,VP Rd & TF St & Seawall Reinstatement (KD9)		164d	26-Mar-18 A	23-Sep-18				
TTA Revert Traffic Back to Original Alignment		105d	26-Mar-18 A	28-Jul-18				
East Bound TTA - IEC East Bound, Victoria Park Road & footpath along Sea Side		93d	28-Mar-18 A	28-Jul-18				
TTM Stage 1 - IEC (East Bound)		6d	21-Jun-18	26-Jun-18				
Reinstatement Existing Structure		6d	21-Jun-18	26-Jun-18				
EB_1020	Install metal parapet on parapet wall (30m)	6d	21-Jun-18	26-Jun-18	Install metal parapet on parapet wall (30m)			
TTM Stage 2 - Revert Traffic back to Original Victoria Road		4d	27-Jun-18	30-Jun-18				
Existing Bridge Parapet Reinstatement		4d	27-Jun-18	30-Jun-18				
EB_1180	Install metal parapet on parapet wall (40m)	4d	27-Jun-18	30-Jun-18	Install metal parapet on parapet wall (40m)			
TTM Stage 3 - Reinstatement of Footpath along Seafront		93d	28-Mar-18 A	28-Jul-18				
Reinstatement of Existing Utilities at Existing Footpath		86d	28-Mar-18 A	24-Jul-18				
EB_1600	Lay HGC, PCCW, Whart T&T and NWT telecom ducts and construct drawpits	10d	28-Mar-18 A	24-Jul-18	Lay HGC, PCCW, Whart T&T and NWT telecom ducts and construct drawpits			
EB_1620	Reinstate permanent water main	5d	18-Apr-18 A	17-Jul-18	Reinstate permanent water main			
EB_1580	Water main Connection by WSD	2d	20-Jun-18 A	20-Jun-18 A	Water main Connection by WSD			
Reinstatement of Permanent Footpath at Seafront		49d	27-May-18 A	26-Jul-18				
EB_1630	Backfilling Subbase	3d	27-May-18 A	29-May-18 A	Subbase			
EB_1640	Concreting of Permanent Footpath	4d	29-May-18 A	25-Jul-18	Concreting of Permanent Footpath			
EB_1650	Pedestrian diversion on Permanent Footpath	1d	26-Jul-18	26-Jul-18	Pedestrian diversion on Permanent Footpath			
Reinstatement Works in Traffic Deck Part B		3d	07-May-18 A	28-Jul-18				
EB_1700	Backfill Type B Material up to 2m below F.F.L (Compaction by proof rolling method of 0.2m each layer)	3d	07-May-18 A	28-Jul-18	Backfill Type B Material up to 2m below F.F.L (Compaction by proof rolling method of 0.2m each layer)			
West Bound - IEC West Bound & Tsing fung Street		74d	26-Mar-18 A	06-Jul-18				
TTM Stage 2 - Revert Traffic back to Original Tsing Fung Street		5d	21-Jun-18	25-Jun-18				
Existing Bridge Parapet Reinstatement		5d	21-Jun-18	25-Jun-18				
IECW_1140	Install metal parapet on parapet wall (60m)	5d	21-Jun-18	25-Jun-18	Install metal parapet on parapet wall (60m)			
TTM Stage 3 - Reinstatement of Victoria Park		21d	26-Mar-18 A	06-Jul-18				
Reinstatement Works inside Victoria Park		21d	26-Mar-18 A	06-Jul-18				
IECW_1470	Slope Reinstatement of Victoria Park	21d	26-Mar-18 A	06-Jul-18	Slope Reinstatement of Victoria Park			
Completion of Minor Outstanding / Remaining Works for KD9		110d	18-May-18 A	23-Sep-18				
East Bound - Minor Outstanding Works in Footpath after Substantial Completion of KD9		88d	18-May-18 A	01-Sep-18				



中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Page 1 of 3

Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip Road 8 Section) - 3 Months Rolling Programme

Date	Revision	Checked	Approved
20-Jun-18	DWP-08 (2) - 3 Months Rolling	TL	TL

Activity ID	Activity Name	Original Duration	Start	Finish	2018											
					Jun			Jul			Aug			Sep		
					1	2	3	4	5	6	7	8	9	10	11	12
Minor Reinstatement Works for Existing Sign Gantry					75d 30-May-18 A 27-Aug-18											
EB_1750	Laying Public Lighting duct	3d	30-May-18 A	25-Aug-18	Laying Public Lighting duct											
EB_1780	Erect Sign Gantry Steel Supports and Sign Gantry Beam across VPR and IEC E/B	4d	29-Jul-18	01-Aug-18	Erect Sign Gantry Steel Supports and Sign Gantry Beam across VPR and IEC E/B											
EB_1790	Installation of E & M at Sign Gantry (night work)	1d	02-Aug-18	02-Aug-18	Installation of E & M at Sign Gantry (night work)											
EB_1760	Connection of Public Lighting by HyD (Lighting)	2d	26-Aug-18	27-Aug-18	Connection of Public Lighting by HyD (Lighting)											
Minor Reinstatement Works for Central Median of IEC & Footbridge					6d 02-Aug-18 07-Aug-18											
EB_1800	Reconstruction of central divider (6m long, night work)	6d	02-Aug-18	07-Aug-18	Reconstruction of central divider (6m long, night work)											
EB_1810	Dismantlement of temp directional sign mounted on extg footbridge	1d	03-Aug-18	03-Aug-18	Dismantlement of temp directional sign mounted on extg footbridge											
Minor Reinstatement Works for Footpath					88d 18-May-18 A 01-Sep-18											
EB_1820	Place kerblines along VPR footpath	3d	18-May-18 A	23-Aug-18	Place kerblines along VPR footpath											
EB_1850	Backfilling subbase material	2d	27-May-18 A	29-May-18 A	subbase material											
EB_1830	Reinstatement of District Council Welcome Sign and opening plaque at Planter area	1d	24-Aug-18	24-Aug-18	Reinstatement of District Council Welcome Sign and opening plaque											
EB_1840	Re-provision of Tree	8d	25-Aug-18	01-Sep-18	Re-provision of Tree											
Minor Reinstatement Works for Bus Stop					56d 23-May-18 A 29-Aug-18											
EB_1860	Reinstatement of Permanent Bus Stop	5d	23-May-18 A	26-Jun-18 A	Reinstatement of Permanent Bus Stop											
EB_1870	Relocation of Bus Stop	1d	27-Jun-18 A	27-Jun-18 A	Relocation of Bus Stop											
EB_1880	Reinstate Planter(Previous Temporary Bus Stop)	5d	25-Aug-18	29-Aug-18	Reinstate Planter(Previous Temporary Bus Stop)											
Minor Reinstatement Works for Loop Detector					4d 04-Aug-18 07-Aug-18											
EB_1900	Construction of concrete plinth and fix counter housing for Loop Detector (ILDS)	3d	04-Aug-18	06-Aug-18	Construction of concrete plinth and fix counter housing for Loop Detector (ILDS)											
EB_1890	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)	1d	07-Aug-18	07-Aug-18	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)											
West Bound - Completion of Minor Outstanding / Remaining Works for KD9					95d 21-Jun-18 23-Sep-18											
Minor Reinstatement Works for Victoria Park					37d 07-Jul-18 12-Aug-18											
IECW_1500	Re-provision of Tree	32d	07-Jul-18	07-Aug-18	Re-provision of Tree											
IECW_1510	Laying Irrigation Main	10d	22-Jul-18	31-Jul-18	Laying Irrigation Main											
IECW_1520	Construct Landscape Footpath and Lightings	7d	06-Aug-18	12-Aug-18	Construct Landscape Footpath and Lightings											
Minor Reinstatement Works in IEC West Bound					95d 21-Jun-18 23-Sep-18											
IECW_1600	Replacement of new movement joint at IEC W/B (Sun midnight only)	8d	21-Jun-18	28-Jun-18	Replacement of new movement joint at IEC W/B (Sun midnight only)											
IECW_1610	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)	57d	29-Jun-18	24-Aug-18	Repairing of extg conc deck surface after milling of temp asphalt											
IECW_1640	Erection of new precast concrete panels (12 nos.) at abutment M facing to VPR	2d	25-Aug-18	26-Aug-18	Erection of new precast concrete panels (12 nos.) at abutment M											
IECW_1620	Repairing of concrete defects on extg concrete deck and abutment M	30d	25-Aug-18	23-Sep-18	Repairing of concrete defects on extg concrete deck and abutment M											
Works in Victoria Park (KD4, KD5, KD9)					169d 01-Mar-18 A 07-Aug-18											
Re-Provisioning Works					169d 01-Mar-18 A 07-Aug-18											
Nursery Compound					169d 01-Mar-18 A 07-Aug-18											
Nursery compound					169d 01-Mar-18 A 07-Aug-18											
ABWF					27d 05-Apr-18 A 07-Aug-18											
Metal Fence					27d 05-Apr-18 A 07-Aug-18											
VP_NC_1820	Installation	30d	05-Apr-18 A	07-Aug-18	Installation											
Fire Services					14d 21-Jun-18 07-Jul-18											
VP_NC_2030	FS inspection	14d	21-Jun-18	07-Jul-18	FS inspection											
Plumbing and Flushing Water Supplies					14d 21-Jun-18 07-Jul-18											
VP_NC_2100	WSD Inspection	14d	21-Jun-18	07-Jul-18	WSD Inspection											
External Works Aside Nursery Compound					56d 01-Mar-18 A 14-Jul-18											
External Works Around Nursery Compound					56d 01-Mar-18 A 14-Jul-18											

Activity ID	Activity Name	Original Duration	Start	Finish	2018											
					Jun			Jul			Aug			Sep		
					1	2	3	4	5	6	7	8	9	10	11	12
VP_NC_2250	Reinstatement of Existing Boundary Fence Wall Around Nursery Compound	45d	01-Mar-18 A	26-May-18 A	Existing Boundary Fence Wall Around Nursery Compound											
VP_NC_2260	EVA Construction	15d	28-May-18 A	14-Jul-18	EVA Construction											
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks		390d	08-Aug-18	01-Sep-19												
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)		365d	08-Aug-18	07-Aug-19												
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365d	08-Aug-18	07-Aug-19												
KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH>500mm)		365d	02-Sep-18	01-Sep-19												
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365d	02-Sep-18	01-Sep-19												
KD18 - Section 11: Transplanted Trees DBH>500mm in Portion VA and XII		365d	08-Aug-18	07-Aug-19												
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365d	08-Aug-18	07-Aug-19												
KD10 - Preservation and Protection of Trees		1088d	21-Mar-13 A	27-Sep-18												
PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	27-Sep-18												
KD15 & KD8 - Mooring Components Upkeep (CBTS and ATS)		979d	15-May-14 A	21-Jun-18												
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	21-Jun-18	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS											
