

Page 1 of 4 CEDD CONTRACT HK/2009/02 3 MONTHS ROLLING PROGRAMME OF WORKS PROGRAMME REVIEWED 8 AUG 2018 (DD 7-9-18) **EXCAVATION TWCR4 AND CONSTRUCTION OF WCR4 EXCAVATE TWCR4 AND INSTALL SEAWALL** 10 10 30-Oct-18 08-Nov-18 32 HK Working Day TRANSPORT OF P5 FILL MATERIAL A1000 TRANSPORT OF P5 FILL MATERIAL TO P34 MARINE EXCAVATION WEST SIDE EXC FOR G400 (1600M3) & 0.5TARMOUR WEST SIDE EXC FOR G400 (1600M3) 8 0.5TARMOUR, WEST SIDE EXC FOR G400 (1600N A1030 20 07-Sep-18* 26-Sep-18 7-Day Workweek-ARRIVAL OF G400 A1040 ARRIVAL OF G400 17-Sep-18 17-Sep-18 143 7-Day Workweek-1 ARRIVAL OF ARMOUR A1050 ARRIVAL OF ARMOUR 21-Sep-18 22-Sep-18 134 HK Working Day **CUTTING D-WALL** EAST SIDE CORE HOLES 01-Sep-18 A 07-Sep-18 7-Day Workweek-EAST SIDE CORE HOLES A1080 WEST SIDE CORE HOLES A1090 WEST SIDE CORE HOLES 05-Sep-18 A 7-Day Workweek-5 12-Sep-18 16 A1100 20 VERTICAL CUT 05-Sep-18 A 11-Sep-18 13 7-Day Workweek-1 HÓRIZONTÁL CUT A1110 HORIZONTAL CUT 20 20 07-Sep-18 26-Sep-18 7-Day Workweek-REMOVAL OF D-WALL A1120 REMOVAL OF D-WALL 20 20 07-Sep-18 26-Sep-18 7-Day Workweek-1 **INSTALL SEAWALL** MANUFACTURE OF SEAWALL BLOCK MANUFACTURE OF SEAWALL BLOCK 27-Jul-18 A MANUFACTURE OF SEAWALL BLOCK A1125 43 19-Oct-18 40 86 7-Day Workweek-1 MANUFACTURE OF FACING STONE A1127 MANUFACTURE OF FACING STONE 15 15 20-Oct-18 03-Nov-18 103 7-Day Workweek-1 1ST DELIVERY 1 1ST DELIVERY A1130 13-Sep-18* 19 7-Day Workweek-13-Sep-18 A1140 2ND DELIVERY 06-Oct-18* 06-Oct-18 7-Day Workweek-1 2ND DELIVERY 3RD DELIVERY A1150 3RD DELIVERY 17 12-Oct-18* 12-Oct-18 7-Day Workweek-A1160 4TH DELIVERY 19-Oct-18 4TH DEL VERY 19-Oct-18* 7-Day Workweek-5TH DELWERY A1170 5TH DELIVERY 27-Oct-18* 27-Oct-18 7-Day Workweek-6TH DELIVERY 6TH DELIVERY 02-Nov-18* 7-Day Workweek-1 7TH DELIVERY A1190 7TH DELIVERY 09-Nov-18* 09-Nov-18 7-Day Workweek-1 A1200 8TH DELIVERY - ► 8TH DELIVERY 15-Nov-18* 15-Nov-18 14 7-Day Workweek-1 INSTALL AST SIDE SEAWALL BLOC MOUNTING ROCK BEDDING MOUNTING ROCK BEDDING 19-Sep-18 24-Sep-18 A1210 7-Day Workweek-LEVELLING A1220 LEVELLING 25-Sep-18 27-Sep-18 19 7-Day Workweek-1 —■ М9 BLOCK A1230 M9 BLOCK 2 2 28-Sep-18 29-Sep-18 19 7-Day Workweek-A1240 LEVELLING LEVELLING 30-Sep-18 04-Oct-18 19 7-Day Workweek-1 IST LAYER OF BLOCK A1250 1ST LAYER OF BLOCK 05-Oct-18 08-Oct-18 19 7-Day Workweek-2ND LAYER A1260 2ND LAYER 09-Oct-18 11-Oct-18 7-Day Workweek-1 ₩ BRD LAYER A1270 3RD LAYER 3 12-Oct-18 14-Oct-18 19 7-Day Workweek-A1280 4TH LAYER 19 4TH LAYER 15-Oct-18 17-Oct-18 7-Day Workweek-► 5TH LAYE A1290 5TH LAYER 3 18-Oct-18 20-Oct-18 19 7-Day Workweek-1 6TH LAYER 6TH LAYER A1300 3 19 7-Day Workweek-21-Oct-18 23-Oct-18 TYPE A A1310 TYPE A 24-Oct-18 27-Oct-18 19 7-Day Workweek-1 GEOTEXTILE AND FILTER GEOTEXTILE AND FILTER A1320 4 28-Oct-18 31-Oct-18 19 7-Day Workweek-A1330 B/F SOIL (5000m3) 01-Nov-18 08-Nov-18 19 7-Day Workweek-1 B/F SOIL (5000m3) PLACE CONC CUBES AND PLACE CONC CUBES AND PARTLY B/F TO +3.5mPD (1000m3) A1340 09-Nov-18 14-Nov-18 19 7-Day Workweek-WEST SIDE SEAWALL BLOCK INSTALL MOUNTING ROCK BEDDING TYPE 12A & 12B MOUNTING ROCK BEDDING TYPE 12A & 12B, MOUNTING ROCK BEDD A1370 15 15 27-Sep-18 11-Oct-18 0 7-Day Workweek-1 A1380 LEVELLING 12-Oct-18 15-Oct-18 📺 LEVELLING, LEVELLING 7-Day Workweek-M9 BLOCK, M9 BLÖCK A1390 M9 BLOCK 16-Oct-18 18-Oct-18 7-Day Workweek-1 LEVELLING, LEVELLING LEVELLING A1400 19-Oct-18 25-Oct-18 7-Day Workweek-A1410 1ST LAYER OF BLOCK 26-Oct-18 7-Day Workweek-1 1ST LAYER OF BLOCK, 1ST LAYER OF BLOCK 31-Oct-18 2ND LAYER, 2ND LAYER A1420 2ND LAYER 5 01-Nov-18 05-Nov-18 7-Day Workweek-A1430 3RD LAYER 3RD LAYER, 3RD LAYER 06-Nov-18 7-Day Workweek-1 4TH LAYER, 4TH LAYER A1440 4TH LAYER 11-Nov-18 15-Nov-18 7-Day Workweek-5TH LAYER, 5TH LA A1450 5TH LAYER 16-Nov-18 7-Day Workweek-1 6TH LAYER, 6TH A1460 6TH LAYER 3 3 20-Nov-18 22-Nov-18 7-Day Workweek-1 TYPEA, TY TYPE A 23-Nov-18 26-Nov-18 7-Day Workweek-FILTER A1480 FILTER 4 27-Nov-18 30-Nov-18 7-Day Workweek-1 A1490 B/F TO +2.8mPD 6 01-Dec-18 06-Dec-18 0 7-Day Workweek-1 Revision Checked Approved Milestone **CHUN WO - CRGL** CEDD CONTRACT NO. HK/2009/02 Critical Milestones **JOINT VENTURE** Current Works

Critical Works Remaining Level of..

WD II - Central Wanchai Bypass at Wan Chai East (Contra	ct 2)
3-MONTH ROLLING PROGRAMME (data date 07-Sep-18	3)

Date	Revision	Checked	Approved

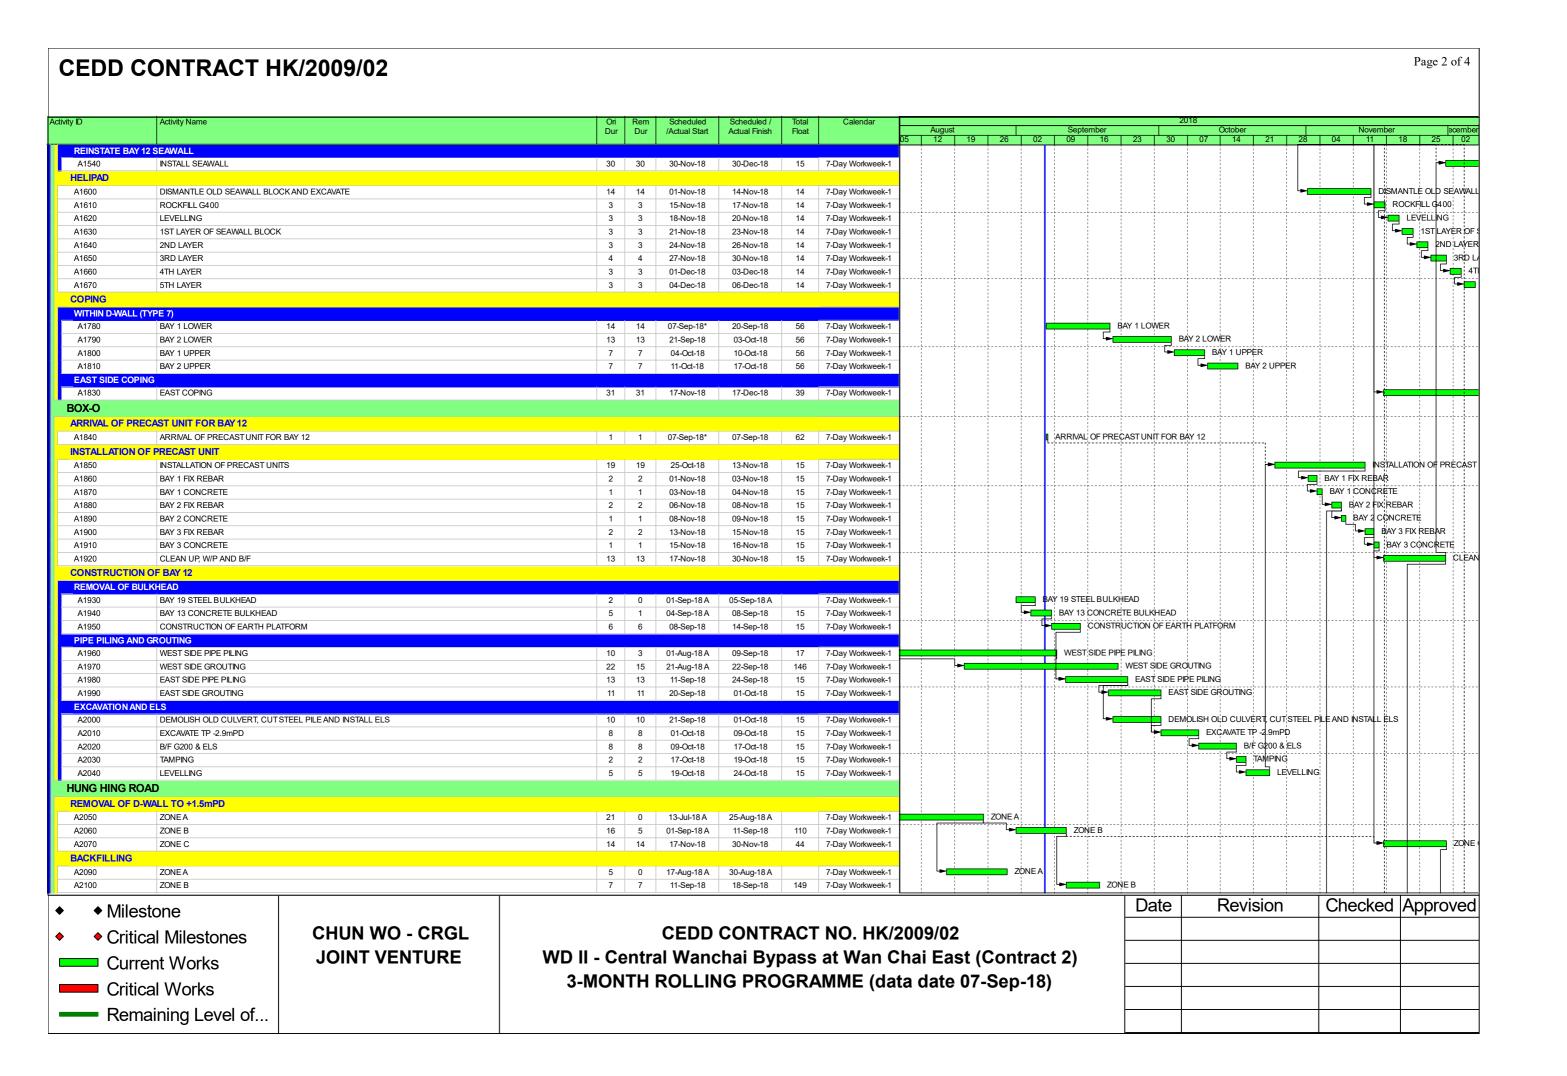

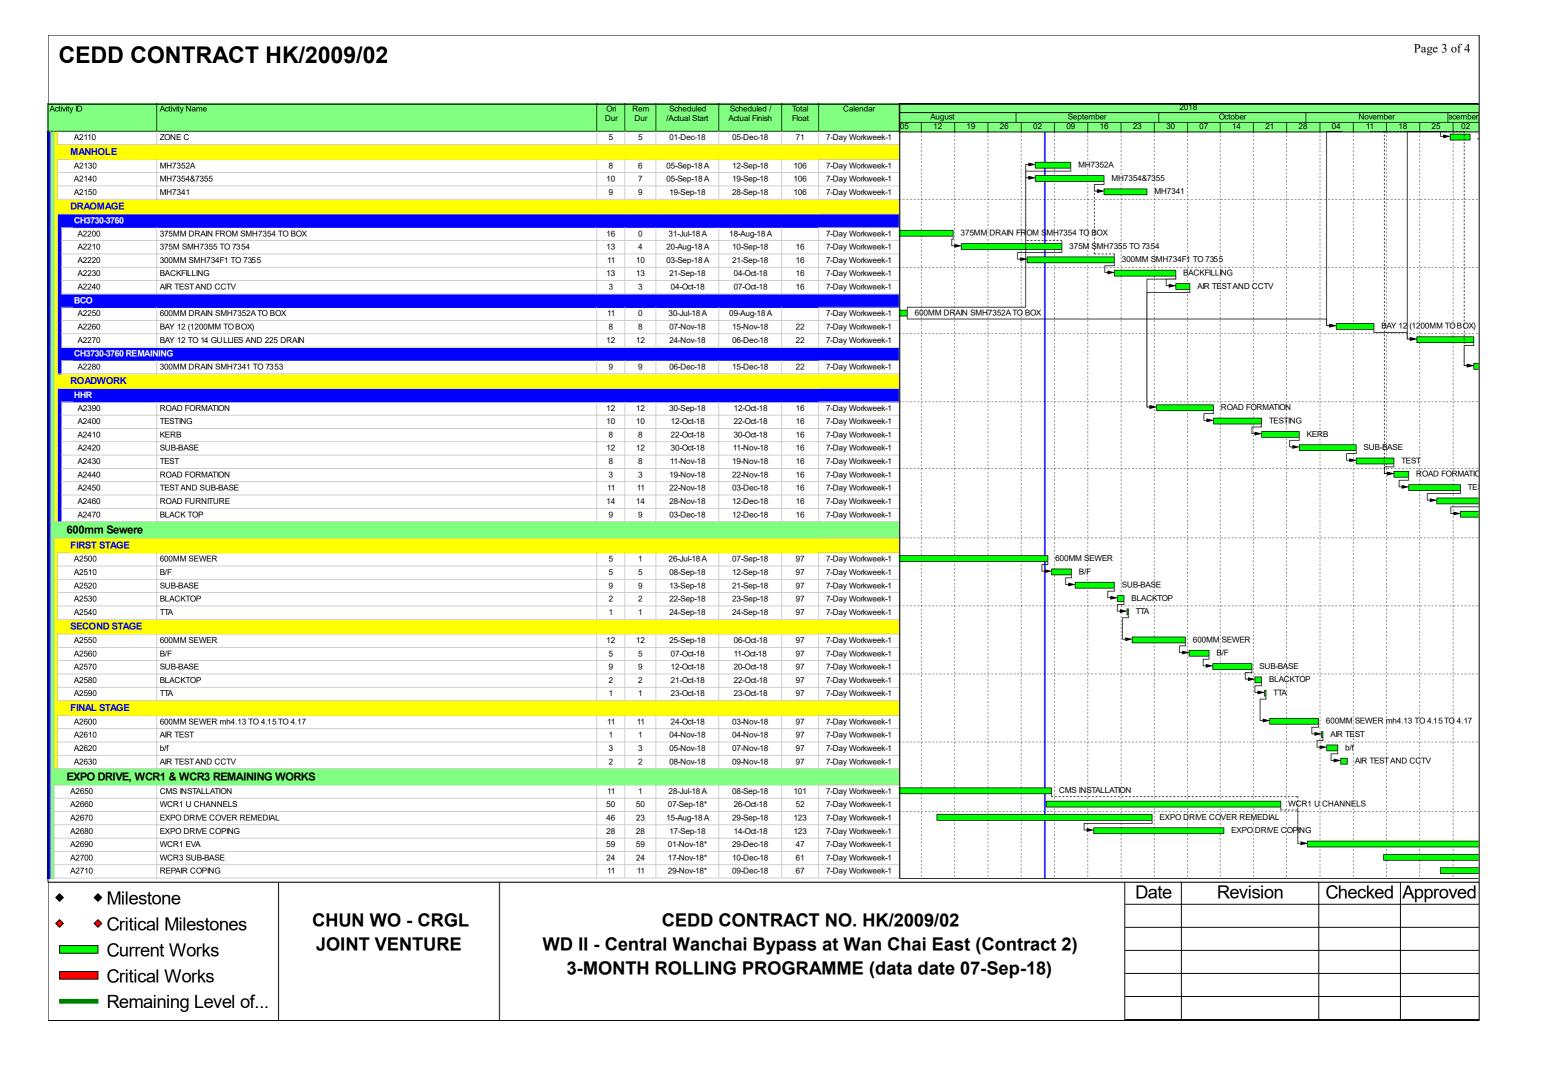

CEDDC	ONTRACT HK/2009/02
	UNIRAGI MN/ZUU9/UZ


Page 4 of 4

Activity ID	Activity Name	Ori	Rem	Scheduled	Scheduled /	Total	Calendar									201	8							
		Dur	Dur	/Actual Start	Actual Finish	Float			Augus	t			Sept	ember			С	october				November		ecember
								05	12	19	26	02	09	16	23	30	07	14	21	28	04	11 18	25	02
A2720	WCR1&3 ARMOUR SLOPE PROFILE	31	31	01-Dec-18*	31-Dec-18	45	7-Day Workweek-1																	
A2740	REINSTATE WCR3 EXIT	23	23	24-Sep-18*	16-Oct-18	121	7-Day Workweek-1	1					i				-	RE	NSTATE V	VCR3 EXT	г		į	
A2750	WCR3 FENCING	23	23	09-Nov-18*	01-Dec-18	75	7-Day Workweek-1	1							:		1		:		<u></u>	1	_	WCR

•	◆ Milestone
•	Critical Milestones
	Current Works
	Critical Works
_	Remaining Level of

CHUN WO - CRGL JOINT VENTURE CEDD CONTRACT NO. HK/2009/02 WD II - Central Wanchai Bypass at Wan Chai East (Contract 2) 3-MONTH ROLLING PROGRAMME (data date 07-Sep-18)

Date	Revision	Checked	Approved



CONTRACTOR'S SUBMISSION

Contract No. HK/2009/02 Wan Chai Development Phase II Central – Wan Chai Bypass at Wan Chai East

То	: AECOM Asia Co. Ltd.	Attn : M	s Gloria Tang	
CS Title CS Ref.	Three-Month Rolling Pro : CWCRGLJV/573/CS/PR/	gramme (Version Date: 1 Fel S-0295 Revision K	bruary 2019)	
Status	☑-1 st submission date	9 February 2018		
Type of Submission	: □Design □Drawings □Safety □Environ.	☐Method Statement ☑Programme / Progress	□Materials □Survey	□QA / QC □Others
Specification Ref.	; N.A.			
Drawing Ref.	: N.A.			
Submission Details	: ⊠Please refer to attachm	ent ⊠Please see below		
Purpose of Submission	on : ⊠For review and appro	val □For record purpose	es:	
Name : Paul Yu	Vo – CRGL Joint Venture J Manager			


c.c. AACL - HO

Issue 02



Wan Chai Development Phase II - East Central - Wan Chai Bypass at Wan Chai Centract: HK/2009/02


as in this version date 21/1/19

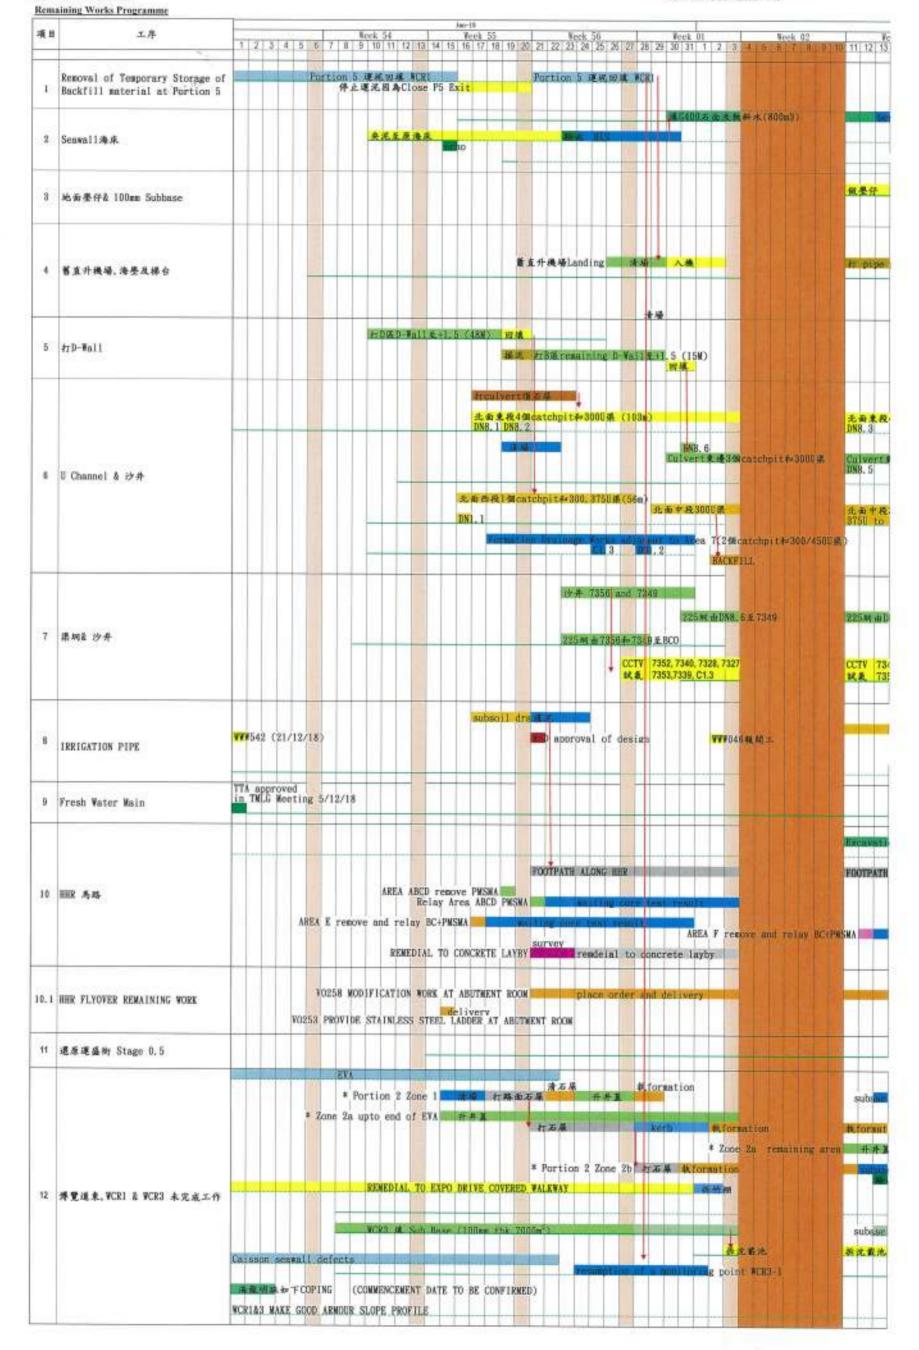




Wan Chai Development Phase II - East Central - Wan Chai Bypass at Wan Chai Contract: HK/2009/02

Barralaina Wash B

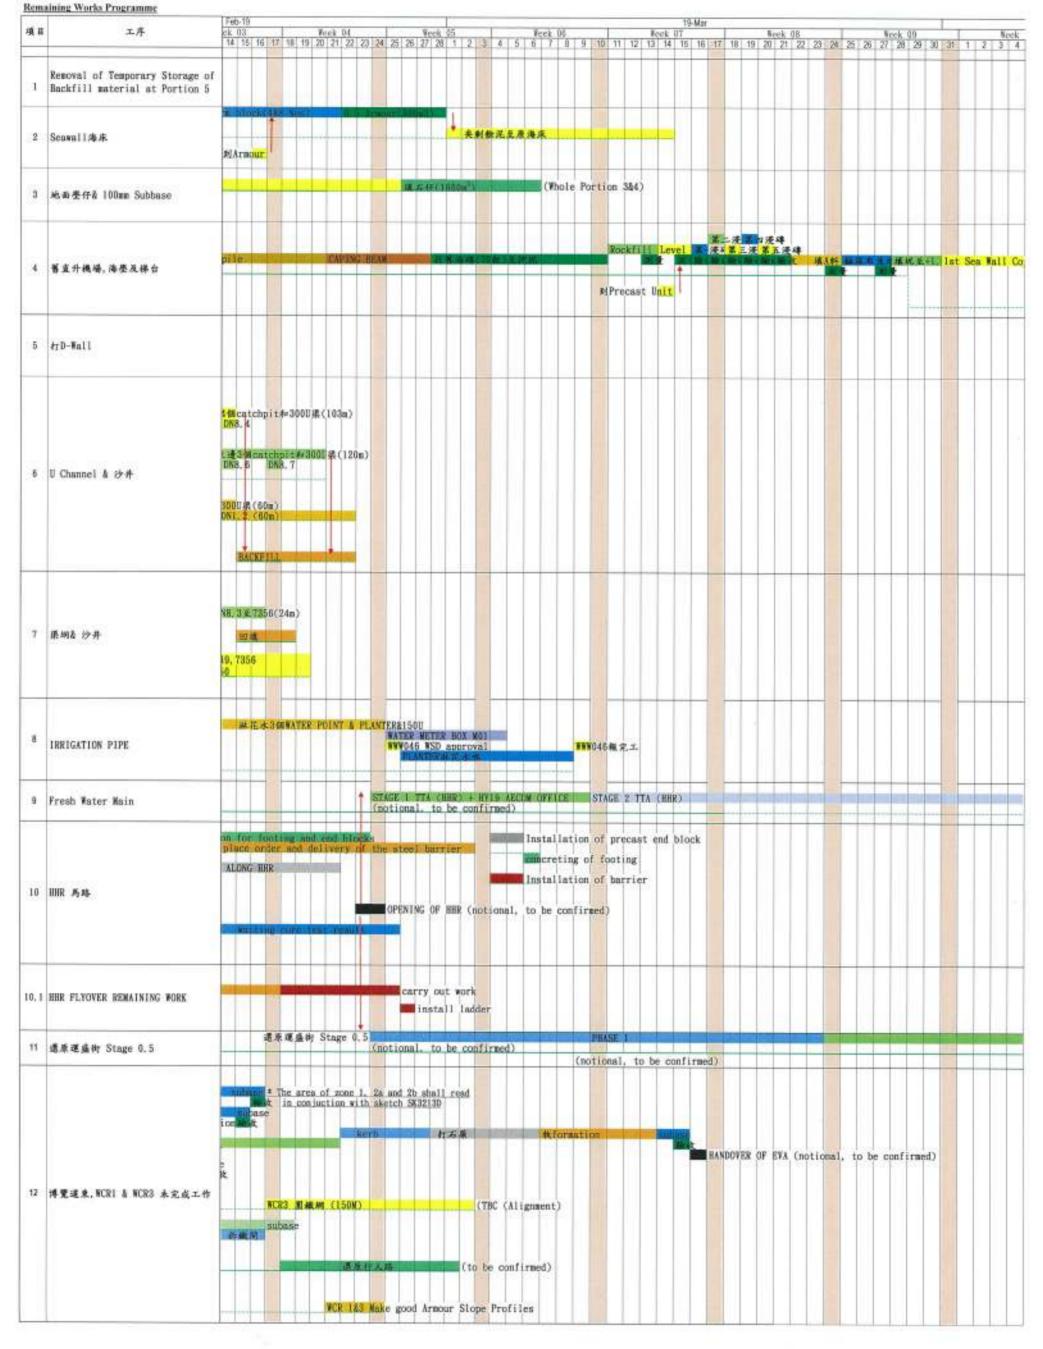




Wan Chai Development Phase II - East Cer Co Re

entral - Wa	n Chai Bypass at Wan	Chal
ontract: HK	/2009/02	
emaining W	orks Programme	
ğπ	工序	1

J. L. L. L.	aining Works Programme	1		15-Apr.	- 1		Mar
項目	工序	5 6 7	Steek II 7 8 9 10 11 12 13 18	Week 2 Week 15 15 16 17 18 19 20 21 22 23 24 25	13 Reek 14 26 27 28 29 30 1 2 3	#cek 15 4 5 6 7 8 9 10 11 12	May Neck 10 Neck 17 13 14 15 16 17 18 19 20 21 22 23 24 25
1	Removal of Temperary Storage of Backfill material at Portion 5						
2	Seawall海床						
3	地看墨仔& 100mm Subbase						
4	菲直升機場。海麥及梯台	ping 2nd Copi	mg 維持対置 を成	安徽Fender Gut dise nile 田林文+2,8 建苯丙基基金 株子() ter			
5	ér D-Wall						
Б	U Channel & 沙井						
7	混烟& 沙科						
8	IRRIGATION PIPE						
9	Fresh Water Main						
10	HHR 馬埠						
. 1	HHR FLYOVER REMAINING WORK						
11	通原運盛物 Stage 0.5	PHASE 2			PHASE/3		
12	博覽道東, WCRI 名 WCRS 未完成工作						



Wan Chai Development Phase II - East Central - Wan Chai Bypass at Wan Chai Contract: HK/2009/02

Remaining Works Programme

項目	nining Works Programme 工序			aut.	1				TR	377		-			. 0.5	An	0			4.100					_			
押品	工件	27 2	29 29	30	31	1 2	3	4	5 5	7	8	9	10 11	Yeel	3 16	15	16 1	7 18	19 19	20 3	1 22	23	24	25	76 Z	k 21 27 7	28 2	9 30
1	Removal of Temporary Storage of Backfill material at Portion 5																											
2.	Scawall 海承																											
3	地面是行车 100mm Subbase																											
4:	省直升機場,海祭及保台																											
5	\$TD-¥m11																											
6	U Channel & 沙州																											
7	摄明在 沙井																											
8	PERIGATION PIPE																											
9	Fresh Water Main																											
10	删除 為路																											
10, 1	HHR FLYOVER REMAINING WORK					Ĭ																						
11	通原連盛街 Stage 0.5																											
12	博覽道東。WCR1 & WCR3 未完成工作																											

by by ID	Activity Name	Remaining Dur	Early Start	Early Finish	Arthurby S.				Centr	Wan	D Con Chai I an Cha	Develo ai Byp	opme	nt Ph	ase II	i Wes	t						20.00	Pa	ge:1/7		
120000	Revised Works Programme Rev.12.0(DD 20 No	CALADA CALADA CALADA	-chioarus	and their	Activity % Complete	Jan	Feb	Mar	Арг	May	Jun 20		Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr		2019 Jun	Jul	Aug	Sep	Oct
	nd Milestone Dates	vember 20	17)	West of																			10				
	Norks Completion (Included Not Granted EOT Enti	Hement of T	he Contractor)																								
KD10840	Completion of Section IIIA	n	ine contraction	08-Sep-18*	0%																						
KD10860	Complection of Section IV	0		30-Aug-18*	0%			1																			
KD10880	Completion of Section V	0		26-Sep-18*	0%																						
KD11010	Completion of Section VII	0		14-Sep-18*	0%																						
KD11020	Completion of Section VIII	0		21-Sep-18*	0%												9										
KD11040	Completion of Section IX	0		21-Sep-19*	0%																						
KD11060	Completion of Section X	0		21-Sep-18*	0%																					•	
Planned Sec	tions of Works Completion			Here des		+																					
KD10080	Planned Section IIIA Completion - Road A2,A4, A5	0		08-Sep-18	0%																						
KD10100	Planned Section IV Completion - Slip Road 3	0		30-Aug-18	0%														1								
KD10140	Planned Section V Completion - Remaining At-Grade Road	0		26-Sep-18	0%																			1			
KD10280	Planned Section VII Completion - Remainder Works	0		14-Sep-18	0%	1																					
KD10300	Planned Section VIII Completion - Landscape Softwork	0		21-Sep-18	0%	1																					
KD10320	Planned Section IX Completion - Establishment Works	0		21-Sep-19	0%			1																			
KD10340	Planned Section X Completion - Tree Protection & Preservation	0		21-Sep-18	0%									*					İ							•	
	d Reclamation Construction																										
Zone CRIII					100																						
Seawall Cons	struction - Zone CRIII																										
Zone CRIII S	eawall- 2nd Stage																	1	1					1			
Seawort 2 S					aluth)								8						1					3			
MAR21371	Zone CRIII - seawall 2 & 12 - Backfilling remaining portion (type A, geotextile and filter)	0	19-Jan-18 A	27-Jan-18 A	100%	-							į					1			1						
Zone D																		1		i			-1				
	truction - Zone D																				1						
Seawall 10 &																		Ī			1						
MAR20630	Zone D - Seawall 10 & 11: Install remaining seawall block	14	20-Feb-18*	05-Mar-18	0%		F	-																			
MAR20650	Zone D - Seawall 10 & 11: Backfill Type A	7	06-Mar-18	12-Mar-18	0%																						
MAR20670	Zone D - Seawall 10 & 11: Lay geotextile and filter	7	13-Mar-18	19-Mar-18	0%			-					***************************************	***************************************		***********						***********			WWW.WSZA		
	ection Completion																	i			İ						
Construction		PRESENT											1					Ī									
	Road A2, A4 & A5																		1					1			
Roadwork &	Utilities - Section 1 (L1806 - L1801)																										
ata Date:	Current Milestone				930		0.500	(52)	4.00										Date			Chec	ked		Approv	ed	
)-Feb-18	Actual Work Critical Remaining Work Remaining Work Remaining Level of Effort				Up (Ref	dated to R	d Wo	orks 2 as	Prog of 20	Feb:	e Reurary	v.12 2018	3)						20-Feb-	-18 1	2						


Page: 2/7

rity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete			-			018				_							2019				
SIIIA10279c	Sec III A - section 1 carriageway - sewerage pipe from M/H	0	02-Jan-18 A	03-Feb-18 A	100%	Jan F	eb Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
SIIIA10293	8C to F88 (night time): construct sewerage pipe Sec III A - section 1 carriageway - sewerage pipe from M/H F8B - F8A (night time)	6	05-Feb-18 A	26-Feb-18	0%	_	-																			
SIIIA10294	Sec III A - section 1 carriageway - sewerage pipe from M/H F8A - F8	8	17-Jan-18 A	28-Feb-18	27.27%																					
SIIIA10295	Sec III A - carriageway - works prrior TTA stage 5: excavation and duct laying of TCSS and public lighting	7	18-Jan-18 A	27-Feb-18	0%																					
SIIIA10298	Sec III A - section 1 carriageway - works prifor TTA stage 5: road kerb	5	28-Feb-18	05-Mar-18	0%		-																			
SHIA10301	Sec III A - section 1 carriageway - works prrior TTA stage S: road formation	2	06-Mar-18	07-Mar-18	0%		1																			
SIIIA10302	Sec III A - section 1 carriageway - works prior TTA stage 5: laying asphalt	5	08-Mar-18	13-Mar-18	0%		-																			
SIIIA10303	Sec III A - section 1 carriageway - works prrior TTA stage 5: road marking & preparation works	3	14-Mar-18	16-Mar-18	0%																					
SIIIA10310	Sec III A - section 1 carriageway - TTA stage 5: Implementation of TTA Stage 5	1	17-Mar-18	17-Mar-18	0%		Y																			
SIIIA10310a	Sec III A - section 1 carriageway - TTA stage 5: remaining sewerage pipe for N/H F8A - M/H F8	12	19-Mar-18	04-Apr-18	0%		=	-																		
SIIIA10310b	Sec III A - section 1 carriageway - TTA stage 5: remaining sewerage pipe for N/H F8A - M/H F8B	18	06-Apr-18	26-Apr-18	0%		***************************************	-		in reterented		C11111111111														
SIIIA10310c	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road- remove sheetpile at U-trough west	5	19-Mar-18	23-Mar-18	0%	1 9																				
SIIIA10310d		21	24-Mar-18	21-Apr-18	0%																					
SIIIA10310e	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road -construct upstand wall above Dwall	25	23-Apr-18	23-May-18	0%												1									
SIIIA10310f	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - roadside barrier	14	24-May-18	08-Jun-18	0%				-																	
SIIIA10310g	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - road formation	7	09-Jun-18	16-Jun-18	0%																					
SIIIA10310h	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - laying asphalt with transition slab	14	19-Jun-18	05-Jul-18	0%																					
SIIIA10312	Sec III A - roadwork and utities section 1 carriageway - Drainage works (12202 - 12201)	15	19-Mar-18	09-Apr-18	0%		-																			
SIIIA10312a	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L1805 - L1801)	15	10-Apr-18	26-Apr-18	0%		į	-	I .																	
SIIIA10312b	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L1805-1807)	12	27-Apr-18	11-May-18	0%																					
SIIIA10313	Sec III A - roadwork and utilities section 1 carriageway - gully pipe (L1807 - L1801)	14	07-May-18	23-May-18	0%																					
SIIIA10320	Sec III A - roadwork and utilities section 1 carriageway - fresh watermain	7	24-May-18	31-May-18	0%				-																	
SIIIA10340	Sec III A - roadwork and utilities section 1 carriageway - utilities: HEC (80m) along carriageway	14	01-Jun-18	16-Jun-18	0%																					
SIIIA10360	Sec III A - roadwork and utilities section 1 carriageway - road kerb & formation	14	19-Jun-18	05-Jul-18	0%					-													- 1			
SIIIA10400	Sec III A - roadwork and utilities section 1 carriageway - black top	7	06-Jul-18	13-Jul-18	0%		1	1			=															
SIIIA10420	Sec III A - Implementation of TTA Stage 7P (Closure of U-turn at Expo Drive)	1	14-Jul-18	14-Jul-18	0%						1															
SIIIA10440	Sec III A - roadwork and utilities section 1 carriageway : breaking existing asphalt	10	16-Jul-18	26-Jul-18	0%																					
SIIIA10460	Sec III A - roadwork and utilities section 1 carriageway: road kerb and formation	14	27-Jul-18	11-Aug-18	0%												3									
SIIIA10480	Sec III A - roadwork and utilities section 1 carriageway : black top	10	13-Aug-18	23-Aug-18	0%			1				1000														
SIIIA10500	Sec III A - roadwork and utilities section 1 carriageway : roadmarking and road furniture	14	24-Aug-18	08-Sep-18	096			1	1																	
Roadwork &	Utilities - Section 2 (L1810 - L1807)																						i			
SIIIA12590	Sec III A - roadwork and utilities section 2 carriageway - black top	0	20-Jan-18 A	27-Jan-18 A	100%	-																				
Roadwork &	Utilities - Section 3 (L1808 - L1102)																	İ								
SIIIA12770	Sec III A - roadwork and utilities section 3 carriageway - utilities: HEC ducting (60m) & crossroad duct (PCCW & HGC)	0	20-Jan-18 A	07-Feb-18 A	100%			1																		
SIIIA12790	Sec III A - roadwork and utilities section 3 carriageway - road kerb & formation	17	08-Feb-18 A	10-Mar-18	0%	-		1																		
SIIIA12810	Sec III A - roadwork and utilities section 3 carriageway - black top	7	12-Mar-18	19-Mar-18	0%						2001120011200														''''''''''''''''''''''''''''''''''''') (min) (m
Roadwork &	Utilities - Section 6 (L1102 - L1411)																									
SIIIA13399	Sec III A - roadwork and utilities section 6 carriageway - gully pipe (L1101 -L1102)	0	12-Jan-18 A	26-Jan-18 A	100%																					
SIIIA13444	Sec III A - roadwork and utities section 6 carriageway - watermain (road crossing)	0	27-Jan-18 A	03-Feb-18 A	100%	-												1					1			
SIIIA13445	Sec III A - roadwork and utities section 6 carriageway - utilities; crossed duct(HEC , HGC, PCCW)	13	05-Feb-18 A	06-Mar-18	0%	-																	-			

Page: 3 / 7

N/ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % I	_					raii Cii	018											50.05				
	Statement	771111111111111111111111111111111111111		SOURCE SOUR	Activity % Complete	Jan	Feb	Mac	Apr	May	Jun	-	Aug	Sep	Oct	Nov	Dec	Ján	Feb	Mar	Apr	May	2019 Jun	Jul	Aug	Sep	00
SIIIA13450	Sec III A - roadwork and utitites section 6 carniageway - road kerb & formation	18	07-Mar-18	27-Mar-18	0%												9										
SIIIA13470	Sec III A - roadwork and utilities section 6 carriageway - black top	7	28-Mar-18	09-Apr-18	0%															1							
SIIIA13570	Achievement of Section IIIA of the Works	0		08-Sep-18	0%																						
Section V - Re	maining At-Grade Road & Road P2				1															1							
Roadwork &	Utilities				-															1							
Section 1 (L1	504 - L1900)													1													
SV12456	Sec V-Roadwork & Utilities Section 1 - implementation of	0	20-Feb-18*	20-Feb-18	0%																						
SV12460	TTA stage 5E (dosure of slow lane at northbound of Expo Sec V - Roadwork & Utilities Section 1 - drinage works	15	20-Feb-18	08-Mar-18	0%														H	1							
SV12462	(L1902 - L1900) Sec V - Roadwork & Utilities Section 1 - guilly pipe (L1902 -	6	09-Mar-18	15-Mar-18	0%									1													
SV12464	L1900) Sec V - Roadwork & Utilities Section 1 - temp. reinstatement	14	16-Mar-18	04-Apr-18	0%																						
	to match with existing Expo Drive						ļ	1		ļ		(10-cyclessor							1	İ							12-15-00005
SV12466	Sec V - Section 1 - Modification to 2nd stage ITA (V.O. 50) : closure of northbound and maintain one lane at southbound	1	14-Jul-18	14-Jul-18	0%																						
5V12468	Sec V - Roadwork & Utilities Section 1 Carriageway - breaking existing asphalt	7	16-Jul-18	23-Jul-18	0%							-															
SV12490	Sec V - Roadwork & Utilities Section 1 Carriageway - Road kerb & formation	10	24-Jul-18	03-Aug-18	0%							_							Į.								
SV12520	Sec V - Roadwork & Utilities Section 1 Carriageway - Black top	7	04-Aug-18	11-Aug-18	0%		1																				
SV12522	Sec V - Section 1 - Implementation of TTA for road dosure of northbound and southbound of Expo Drive	3	13-Aug-18	15-Aug-18	0%								a														
SV12524	Sec V - Section 1 - Northbound & Southbound of Expo Drive : breaking asphalt	14	16-Aug-18	31-Aug-18	0%																						
SV12526	Sec V - Section 1 - Northbound & Southbound of Expo Drive : road kerb & formation	14	01-Sep-18	17-Sep-18	0%		0																				
SV12528	Sec V - Section 1 - Northbound & Southbound of Expo Drive :	7	18-Sep-18	26-Sep-18	0%		1																				
SV12570	Sec V - Roadwork & Utilities Section 1 footpath -	12	29-Dec-17 A	05-Mar-18	60%			-																			
SV12580	utilities:TCSS Sec V - Roadwork & Utilities Section I footpath - paving	29	06-Mar-18	12-Apr-18	0%		1		_																		
Section 2 (L1	block 510 - L1504)					-		-		-								+	-		-						
SV12624	Sec V - Roadwork & Utilities Section 1 Carriageway - road	0	04-Jan-18 A	30-Jan-18 A	100%		il													Ĭ.							
SV12626	kerb & formation Sec V - Roadwork & Utilities Section 1 Carriageway - black	13	31-Jan-18 A	06-Mar-18	0%			_																			
	top				555			I												l l							
SV12692	Sec. V - Roadwork & Utilities Section 2 footpath - U channel	11	17-Jan-18 A	03-Mar-18	21.43%																						
SV12695	Sec V - Roadwork & Utilities Section 2 footpath - Watermain	13	05-Mar-18	19-Mar-18	0%																						
SV12700	Sec V - Roadwork & Utilities Section 2 footpath - utilities: TCSS	16	20-Mar-18	11-Apr-18	0%		1	-											1	ľ							
SV12740	Sec V - Roadwork & Utilities Section 2 footpath - paving block	18	12-Apr-18	03-May-18	0%																						
Section 3 (Ca	Ilvert L - L1510)																										
SIV12860	Sec V - Roadwork & Utilities Section 3 footpath - Utilities: TCSS, HGC, PCCW)	30	16-Jan-18 A	26-Mar-18	11.76%			-											1	B							
SIV12880	Sec V - Roadwork & Utilities Section 3 footpath - Paving block	21	27-Mar-18	24-Apr-18	0%				_																		
Section 4 (K1	106 - Culvert L)					(-										Ť						ļ				ļ
SIV12282	Sec V - Roadwork & Utilities Section 4 Carriageway -	10	20-Feb-18	02-Mar-18	0%		-	ò						İ													
SIV12300	Drainage Works (L1311 - Culvert L, L1201 - Culvert L) Sec V - Roadwork & Utilities Section 4 Carriageway - Gully	7	03-Mar-18	10-Mar-18	0%		1																				
SIV12302	pipe (L1301 - Culvert L, L1201 - Culvert L) Sec V - Roadwork & Utilities Section 4 Carriageway -	6	12-Mar-18	17-Mar-18	0%		1																				
SIV12305	watermain Sec V - Roadwork & Utilities Section 4 Carriageway - utilities	. 7	19-Mar-18	26-Mar-18	0%																						
SIV12310	: cross road duct Sec V - Roadwork & Utilities Section 4 Carriageway - Road	15	27-Mar-18	17-Apr-18	0%			1											ļ								
	kerb & formation : between culvert K and culvert L				0.0000		1	1 1																			
SIV12320	Sec V - Roadwork & Utilities Section 4 Carriageway - Black top : between culvert K and culvert L	10	18-Apr-18	28-Apr-18	0%		*		-																		
SIV12340	Sec V - Roadwork & Utilities Section 4 Carriageway - Black top : at west of culvert K	7	20-Feb-18	27-Feb-18	0%														1								
SIV12422	Sec V - Roadwork & Utilities Section 4 footpath - Utilities : TCSS	20	20-Feb-18	14-Mar-18	0%														1								
SIV12440	Sec V - Roadwork & Utilities Section 4 footpath - Utilities : HGC & PCCW	8	15-Mar-18	23-Mar-18	0%																						


Page: 4/7

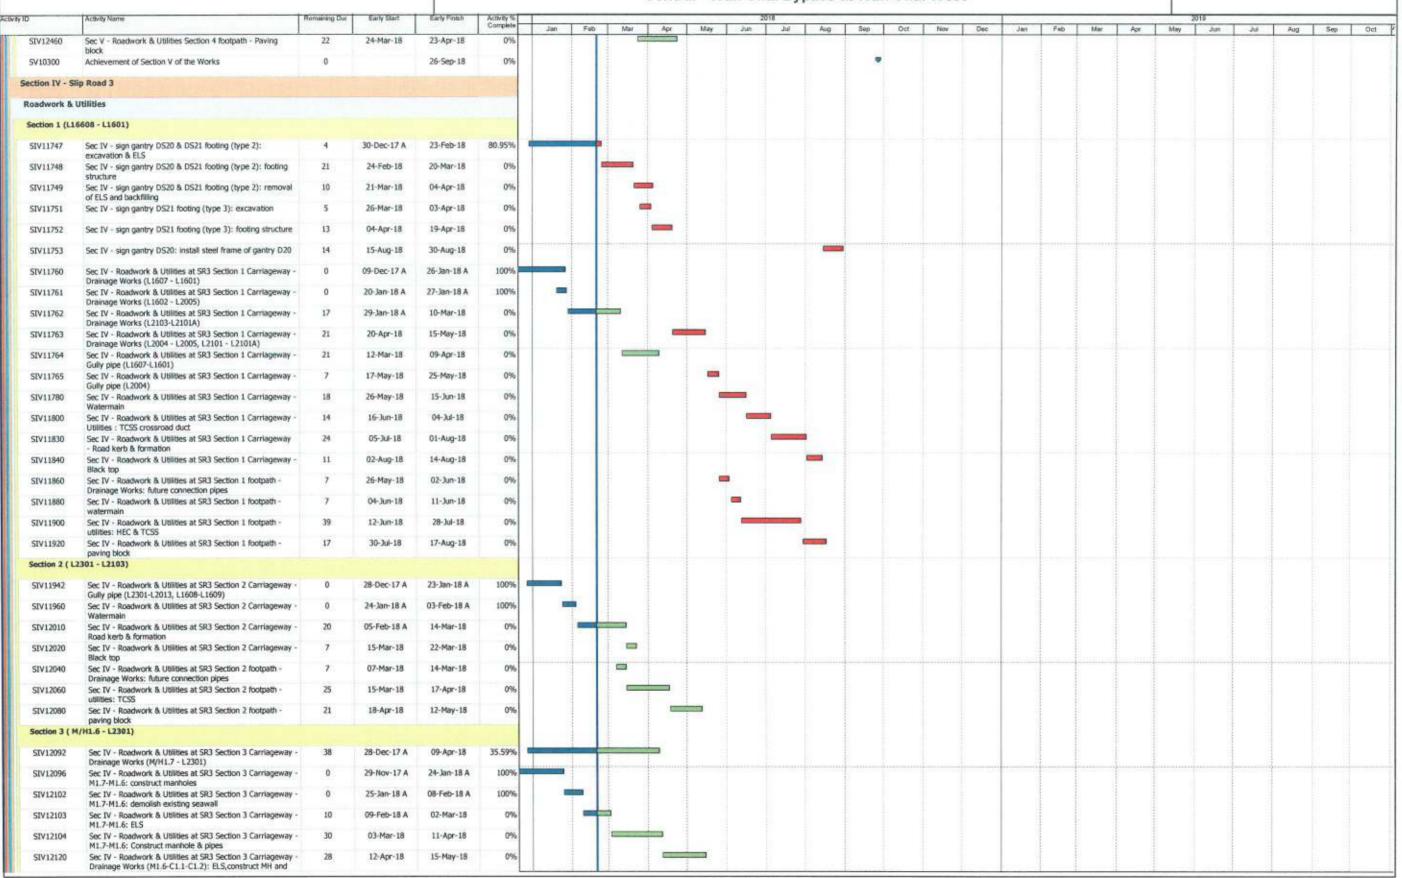

n	-	-	 . /	7	у.
P	aq	e	 14	1	

Vity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity %.	Central - Wan Chai Bypass at Wan Chai West				
WEIGHT	N. 17 (1.30)		Cong Story	Carly Fillian	Activity % Complete	Feb Mar Apr May Jun Jul Acig Sep Oct Nov Dec Jan Fab Mar Apr N	2019 May Jun	Jul	Aug	Sep Oc
SIV12121	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Drainage Works (M1.6-C1.1-C1.2): Backfilling & shift lane	6	16-May-18	23-May-18	0%		ay Jun	310	ma	sep Us
SIV12122	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Drainage Works (M1.6-C1.1-C1.2): Construct MH C1.2	5	24-May-18	29-May-18	0%					
SIV12140	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Gully pipe (M/H 1.7 - L2301)	32	10-Apr-18	17-May-18	0%			İ		
STV12150	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	14	18-May-18	04-Jun-18	0%					
SIV12155	Road kerb Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - formation	10	05-Jun-18	15-Jun-18	0%					
SIV12160	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Black top	7	16-Jun-18	25-Jun-18	0%					
SIV12170	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - Utilities: TCSS	21	10-May-18	04-Jun-18	0%					
SIV12180	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - U channel	10	05-Jun-18	15-Jun-18	0%					
SIV12220	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - Paving block	25	16-Jun-18	17-Jul-18	0%					
SIV12222	Achievement of Section IV of the Works	0		30-Aug-18	0%					
Section VII - Re	emainder Works							ļ		
Road & Draina	ge Works (Culvert L - M/H1.7, Adjacent to SR3)									
SVII11600	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway -	48	08-Jan-18 A	20-Apr-18	18.64%					
SVII11620	Drainage Works (Culvert L -MH1.7) Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway :	3	21-Apr-18	24-Apr-18	0%					
SVII11640	traffic diversion at Lung King Street Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway -	27	25-Apr-18	28-May-18	0%					
SVII11650	Gully pipe (Culvert L -MH1.7) Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway -	7	29-May-18	05-Jun-18	0%					
SVII11654	TCSS duct Sec TV - Roadwork & Utilities at SR3 Section 4 Carriageway -	14	06-Jun-18	22-Jun-18	0%					
SVII11660	road kerb & formation Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway -	6	23-Jun-18	29-Jun-18	0%					
SVII11680	Black top Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - U	14	29-May-18	13-Jun-18	0%					
SVII11700	channel Sec IV - Roadwork & Utilities at SR3 Section 4 footpath -	14	14-Jun-18	30-Jun-18	0%					
SVII11720	utilities: TCSS Sec IV - Roadwork & Utilities at SR3 Section 4 footpath -	14	03-Jul-18	18-Jul-18	0%					
Retaining Wall	paving block RW5 Construction									
SVII10660	Sec VII - Retaining Wall RW5 (bay 1) - construct base slab	22	20-Mar-18	18-Apr-18	0%					
SVII10680	and wall Sec VII - Retaining wall RW5 (bay 2) - construct base slab	22	19-Apr-18	15-May-18	0%		4 9			
SVII10800	and wall Sec VII - Retaining wall RW5 (bay 3) - construct base slab	22	20-Mar-18	18-Apr-18	0%					
SVII10820	and wall Sec VII - Retaining wall RW5 (bay 4) - construct base slab	22	19-Apr-18		0%					
SVII10860	and wall Sec VII - Retaining wall RW5 - curing, removal formwork		TO SECURE A SECURE	15-May-18	0000					
			16-May-18	25-May-18	0%					
Landing Steps										
Landing Steps	BSW13									
SVII10900	Sec VII - Landing steps (BSW13) - install vertical fender / step fender	15	15-May-18	01-Jun-18	0%		1			
SVII10920	Sec VII - Landing steps (BSW13) - install s.s. handrail / tactile / sign board / bollard	25	02-Jun-18	03-Jul-18	0%					
Landing Steps										
SVII10980	Sec VII - Landing steps (BSW4) - install vertical fender / step fender	15	20-Jun-18	07-Jul-18	0%					
SVII11000	Sec VII - Landing steps (BSW4) - Install s.s. handrall / tactile / sign board / bollard	25	09-Jul-18	06-Aug-18	0%					
Landing Steps										
SVII11060	Sec VII - Landing steps (BSW5) - install vertical fender / step	15	25-Jul-18	10-Aug-18	0%	 				
SVII11080	fender Sec VII - Landing steps (BSW5) - install s.s. handrail / tactile	25	11-Aug-18	08-Sep-18	0%					
Landing Steps	/ sign board / bollard BSW9									
SVII11140	Sec VII - Landing steps (BSW9) - install vertical fender / step	15	13-Jun-18	30-Jun-18	0%					
SVII11160	fender Sec VII - Landing steps (BSW9) - install s.s. handrail / factile	25	03-Jul-18	31-Jul-18	0%					
21111100	/ sign board / bollard		03-341-10	31-VW-19	U%			Ī		

Page: 6/7

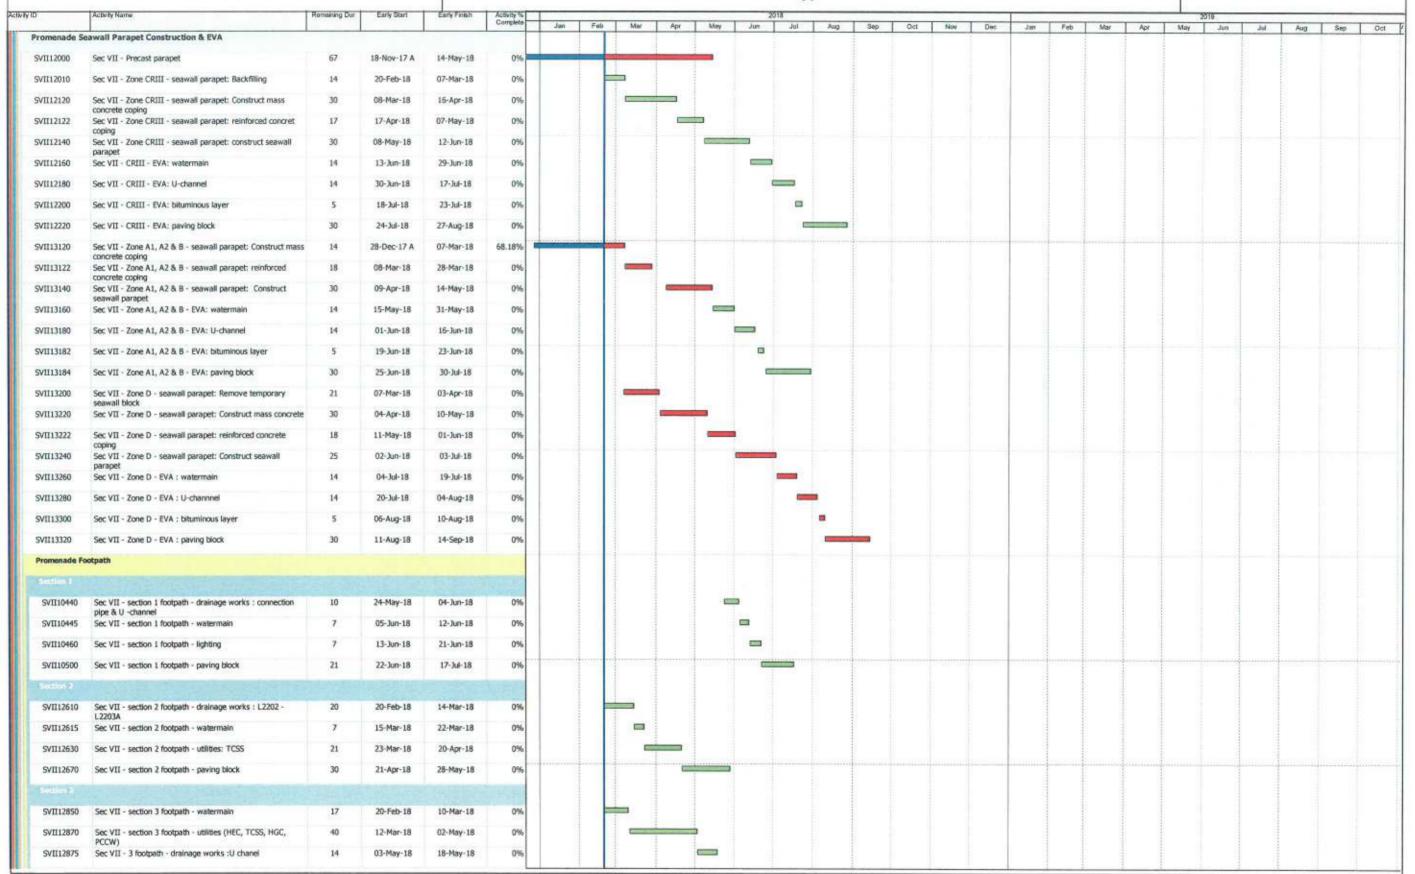

Page:7/7

