


Programme for Outstanding and Defective Works

ID	Task Name	Duration	Start	Finish	2019																															
					July 2019							August 2019							September 2019							October 2019										
					14	17	20	23	26	29	1	4	7	10	13	16	19	22	25	28	31	3	6	9	12	15	18	21	24	27	30	3	6	9	12	15
1	15. Reinstatement of Hung Hing Road and Wan Shing Street in Accordance to Hung Hing Road Traffic Diversion Reinstatement Stage 0.5 Scheme Under VO No. 257 on Hung Hing Road	248 days	Fri 1/3/19	Sun 3/11/19																																
2	Phase 1 (Completed)	41 days	Fri 1/3/19	Wed 10/4/19																																
55	Phase 2 (Completed)	41 days	Tue 2/4/19	Sun 12/5/19																																
169	Yacht Club (40m Long)	43 days	Fri 15/3/19	Fri 26/4/19																																
182	Triangle Island (40m Long)	28 days	Fri 31/5/19	Thu 27/6/19																																
194	Phase 3	144 days	Thu 13/6/19	Sun 3/11/19																																
195	Advacne Work	35 days	Thu 13/6/19	Wed 17/7/19																																
200	Construction of Road Kerb and Pavement (Portion 5)	23 days	Thu 18/7/19	Fri 9/8/19																																
201	TTA Implementation	1 day	Thu 18/7/19	Thu 18/7/19																																
202	Demolition of Concrete and Asphalt Pavement	4 days	Fri 19/7/19	Mon 22/7/19																																
203	Removal of Steel Plate	4 days	Tue 23/7/19	Fri 26/7/19																																
204	Installation of Kerb	2 days	Sat 27/7/19	Sun 28/7/19																																
205	Subbase Levelling	1 day	Mon 29/7/19	Mon 29/7/19																																
206	SRT for Sub-base	5 days	Tue 30/7/19	Sat 3/8/19																																
207	Concrete Laying	1 day	Sun 4/8/19	Sun 4/8/19																																
208	Concrete Curing	3 days	Mon 5/8/19	Wed 7/8/19																																
209	Existing Asphalt Patch Up Work at Water Ponding Area (Photo 3, 4 & 5, Figure 211) (Concurrent with ID 669)	2 days	Thu 8/8/19	Fri 9/8/19																																
210	Demolition of water ponding area	1 day	Thu 8/8/19	Thu 8/8/19																																
211	Patching Up with Asphalt layer	1 day	Fri 9/8/19	Fri 9/8/19																																
212	Construction of Road Kerb and Pavement (Portion 4)	30 days	Fri 2/8/19	Sat 31/8/19																																
213	TTA Implementation	1 day	Sat 10/8/19	Sat 10/8/19																																
214	Demolition of Concrete and Asphalt Pavement	4 days	Sun 11/8/19	Wed 14/8/19																																
215	Removal of Steel Plate	4 days	Thu 15/8/19	Sun 18/8/19																																
216	Installation of Kerb	1 day	Mon 19/8/19	Mon 19/8/19																																
217	Subbase Levelling	1 day	Tue 20/8/19	Tue 20/8/19																																
218	SRT for Sub-base	5 days	Wed 21/8/19	Sun 25/8/19																																
219	Concrete Laying	1 day	Mon 26/8/19	Mon 26/8/19																																
220	Concrete Curing	3 days	Tue 27/8/19	Thu 29/8/19																																
221	Existing Asphalt Patch Up Work at Water Ponding Area (Photo 1, Figure 212)	2 days	Fri 30/8/19	Sat 31/8/19																																
224	Repaving Works at Yacht Club (Photo 2, Figure 216-1), Same as	30 days	Fri 2/8/19	Sat 31/8/19																																
231	Construction of Trial Pit and Installation of decking (Portion 3)	21 days	Mon 2/9/19	Sun 22/9/19																																
232	TTA Implementation	1 day	Mon 2/9/19	Mon 2/9/19																																
233	Demolition of Concrete and Asphalt Pavement	4 days	Tue 3/9/19	Fri 6/9/19																																
234	Removal of Steel Plate and installation of ELS for waterpipe	4 days	Sat 7/9/19	Tue 10/9/19																																
235	Kerb Installation and installation of decking	2 days	Wed 11/9/19	Thu 12/9/19																																
236	Subbase Levelling	1 day	Fri 13/9/19	Fri 13/9/19																																
237	SRT for Sub-base	5 days	Sat 14/9/19	Wed 18/9/19																																
238	Concrete Laying	1 day	Thu 19/9/19	Thu 19/9/19																																
239	Concrete Curing	3 days	Fri 20/9/19	Sun 22/9/19																																
240	Construction of Road Kerb and Pavement (Portion 2)	21 days	Mon 23/9/19	Sun 13/10/19																																
249	Construction of Road Kerb and Pavement (Portion 1)	21 days	Mon 14/10/19	Sun 3/11/19																																
258	Phase 3.5 (Remaining Works for HHR0.5 Scheme & Cable Duct Laying)	69 days	Tue 14/5/19	Sun 21/7/19																																
259	Construction of Footpath at HHR (Up Birdge)	11 days	Fri 31/5/19	Mon 10/6/19																																

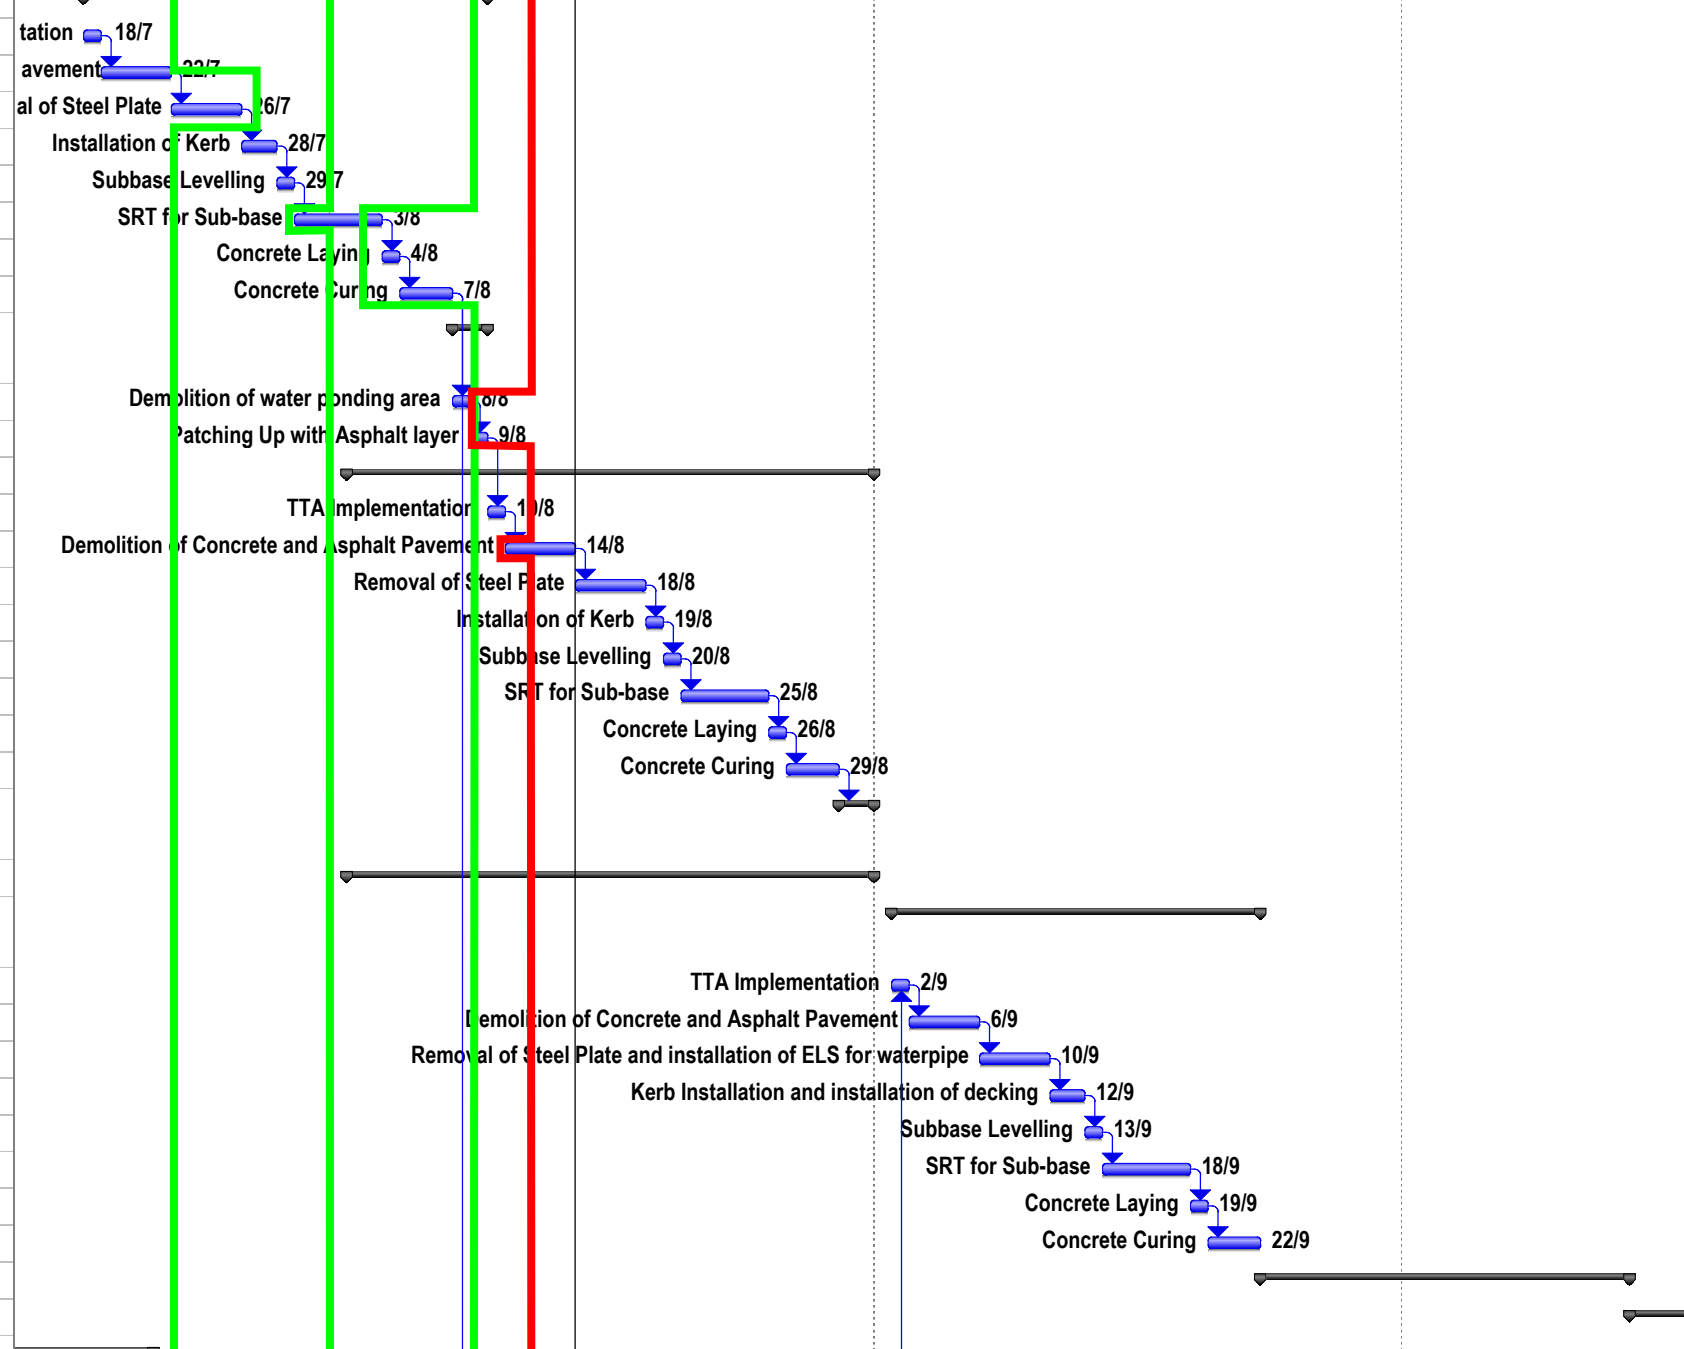

Programme for Outstanding and Defective Works

ID	Task Name	Duration	Start	Finish	Qtr 3, 2019																															
					July 2019							August 2019							September 2019							October 2019										
					14	17	20	23	26	29	1	4	7	10	13	16	19	22	25	28	31	3	6	9	12	15	18	21	24	27	30	3	6	9	12	15
435	Backfilling of Subbase Level and SRT	8 days	Tue 13/8/19	Tue 20/8/19																																
436	RB Laying	1 day	Wed 21/8/19	Wed 21/8/19																																
437	BC Laying	1 day	Thu 22/8/19	Thu 22/8/19																																
438	WC Laying	1 day	Fri 23/8/19	Fri 23/8/19																																
439	Run-in at EVA (Western Portion)	16 days	Sat 24/8/19	Sun 8/9/19																																
440	TTA Implementation	1 day	Sat 24/8/19	Sat 24/8/19																																
441	Demolition and Removal of Asphalt Surface	1 day	Sun 25/8/19	Sun 25/8/19																																
442	Excavation for PVC duct laying	1 day	Mon 26/8/19	Mon 26/8/19																																
443	Duct Laying	1 day	Tue 27/8/19	Tue 27/8/19																																
444	Backfilling to Formaiton Level	1 day	Wed 28/8/19	Wed 28/8/19																																
445	Backfilling of Subbase Level and SRT	8 days	Thu 29/8/19	Thu 5/9/19																																
446	RB Laying	1 day	Fri 6/9/19	Fri 6/9/19																																
447	BC Laying	1 day	Sat 7/9/19	Sat 7/9/19																																
448	WC Laying	1 day	Sun 8/9/19	Sun 8/9/19																																
449	Construction of Lighting Cable Duct (Yacht Club)	10 days	Mon 4/11/19	Wed 13/11/19																																
450	TTA Implementation	1 day	Mon 4/11/19	Mon 4/11/19																																
451	Demolition of Concrete Pavement	2 days	Tue 5/11/19	Wed 6/11/19																																
452	PVC Duct Laying	1 day	Thu 7/11/19	Thu 7/11/19																																
453	Backfilling of Trench	1 day	Fri 8/11/19	Fri 8/11/19																																
454	Subbase Laying and SRT	4 days	Sat 9/11/19	Tue 12/11/19																																
455	Concrete Laying	1 day	Wed 13/11/19	Wed 13/11/19																																
456	Installation of Lamp Post (West of Triangular Island) (8 nos.)	26 days	Sat 10/8/19	Wed 4/9/19																																
457	Inspection of laid cable duct by Hyd	7 days	Sat 10/8/19	Fri 16/8/19																																
458	Preparation work by Hyd Lighting Division for instllation of Lamp Post (8 nos.)	14 days	Sat 17/8/19	Fri 30/8/19																																
459	Installation of Lamp Post (2 nos./day)	5 days	Sat 31/8/19	Wed 4/9/19																																
460	Installation of Lamp Post (East of Triangular Island to Yacht Club) (6 nos.)	26 days	Thu 14/11/19	Mon 9/12/19																																
461	Inspection of laid cable duct Hyd	7 days	Thu 14/11/19	Wed 20/11/19																																
462	Preparation work by HyD Lighting Division for instllation of Lamp Post (6 nos.)	14 days	Thu 21/11/19	Wed 4/12/19																																
463	Installation of Lamp Post (2 nos./day)	5 days	Thu 5/12/19	Mon 9/12/19																																
464	Construction Directional Sign at Triangle Island	213 days	Tue 14/5/19	Thu 12/12/19																																
465	Advance Work	211 days	Tue 14/5/19	Tue 10/12/19																																
466	Submit shop drawing of traffic sign and frame to AECOM	0 days	Tue 14/5/19	Tue 14/5/19																																
467	Approval of shop drawing of traffic sign and frame by AECOM	14 days	Tue 14/5/19	Mon 27/5/19																																
468	Procurement of traffic sign and frame	30 days	Tue 28/5/19	Wed 26/6/19																																
469	Delivery of traffic sign and frame	0 days	Wed 26/6/19	Wed 26/6/19																																
470	Design of footing	7 days	Thu 6/6/19	Thu 13/6/19																																
471	Obtain ICE certificate for footing	1 day	Thu 13/6/19	Fri 14/6/19																																
472	Submission to AECOM	0 days	Fri 14/6/19	Fri 14/6/19																																
473	Approval of footing design	180 days	Fri 14/6/19	Tue 10/12/19																																
474	Site Work	168 days	Fri 28/6/19	Thu 12/12/19																																

Task Milestone Rolled Up Task Rolled Up Progress External Tasks Group By Summary

Progress Summary Rolled Up Milestone Split Project Summary Deadline

Activity ID	Activity Name	Original Duration	Start	Finish	2019																	
					Aug			Sep			Oct			Nov								
Total		385	21-Mar-19 A	02-Apr-20																		
DWP-08 - (2) - Update Progress As of 20 Aug 19		385	21-Mar-19 A	02-Apr-20																		
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks		385	21-Mar-19 A	02-Apr-20																		
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)		365	21-Mar-19 A	29-Jan-20																		
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365	21-Mar-19 A	29-Jan-20																		
KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH>500mm)		365	21-Mar-19 A	02-Apr-20																		
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365	21-Mar-19 A	02-Apr-20																		
KD18 - Section 11: Transplanted Trees DBH>500mm in Portion VA and XII		365	21-Mar-19 A	02-Apr-20																		
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365	21-Mar-19 A	02-Apr-20																		



中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Page 1 of 1
Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel (Slip Road 8 Section) - 3 Months Rolling Programme

Date	Revision	Checked	Approved
20-Aug-19	DWP-08 (2) - 3 Months Rolling	TL	TL
