

Activity ID	Activity Name	On Dur	Rem Dur	Scheduled /Actual Start	Scheduled / Actual Finish	Total Float	Calendar	2018																	
								August			September			October			November			December					
								05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	02
3 MONTHS ROLLING PROGRAMME OF WORKS PROGRAMME REVIEWED 8 AUG 2018 (DD 7-9-18)																									
EXCAVATION TWCR4 AND CONSTRUCTION OF WCR4																									
EXCAVATE TWCR4 AND INSTALL SEAWALL																									
A1000	TRANSPORT OF P5 FILL MATERIAL TO P34	10	10	30-Oct-18	08-Nov-18	32	HK Working Day	TRANSPORT OF P5 FILL MATERIAL																	
MARINE EXCAVATION																									
A1030	WEST SIDE EXC FOR G400 (1600M3) & 0.5T ARMOUR	20	20	07-Sep-18*	26-Sep-18	0	7-Day Workweek-1	WEST SIDE EXC FOR G400 (1600M3) & 0.5T ARMOUR, WEST SIDE EXC FOR G400 (1600M3)																	
A1040	ARRIVAL OF G400	1	1	17-Sep-18	17-Sep-18	143	7-Day Workweek-1	ARRIVAL OF G400																	
A1050	ARRIVAL OF ARMOUR	1	1	21-Sep-18	22-Sep-18	134	HK Working Day	ARRIVAL OF ARMOUR																	
CUTTING D-WALL																									
A1080	EAST SIDE CORE HOLES	9	1	01-Sep-18 A	07-Sep-18	16	7-Day Workweek-1	EAST SIDE CORE HOLES																	
A1090	WEST SIDE CORE HOLES	5	5	05-Sep-18 A	12-Sep-18	16	7-Day Workweek-1	WEST SIDE CORE HOLES																	
A1100	VERTICAL CUT	20	5	05-Sep-18 A	11-Sep-18	13	7-Day Workweek-1	VERTICAL CUT																	
A1110	HORIZONTAL CUT	20	20	07-Sep-18	26-Sep-18	5	7-Day Workweek-1	HORIZONTAL CUT																	
A1120	REMOVAL OF D-WALL	20	20	07-Sep-18	26-Sep-18	5	7-Day Workweek-1	REMOVAL OF D-WALL																	
INSTALL SEAWALL																									
MANUFACTURE OF SEAWALL BLOCK																									
A1125	MANUFACTURE OF SEAWALL BLOCK	86	43	27-Jul-18 A	19-Oct-18	40	7-Day Workweek-1	MANUFACTURE OF SEAWALL BLOCK																	
A1127	MANUFACTURE OF FACING STONE	15	15	20-Oct-18	03-Nov-18	103	7-Day Workweek-1	MANUFACTURE OF FACING STONE																	
A1130	1ST DELIVERY	1	1	13-Sep-18*	13-Sep-18	19	7-Day Workweek-1	1ST DELIVERY																	
A1140	2ND DELIVERY	1	1	06-Oct-18*	06-Oct-18	9	7-Day Workweek-1	2ND DELIVERY																	
A1150	3RD DELIVERY	1	1	12-Oct-18*	12-Oct-18	17	7-Day Workweek-1	3RD DELIVERY																	
A1160	4TH DELIVERY	1	1	19-Oct-18*	19-Oct-18	11	7-Day Workweek-1	4TH DELIVERY																	
A1170	5TH DELIVERY	1	1	27-Oct-18*	27-Oct-18	4	7-Day Workweek-1	5TH DELIVERY																	
A1180	6TH DELIVERY	1	1	02-Nov-18*	02-Nov-18	3	7-Day Workweek-1	6TH DELIVERY																	
A1190	7TH DELIVERY	1	1	09-Nov-18*	09-Nov-18	6	7-Day Workweek-1	7TH DELIVERY																	
A1200	8TH DELIVERY	1	1	15-Nov-18*	15-Nov-18	14	7-Day Workweek-1	8TH DELIVERY																	
INSTALLATION OF EAST SIDE SEAWALL BLOCK																									
A1210	MOUNTING ROCK BEDDING	6	6	19-Sep-18	24-Sep-18	19	7-Day Workweek-1	MOUNTING ROCK BEDDING																	
A1220	LEVELLING	3	3	25-Sep-18	27-Sep-18	19	7-Day Workweek-1	LEVELLING																	
A1230	M9 BLOCK	2	2	28-Sep-18	29-Sep-18	19	7-Day Workweek-1	M9 BLOCK																	
A1240	LEVELLING	5	5	30-Sep-18	04-Oct-18	19	7-Day Workweek-1	LEVELLING																	
A1250	1ST LAYER OF BLOCK	4	4	05-Oct-18	08-Oct-18	19	7-Day Workweek-1	1ST LAYER OF BLOCK																	
A1260	2ND LAYER	3	3	09-Oct-18	11-Oct-18	19	7-Day Workweek-1	2ND LAYER																	
A1270	3RD LAYER	3	3	12-Oct-18	14-Oct-18	19	7-Day Workweek-1	3RD LAYER																	
A1280	4TH LAYER	3	3	15-Oct-18	17-Oct-18	19	7-Day Workweek-1	4TH LAYER																	
A1290	5TH LAYER	3	3	18-Oct-18	20-Oct-18	19	7-Day Workweek-1	5TH LAYER																	
A1300	6TH LAYER	3	3	21-Oct-18	23-Oct-18	19	7-Day Workweek-1	6TH LAYER																	
A1310	TYPE A	4	4	24-Oct-18	27-Oct-18	19	7-Day Workweek-1	TYPE A																	
A1320	GEOTEXTILE AND FILTER	4	4	28-Oct-18	31-Oct-18	19	7-Day Workweek-1	GEOTEXTILE AND FILTER																	
A1330	B/F SOIL (5000m3)	8	8	01-Nov-18	08-Nov-18	19	7-Day Workweek-1	B/F SOIL (5000m3)																	
A1340	PLACE CONC CUBES AND PARTLY B/F TO +3.5mPD (1000m3)	6	6	09-Nov-18	14-Nov-18	19	7-Day Workweek-1	PLACE CONC CUBES AND																	
INSTALLATION OF WEST SIDE SEAWALL BLOCK																									
A1370	MOUNTING ROCK BEDDING TYPE 12A & 12B	15	15	27-Sep-18	11-Oct-18	0	7-Day Workweek-1	MOUNTING ROCK BEDDING TYPE 12A & 12B; MOUNTING ROCK BEDDING																	
A1380	LEVELLING	4	4	12-Oct-18	15-Oct-18	0	7-Day Workweek-1	LEVELLING, LEVELLING																	
A1390	M9 BLOCK	3	3	16-Oct-18	18-Oct-18	0	7-Day Workweek-1	M9 BLOCK, M9 BLOCK																	
A1400	LEVELLING	7	7	19-Oct-18	25-Oct-18	0	7-Day Workweek-1	LEVELLING, LEVELLING																	
A1410	1ST LAYER OF BLOCK	6	6	26-Oct-18	31-Oct-18	0	7-Day Workweek-1	1ST LAYER OF BLOCK, 1ST LAYER OF BLOCK																	
A1420	2ND LAYER	5	5	01-Nov-18	05-Nov-18	0	7-Day Workweek-1	2ND LAYER, 2ND LAYER																	
A1430	3RD LAYER	5	5	06-Nov-18	10-Nov-18	0	7-Day Workweek-1	3RD LAYER, 3RD LAYER																	
A1440	4TH LAYER	5	5	11-Nov-18	15-Nov-18	0	7-Day Workweek-1	4TH LAYER, 4TH LAYER																	
A1450	5TH LAYER	4	4	16-Nov-18	19-Nov-18	0	7-Day Workweek-1	5TH LAYER, 5TH LAYER																	
A1460	6TH LAYER	3	3	20-Nov-18	22-Nov-18	0	7-Day Workweek-1	6TH LAYER, 6TH LAYER																	
A1470	TYPE A	4	4	23-Nov-18	26-Nov-18	0	7-Day Workweek-1	TYPE A, TYPE A																	
A1480	FILTER	4	4	27-Nov-18	30-Nov-18	0	7-Day Workweek-1	FILTER																	
A1490	B/F TO +2.8mPD	6	6	01-Dec-18	06-Dec-18	0	7-Day Workweek-1																		

- ◆ Milestone
- ◆ Critical Milestones
- █ Current Works
- █ Critical Works
- █ Remaining Level of...

**CHUN WO - CRGL
JOINT VENTURE**

**CEDD CONTRACT NO. HK/2009/02
WD II - Central Wanchai Bypass at Wan Chai East (Contract 2)
3-MONTH ROLLING PROGRAMME (data date 07-Sep-18)**

Date	Revision	Checked	Approved

Activity ID	Activity Name	On Dur	Rem Dur	Scheduled /Actual Start	Scheduled / Actual Finish	Total Float	Calendar	2018																	
								August				September				October				November					
								05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	02
REINSTATE BAY 12 SEAWALL																									
A1540	INSTALL SEAWALL	30	30	30-Nov-18	30-Dec-18	15	7-Day Workweek-1																		
HELIPAD																									
A1600	DISMANTLE OLD SEAWALL BLOCK AND EXCAVATE	14	14	01-Nov-18	14-Nov-18	14	7-Day Workweek-1																		
A1610	ROCKFILL G400	3	3	15-Nov-18	17-Nov-18	14	7-Day Workweek-1																		
A1620	LEVELLING	3	3	18-Nov-18	20-Nov-18	14	7-Day Workweek-1																		
A1630	1ST LAYER OF SEAWALL BLOCK	3	3	21-Nov-18	23-Nov-18	14	7-Day Workweek-1																		
A1640	2ND LAYER	3	3	24-Nov-18	26-Nov-18	14	7-Day Workweek-1																		
A1650	3RD LAYER	4	4	27-Nov-18	30-Nov-18	14	7-Day Workweek-1																		
A1660	4TH LAYER	3	3	01-Dec-18	03-Dec-18	14	7-Day Workweek-1																		
A1670	5TH LAYER	3	3	04-Dec-18	06-Dec-18	14	7-Day Workweek-1																		
COPING																									
WITHIN D-WALL (TYPE 7)																									
A1780	BAY 1 LOWER	14	14	07-Sep-18*	20-Sep-18	56	7-Day Workweek-1																		
A1790	BAY 2 LOWER	13	13	21-Sep-18	03-Oct-18	56	7-Day Workweek-1																		
A1800	BAY 1 UPPER	7	7	04-Oct-18	10-Oct-18	56	7-Day Workweek-1																		
A1810	BAY 2 UPPER	7	7	11-Oct-18	17-Oct-18	56	7-Day Workweek-1																		
EAST SIDE COPING																									
A1830	EAST COPING	31	31	17-Nov-18	17-Dec-18	39	7-Day Workweek-1																		
BOX-O																									
ARRIVAL OF PRECAST UNIT FOR BAY 12																									
A1840	ARRIVAL OF PRECAST UNIT FOR BAY 12	1	1	07-Sep-18*	07-Sep-18	62	7-Day Workweek-1																		
INSTALLATION OF PRECAST UNIT																									
A1850	INSTALLATION OF PRECAST UNITS	19	19	25-Oct-18	13-Nov-18	15	7-Day Workweek-1																		
A1860	BAY 1 FIX REBAR	2	2	01-Nov-18	03-Nov-18	15	7-Day Workweek-1																		
A1870	BAY 1 CONCRETE	1	1	03-Nov-18	04-Nov-18	15	7-Day Workweek-1																		
A1880	BAY 2 FIX REBAR	2	2	06-Nov-18	08-Nov-18	15	7-Day Workweek-1																		
A1890	BAY 2 CONCRETE	1	1	08-Nov-18	09-Nov-18	15	7-Day Workweek-1																		
A1900	BAY 3 FIX REBAR	2	2	13-Nov-18	15-Nov-18	15	7-Day Workweek-1																		
A1910	BAY 3 CONCRETE	1	1	15-Nov-18	16-Nov-18	15	7-Day Workweek-1																		
A1920	CLEAN UP, W/P AND B/F	13	13	17-Nov-18	30-Nov-18	15	7-Day Workweek-1																		
CONSTRUCTION OF BAY 12																									
REMOVAL OF BULKHEAD																									
A1930	BAY 19 STEEL BULKHEAD	2	0	01-Sep-18 A	05-Sep-18 A		7-Day Workweek-1																		
A1940	BAY 13 CONCRETE BULKHEAD	5	1	04-Sep-18 A	08-Sep-18	15	7-Day Workweek-1																		
A1950	CONSTRUCTION OF EARTH PLATFORM	6	6	08-Sep-18	14-Sep-18	15	7-Day Workweek-1																		
PIPE PILING AND GROUTING																									
A1960	WEST SIDE PIPE PILING	10	3	01-Aug-18 A	09-Sep-18	17	7-Day Workweek-1																		
A1970	WEST SIDE GROUTING	22	15	21-Aug-18 A	22-Sep-18	146	7-Day Workweek-1																		
A1980	EAST SIDE PIPE PILING	13	13	11-Sep-18	24-Sep-18	15	7-Day Workweek-1																		
A1990	EAST SIDE GROUTING	11	11	20-Sep-18	01-Oct-18	15	7-Day Workweek-1																		
EXCAVATION AND ELS																									
A2000	DEMOLISH OLD CULVERT, CUT STEEL PILE AND INSTALL ELS	10	10	21-Sep-18	01-Oct-18	15	7-Day Workweek-1																		
A2010	EXCAVATE TP -2.9mPD	8	8	01-Oct-18	09-Oct-18	15	7-Day Workweek-1																		
A2020	B/F G200 & ELS	8	8	09-Oct-18	17-Oct-18	15	7-Day Workweek-1																		
A2030	TAMPING	2	2	17-Oct-18	19-Oct-18	15	7-Day Workweek-1																		
A2040	LEVELLING	5	5	19-Oct-18	24-Oct-18	15	7-Day Workweek-1																		
HUNG HING ROAD																									
REMOVAL OF D-WALL TO +1.5mPD																									
A2050	ZONE A	21	0	13-Jul-18 A	25-Aug-18 A		7-Day Workweek-1																		
A2060	ZONE B	16	5	01-Sep-18 A	11-Sep-18	110	7-Day Workweek-1																		
A2070	ZONE C	14	14	17-Nov-18	30-Nov-18	44	7-Day Workweek-1																		
BACKFILLING																									
A2090	ZONE A	5	0	17-Aug-18 A	30-Aug-18 A		7-Day Workweek-1																		
A2100	ZONE B	7	7	11-Sep-18	18-Sep-18	149	7-Day Workweek-1																		

- ◆ Milestone
- ◆ Critical Milestones
- Current Works
- Critical Works
- Remaining Level of...

**CHUN WO - CRGL
JOINT VENTURE**

**CEDD CONTRACT NO. HK/2009/02
WD II - Central Wanchai Bypass at Wan Chai East (Contract 2)
3-MONTH ROLLING PROGRAMME (data date 07-Sep-18)**

Date	Revision	Checked	Approved

Activity ID	Activity Name	On Dur	Rem Dur	Scheduled /Actual Start	Scheduled /Actual Finish	Total Float	Calendar	2018																
								August			September			October			November							
A2110	ZONE C	5	5	01-Dec-18	05-Dec-18	71	7-Day Workweek-1																	
MANHOLE																								
A2130	MH7352A	8	6	05-Sep-18 A	12-Sep-18	106	7-Day Workweek-1																	
A2140	MH7354&7355	10	7	05-Sep-18 A	19-Sep-18	106	7-Day Workweek-1																	
A2150	MH7341	9	9	19-Sep-18	28-Sep-18	106	7-Day Workweek-1																	
DRAOMAGE																								
CH3730-3760																								
A2200	375MM DRAIN FROM SMH7354 TO BOX	16	0	31-Jul-18 A	18-Aug-18 A		7-Day Workweek-1																	
A2210	375M SMH7355 TO 7354	13	4	20-Aug-18 A	10-Sep-18	16	7-Day Workweek-1																	
A2220	300MM SMH734F1 TO 7355	11	10	03-Sep-18 A	21-Sep-18	16	7-Day Workweek-1																	
A2230	BACKFILLING	13	13	21-Sep-18	04-Oct-18	16	7-Day Workweek-1																	
A2240	AIR TEST AND CCTV	3	3	04-Oct-18	07-Oct-18	16	7-Day Workweek-1																	
BCO																								
A2250	600MM DRAIN SMH7352A TO BOX	11	0	30-Jul-18 A	09-Aug-18 A		7-Day Workweek-1																	
A2260	BAY 12 (1200MM TO BOX)	8	8	07-Nov-18	15-Nov-18	22	7-Day Workweek-1																	
A2270	BAY 12 TO 14 GULLUES AND 225 DRAIN	12	12	24-Nov-18	06-Dec-18	22	7-Day Workweek-1																	
CH3730-3760 REMAINING																								
A2280	300MM DRAIN SMH7341 TO 7353	9	9	06-Dec-18	15-Dec-18	22	7-Day Workweek-1																	
ROADWORK																								
HHR																								
A2390	ROAD FORMATION	12	12	30-Sep-18	12-Oct-18	16	7-Day Workweek-1																	
A2400	TESTING	10	10	12-Oct-18	22-Oct-18	16	7-Day Workweek-1																	
A2410	KERB	8	8	22-Oct-18	30-Oct-18	16	7-Day Workweek-1																	
A2420	SUB-BASE	12	12	30-Oct-18	11-Nov-18	16	7-Day Workweek-1																	
A2430	TEST	8	8	11-Nov-18	19-Nov-18	16	7-Day Workweek-1																	
A2440	ROAD FORMATION	3	3	19-Nov-18	22-Nov-18	16	7-Day Workweek-1																	
A2450	TEST AND SUB-BASE	11	11	22-Nov-18	03-Dec-18	16	7-Day Workweek-1																	
A2460	ROAD FURNITURE	14	14	28-Nov-18	12-Dec-18	16	7-Day Workweek-1																	
A2470	BLACK TOP	9	9	03-Dec-18	12-Dec-18	16	7-Day Workweek-1																	
600mm Sewere																								
FIRST STAGE																								
A2500	600MM SEWER	5	1	26-Jul-18 A	07-Sep-18	97	7-Day Workweek-1																	
A2510	B/F	5	5	08-Sep-18	12-Sep-18	97	7-Day Workweek-1																	
A2520	SUB-BASE	9	9	13-Sep-18	21-Sep-18	97	7-Day Workweek-1																	
A2530	BLACKTOP	2	2	22-Sep-18	23-Sep-18	97	7-Day Workweek-1																	
A2540	TTA	1	1	24-Sep-18	24-Sep-18	97	7-Day Workweek-1																	
SECOND STAGE																								
A2550	600MM SEWER	12	12	25-Sep-18	06-Oct-18	97	7-Day Workweek-1																	
A2560	B/F	5	5	07-Oct-18	11-Oct-18	97	7-Day Workweek-1																	
A2570	SUB-BASE	9	9	12-Oct-18	20-Oct-18	97	7-Day Workweek-1																	
A2580	BLACKTOP	2	2	21-Oct-18	22-Oct-18	97	7-Day Workweek-1																	
A2590	TTA	1	1	23-Oct-18	23-Oct-18	97	7-Day Workweek-1																	
FINAL STAGE																								
A2600	600MM SEWER mh4.13 TO 4.15 TO 4.17	11	11	24-Oct-18	03-Nov-18	97	7-Day Workweek-1																	
A2610	AIR TEST	1	1	04-Nov-18	04-Nov-18	97	7-Day Workweek-1																	
A2620	b/f	3	3	05-Nov-18	07-Nov-18	97	7-Day Workweek-1																	
A2630	AIR TEST AND CCTV	2	2	08-Nov-18	09-Nov-18	97	7-Day Workweek-1																	
EXPO DRIVE, WCR1 & WCR3 REMAINING WORKS																								
A2650	CMS INSTALLATION	11	1	28-Jul-18 A	08-Sep-18	101	7-Day Workweek-1																	
A2660	WCR1 U CHANNELS	50	50	07-Sep-18*	26-Oct-18	52	7-Day Workweek-1																	
A2670	EXPO DRIVE COVER REMEDIAL	46	23	15-Aug-18 A	29-Sep-18	123	7-Day Workweek-1																	
A2680	EXPO DRIVE COPING	28	28	17-Sep-18	14-Oct-18	123	7-Day Workweek-1																	
A2690	WCR1 EVA	59	59	01-Nov-18*	29-Dec-18	47	7-Day Workweek-1																	
A2700	WCR3 SUB-BASE	24	24	17-Nov-18*	10-Dec-18	61	7-Day Workweek-1																	
A2710	REPAIR COPING	11	11	29-Nov-18*	09-Dec-18	67	7-Day Workweek-1																	

- ◆ Milestone
- ◆ Critical Milestones
- █ Current Works
- █ Critical Works
- █ Remaining Level of...

**CHUN WO - CRGL
JOINT VENTURE**

**CEDD CONTRACT NO. HK/2009/02
WD II - Central Wanchai Bypass at Wan Chai East (Contract 2)
3-MONTH ROLLING PROGRAMME (data date 07-Sep-18)**

Date	Revision	Checked	Approved

Activity ID	Activity Name	On Dur	Rem Dur	Scheduled /Actual Start	Scheduled / Actual Finish	Total Float	Calendar	2018																	
								August				September				October				November					
								05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	02
A2720	WCR1&3 ARMOUR SLOPE PROFILE	31	31	01-Dec-18*	31-Dec-18	45	7-Day Workweek-1																		
A2740	REINSTATE WCR3 EXIT	23	23	24-Sep-18*	16-Oct-18	121	7-Day Workweek-1																		
A2750	WCR3 FENCING	23	23	09-Nov-18*	01-Dec-18	75	7-Day Workweek-1																		

<ul style="list-style-type: none"> ◆ Milestone ◆ Critical Milestones █ Current Works █ Critical Works █ Remaining Level of... 	CHUN WO - CRGL JOINT VENTURE	CEDD CONTRACT NO. HK/2009/02 WD II - Central Wanchai Bypass at Wan Chai East (Contract 2) 3-MONTH ROLLING PROGRAMME (data date 07-Sep-18)	Date	Revision	Checked	Approved

**CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West**


Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019							
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
HK/2012/08 Revised Works Programme Rev.12.0(DD 20 November 2017)																									
Key Dates and Milestone Dates																									
Sections of Works Completion (Included Not Granted EOT Entitlement of The Contractor)																									
KD10840	Completion of Section IIIA	0		08-Sep-18*	0%																				
KD10860	Completion of Section IV	0		30-Aug-18*	0%																				
KD10880	Completion of Section V	0		26-Sep-18*	0%																				
KD11010	Completion of Section VII	0		14-Sep-18*	0%																				
KD11020	Completion of Section VIII	0		21-Sep-18*	0%																				
KD11040	Completion of Section IX	0		21-Sep-19*	0%																				
KD11060	Completion of Section X	0		21-Sep-18*	0%																				
Planned Sections of Works Completion																									
KD10080	Planned Section IIIA Completion - Road A2,A4, A5	0		08-Sep-18	0%																				
KD10100	Planned Section IV Completion - Slip Road 3	0		30-Aug-18	0%																				
KD10140	Planned Section V Completion - Remaining At-Grade Road	0		26-Sep-18	0%																				
KD10280	Planned Section VII Completion - Remainder Works	0		14-Sep-18	0%																				
KD10300	Planned Section VIII Completion - Landscape Softwork	0		21-Sep-18	0%																				
KD10320	Planned Section IX Completion - Establishment Works	0		21-Sep-19	0%																				
KD10340	Planned Section X Completion - Tree Protection & Preservation	0		21-Sep-18	0%																				
Dredging and Reclamation																									
Marine Work Construction																									
Zone CRIII																									
Seawall Construction - Zone CRIII																									
Zone CRIII Seawall- 2nd Stage																									
Seawall 2 & 12																									
MAR21371	Zone CRIII - seawall 2 & 12 - Backfilling remaining portion (type A, geotextile and filter)	0	19-Jan-18 A	27-Jan-18 A	100%	■																			
Zone D																									
Seawall Construction - Zone D																									
Seawall 10 & 11																									
MAR20630	Zone D - Seawall 10 & 11: Install remaining seawall block	14	20-Feb-18*	05-Mar-18	0%		■																		
MAR20650	Zone D - Seawall 10 & 11: Backfill Type A	7	06-Mar-18	12-Mar-18	0%			■																	
MAR20670	Zone D - Seawall 10 & 11: Lay geotextile and filter	7	13-Mar-18	19-Mar-18	0%			■																	
Works for Section Completion																									
Construction																									
Section III A - Road A2, A4 & A5																									
Roadwork & Utilities - Section 1 (L1806 - L1801)																									

Data Date: 20-Feb-18

- ◆ Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Remaining Level of Effort

**Updated Works Programme Rev.12
(Ref. to Rev.12 as of 20 February 2018)**

Date	Revision	Checked	Approved
20-Feb-18	12		

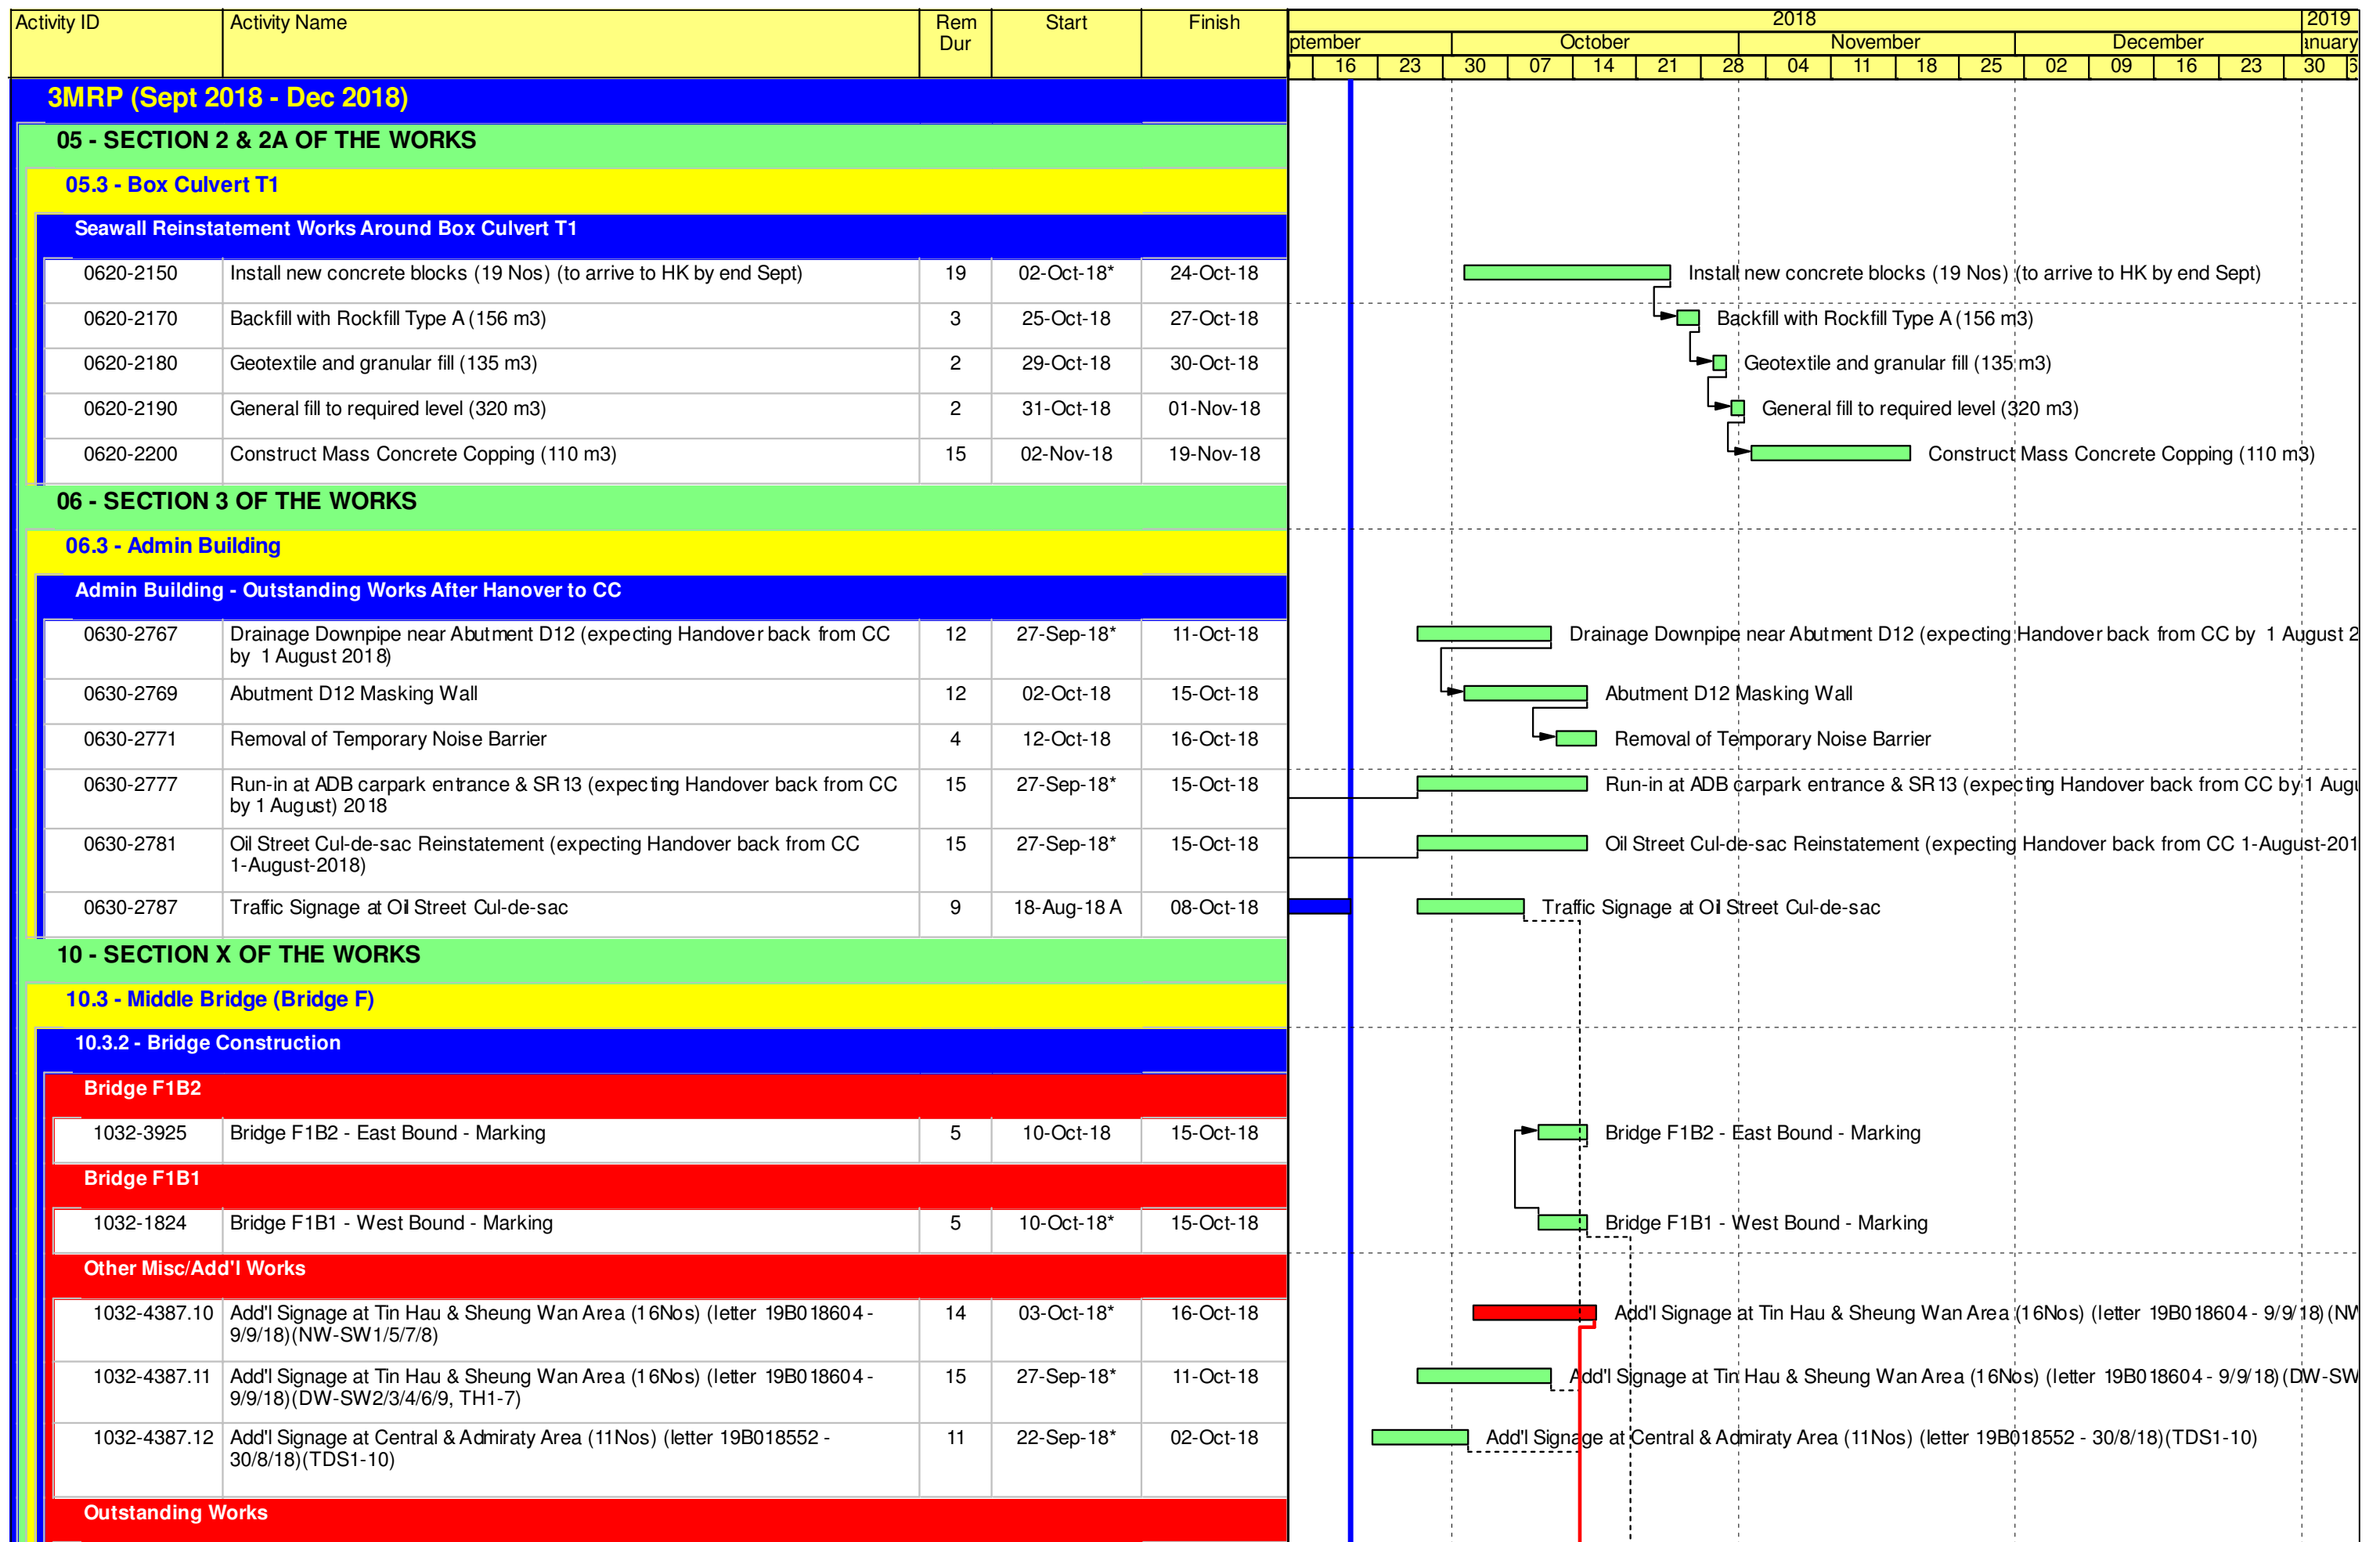

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Sept.2018 to 20.Dec.2018)

Activity ID	Activity Name	Original Duration	Start	Finish	2018			
					Sep	Oct	Nov	Dec
Total		2421d	21-Mar-13 A	05-Nov-19				
DWP-08 - (2) - Update Progress As of 20 Sep 18		2421d	21-Mar-13 A	05-Nov-19				
Works in KD9 (Include Re-provisioning Works of KD4,KD5)		339d	30-Jan-18 A	24-Dec-18				
External Works Under KD9		178d	30-Jan-18 A	20-Dec-18				
Zone 4 up to Elderly Facilities		178d	30-Jan-18 A	20-Dec-18				
Elderly Facilities V/039 Received on 22 Jun 2017		178d	30-Jan-18 A	20-Dec-18				
EXW_2270	Facilities fabrication	90d	30-Jan-18 A	15-Nov-18				Facilities fabrication
EXW_2280	Ground levelling, drainage works and safety met installation	30d	16-Nov-18	20-Dec-18				Ground levelling, drainage works and safety met installation
Additional Walkway & Arbour V/040 Received on 22 Aug 2017		30d	03-May-18 A	31-Oct-18				
EXW_2320	Arbour installation and walkway construction	30d	03-May-18 A	31-Oct-18				Arbour installation and walkway construction
Reverting Traffic for IEC,VP Rd & TF St & Seawall Reinstatement (KD9)		256d	13-Apr-18 A	24-Dec-18				
TTA Revert Traffic Back to Original Alignment		171d	13-Apr-18 A	04-Oct-18				
East Bound TTA - IEC East Bound, Victoria Park Road & footpath along Sea Side		10d	21-Sep-18	30-Sep-18				
TTM Stage 1 - IEC (East Bound)		6d	21-Sep-18	26-Sep-18				
Reinstatement Existing Structure		6d	21-Sep-18	26-Sep-18				
EB_1020	Install metal parapet on parapet wall (30m)	6d	21-Sep-18	26-Sep-18				Install metal parapet on parapet wall (30m)
TTM Stage 2 - Revert Traffic back to Original Victoria Road		4d	27-Sep-18	30-Sep-18				
Existing Bridge Parapet Reinstatement		4d	27-Sep-18	30-Sep-18				
EB_1180	Install metal parapet on parapet wall (40m)	4d	27-Sep-18	30-Sep-18				Install metal parapet on parapet wall (40m)
West Bound - IEC West Bound & Tsing fung Street		166d	13-Apr-18 A	04-Oct-18				
TTM Stage 2 - Revert Traffic back to Original Tsing Fung Street		5d	21-Sep-18	25-Sep-18				
Existing Bridge Parapet Reinstatement		5d	21-Sep-18	25-Sep-18				
IECW_1140	Install metal parapet on parapet wall (60m)	5d	21-Sep-18	25-Sep-18				Install metal parapet on parapet wall (60m)
TTM Stage 3 - Reinstatement of Victoria Park		21d	13-Apr-18 A	04-Oct-18				
Reinstatement Works inside Victoria Park		21d	13-Apr-18 A	04-Oct-18				
IECW_1470	Slope Reinstatement of Victoria Park	21d	13-Apr-18 A	04-Oct-18				Slope Reinstatement of Victoria Park
Completion of Minor Outstanding / Remaining Works for KD9		200d	03-May-18 A	24-Dec-18				
East Bound - Minor Outstanding Works in Footpath after Substantial Completion of KD9		150d	18-May-18 A	08-Oct-18				
Minor Reinstatement Works for Existing Sign Gantry		3d	14-Sep-18 A	19-Sep-18 A				
EB_1760	Connection of Public Lighting by HyD (Lighting)	2d	14-Sep-18 A	18-Sep-18 A				Connection of Public Lighting by HyD (Lighting)
EB_1790	Installation of E & M at Sign Gantry (night work)	1d	19-Sep-18 A	19-Sep-18 A				Installation of E & M at Sign Gantry (night work)
Minor Reinstatement Works for Central Median of IEC & Footbridge		6d	01-Oct-18	06-Oct-18				
EB_1800	Reconstruction of central divider (6m long, night work)	6d	01-Oct-18	06-Oct-18				Reconstruction of central divider (6m long, night work)
EB_1810	Dismantlement of temp directional sign mounted on extg footbridge	1d	01-Oct-18	01-Oct-18				Dismantlement of temp directional sign mounted on extg footbridge
Minor Reinstatement Works for Footpath		150d	18-May-18 A	08-Oct-18				
EB_1820	Place kerblines along VPR footpath	3d	18-May-18 A	17-Sep-18 A				Place kerblines along VPR footpath
EB_1840	Re-provision of Tree	8d	27-Sep-18 A	08-Oct-18				Re-provision of Tree
EB_1830	Reinstatement of District Council Welcome Sign and opening plaque at Planter area	1d	03-Oct-18 A	03-Oct-18 A				Reinstatement of District Council Welcome Sign and opening plaque at Planter area
Minor Reinstatement Works for Bus Stop		5d	20-Jul-18 A	05-Oct-18				
EB_1880	Reinstate Planter (Previous Temporary Bus Stop)	5d	20-Jul-18 A	05-Oct-18				Reinstate Planter (Previous Temporary Bus Stop)
Minor Reinstatement Works for Loop Detector		1d	23-Aug-18 A	24-Aug-18 A				
EB_1890	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)	1d	23-Aug-18 A	24-Aug-18 A				E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)
West Bound - Completion of Minor Outstanding / Remaining Works for KD9		142d	03-May-18 A	24-Dec-18				



- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Date	Revision	Checked	Approved
20-Sep-18	DWP-08 (2) - 3 Months Rolling	TL	TL

Activity ID	Activity Name	Original Duration	Start	Finish	2018			
					Sep	Oct	Nov	Dec
Minor Reinstatement Works for Victoria Park								
IECW_1500	Re-provision of Tree	32d	03-May-18 A	05-Nov-18				Re-provision of Tree
IECW_1510	Laying Irrigation Main	10d	27-Sep-18 A	14-Oct-18				Laying Irrigation Main
IECW_1520	Construct Landscape Footpath and Lightings	7d	20-Oct-18	26-Oct-18				Construct Landscape Footpath and Lightings
Minor Reinstatement Works in IEC West Bound								
IECW_1600	Replacement of new movement joint at IEC W/B (Sun midnight only)	8d	21-Sep-18	28-Sep-18				Replacement of new movement joint at IEC W/B (Sun midnight only)
IECW_1610	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)	57d	29-Sep-18	24-Nov-18				Repairing of extg conc deck surface after milling of temp asphalt
IECW_1620	Repairing of concrete defects on extg concrete deck and abutment M	30d	25-Nov-18	24-Dec-18				Repairing of concrete defects on extg concrete deck and abutment M
Works in Victoria Park (KD4, KD5, KD9)								
Re-Provisioning Works								
Nursery Compound								
Nursery compound								
ABWF								
Metal Fence								
VP_NC_1820	Installation	30d	05-Apr-18 A	09-Nov-18				Installation
Fire Services								
VP_NC_2030	FS inspection	14d	20-Aug-18 A	09-Oct-18				FS inspection
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks								
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)								
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365d	06-Nov-18	05-Nov-19				
KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH>500mm)								
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365d	06-Nov-18	05-Nov-19				
KD18 - Section 11: Transplanted Trees DBH>500mm in Portion VA and XII								
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365d	06-Nov-18	05-Nov-19				
KD10 - Preservation and Protection of Trees								
PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	28-Dec-18				
KD15 & KD8 - Mooring Components Upkeep (CBTS and ATS)								
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	21-Sep-18				Mooring Upkeep at Portion X(10) & XVI(16) - CBTS



中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Date	Revision	Checked	Approved
20-Sep-18	DWP-08 (2) - 3 Months Rolling	TL	TL

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018																		
						Sep			Oct			Nov			Dec									
Update 2018-09-20 CWB(CC) - Commissioning Contract (DWP 4a)																								
PRELIMINARIES AND GENERAL REQUIREMENTS																								
Salient Key Dates and Milestones																								
Contract Key Dates																								
KD002	KD2 - Achievement of Stage 2 (1635 days) - include EOT No.12 (403 days)	0		20-Sep-18*	-30																			
KD004	KD4 - Achievement of Stage 4 (1711 days) - include EOT No.12 (415 days)	0		04-Nov-18*	-49																			
KD005	KD5 - Achievement of Stage 5 (1711 days) - include EOT No.12 (415 days)	0		04-Nov-18*	-49																			
KD006	KD6 - Completion of Section 1 of the Works (1711 days) - include EOT No.12 (415 days)	0		04-Nov-18*	-49																			
Anticipated Completion Dates																								
KD04	KD4 - Achievement of Stage 4 (1711 days) - include EOT No.12 (415 days)	0		20-Sep-18*	-3																			
KD05	KD5 - Achievement of Stage 5 (1711 days) - include EOT No.12 (415 days)	0		16-Oct-18*	-30																			
KD06	KD6 - Completion of Section 1 of the Works (1711 days) - include EOT No.12 (415 days)	0		06-Dec-18*	-81																			
KD11	KD11 - Completion of Section 6 of the Works (1445 days) - include EOT No.12 (149 days)	0		06-Dec-18*	-298																			
Possession Dates and Vacation Dates																								
PO-IIa	Possession of Portion IIa (Day 1) - WVB below +6.5mPD	1329	28-Feb-14 A	18-Oct-18	-280																			
PO-III	Possession of Portion III (Day 120) - CH1805-2600	1209	28-Jun-14 A	18-Oct-18	-280																			
PO-Ib	Possession of Portion Ib (Day 242) - CH1580-1805	1087	28-Oct-14 A	18-Oct-18	-280																			
PO-IXd	Possession of Portion IXd (Day 266) - CH4600-4860	1063	21-Nov-14 A	18-Oct-18	-280																			
PO-XI	Possession of Portion XI (Day 296) - EVS	1033	21-Dec-14 A	18-Oct-18	-32																			
PO-Ilc	Possession of Portion Ilc (Day 336) - CH1360-1580	993	30-Jan-15 A	18-Oct-18	-280																			
PO-Ilb	Possession of Portion Ilb (Day 336) - WVB above +6.5mPD	669	30-Jan-15 A	18-Oct-18	-280																			
PO-IXa	Possession of Portion IXa (Day 392) - CH4860-5150	937	27-Mar-15 A	18-Oct-18	-280																			
PO-Va	Possession of Portion V (Day 607) - CH2950-3210	722	28-Oct-15 A	18-Oct-18	-280																			
PO-VII_a1	Possession of Portion VII (Day 762) - CH3911-4250 (below -6.0mPD)	659	30-Dec-15 A	18-Oct-18	-280																			

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 55 (September 2018)

THREE MONTH ROLLING

Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 1 of 23






Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Sep	Oct	Nov	Dec
PO-Vc	Possession of Portion V (Day 607) - CH3210-3250	658	15-Jan-16 A	18-Oct-18	-272	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-Vlb_b1	Possession of Portion Vlb (Day 761) - CH3428-3625 (E/B)	619	18-Feb-16 A	18-Oct-18	-280	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-Vlb_b2	Possession of Portion Vlb (Day 761) - CH3428-3625 (W/B)	568	29-Feb-16 A	18-Oct-18	-257	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-Xa_1	Possession of Portion Xa (Day 650) - ADB Southern Portion (AECOM letter ref: 2015007890T)	589	07-Mar-16 A	18-Oct-18	-464	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-Xb_1	Possession of Portion Xb (Day 804) - ADB Northern Portion	589	07-Mar-16 A	18-Oct-18	-464	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-Vb1	Possession of Portion V (Day 607) - SR3	587	11-Mar-16 A	18-Oct-18	-32	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-Ia	Possession of Portion Ia (Day 789) - SCB / SCP1 / SCP2 / Rumsey Street Flyover	600	28-Mar-16 A	18-Oct-18	-425	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-VII_a2	Possession of Portion VII (Day 762) - CH3800-3911 (below -6.0mPD)	567	31-Mar-16 A	18-Oct-18	-280	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-IXc_1	Possession of Portion IXc (Day 712) - EVB above 3.6mPD - Relinquished on 12 Apr 2016	445	29-Jul-16 A	18-Oct-18	-433	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-IXb_1	Possession of Portion IXb (Day 712) - EVB (below +3.6mPD to tunnel top slab) - Relinquished on 12 Apr 2016	445	05-Aug-16 A	18-Oct-18	-433	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-VIa_a	Possession of Portion VIa (Day 823) - CH3250-3283	425	15-Aug-16 A	18-Oct-18	-257	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-Vb2_a	Possession of Portion V (Day 607) - SR2	456	15-Aug-16 A	18-Oct-18	-272	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-VIc_a	Possession of Portion VIc (Day 761) - CH3770-3800 (Access Shaft Opening)	391	23-Sep-16 A	18-Oct-18	-280	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-VIb_c	Possession of Portion VIb (Day 761) - CH3625-3770	391	23-Sep-16 A	18-Oct-18	-280	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-IVa1	Possession of Portion IVa (Day 930) - CH2600-2720	323	30-Nov-16 A	18-Oct-18	-280	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-IVb2	Possession of Portion IVb (Day 930) - MVB (GL D-H)	233	28-Feb-17 A	18-Oct-18	-458	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-VIIIa_a	Possession of Portion VIIIa (Day 929) - CH4530-4591 W/B	233	28-Feb-17 A	18-Oct-18	-280	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-VIIIa	Possession of Portion VIIIa (Day 929) - CH4250-4600 (Remaining)	241	12-Mar-17 A	18-Oct-18	-280	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-VIIIb	Possession of Portion VIIIb (Day 929) - SR8 (CH700-350)	233	12-Mar-17 A	18-Oct-18	-280	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-VIIIc	Possession of Portion VIIIc (Day 1039) - SR8 (CH350-310) / SCP4	233	12-Mar-17 A	18-Oct-18	-272	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-IVa2_a	Possession of Portion IVa (Day 930) - CH2720-2950	241	12-Mar-17 A	18-Oct-18	-280	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-IVb1	Possession of Portion IVb (Day 930) - MVB (GL A-C)	239	14-Mar-17 A	18-Oct-18	-458	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-IVa2_b	Possession of Portion IVa (Day 930) - SR1	203	30-Mar-17 A	18-Oct-18	-280	[Gantt bars for Sep, Oct, Nov, Dec]			
PO-Vb2_b	Possession of Portion V (Day 607) - SCP3	182	03-Jul-17 A	18-Oct-18	-272	[Gantt bars for Sep, Oct, Nov, Dec]			

-  Current Milestone
-  Remaining Work
-  Level of Effort
-  Project Baseline
-  Baseline Milestone
-  Actual Work
-  Critical Remaining Work

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING



Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 2 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

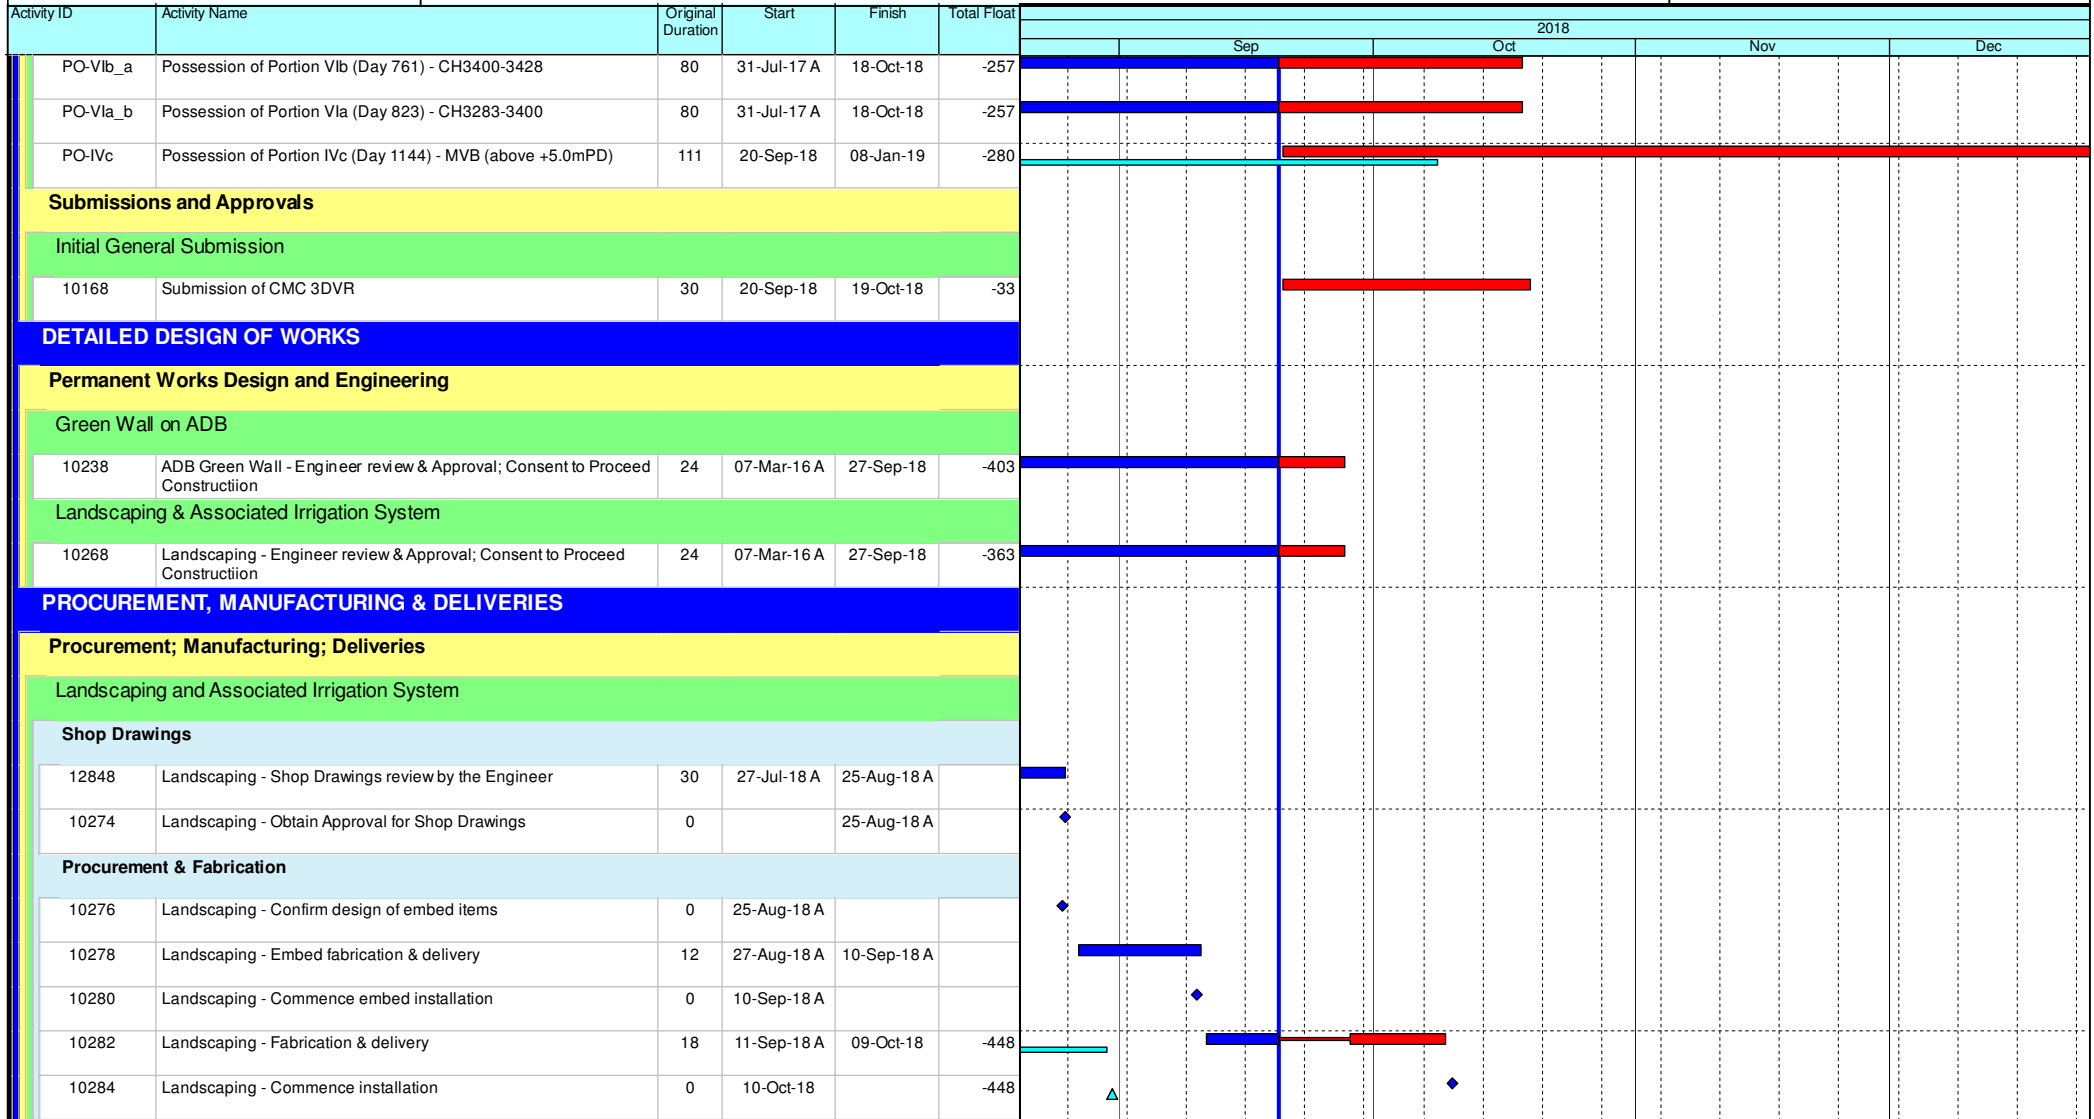

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING



Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 3 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

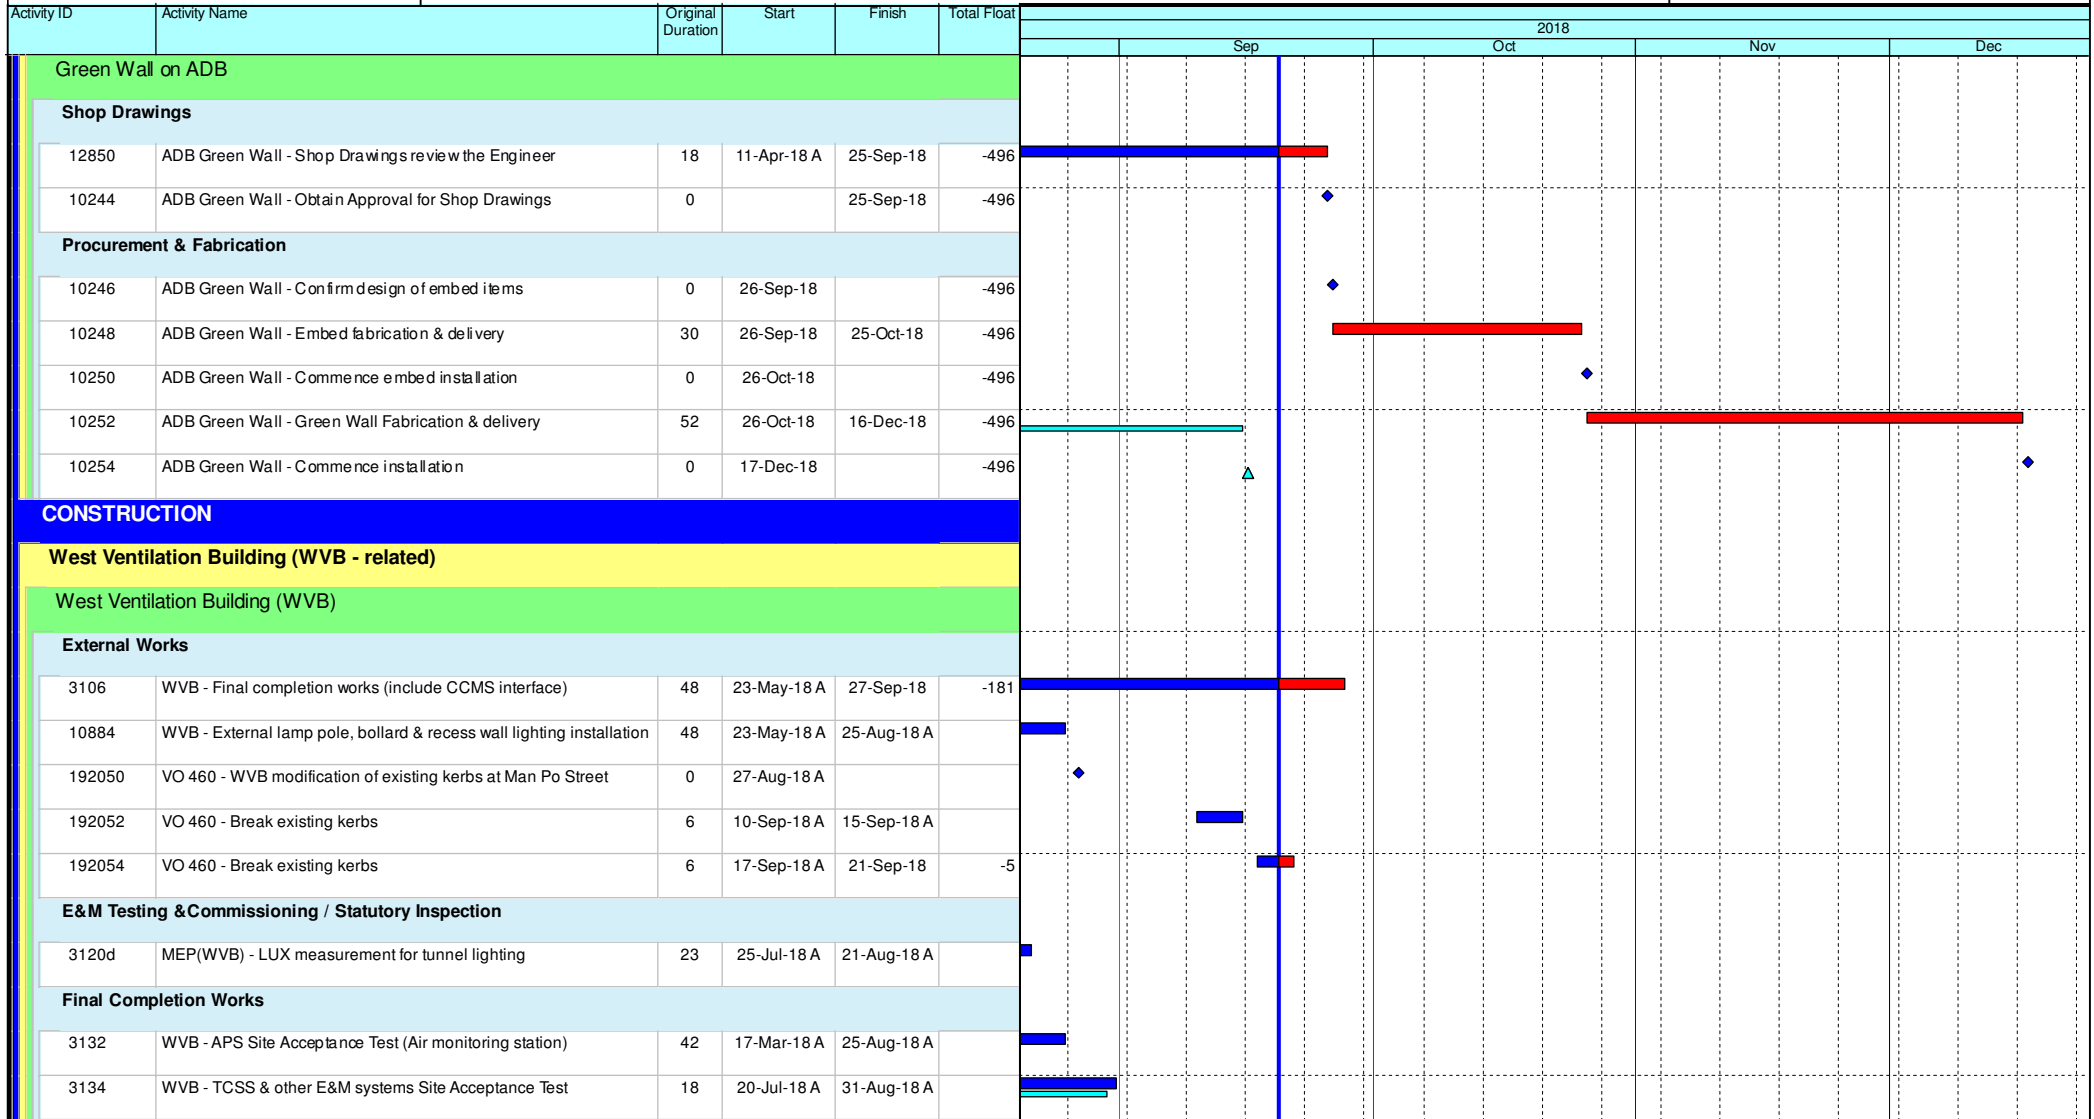

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING



Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 4 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

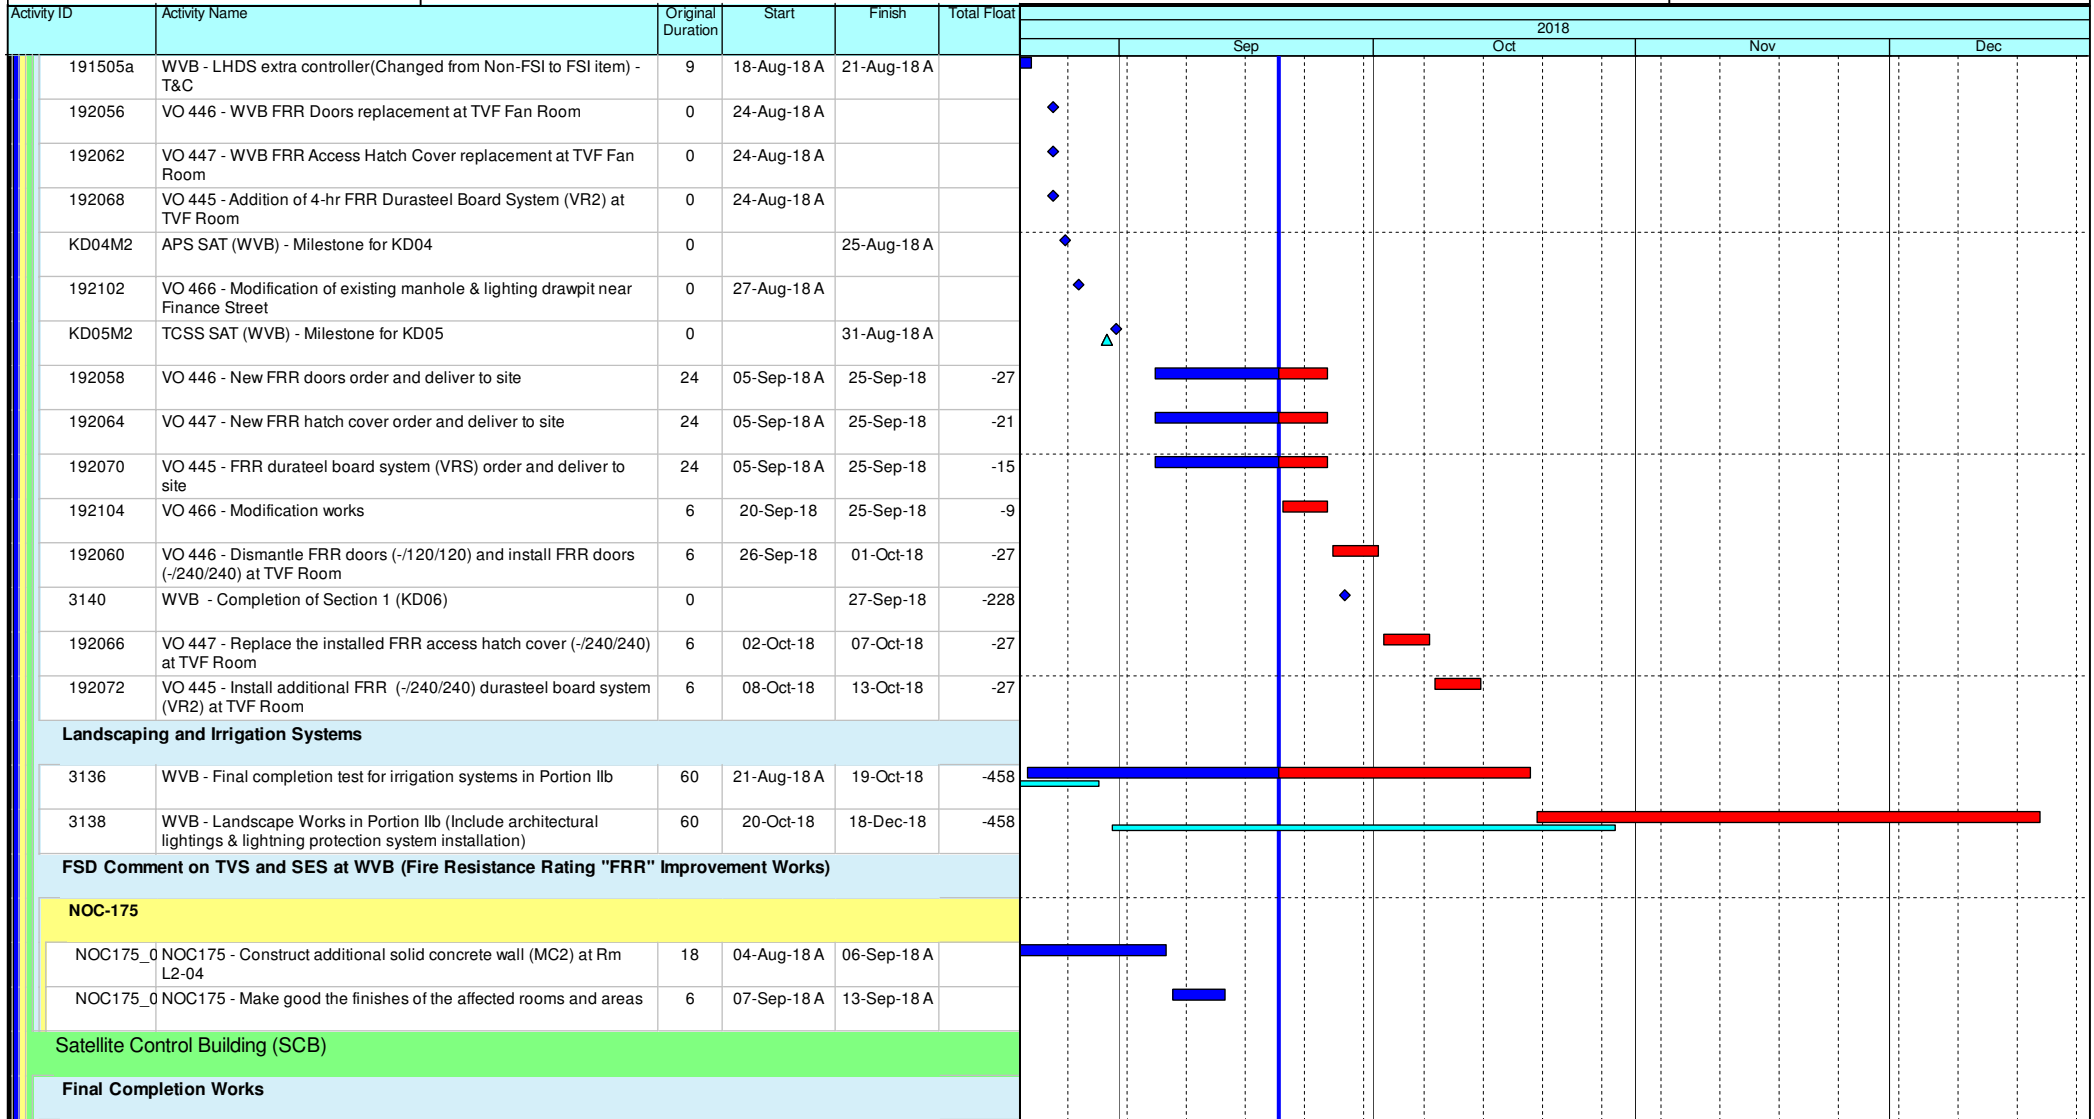

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING



Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 5 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

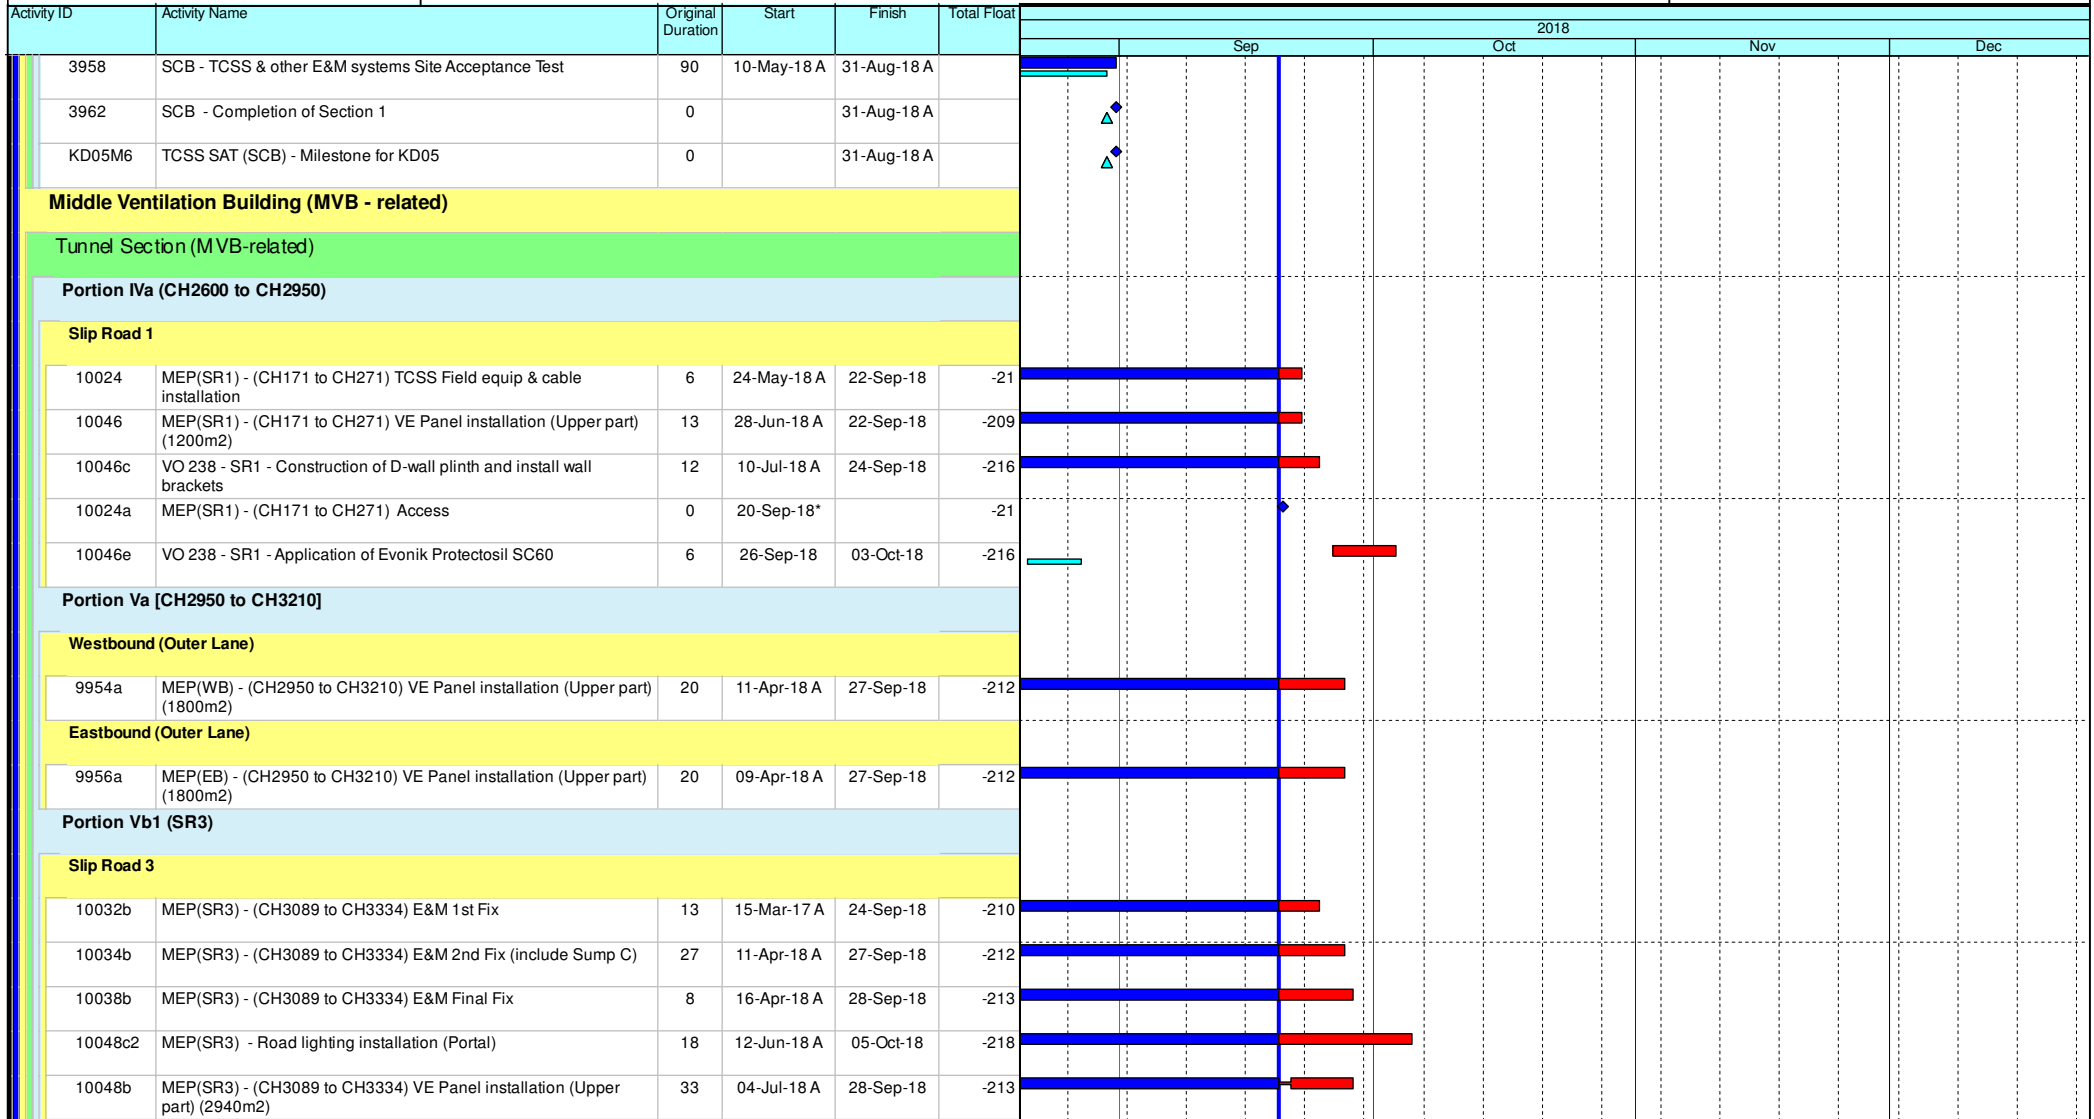

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING



Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 6 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

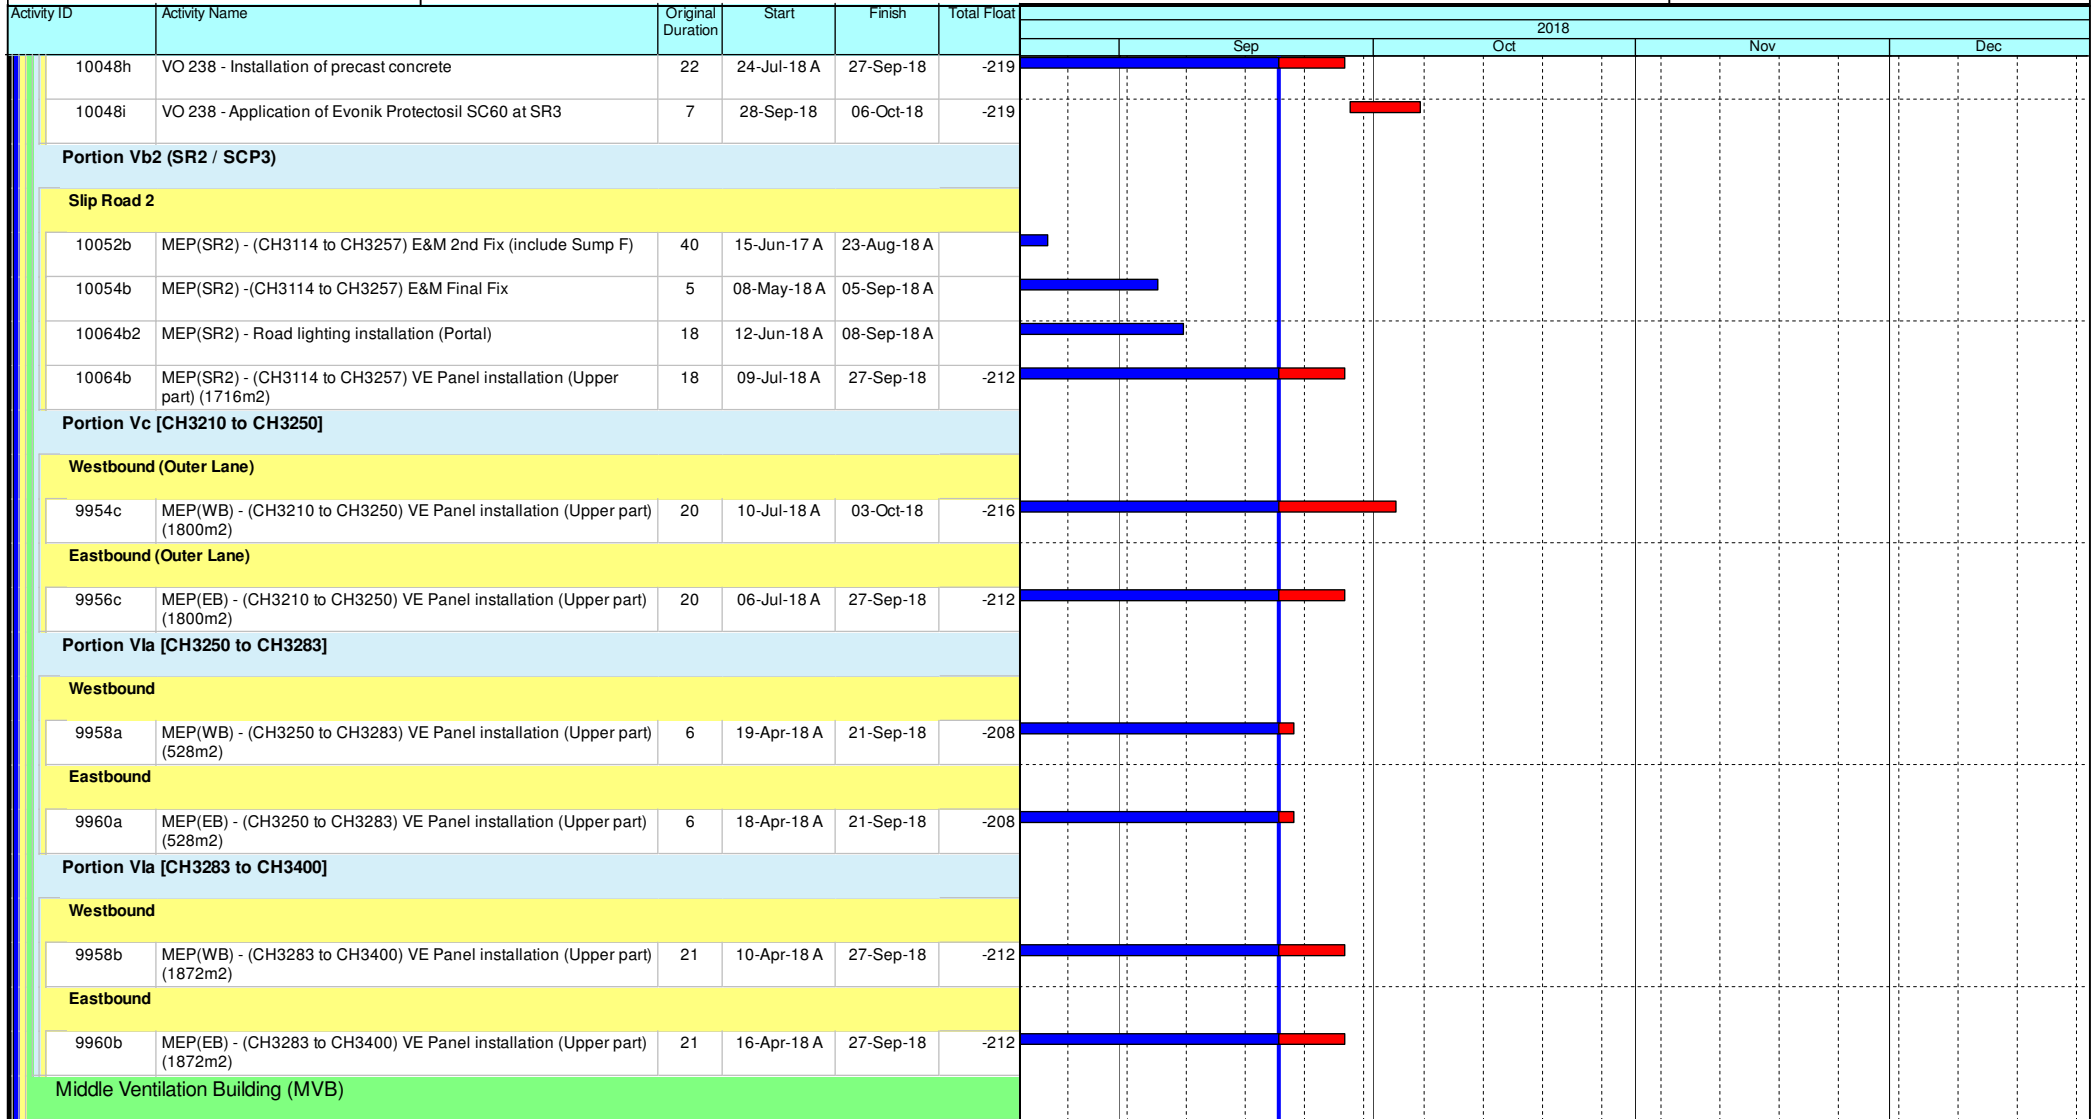

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING



Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 7 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

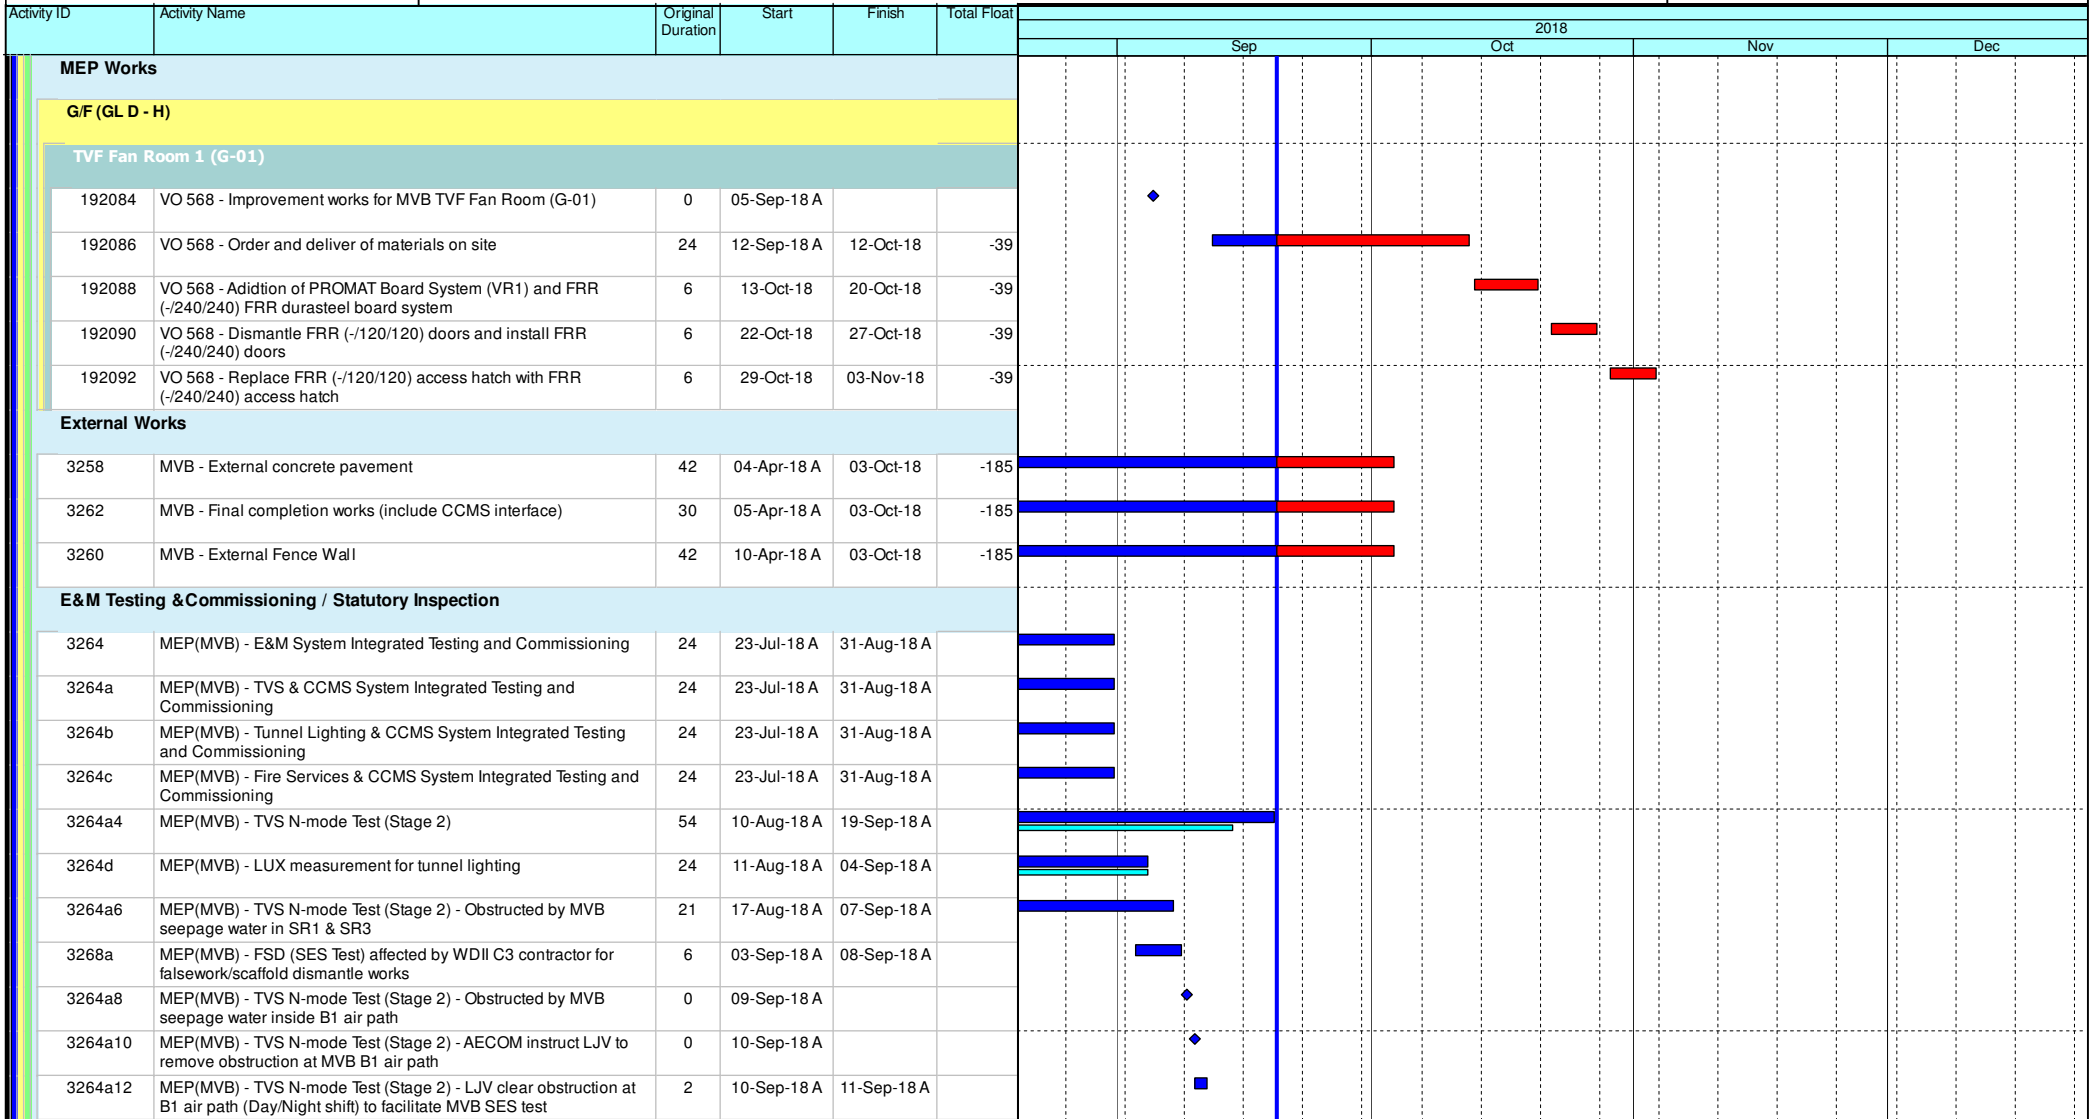

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING



Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 8 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

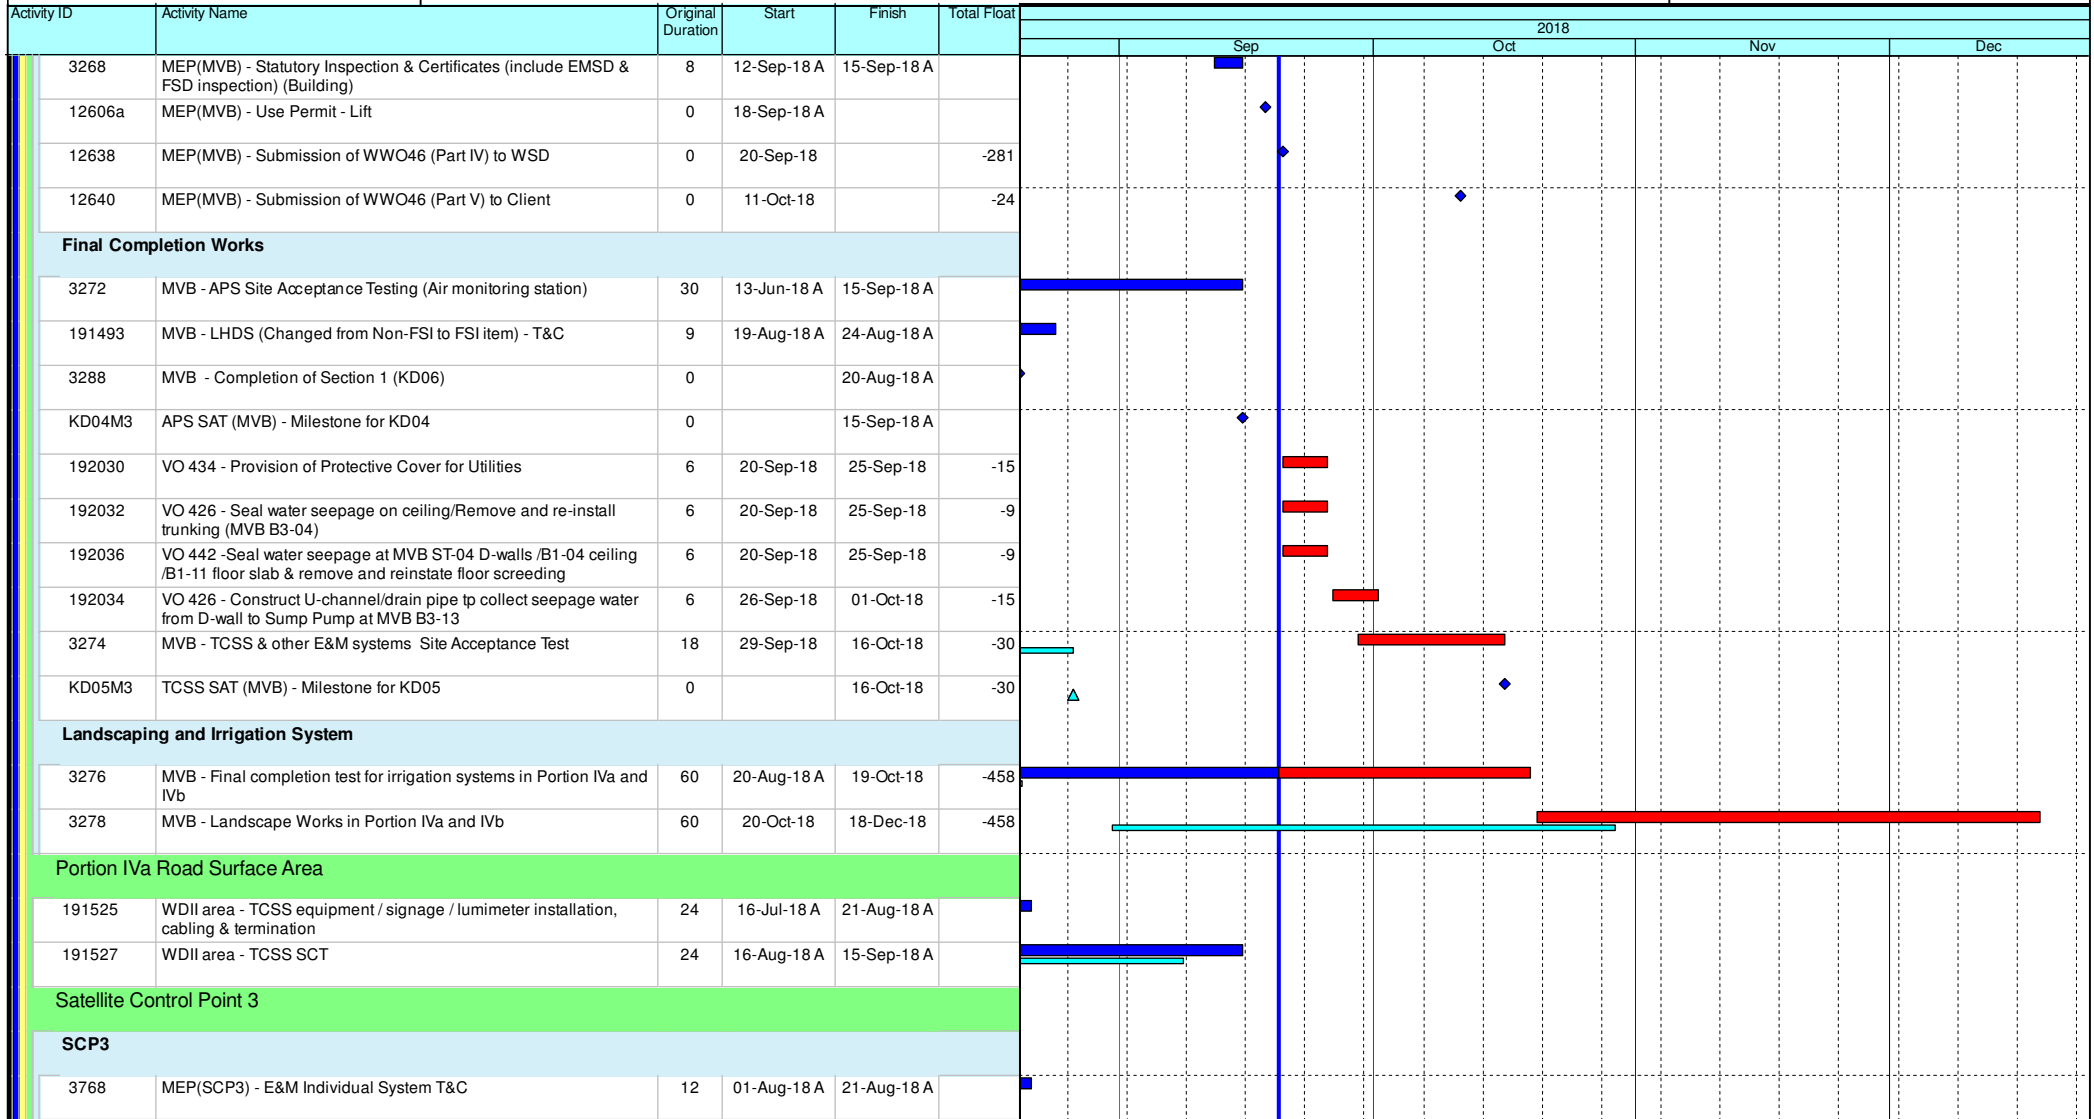

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING



Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 9 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

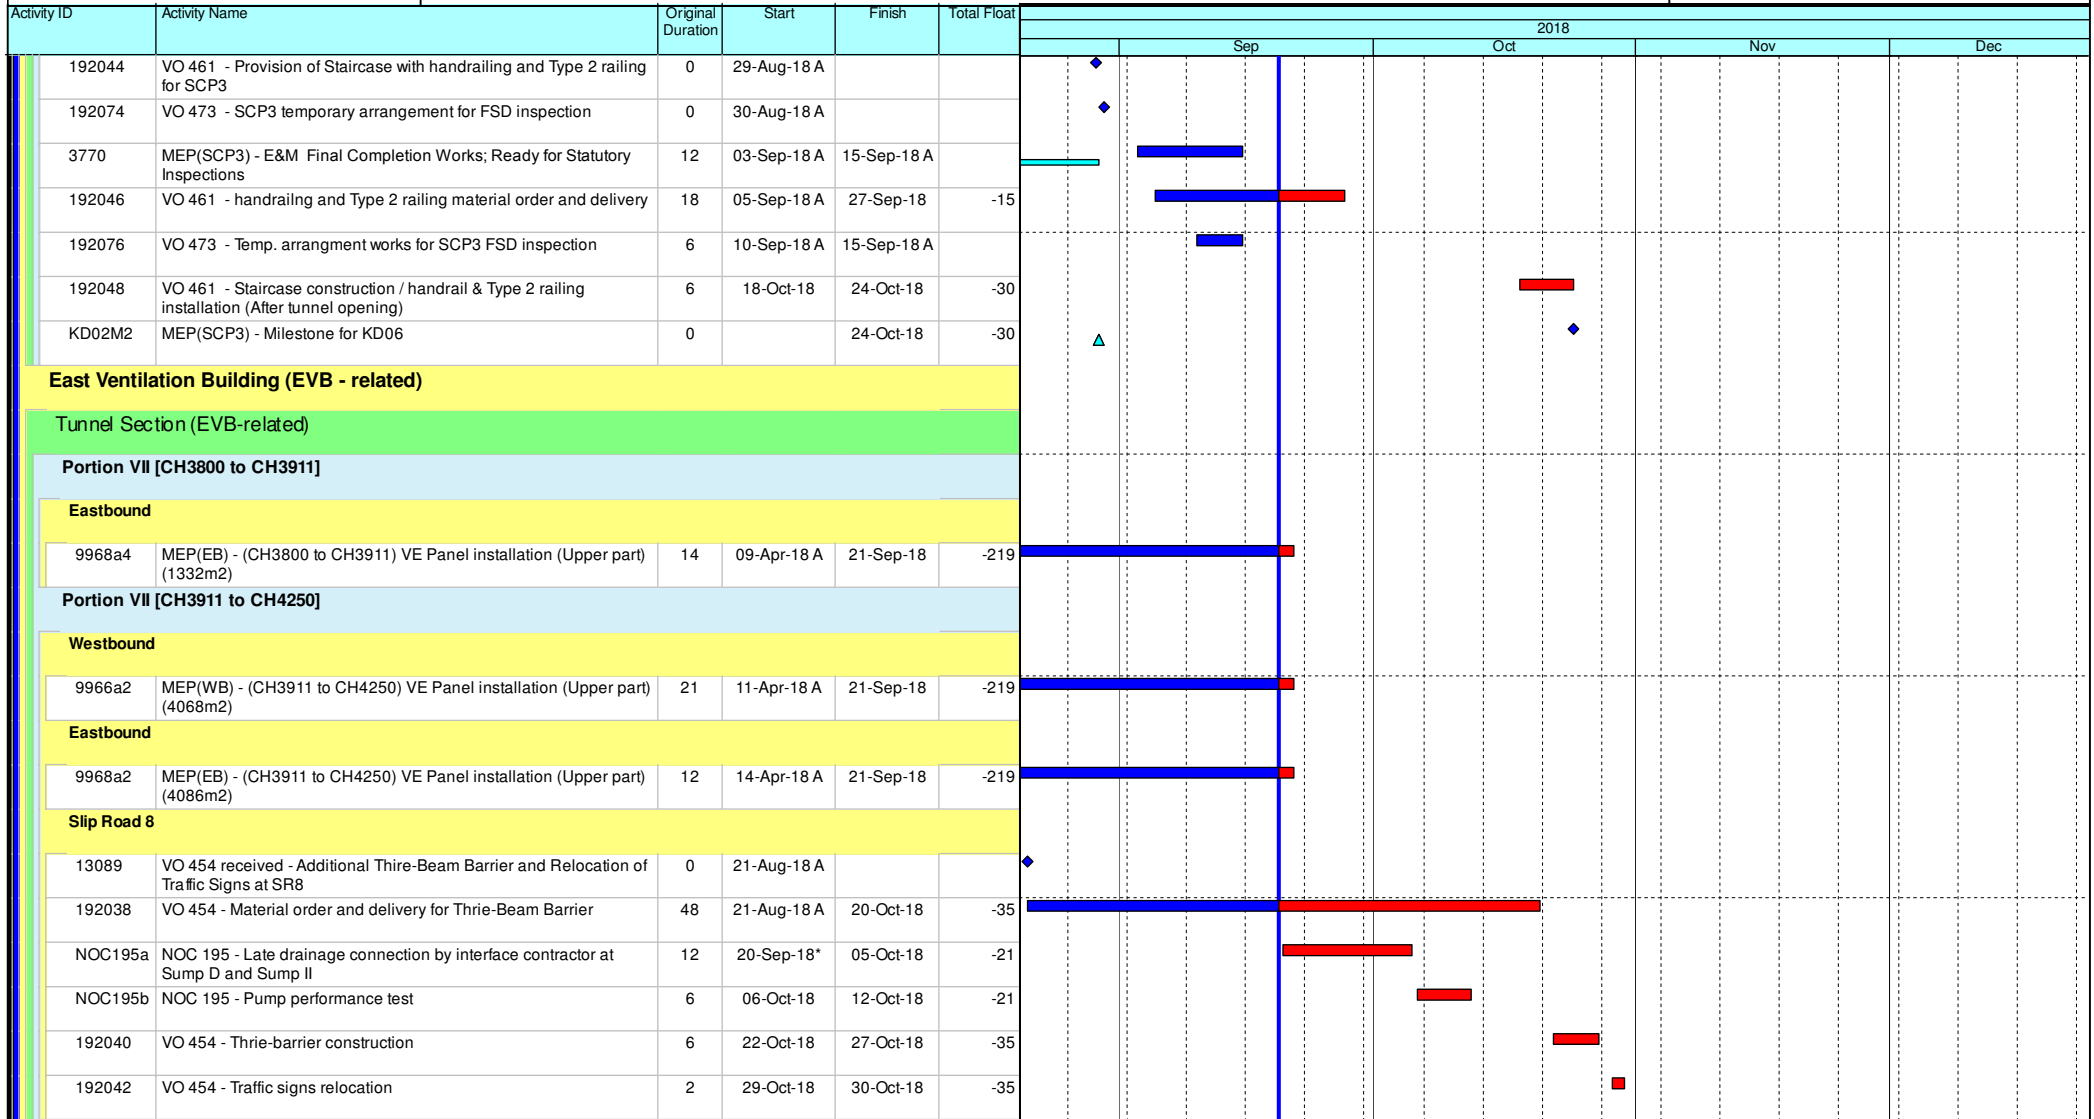

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING



Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 10 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

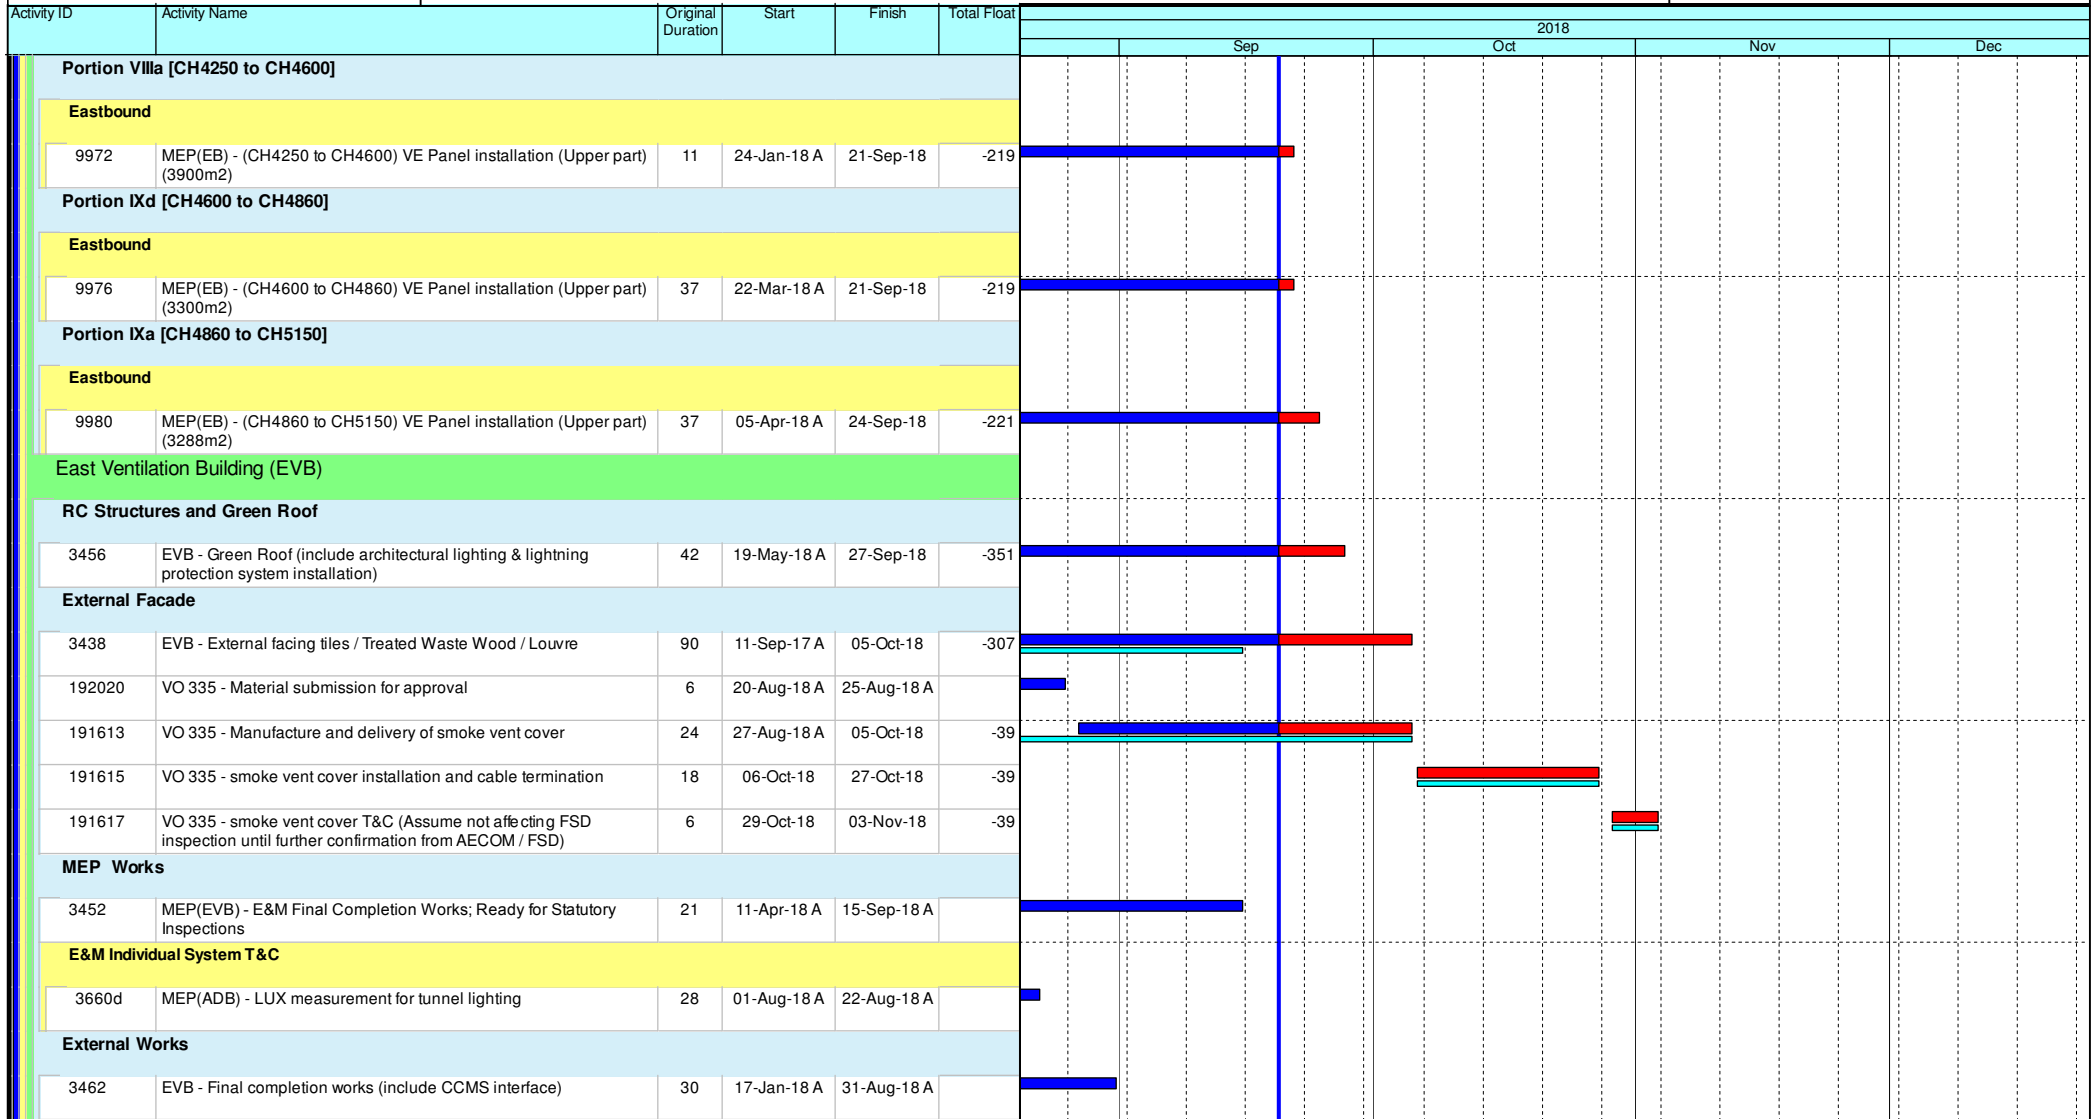

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING



Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 11 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

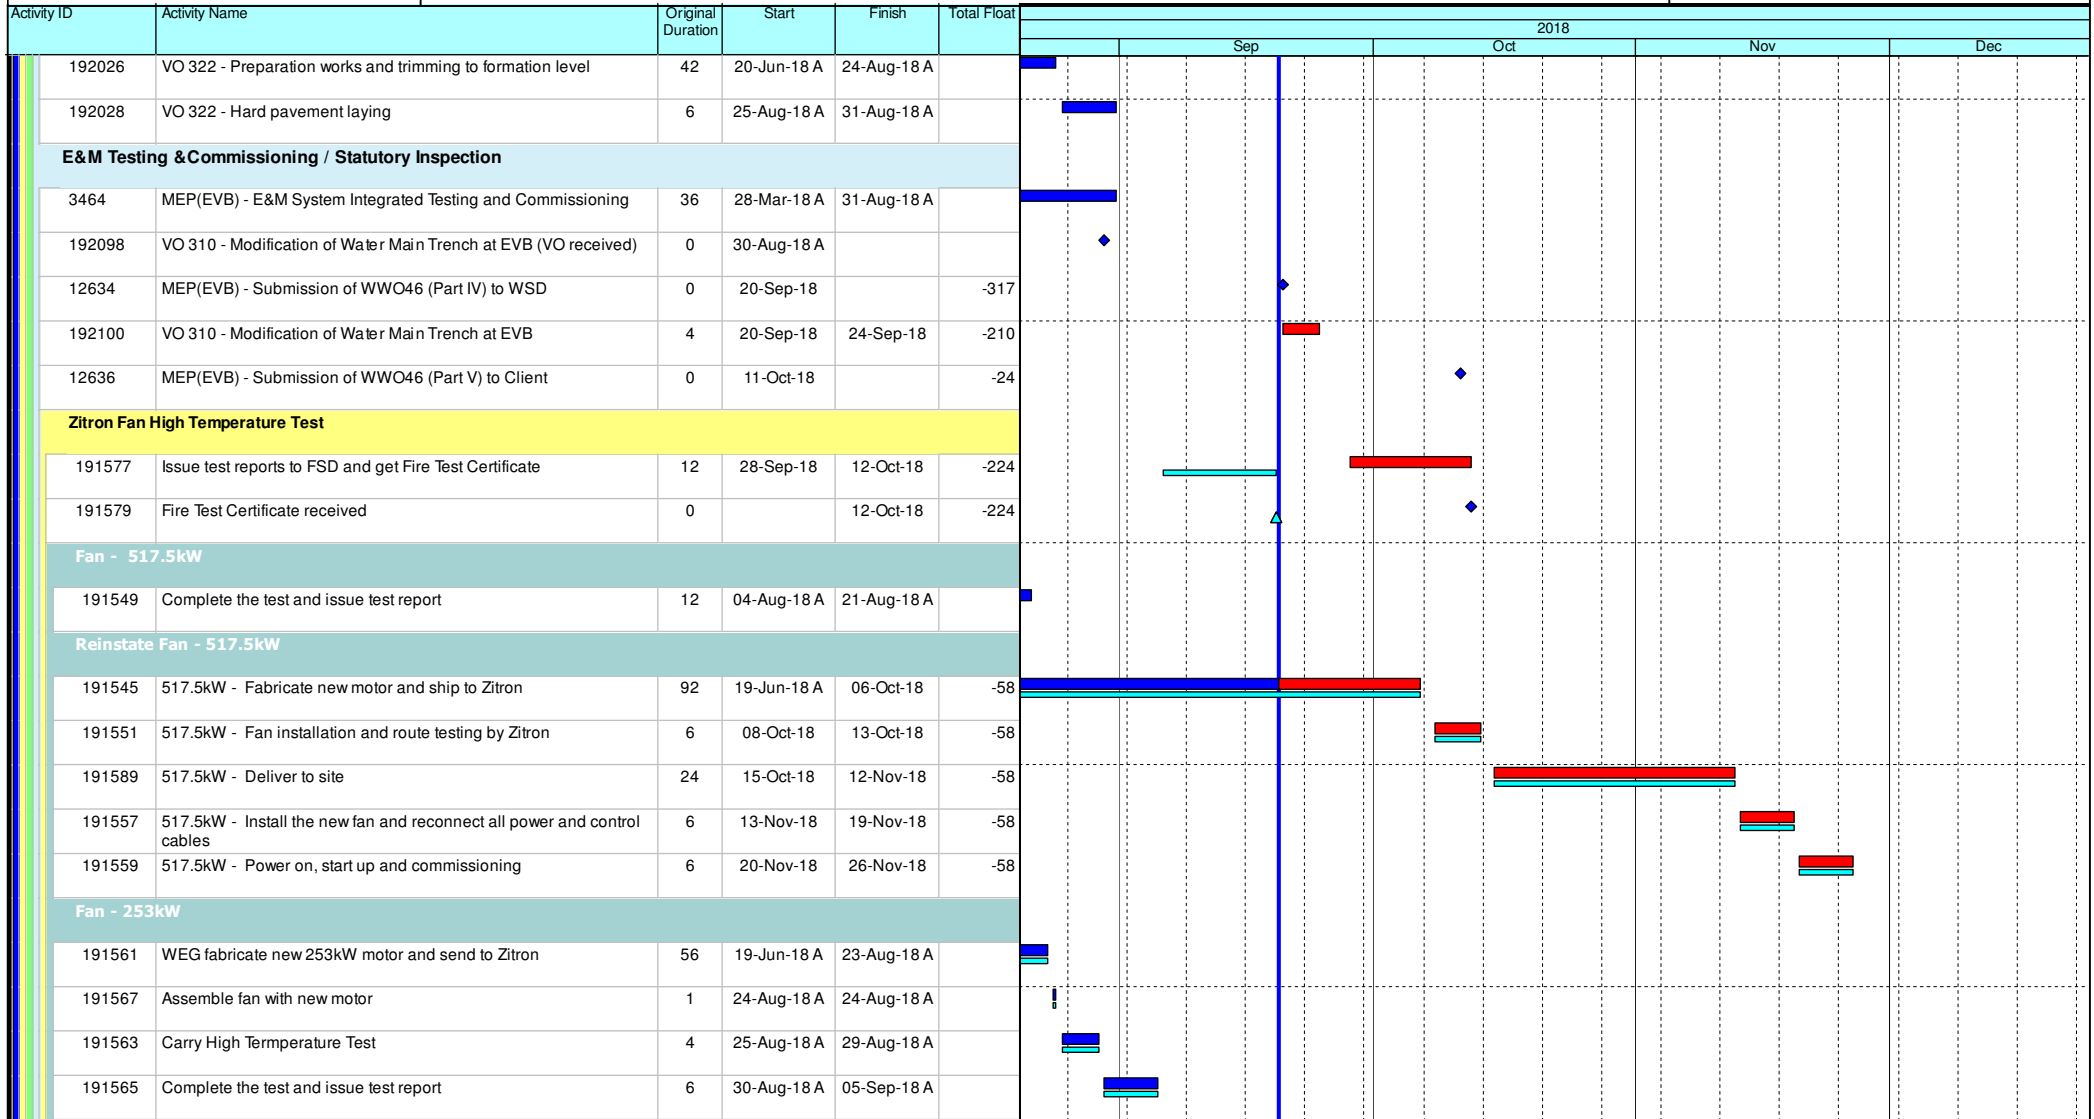

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING



Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 12 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

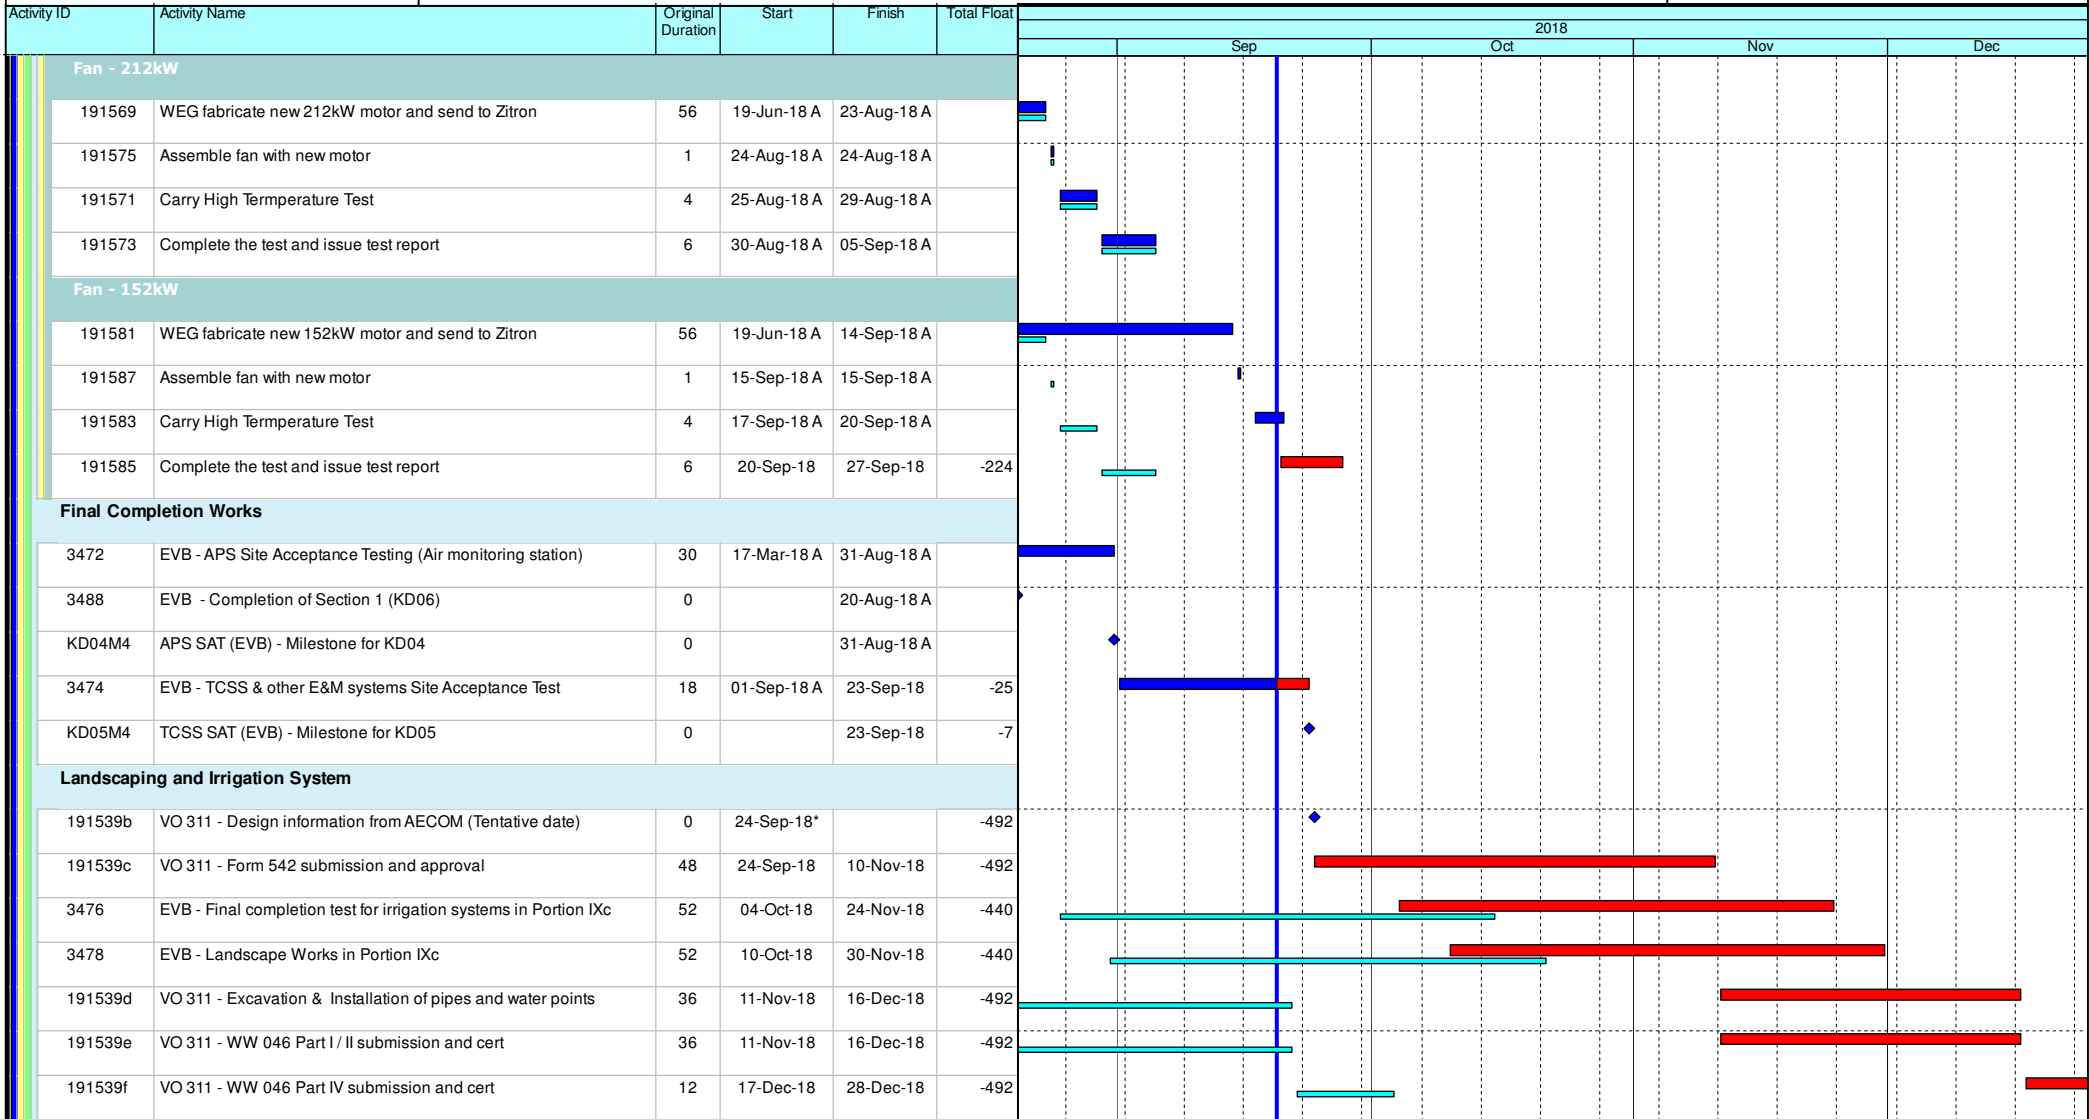

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING

Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 13 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Sep	Oct	Nov	Dec
191539g	VO 311 - Backfill	12	17-Dec-18	28-Dec-18	-492				
Tunnel Flexible Pavement (EVB-related)									
5818	Road(WB) - (CH3770 to CH5149.3) Road Marking & Traffic Sign	17	26-Jun-18 A	27-Sep-18	-222				
5826	Road(SR8) - (CH210 to CH1000) Road Marking & Traffic Sign	10	28-Sep-18	10-Oct-18	-222				
Administration Building (ADB)									
RC Structures (Portion Xa / Xb)									
13484	ADB - Green Wall	35	17-Dec-18	29-Jan-19	-402				
External Facade									
13248	ADB - External facing tiles / Louvre	48	27-Dec-17 A	06-Sep-18 A					
MEP & ABWF Works									
13252	ADB - Metal works / steel platform / Ladders / Handrails	42	13-Feb-18 A	30-Aug-18 A					
13258	MEP(ADB) - E&M Final Completion Works; Ready for Statutory Inspections	30	07-Sep-18 A	12-Oct-18	-344				
External Works									
13432	ADB - Road and drainage works (EVA)	42	11-Dec-17 A	05-Oct-18	-21				
13438	ADB - Final completion works (include CCMS interface)	90	09-Jan-18 A	05-Oct-18	-187				
13434	ADB - External concrete pavement (EVA)	24	18-Jan-18 A	09-Oct-18	-18				
13436	ADB - External Fence Wall (include metal gate)	130	18-May-18 A	12-Oct-18	-21				
3254f	VO 209 - VO Works installation (Street fire hydrant and water connection at EVA of ADB)	30	19-Jul-18 A	23-Aug-18 A					
3263b	VO 221 - Manholes by others to be modified to match with the final road and paved levels	48	27-Jul-18 A	27-Sep-18	-9				
E&M Testing & Commissioning / Statutory Inspection									
13446	MEP(ADB) - Statutory Inspection & Certificates (include EMSD & FSD inspection) (Building)	7	12-Jun-18 A	26-Sep-18	-10				
13458	MEP(ADB) - Submission of WWO46 (Part IV) to WSD	0	20-Sep-18		-222				
KD03M7	MEP(ADB) - Milestone for KD06	0		20-Sep-18	-3				
13446a	MEP(ADB) - Statutory Inspection & Certificates (FSD inspection) (SFH & EVA)	2	27-Sep-18	28-Sep-18	-10				

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline
- ▲ Baseline Milestone

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING



Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 14 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

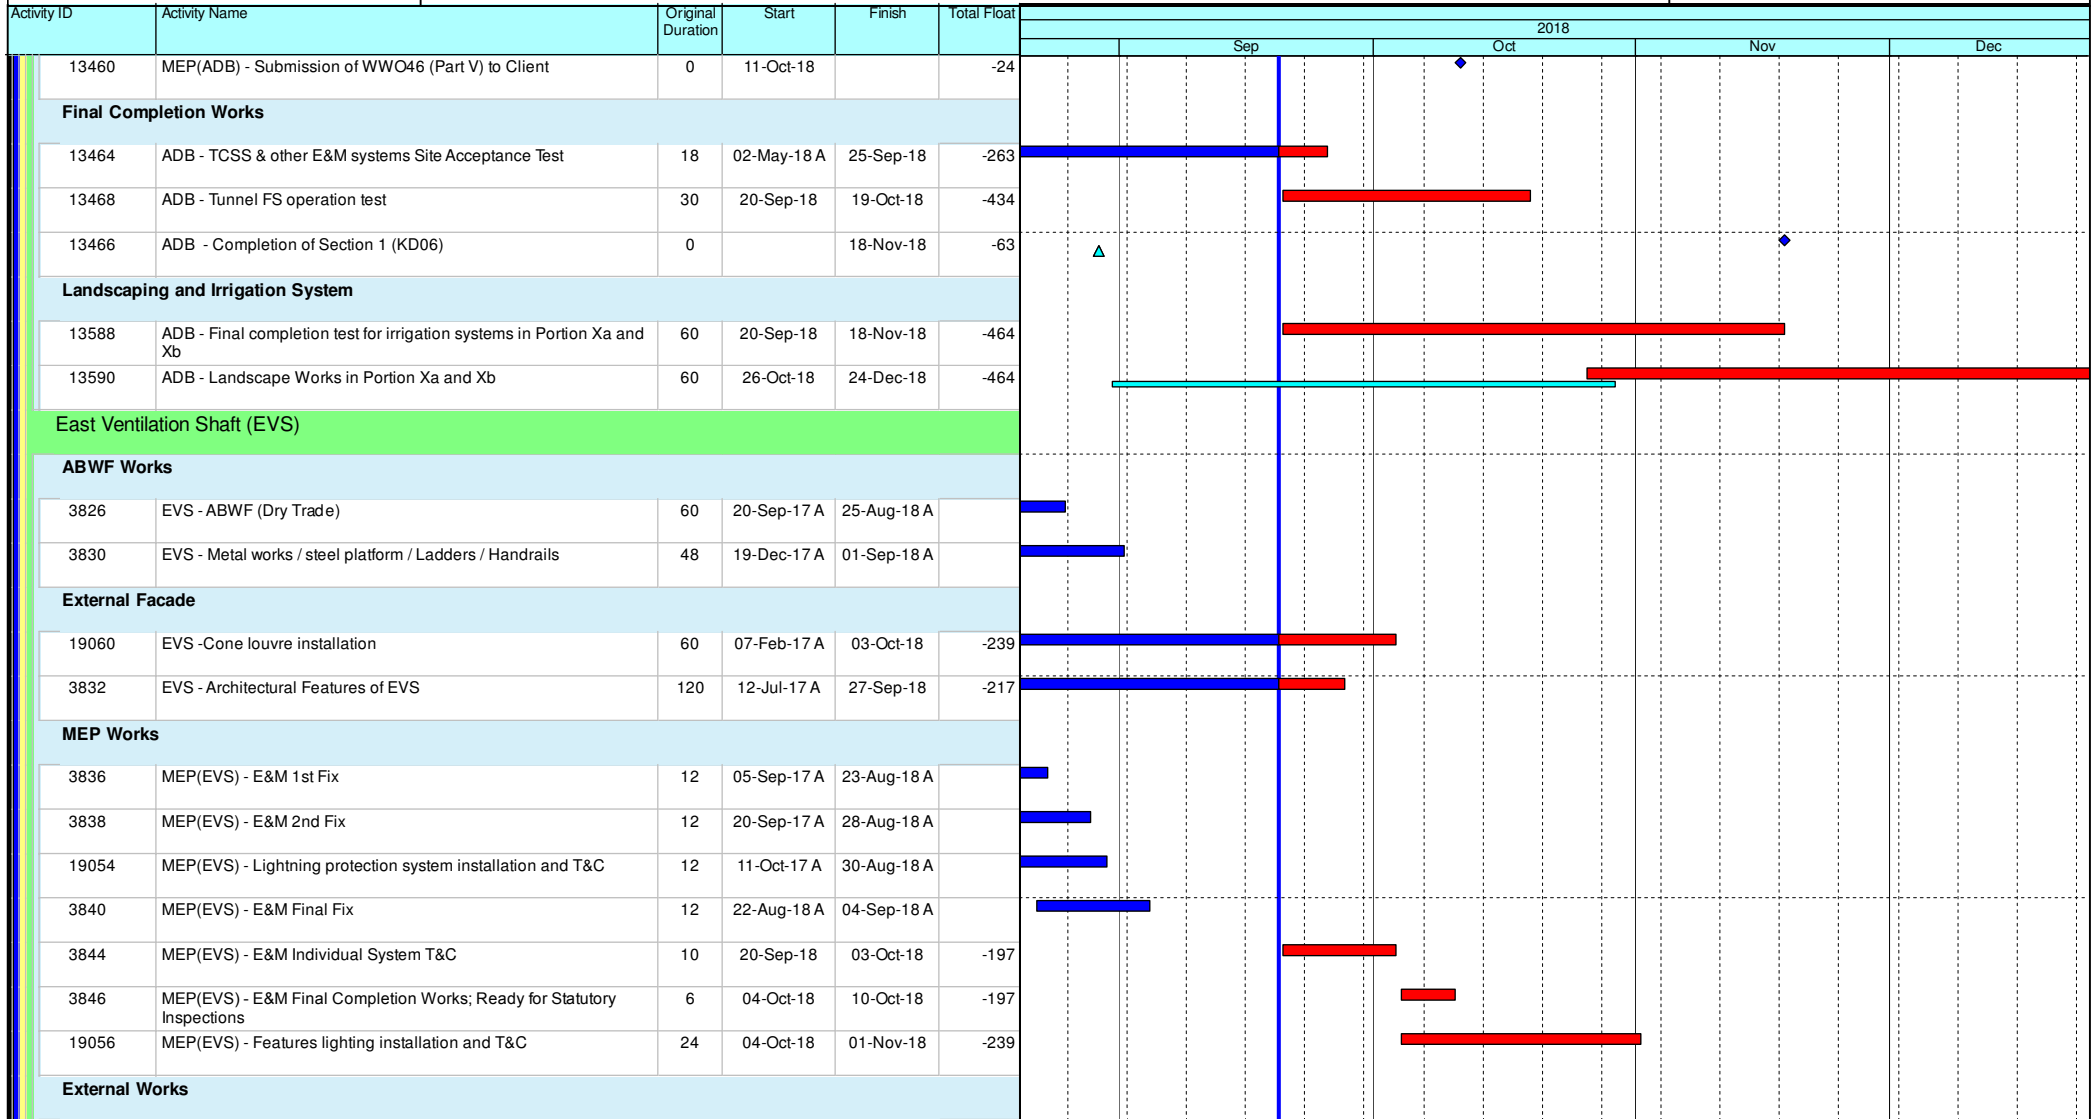

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING

Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 15 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018				
						Sep	Oct	Nov	Dec	
						192078	VO 443 - Improvement Works at EVS	0	23-Aug-18 A	
3850	EVS - External concrete pavement	12	04-Oct-18	18-Oct-18	-197		██████████			
3854	EVS - Final completion works (include CCMS interface)	12	04-Oct-18	18-Oct-18	-197		██████████			
192080	VO 443 - Scaffolding dismantle	6	02-Nov-18	08-Nov-18	-239			██████		
192082	VO 443 - Construction of the improvement works	24	09-Nov-18	06-Dec-18	-239			████████████████████		
E&M Testing & Commissioning / Statutory Inspection										
3856	MEP(EVS) - E&M System Integrated Testing and Commissioning	6	11-Oct-18	16-Oct-18	-248		██████			
3858	MEP(EVS) - Ready for Statutory Inspection (with EVB)	0	19-Oct-18		-249		◆			
KD03M4	MEP(EVS) - Milestone for KD03	0		19-Oct-18	-32		◆			
Final Completion Works										
3880	EVS - Completion of Section 1 (KD06)	0		06-Dec-18	-298				◆	
Satellite Control Points 4 / 5										
SCP5										
3886	SCP5 - External Works	24	18-Jun-18 A	29-Aug-18 A		██████████				
3882	MEP(SCP5) - E&M Individual System T&C	12	16-Aug-18 A	30-Aug-18 A		██████████				
3884	MEP(SCP5) - E&M Final Completion Works; Ready for Statutory Inspections	12	31-Aug-18 A	13-Sep-18 A		██████████				
KD03M5	MEP(SCP5) - Milestone for KD06	0		13-Sep-18 A			▲			
External Works										
Rumsey Street Flyover for Paymnet & Traffic Barrier										
5902p	RS - Pavement tie-in works at CORC W/B	30	14-Aug-18 A	05-Oct-18	-224	████████████████████	██████████			
5902g	RS - Install new directional sign	6	28-Sep-18	05-Oct-18	-224		██████			
5902r	RS - Road pavement tie-in E/B and W/B of CORC	6	06-Oct-18	12-Oct-18	-224		██████			
5902q	RS - Road marking	6	06-Oct-18	12-Oct-18	-224		██████			
5902m	RS - Demolish existing nosing and crush cushion	48	18-Oct-18	12-Dec-18	-143	████████████████████		████████████████████		

- ◆ Current Milestone
- █ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING

Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 16 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Sep	Oct	Nov	Dec
5904a	RS - Construct permanent parapet and nosing	102	18-Oct-18	23-Feb-19	-227				
5902n	RS - Paving works on Bridge B	12	01-Nov-18	14-Nov-18	-143				
Area A/B									
Area B									
Area B TCSS									
Approach Road / Landscape Deck / Noise Enclosure (No TTA)									
10288b4	Area B TCSS equipment Testing & Commissioning	25	16-Aug-18 A	11-Sep-18 A					
NOC 163 - Optical Fibre Damaged - Need to be Replaced (From Gantry ADS06 to ADB Computer Room)									
10288b1	TCSS optic fibre order and delivery	48	25-Jun-18 A	24-Aug-18 A					
10288b1	Pull out damaged cable (Require TTA for 1 night shift)	2	25-Aug-18 A	27-Aug-18 A					
10288b1	Lay the new cable from gantry ADS06 to ADB Computer room (Require TTA for 2 night shifts)	2	28-Aug-18 A	29-Aug-18 A					
10288b1	Cable termination at ADB Computer Room (Require TTA for 2 night shifts)	2	30-Aug-18 A	31-Aug-18 A					
Existing IEC (Live Traffic, TTA) - Night Shift									
10288b26	Area B TCSS equipment Testing & Commissioning	12	18-Aug-18 A	31-Aug-18 A					
Area B Tunnel Lighting									
Landscape Deck (Bay C1 to C5)									
Landscape Deck (Bay C1 & C2A-2 Remaining Bay (W/B))									
10288c3	T&C and energisation	6	11-Sep-18 A	22-Sep-18	-227				
10288c3	LUX measurement	18	24-Sep-18	16-Oct-18	-227				
Landscape Deck (Bay C1 & C2A-2 Remaining Bay (E/B))									
10288c4	T&C and energisation	3	16-Aug-18 A	22-Sep-18	-227				
10288c4	LUX measurement	18	24-Sep-18	16-Oct-18	-227				
Landscape Deck (Bay C2A-1 to B1 & C3 Bay (W/B))									
10288c5	T&C and energisation	6	11-Sep-18 A	22-Sep-18	-227				

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING



Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 17 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

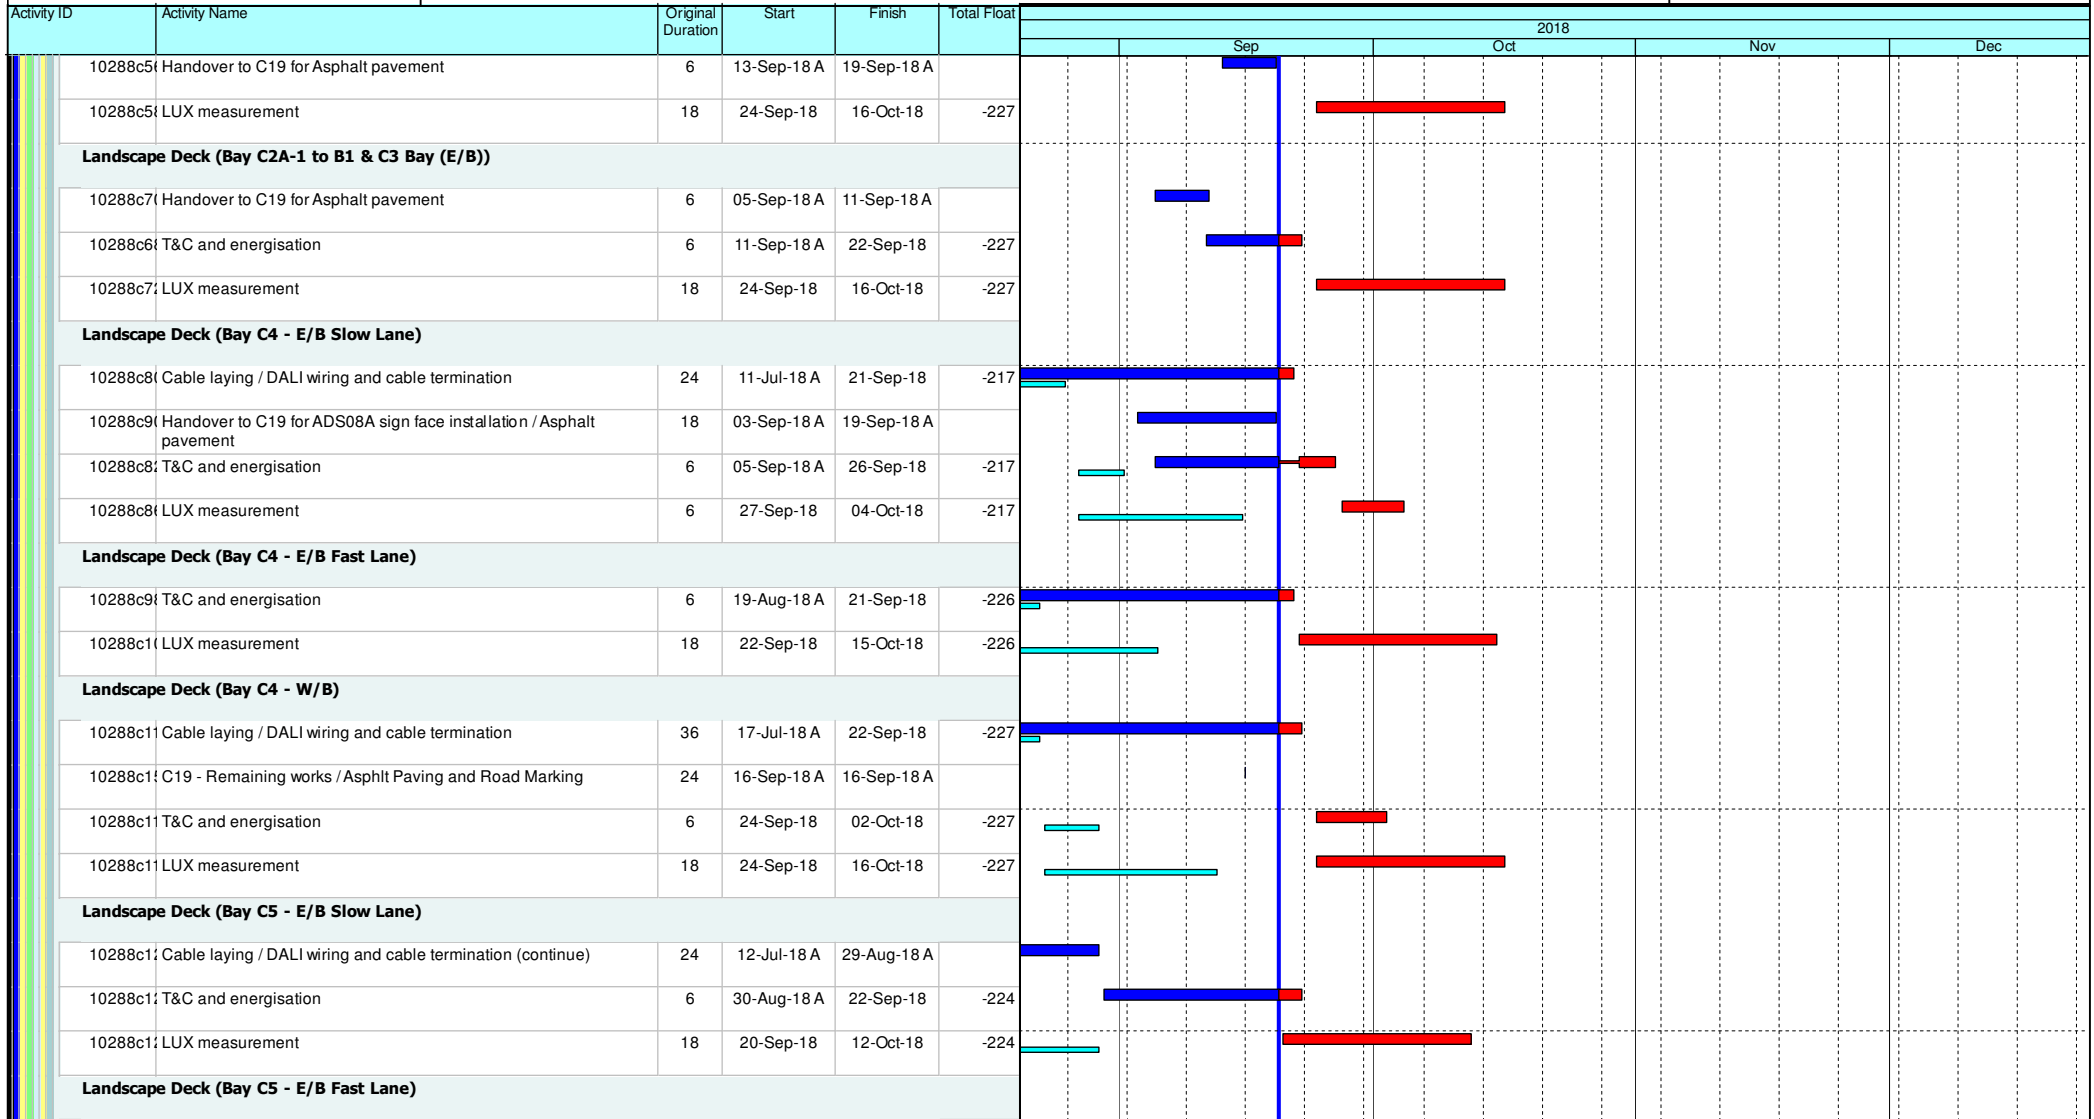

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING



Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 18 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

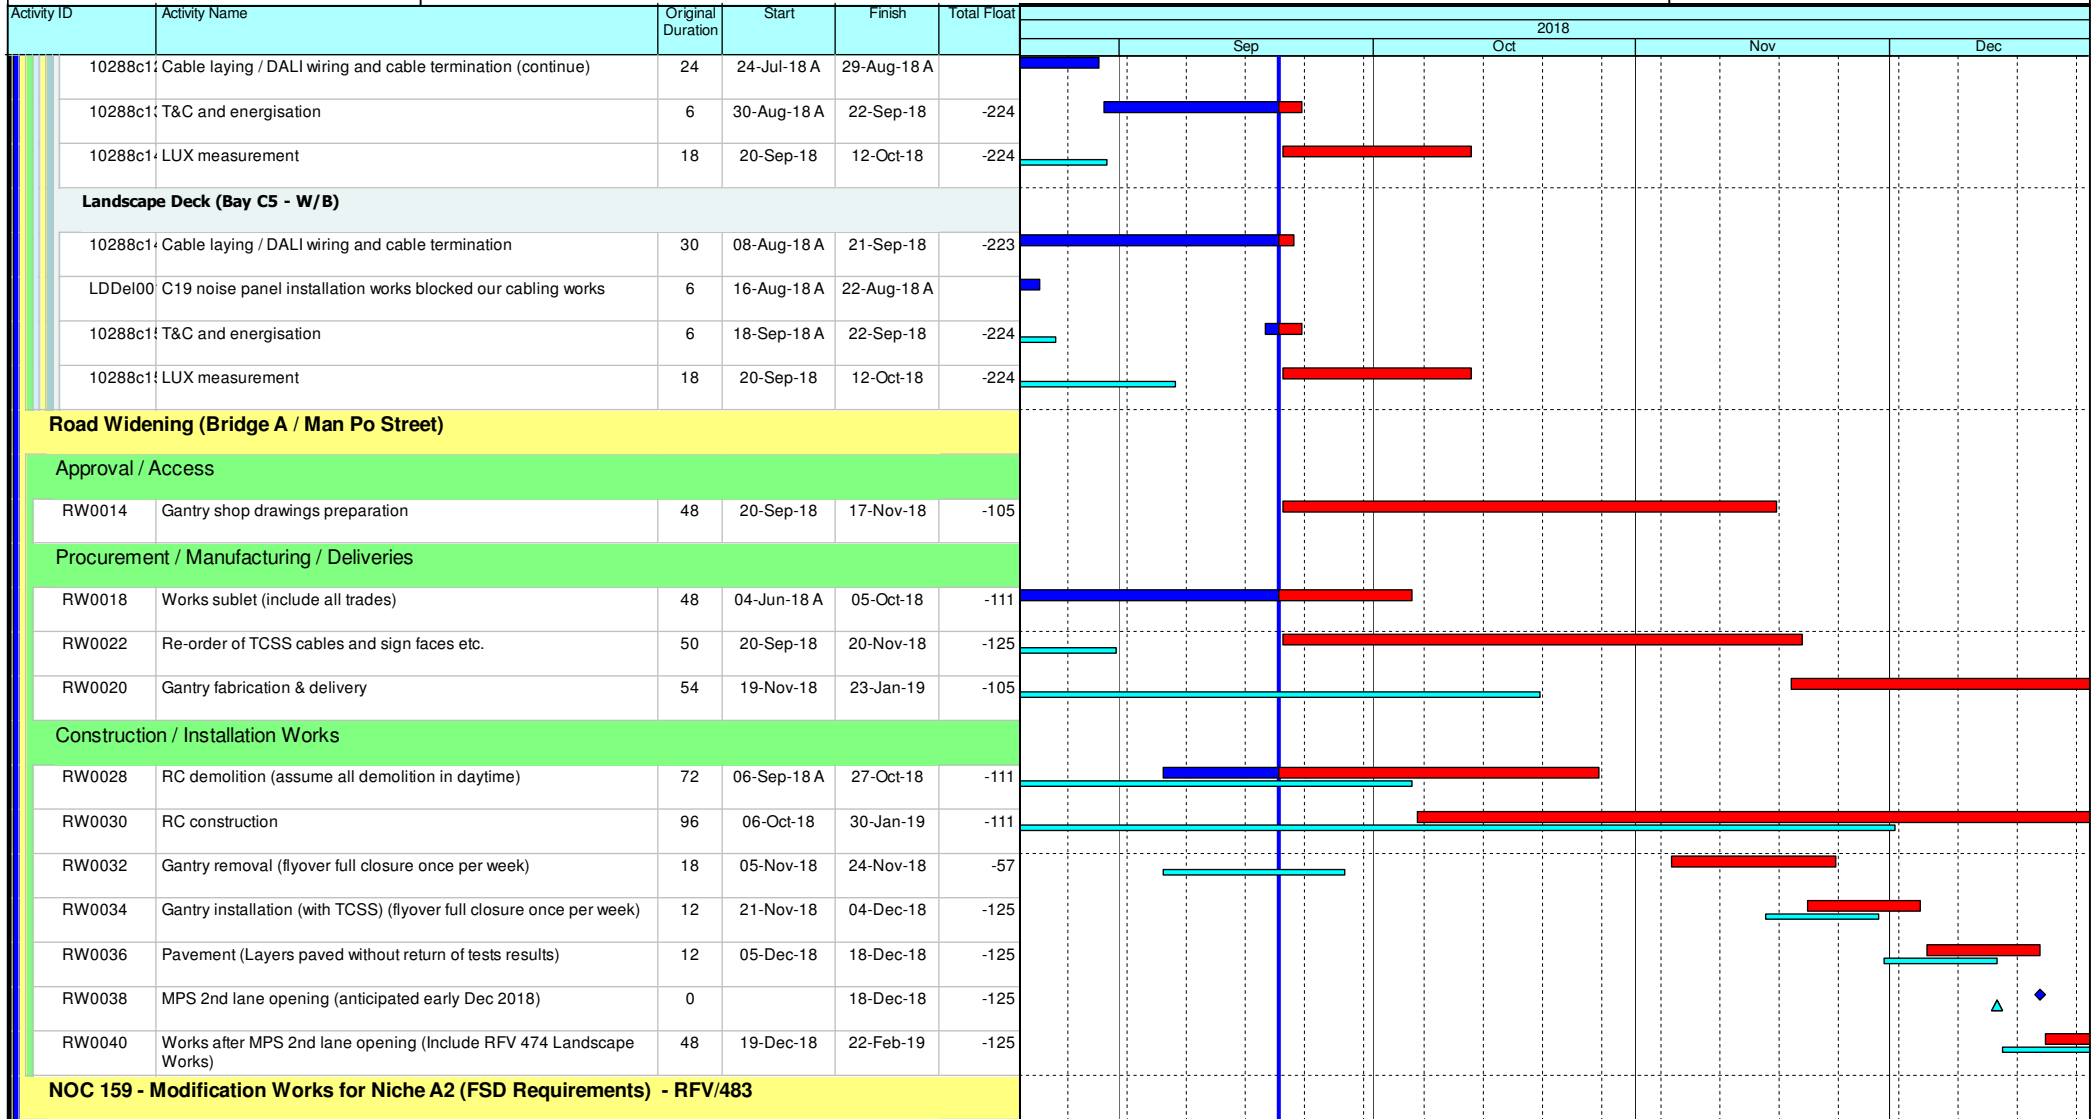

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING



Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 19 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

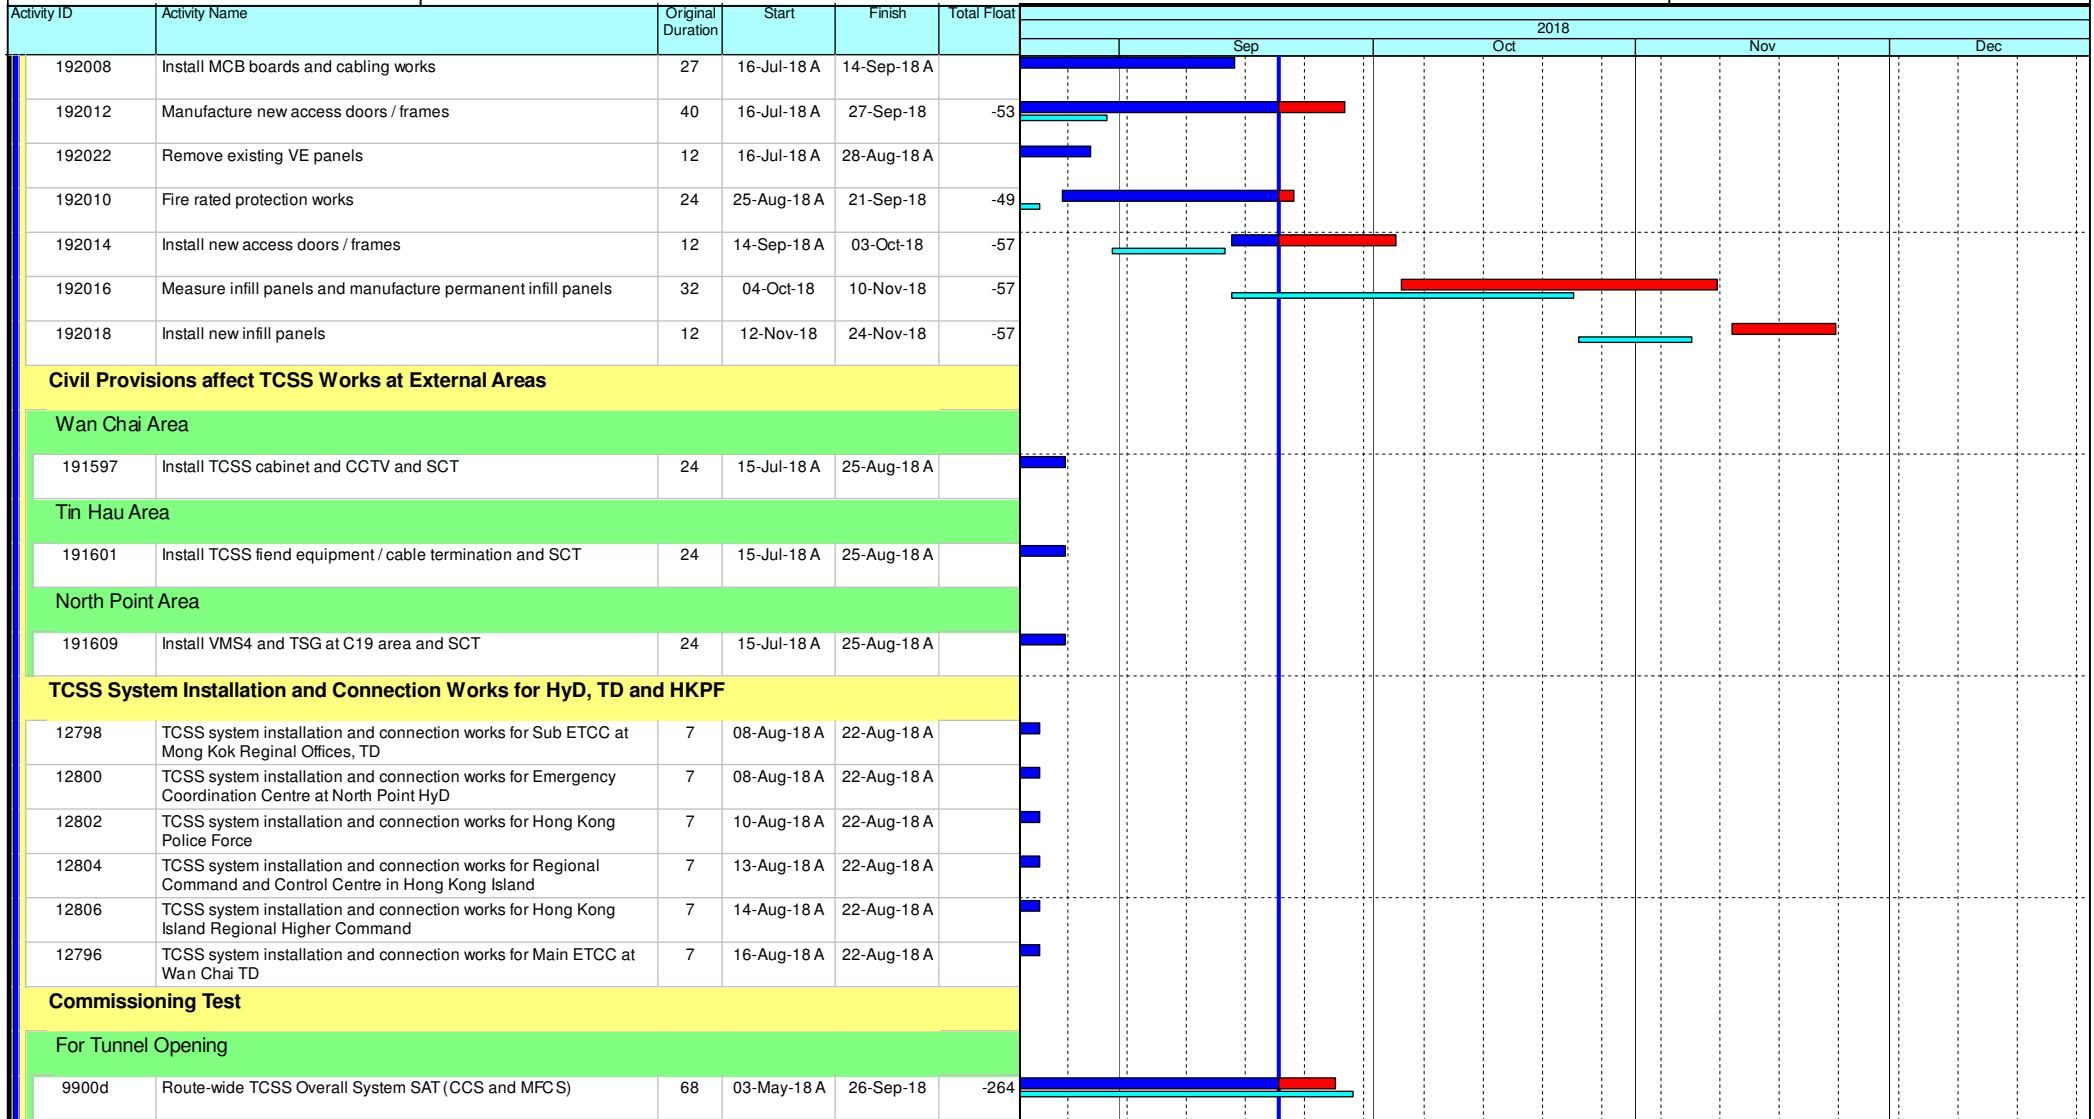

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING



Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 20 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

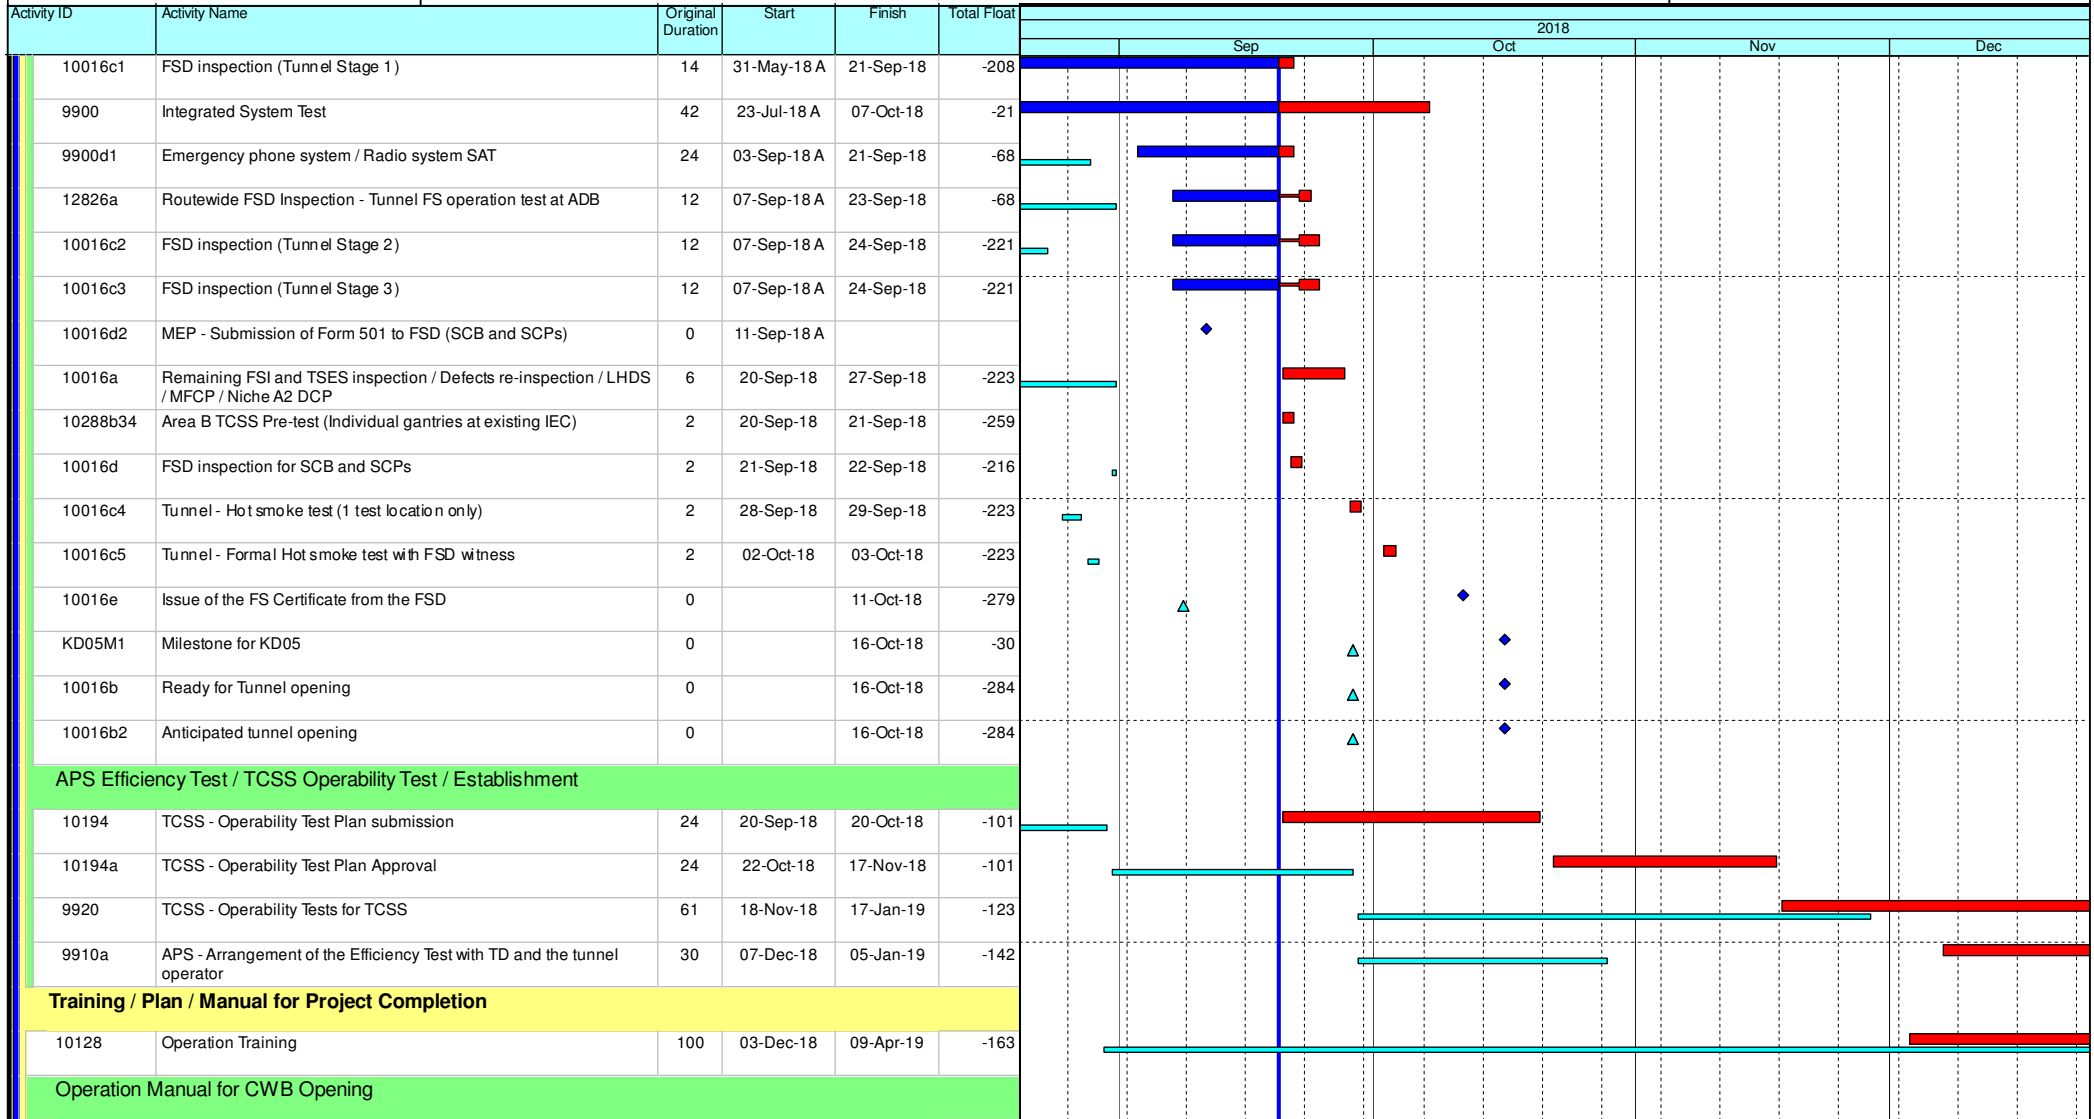

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING



Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 21 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

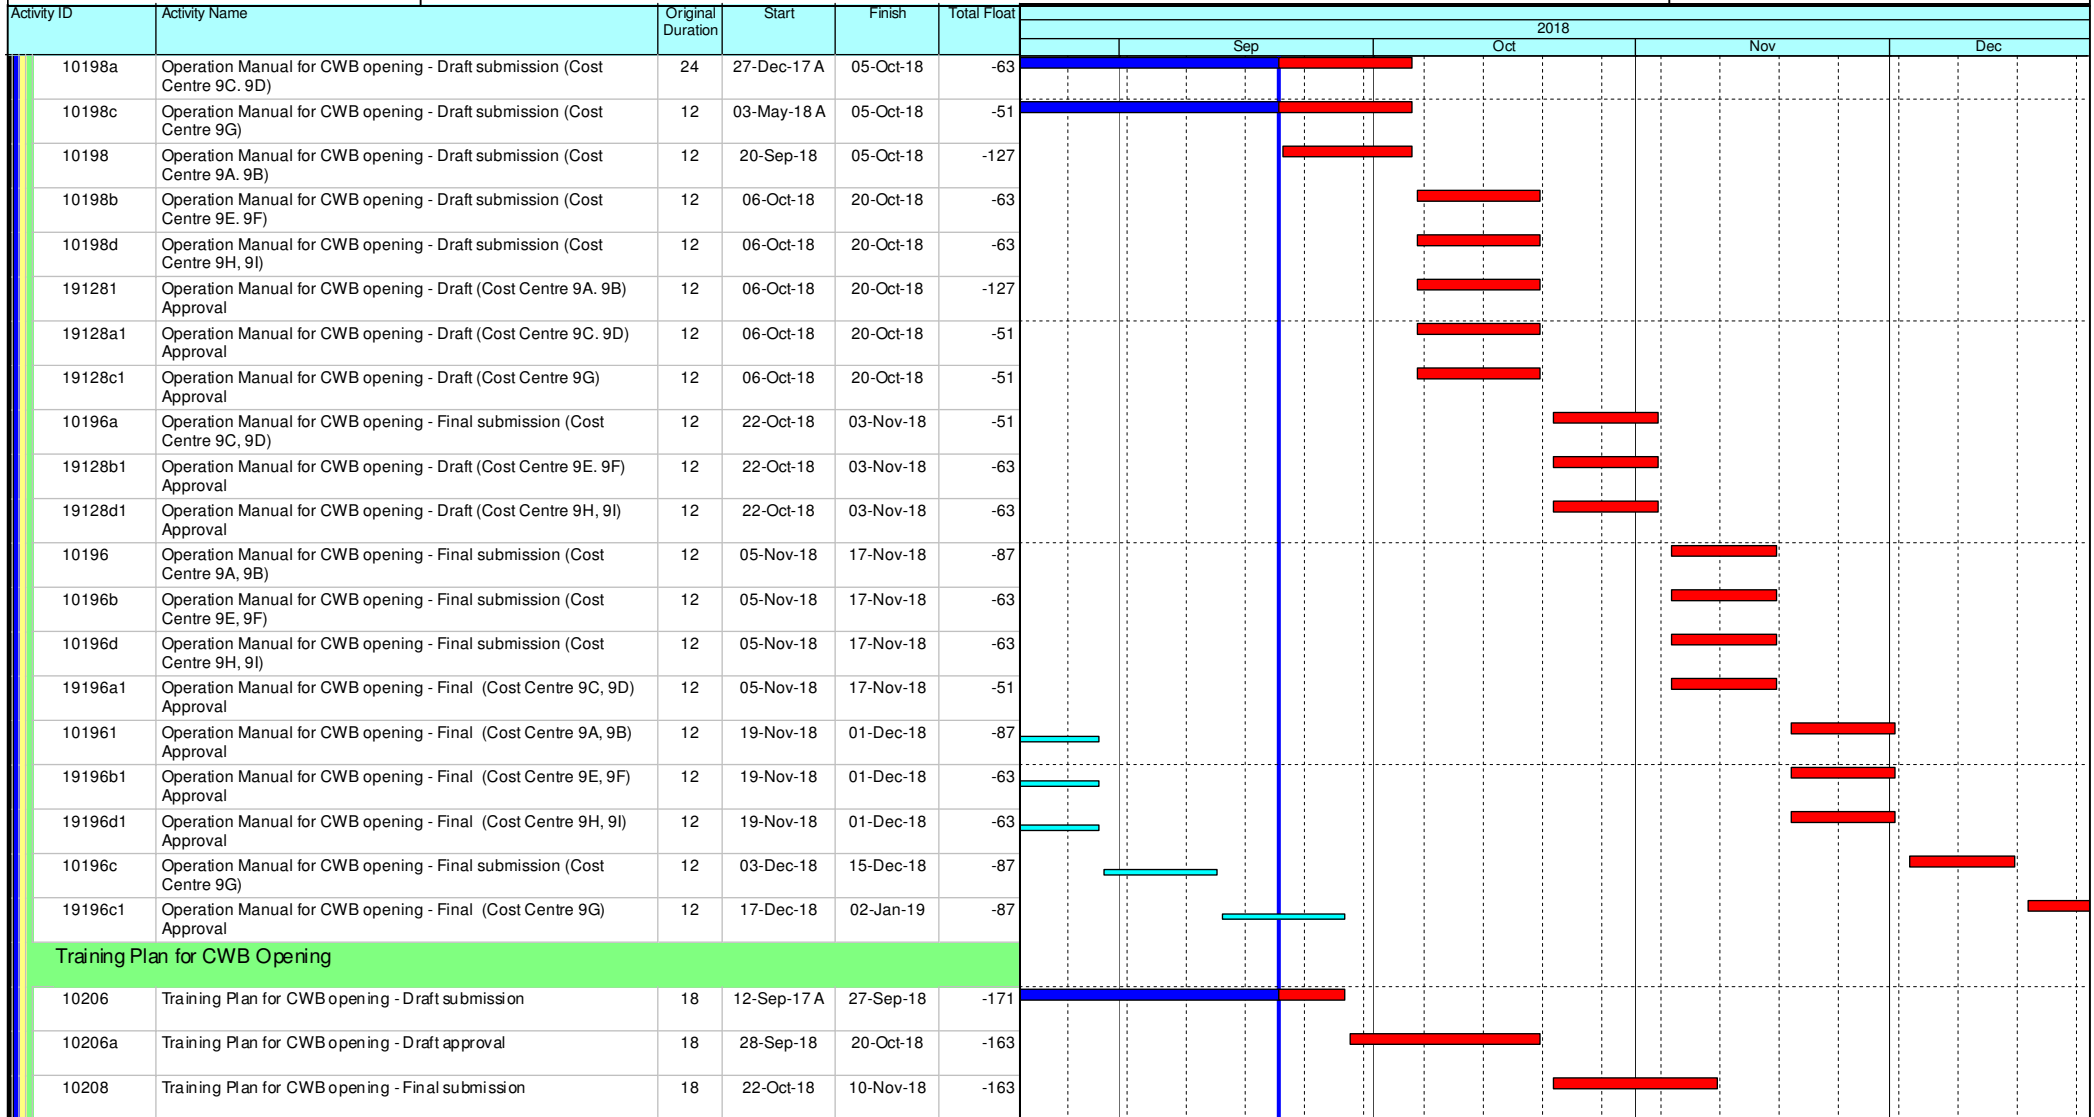

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING


Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 22 of 23








Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW

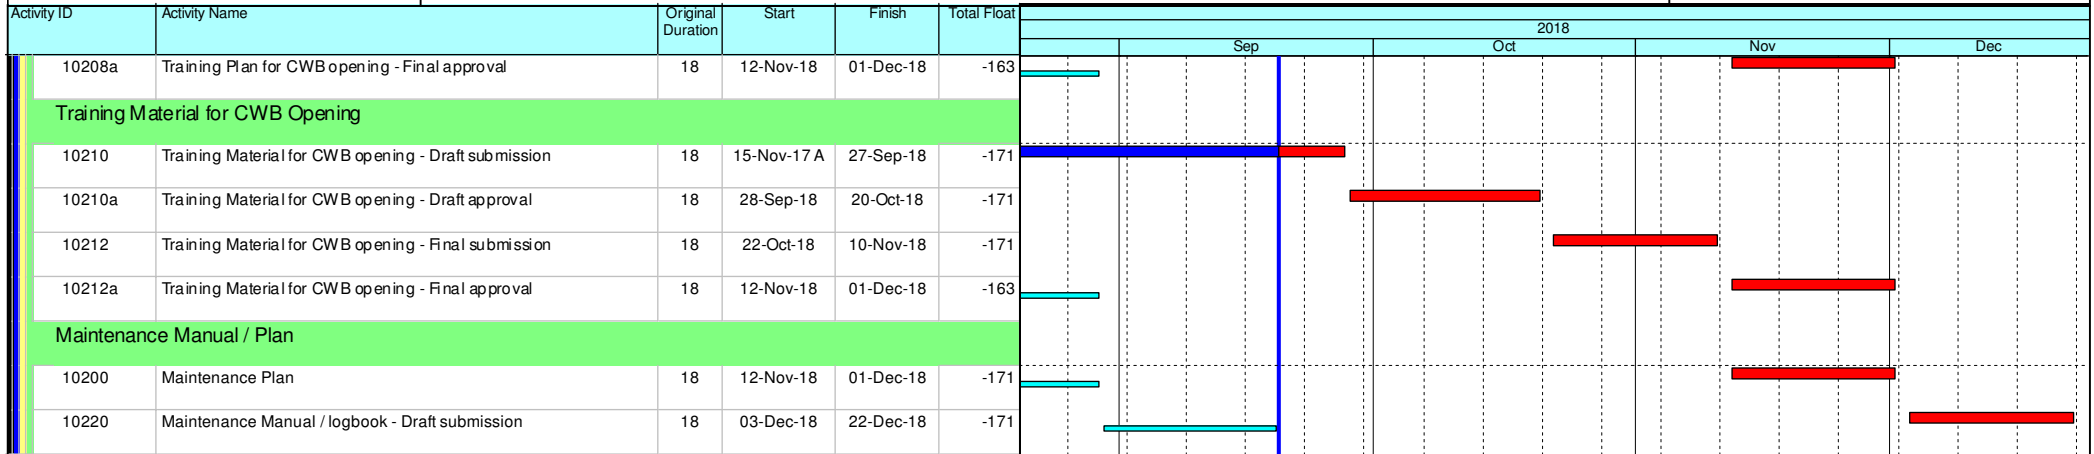Data Date: 20-Sep-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.



-  Current Milestone
-  Level of Effort
-  Baseline Milestone
-  Actual Work
-  Critical Remaining Work
-  Remaining Work
-  Project Baseline

Leighton Contractors (Asia) Limited Programme Update 55 (September 2018) THREE MONTH ROLLING

Project ID: H2613-U055
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U055
 Page 23 of 23

Date	Revision	Checked	Approv...
20-Aug-18	U054	AT	CW
20-Sep-18	U055	AT	CW
