



CONTRACTOR'S SUBMISSION

Contract No. HK/2009/02
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai East

To : **AECOM Asia Co. Ltd.** Attn : **Ms Gloria Tang**

CS Title : **Three-Month Rolling Programme (Version Date: 1 February 2019)**

CS Ref. : **CWCRGLJV/573/CS/PR/S-0295** Revision **K**

Status : -1st submission date : **9 February 2018**

Type of Submission : Design Drawings Method Statement Materials QA / QC
 Safety Environ. Programme / Progress Survey Others

Specification Ref. : **N.A.**

Drawing Ref. : **N.A.**

Submission Details : Please refer to attachment Please see below

We would like to further submit the Three-Month Rolling Programme Version Date: 1 February 2019 (Excel Version) with minor revision of the construction of subbase at Portion 5 to suit the latest information of delivery of subbase material after Lunar New Year for your information and comments.

Purpose of Submission : For review and approval For record purposes

Remarks:

From : Chun Wo - CRGL Joint Venture
Name : Paul Yu
Title : Project Manager
Signature :

Date :  February 2019

 PY/DY

Originator : Jeffrey Ng

**Wan Chai Development Phase II - East
 Central - Wan Chai Bypass at Wan Chai**

Contract: HK/2009/02

Remaining Works Programme

項目	工序	Jan-19													Wc																														
		Week 54			Week 55			Week 56			Week 01			Week 02																															
		1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13
1	Removal of Temporary Storage of Backfill material at Portion 5	Portion 5 運泥回填 WCR1 停止運泥因為Close P5 Exit													Portion 5 運泥回填 WCR1																														
2	Seawall海床	受泥區原海床													填600石面及鋪碎石(400m)																														
3	地面墊仔& 100mm Subbase																																					做墊仔							
4	舊直升機場, 海墜及梯台														舊直升機場Landing 清場 入機													打 pipe																	
5	打D-Wall	打D區D-Wall至+1.5 (-45M) 回填													打D區 remaining D-Wall至+1.5 (15M) 回填																														
6	U Channel & 沙井														北面東段4個catchpit+3000渠 (108m) DN8, 1 DN8, 2 DN8, 6 Culvert東邊3個catchpit+3000渠 Culvert DN8, 5 北面西段1個catchpit+300, 3750渠 (56m) DN1, 1 北面中段3000渠 北面中段3750 to Section drainage for the adjacent Area T (2個catchpit+300/450渠) DN3, DN2 BACKFILL													北面東段 DN8, 3 Culvert DN8, 5 北面中段 3750 to																	
7	渠網& 沙井														沙井 7350 and 7349 225呎由DN8, 5至7349 225呎由7350和7349至BCO CCTV 7352, 7346, 7328, 7327 試表 7353, 7338, C1, 3													225呎由 CCTV 7353																	
8	IRRIGATION PIPE	VVV542 (21/12/18)													subsoil drainage													approval of design	VVV046 46呎鋪土																
9	Fresh Water Main	TTA approved in TMLG Meeting 5/12/18																																											
10	HRR 馬路														FOOTPATH ALONG HRR AREA ABCD remove PMSMA Relay Area ABCD PMSMA AREA E remove and relay BC+PMSMA AREA F remove and relay BC+PMSMA REMEDIAL TO CONCRETE LAYBY survey remedial to concrete layby													excavated FOOTPATH																	
10.1	HRR FLYOVER REMAINING WORK														V0258 MODIFICATION WORK AT ABUTMENT ROOM V0253 PROVIDE STAINLESS STEEL LADDER AT ABUTMENT ROOM place order and delivery delivery																														
11	還原運泥街 Stage 0.5	EYA																																											
12	博覽道東, WCR1 & WCR3 未完成工作	* Portion 2 Zone 1 打石渠 行路面石渠 打石渠 軟formation * Zone 2a upto end of EYA 打石渠 打石渠 軟formation * Zone 2a remaining area 打石渠 * Portion 2 Zone 2b 打石渠 軟formation REMEDIAL TO EXPO DRIVE COVERED WALKWAY 打石渠 WCR3 填 Sub Base (100mm thk 7000m²) Caisson seawall defects 拆泥岩池 海墜填土及下COPING (COMMENCEMENT DATE TO BE CONFIRMED) WCR1&3 MAKE GOOD ARMOUR SLOPE PROFILE													subsoil 軟formation 軟formation 軟formation 軟formation subsoil 拆泥岩池																														

Wan Chai Development Phase II - East
Central - Wan Chai Bypass at Wan Chai
Contract: HK/2009/02
Remaining Works Programme

項目	工序	June																																		
		Week 18					Week 19					Week 20					Week 21					Week 22														
		27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30
1	Removal of Temporary Storage of Backfill material at Portion 5																																			
2	Seawall 海床																																			
3	地面墊仔 100mm Subbase																																			
4	舊直升機塔, 海墜及梯台																																			
5	打D-Wall																																			
6	U Channel & 沙井																																			
7	渠網 & 沙井																																			
8	IRRIGATION PIPE																																			
9	Fresh Water Main																																			
10	HHR 馬路																																			
10.1	HHR FLYOVER REMAINING WORK																																			
11	還原運盛街 Stage 0.5																																			
12	博覽道東, WCR1 & WCR3 未完成工作																																			

**CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019							
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
HK/2012/08 Revised Works Programme Rev.12.0(DD 20 November 2017)																									
Key Dates and Milestone Dates																									
Sections of Works Completion (Included Not Granted EOT Entitlement of The Contractor)																									
KD10840	Completion of Section IIIA	0		08-Sep-18*	0%																				
KD10860	Completion of Section IV	0		30-Aug-18*	0%																				
KD10880	Completion of Section V	0		26-Sep-18*	0%																				
KD11010	Completion of Section VII	0		14-Sep-18*	0%																				
KD11020	Completion of Section VIII	0		21-Sep-18*	0%																				
KD11040	Completion of Section IX	0		21-Sep-19*	0%																				
KD11060	Completion of Section X	0		21-Sep-18*	0%																				
Planned Sections of Works Completion																									
KD10080	Planned Section IIIA Completion - Road A2,A4, A5	0		08-Sep-18	0%																				
KD10100	Planned Section IV Completion - Slip Road 3	0		30-Aug-18	0%																				
KD10140	Planned Section V Completion - Remaining At-Grade Road	0		26-Sep-18	0%																				
KD10280	Planned Section VII Completion - Remainder Works	0		14-Sep-18	0%																				
KD10300	Planned Section VIII Completion - Landscape Softwork	0		21-Sep-18	0%																				
KD10320	Planned Section IX Completion - Establishment Works	0		21-Sep-19	0%																				
KD10340	Planned Section X Completion - Tree Protection & Preservation	0		21-Sep-18	0%																				
Dredging and Reclamation																									
Marine Work Construction																									
Zone CRIII																									
Seawall Construction - Zone CRIII																									
Zone CRIII Seawall- 2nd Stage																									
Seawall 2 & 12																									
MAR21371	Zone CRIII - seawall 2 & 12 - Backfilling remaining portion (type A, geotextile and filter)	0	19-Jan-18 A	27-Jan-18 A	100%	■																			
Zone D																									
Seawall Construction - Zone D																									
Seawall 10 & 11																									
MAR20630	Zone D - Seawall 10 & 11: Install remaining seawall block	14	20-Feb-18*	05-Mar-18	0%		■																		
MAR20650	Zone D - Seawall 10 & 11: Backfill Type A	7	06-Mar-18	12-Mar-18	0%			■																	
MAR20670	Zone D - Seawall 10 & 11: Lay geotextile and filter	7	13-Mar-18	19-Mar-18	0%			■																	
Works for Section Completion																									
Construction																									
Section III A - Road A2, A4 & A5																									
Roadwork & Utilities - Section 1 (L1806 - L1801)																									

Data Date:
20-Feb-18

- ◆ Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Remaining Level of Effort

**Updated Works Programme Rev.12
(Ref. to Rev.12 as of 20 February 2018)**


Date	Revision	Checked	Approved
20-Feb-18	12		

CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019					
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
Promenade Seawall Parapet Construction & EVA																							
SVII12000	Sec VII - Precast parapet	67	18-Nov-17 A	14-May-18	0%																		
SVII12010	Sec VII - Zone CRIII - seawall parapet: Backfilling	14	20-Feb-18	07-Mar-18	0%																		
SVII12120	Sec VII - Zone CRIII - seawall parapet: Construct mass concrete coping	30	08-Mar-18	16-Apr-18	0%																		
SVII12122	Sec VII - Zone CRIII - seawall parapet: reinforced concret coping	17	17-Apr-18	07-May-18	0%																		
SVII12140	Sec VII - Zone CRIII - seawall parapet: construct seawall parapet	30	08-May-18	12-Jun-18	0%																		
SVII12160	Sec VII - CRIII - EVA: watermain	14	13-Jun-18	29-Jun-18	0%																		
SVII12180	Sec VII - CRIII - EVA: U-channel	14	30-Jun-18	17-Jul-18	0%																		
SVII12200	Sec VII - CRIII - EVA: bituminous layer	5	18-Jul-18	23-Jul-18	0%																		
SVII12220	Sec VII - CRIII - EVA: paving block	30	24-Jul-18	27-Aug-18	0%																		
SVII13120	Sec VII - Zone A1, A2 & B - seawall parapet: Construct mass concrete coping	14	28-Dec-17 A	07-Mar-18	68.18%																		
SVII13122	Sec VII - Zone A1, A2 & B - seawall parapet: reinforced concrete coping	18	08-Mar-18	28-Mar-18	0%																		
SVII13140	Sec VII - Zone A1, A2 & B - seawall parapet: Construct seawall parapet	30	09-Apr-18	14-May-18	0%																		
SVII13160	Sec VII - Zone A1, A2 & B - EVA: watermain	14	15-May-18	31-May-18	0%																		
SVII13180	Sec VII - Zone A1, A2 & B - EVA: U-channel	14	01-Jun-18	16-Jun-18	0%																		
SVII13182	Sec VII - Zone A1, A2 & B - EVA: bituminous layer	5	19-Jun-18	23-Jun-18	0%																		
SVII13184	Sec VII - Zone A1, A2 & B - EVA: paving block	30	25-Jun-18	30-Jul-18	0%																		
SVII13200	Sec VII - Zone D - seawall parapet: Remove temporary seawall block	21	07-Mar-18	03-Apr-18	0%																		
SVII13220	Sec VII - Zone D - seawall parapet: Construct mass concrete	30	04-Apr-18	10-May-18	0%																		
SVII13222	Sec VII - Zone D - seawall parapet: reinforced concrete coping	18	11-May-18	01-Jun-18	0%																		
SVII13240	Sec VII - Zone D - seawall parapet: Construct seawall parapet	25	02-Jun-18	03-Jul-18	0%																		
SVII13260	Sec VII - Zone D - EVA : watermain	14	04-Jul-18	19-Jul-18	0%																		
SVII13280	Sec VII - Zone D - EVA : U-channel	14	20-Jul-18	04-Aug-18	0%																		
SVII13300	Sec VII - Zone D - EVA : bituminous layer	5	06-Aug-18	10-Aug-18	0%																		
SVII13320	Sec VII - Zone D - EVA : paving block	30	11-Aug-18	14-Sep-18	0%																		
Promenade Footpath																							
Section 1																							
SVII10440	Sec VII - section 1 footpath - drainage works : connection pipe & U -channel	10	24-May-18	04-Jun-18	0%																		
SVII10445	Sec VII - section 1 footpath - watermain	7	05-Jun-18	12-Jun-18	0%																		
SVII10460	Sec VII - section 1 footpath - lighting	7	13-Jun-18	21-Jun-18	0%																		
SVII10500	Sec VII - section 1 footpath - paving block	21	22-Jun-18	17-Jul-18	0%																		
Section 2																							
SVII12610	Sec VII - section 2 footpath - drainage works : L2202 - L2203A	20	20-Feb-18	14-Mar-18	0%																		
SVII12615	Sec VII - section 2 footpath - watermain	7	15-Mar-18	22-Mar-18	0%																		
SVII12630	Sec VII - section 2 footpath - utilities: TCSS	21	23-Mar-18	20-Apr-18	0%																		
SVII12670	Sec VII - section 2 footpath - paving block	30	21-Apr-18	28-May-18	0%																		
Section 3																							
SVII12850	Sec VII - section 3 footpath - watermain	17	20-Feb-18	10-Mar-18	0%																		
SVII12870	Sec VII - section 3 footpath - utilities (HEC, TCSS, HGC, PCCW)	40	12-Mar-18	02-May-18	0%																		
SVII12875	Sec VII - 3 footpath - drainage works :U chanel	14	03-May-18	18-May-18	0%																		

CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019												
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct			
SVII12890	Sec VII - section 3 footpath - paving block	30	19-May-18	25-Jun-18	0%																									
Section 4																														
SVII13049	Sec VII - section 4 footpath - watermain	1	14-Nov-17 A	20-Feb-18	95.24%																									
SVII13050	Sec VII - section 4 footpath - drainage works (L2203 -L2203A)	21	21-Feb-18	16-Mar-18	0%																									
SVII13055	Sec VII - section 4 footpath - utilities: HEC, TCSS, HEC & PCCW	49	17-Mar-18	18-May-18	0%																									
SVII13110	Sec VII - section 4 footpath - paving block	25	19-May-18	19-Jun-18	0%																									
Section 5																														
SVII13270	Sec VII - section 5 footpath - drainage works :L2203A -L2204	14	17-Mar-18	06-Apr-18	0%																									
SVII13275	Sec VII - section 5 footpath - watermain	14	07-Apr-18	23-Apr-18	0%																									
SVII13310	Sec VII - section 5 footpath - utilities: HEC, TCSS, HGC, PCCW	42	24-Apr-18	13-Jun-18	0%																									
SVII13330	Sec VII - section 5 footpath - paving block	22	14-Jun-18	11-Jul-18	0%																									
Section 6																														
SVII13490	Sec VII - section 6 footpath - drainage works(Culvert L - L2204)	14	20-Feb-18	07-Mar-18	0%																									
SVII13510	Sec VII - section 6 footpath - watermain	13	08-Mar-18	22-Mar-18	0%																									
SVII13514	Sec VII - section 6 footpath - U channel	20	23-Mar-18	19-Apr-18	0%																									
SVII13530	Sec VII - section 6 footpath - utilities: HEC, TCSS, HGC, PCCW	49	23-Mar-18	25-May-18	0%																									
SVII13550	Sec III A - section 6 footpath - paving block	25	26-May-18	25-Jun-18	0%																									
SVII19420	Achievement of Section VII of the Works	0		14-Sep-18	0%																									
Section VIII - Landscape Softworks																														
Soft Landscaping Works																														
SVIII10040	Sec VIII - Trees Planting	141	04-May-18	21-Sep-18	0%																									
SVIII10060	Sec VIII - Shrubs Planting	141	04-May-18	21-Sep-18	0%																									
SVIII10080	Achievement of Section VIII of the Works	0		21-Sep-18	0%																									
Section IX - Establishment Works																														
Soft Landscaping Works																														
SDX10020	Sec IX - Establishment Works	365	22-Sep-18	21-Sep-19	0%																									
SDX10040	Achievement of Section IX of the Works	0		21-Sep-19	0%																									
Section X - Protection & Preservation of Trees																														
Summary of Section X - Protection & Preservation of Trees																														
SX10000	Achievement of Section X of the Works	0		21-Sep-18	0%																									
Soft Landscaping Works																														
SX10020	Sec X - Protection & Preservation of Trees	214	31-Jan-13 A	21-Sep-18	86.89%																									

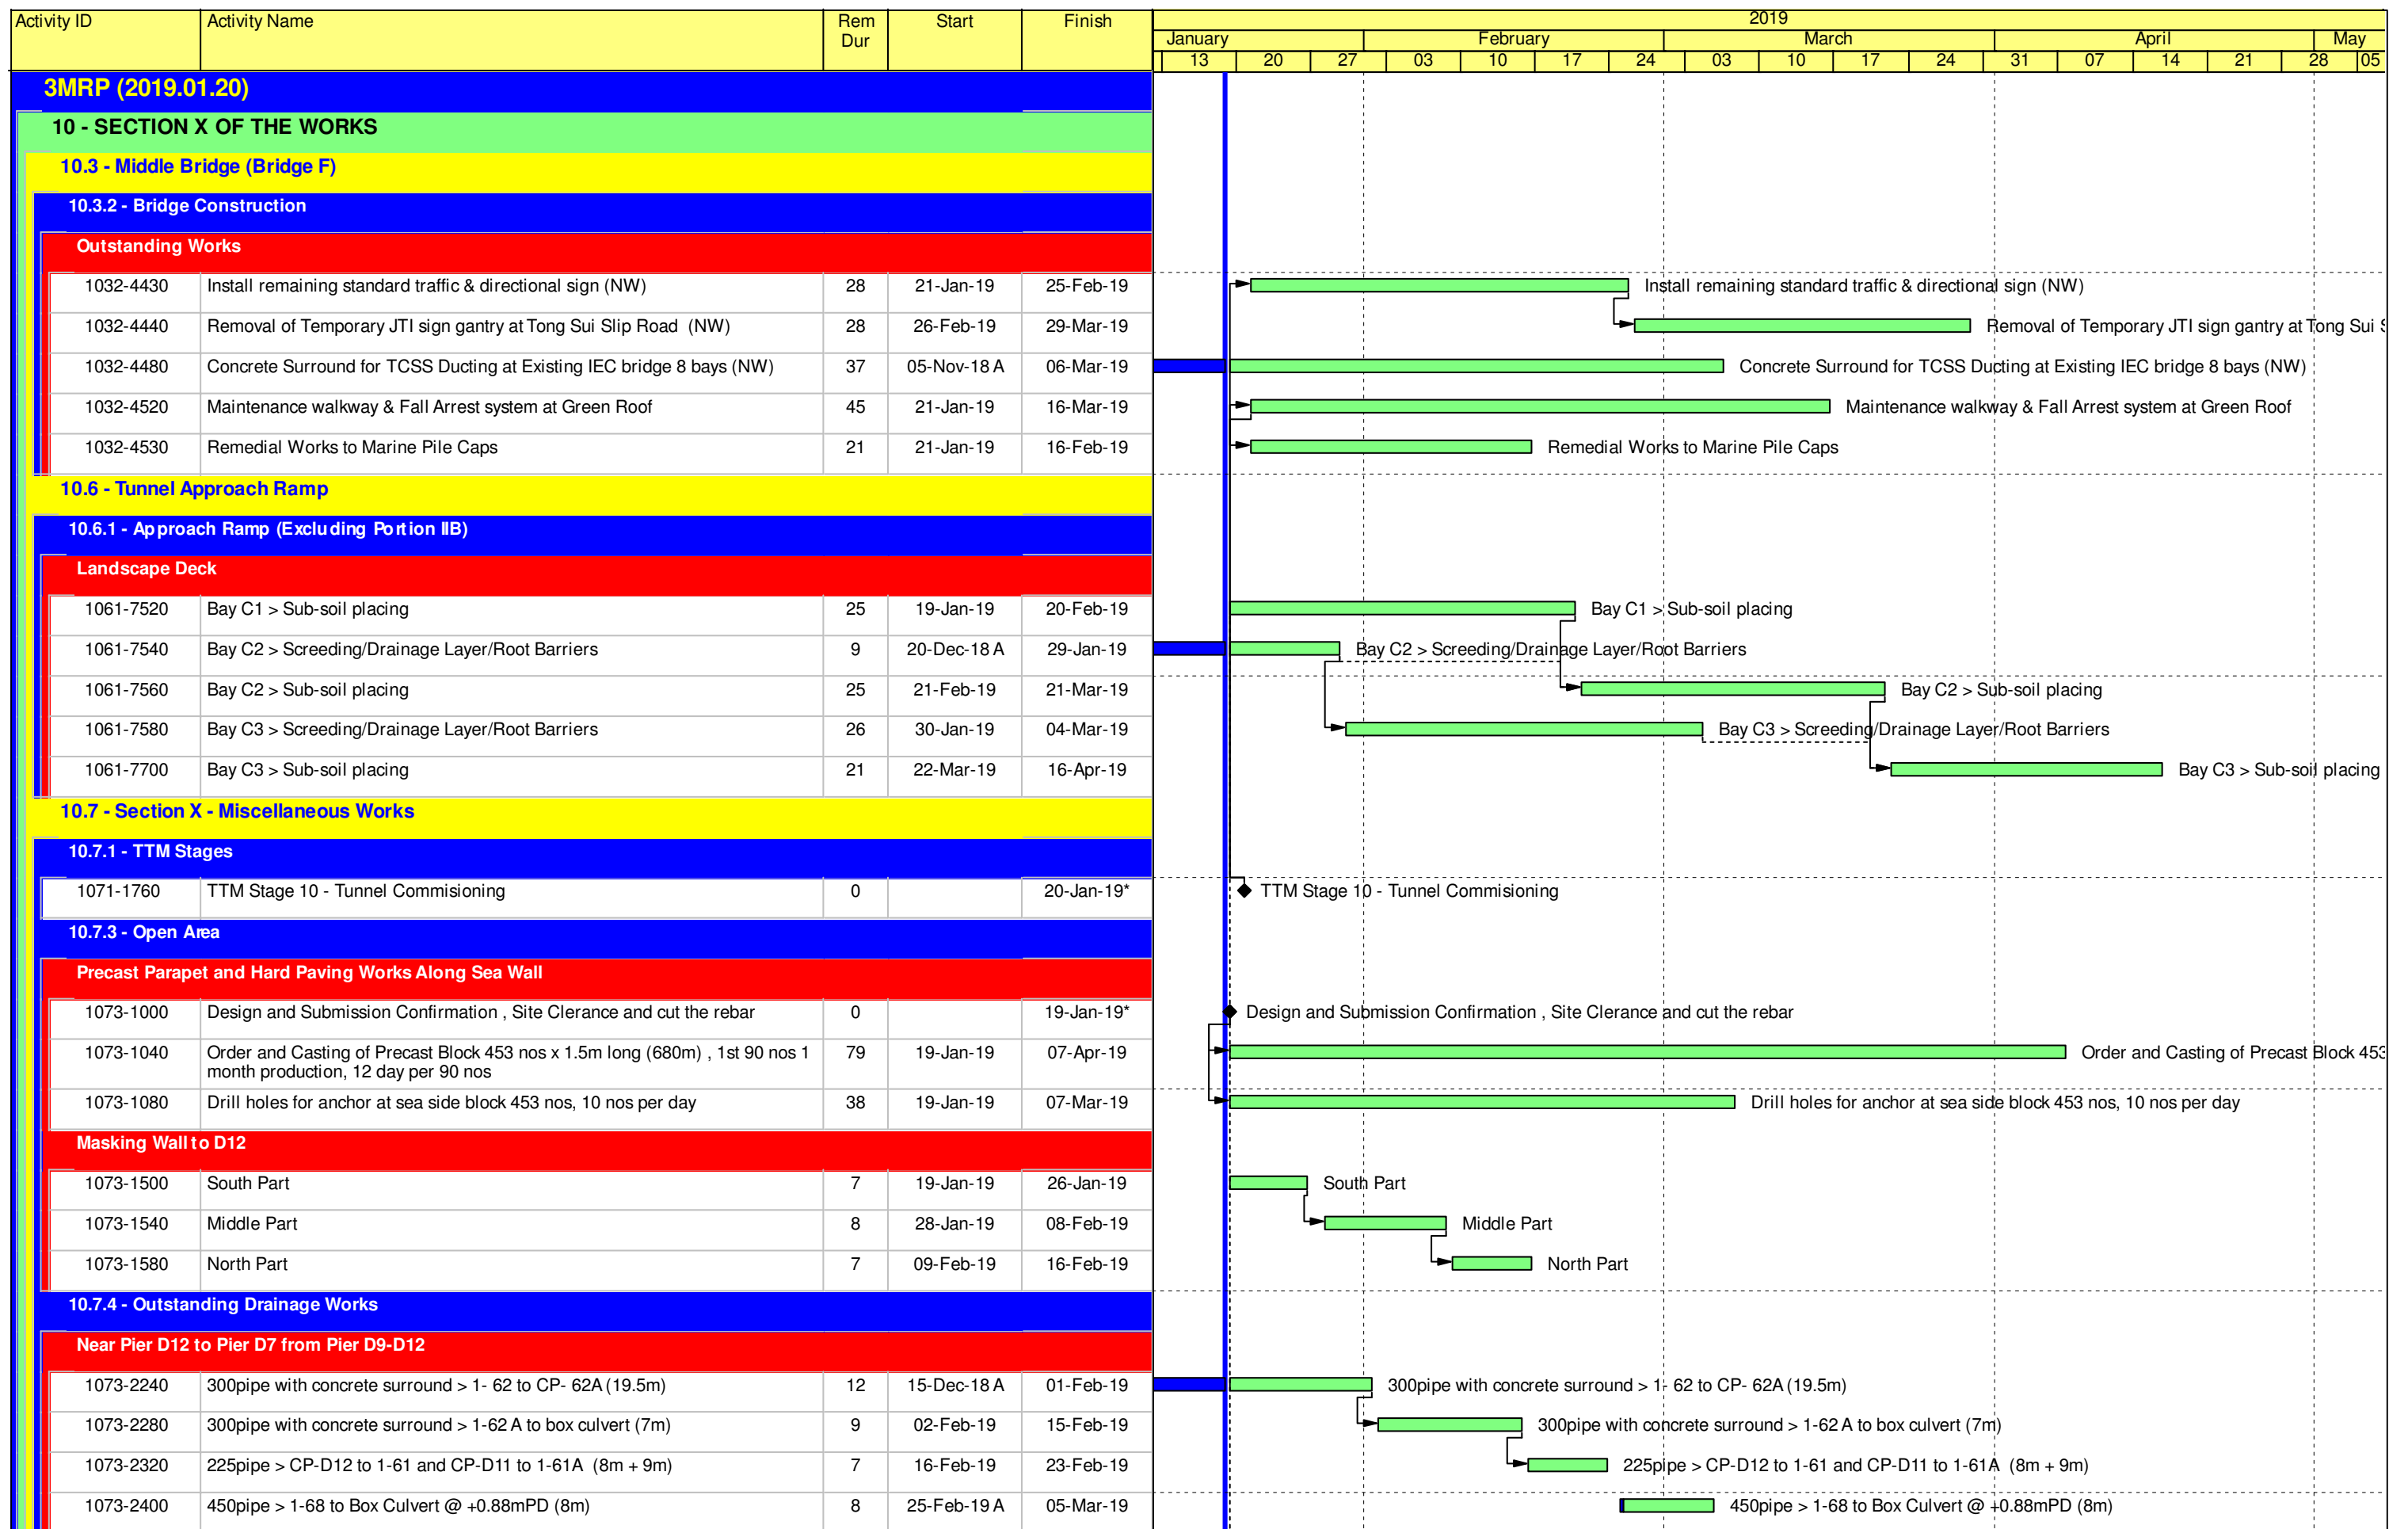


█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Jan.2019 to 20.Apr.2019)



Contract HY/2009/19
Three Months Rolling Programme (20.Jan.2019 to 20.Apr.2019)

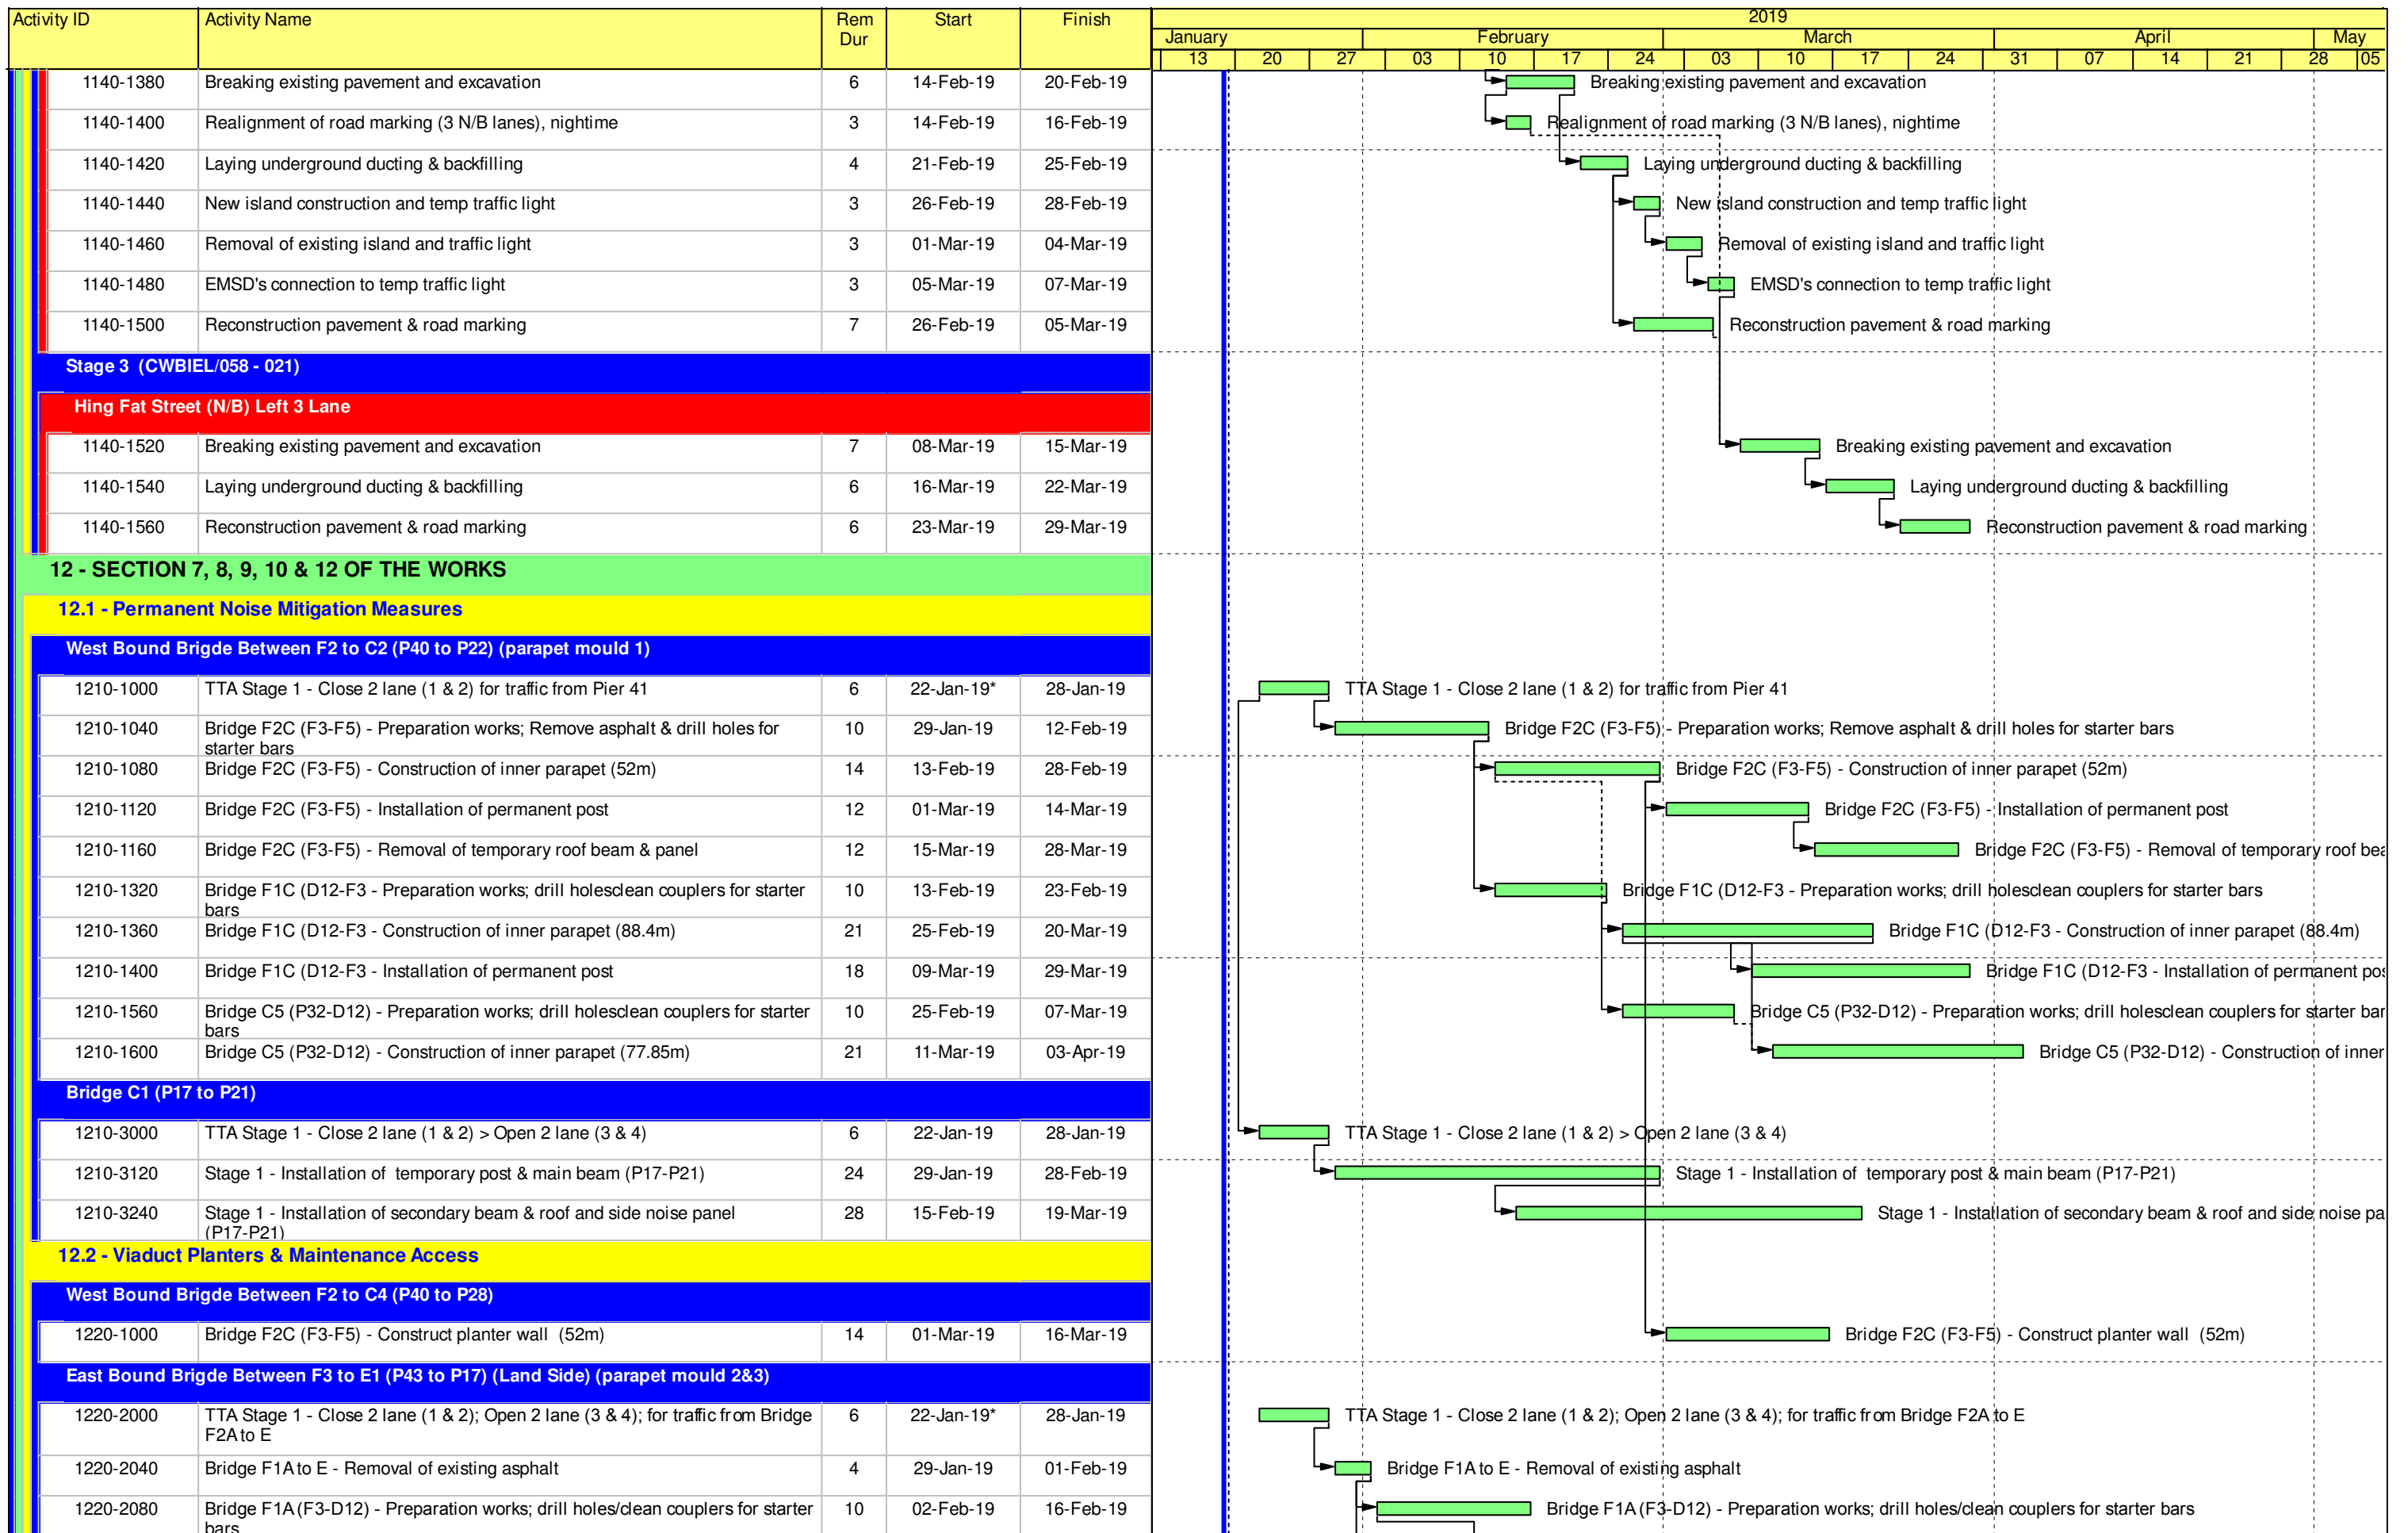

■ Remaining Level of Effort ■ Remaining Work
■ Actual Level of Effort ■ Critical Remaining Work
■ Actual Work ◆ ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Jan.2019 to 20.Apr.2019)

Activity ID	Activity Name	Rem Dur	Start	Finish	2019																
					January			February				March				April				May	
					13	20	27	03	10	17	24	03	10	17	24	31	07	14	21	28	05
1220-2120	Bridge F1A (F3-D12) - Construction of inner parapet (88.4m)	21	13-Feb-19	08-Mar-19	Bridge F1A (F3-D12) - Construction of inner parapet (88.4m)																
1220-2160	Bridge F1A (F3-D12) - Construct planter wall (88.4m)	21	25-Feb-19	20-Mar-19	Bridge F1A (F3-D12) - Construct planter wall (88.4m)																
1220-2680	Bridge D2 (D6-D4) - Preparation works; drill holes/clean couplers for starter bars	10	02-Feb-19	16-Feb-19	Bridge D2 (D6-D4) - Preparation works; drill holes/clean couplers for starter bars																
1220-2720	Bridge D2 (D6-D4) - Construction of inner parapet (120m)	21	13-Feb-19	08-Mar-19	Bridge D2 (D6-D4) - Construction of inner parapet (120m)																
1220-2760	Bridge D2 (D6-D4) - Construct planter wall (120m)	21	25-Feb-19	20-Mar-19	Bridge D2 (D6-D4) - Construct planter wall (120m)																
1220-2840	Bridge D1 (D4-D1) - Preparation works; drill holes/clean couplers for starter bars	10	18-Feb-19	28-Feb-19	Bridge D1 (D4-D1) - Preparation works; drill holes/clean couplers for starter bars																
1220-2880	Bridge D1 (D4-D1) - Construction of inner parapet (119m)	21	09-Mar-19	02-Apr-19	Bridge D1 (D4-D1) - Construction of inner parapet (119m)																
12.3 - Waterworks																					
1230-1000	Irrigation System - Landscape Deck	121	21-Jan-19	19-Jun-19	Irrigation System - Landscape Deck																
12.4 - Soft Landscape																					
1240-1000	Top soil & Foothpath at Landscape Deck & green roof	97	23-Mar-19	20-Jul-19	Top soil & Foothpath at Landscape Deck & green roof																
15 - SECTION 13A OF THE WORKS																					
15.1 - Soft Landscape																					
1510-1000	Establishment Works at Portion XIII	365	14-May-19	12-May-20	Establishment Works at Portion XIII																

- █ Remaining Level of Effort
- █ Actual Level of Effort
- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work
- ◆ Milestone

Activity ID	Activity Name	Original Duration	Start	Finish	2019																		
					Feb	Mar	Apr	May															
Total		2566d	21-Mar-13 A	29-Mar-20																			
DWP-08 - (2) - Update Progress As of 20 Feb 19		2566d	21-Mar-13 A	29-Mar-20																			
Works in KD9 (Include Re-provisioning Works of KD4,KD5)		227d	03-May-18 A	30-Mar-19																			
External Works Under KD9		30d	16-Nov-18 A	22-Feb-19																			
Zone 4 up to Elderly Facilities		30d	16-Nov-18 A	22-Feb-19																			
Elderly Facilities V039 Received on 22 Jun 2017		30d	16-Nov-18 A	22-Feb-19																			
EXW_2280	Ground levelling, drainage works and safety met installation	30d	16-Nov-18 A	22-Feb-19																			
Reverting Traffic for IEC,VP Rd & TF St & Seawall Reinstatement (KD9)		227d	03-May-18 A	30-Mar-19																			
TTA Revert Traffic Back to Original Alignment		19d	01-Dec-18 A	31-Dec-18 A																			
East Bound TTA - IEC East Bound, Victoria Park Road & footpath along Sea Side		10d	01-Dec-18 A	07-Dec-18 A																			
TTM Stage 1 - IEC (East Bound)		6d	01-Dec-18 A	07-Dec-18 A																			
Reinstatement Existing Structure		6d	01-Dec-18 A	07-Dec-18 A																			
EB_1020	Install metal parapet on parapet wall (30m)	6d	01-Dec-18 A	07-Dec-18 A																			
TTM Stage 2 - Revert Traffic back to Original Victoria Road		4d	01-Dec-18 A	07-Dec-18 A																			
Existing Bridge Parapet Reinstatement		4d	01-Dec-18 A	07-Dec-18 A																			
EB_1180	Install metal parapet on parapet wall (40m)	4d	01-Dec-18 A	07-Dec-18 A																			
West Bound - IEC West Bound & Tsing fung Street		5d	29-Dec-18 A	31-Dec-18 A																			
TTM Stage 2 - Revert Traffic back to Original Tsing Fung Street		5d	29-Dec-18 A	31-Dec-18 A																			
Existing Bridge Parapet Reinstatement		5d	29-Dec-18 A	31-Dec-18 A																			
IECW_1140	Install metal parapet on parapet wall (60m)	5d	29-Dec-18 A	31-Dec-18 A																			
Completion of Minor Outstanding / Remaining Works for KD9		227d	03-May-18 A	30-Mar-19																			
East Bound - Minor Outstanding Works in Footpath after Substantial Completion of KD9		131d	23-Aug-18 A	20-Dec-18 A																			
Minor Reinstatement Works for Existing Sign Gantry		3d	14-Sep-18 A	19-Sep-18 A																			
EB_1760	Connection of Public Lighting by HyD (Lighting)	2d	14-Sep-18 A	18-Sep-18 A																			
EB_1790	Installation of E & M at Sign Gantry (night work)	1d	19-Sep-18 A	19-Sep-18 A																			
Minor Reinstatement Works for Central Median of IEC & Footbridge		6d	05-Dec-18 A	20-Dec-18 A																			
EB_1810	Dismantlement of temp directional sign mounted on extg footbridge	1d	05-Dec-18 A	05-Dec-18 A																			
EB_1800	Reconstruction of central divider (6m long, night work)	6d	17-Dec-18 A	20-Dec-18 A																			
Minor Reinstatement Works for Footpath		9d	27-Sep-18 A	15-Nov-18 A																			
EB_1840	Re-provision of Tree	8d	27-Sep-18 A	15-Nov-18 A																			
EB_1830	Reinstatement of District Council Welcome Sign and opening plaque at Planter area	1d	03-Oct-18 A	03-Oct-18 A																			
Minor Reinstatement Works for Loop Detector		1d	23-Aug-18 A	24-Aug-18 A																			
EB_1890	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)	1d	23-Aug-18 A	24-Aug-18 A																			
West Bound - Completion of Minor Outstanding / Remaining Works for KD9		227d	03-May-18 A	30-Mar-19																			
Minor Reinstatement Works for Victoria Park		126d	03-May-18 A	30-Mar-19																			
IECW_1500	Re-provision of Tree	32d	03-May-18 A	30-Mar-19																			
IECW_1510	Laying Irrigation Main	10d	27-Sep-18 A	12-Jan-19 A																			
IECW_1520	Construct Landscape Footpath and Lightings	7d	05-Nov-18 A	16-Jan-19 A																			
Minor Reinstatement Works in IEC West Bound		119d	15-Oct-18 A	31-Dec-18 A																			
IECW_1620	Repairing of concrete defects on extg concrete deck and abutment M	30d	15-Oct-18 A	24-Nov-18 A																			
IECW_1610	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)	57d	24-Nov-18 A	24-Dec-18 A																			
IECW_1660	Replacement of new rubber seal on extg MJ at IEC W/B and E/B (night work)	4d	26-Nov-18 A	31-Dec-18 A																			
IECW_1600	Replacement of new movement joint at IEC W/B (Sun midnight only)	8d	27-Dec-18 A	30-Dec-18 A																			



- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Page 1 of 2
Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel (Slip Road 8 Section) - 3 Months Rolling Programme

Date	Revision	Checked	Approved
20-Feb-19	DWP-08 (2) - 3 Months Rolling	TL	TL

Activity ID	Activity Name	Original Duration	Start	Finish	2019																			
					Feb			Mar			Apr			May										
Works in Victoria Park (KD4, KD5, KD9)																								
Re-Provisioning Works																								
Nursery Compound																								
Nursery compound																								
Fire Sreivces																								
VP_NC_2030	FS inspection	14d	20-Aug-18 A	27-Sep-18 A																				
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks																								
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)																								
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365d	31-Mar-19	29-Mar-20																				
KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH>500mm)																								
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365d	31-Mar-19	29-Mar-20																				
KD18 - Section 11: Transplanted Trees DBH>500mm in Portion VA and XII																								
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365d	31-Mar-19	29-Mar-20																				
KD10 - Preservation and Protection of Trees																								
PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	02-Apr-19																				
KD15 & KD8 - Mooring Components Upkeep (CBTS and ATS)																								
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	21-Feb-19																				

■ Preservation and Protection of Existing Trees

■ Mooring Upkeep at Portion X(10) & XVI(16) - CBTS



- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Page 2 of 2
Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel (Slip Road 8 Section) - 3 Months Rolling Programme

Date	Revision	Checked	Approved
20-Feb-19	DWP-08 (2) - 3 Months Rolling	TL	TL

Data Date: 20-Mar-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2019											
						Mar			Apr			May			Jun		
Update 2019-03-20 CWB(CC) - Commissioning Contract (DWP 4b)																	
PRELIMINARIES AND GENERAL REQUIREMENTS																	
Salient Key Dates and Milestones																	
Anticipated Completion Dates																	
KD11	KD11 - Completion of Section 6 of the Works (1445 days) - include EOT No.12 (149 days)	0		31-Mar-19*	-413	◆											
KD07	KD07 - Completion of Section 2 of the Works (1771 days) - include EOT No.12 (414 days)	0		19-May-19*	-245	▲ ◆											
KD09	KD09 - Completion of Section 4 of the Works (1445 days) - include EOT No.12 (149 days)	0		19-Jun-19*	-641	▲ ◆											
Possession Dates and Vacation Dates																	
PO-IIa	Possession of Portion IIa (Day 1) - WVb below +6.5mPD	1329	28-Feb-14 A	17-Apr-19	-401	—											
PO-III	Possession of Portion III (Day 120) - CH1805-2600	1209	28-Jun-14 A	17-Apr-19	-401	—											
PO-Ib	Possession of Portion Ib (Day 242) - CH1580-1905	1087	28-Oct-14 A	17-Apr-19	-401	—											
PO-IXd	Possession of Portion IXd (Day 266) - CH4600-4860	1063	21-Nov-14 A	17-Apr-19	-401	—											
PO-XI	Possession of Portion XI (Day 296) - EVS	1033	21-Dec-14 A	17-Apr-19	-213	—											
PO-IIc	Possession of Portion IIc (Day 336) - CH1360-1580	993	30-Jan-15 A	17-Apr-19	-401	—											
PO-IIb	Possession of Portion IIb (Day 336) - WVb above +6.5mPD	669	30-Jan-15 A	17-Apr-19	-401	—											
PO-IXa	Possession of Portion IXa (Day 392) - CH4860-5150	937	27-Mar-15 A	17-Apr-19	-401	—											
PO-Va	Possession of Portion V (Day 607) - CH2950-3210	722	28-Oct-15 A	17-Apr-19	-401	—											
PO-VII_a1	Possession of Portion VII (Day 762) - CH3911-4250 (below -6.0mPD)	659	30-Dec-15 A	17-Apr-19	-401	—											
PO-Vc	Possession of Portion V (Day 607) - CH3210-3250	658	15-Jan-16 A	17-Apr-19	-401	—											
PO-VIb_b1	Possession of Portion VIb (Day 761) - CH3428-3625 (E/B)	619	18-Feb-16 A	17-Apr-19	-401	—											
PO-VIb_b2	Possession of Portion VIb (Day 761) - CH3428-3625 (W/B)	568	29-Feb-16 A	17-Apr-19	-401	—											
PO-Xa_1	Possession of Portion Xa (Day 650) - ADB Southern Portion (AECOM letter ref: 2015007890T)	589	07-Mar-16 A	17-Apr-19	-597	—											
PO-Xb_1	Possession of Portion Xb (Day 804) - ADB Northern Portion	589	07-Mar-16 A	17-Apr-19	-597	—											
PO-Vb1	Possession of Portion V (Day 607) - SR3	587	11-Mar-16 A	17-Apr-19	-213	—											

- ◆ Current Milestone
- Level of Effort
- ▲ Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 61 (March 2019)

THREE MONTH ROLLING

Project ID: H2613-U061
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U060
 Page 1 of 4

Date	Revision	Checked	Approv...
20-Feb-19	U060	AT	CW
20-Mar-19	U061	AT	CW

Data Date: 20-Mar-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2019			
						Mar	Apr	May	Jun
PO-Ia	Possession of Portion Ia (Day 789) - SCB / SCP1 / SCP2 / Rumsey Street Flyover	600	28-Mar-16 A	17-Apr-19	-585				
PO-VII_a2	Possession of Portion VII (Day 762) - CH3800-3911 (below -6.0mPD)	567	31-Mar-16 A	17-Apr-19	-401				
PO-IXc_1	Possession of Portion IXc (Day 712) - EVB above 3.6mPD - Relinquished on 12 Apr 2016	445	29-Jul-16 A	17-Apr-19	-549				
PO-IXb_1	Possession of Portion IXb (Day 712) - EVB (below +3.6mPD to tunnel top slab) - Relinquished on 12 Apr 2016	445	05-Aug-16 A	17-Apr-19	-549				
PO-VIa_a	Possession of Portion VIa (Day 823) - CH3250-3283	425	15-Aug-16 A	17-Apr-19	-401				
PO-Vb2_a	Possession of Portion V (Day 607) - SR2	456	15-Aug-16 A	17-Apr-19	-401				
PO-VIc_a	Possession of Portion VIc (Day 761) - CH3770-3800 (Access Shaft Opening)	391	23-Sep-16 A	17-Apr-19	-401				
PO-VIb_c	Possession of Portion VIb (Day 761) - CH3625-3770	391	23-Sep-16 A	17-Apr-19	-401				
PO-IVa1	Possession of Portion IVa (Day 930) - CH2600-2720	323	30-Nov-16 A	17-Apr-19	-401				
PO-IVb2	Possession of Portion IVb (Day 930) - MVB (GLD-H)	233	28-Feb-17 A	17-Apr-19	-549				
PO-VIIIa_a	Possession of Portion VIIIa (Day 929) - CH4530-4591 W/B	233	28-Feb-17 A	17-Apr-19	-401				
PO-VIIIa	Possession of Portion VIIIa (Day 929) - CH4250-4600 (Remaining)	241	12-Mar-17 A	17-Apr-19	-401				
PO-VIIIb	Possession of Portion VIIIb (Day 929) - SR8 (CH700-350)	233	12-Mar-17 A	17-Apr-19	-401				
PO-VIIIc	Possession of Portion VIIIc (Day 1039) - SR8 (CH350-310) / SCP4	233	12-Mar-17 A	17-Apr-19	-401				
PO-IVa2_a	Possession of Portion IVa (Day 930) - CH2720-2950	241	12-Mar-17 A	17-Apr-19	-401				
PO-IVb1	Possession of Portion IVb (Day 930) - MVB (GLA-C)	239	14-Mar-17 A	17-Apr-19	-549				
PO-IVa2_b	Possession of Portion IVa (Day 930) - SR1	203	30-Mar-17 A	17-Apr-19	-401				
PO-Vb2_b	Possession of Portion V (Day 607) - SCP3	182	03-Jul-17 A	17-Apr-19	-401				
PO-VIb_a	Possession of Portion VIb (Day 761) - CH3400-3428	80	31-Jul-17 A	17-Apr-19	-401				
PO-VIa_b	Possession of Portion VIa (Day 823) - CH3283-3400	80	31-Jul-17 A	17-Apr-19	-401				
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-Mar-19	08-Jul-19	-401				
Submissions and Approvals									
Initial General Submission									
10168	Submission of CMC 3DVR	30	20-Mar-19	18-Apr-19	-214				

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 61 (March 2019) THREE MONTH ROLLING



Project ID: H2613-U061
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U060
 Page 2 of 4

Date	Revision	Checked	Approv...
20-Feb-19	U060	AT	CW
20-Mar-19	U061	AT	CW

Data Date: 20-Mar-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

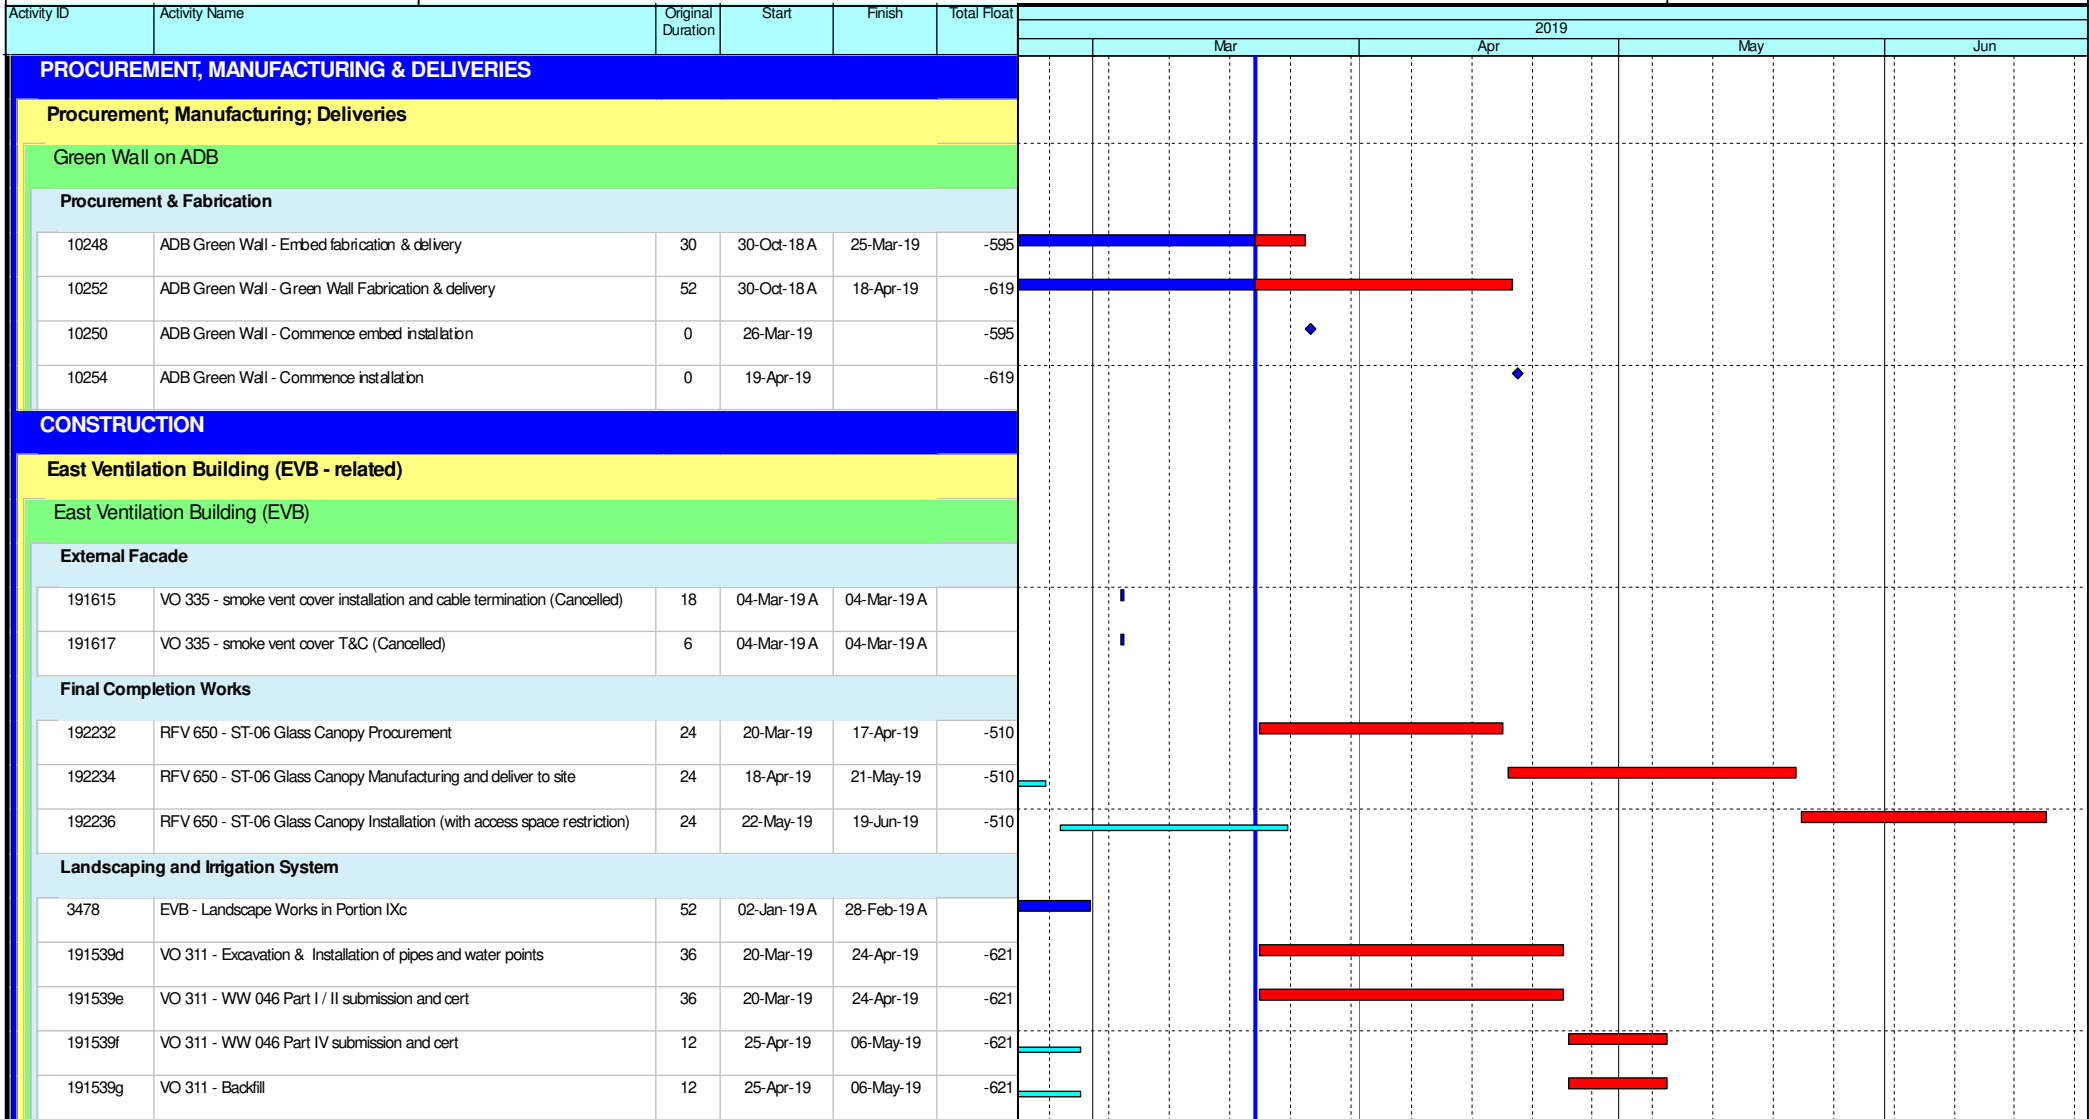

Leighton Contractors (Asia) Limited Programme Update 61 (March 2019) THREE MONTH ROLLING



Project ID: H2613-U061
 Baseline: DWP4a
 Layout: Update Three Month Rolling
 U060
 Page 3 of 4

Date	Revision	Checked	Approv...
20-Feb-19	U060	AT	CW
20-Mar-19	U061	AT	CW

Data Date: 20-Mar-19

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

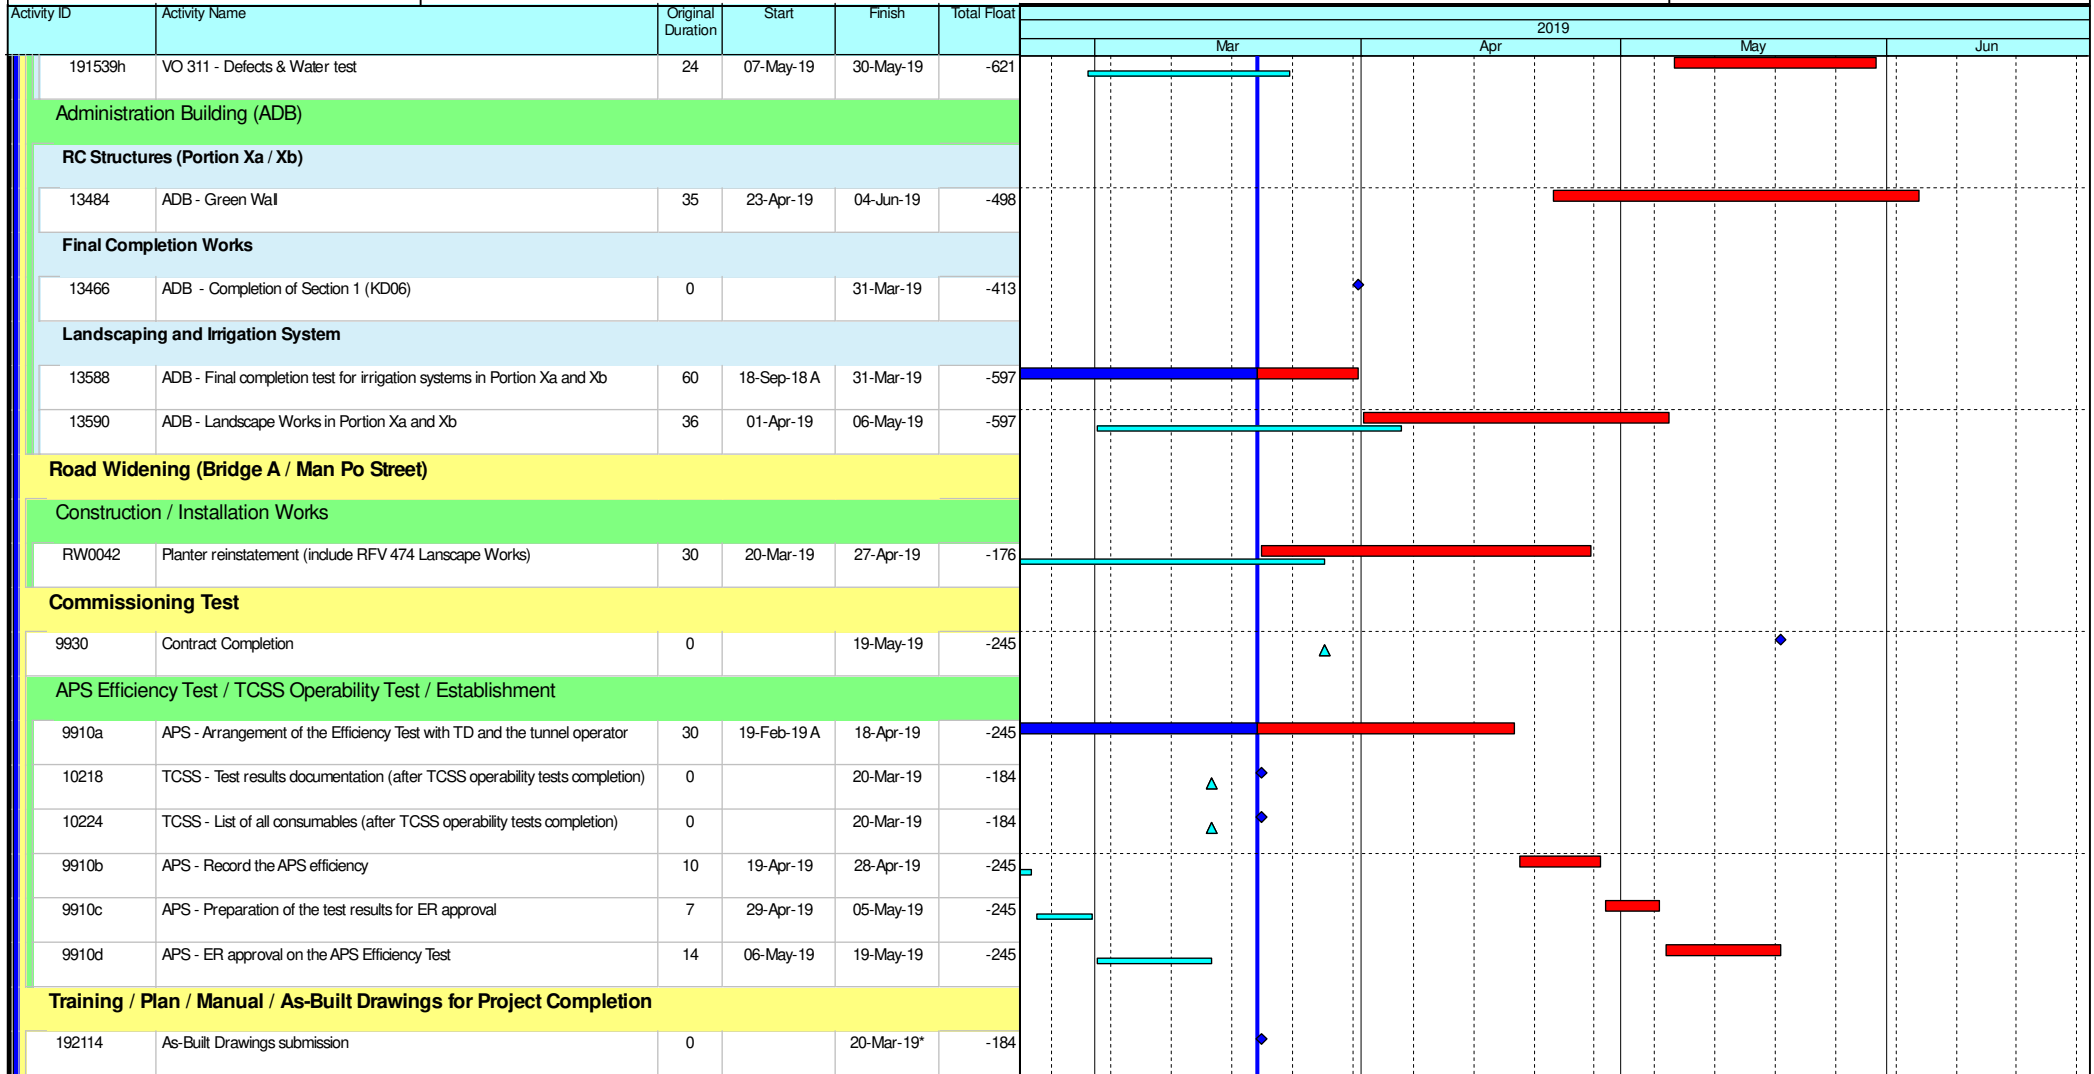

Leighton Contractors (Asia) Limited Programme Update 61 (March 2019) THREE MONTH ROLLING

Project ID: H2613-U061
Baseline: DWP4a
Layout: Update Three Month Rolling
U060
Page 4 of 4

Date	Revision	Checked	Approv...
20-Feb-19	U060	AT	CW
20-Mar-19	U061	AT	CW
