


# Programme for Outstanding and Defective Works

ID	Task Name	Duration	Start	Finish	2019																															
					July 2019							August 2019							September 2019							October 2019										
					14	17	20	23	26	29	1	4	7	10	13	16	19	22	25	28	31	3	6	9	12	15	18	21	24	27	30	3	6	9	12	15
1	<b>15. Reinstatement of Hung Hing Road and Wan Shing Street in Accordance to Hung Hing Road Traffic Diversion Reinstatement Stage 0.5 Scheme Under VO No. 257 on Hung Hing Road</b>	248 days	Fri 1/3/19	Sun 3/11/19																																
2	Phase 1 (Completed)	41 days	Fri 1/3/19	Wed 10/4/19																																
55	Phase 2 (Completed)	41 days	Tue 2/4/19	Sun 12/5/19																																
169	Yacht Club (40m Long)	43 days	Fri 15/3/19	Fri 26/4/19																																
182	Triangle Island (40m Long)	28 days	Fri 31/5/19	Thu 27/6/19																																
194	Phase 3	144 days	Thu 13/6/19	Sun 3/11/19																																
195	Advacne Work	35 days	Thu 13/6/19	Wed 17/7/19																																
200	Construction of Road Kerb and Pavement (Portion 5)	23 days	Thu 18/7/19	Fri 9/8/19																																
201	TTA Implementation	1 day	Thu 18/7/19	Thu 18/7/19																																
202	Demolition of Concrete and Asphalt Pavement	4 days	Fri 19/7/19	Mon 22/7/19																																
203	Removal of Steel Plate	4 days	Tue 23/7/19	Fri 26/7/19																																
204	Installation of Kerb	2 days	Sat 27/7/19	Sun 28/7/19																																
205	Subbase Levelling	1 day	Mon 29/7/19	Mon 29/7/19																																
206	SRT for Sub-base	5 days	Tue 30/7/19	Sat 3/8/19																																
207	Concrete Laying	1 day	Sun 4/8/19	Sun 4/8/19																																
208	Concrete Curing	3 days	Mon 5/8/19	Wed 7/8/19																																
209	Existing Asphalt Patch Up Work at Water Ponding Area (Photo 3, 4 & 5, Figure 211) (Concurrent with ID 669)	2 days	Thu 8/8/19	Fri 9/8/19																																
210	Demolition of water ponding area	1 day	Thu 8/8/19	Thu 8/8/19																																
211	Patching Up with Asphalt layer	1 day	Fri 9/8/19	Fri 9/8/19																																
212	Construction of Road Kerb and Pavement (Portion 4)	30 days	Fri 2/8/19	Sat 31/8/19																																
213	TTA Implementation	1 day	Sat 10/8/19	Sat 10/8/19																																
214	Demolition of Concrete and Asphalt Pavement	4 days	Sun 11/8/19	Wed 14/8/19																																
215	Removal of Steel Plate	4 days	Thu 15/8/19	Sun 18/8/19																																
216	Installation of Kerb	1 day	Mon 19/8/19	Mon 19/8/19																																
217	Subbase Levelling	1 day	Tue 20/8/19	Tue 20/8/19																																
218	SRT for Sub-base	5 days	Wed 21/8/19	Sun 25/8/19																																
219	Concrete Laying	1 day	Mon 26/8/19	Mon 26/8/19																																
220	Concrete Curing	3 days	Tue 27/8/19	Thu 29/8/19																																
221	Existing Asphalt Patch Up Work at Water Ponding Area (Photo 1, Figure 212)	2 days	Fri 30/8/19	Sat 31/8/19																																
224	Repaving Works at Yacht Club (Photo 2, Figure 216-1), Same as	30 days	Fri 2/8/19	Sat 31/8/19																																
231	Construction of Trial Pit and Installation of decking (Portion 3)	21 days	Mon 2/9/19	Sun 22/9/19																																
232	TTA Implementation	1 day	Mon 2/9/19	Mon 2/9/19																																
233	Demolition of Concrete and Asphalt Pavement	4 days	Tue 3/9/19	Fri 6/9/19																																
234	Removal of Steel Plate and installation of ELS for waterpipe	4 days	Sat 7/9/19	Tue 10/9/19																																
235	Kerb Installation and installation of decking	2 days	Wed 11/9/19	Thu 12/9/19																																
236	Subbase Levelling	1 day	Fri 13/9/19	Fri 13/9/19																																
237	SRT for Sub-base	5 days	Sat 14/9/19	Wed 18/9/19																																
238	Concrete Laying	1 day	Thu 19/9/19	Thu 19/9/19																																
239	Concrete Curing	3 days	Fri 20/9/19	Sun 22/9/19																																
240	Construction of Road Kerb and Pavement (Portion 2)	21 days	Mon 23/9/19	Sun 13/10/19																																
249	Construction of Road Kerb and Pavement (Portion 1)	21 days	Mon 14/10/19	Sun 3/11/19																																
258	Phase 3.5 (Remaining Works for HHR0.5 Scheme & Cable Duct Laying)	69 days	Tue 14/5/19	Sun 21/7/19																																
259	Construction of Footpath at HHR (Up Birdge)	11 days	Fri 31/5/19	Mon 10/6/19																																



Task Milestone Rolled Up Task Rolled Up Progress External Tasks Group By Summary  
Progress Summary Rolled Up Milestone Split Project Summary Deadline

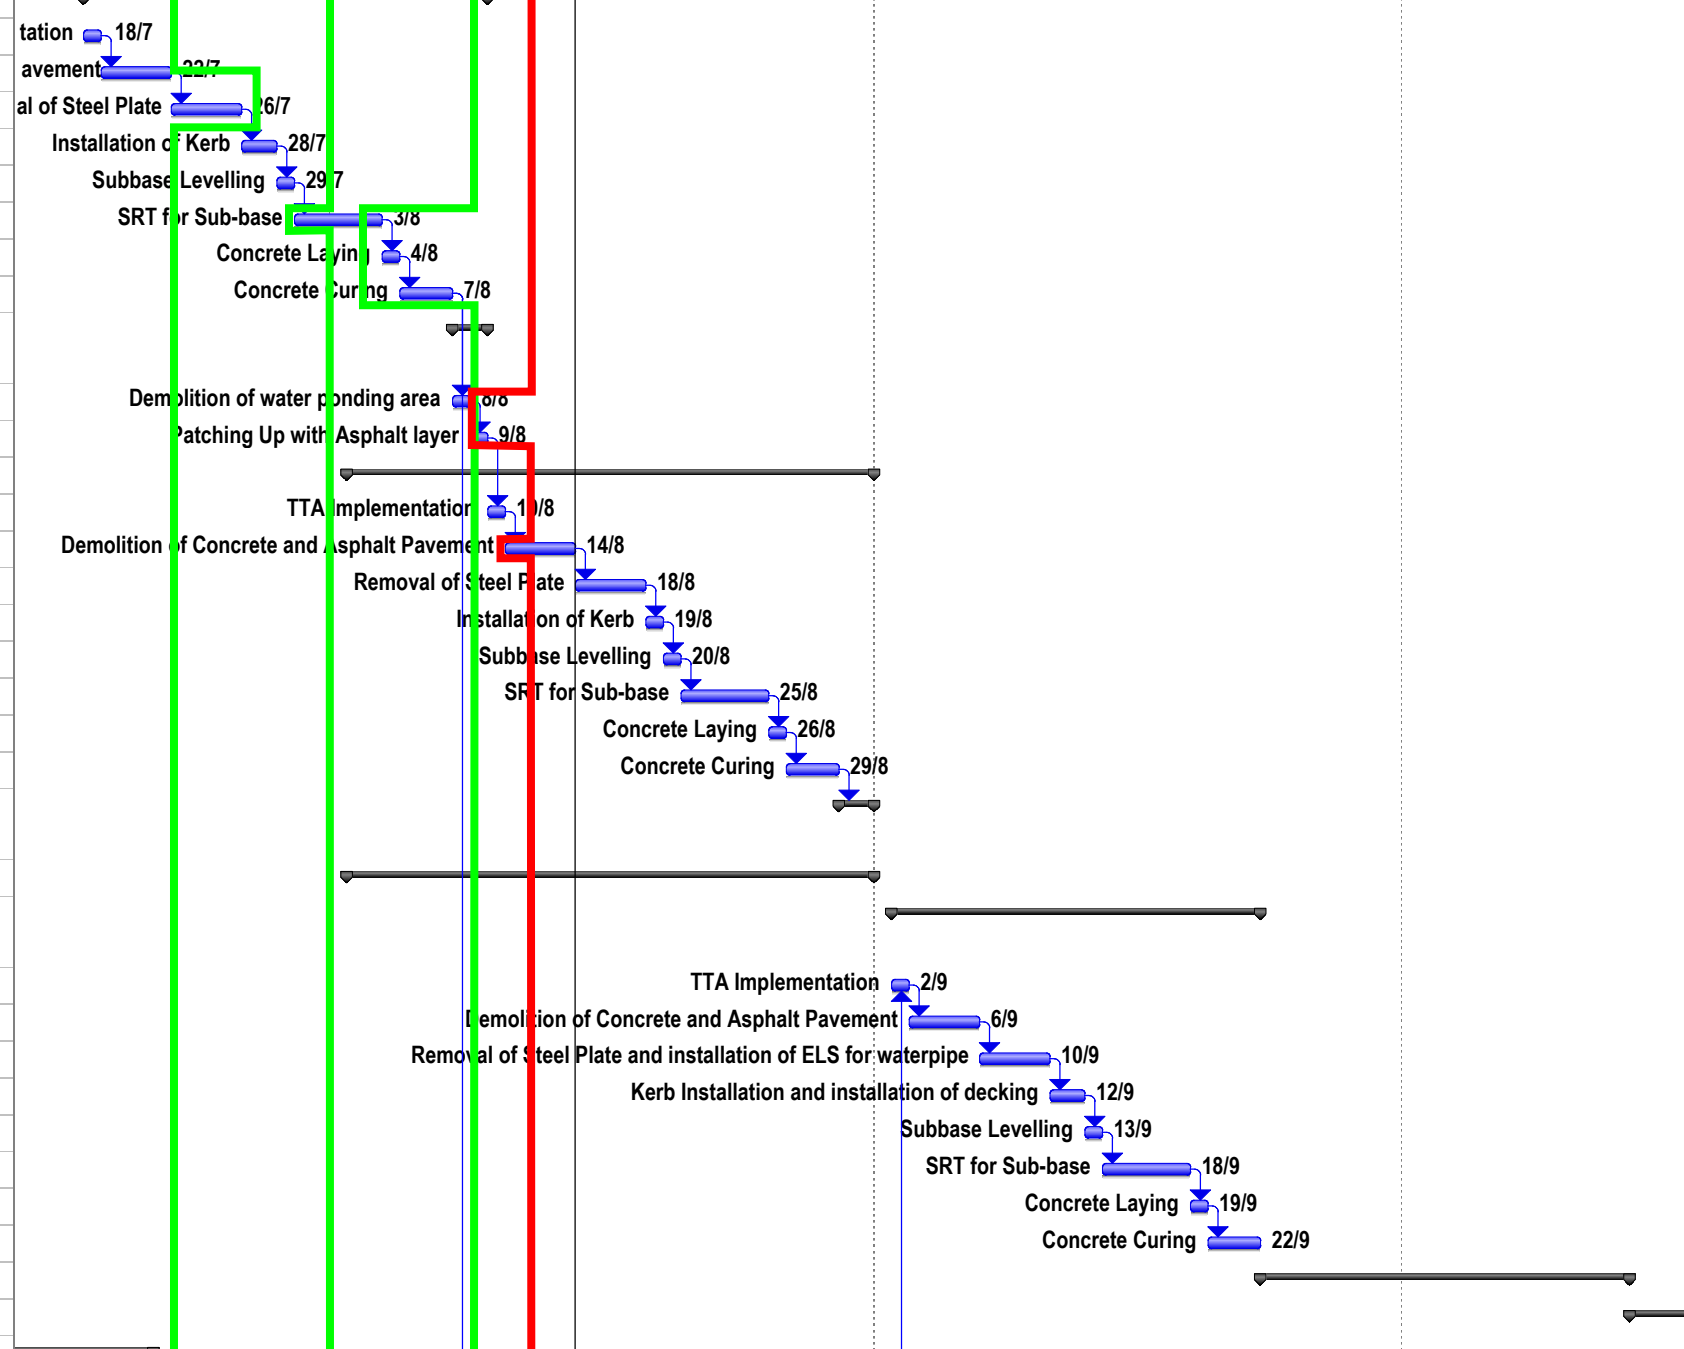

# Programme for Outstanding and Defective Works

ID	Task Name	Duration	Start	Finish	Qtr 3, 2019																														
					July 2019							August 2019							September 2019							October 2019									
387	Backfilling of Subbase Level and SRT	8 days	Tue 30/7/19	Tue 6/8/19	g of Subbase Level and SRT																														
388	RB Laying	1 day	Wed 7/8/19	Wed 7/8/19	RB Laying																														
389	BC Laying	1 day	Thu 8/8/19	Thu 8/8/19	BC Laying																														
390	WC Laying	1 day	Fri 9/8/19	Fri 9/8/19	WC Laying																														
391	<b>Construction of Cross road duct (Opposite to SPCA)</b>	<b>85 days</b>	<b>Fri 17/5/19</b>	<b>Fri 9/8/19</b>																															
392	Endorsement of TTA Drawing (Notional)	57 days	Fri 17/5/19	Fri 12/7/19	2/7																														
393	Application Road Work Advise	7 days	Sat 13/7/19	Fri 19/7/19	19/7																														
394	TTA Implementation	1 day	Sat 20/7/19	Sat 20/7/19	20/7																														
395	Demolition and Removal of Asphalt and Concrete Surface	5 days	Sun 21/7/19	Thu 25/7/19	25/7																														
396	Excavation for PVC duct laying	3 days	Fri 26/7/19	Sun 28/7/19	28/7																														
397	Duct Laying	2 days	Mon 29/7/19	Tue 30/7/19	30/7																														
398	Backfilling to Formaiton Level	1 day	Wed 31/7/19	Wed 31/7/19	31/7																														
399	Backfilling of Subbase Level and SRT	7 days	Thu 1/8/19	Wed 7/8/19	7/8																														
400	RB Laying	1 day	Thu 8/8/19	Thu 8/8/19	8/8																														
401	BC Laying	1 day	Fri 9/8/19	Fri 9/8/19	9/8																														
402	<b>Construction of cross road duct (Bus Lane)</b>	<b>73 days</b>	<b>Fri 31/5/19</b>	<b>Sun 11/8/19</b>																															
403	Endorsement of TTA Drawing	22 days	Fri 31/5/19	Fri 21/6/19																															
404	Application Road Work Advise	7 days	Sat 22/6/19	Fri 28/6/19																															
405	<b>Cross road duct at Bus Lane (Northern Portion)</b>	<b>19 days</b>	<b>Fri 5/7/19</b>	<b>Tue 23/7/19</b>																															
406	TTA Implementation	1 day	Fri 5/7/19	Fri 5/7/19																															
407	Demolition and Removal of Asphalt Surface	2 days	Sat 6/7/19	Sun 7/7/19																															
408	Excavation for PVC duct laying	3 days	Mon 8/7/19	Wed 10/7/19																															
409	Duct Laying	1 day	Thu 11/7/19	Thu 11/7/19																															
410	Backfilling to Formaiton Level	1 day	Fri 12/7/19	Fri 12/7/19																															
411	Backfilling of Subbase Level and SRT	8 days	Sat 13/7/19	Sat 20/7/19	20/7																														
412	RB Laying	1 day	Sun 21/7/19	Sun 21/7/19	21/7																														
413	BC Laying	1 day	Mon 22/7/19	Mon 22/7/19	22/7																														
414	WC Laying	1 day	Tue 23/7/19	Tue 23/7/19	23/7																														
415	<b>Cross road duct at Bus Lane (Southern Portion)</b>	<b>19 days</b>	<b>Wed 24/7/19</b>	<b>Sun 11/8/19</b>																															
416	TTA Implementation	1 day	Wed 24/7/19	Wed 24/7/19	24/7																														
417	Demolition and Removal of Asphalt Surface	2 days	Thu 25/7/19	Fri 26/7/19	26/7																														
418	Excavation for PVC duct laying	3 days	Sat 27/7/19	Mon 29/7/19	29/7																														
419	Duct Laying	1 day	Tue 30/7/19	Tue 30/7/19	30/7																														
420	Backfilling to Formaiton Level	1 day	Wed 31/7/19	Wed 31/7/19	31/7																														
421	Backfilling of Subbase Level and SRT	8 days	Thu 1/8/19	Thu 8/8/19	8/8																														
422	Road Base Laying	1 day	Fri 9/8/19	Fri 9/8/19	9/8																														
423	BC Laying	1 day	Sat 10/8/19	Sat 10/8/19	10/8																														
424	WC Laying	1 day	Sun 11/8/19	Sun 11/8/19	11/8																														
425	<b>Construction of Cross road duct (EVA Access)</b>	<b>115 days</b>	<b>Fri 17/5/19</b>	<b>Sun 8/9/19</b>																															
426	Endorsement of TTA Drawing	22 days	Fri 17/5/19	Fri 7/6/19																															
427	Application Road Work Advise	7 days	Sat 8/6/19	Fri 14/6/19																															
428	Seeking Permission from FSD for Enclosure of EVA access	27 days	Sat 8/6/19	Thu 4/7/19																															
429	<b>Run-in at EVA (Eastern Portion)</b>	<b>16 days</b>	<b>Thu 8/8/19</b>	<b>Fri 23/8/19</b>																															
430	TTA Implementation	1 day	Thu 8/8/19	Thu 8/8/19	8/8																														
431	Demolition and Removal of Asphalt Surface	1 day	Fri 9/8/19	Fri 9/8/19	9/8																														
432	Excavation for PVC duct laying	1 day	Sat 10/8/19	Sat 10/8/19	10/8																														
433	Duct Laying	1 day	Sun 11/8/19	Sun 11/8/19	11/8																														
434	Backfilling to Formaiton Level	1 day	Mon 12/8/19	Mon 12/8/19	12/8																														


Task Milestone Rolled Up Task Rolled Up Progress External Tasks Group By Summary

Progress Summary Rolled Up Milestone Split Project Summary Deadline



# Programme for Outstanding and Defective Works

ID	Task Name	Duration	Start	Finish	Qtr 3, 2019																															
					July 2019							August 2019							September 2019							October 2019										
					14	17	20	23	26	29	1	4	7	10	13	16	19	22	25	28	31	3	6	9	12	15	18	21	24	27	30	3	6	9	12	15
435	Backfilling of Subbase Level and SRT	8 days	Tue 13/8/19	Tue 20/8/19																																
436	RB Laying	1 day	Wed 21/8/19	Wed 21/8/19																																
437	BC Laying	1 day	Thu 22/8/19	Thu 22/8/19																																
438	WC Laying	1 day	Fri 23/8/19	Fri 23/8/19																																
439	<b>Run-in at EVA (Western Portion)</b>	<b>16 days</b>	<b>Sat 24/8/19</b>	<b>Sun 8/9/19</b>																																
440	TTA Implementation	1 day	Sat 24/8/19	Sat 24/8/19																																
441	Demolition and Removal of Asphalt Surface	1 day	Sun 25/8/19	Sun 25/8/19																																
442	Excavation for PVC duct laying	1 day	Mon 26/8/19	Mon 26/8/19																																
443	Duct Laying	1 day	Tue 27/8/19	Tue 27/8/19																																
444	Backfilling to Formaiton Level	1 day	Wed 28/8/19	Wed 28/8/19																																
445	Backfilling of Subbase Level and SRT	8 days	Thu 29/8/19	Thu 5/9/19																																
446	RB Laying	1 day	Fri 6/9/19	Fri 6/9/19																																
447	BC Laying	1 day	Sat 7/9/19	Sat 7/9/19																																
448	WC Laying	1 day	Sun 8/9/19	Sun 8/9/19																																
449	<b>Construction of Lighting Cable Duct (Yacht Club)</b>	<b>10 days</b>	<b>Mon 4/11/19</b>	<b>Wed 13/11/19</b>																																
450	TTA Implementation	1 day	Mon 4/11/19	Mon 4/11/19																																
451	Demolition of Concrete Pavement	2 days	Tue 5/11/19	Wed 6/11/19																																
452	PVC Duct Laying	1 day	Thu 7/11/19	Thu 7/11/19																																
453	Backfilling of Trench	1 day	Fri 8/11/19	Fri 8/11/19																																
454	Subbase Laying and SRT	4 days	Sat 9/11/19	Tue 12/11/19																																
455	Concrete Laying	1 day	Wed 13/11/19	Wed 13/11/19																																
456	<b>Installation of Lamp Post (West of Triangular Island) (8 nos.)</b>	<b>26 days</b>	<b>Sat 10/8/19</b>	<b>Wed 4/9/19</b>																																
457	Inspection of laid cable duct by Hyd	7 days	Sat 10/8/19	Fri 16/8/19																																
458	Preparation work by Hyd Lighting Division for instllation of Lamp Post (8 nos.)	14 days	Sat 17/8/19	Fri 30/8/19																																
459	Installation of Lamp Post (2 nos./day)	5 days	Sat 31/8/19	Wed 4/9/19																																
460	<b>Installation of Lamp Post (East of Triangular Island to Yacht Club) (6 nos.)</b>	<b>26 days</b>	<b>Thu 14/11/19</b>	<b>Mon 9/12/19</b>																																
461	Inspection of laid cable duct Hyd	7 days	Thu 14/11/19	Wed 20/11/19																																
462	Preparation work by HyD Lighting Division for instllation of Lamp Post (6 nos.)	14 days	Thu 21/11/19	Wed 4/12/19																																
463	Installation of Lamp Post (2 nos./day)	5 days	Thu 5/12/19	Mon 9/12/19																																
464	<b>Construction Directional Sign at Triangle Island</b>	<b>213 days</b>	<b>Tue 14/5/19</b>	<b>Thu 12/12/19</b>																																
465	<b>Advance Work</b>	<b>211 days</b>	<b>Tue 14/5/19</b>	<b>Tue 10/12/19</b>																																
466	Submit shop drawing of traffic sign and frame to AECOM	0 days	Tue 14/5/19	Tue 14/5/19																																
467	Approval of shop drawing of traffic sign and frame by AECOM	14 days	Tue 14/5/19	Mon 27/5/19																																
468	Procurement of traffic sign and frame	30 days	Tue 28/5/19	Wed 26/6/19																																
469	Delivery of traffic sign and frame	0 days	Wed 26/6/19	Wed 26/6/19																																
470	Design of footing	7 days	Thu 6/6/19	Thu 13/6/19																																
471	Obtain ICE certificate for footing	1 day	Thu 13/6/19	Fri 14/6/19																																
472	Submission to AECOM	0 days	Fri 14/6/19	Fri 14/6/19																																
473	Approval of footing design	180 days	Fri 14/6/19	Tue 10/12/19																																
474	<b>Site Work</b>	<b>168 days</b>	<b>Fri 28/6/19</b>	<b>Thu 12/12/19</b>																																

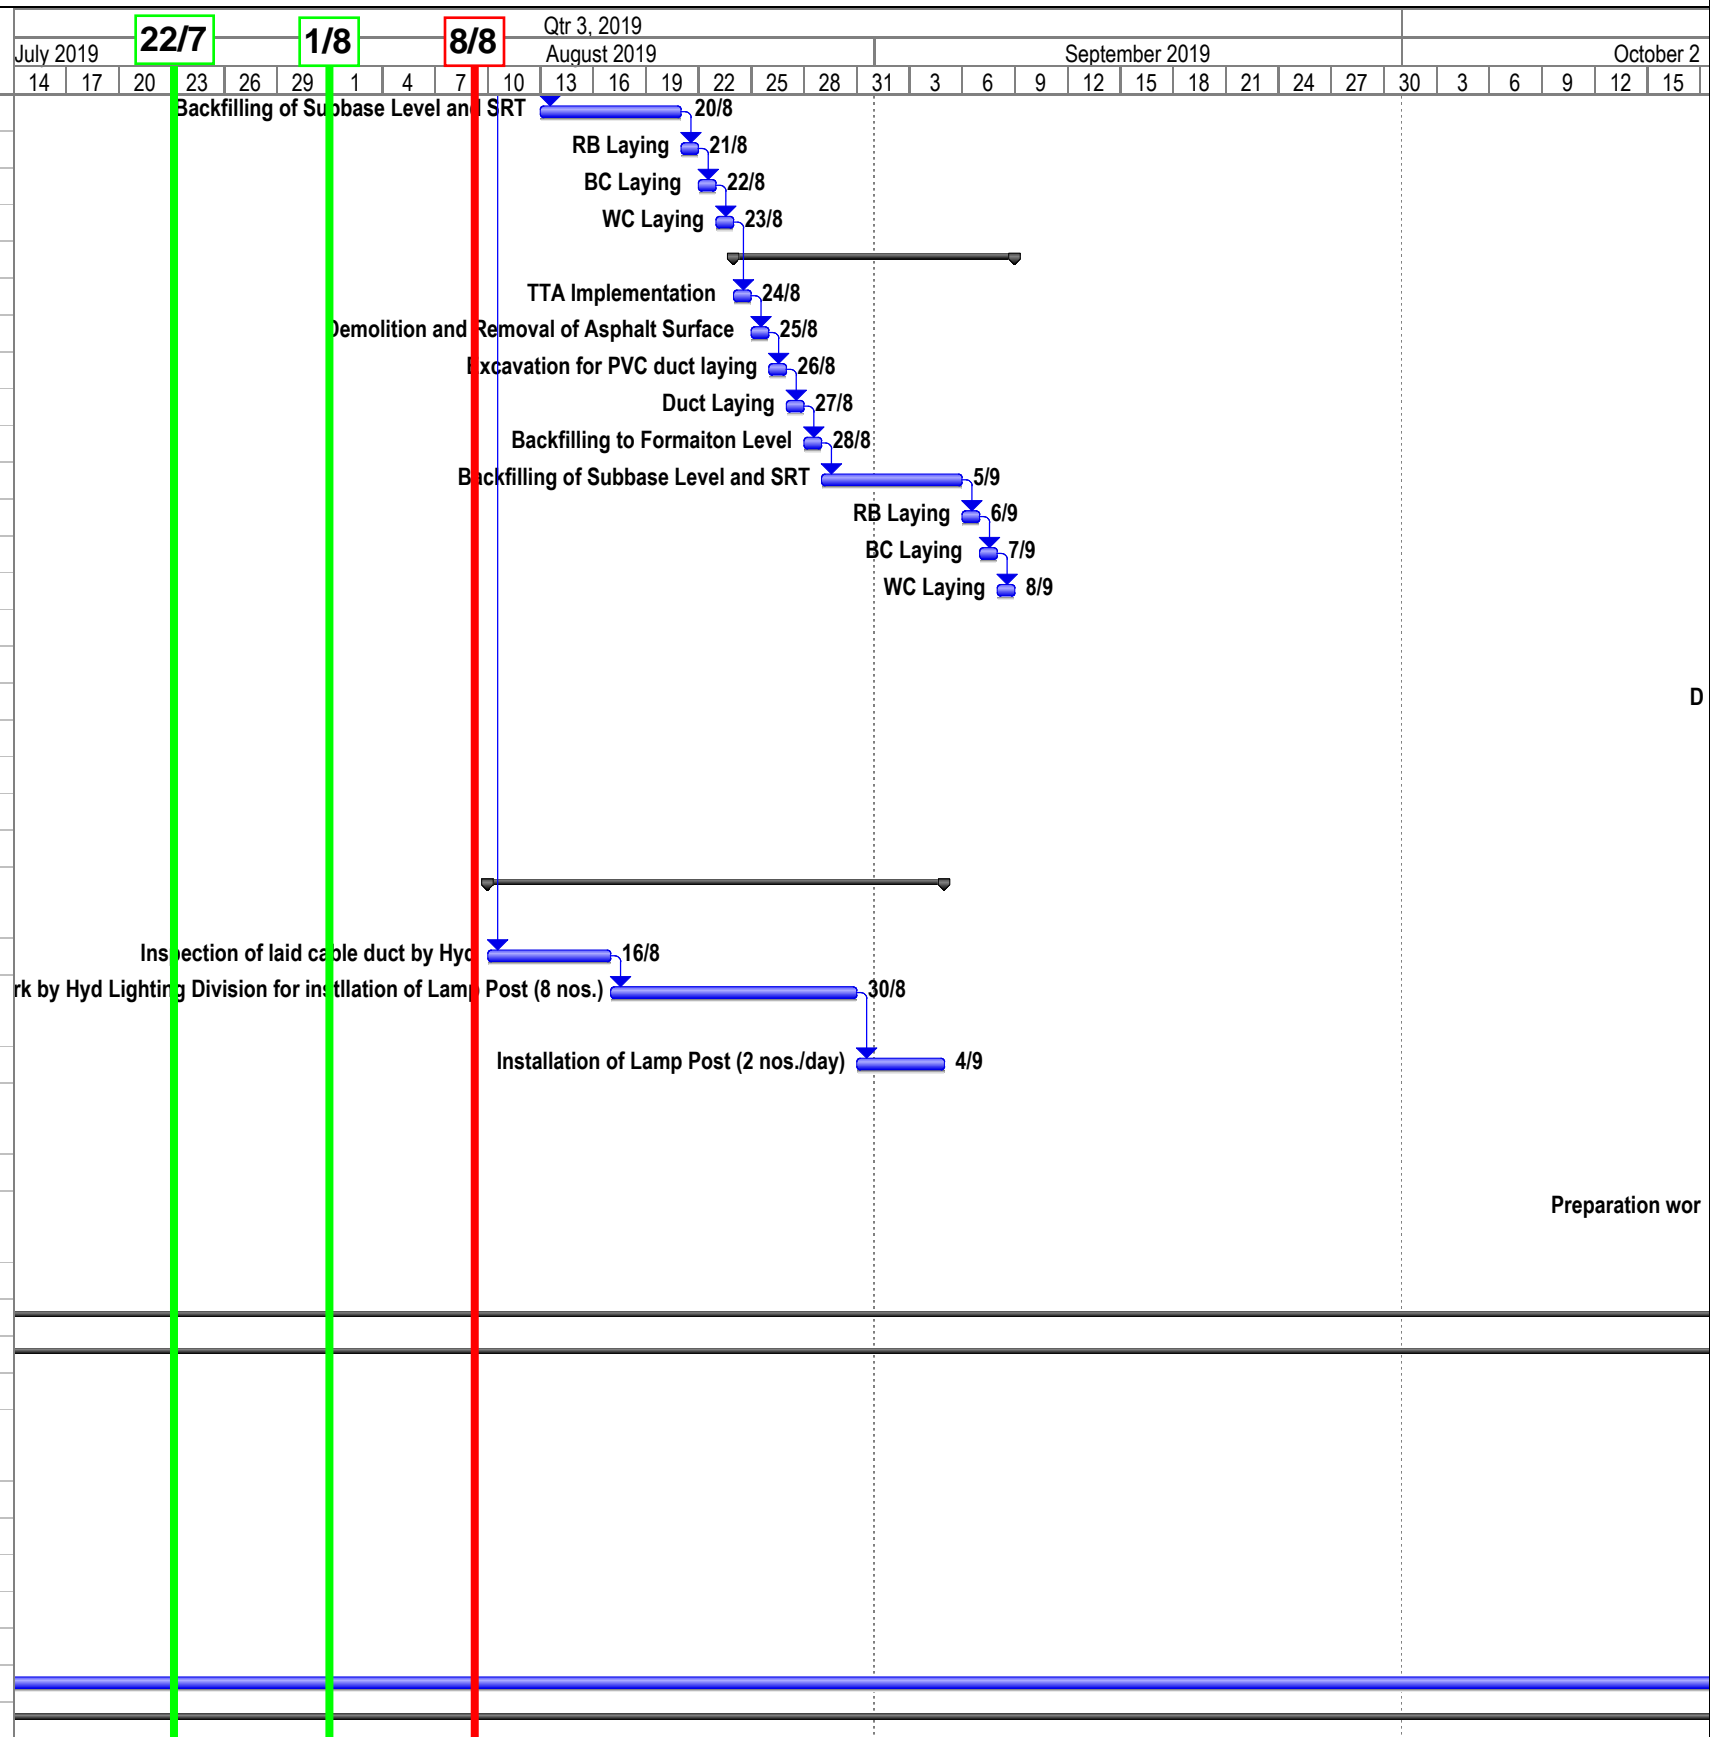

Task Milestone Rolled Up Task Rolled Up Progress External Tasks Group By Summary

Progress Summary Rolled Up Milestone Split Project Summary Deadline

Activity ID	Activity Name	Rem Dur	Start	Finish	2019																
					August			September				October				November				December	
					11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	01

**3MRP (2019.08.20)**

**01 - CONTRACT DATES**

**01.2 - Possession of Site**

0120-3600	Possession to Portion XIII	0	20-Aug-19*	
-----------	----------------------------	---	------------	--

**01.3 - Handback to Employer**

0130-2400	Handover Portion XI(A (Current Due Day + 28d = 29 Dec 2015)	0		12-Dec-19*
0130-2500	Handover Portion XI(C (Current Due Day + 28d = 17 Feb 2019)	0		24-Apr-20*
0130-2600	Handover Portion XI(B ((Current due date not known. Not instructed to commence yet))	0		18-Jul-20*
0130-2700	Handover Portion VI (Current Due Day + 28d = 22 Nov 2019)	0		09-Jul-20*
0130-2800	Handover Portion IA (Current Due Day + 28d = 22 Nov 2019)	0		09-Jul-20*
0130-2900	Handover Portion VII(A (Current Due Day + 28d = 22 Nov 2019)	0		09-Jul-20*
0130-3000	Handover Portion X (Current Due Day + 28d = 22 Nov 2019)	0		09-Jul-20*
0130-3100	Handover Portion III (Current Due Day + 28d = 22 Nov 2019)	0		09-Jul-20*
0130-3200	Handover Portion VA (Current Due Day + 28d = 22 Nov 2019)	0		09-Jul-20*
0130-3300	Handover Portion VC (Current Due Day + 28d = 22 Nov 2019)	0		09-Jul-20*
0130-3400	Handover Portion IVA (Current Due Day + 28d = 22 Nov 2019)	0		09-Jul-20*
0130-3500	Handover Portion IIA (Current Due Day + 28d = 22 Nov 2019)	0		21-Jan-20*
0130-3600	Handover Portion IIB (Current Due Day + 28d = 22 Nov 2019)	0		21-Jan-20*
0130-3700	Handover Portion XIII (Current due date not known. Not instructed to commence yet)	0		18-Jul-20*

**01.4 - Key Dates**

0140-0900	KD1 - Completion of Section X of the Works (Current Due Date - 20 Jan 2019)	0		27-Mar-20*
0140-1800	KD14 - Completion of Section 11 of the Works (Current Due Date - 1 Dec 2015)	0		14-Nov-19*
0140-2000	KD10 - Completion of Section 7 of the Works (Current Due Date - 25 Oct 2019)	0		11-Jun-20*
0140-2100	KD11 - Completion of Section 8 of the Works (Current Due Date - 25 Oct 2019)	0		11-Jun-20*
0140-2200	KD12 - Completion of Section 9 of the Works (Current Due Date - 25 Oct 2019)	0		11-Jun-20*
0140-2300	KD13 - Completion of Section 10 of the Works (Current Due Date - 25 Oct 2019)	0		11-Jun-20*
0140-2400	KD15 - Completion of Section 12 of the Works (Current Due Date - 25 Oct 2019)	0		24-Dec-19*
0140-2500	KD16 - Completion of Section 13 of the Works (Current due date not known. Not instructed to commence yet)	0		20-Jun-20*
0140-2600	KD19 - Completion of Section 14 of the Works (Current Due Date - 25 Oct 2019)	0		27-Jun-20
0140-2700	KD17 - Completion of Section 13A of the Works (Current Due Date - 25 Oct 2020)	0		21-Jun-21
0140-2800	KD18 - Completion of Section 13B of the Works (Current Due Date - 25 Oct 2020)	0		20-Jun-21


**10 - SECTION X OF THE WORKS**

**10.3 - Middle Bridge (Bridge F)**

**10.3.2 - Bridge Construction**


**Remaining Works**

1032-4500a	Concrete Surround for TCSS Ducting at Existing IEC bridge Bay 1 (Nightwork)	5	20-Aug-19*	24-Aug-19
1032-4500b	Concrete Surround for TCSS Ducting at Existing IEC bridge Bay 2 (Nightwork)	5	26-Aug-19	30-Aug-19

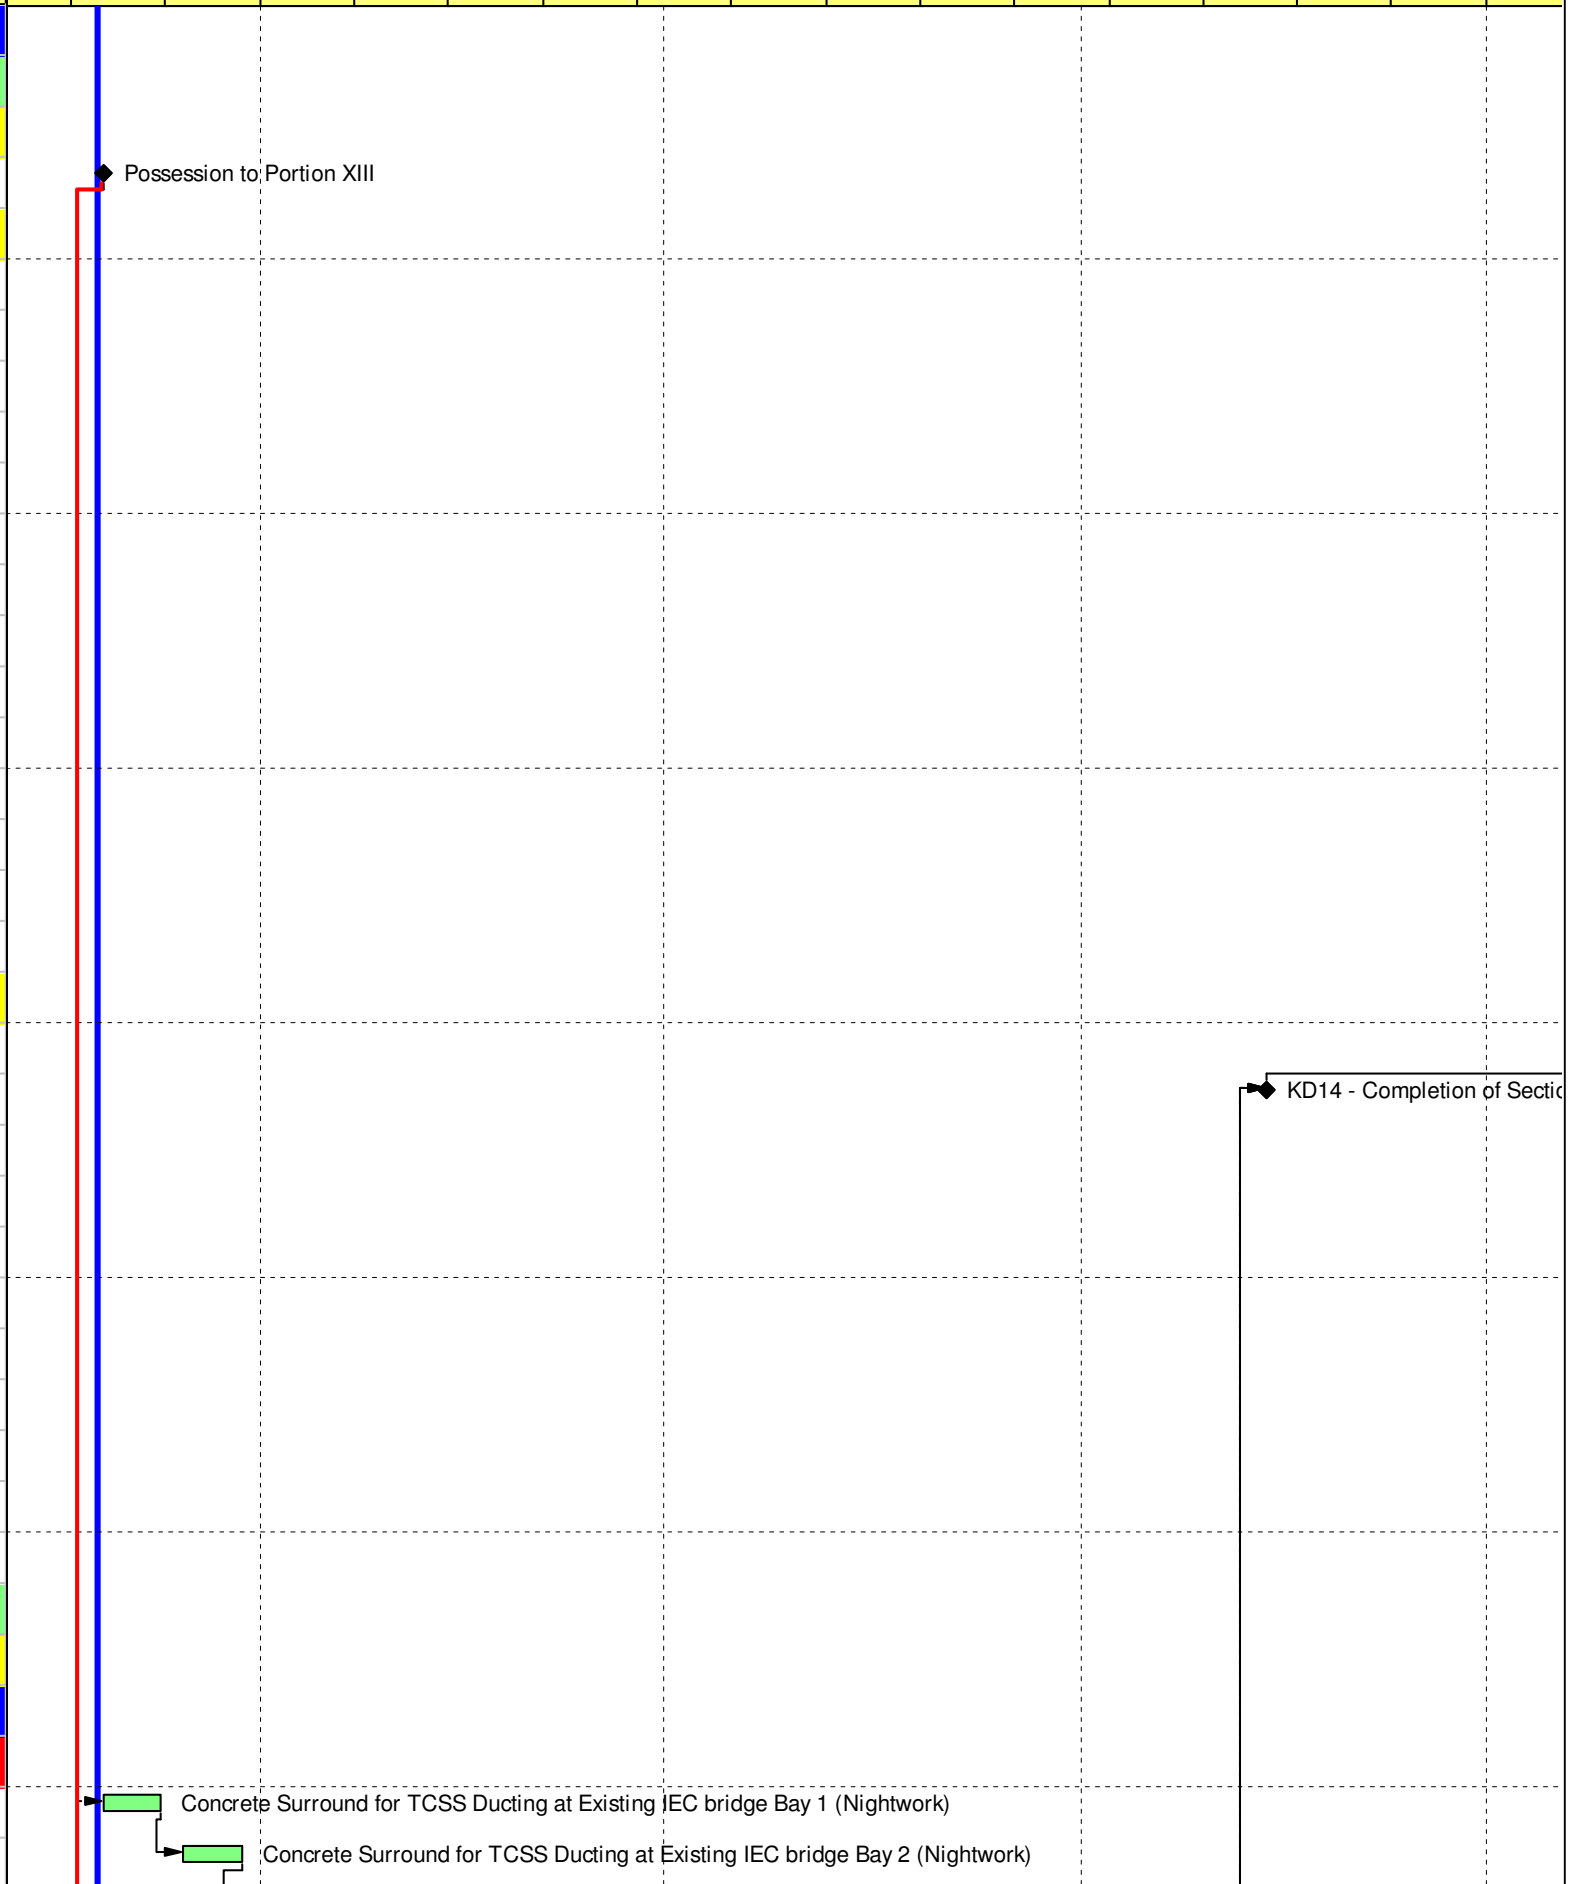

	Remaining Level of Effort		Remaining Work
	Actual Level of Effort		Critical Remaining Work
	Actual Work		Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Aug.2019 to 20.Nov.2019)**

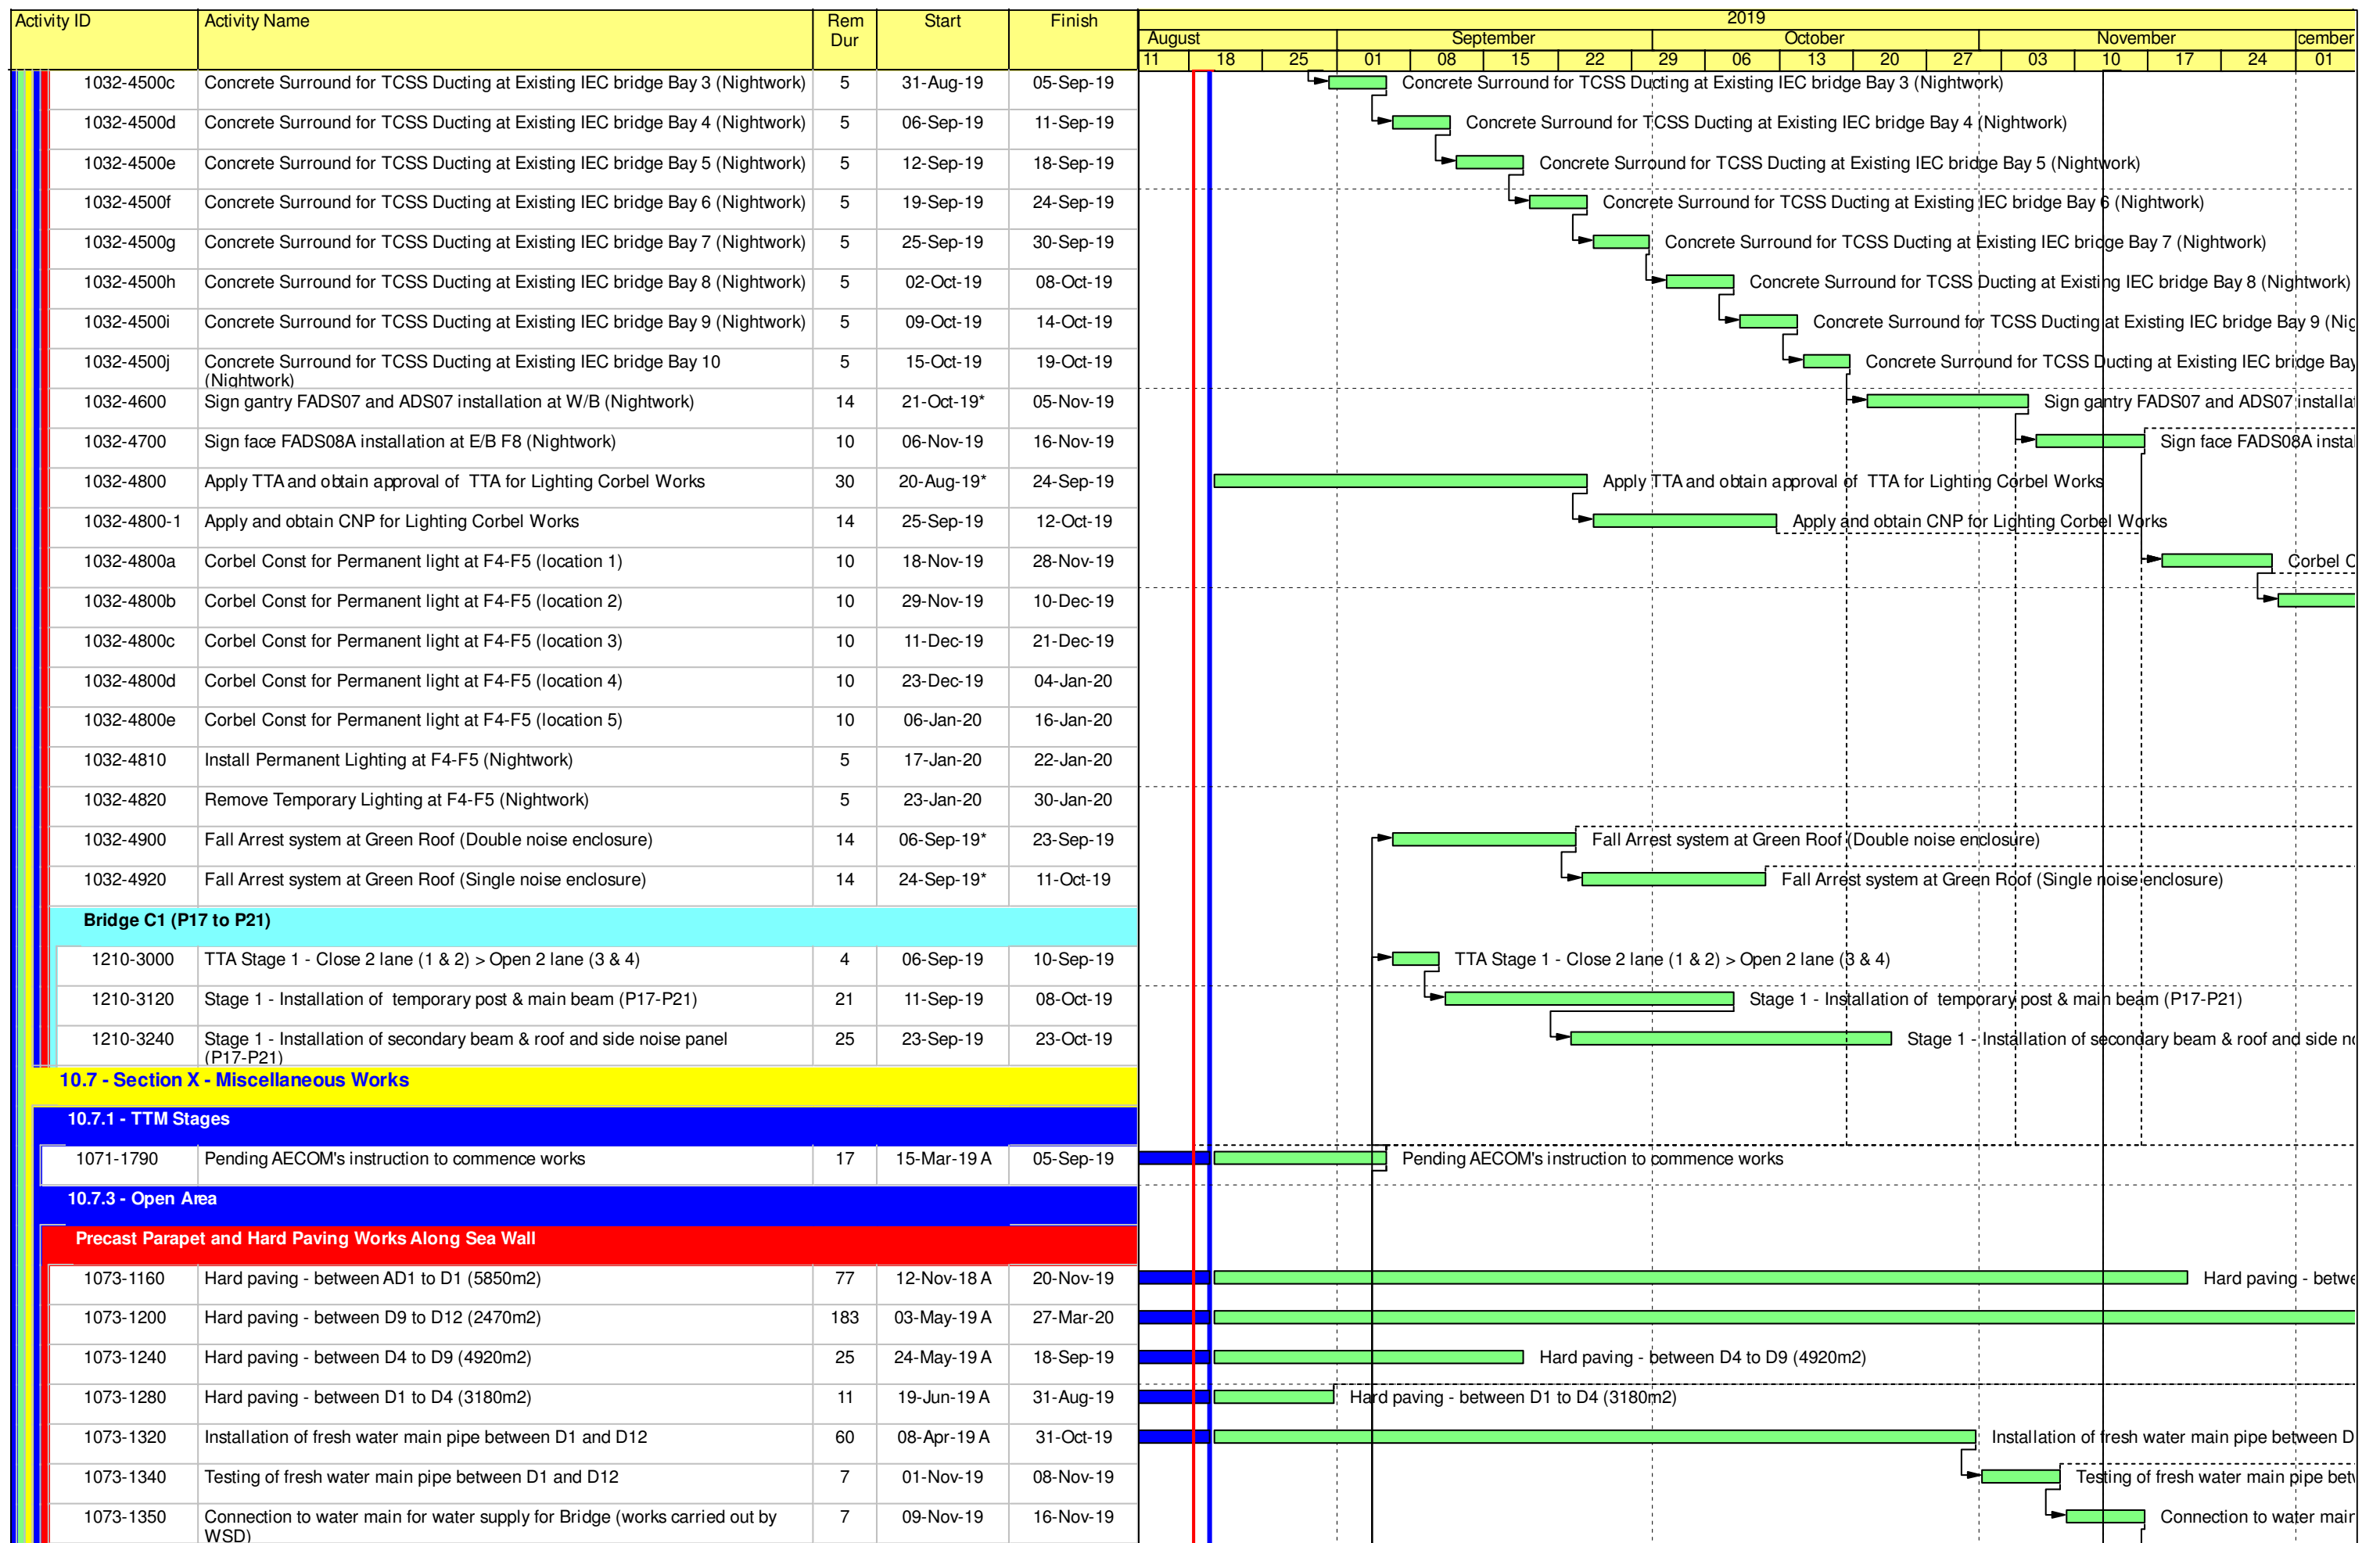

Activity ID	Activity Name	Rem Dur	Start	Finish	2019																		
					August			September				October				November				December			
					11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	01		
1073-1360	Removal of as constructed fire main at IEC E/B and W/B	90	18-Nov-19	05-Mar-20	[Gantt bar from 10/17/19 to 03/01/20]																		
<b>Masking Wall to D12</b>																							
1073-1500	South Part	21	20-Aug-19*	12-Sep-19	[Gantt bar from 20/08/19 to 12/09/19]																		
1073-1540	Middle Part	21	28-Aug-19	21-Sep-19	[Gantt bar from 28/08/19 to 21/09/19]																		
1073-1580	North Part	21	05-Sep-19	30-Sep-19	[Gantt bar from 05/09/19 to 30/09/19]																		
<b>10.7.4 - Outstanding Drainage Works</b>																							
<b>Near Pier D12 to Pier D7 from Pier D9-D12</b>																							
1073-2520	Backfilling 1m height	15	27-Apr-19 A	05-Sep-19	[Gantt bar from 27/04/19 to 05/09/19]																		
<b>Bet Pier D19-D26 - West of SR13 to Box Culvert (to commence after removal of girder)</b>																							
1073-2760	225 U Channel (4days/20m) (110m)	24	26-Aug-19*	23-Sep-19	[Gantt bar from 26/08/19 to 23/09/19]																		
1073-2800	Drain pit to Sand Trap with 225 pipe (10m)	5	24-Sep-19	28-Sep-19	[Gantt bar from 24/09/19 to 28/09/19]																		
<b>11 - SECTION 11 OF THE WORKS</b>																							
<b>11.4- Hing Fat Street</b>																							
<b>Stage 5 (TTA Drg. no.: CWBIEL/058-0921)</b>																							
1140-1930	Reconstruction pavement & road marking	7	23-Aug-19 A	27-Aug-19	[Gantt bar from 23/08/19 to 27/08/19]																		
1140-1940	EMSD connection to traffic light and public light (by others)	5	28-Aug-19	02-Sep-19	[Gantt bar from 28/08/19 to 02/09/19]																		
1140-1950	Remove existing gully and construct new gully (Portion)	14	05-Aug-19 A	04-Sep-19	[Gantt bar from 05/08/19 to 04/09/19]																		
<b>Triangular Island at Junction of Tsing Fung Street</b>																							
1140-2000	New kerb construction	11	19-Jun-19 A	31-Aug-19	[Gantt bar from 19/06/19 to 31/08/19]																		
1140-2030	Beam barrier construction	5	11-Sep-19*	17-Sep-19	[Gantt bar from 11/09/19 to 17/09/19]																		
1140-2040	Planting (including tranplanting tree)	53	11-Sep-19*	14-Nov-19	[Gantt bar from 11/09/19 to 14/11/19]																		
<b>Triangular Island at Junction of Wing Hing Street</b>																							
1140-2120	Hard paving	29	20-Aug-19	23-Sep-19	[Gantt bar from 20/08/19 to 23/09/19]																		
1140-2150	Construct beam barrier and Type 2 railing	14	24-Sep-19	11-Oct-19	[Gantt bar from 24/09/19 to 11/10/19]																		
1140-2170	Reinstate directional sign (by others)	30	12-Oct-19*	15-Nov-19	[Gantt bar from 12/10/19 to 15/11/19]																		
<b>Other Areas</b>																							
1140-2200	Modify existing island near Gordon Road	21	20-Aug-19*	12-Sep-19	[Gantt bar from 20/08/19 to 12/09/19]																		
1140-2210	New pedestrian crossing at Tsing Fung Street	25	15-Jul-19 A	18-Sep-19	[Gantt bar from 15/07/19 to 18/09/19]																		
1140-2220	Realignment of kerb along Hing Fat Street between Wing Hing Street and Tsing Fung Street	25	13-Aug-19 A	18-Sep-19	[Gantt bar from 13/08/19 to 18/09/19]																		
1140-2230	Remove existing gully and construct new gully (remaining)	49	11-Sep-19 A	18-Oct-19	[Gantt bar from 11/09/19 to 18/10/19]																		
1140-2250	Construction of Type 2 railing	23	19-Oct-19	14-Nov-19	[Gantt bar from 19/10/19 to 14/11/19]																		
<b>12 - SECTION 7, 8, 9, 10 &amp; 12 OF THE WORKS</b>																							
<b>12.1 - Landscape Deck</b>																							
1200-7700	Bay C3 > Sub-soil placing	30	25-Sep-19*	31-Oct-19	[Gantt bar from 25/09/19 to 31/10/19]																		
1200-7780	Bay C5 > Sub-soil placing	30	22-Jul-19 A	24-Sep-19	[Gantt bar from 22/07/19 to 24/09/19]																		
<b>12.2 - Permanent Noise Mitigation Measures</b>																							
<b>West Bound Bridge Between F2 to C2 (P40 to P22) (parapet mould 1)</b>																							

■ Remaining Level of Effort    ■ Remaining Work  
■ Actual Level of Effort    ■ Critical Remaining Work  
■ Actual Work    ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Aug.2019 to 20.Nov.2019)**



Activity ID	Activity Name	Rem Dur	Start	Finish	2019																	
					August			September				October				November				December		
					11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	01	
1210-1000	TTA Stage 1 - Close 2 lane (1 & 2) for traffic from Pier 41	4	06-Sep-19*	10-Sep-19																		
1210-1040	Bridge F2C (F3-F5) - Preparation works; Remove asphalt & drill holes for starter bars	6	11-Sep-19	18-Sep-19																		
1210-1080	Bridge F2C (F3-F5) - Construction of inner parapet (52m)	14	19-Sep-19	05-Oct-19																		
1210-1320	Bridge F1C (D12-F3 - Preparation works; drill holes/clean couplers for starter bars	8	19-Sep-19	27-Sep-19																		
<b>12.3 - Viaduct Planters &amp; Maintenance Access</b>																						
<b>East Bound Bridge Between F3 to E1 (P43 to P17) (Land Side) (parapet mould 2&amp;3)</b>																						
1220-2000	TTA Stage 1 - Close 2 lane (1 & 2); Open 2 lane (3 & 4); for traffic from Bridge F2A to E	4	06-Sep-19*	10-Sep-19																		
1220-2040	Bridge F1A to E - Removal of existing asphalt	4	11-Sep-19	16-Sep-19																		
1220-2080	Bridge F1A (F3-D12) - Preparation works; drill holes/clean couplers for starter bars	10	17-Sep-19	27-Sep-19																		
1220-2120	Bridge F1A (F3-D12) - Construction of inner parapet (88.4m)	15	24-Sep-19	12-Oct-19																		
1220-2160	Bridge F1A (F3-D12) - Construct planter wall (88.4m)	15	24-Sep-19	12-Oct-19																		
1220-2680	Bridge D2 (D6-D4) - Preparation works; drill holes/clean couplers for starter bars	10	17-Sep-19	27-Sep-19																		
1220-2720	Bridge D2 (D6-D4) - Construction of inner parapet (120m)	20	24-Sep-19	18-Oct-19																		
1220-2760	Bridge D2 (D6-D4) - Construct planter wall (120m)	20	24-Sep-19	18-Oct-19																		
<b>12.4 - Waterworks</b>																						
1230-1010	Irrigation System - Landscape Deck C1	30	20-Aug-19*	24-Sep-19																		
1230-1020	Irrigation System - Landscape Deck C2	30	20-Aug-19*	24-Sep-19																		
1230-1100a	Irrigation System - Green Roof (Bridge F1)	30	20-Aug-19*	24-Sep-19																		
1230-1100b	Irrigation System - Green Roof (Bridge F2)	30	25-Sep-19*	31-Oct-19																		
1230-1100c	Irrigation System - Green Roof (Bridge F3)	30	01-Nov-19	05-Dec-19																		
1230-1200	Irrigation System (Landscape Deck C1 & C2) - Testing	7	25-Sep-19	03-Oct-19																		
1230-1300	Connect to watermain for Water Supply (Landscape Deck C1 & C2) - Works carried out by WSD	7	04-Oct-19	12-Oct-19																		
<b>12.5 - Soft &amp; Hard Landscape</b>																						
1240-1010	U Channel & Footpath at Landscape Deck C1	41	29-May-19 A	09-Oct-19																		
1240-1020	U Channel & Footpath at Landscape Deck C2	34	28-Aug-19	09-Oct-19																		
1240-1030	U Channel & Footpath at Landscape Deck C3	30	09-Nov-19	13-Dec-19																		
1240-1040	U Channel & Footpath at Landscape Deck C4	30	29-Oct-19	02-Dec-19																		
1240-1050	U Channel & Footpath at Landscape Deck C5	30	25-Sep-19	31-Oct-19																		
1240-1060	Material submission and obtain approval for Green Roof Soft Landscape Works	28	15-Feb-19 A	21-Sep-19																		
1240-1060a	Root barrier (Green roof)	7	23-Sep-19*	30-Sep-19																		
1240-1060b	Drainage composite (Green roof)	14	02-Oct-19	18-Oct-19																		
1240-1070a	Top soil - Laying 150mm leca at Green Roof (Bridge F1)	10	19-Oct-19	30-Oct-19																		
1240-1070b	Top soil - Laying 150mm soil mix at Green Roof (Bridge F1)	40	31-Oct-19	16-Dec-19																		
1240-1070c	Top soil - Laying ploughing soil at Green Roof (Bridge F1)	2	17-Dec-19	18-Dec-19																		
1240-1260a	Planter box installation at Bridge W/B (F2C)	12	02-Nov-19	15-Nov-19																		
1240-1260b	Planter box installation at Bridge W/B (F1C)	36	03-Dec-19	15-Jan-20																		
1240-1260c	Planter box installation at Bridge W/B (C5)	36	28-Dec-19	11-Feb-20																		

■ Remaining Level of Effort    ■ Remaining Work  
■ Actual Level of Effort    ■ Critical Remaining Work  
■ Actual Work    ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Aug.2019 to 20.Nov.2019)**



Activity ID	Activity Name	Rem Dur	Start	Finish	2019																			
					August			September				October				November				December				
					11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	01			
1240-1310	Planting at Landscape Deck C1	65	10-Oct-19	24-Dec-19																				
1240-1320	Planting at Landscape Deck C2	65	25-Sep-19	11-Dec-19																				
1240-1340	Planting at Landscape Deck C4	30	03-Dec-19	08-Jan-20																				
1240-1350	Planting at Landscape Deck C5	30	01-Nov-19	05-Dec-19																				
1240-1700	Achieve KD15	0		24-Dec-19																				
<b>13 - SECTION 13 OF THE WORKS</b>																								
<b>13.2 - Roadworks</b>																								
1320-1020a	Apply TTA and obtain approval of TTA for Rumsey Street Flyover Demolition Works	30	20-Aug-19	24-Sep-19*																				
1320-1020b	Apply RA and obtain approval of RA for Rumsey Street Flyover Demolition Works	7	25-Sep-19	03-Oct-19																				
1320-1020c	Implementation of TTA	2	04-Oct-19	05-Oct-19																				
1320-1020d	Submit method statement and obtain approval for Rumsey Street Flyover Demolition Works	30	20-Aug-19	24-Sep-19*																				
<b>16 - SECTION 13B OF THE WORKS</b>																								
<b>16.1 - Soft Landscape</b>																								
1610-1100	Establishment Works at Portion IIA	365	25-Dec-19	23-Dec-20																				



<span style="color: green;">█</span> Remaining Level of Effort	<span style="background-color: lightgreen;">█</span> Remaining Work
<span style="color: blue;">█</span> Actual Level of Effort	<span style="background-color: red;">█</span> Critical Remaining Work
<span style="background-color: blue;">█</span> Actual Work	◆ ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Aug.2019 to 20.Nov.2019)**

Activity ID	Activity Name	Original Duration	Start	Finish	2019															
					Aug			Sep			Oct			Nov						
<b>Total</b>		385	21-Mar-19 A	02-Apr-20																
<b>DWP-08 - (2) - Update Progress As of 20 Aug 19</b>		385	21-Mar-19 A	02-Apr-20																
<b>KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks</b>		385	21-Mar-19 A	02-Apr-20																
<b>KD11 - Section 7A: Portion XIV &amp; XV (Victoria Park Open Space)</b>		365	21-Mar-19 A	29-Jan-20																
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365	21-Mar-19 A	29-Jan-20																
<b>KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH&gt;500mm)</b>		365	21-Mar-19 A	02-Apr-20																
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365	21-Mar-19 A	02-Apr-20																
<b>KD18 - Section 11: Transplanted Trees DBH&gt;500mm in Portion VA and XII</b>		365	21-Mar-19 A	02-Apr-20																
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365	21-Mar-19 A	02-Apr-20																

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Page 1 of 1  
 Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel (Slip Road 8 Section) - 3 Months Rolling Programme

Date	Revision	Checked	Approved
20-Aug-19	DWP-08 (2) - 3 Months Rolling	TL	TL

Data Date: 20-Aug-19

# CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2019			
						Aug	Sep	Oct	Nov
<b>Update 2019-08-20 CWB(CC) - Commissioning Contract (DWP 4d)</b>									
<b>PRELIMINARIES AND GENERAL REQUIREMENTS</b>									
<b>Salient Key Dates and Milestones</b>									
Anticipated Completion Dates									
KD09	KD9 - Completion of Section 4 of the Works (1445 days) - include EOT No.12 (149 days)	0		31-Oct-19*	-775			▲	◆
Possession Dates and Vacation Dates									
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-Aug-19	08-Dec-19	-554	[Red bar from Aug 20 to Dec 08]			
<b>Submissions and Approvals</b>									
Initial General Submission									
10168	Submission of CMC 3DVR	30	20-Aug-19	18-Sep-19	-367	[Red bar from Aug 20 to Sep 18]			
<b>PROCUREMENT, MANUFACTURING &amp; DELIVERIES</b>									
<b>Procurement; Manufacturing; Deliveries</b>									
Green Wall on ADB									
Procurement & Fabrication									
10248	ADB Green Wall - Embed fabrication & delivery	30	30-Oct-18 A	10-Aug-19 A		[Blue bar from Oct 30 18 to Aug 10 19]			
10252	ADB Green Wall - Green Wall Fabrication & delivery	52	30-Oct-18 A	25-Aug-19	-748	[Blue bar from Oct 30 18 to Aug 25 19]			
10250	ADB Green Wall - Commence embed installation	0	12-Aug-19 A			▲		◆	
10254	ADB Green Wall - Commence installation	0	26-Aug-19		-748	▲	▲	◆	◆
<b>CONSTRUCTION</b>									
<b>East Ventilation Building (EVB - related)</b>									
East Ventilation Building (EVB)									
Final Completion Works									
192232	RFV 650 - ST-06 Glass Canopy Procurement (* Additional work without completion time frame)	24	01-Aug-19 A	02-Sep-19	-621	[Blue bar from Aug 01 to Sep 02]			
192234	RFV 650 - ST-06 Glass Canopy Manufacturing and deliver to site (* Additional work without completion time frame)	24	03-Sep-19	02-Oct-19	-621	[Red bar from Sep 03 to Oct 02]			

<ul style="list-style-type: none"> <li>◆ Current Milestone</li> <li>▬ Level of Effort</li> <li>▲ Baseline Milestone</li> <li>▬ Actual Work</li> <li>▬ Critical Remaining Work</li> </ul>	<ul style="list-style-type: none"> <li>▬ Remaining Work</li> <li>▬ Project Baseline</li> </ul>
--	--

## Leighton Contractors (Asia) Limited

### Programme Update 66 (August 2019)

#### THREE MONTH ROLLING



Project ID: H2613-U066  
 Baseline: DWP4d  
 Layout: Update Three Month Rolling  
 U066  
 Page 1 of 3

Date	Revision	Checked	Approv...
20-Jul-19	U065	AT	CW
20-Aug-19	U066	AT	CW

Data Date: 20-Aug-19

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

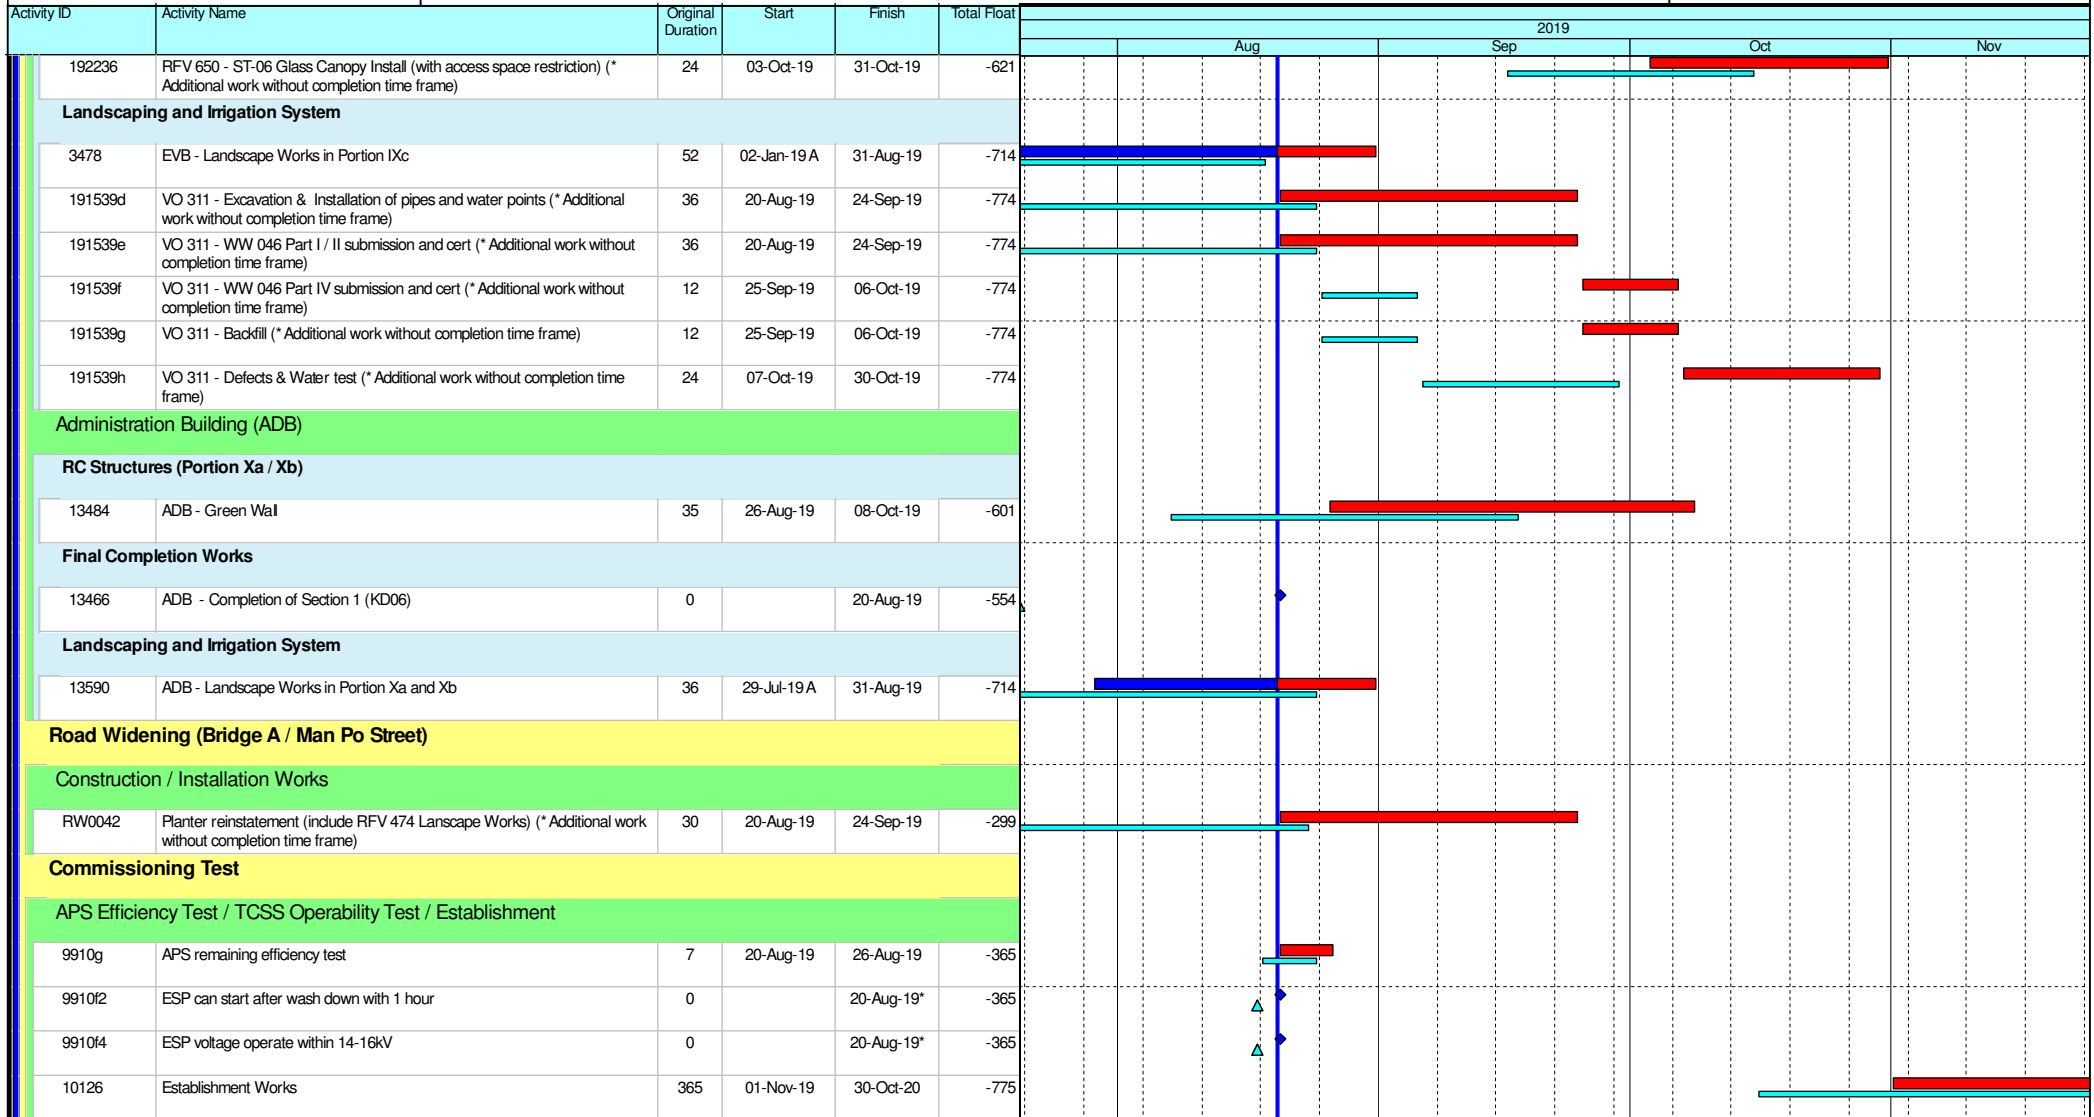

### Leighton Contractors (Asia) Limited Programme Update 66 (August 2019) THREE MONTH ROLLING

Project ID: H2613-U066  
 Baseline: DWP4d  
 Layout: Update Three Month Rolling  
 U066  
 Page 2 of 3

Date	Revision	Checked	Approv...
20-Jul-19	U065	AT	CW
20-Aug-19	U066	AT	CW










Data Date: 20-Aug-19

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2019																
						Aug			Sep			Oct			Nov							
<b>Training / Plan / Manual / As-Built Drawings for Project Completion</b>																						
192114	As-Built Drawings submission	0		20-Aug-19*	-337																	
10226	Routine Maintenance Records / Maintenance Monthly Report	0	01-Nov-19		-410																	

-  Current Milestone
-  Level of Effort
-  Actual Work
-  Critical Remaining Work
-  Remaining Work
-  Project Baseline
-  Baseline Milestone

### Leighton Contractors (Asia) Limited Programme Update 66 (August 2019) THREE MONTH ROLLING

Project ID: H2613-U066  
 Baseline: DWP4d  
 Layout: Update Three Month Rolling  
 U066  
 Page 3 of 3

Date	Revision	Checked	Approv...
20-Jul-19	U065	AT	CW
20-Aug-19	U066	AT	CW
