


Contract No. HK/2009/01

Wan Chai Development Phase II – Central -Wan Chai Bypass at  
Hong Kong Convention and Exhibition Centre

**Construction Activities for Three Months Rolling**

Construction Activities	December 2017	January 2018	February 2018
Reinstatement of Amenity Area			













Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2018	2018	2018	
					Jan	Feb	Mar	
<b>HK/2012/08 Revised Works Programme Rev.12.0(DD 20 November 2017)</b>								
<b>Dredging and Reclamation</b>								
<b>Marine Work Construction</b>								
<b>Zone D</b>								
<b>Seawall Construction - Zone D</b>								
<b>Seawall 10 &amp; 11</b>								
MAR20630	Zone D - Seawall 10 & 11: Install remaining seawall block	14	08-Jan-2018*	21-Jan-2018	[Green bar]			
MAR20650	Zone D - Seawall 10 & 11: Backfill Type A	7	22-Jan-2018	28-Jan-2018	[Green bar]			
MAR20670	Zone D - Seawall 10 & 11: Lay geotextile and filter	7	29-Jan-2018	04-Feb-2018	[Green bar]			
<b>Works for Section Completion</b>								
<b>Construction</b>								
<b>Section III A - Road A2, A4 &amp; A5</b>								
<b>Roadwork &amp; Utilities - Section 1 (L1806 - L1801)</b>								
SIIIA10270	Sec III A - section 1 carriageway - Construct M/H F9	7	20-Dec-2017	29-Dec-2017	[Green bar]			
SIIIA10272	Sec III A - section 1 carriageway - connect M/F F9 to existing pipe	7	30-Dec-2017	08-Jan-2018	[Green bar]			
SIIIA10274	Sec III A - section 1 carriageway - construct M/H F8C	7	20-Dec-2017	29-Dec-2017	[Green bar]			
SIIIA10276	Sec III A - section 1 carriageway - sewerage pipe from M/H F9 to F8C	3	30-Dec-2017	03-Jan-2018	[Green bar]			
SIIIA10278	Sec III A - section 1 carriageway - sewerage pipe from M/H 8C to F8B	15	30-Dec-2017	17-Jan-2018	[Green bar]			
SIIIA10279b	Sec III A - section 1 carriageway - sewerage pipe from M/H 8C to F8B (night time): construct M/H F8B	6	13-Dec-2017 A	28-Dec-2017	[Green bar]			
SIIIA10279c	Sec III A - section 1 carriageway - sewerage pipe from M/H 8C to F8B (night time): construct sewerage pipe	29	02-Jan-2018	03-Feb-2018	[Red bar]			
SIIIA10292	Sec III A - section 1 carriageway - construct M/H F8A	7	09-Jan-2018	16-Jan-2018	[Green bar]			
SIIIA10293	Sec III A - section 1 carriageway - sewerage pipe from M/H F8B - F8A (night time)	6	05-Feb-2018	10-Feb-2018	[Red bar]			
SIIIA10294	Sec III A - section 1 carriageway - sewerage pipe from M/H F8A - F8	11	17-Jan-2018	29-Jan-2018	[Green bar]			
SIIIA10295	Sec III A - carriageway - works prior TTA stage 5: excavation and duct laying of TCSS and public lighting	7	18-Jan-2018	25-Jan-2018	[Green bar]			
SIIIA10296	Sec III A - section 1 carriageway - works prior TTA stage 5: reinstate damaged manhole and pipeline	14	20-Dec-2017	08-Jan-2018	[Green bar]			
SIIIA10297	Sec III A - section 1 carriageway - works prior TTA stage 5: construct 225mm storm drain from D5.2 to existing	7	09-Jan-2018	16-Jan-2018	[Green bar]			
SIIIA10298	Sec III A - section 1 carriageway - works prior TTA stage 5: road kerb	5	26-Jan-2018	31-Jan-2018	[Green bar]			
SIIIA10301	Sec III A - section 1 carriageway - works prior TTA stage 5: road formation	2	01-Feb-2018	02-Feb-2018	[Green bar]			
SIIIA10302	Sec III A - section 1 carriageway - works prior TTA stage 5: laying asphalt	5	03-Feb-2018	08-Feb-2018	[Green bar]			
SIIIA10303	Sec III A - section 1 carriageway - works prior TTA stage 5: road marking & preparation works	3	12-Feb-2018	14-Feb-2018	[Red bar]			
SIIIA10310	Sec III A - section 1 carriageway - TTA stage 5: Implementation of TTA Stage 5	1	15-Feb-2018	15-Feb-2018	[Red dot]			
<b>Roadwork &amp; Utilities - Section 2 (L1810 - L1807)</b>								
SIIIA12550	Sec III A - roadwork and utilities section 2 carriageway - Utilities: HEC along carriageway & Crossroad duct (HEC &	7	25-Nov-2017 A	29-Dec-2017	[Green bar]			
SIIIA12570	Sec III A - roadwork and utilities section 2 carriageway - road kerb & formation	17	30-Dec-2017	19-Jan-2018	[Green bar]			
SIIIA12590	Sec III A - roadwork and utilities section 2 carriageway - black top	7	20-Jan-2018	27-Jan-2018	[Green bar]			

Data Date: 20-Dec-2017

- ◆ Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- ▬ Remaining Level of Effort

**3 Months Rolling Programme for Non-CR III Area (January 2018 - March 2018)**  
(Ref. to Revised Works Programme Rev.12)

Date	Revision	Checked	Approved
20-Dec-2017	12		



Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2018		
					Jan	Feb	Mar
<b>Roadwork &amp; Utilities - Section 3 (L1808 - L1102)</b>							
SI3A12710	Sec III A - roadwork and utilities section 3 carriageway - Drainage works (L1301 - L1102)	2	11-Dec-2017 A	21-Dec-2017			
SI3A12750	Sec III A - roadwork and utilities section 3 carriageway - gully pipe (L1808A - L1102)	12	22-Dec-2017	08-Jan-2018			
SI3A12762	Sec III A - roadwork and utilities section 3 carriageway - watermain	10	09-Jan-2018	19-Jan-2018			
SI3A12770	Sec III A - roadwork and utilities section 3 carriageway - utilities: HEC ducting (60m) & crossroad duct (PCCW & HGC)	16	20-Jan-2018	07-Feb-2018			
SI3A12790	Sec III A - roadwork and utilities section 3 carriageway - road kerb & formation	17	08-Feb-2018	02-Mar-2018			
<b>Roadwork &amp; Utilities - Section 4 (L1406 - L1401)</b>							
SI3A12950	Sec III A - roadwork and utilities section 4 carriageway - drainage works (L1402 - L1401)	4	11-Dec-2017 A	23-Dec-2017			
SI3A12970	Sec III A - roadwork and utilities section 4 carriageway - gully pipe (L1401)	10	27-Dec-2017	08-Jan-2018			
SI3A13000	Sec III A - roadwork and utilities section 4 carriageway - formation (L1401)	5	09-Jan-2018	13-Jan-2018			
SI3A13050	Sec III A - roadwork and utilities section 4 carriageway - black top (L1401)	5	15-Jan-2018	19-Jan-2018			
<b>Roadwork &amp; Utilities - Section 6 (L1102 - L1411)</b>							
SI3A13380	Sec III A - roadwork and utilities section 6 carriageway - sealing up the gap beneath bay 12 of culvert L	0	08-Nov-2017 A	01-Dec-2017 A			
SI3A13385	Sec III A - roadwork and utilities section 6 carriageway - Waterproofing of water channel	3	02-Dec-2017 A	22-Dec-2017			
SI3A13389	Sec III A - roadwork and utilities section 6 carriageway - Backfilling of water channel from bay 16 to bay 20B	5	23-Dec-2017	30-Dec-2017			
SI3A13395	Sec III A - roadwork and utilities section 6 carriageway - Drainage works (L1101-L1102)	9	02-Jan-2018	11-Jan-2018			
SI3A13399	Sec III A - roadwork and utilities section 6 carriageway - gully pipe (L1101 - L1102)	8	12-Jan-2018	20-Jan-2018			
SI3A13444	Sec III A - roadwork and utilities section 6 carriageway - watermain (road crossing)	7	22-Jan-2018	29-Jan-2018			
SI3A13445	Sec III A - roadwork and utilities section 6 carriageway - utilities: crossed duct(HEC , HGC, PCCW)	13	30-Jan-2018	13-Feb-2018			
SI3A13450	Sec III A - roadwork and utilities section 6 carriageway - road kerb & formation	18	14-Feb-2018	09-Mar-2018			
<b>Section V - Remaining At-Grade Road &amp; Road P2</b>							
<b>Roadwork &amp; Utilities</b>							
<b>Section 1 (L1504 - L1900)</b>							
SV12456	Sec V-Roadwork & Utilities Section 1 - implementation of TTA stage 5E (closure of slow lane at northbound of Expo	1	15-Jan-2018*	15-Jan-2018			
SV12460	Sec V - Roadwork & Utilities Section 1 - drainage works (L1902 - L1900)	15	16-Jan-2018	01-Feb-2018			
SV12462	Sec V - Roadwork & Utilities Section 1 - gully pipe (L1902 - L1900)	6	02-Feb-2018	08-Feb-2018			
SV12464	Sec V - Roadwork & Utilities Section 1 - temp. reinstatement to match with existing Expo Drive	14	09-Feb-2018	28-Feb-2018			
SV12540	Sec V - Roadwork & Utilities Section 1 footpath - Watermain	6	11-Dec-2017 A	28-Dec-2017			
SV12570	Sec V - Roadwork & Utilities Section 1 footpath - utilities:TCSS	30	29-Dec-2017	02-Feb-2018			
SV12580	Sec V - Roadwork & Utilities Section 1 footpath - paving block	29	03-Feb-2018	12-Mar-2018			
<b>Section 2 (L1510 - L1504)</b>							
SV12622	Sec V - Roadwork & Utilities Section 1 Carriageway - gully pipe (L1611 - L1609)	8	13-Dec-2017 A	30-Dec-2017			
SV12624	Sec V - Roadwork & Utilities Section 1 Carriageway - road kerb & formation	21	02-Jan-2018	25-Jan-2018			
SV12626	Sec V - Roadwork & Utilities Section 1 Carriageway - black top	13	26-Jan-2018	09-Feb-2018			
SV12690	Sec V - Roadwork & Utilities Section 2 footpath - Drainage Works (L2104 - L2105)	18	23-Dec-2017	16-Jan-2018			
SV12692	Sec V - Roadwork & Utilities Section 2 footpath - U channel	14	17-Jan-2018	01-Feb-2018			
SV12695	Sec V - Roadwork & Utilities Section 2 footpath - Watermain	13	02-Feb-2018	20-Feb-2018			
<b>Section 3 (Culvert L - L1510)</b>							
SIV12810	Sec V - Roadwork & Utilities Section 3 Carriageway - Gully pipe (Culvert L - L1611)	3	24-Nov-2017 A	22-Dec-2017			
SIV12820	Sec V - Roadwork & Utilities Section 3 Carriageway - Black top	21	23-Dec-2017	19-Jan-2018			



Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2018		
					Jan	Feb	Mar
SIV12844	Sec V - Roadwork & Utilities Section 3 footpath - U channel	6	02-Dec-2017 A	28-Dec-2017			
SIV12850	Sec V - Roadwork & Utilities footpath - Watermain	14	29-Dec-2017	15-Jan-2018			
SIV12860	Sec V - Roadwork & Utilities Section 3 footpath - Utilities: TCSS, HGC, PCCW)	34	16-Jan-2018	27-Feb-2018			
<b>Section IV - Slip Road 3</b>							
<b>Roadwork &amp; Utilities</b>							
<b>Section 1 (L1608 - L1601)</b>							
SIV11740	Sec IV - Re-Possion of the areas S and P	0	08-Dec-2017 A				
SIV11742	Sec IV - Re-Possion of the area at the end of Road P2	0	30-Dec-2017*				
SIV11744	Sec IV - sign gantry DS20 footing (type 1): remove existing 600mm drain pipe	4	20-Dec-2017*	23-Dec-2017			
SIV11745	Sec IV - sign gantry DS20 footing (type 1): excavation	2	27-Dec-2017	28-Dec-2017			
SIV11746	Sec IV - sign gantry DS20 footing (type 1): footing structure	14	29-Dec-2017	15-Jan-2018			
SIV11747	Sec IV - sign gantry DS20 & DS21 footing (type 2): excavation & ELS	21	30-Dec-2017	24-Jan-2018			
SIV11748	Sec IV - sign gantry DS20 & DS21 footing (type 2): footing structure	21	25-Jan-2018	21-Feb-2018			
SIV11760	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Drainage Works (L1607 - L1601)	30	09-Dec-2017 A	26-Jan-2018			
SIV11761	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Drainage Works (L1602 - L2005)	7	16-Jan-2018	23-Jan-2018			
SIV11762	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Drainage Works (L2103-L2101A)	17	27-Jan-2018	15-Feb-2018			
<b>Section 2 (L2301 - L2103)</b>							
SIV11940	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Drainage Works (L2301-L2103)	5	09-Dec-2017 A	27-Dec-2017			
SIV11942	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Gully pipe (L2301-L2013, L1608-L1609)	22	28-Dec-2017	23-Jan-2018			
SIV11960	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Watermain	10	24-Jan-2018	03-Feb-2018			
SIV12010	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Road kerb & formation	20	05-Feb-2018	02-Mar-2018			
<b>Section 3 (M/H1.6 - L2301)</b>							
SIV12092	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Drainage Works (M/H1.7 - L2301)	59	28-Dec-2017	10-Mar-2018			
SIV12096	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - M1.7-M1.6: construct manholes	28	29-Nov-2017 A	24-Jan-2018			
SIV12102	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - M1.7-M1.6: demolish existing seawall	13	25-Jan-2018	08-Feb-2018			
SIV12103	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - M1.7-M1.6: ELS	10	09-Feb-2018	23-Feb-2018			
<b>Section VII - Remainder Works</b>							
<b>Road &amp; Drainage Works (Culvert L - M/H1.7, Adjacent to SR3)</b>							
SVII11600	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - Drainage Works (Culvert L -MH1.7)	59	08-Jan-2018	20-Mar-2018			
<b>Retaining Wall RW5 Construction</b>							
SVII10660	Sec VII - Retaining Wall RW5 (bay 1) - construct base slab and wall	22	05-Feb-2018	05-Mar-2018			
SVII10800	Sec VII - Retaining wall RW5 (bay 3) - construct base slab and wall	22	05-Feb-2018	05-Mar-2018			
<b>Promenade Seawall Parapet Construction &amp; EVA</b>							
<b>Promenade Footpath</b>							
<b>Section 2</b>							
SVII12610	Sec VII - section 2 footpath - drainage works : L2202 - L2203A	20	29-Jan-2018	23-Feb-2018			
<b>Section 3</b>							
SVII12850	Sec VII - section 3 footpath - watermain	17	20-Jan-2018	08-Feb-2018			
SVII12870	Sec VII - section 3 footpath - utilities (HEC, TCSS, HGC, PCCW)	40	09-Feb-2018	03-Apr-2018			
<b>Section 4</b>							





Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2018		
					Jan	Feb	Mar
SVII13050	Sec VII - section 4 footpath - drainage works (L2203 -L2203A)	0	21-Nov-2017 A	14-Dec-2017 A			
SVII13110	Sec VII - section 4 footpath - paving block	25	14-Feb-2018	17-Mar-2018		[Green bar spanning Feb and Mar]	
<b>Section 5</b>							
SVII13270	Sec VII - section 5 footpath - drainage works :L2203A -L2204	10	15-Dec-2017 A	03-Jan-2018	[Green bar]		
SVII13275	Sec VII - section 5 footpath - watermain	14	04-Jan-2018	19-Jan-2018	[Green bar]		
SVII13310	Sec VII - section 5 footpath - utilities: HEC, TCSS, HGC, PCCW	42	20-Jan-2018	13-Mar-2018		[Green bar spanning Feb and Mar]	
<b>Section 6</b>							
SVII13490	Sec VII - section 6 footpath - drainage works(Culvert L - L2204)	14	12-Jan-2018	27-Jan-2018	[Green bar]		
SVII13510	Sec VII - section 6 footpath - watermain	13	03-Feb-2018	21-Feb-2018		[Green bar]	
<b>Section X - Protection &amp; Preservation of Trees</b>							
<b>Soft Landscaping Works</b>							
SX10020	Sec X - Protection & Preservation of Trees	276	31-Jan-2013 A	21-Sep-2018	[Red bar spanning all months]		

Activity ID	Activity Name	Rem Dur	Start	Finish	2017							2018						
					December							January						
					17	24	31	07	14	21	28	February			March			
								04	11	18	25	04	11	18	25			
<b>3MRP (Dec 2017 - Mar 2018)</b>																		
<b>03 - PRELIMINARY WORKS</b>																		
<b>03.3 - Interface Works</b>																		
0330-1040	Relocate FEHD to Permanent Depot	9	30-Dec-17	10-Jan-18														
0330-1045	Clean-up Area after Relocation	3	11-Jan-18	13-Jan-18														
<b>FEHD Permanent Depot</b>																		
0330-1071	Installation of Post (43Nos) > Facility Area 5 & 10	6	20-Dec-17*	27-Dec-17														
0330-1073	Construction of Steel Roof > Facility Area 5 & 10	6	26-Dec-17	02-Jan-18														
0330-1075	Sprinkler System Installation > Facility Area 5 & 10	7	30-Dec-17	08-Jan-18														
0330-1077	T & C of Sprinkler System > Facility Area 5 & 10	6	09-Jan-18	15-Jan-18														
0330-1081	Installation of Post (73Nos) > Facility Area 6, 8 & 9	9	20-Dec-17	30-Dec-17														
0330-1095	Signage Works & remaining light post	3	20-Dec-17	22-Dec-17														
A4910	Road Marking & Misc Works	8	20-Dec-17	29-Dec-17														
<b>10 - SECTION X OF THE WORKS</b>																		
<b>10.1 - E/B Bridges (Bridge D, E and F)</b>																		
<b>10.1.4 - Bridge E / Hing Fat Slip Road</b>																		
<b>Bridge Construction</b>																		
1014-2280	Bridge E - Construct Permanent parapet at "TB" Tie-in	9	08-Sep-17 A	30-Dec-17														
<b>10.3 - Middle Bridge (Bridge F)</b>																		
<b>10.3.2 - Bridge Construction</b>																		
<b>Bridge F3B</b>																		
1032-2550	Bridge F3B - Installation of CC & Temporary Lighting	14	04-Dec-17 A	06-Jan-18														
1032-2560	Bridge F3B - Deck Road Waterproofing, Surfacing & Marking	6	08-Jan-18	13-Jan-18														
1032-2561	Divert 2 Lane Traffic (Stage 1)	0	14-Jan-18															
1032-2562	Bridge F3B - Construct Int. Double Noise Encl. (83m) (stage 2)	26	15-Jan-18	13-Feb-18														
1032-2563	Bridge F3B - Deck Road Waterproofing, Surfacing & Marking	6	08-Feb-18	14-Feb-18														
1032-2564	Divert 2 Lane Traffic (Stage 2)	0	15-Feb-18															
<b>Bridge F2B</b>																		
1032-3120	Bridge F2B - Construct Int. Double Noise Encl.	14	11-Nov-17 A	06-Jan-18														
1032-3140	Bridge F2B - Deck Road Waterproofing, Surfacing & Marking	6	08-Jan-18	13-Jan-18														
<b>Bridge F1B2</b>																		
1032-3840	Bridge F1B2 - Longitudinal Stitching	33	19-Jan-18	01-Mar-18														
1032-3860	Bridge F1B2 - Southern Parapet	24	14-Dec-17 A	18-Jan-18														
1032-3880	Bridge F1B2 - Construct Int. Double Noise Encl. Bridge F1B2	48	13-Jan-18	13-Mar-18														
1032-3900	Bridge F1B2 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking	7	14-Mar-18	21-Mar-18														
<b>Bridge F1B1</b>																		
1032-1740	Bridge F1B1 - Longitudinal Stitching	57	16-Dec-17 A	01-Mar-18														
1032-1760	Bridge F1B1 - Construct Median Barriers	30	29-Dec-17	02-Feb-18														
1032-1780	Bridge F1B1 - Construct Int. Double Noise Encl. Bridge F1B2	46	16-Jan-18	13-Mar-18														

Remaining Level of Effort    Remaining Work  
 Actual Level of Effort    Critical Remaining Work  
 Actual Work    Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Dec.2017 to 19.Mar.2018)**













Activity ID	Activity Name	Rem Dur	Start	Finish	2018																	
					January					February					March				April			
					21	28	04	11	18	25	04	11	18	25	01	08	15	22	29			
<b>3MRP (Jan 2018 - April 2018)</b>																						
<b>03 - PRELIMINARY WORKS</b>																						
<b>03.3 - Interface Works</b>																						
<b>FEHD Permanent Depot</b>																						
0330-1071	Installation of Post (43Nos) > Facility Area 5 & 10	6	22-Jan-18*	27-Jan-18	Installation of Post (43Nos) > Facility Area 5 & 10																	
0330-1073	Construction of Steel Roof > Facility Area 5 & 10	6	26-Jan-18	01-Feb-18	Construction of Steel Roof > Facility Area 5 & 10																	
0330-1075	Sprinkler System Installation > Facility Area 5 & 10	7	31-Jan-18	07-Feb-18	Sprinkler System Installation > Facility Area 5 & 10																	
0330-1077	T & C of Sprinkler System > Facility Area 5 & 10	6	08-Feb-18	14-Feb-18	T & C of Sprinkler System > Facility Area 5 & 10																	
0330-1081	Installation of Post (73Nos) > Facility Area 6, 8 & 9	9	20-Jan-18	30-Jan-18	Installation of Post (73Nos) > Facility Area 6, 8 & 9																	
<b>10 - SECTION X OF THE WORKS</b>																						
<b>10.3 - Middle Bridge (Bridge F)</b>																						
<b>10.3.2 - Bridge Construction</b>																						
<b>Bridge F3B</b>																						
1032-2562	Bridge F3B - Construct Int. Double Noise Encl. (83m) (stage 2)	21	15-Jan-18 A	13-Feb-18	Bridge F3B - Construct Int. Double Noise Encl. (83m) (stage 2)																	
1032-2563	Bridge F3B - Deck Road Waterproofing, Surfacing & Marking	6	08-Feb-18	14-Feb-18	Bridge F3B - Deck Road Waterproofing, Surfacing & Marking																	
1032-2564	Divert 2 Lane Traffic (Stage 2)	0	15-Feb-18		◆ Divert 2 Lane Traffic (Stage 2)																	
<b>Bridge F1B2</b>																						
1032-3840	Bridge F1B2 - Longitudinal Stitching	27	19-Jan-18 A	01-Mar-18	Bridge F1B2 - Longitudinal Stitching																	
1032-3860	Bridge F1B2 - Southern Parapet	5	14-Dec-17 A	25-Jan-18	Bridge F1B2 - Southern Parapet																	
1032-3880	Bridge F1B2 - Construct Int. Double Noise Encl. Bridge F1B2	30	13-Jan-18 A	27-Feb-18	Bridge F1B2 - Construct Int. Double Noise Encl. Bridge F1B2																	
1032-3900	Bridge F1B2 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking	7	02-Mar-18	09-Mar-18	Bridge F1B2 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking																	
<b>Bridge F1B1</b>																						
1032-1740	Bridge F1B1 - Longitudinal Stitching	0	16-Dec-17 A	17-Jan-18 A	Bridge F1B1 - Longitudinal Stitching																	
1032-1780	Bridge F1B1 - Construct Int. Double Noise Encl. Bridge F1B2	30	16-Jan-18 A	27-Feb-18	Bridge F1B1 - Construct Int. Double Noise Encl. Bridge F1B2																	
1032-1800	Bridge F1B1 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking	7	02-Mar-18	09-Mar-18	Bridge F1B1 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking																	
<b>Bridge F5</b>																						
1032-4040	Cutting of Deck Between Temp. TD & E/B > Pier F5-F8	12	15-Feb-18	03-Mar-18	Cutting of Deck Between Temp. TD & E/B > Pier F5-F8																	
1032-4060	Cutting of Deck Between Temp. TD & E/B > Pier F8-F11	12	05-Mar-18	17-Mar-18	Cutting of Deck Between Temp. TD & E/B > Pier F8-F11																	
1032-4080	Cutting of Deck Between Temp. TD & E/B > Pier F11-F14	12	19-Mar-18	03-Apr-18	Cutting of Deck Between Temp. TD & E/B > Pier F11-F14																	
1032-4100	Construction Parapet (Northside) > Pier F5-F8	12	26-Feb-18	10-Mar-18	Construction Parapet (Northside) > Pier F5-F8																	
1032-4120	Construction Parapet (Northside) > Pier F8-F11	12	12-Mar-18	24-Mar-18	Construction Parapet (Northside) > Pier F8-F11																	
1032-4140	Construction Parapet (Northside) > Pier F11-F14	12	26-Mar-18	11-Apr-18	Construction Parapet (Northside) > Pier F11-F14																	
1032-4160	Construct Noise Enclosure (Northside) > Pier F5 - F8	24	12-Mar-18	11-Apr-18	Construct Noise Enclosure (Northside) > Pier F5 - F8																	
<b>All Middle Bridge F (Common)</b>																						
1032-4240	Fresh Water Main 150DI at Bridge F Deck	52	27-Nov-17 A	24-Mar-18	Fresh Water Main 150DI at Bridge F Deck																	
1032-4260	Bridge F Sign Gantries and Misc. Mounting Structure/Support	25	26-Dec-17 A	21-Feb-18*	Bridge F Sign Gantries and Misc. Mounting Structure/Support																	
1032-4356	Sign Gantry (DS06B,DS06A & FADS06) (Nighth work)	50	22-Feb-18	24-Apr-18	Sign Gantry (DS06B,DS06A & FADS06) (Nighth work)																	

█ Remaining Level of Effort    █ Remaining Work  
█ Actual Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme (20.Jan.2018 to 19.Apr.2018)**

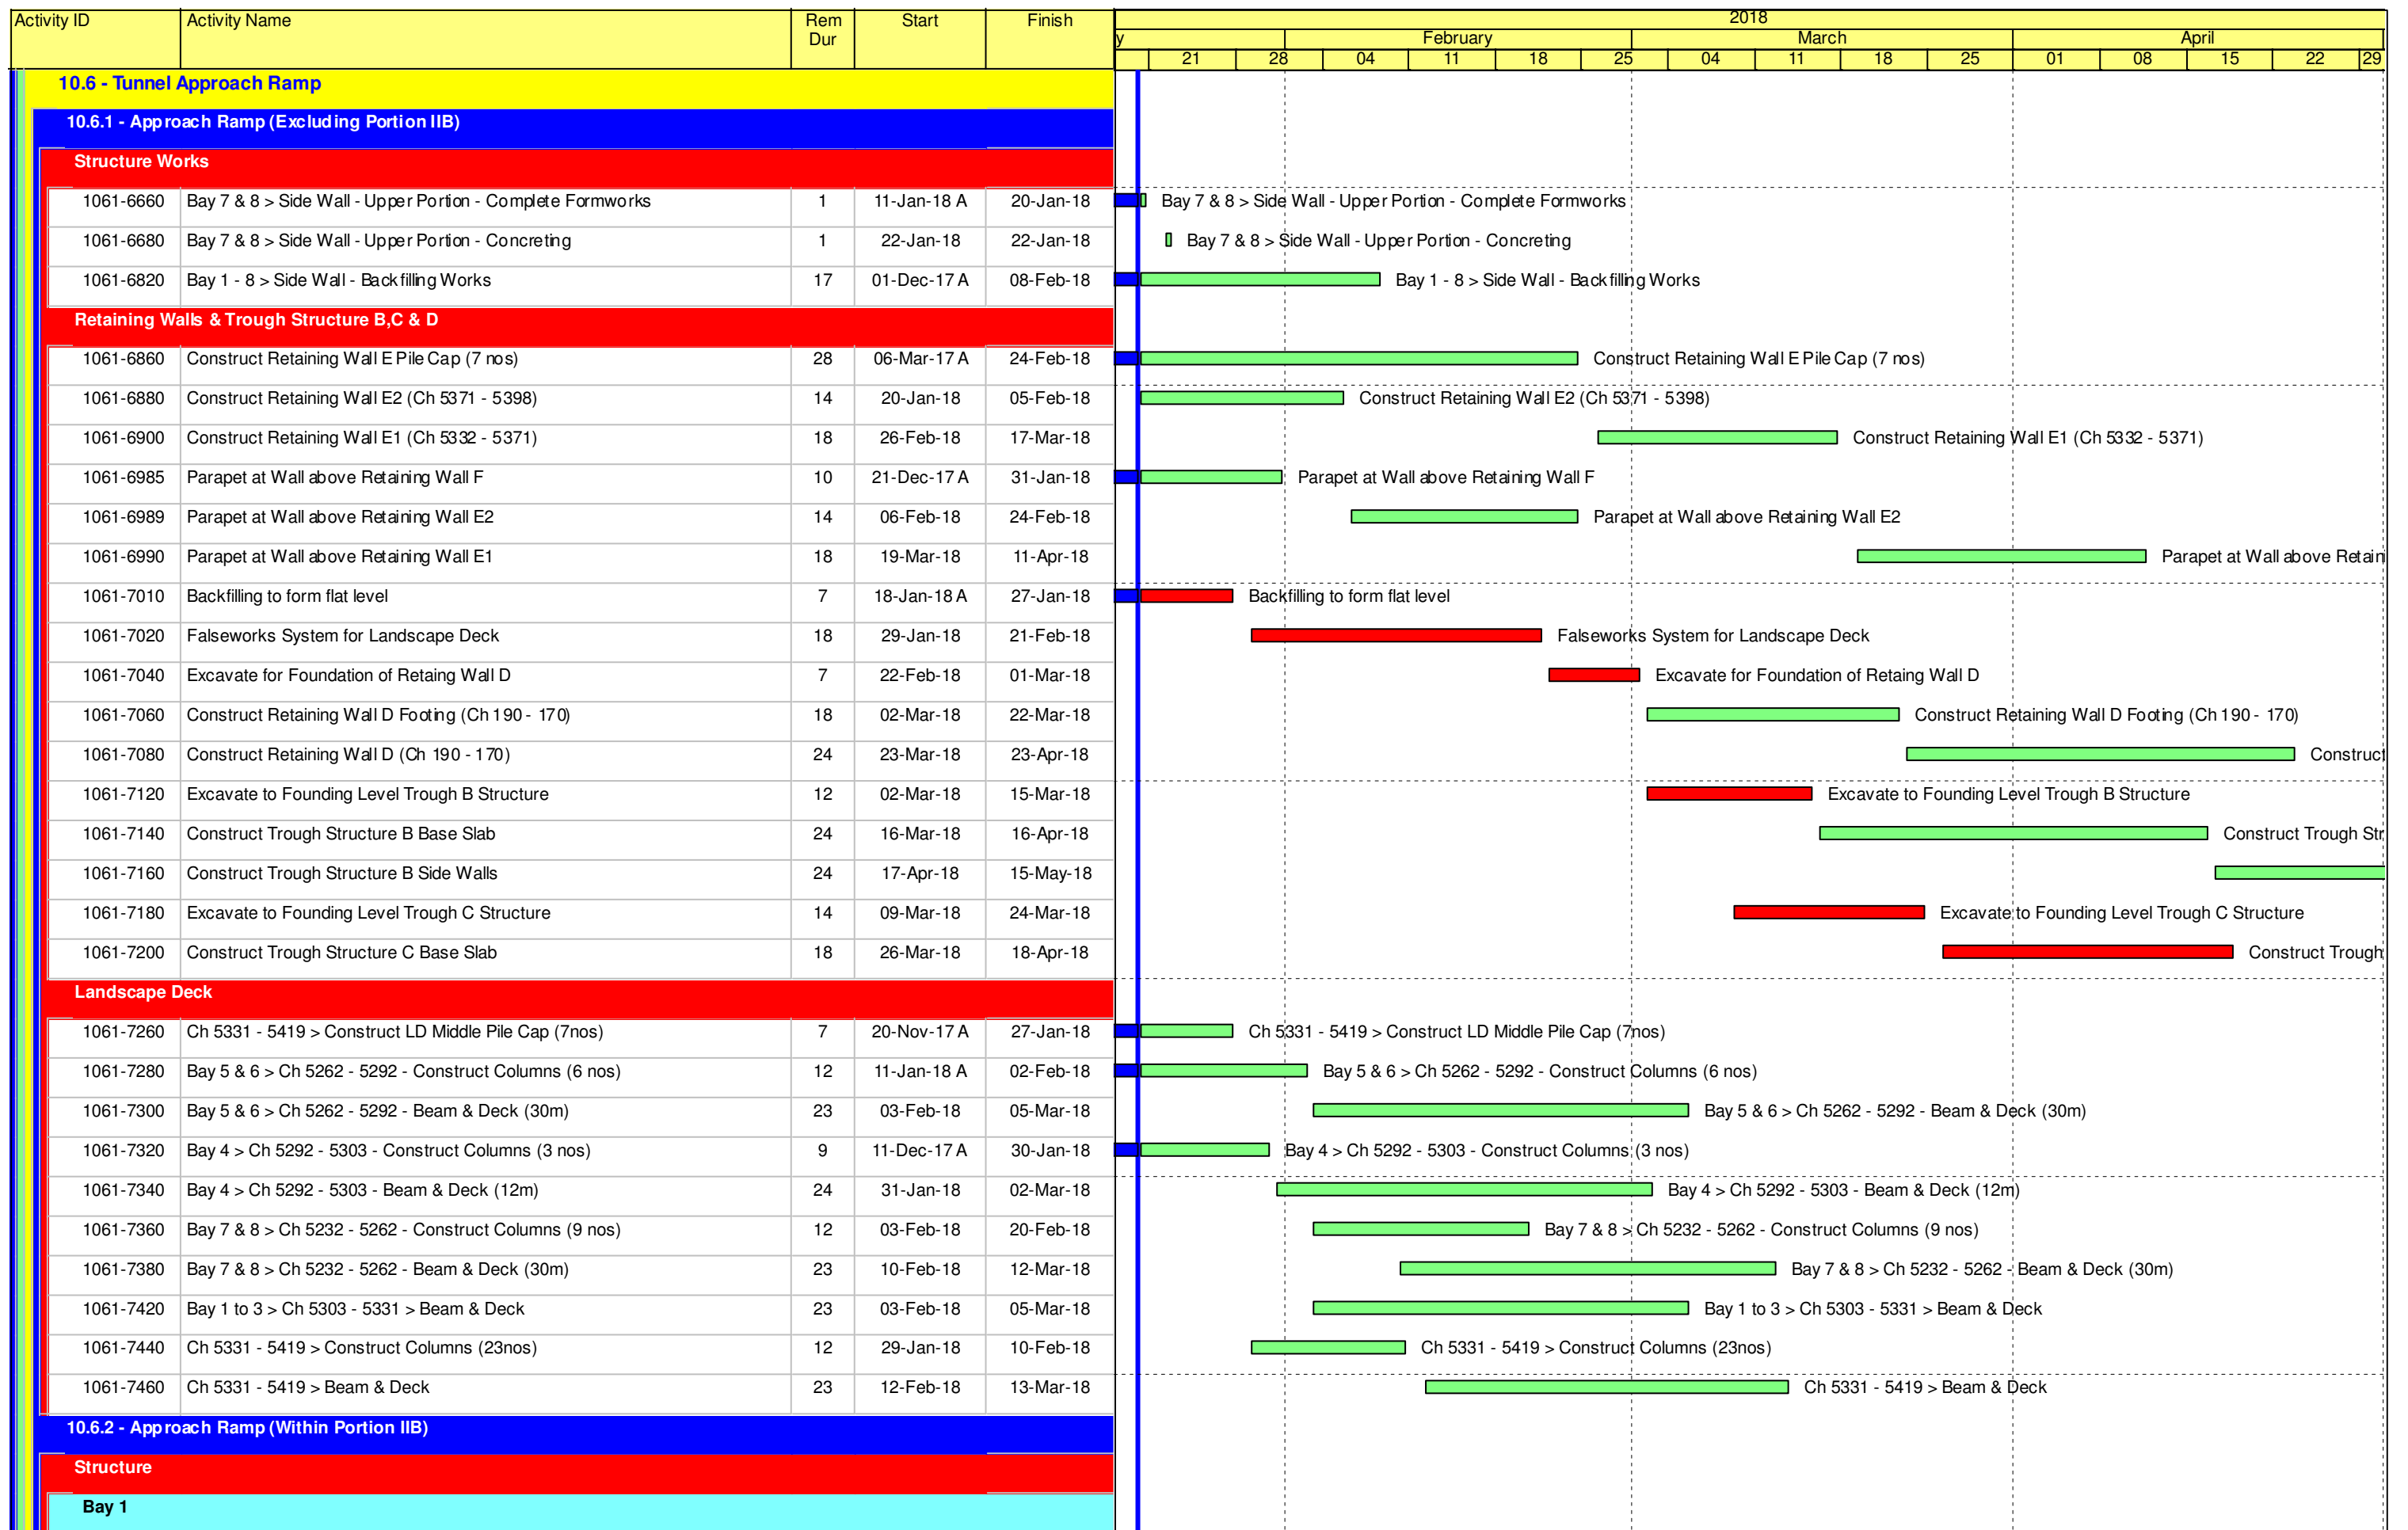









Activity ID	Activity Name	Original Duration	Start	Finish	2018											
					Feb	Mar	Apr	May	Jun							
<b>Elderly Facilities V/039 Received on 22 Jun 2017</b>																
EXW_2270	Facilities fabrication	90d	30-Jan-18 A	15-May-18	Facilities fabrication											
<b>Additional Walkway &amp; Arbour V/040 Received on 22 Aug 2017</b>																
EXW_2300	Arbour confirmation and fabrication	60d	15-Feb-18 A	16-Mar-18	Arbour confirmation and fabrication											
EXW_2310	Associated drainage works for the walkway	20d	17-Mar-18	12-Apr-18	Associated drainage works for the walkway											
<b>Reverting Traffic for IEC,VP Rd &amp; TF St &amp; Seawall Reinstatement (KD9)</b>																
<b>TTA Revert Traffic Back to Original Alignment</b>																
<b>East Bound TTA - IEC East Bound, Victoria Park Road &amp; footpath along Sea Side</b>																
<b>TTM Stage 1 - IEC (East Bound)</b>																
<b>Reinstatement Existing Structure</b>																
EB_1020	Install metal parapet on parapet wall (30m)	6d	28-Feb-18	05-Mar-18	Install metal parapet on parapet wall (30m)											
<b>TTM Stage 2 - Revert Traffic back to Original Victoria Road</b>																
<b>Existing Bridge Parapet Reinstatement</b>																
EB_1180	Install metal parapet on parapet wall (40m)	4d	06-Mar-18	09-Mar-18	Install metal parapet on parapet wall (40m)											
<b>TTM Stage 3 - Reinstatement of Footpath along Seafront</b>																
<b>Reinstatement Works in Traffic Deck Part A</b>																
EB_1540	Break two concrete footings	2d	31-Jan-18 A	16-Mar-18	Break two concrete footings											
EB_1520	Break pipe piles and cut sheet pile	6d	10-Feb-18 A	26-Feb-18 A	Break pipe piles and cut sheet pile											
EB_1530	Backfill Subbase material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)	3d	17-Mar-18	19-Mar-18	Backfill Subbase material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)											
<b>Reinstatement of Existing Gas Main</b>																
EB_1560	Excavation for DN400mm Gas main	3d	20-Mar-18	22-Mar-18	Excavation for DN400mm Gas main											
EB_1570	Laying DN400mm gas main by HKCG at VPR footpath	14d	23-Mar-18	05-Apr-18	Laying DN400mm gas main by HKCG at VPR footpath											
<b>West Bound - IEC West Bound &amp; Tsing fung Street</b>																
<b>TTM Stage 2 - Revert Traffic back to Original Tsing Fung Street</b>																
<b>Existing Bridge Parapet Reinstatement</b>																
IECW_1140	Install metal parapet on parapet wall (60m)	5d	28-Feb-18	04-Mar-18	Install metal parapet on parapet wall (60m)											
<b>TTM Stage 3 - Reinstatement of Victoria Park</b>																
<b>Reinstatement Works in Traffic Deck</b>																
IECW_1390	Cut pipe piles and sheet pile	5d	18-Jan-18 A	13-Mar-18	Cut pipe piles and sheet pile											
IECW_1400	Backfill General Fill Material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)	3d	14-Mar-18	16-Mar-18	Backfill General Fill Material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)											
<b>Reinstatement Works inside Victoria Park</b>																
IECW_1440	Reinstatement of Boundary Fence	21d	29-Jan-18 A	17-Mar-18	Reinstatement of Boundary Fence											
IECW_1460	Cutting sheet pile to 1.5m below finish slope profile (MS 169B)	10d	19-Mar-18	28-Mar-18	Cutting sheet pile to 1.5m below finish slope profile (MS 169B)											
IECW_1470	Slope Reinstatement of Victoria Park	21d	26-Mar-18	23-Apr-18	Slope Reinstatement of Victoria Park											
<b>Completion of Minor Outstanding / Remaining Works for KD9</b>																
<b>West Bound - Completion of Minor Outstanding / Remaining Works for KD9</b>																
<b>Minor Reinstatement Works for Tsing Fung Street</b>																
IECW_1530	Laying Public Lighting duct	6d	18-Mar-18	23-Mar-18	Laying Public Lighting duct											
IECW_1540	Installation of public lighting post and connection by HyD	7d	24-Mar-18	30-Mar-18	Installation of public lighting post and connection by HyD											
IECW_1550	Well compact road formation level and subbase for SRT	6d	24-Mar-18	29-Mar-18	Well compact road formation level and subbase for SRT											
<b>Minor Reinstatement Works in IEC West Bound</b>																
IECW_1600	Replacement of new movement joint at IEC W/B (Sun midnight only)	8d	28-Feb-18	07-Mar-18	Replacement of new movement joint at IEC W/B (Sun midnight only)											
IECW_1630	Repairing of 300 dia. concrete pipeline by lining under slow lane of IEC W/B	2d	28-Feb-18*	01-Mar-18	Repairing of 300 dia. concrete pipeline by lining under slow lane of IEC W/B											
IECW_1610	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)	59d	08-Mar-18	05-May-18	Repairing of extg conc deck surface after milling of ten											

Activity ID	Activity Name	Original Duration	Start	Finish	2018					
					Feb	Mar	Apr	May	Jun	
<b>Works in Victoria Park (KD4, KD5, KD9)</b>										
<b>Re-Provisioning Works</b>										
<b>Nursery Compound</b>										
<b>Nursery compound</b>										
<b>ABWF</b>										
<b>Finishes &amp; Waterproofing</b>										
VP_NC_1500	External wall tile cleaning	3d	23-Oct-17 A	20-Mar-18	External wall tile cleaning					
VP_NC_1420	Painting to wall & ceiling in general (final coat)	4d	15-Mar-18*	19-Mar-18	Painting to wall & ceiling in general (final coat)					
<b>Switch room Cut-out Frame &amp; Chequer Plate</b>										
VP_NC_1690	Installation	1d	13-Feb-18 A	14-Feb-18 A	Installation					
<b>Signage</b>										
VP_NC_1720	Installation	7d	21-Feb-18 A	28-Feb-18 A	Installation					
<b>Metal Fence</b>										
VP_NC_1820	Installation	30d	15-Jan-18 A	29-Mar-18	Installation					
<b>E&amp;M</b>										
VP_NC_1890	Form WR1 submission	7d	09-Feb-18 A	13-Feb-18 A	Form WR1 submission					
VP_NC_1900	Expected power on date	7d	14-Feb-18 A	14-Feb-18 A	Expected power on date					
<b>Fire Services</b>										
VP_NC_1960	Pump and water pipe installation	10d	22-Dec-17 A	10-Mar-18	Pump and water pipe installation					
VP_NC_1980	Hose Reel installation, Breakglass and Alarm	3d	10-Feb-18 A	13-Feb-18 A	Hose Reel installation, Breakglass and Alarm					
VP_NC_1930	FS pipe connection from u/g to water meter room	2d	24-Feb-18 A	28-Feb-18 A	FS pipe connection from u/g to water meter room					
<b>Plumbing and Flushing Water Supplies</b>										
VP_NC_2080	Cleaning of potable water pipe and sampling to WSD	7d	17-Feb-18 A	26-Feb-18 A	Cleaning of potable water pipe and sampling to WSD					
VP_NC_2100	WSD Inspection	14d	28-Feb-18	15-Mar-18	WSD Inspection					
<b>GRP Water Tank Installation</b>										
VP_NC_2130	Final As-fitted drawing submission to WSD	7d	30-Jan-18 A	06-Feb-18 A	Final drawing submission to WSD					
<b>External Works Aside Nursery Compound</b>										
<b>Drainage</b>										
VP_NC_2150	U channel at toilet	2d	30-Jan-18 A	31-Jan-18 A	U channel					
VP_NC_2190	SS angle to shower room u channel	1d	31-Jan-18 A	31-Jan-18 A	SS angle to shower room u channel					
VP_NC_2140	Drainage work at External area	15d	28-Feb-18	16-Mar-18	Drainage work at External area					
<b>Water Works</b>										
VP_NC_2220	FS Fresh & Salt Water, Fresh Water and Irrigation System	15d	07-Feb-18 A	27-Feb-18 A	FS Fresh & Salt Water, Fresh Water and Irrigation System					
<b>External Works Around Nursery Compound</b>										
VP_NC_2250	Reinstatement of Existing Boundary Fence Wall Around Nursery Compound	45d	28-Feb-18	24-Apr-18	Reinstatement of Existing Boundary Fence Wall Around Nursery Compound					
<b>KD10 - Preservation and Protection of Trees</b>										
PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	21-Jun-18	Preservation and Protection of Existing Trees					
<b>KD15 &amp; KD8 - Mooring Components Upkeep (CBTS and ATS)</b>										
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	28-Feb-18	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS					

Data Date: 20-Nov-17

# HY/2009/18 Central - Wan Chai Bypass (Central Interchange)

TASK filters: 3 Months\_1, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017				2018					
						Nov		Dec		Jan		Feb			
						1	2	1	2	1	2	1	2		
<b>Update 2017-11-20 CWB - Central Interchange (2014-06-20) Revised DWP R7</b>															
<b>PRELIMINARIES</b>															
<b>Access Dates &amp; Milestones</b>															
<b>Commencement &amp; Completion</b>															
1010	Contract DLP and Establishment Works for Landscape Completion	0		20-Nov-17*	-294										
1005	Contract Construction Completion	0		20-Nov-17*	-659										
<b>SECTION 7, 7A, 7B &amp; 7C - LANDSCAPE ESTABLISHMENT</b>															
4030	EST - Portion V Landscape Establishment	365	12-Jan-17 A	11-Jan-18	-800	[Red bar from Nov 12 to Dec 11]									
<b>SECTION 8 - PRESERVATION &amp; PROTECTION OF TREES</b>															
4100	Tree - Preservation & Protection of Existing Trees	1759	14-Dec-10 A	20-Nov-17	-659	[Green bar from Dec 14 to Nov 20]									
<b>Key Dates for Completion of Sections</b>															
<b>Anticipated Completion</b>															
1094	KD12 - Anticipated Completion	0		20-Nov-17*	-747										
1114	KD10 - Anticipated Completion	0		20-Nov-17*	-659										
1124	KD11 - Anticipated Completion	0		20-Nov-17*	-652										
1139	KD16 - Anticipated Completion	0		20-Nov-17*	-659										
1104	KD14 - Anticipated Completion	0		11-Jan-18*	-800										
<b>Portion Handover Dates</b>															
<b>Anticipated Handover</b>															
2960a	Portion IIIA Handover - Remaining (KD3 + 28 days) - (EOT 26.5 days added)	0		20-Nov-17*	-962										

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

## Leighton Contractors (Asia) Limited Programme Update 86 (November 2017) THREE MONTH ROLLING

Project ID: U086  
 Baseline: DCP7-2c  
 Layout: Update Three Month Rolling  
 U086  
 Page 1 of 1

Date	Revision	Checked	Appro...
20-Oct-17	U085	AT	PT
20-Nov-17	U086	AT	DG

Data Date: 20-Feb-18

# CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Feb	Mar	Apr	May
<b>Update 2018-02-20 CWB(CC) - Commissioning Contract (SA)</b>									
<b>PRELIMINARIES AND GENERAL REQUIREMENTS</b>									
<b>Salient Key Dates and Milestones</b>									
<b>Contract Key Dates</b>									
KD007	KD7 - Completion of Section 2 of the Works (1437 days) - include EOT (80 days)	0		03-Feb-18 A		▲			
KD008	KD8 - Completion of Section 3 of the Works (1437 days) - include EOT (80 days)	0		03-Feb-18 A		▲			
<b>Anticipated Completion Dates</b>									
KD01	KD1 - Achievement of Stage 1 (1177 days) - include EOT No.3 (123 days)	0		05-Feb-18 A		▲			
KD02	KD2 - Achievement of Stage 2 (1232 days)	0		15-May-18*	-305			▲	◆
KD03	KD3 - Achievement of Stage 3 (1318 days) - include EOT (140 days)	0		15-May-18*	-219		▲		◆
<b>Possession Dates and Vacation Dates</b>									
PO-IIa	Possession of Portion IIa (Day 1) - WVB below +6.5mPD	1329	28-Feb-14 A	20-Mar-18	-269	[Bar chart showing possession period from Feb to Mar]			
PO-III	Possession of Portion III (Day 120) - CH1805-2600	1209	28-Jun-14 A	20-Mar-18	-284	[Bar chart showing possession period from Jun to Mar]			
PO-Ib	Possession of Portion Ib (Day 242) - CH1580-1805	1087	28-Oct-14 A	20-Mar-18	-264	[Bar chart showing possession period from Oct to Mar]			
PO-IXd	Possession of Portion IXd (Day 266) - CH4600-4860	1063	21-Nov-14 A	20-Mar-18	-195	[Bar chart showing possession period from Nov to Mar]			
PO-XI	Possession of Portion XI (Day 296) - EVS	1033	21-Dec-14 A	20-Mar-18	180	[Bar chart showing possession period from Dec to Mar]			
PO-IIc	Possession of Portion IIc (Day 336) - CH1360-1580	993	30-Jan-15 A	20-Mar-18	-269	[Bar chart showing possession period from Jan to Mar]			
PO-IIb	Possession of Portion IIb (Day 336) - WVB above +6.5mPD	669	30-Jan-15 A	20-Mar-18	-269	[Bar chart showing possession period from Jan to Mar]			
PO-IXa	Possession of Portion IXa (Day 392) - CH4860-5150	937	27-Mar-15 A	20-Mar-18	-195	[Bar chart showing possession period from Mar to Mar]			
PO-Va	Possession of Portion V (Day 607) - CH2950-3210	722	28-Oct-15 A	20-Mar-18	-284	[Bar chart showing possession period from Oct to Mar]			
PO-VII_a1	Possession of Portion VII (Day 762) - CH3911-4250 (below -6.0mPD)	659	30-Dec-15 A	20-Mar-18	-203	[Bar chart showing possession period from Dec to Mar]			
PO-Vc	Possession of Portion V (Day 607) - CH3210-3250	658	15-Jan-16 A	20-Mar-18	-265	[Bar chart showing possession period from Jan to Mar]			
PO-VIb_b1	Possession of Portion VIb (Day 761) - CH3428-3625 (E/B)	619	18-Feb-16 A	20-Mar-18	-279	[Bar chart showing possession period from Feb to Mar]			
PO-VIb_b2	Possession of Portion VIb (Day 761) - CH3428-3625 (W/B)	568	29-Feb-16 A	20-Mar-18	-264	[Bar chart showing possession period from Feb to Mar]			

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

## Leighton Contractors (Asia) Limited

### Programme Update 48 (February 2018)

#### THREE MONTH ROLLING

Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 1 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW



Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Feb	Mar	Apr	May
PO-Xa_1	Possession of Portion Xa (Day 650) - ADB Southern Portion (AECOM letter ref: 2015007890T)	589	07-Mar-16 A	20-Mar-18	-323				
PO-Xb_1	Possession of Portion Xb (Day 804) - ADB Northern Portion	589	07-Mar-16 A	20-Mar-18	-323				
PO-Vb1	Possession of Portion V (Day 607) - SR3	587	11-Mar-16 A	20-Mar-18	180				
PO-Ia	Possession of Portion Ia (Day 789) - SCB / SCP1 / SCP2 / Rumsey Street Flyover	600	28-Mar-16 A	20-Mar-18	-307				
PO-VII_a2	Possession of Portion VII (Day 762) - CH3800-3911 (below -6.0mPD)	567	31-Mar-16 A	20-Mar-18	-250				
PO-IXc_1	Possession of Portion IXc (Day 712) - EVB above 3.6mPD - Relinquished on 12 Apr 2016	445	29-Jul-16 A	20-Mar-18	-274				
PO-IXb_1	Possession of Portion IXb (Day 712) - EVB (below +3.6mPD to tunnel top slab) - Relinquished on 12 Apr 2016	445	05-Aug-16 A	20-Mar-18	-274				
PO-VIa_a	Possession of Portion VIa (Day 823) - CH3250-3283	425	15-Aug-16 A	20-Mar-18	-269				
PO-Vb2_a	Possession of Portion V (Day 607) - SR2	456	15-Aug-16 A	20-Mar-18	-265				
PO-VIc_a	Possession of Portion VIc (Day 761) - CH3770-3800 (Access Shaft Opening)	391	23-Sep-16 A	20-Mar-18	-264				
PO-VIb_c	Possession of Portion VIb (Day 761) - CH3625-3770	391	23-Sep-16 A	20-Mar-18	-279				
PO-IVa1	Possession of Portion IVa (Day 930) - CH2600-2720	323	30-Nov-16 A	20-Mar-18	-271				
PO-IVb2	Possession of Portion IVb (Day 930) - MVB (GL D-H)	233	28-Feb-17 A	20-Mar-18	-320				
PO-VIIIa_a	Possession of Portion VIIIa (Day 929) - CH4530-4591 W/B	233	28-Feb-17 A	20-Mar-18	-245				
PO-VIIIa	Possession of Portion VIIIa (Day 929) - CH4250-4600 (Remaining)	241	12-Mar-17 A	20-Mar-18	-245				
PO-VIIIb	Possession of Portion VIIIb (Day 929) - SR8 (CH700-350)	233	12-Mar-17 A	20-Mar-18	-192				
PO-VIIIc	Possession of Portion VIIIc (Day 1039) - SR8 (CH350-310) / SCP4	233	12-Mar-17 A	20-Mar-18	-241				
PO-IVa2_a	Possession of Portion IVa (Day 930) - CH2720-2950	241	12-Mar-17 A	20-Mar-18	-267				
PO-IVb1	Possession of Portion IVb (Day 930) - MVB (GL A-C)	239	14-Mar-17 A	20-Mar-18	-320				
PO-IVa2_b	Possession of Portion IVa (Day 930) - SR1	203	30-Mar-17 A	20-Mar-18	-267				
PO-Vb2_b	Possession of Portion V (Day 607) - SCP3	182	03-Jul-17 A	20-Mar-18	-265				
PO-VIb_a	Possession of Portion VIb (Day 761) - CH3400-3428	80	31-Jul-17 A	20-Mar-18	-264				
PO-VIa_b	Possession of Portion VIa (Day 823) - CH3283-3400	80	31-Jul-17 A	20-Mar-18	-284				
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-Feb-18	10-Jun-18	-262				

- Current Milestone
- Level of Effort
- Remaining Work
- Project Baseline
- Baseline Milestone
- Actual Work
- Critical Remaining Work

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 2 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018											
						Feb			Mar			Apr			May		
<b>Submissions and Approvals</b>																	
Initial General Submission																	
10168	Submission of CMC 3DVR	30	20-Mar-18	18-Apr-18	-74												
<b>DETAILED DESIGN OF WORKS</b>																	
<b>Permanent Works Design and Engineering</b>																	
Green Roof on EVB																	
2166	EVB Roof - Engineer review & Approval; Consent to Proceed Construction	24	18-Apr-16 A	06-Mar-18	-279												
Green Wall on ADB																	
10238	ADB Green Wall - Engineer review & Approval; Consent to Proceed Construction	24	07-Mar-16 A	08-Mar-18	-269												
Landscaping & Associated Irrigation System																	
10268	Landscaping - Engineer review & Approval; Consent to Proceed Construction	24	07-Mar-16 A	08-Mar-18	-238												
<b>PROCUREMENT, MANUFACTURING &amp; DELIVERIES</b>																	
<b>Procurement; Manufacturing; Deliveries</b>																	
Green Roof on EVB																	
Shop Drawings																	
12846	EVB Green Roof - Shop Drawings review the Engineer	30	03-Aug-17 A	27-Feb-18	-342												
2230	EVB Green Roof - Obtain Approval for Shop Drawings	0		27-Feb-18	-342												
Procurement & Fabrication																	
2232	EVB Green Roof - Confirm design of embed items	0	07-Mar-18		-349												
2234	EVB Green Roof - Embed fabrication & delivery	30	07-Mar-18	05-Apr-18	-349												
2236	EVB Green Roof - Commence embed installation	0	06-Apr-18		-349												
2238	EVB Green Roof - Green Roof Fabrication & delivery	30	06-Apr-18	05-May-18	-349												
2240	EVB Green Roof - Commence installation	0	06-May-18		-349												
Landscaping and Associated Irrigation System																	

- Current Milestone
- Remaining Work
- Level of Effort
- Project Baseline
- Baseline Milestone
- Actual Work
- Critical Remaining Work

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 3 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

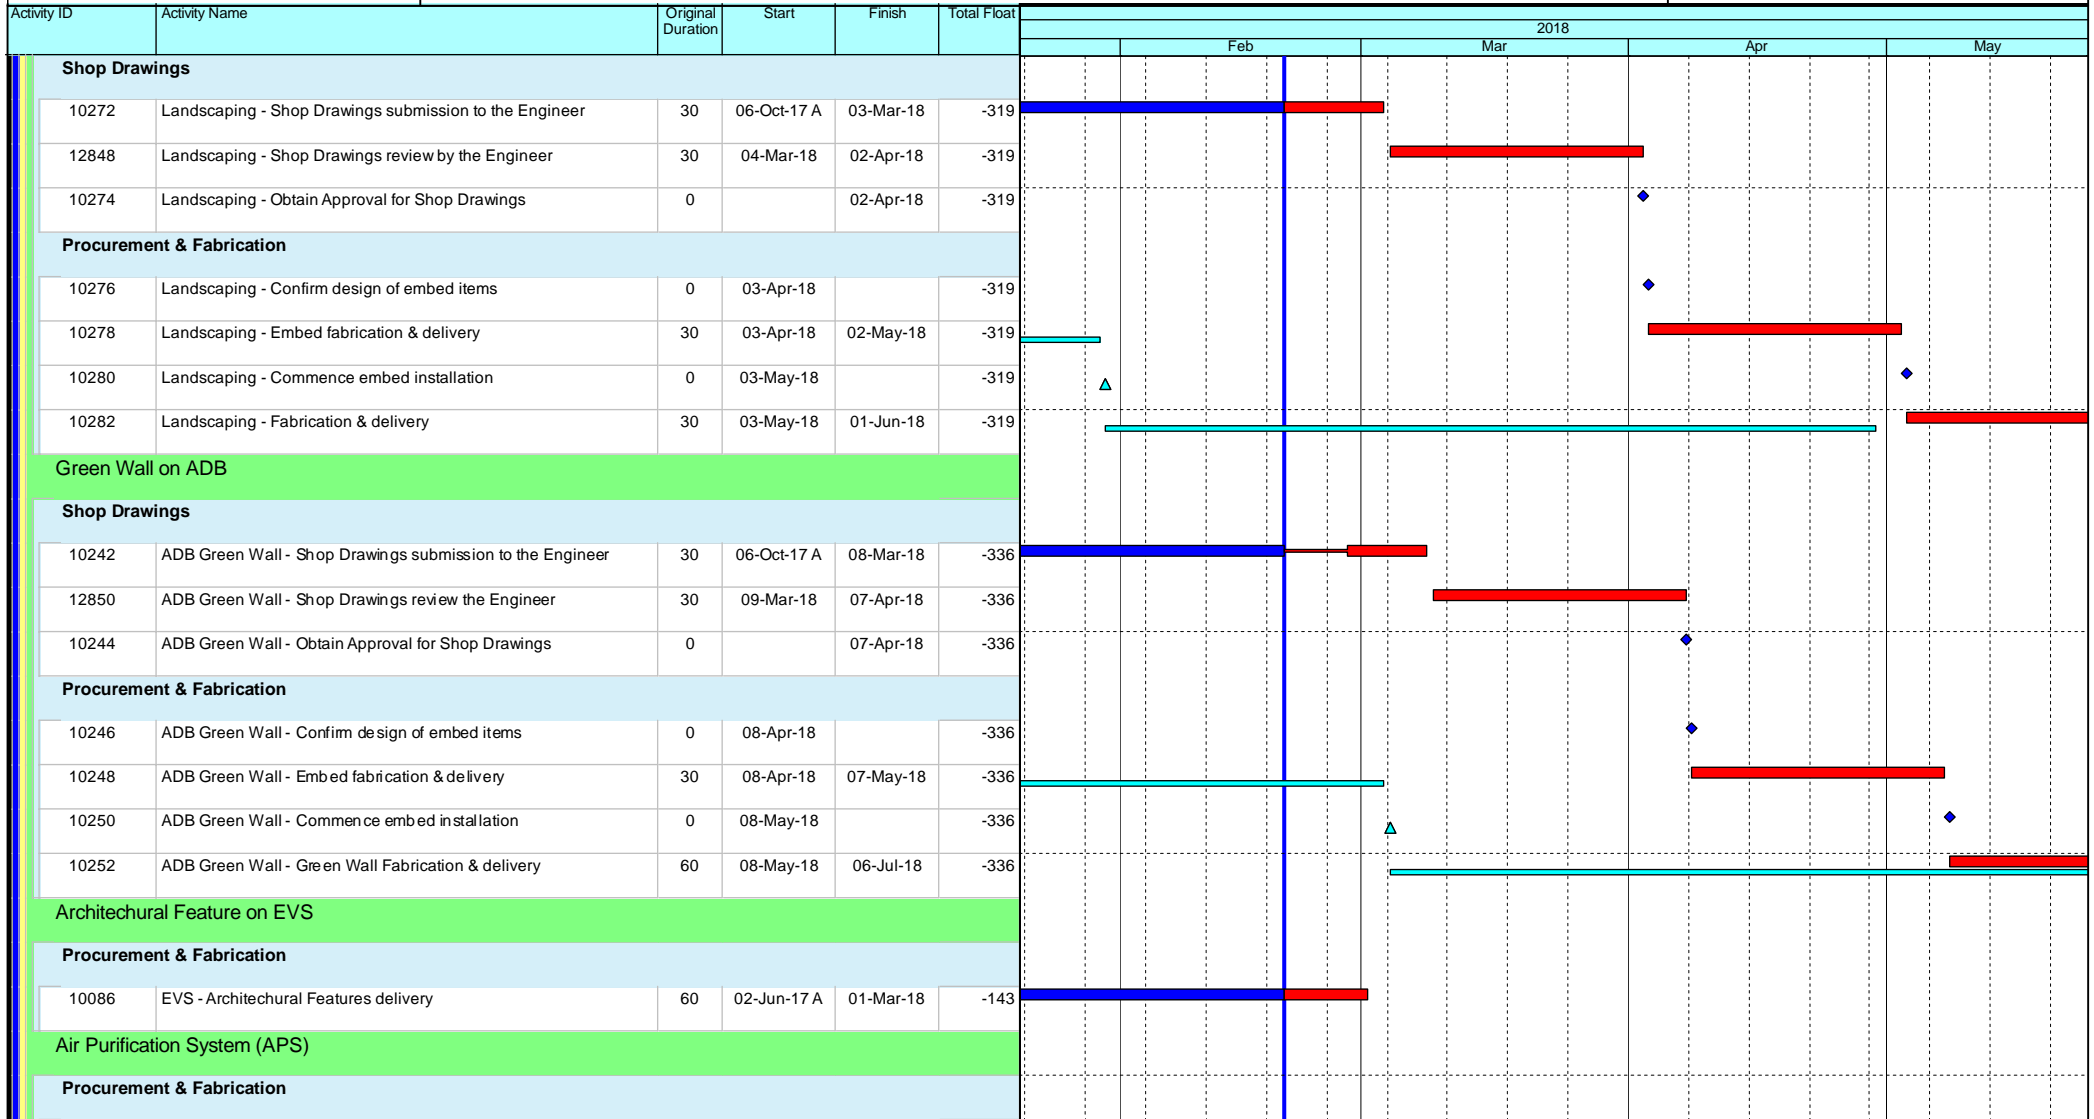

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048  
Baseline: SA01  
Layout: Update Three Month Rolling  
U048  
Page 4 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018											
						Feb			Mar			Apr			May		
13664	APS - Ship to HK Store (3rd Batch)	80	03-Aug-17 A	01-Mar-18	-138												
2368	APS - QA Stored Equipment	6	23-Aug-17 A	01-Mar-18	-138												
<b>CONSTRUCTION</b>																	
<b>West Ventilation Building (WVB - related)</b>																	
Tunnel Section (WVB-related)																	
Portion Ia, IIc [CH840 to CH1360]																	
13086a	Request for VO / instruction for TCSS equipment installation and cabling (Ganty FADS01) (Ref: H2613-LJV-LE-4022)	24	04-Oct-16 A	15-Mar-18	-162												
13086	TCSS cabling and sign face installation (FADS01)	40	16-Mar-18	07-May-18	-162												
<b>Westbound</b>																	
5000	MEP(WB) - (CH840 to CH1360) E&M 1st Fix	29	05-Jun-17 A	01-Mar-18	-134												
5008	MEP(WB) - (CH840 to CH1360) E&M 2nd Fix (include Sump A)	58	12-Jun-17 A	22-Mar-18	-152												
5016	MEP(WB) - (CH840 to CH1360) E&M Final Fix	24	23-Mar-18	24-Apr-18	-152												
5024	MEP(WB) - (CH840 to CH1360) TCSS Field equip & cable installation	18	03-Apr-18	24-Apr-18	-152												
<b>Eastbound</b>																	
6100	MEP(EB) - (CH840 to CH1360) E&M 1st Fix	29	01-Mar-17 A	01-Mar-18	-134												
6102	MEP(EB) - (CH840 to CH1360) E&M 2nd Fix (include Sump A)	58	22-May-17 A	22-Mar-18	-152												
6104	MEP(EB) - (CH840 to CH1360) E&M Final Fix	24	23-Mar-18	24-Apr-18	-152												
6106	MEP(EB) - (CH840 to CH1360) TCSS Field equip & cable installation	18	03-Apr-18	24-Apr-18	-152												
<b>West Ventilation Building (WVB)</b>																	
<b>RC Structures and Metal Roof</b>																	
<b>Metal Roof</b>																	
10454	WVB - Touch up (Steel structure)	12	24-Jan-18 A	05-Feb-18 A													
10456	WVB - Touch up (Roof cladding)	12	23-Feb-18	08-Mar-18	-189												
<b>Metal Roof Eastern Side (M.J. East)</b>																	

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 5 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

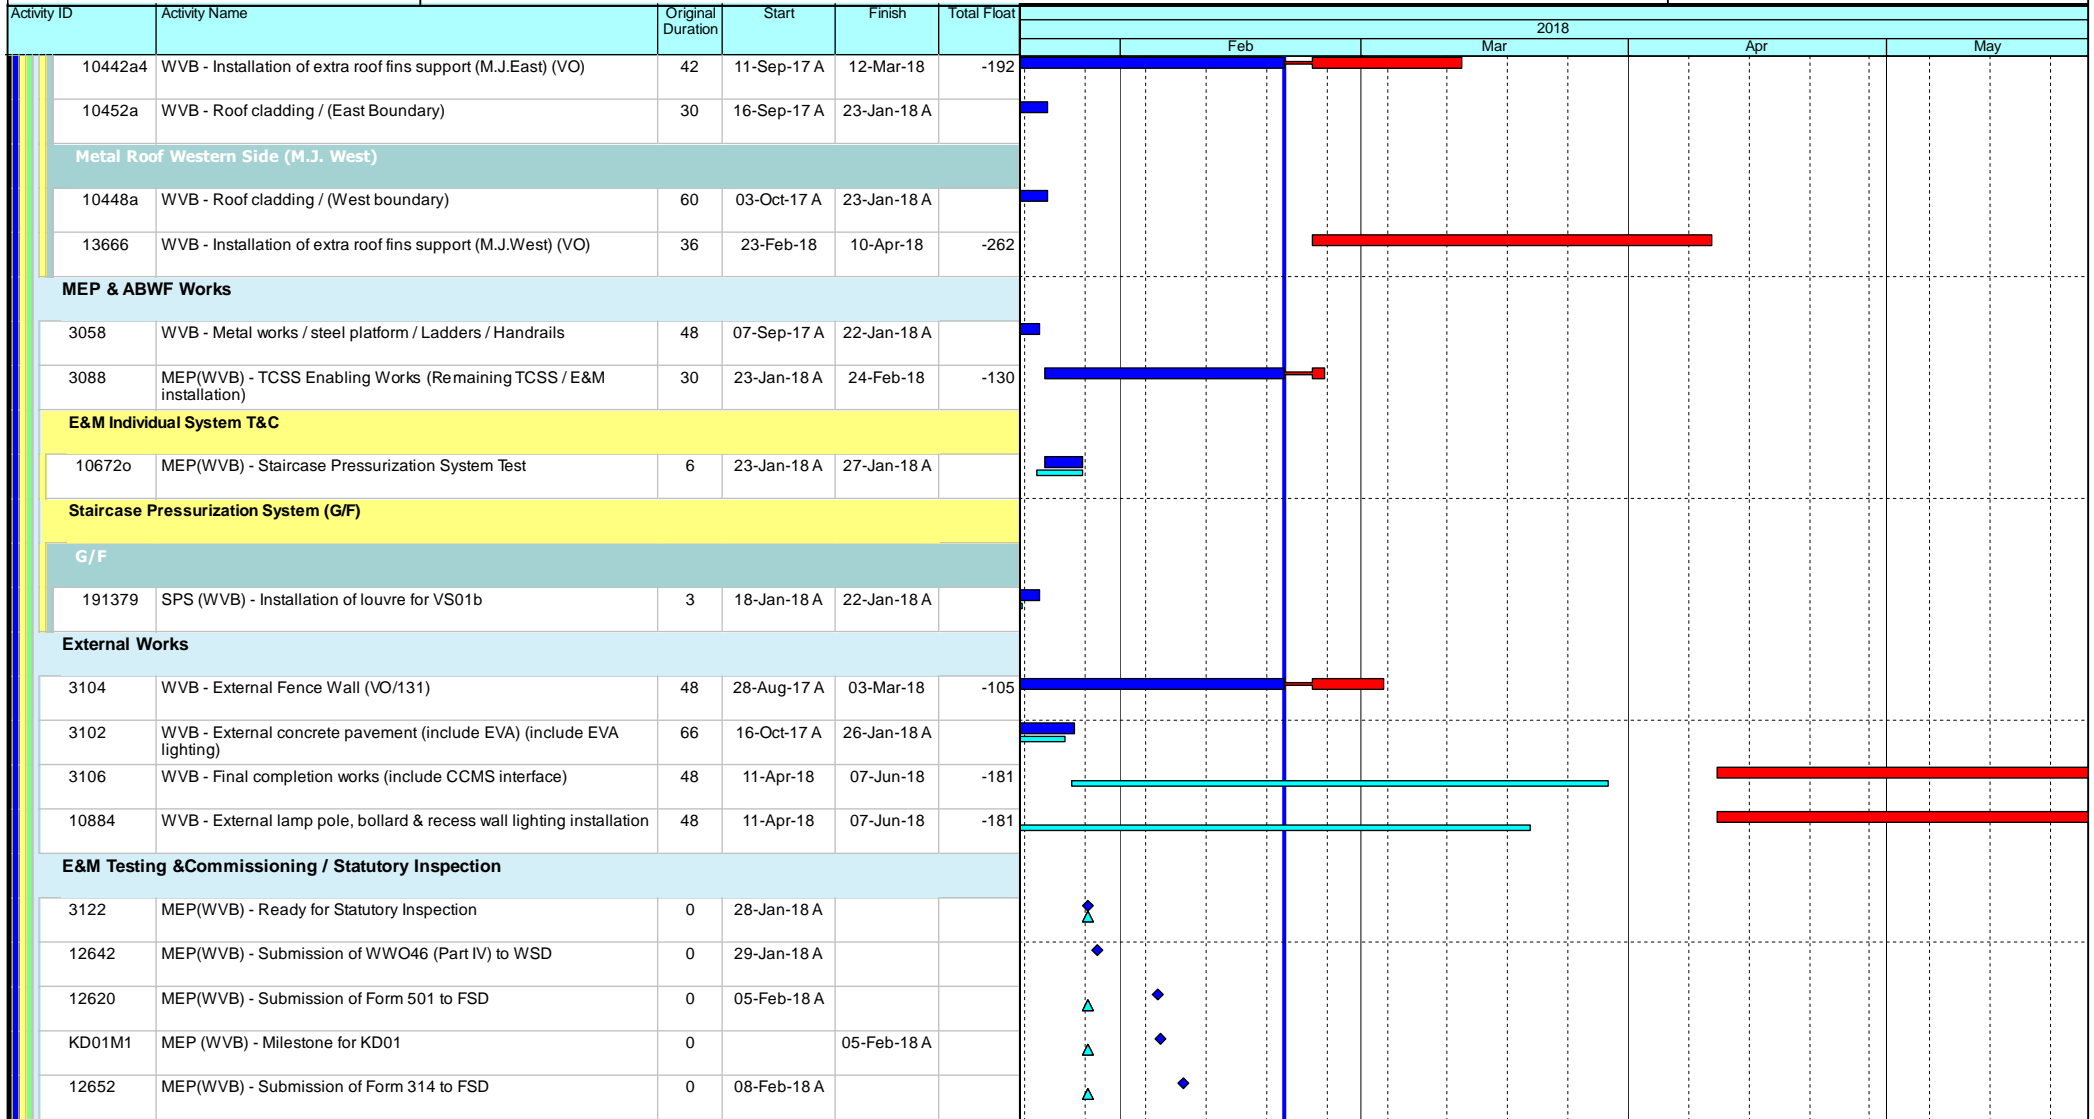

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 6 of 43



Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW



Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

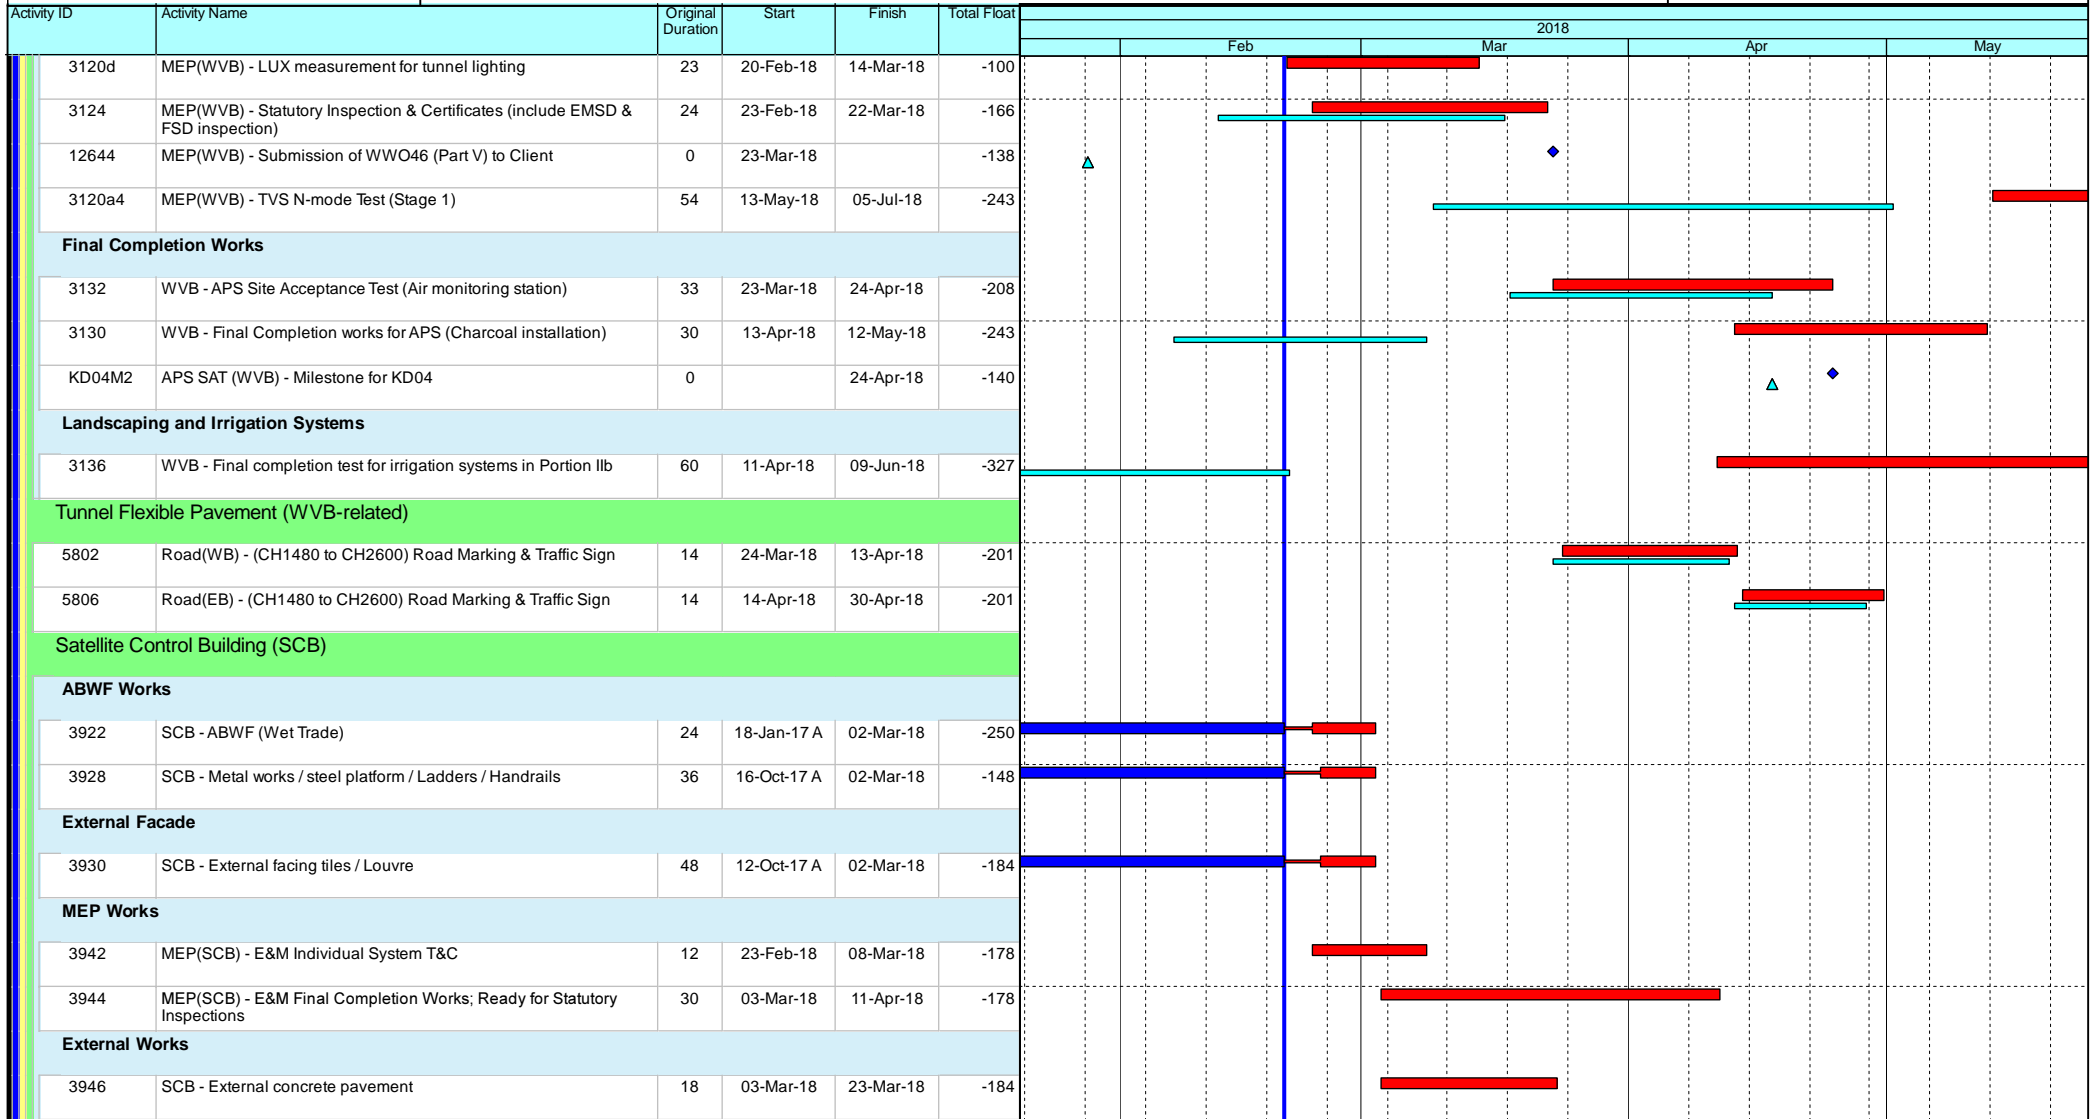

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 7 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW



Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018					
						Feb	Mar	Apr	May		
<b>Slip Road 1</b>											
10020	MEP(SR1) - (CH171 to CH271) E&M 2nd Fix (include Sump B)	30	15-Dec-17 A	01-Mar-18	-203						
10022	MEP(SR1) - (CH171 to CH271) E&M Final Fix	4	02-Mar-18	06-Mar-18	-203						
10046a	MEP(SR1) - (CH171 to CH271) VE Panel installation (Lower part) (1200m2)	13	15-Mar-18	29-Mar-18	-210						
10024	MEP(SR1) - (CH171 to CH271) TCSS Field equip & cable installation	6	17-Mar-18	23-Mar-18	-99						
10046	MEP(SR1) - (CH171 to CH271) VE Panel installation (Upper part) (1200m2)	13	20-Mar-18	07-Apr-18	-214						
<b>Westbound (CH2600 to CH2720)</b>											
9950a1	MEP(WB) - (CH2600 to CH2720) VE Panel installation (Lower part) (1400m2)	9	02-Aug-17 A	24-Feb-18	-206						
5102a	MEP(WB) - (CH2600 to CH2720) E&M 2nd Fix	12	23-Nov-17 A	01-Mar-18	-221						
9950a3	MEP(WB) - (CH2600 to CH2720) VE Panel installation (Upper part) (1750m2)	11	05-Mar-18	16-Mar-18	-223						
5104a	MEP(WB) - (CH2600 to CH2720) E&M Final Fix	6	10-Mar-18	16-Mar-18	-93						
5106a	MEP(WB) - (CH2600 to CH2720) TCSS Field equip & cable installation	6	10-Mar-18	16-Mar-18	-223						
<b>Eastbound (CH2600 to CH2720)</b>											
5120a	MEP(EB) - (CH2600 to CH2720) E&M 2nd Fix	7	04-Dec-17 A	24-Feb-18	-218						
9952a1	MEP(EB) - (CH2600 to CH2720) VE Panel installation (Lower part) (1400m2)	9	26-Feb-18	07-Mar-18	-204						
5122a	MEP(EB) - (CH2600 to CH2720) E&M Final Fix	6	03-Mar-18	09-Mar-18	-217						
5124a	MEP(EB) - (CH2600 to CH2720) TCSS Field equip & cable installation	6	03-Mar-18	09-Mar-18	-223						
9952a3	MEP(EB) - (CH2600 to CH2720) VE Panel installation (Upper part) (1750m2)	11	17-Mar-18	29-Mar-18	-223						
<b>Westbound (CH2720 to CH2950)</b>											
5102b	MEP(WB) - (CH2720 to CH2950) E&M 2nd Fix	12	29-Dec-17 A	28-Feb-18	-211						
9950b	MEP(WB) - (CH2720 to CH2950) VE Panel installation (Lower part) (2247m2)	13	23-Feb-18	09-Mar-18	-206						
9950b1	MEP(WB) - (CH2720 to CH2950) VE Panel installation (Upper part) (2247m2)	13	05-Mar-18	19-Mar-18	-214						
5104b	MEP(WB) - (CH2720 to CH2950) E&M Final Fix	12	06-Mar-18	19-Mar-18	-95						
5106b	MEP(WB) - (CH2720 to CH2950) TCSS Field equip & cable installation	12	06-Mar-18	19-Mar-18	-217						

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 9 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

# CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

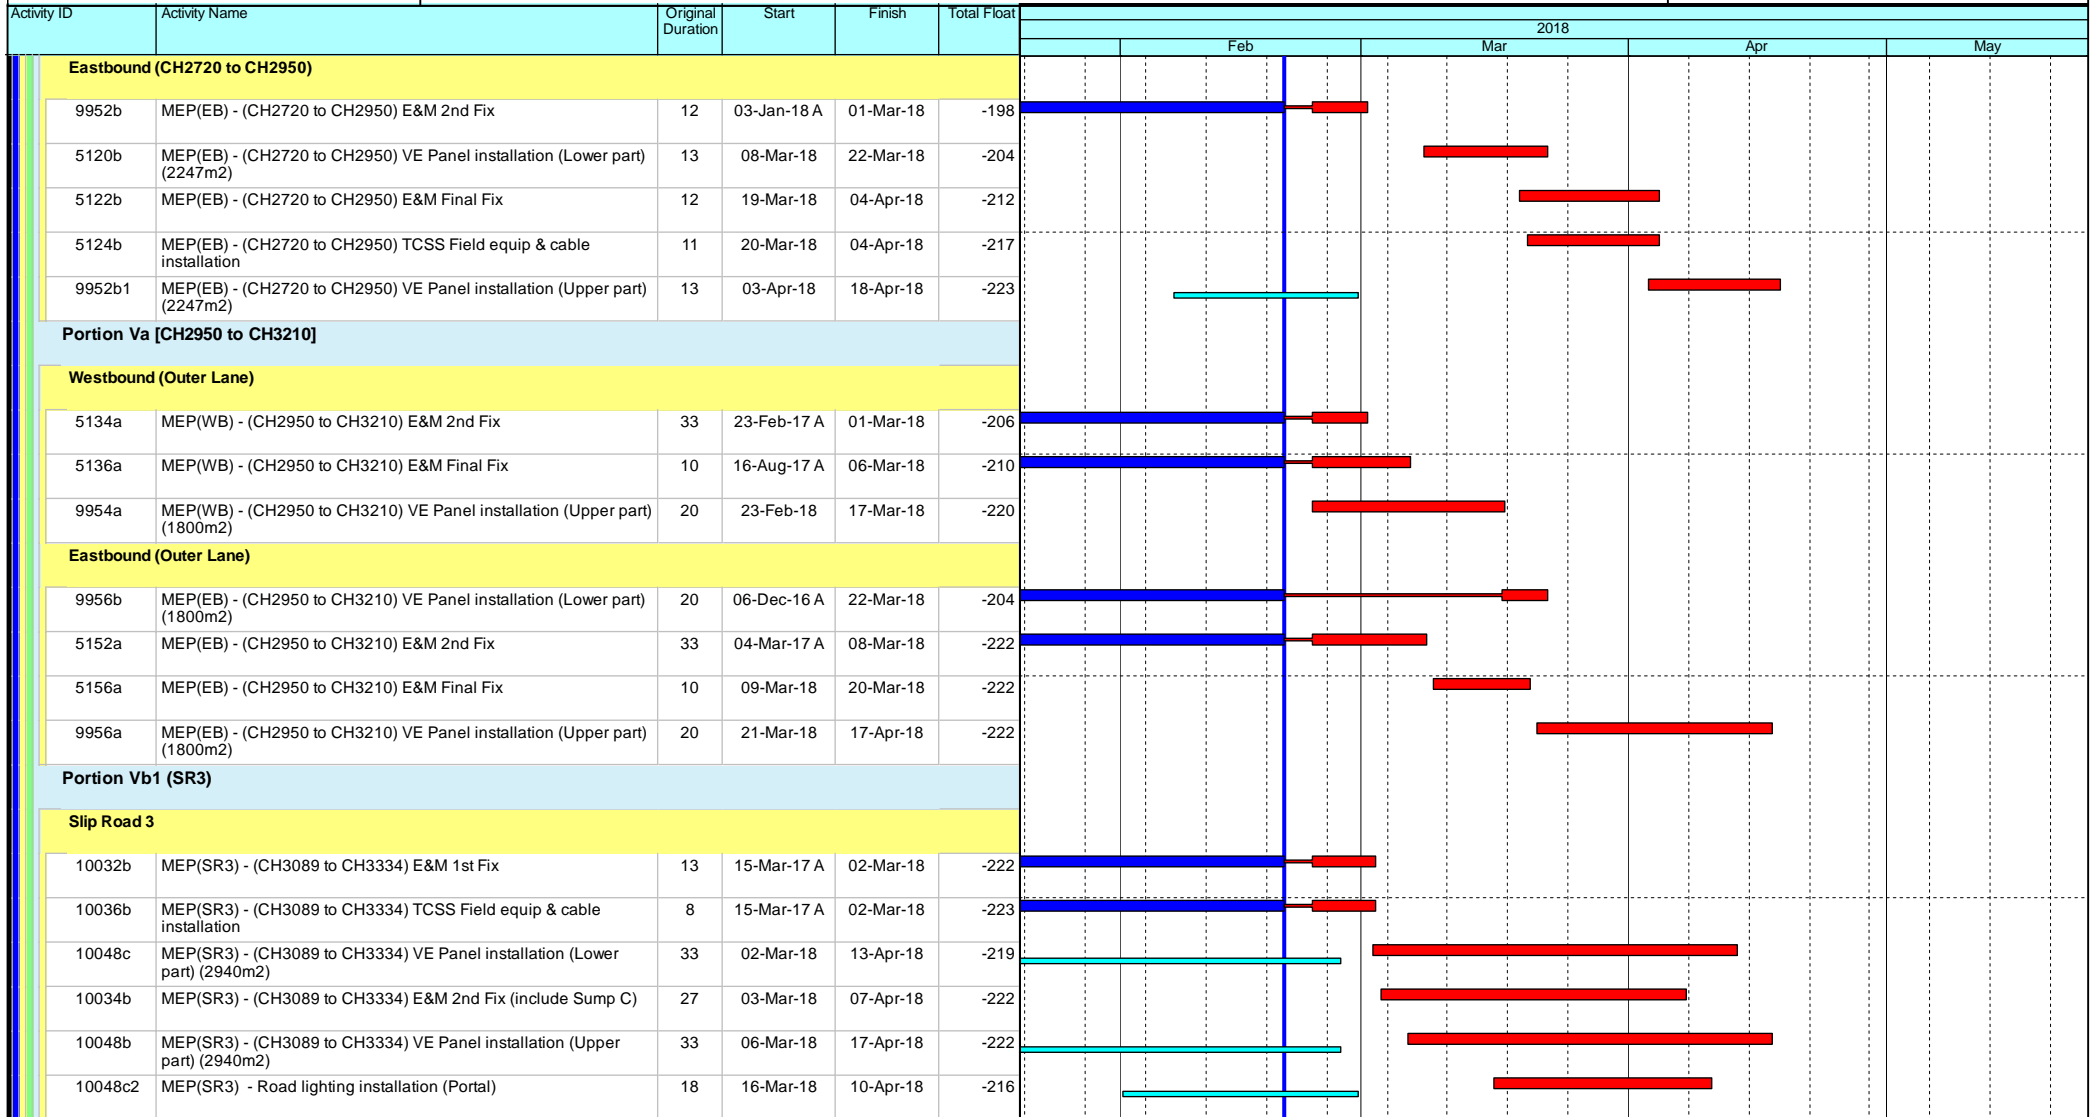

## Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 10 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018				
						Feb	Mar	Apr	May	
10038b	MEP(SR3) - (CH3089 to CH3334) E&M Final Fix	8	09-Apr-18	17-Apr-18	-222					
<b>Portion Vb2 (SR2 / SCP3)</b>										
<b>Slip Road 2</b>										
10050b	MEP(SR2) - (CH3114 to CH3257) E&M 1st Fix	8	08-Mar-17 A	27-Feb-18	-184					
10056b	MEP(SR2) - (CH3114 to CH3257) TCSS Field equip & cable installation	5	16-Mar-17 A	27-Feb-18	-217					
10052b	MEP(SR2) - (CH3114 to CH3257) E&M 2nd Fix (include Sump F)	40	15-Jun-17 A	23-Mar-18	-205					
10064b2	MEP(SR2) - Road lighting installation (Portal)	18	23-Feb-18	15-Mar-18	-216					
10054b	MEP(SR2) -(CH3114 to CH3257) E&M Final Fix	5	24-Mar-18	29-Mar-18	-145					
10064b	MEP(SR2) - (CH3114 to CH3257) VE Panel installation (Upper part) (1716m2)	18	12-Apr-18	03-May-18	-152					
10064c	MEP(SR2) - (CH3114 to CH3257) VE Panel installation (Lower part) (1716m2)	18	12-Apr-18	03-May-18	-152					
<b>Portion Vc [CH3210 to CH3250]</b>										
<b>Westbound (Outer Lane)</b>										
5134c	MEP(WB) - (CH3210 to CH3250) E&M 2nd Fix	18	23-Feb-17 A	05-Mar-18	-199					
5136c	MEP(WB) - (CH3210 to CH3250) E&M Final Fix	10	06-Mar-18	16-Mar-18	-199					
9954c	MEP(WB) - (CH3210 to CH3250) VE Panel installation (Upper part) (1800m2)	20	19-Mar-18	14-Apr-18	-220					
<b>Eastbound (Outer Lane)</b>										
5152c	MEP(EB) - (CH3210 to CH3250) E&M 2nd Fix	18	02-Mar-17 A	05-Mar-18	-199					
5156c	MEP(EB) - (CH3210 to CH3250) E&M Final Fix	10	06-Mar-18	16-Mar-18	-199					
9956c	MEP(EB) - (CH3210 to CH3250) VE Panel installation (Upper part) (1800m2)	20	10-Apr-18	03-May-18	-152					
<b>Portion VIa [CH3250 to CH3283]</b>										
<b>Westbound</b>										
5166a	MEP(WB) - (CH3250 to CH3283) E&M 2nd Fix	6	27-Nov-17 A	27-Feb-18	-217					
9958a1	MEP(WB) - (CH3250 to CH3283) VE Panel installation (Lower part) (528m2)	6	23-Feb-18	01-Mar-18	-219					
5170a	MEP(WB) - (CH3250 to CH3283) TCSS Field equip & cable installation	5	28-Feb-18	05-Mar-18	-217					

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline
- ▲ Baseline Milestone

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 11 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

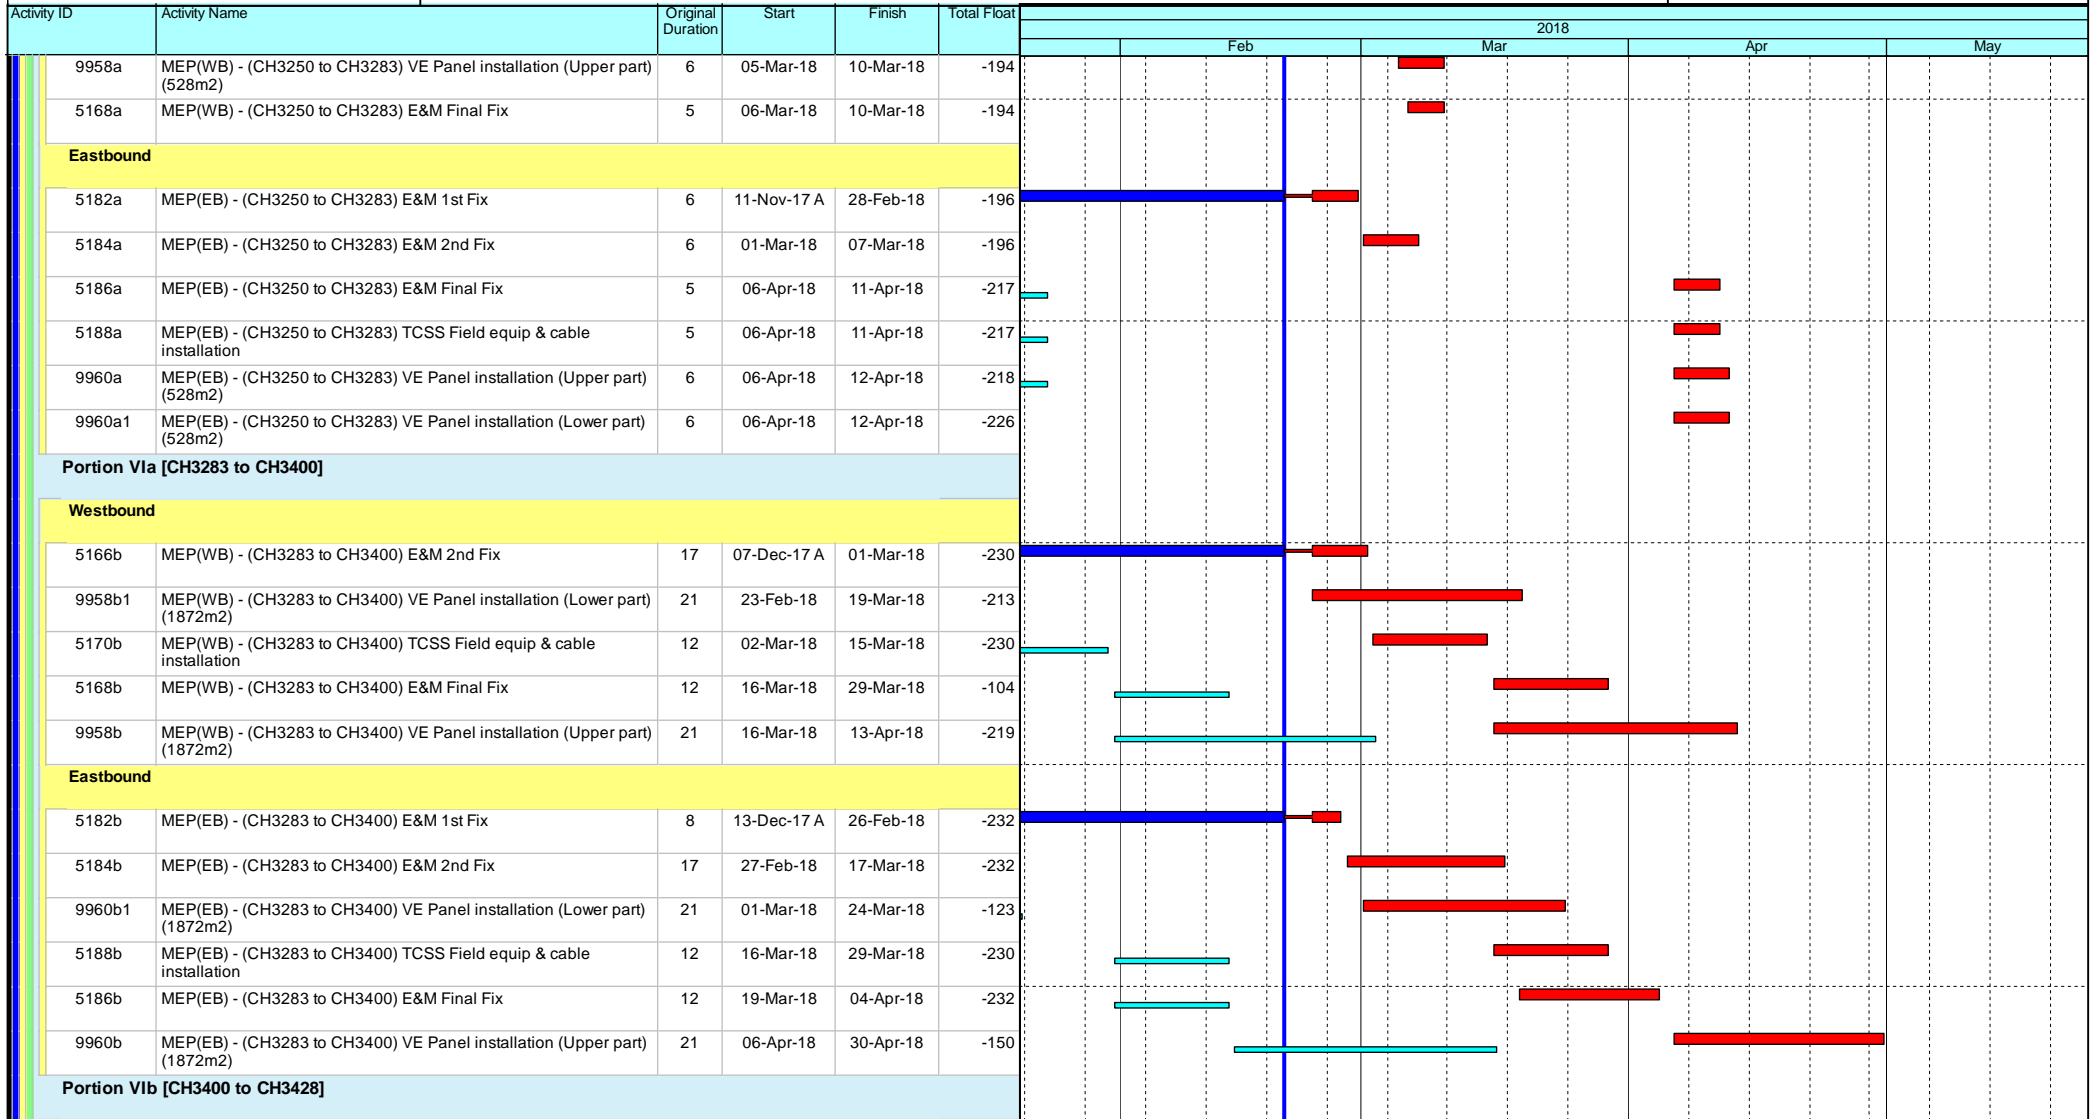

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 12 of 43



Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW



Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

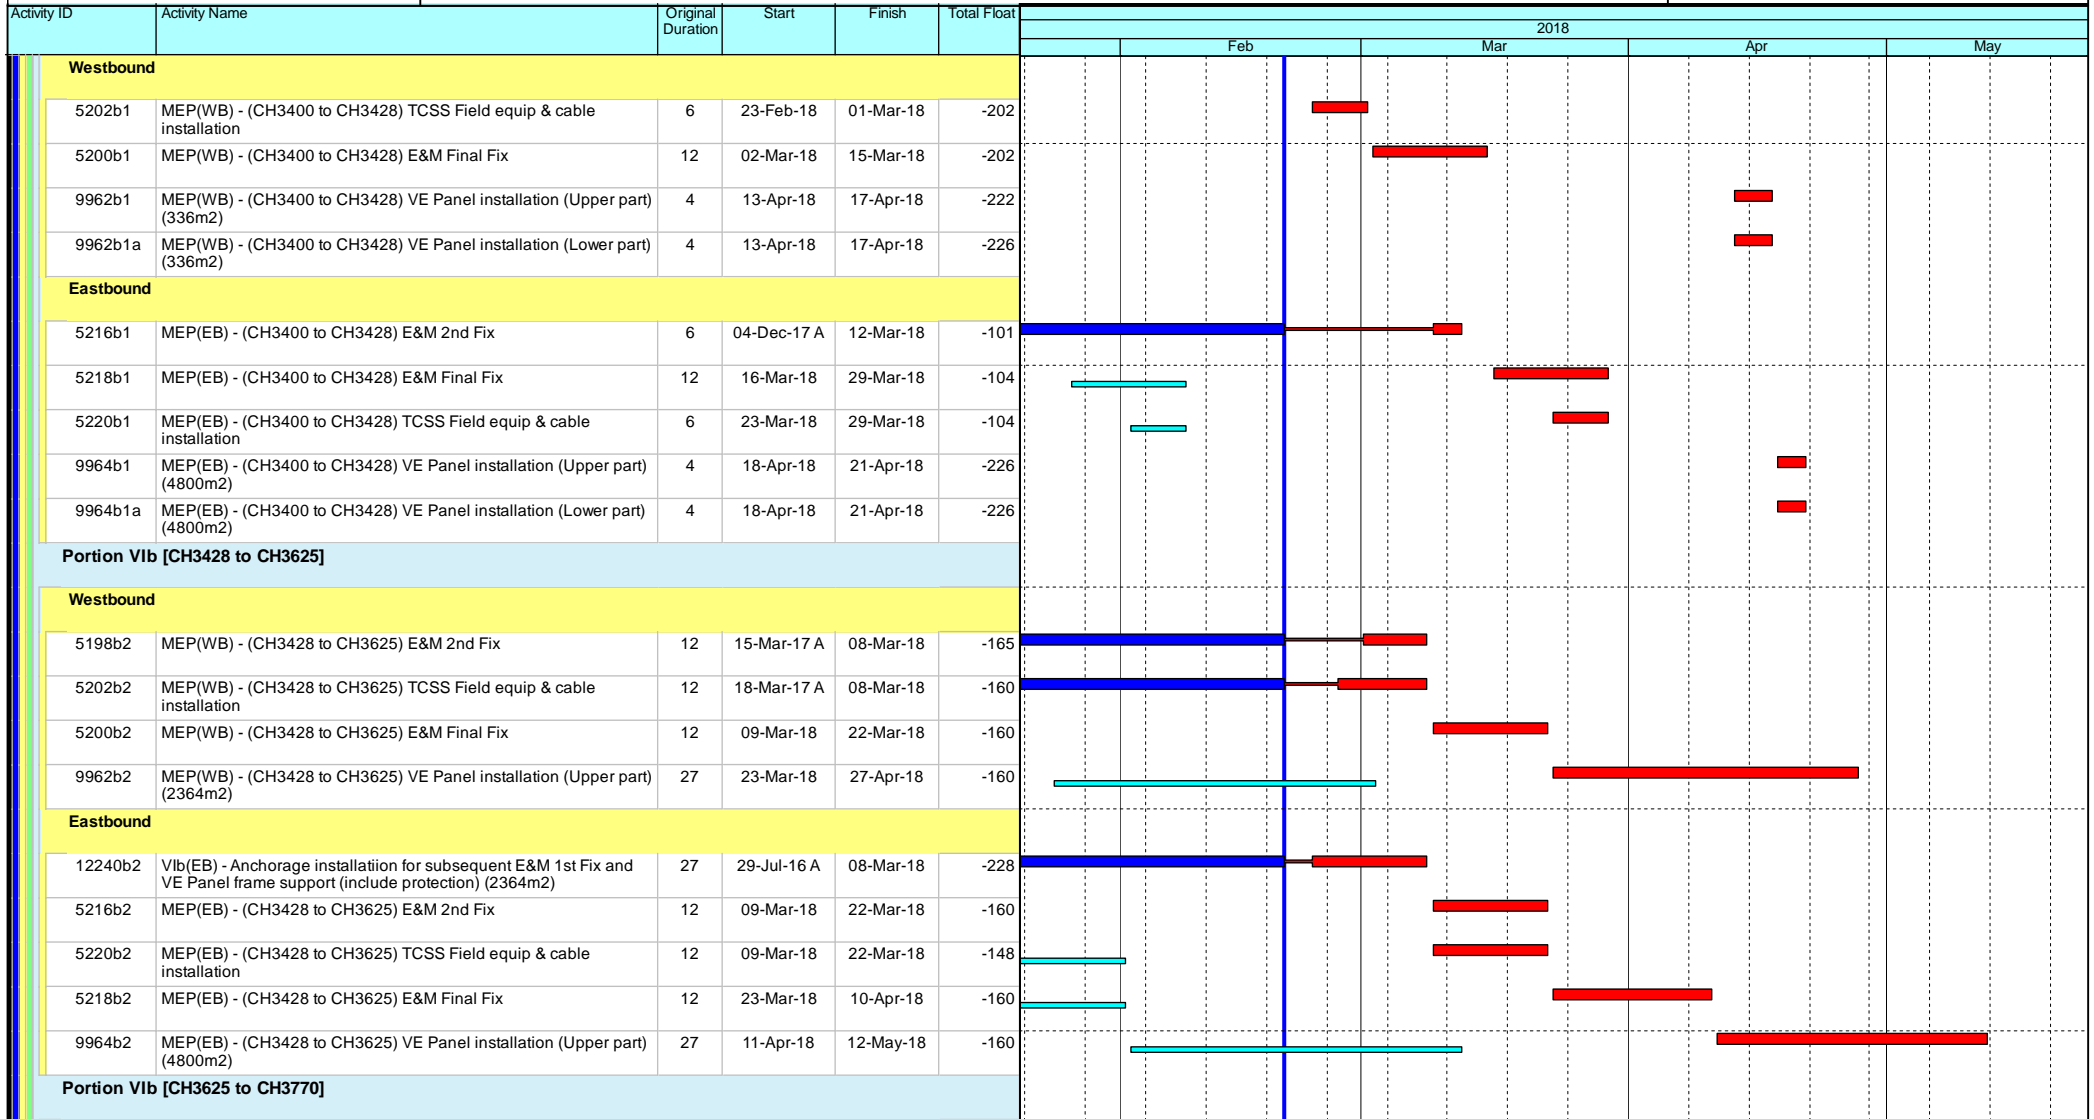

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 13 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

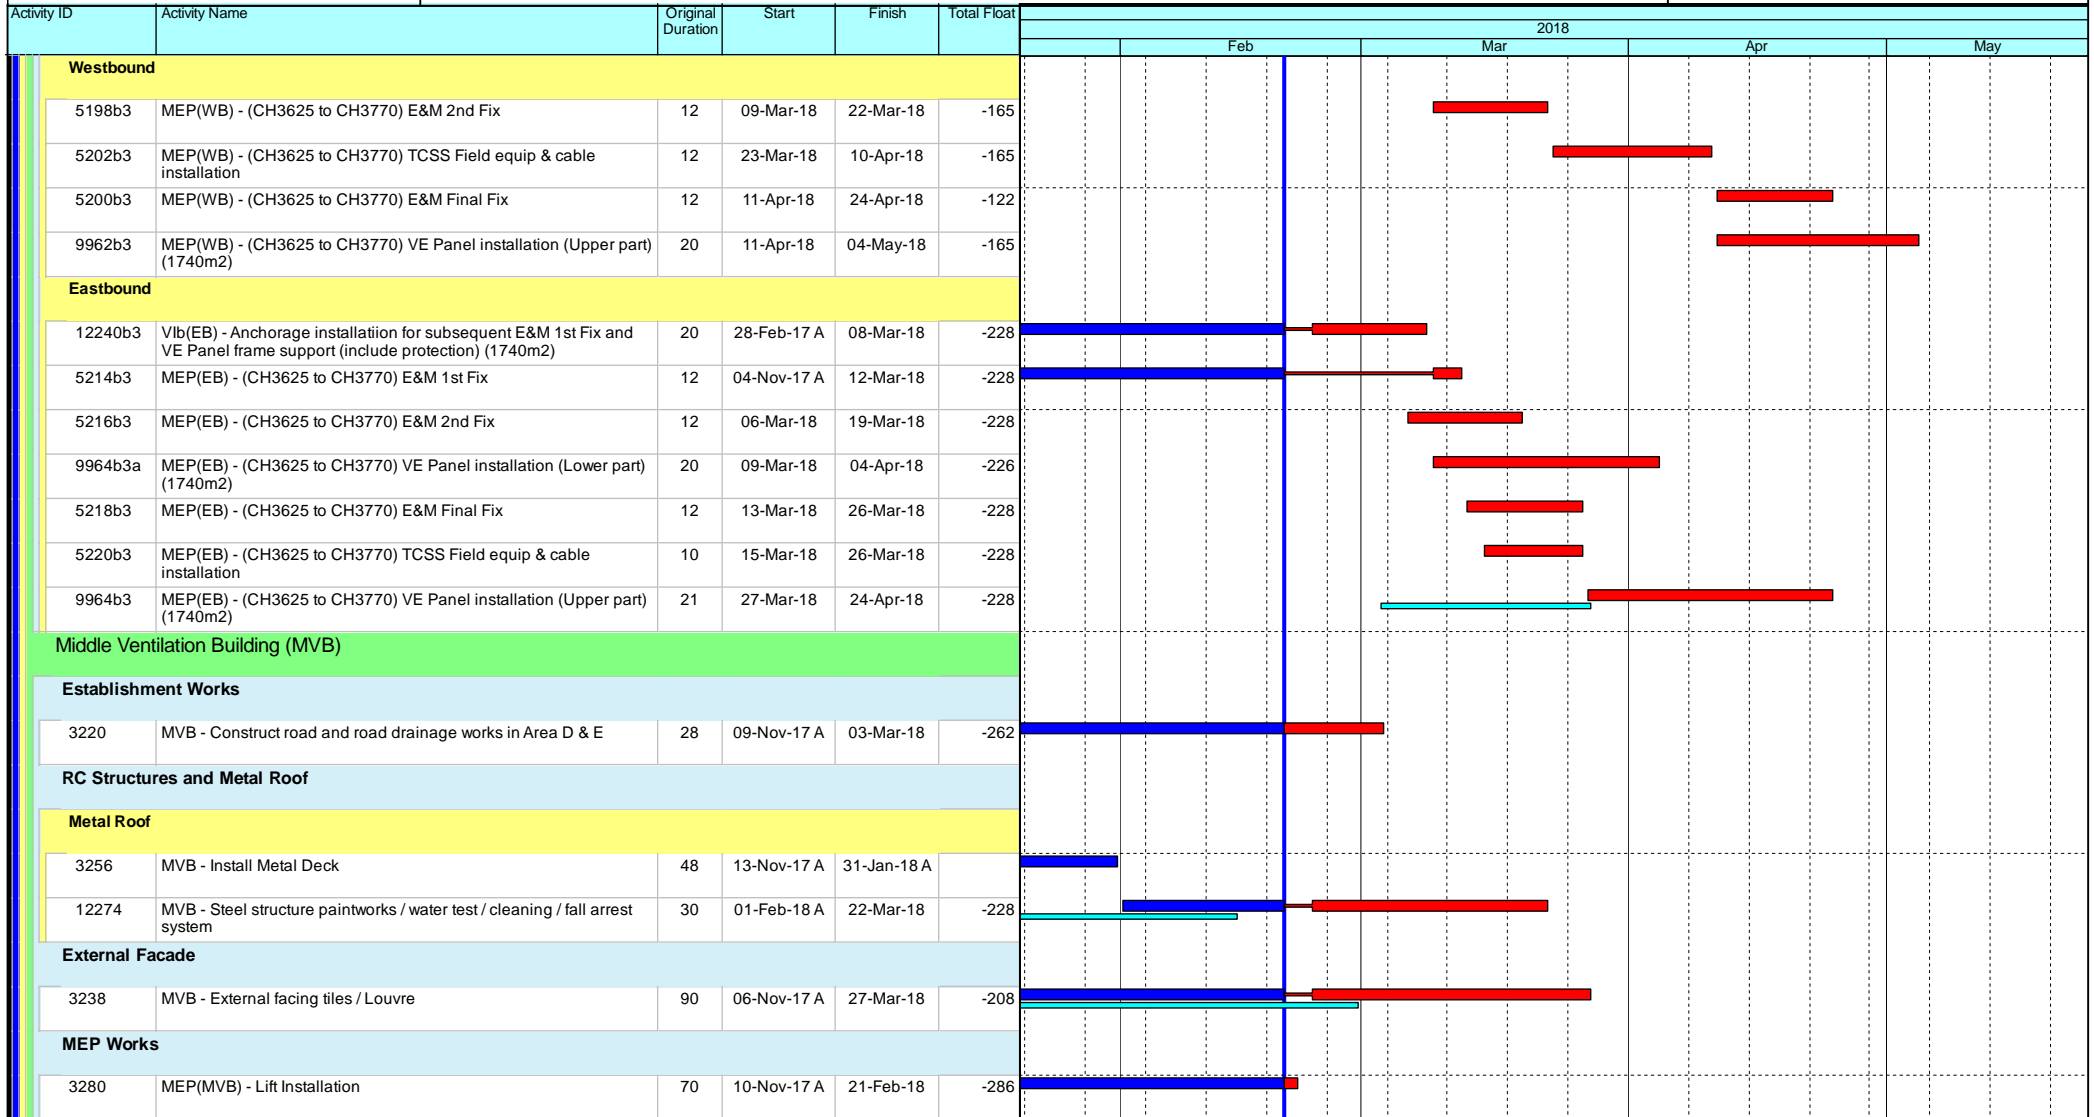

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 14 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

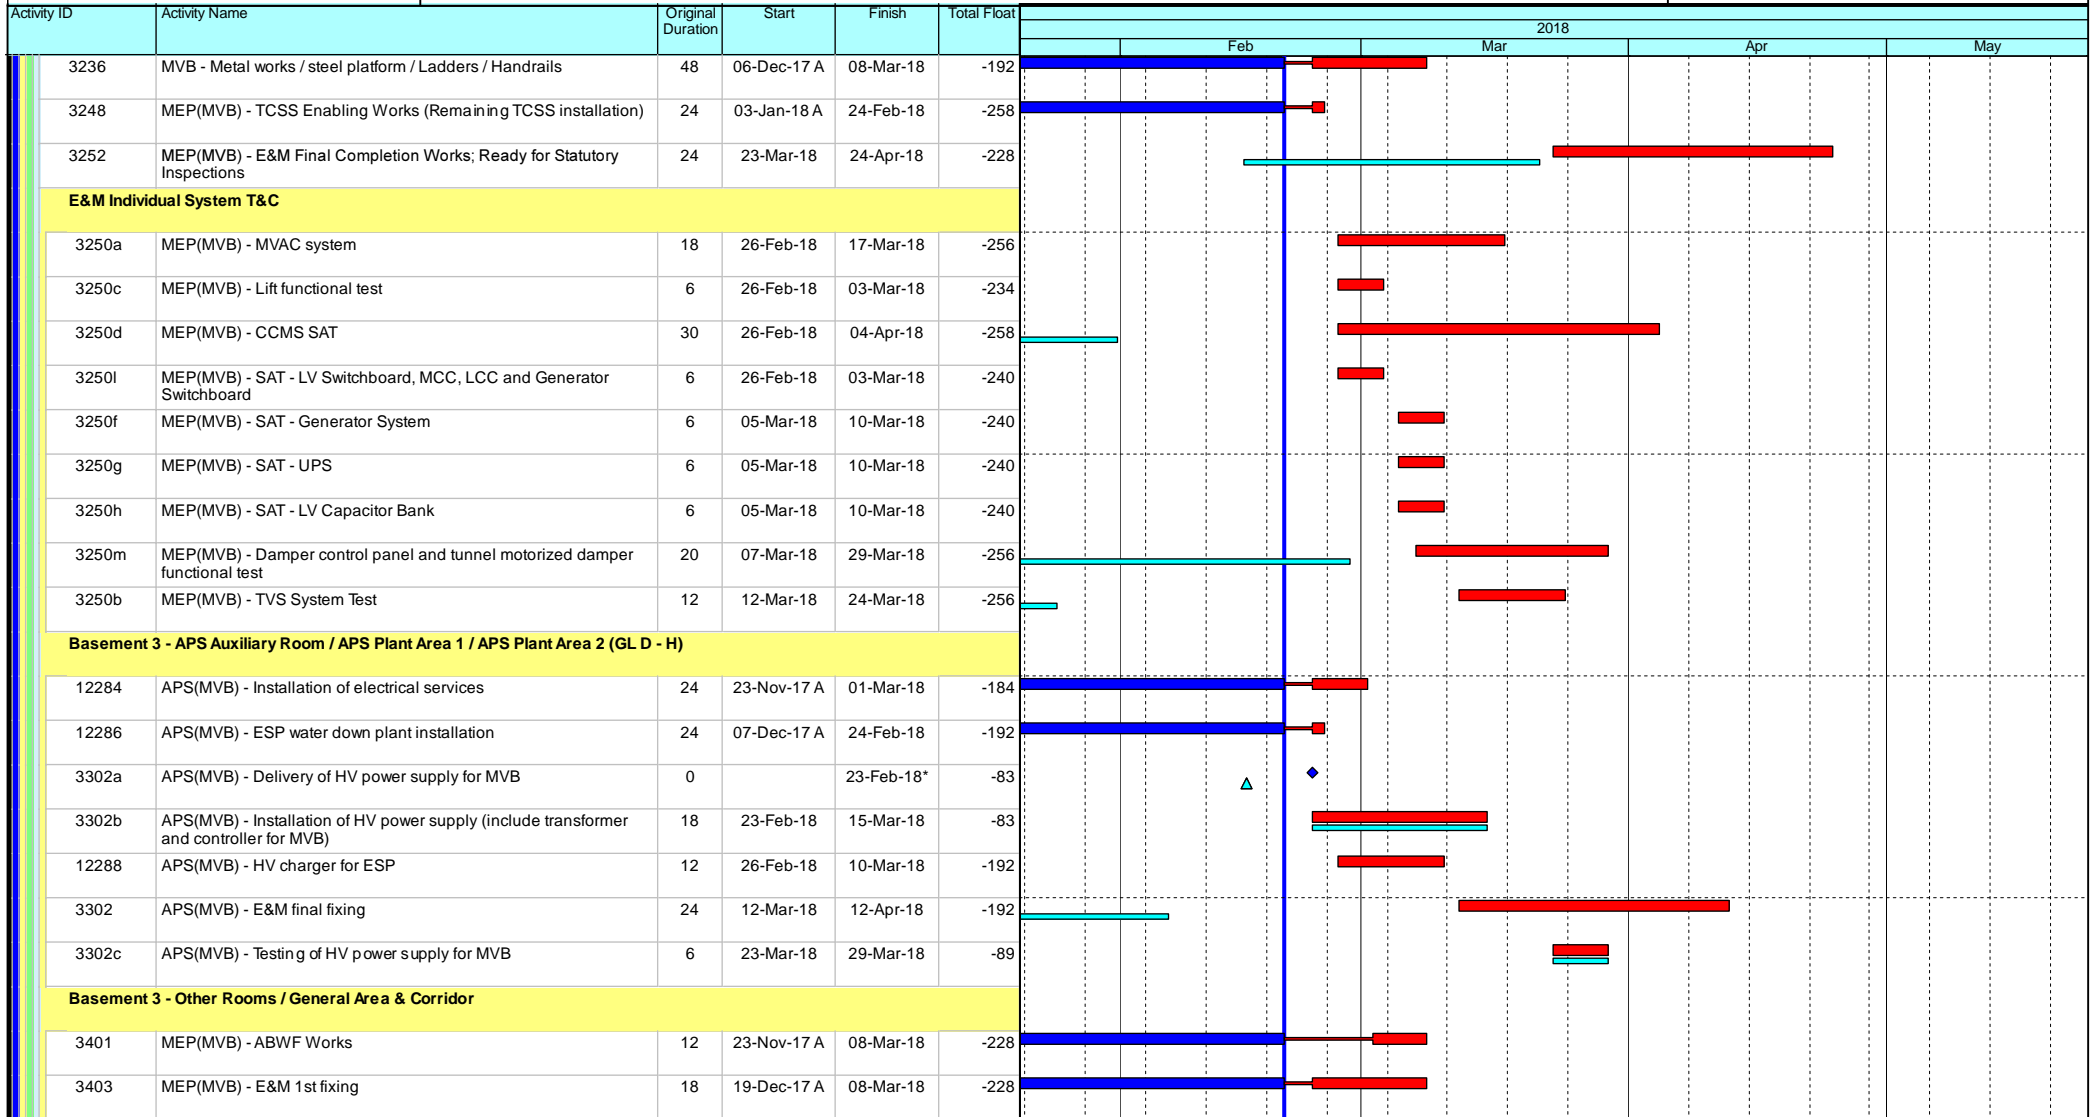

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 15 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

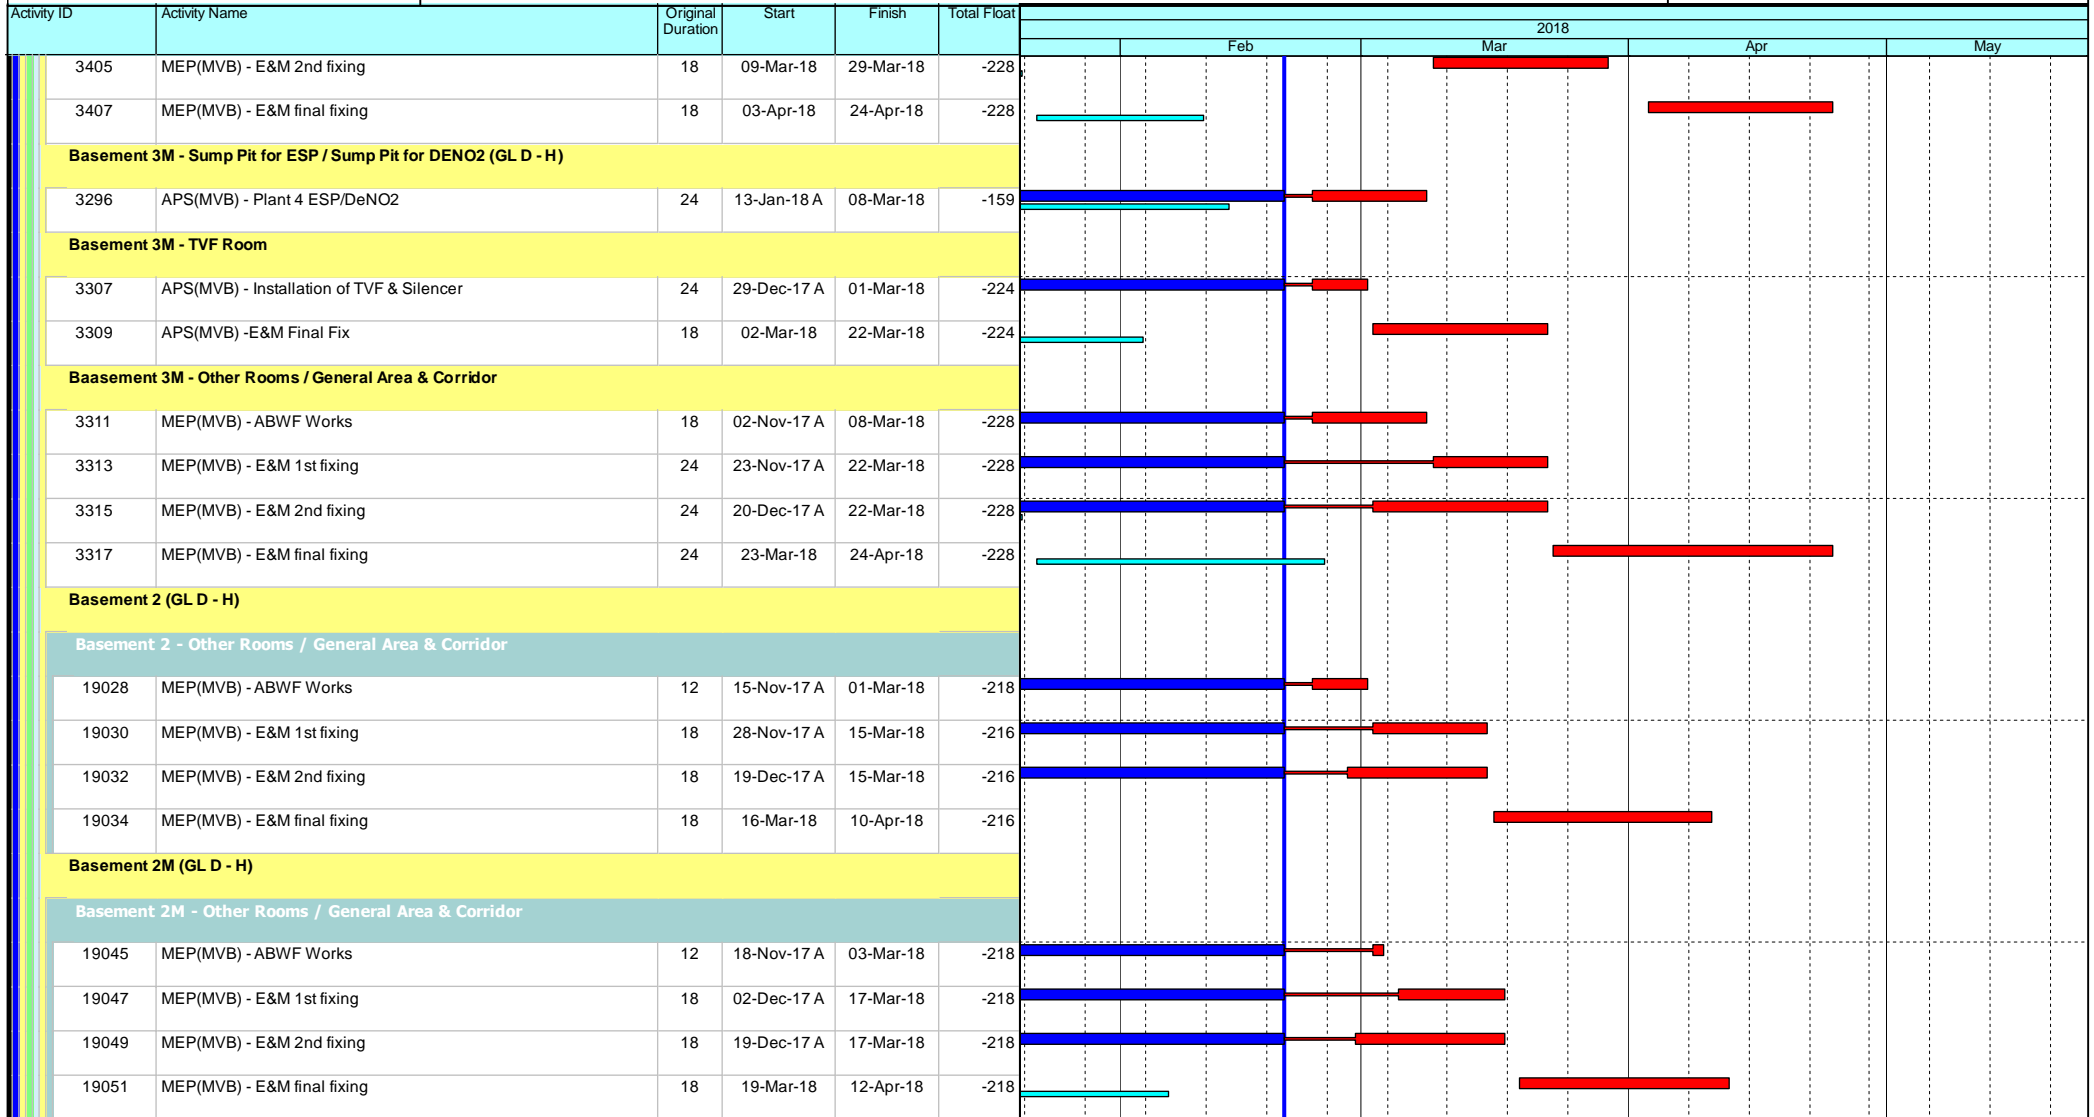

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 16 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

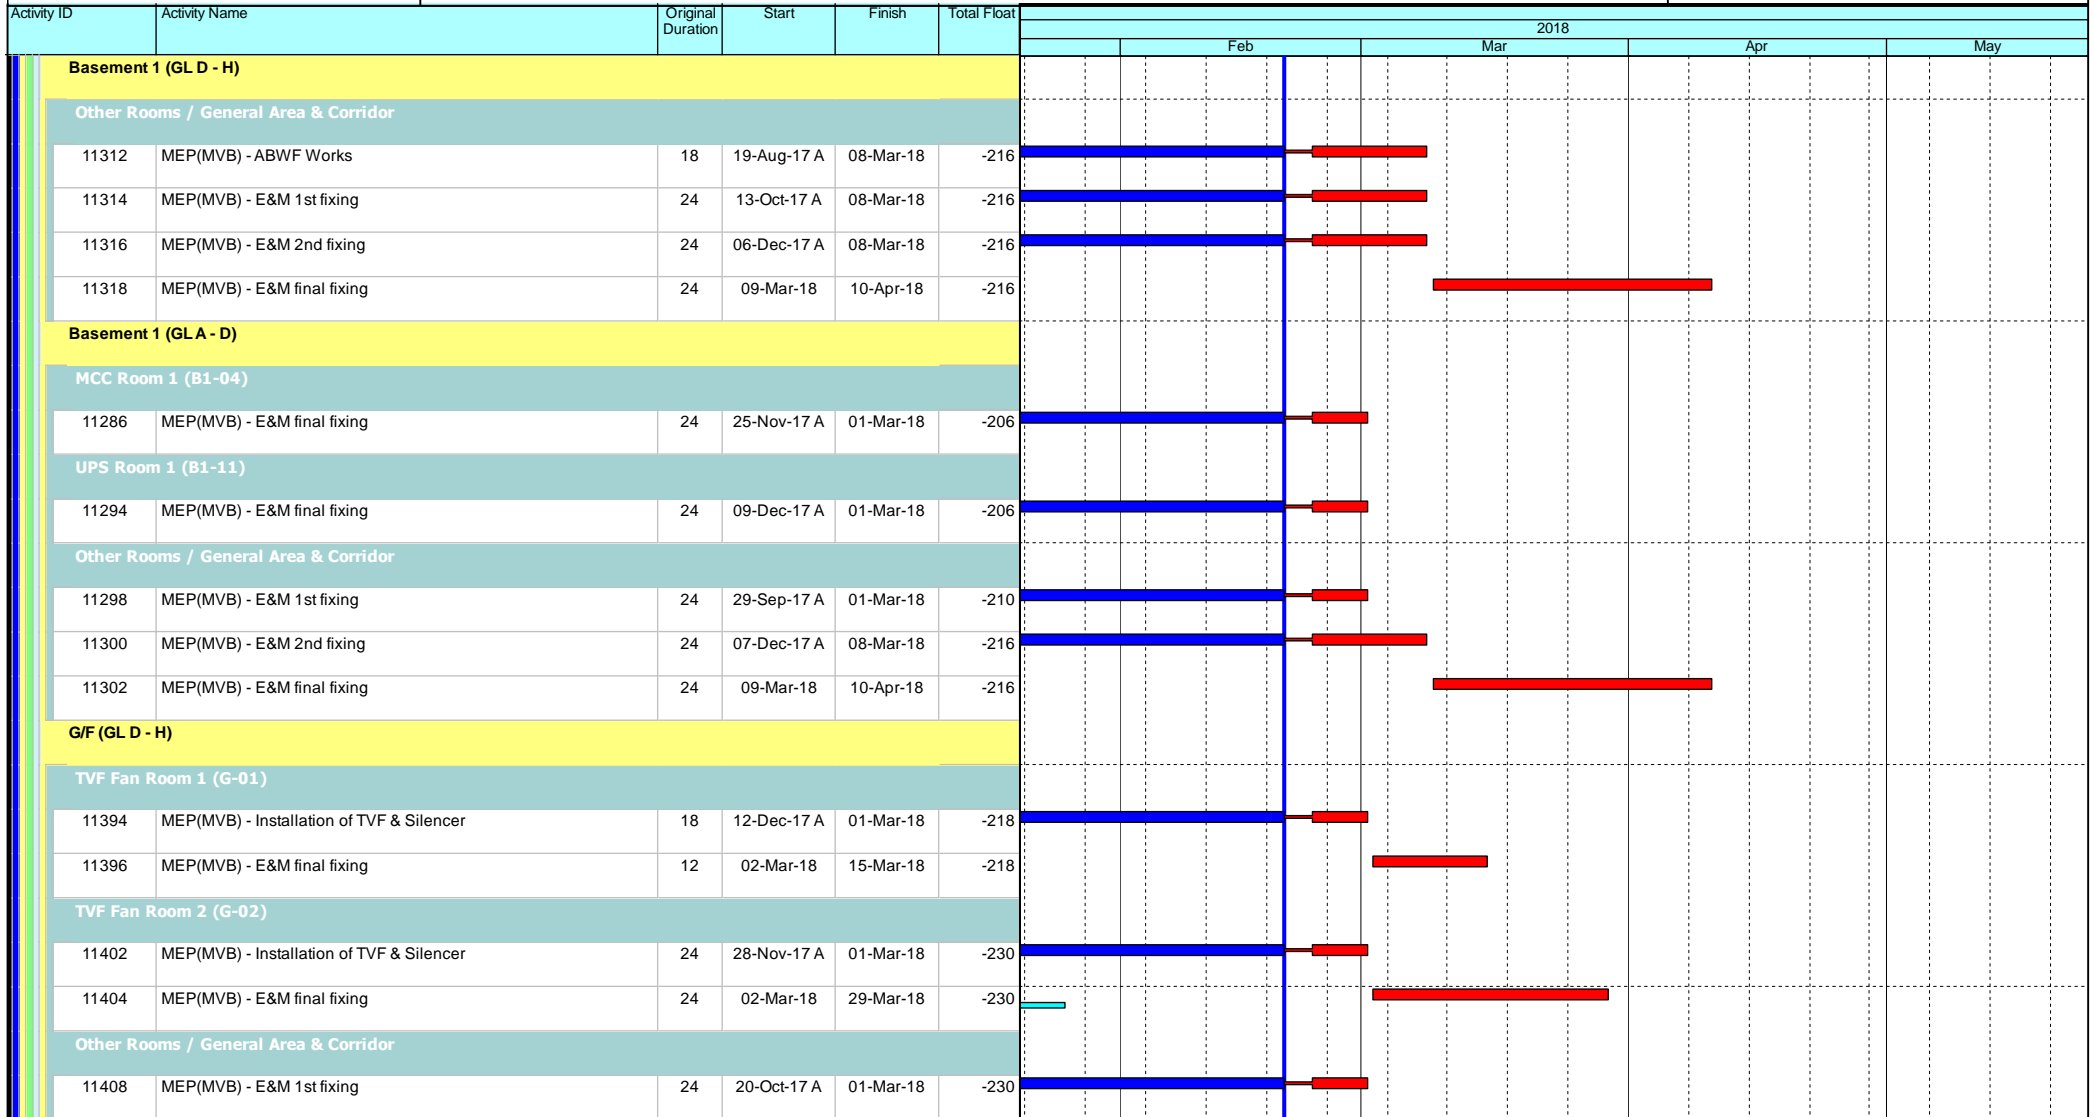

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 17 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

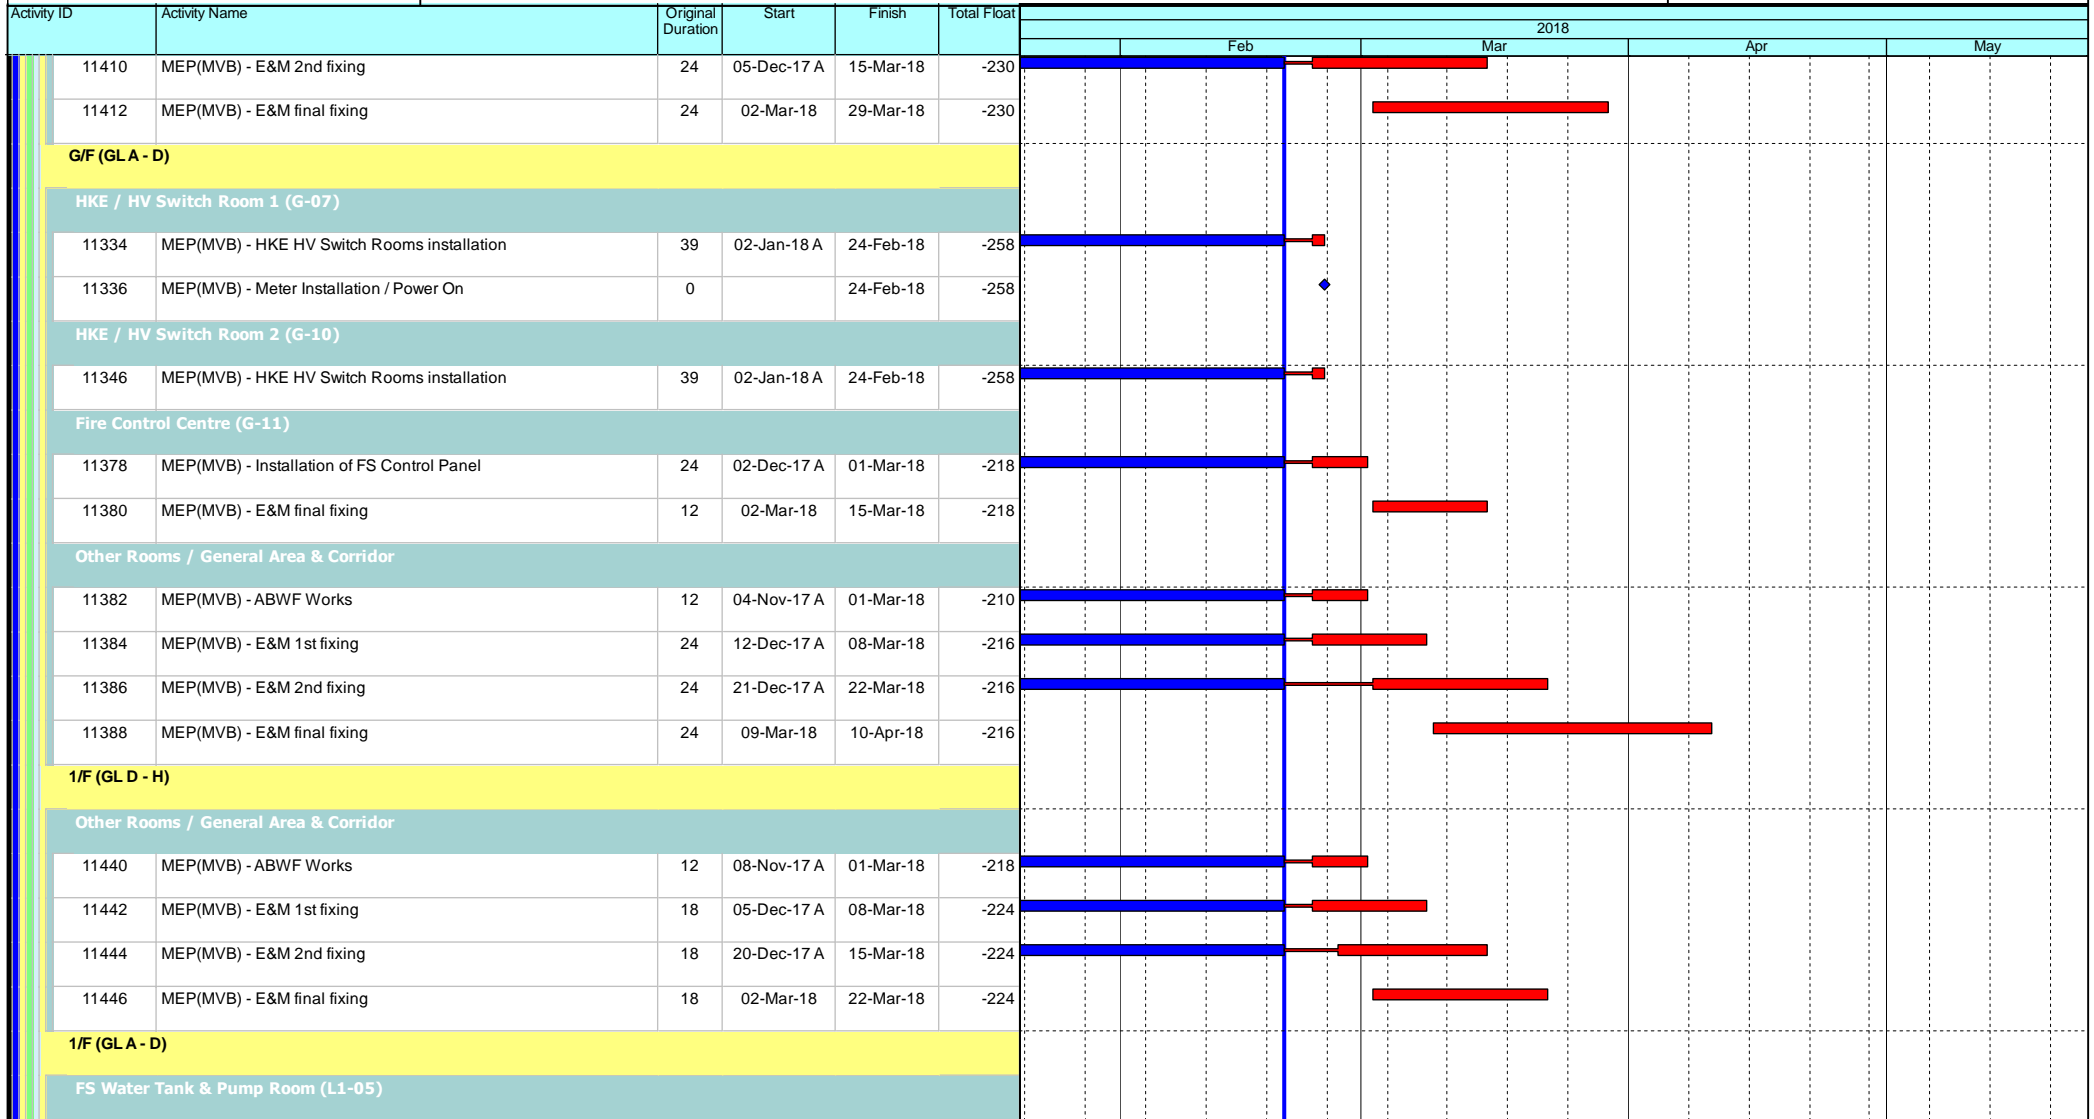

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 18 of 43



Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW



Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

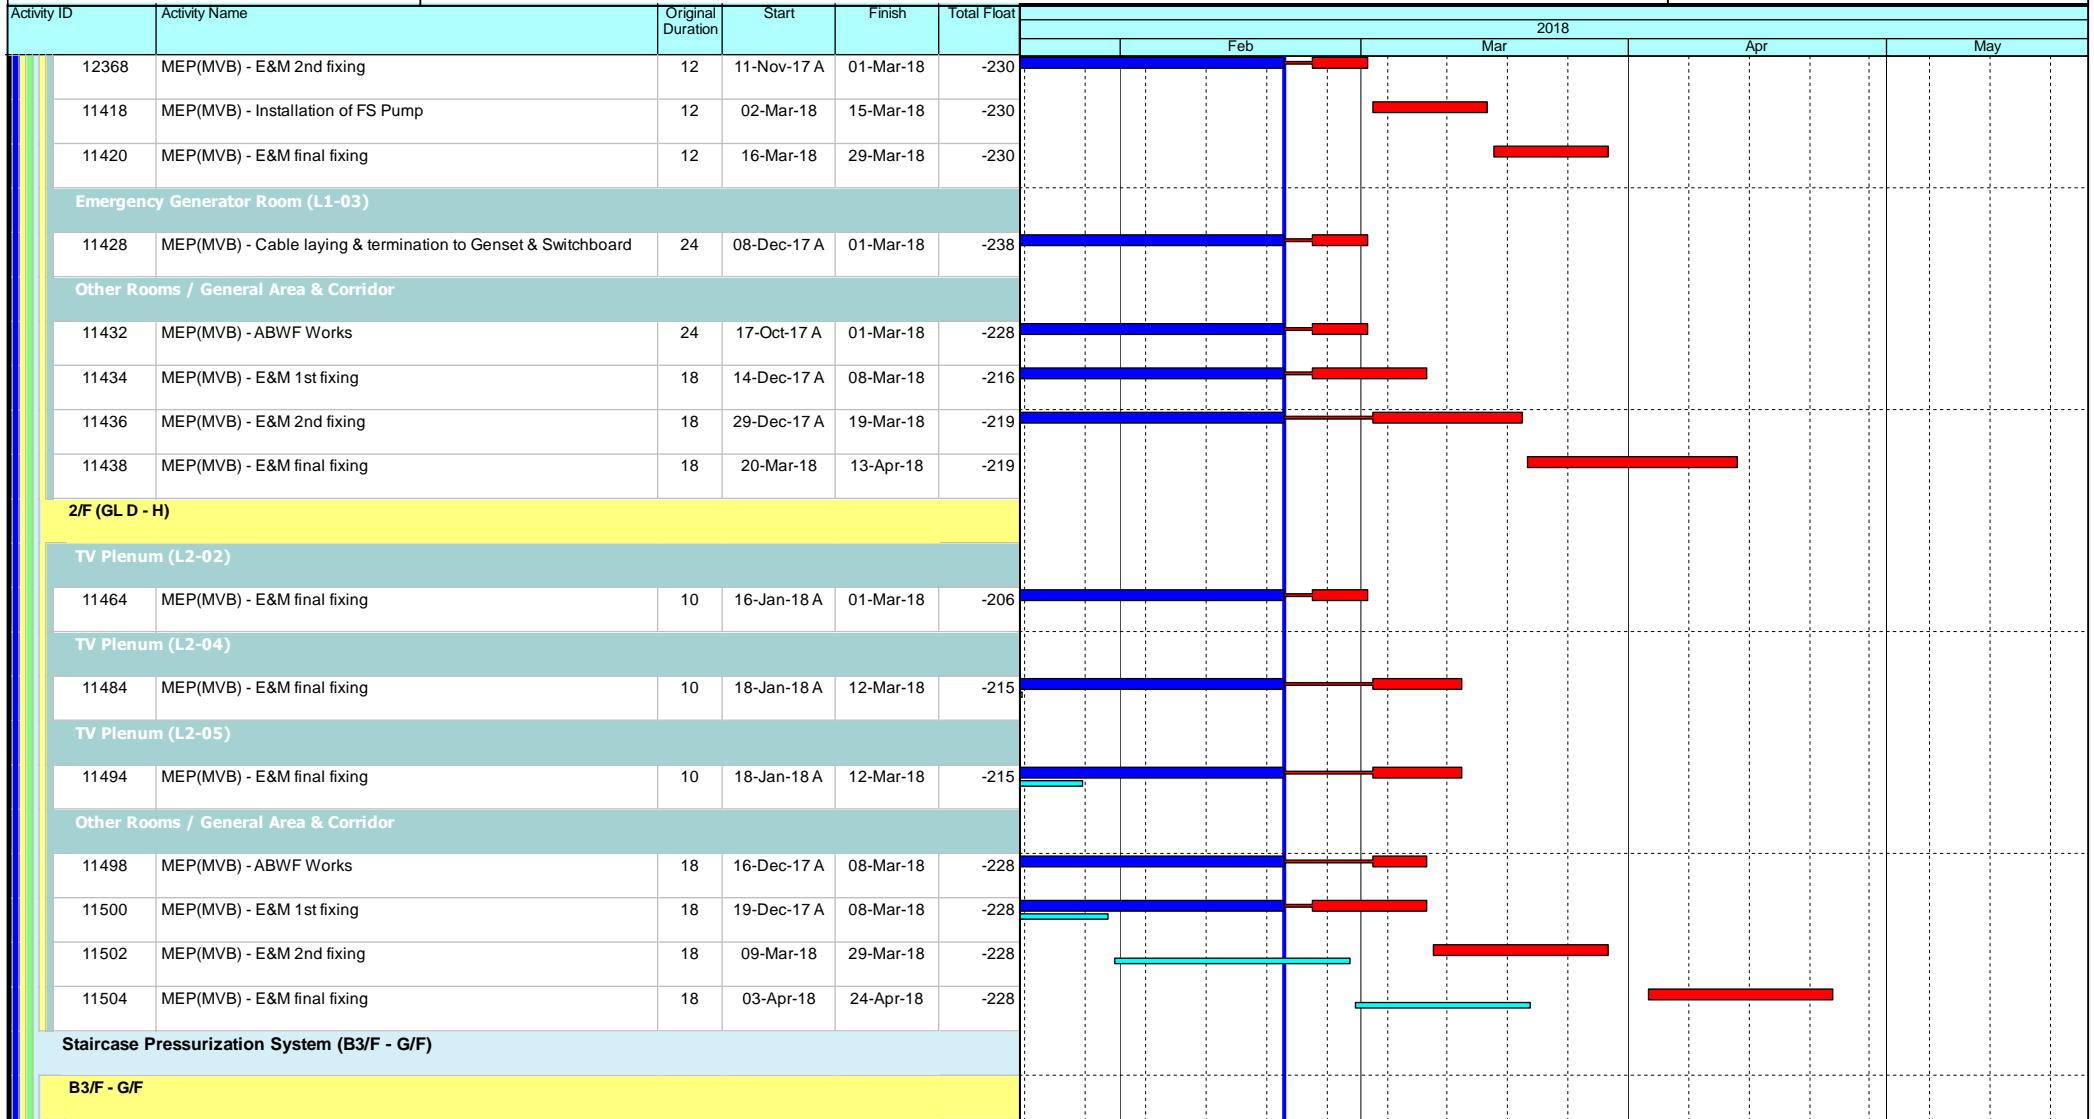

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 19 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

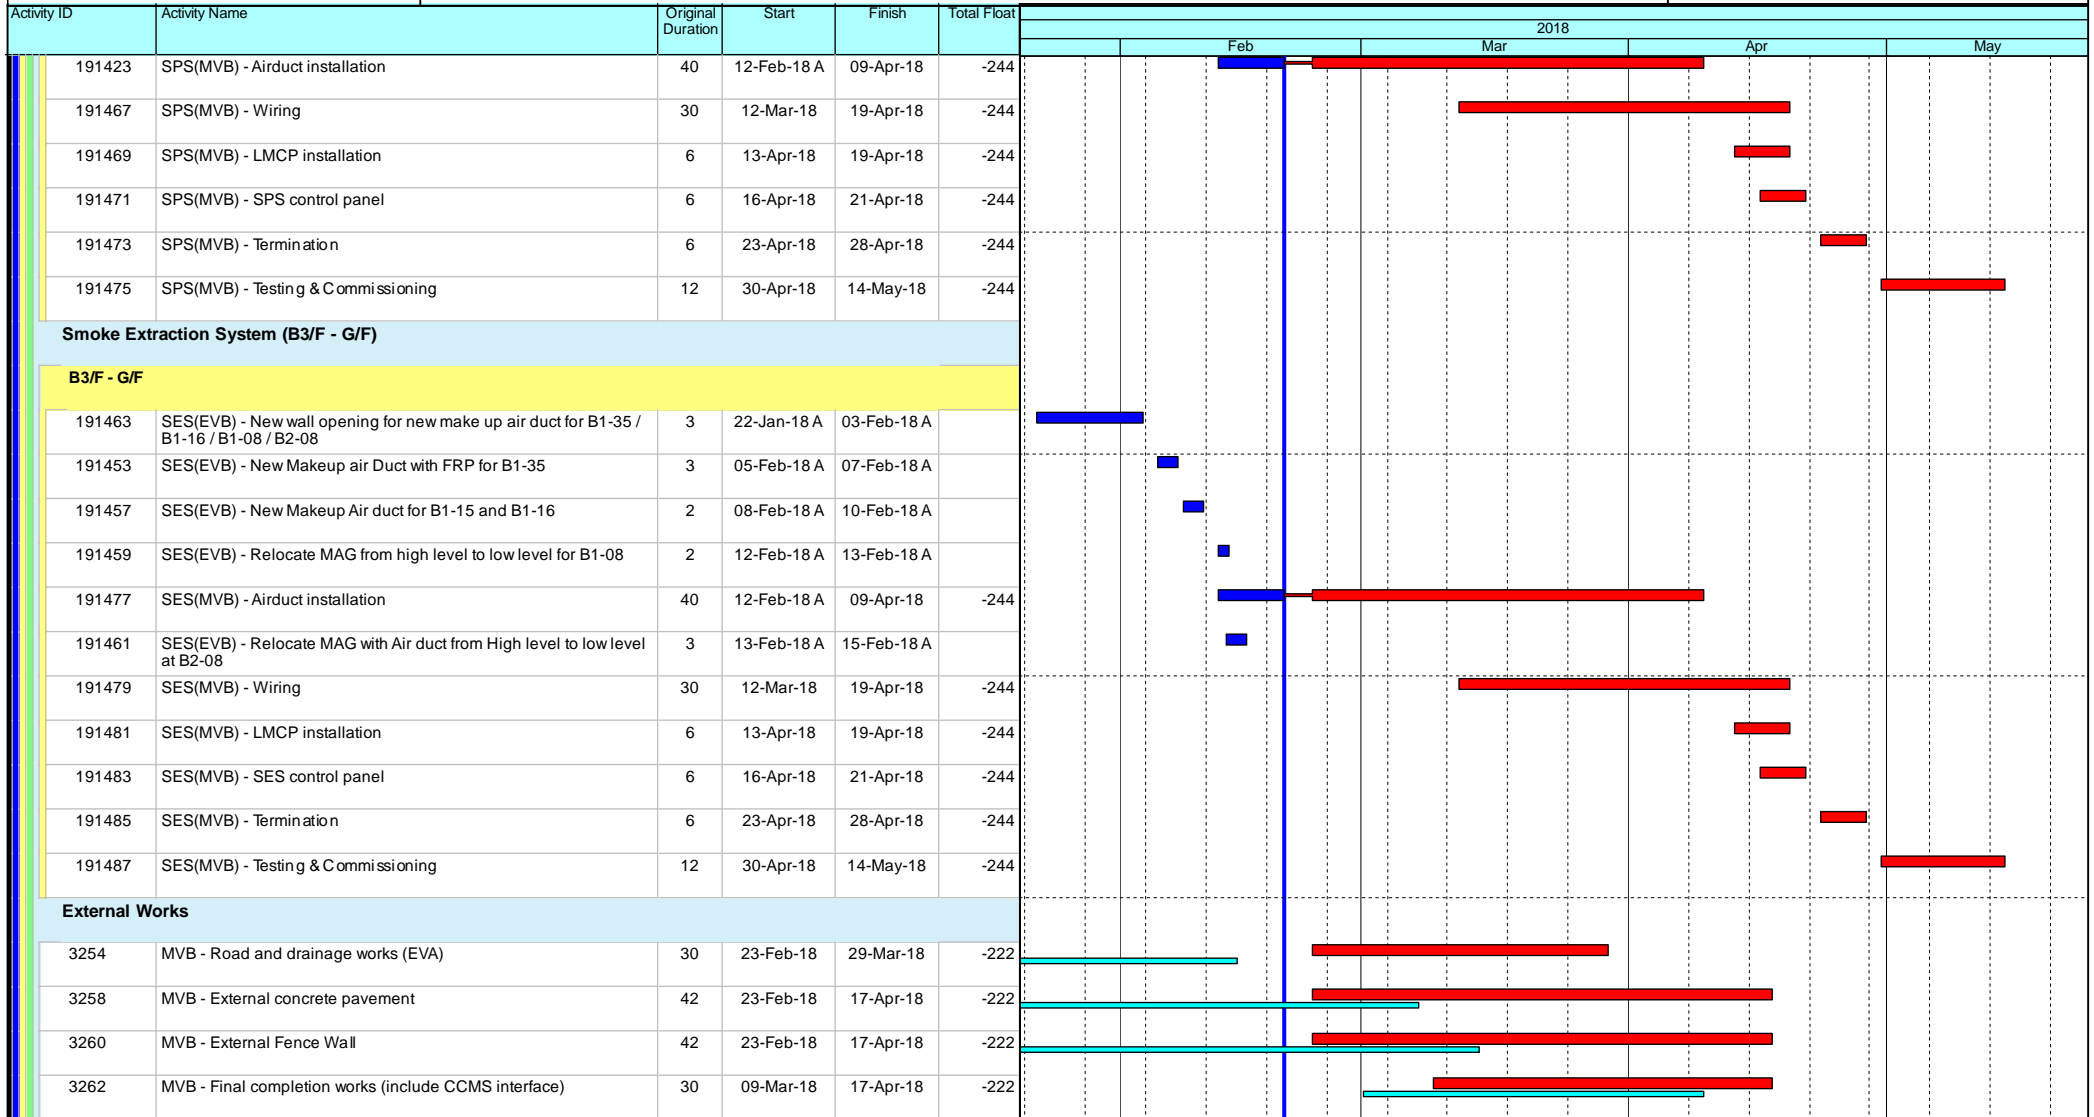

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING


Project ID: H2613-U048  
Baseline: SA01  
Layout: Update Three Month Rolling  
U048  
Page 20 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

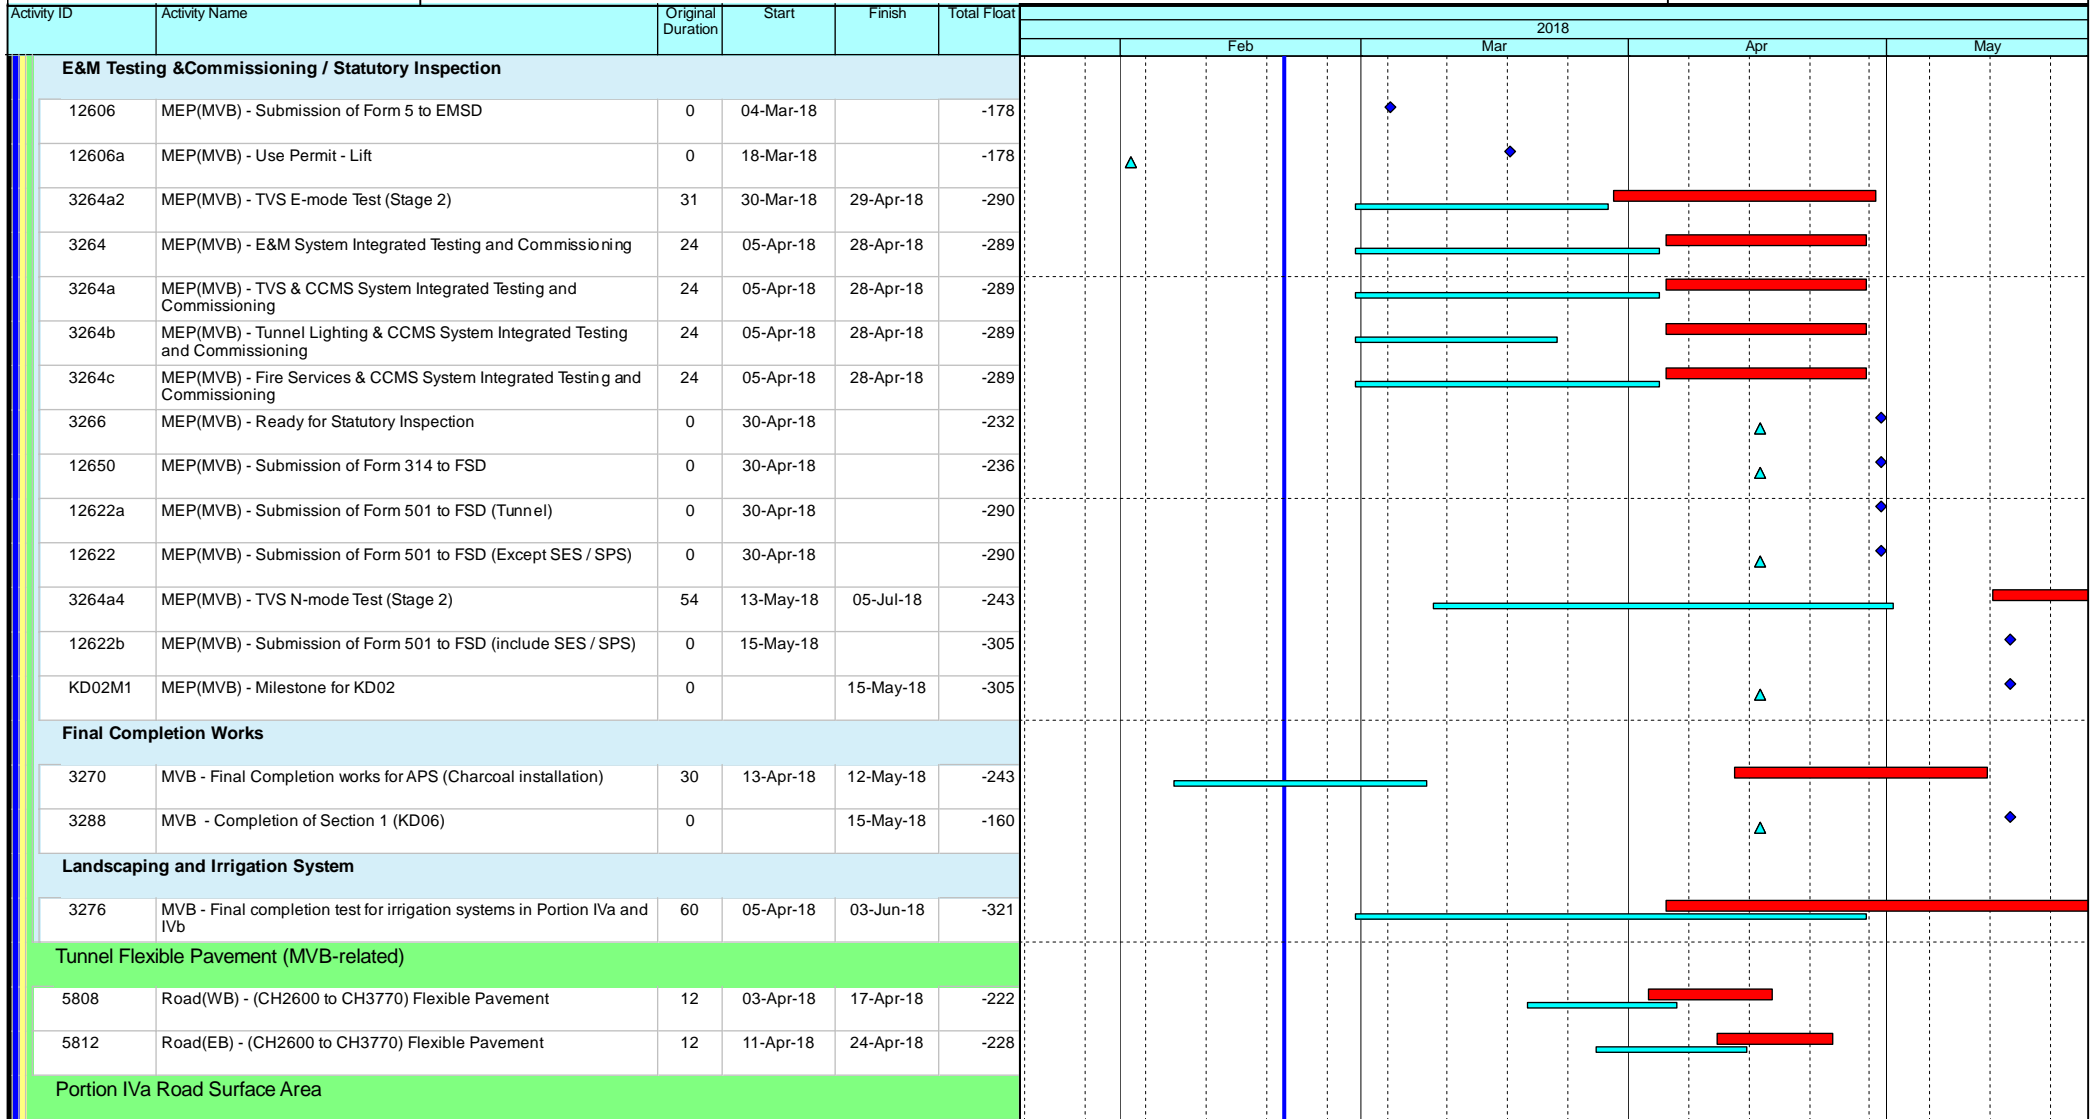

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 21 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

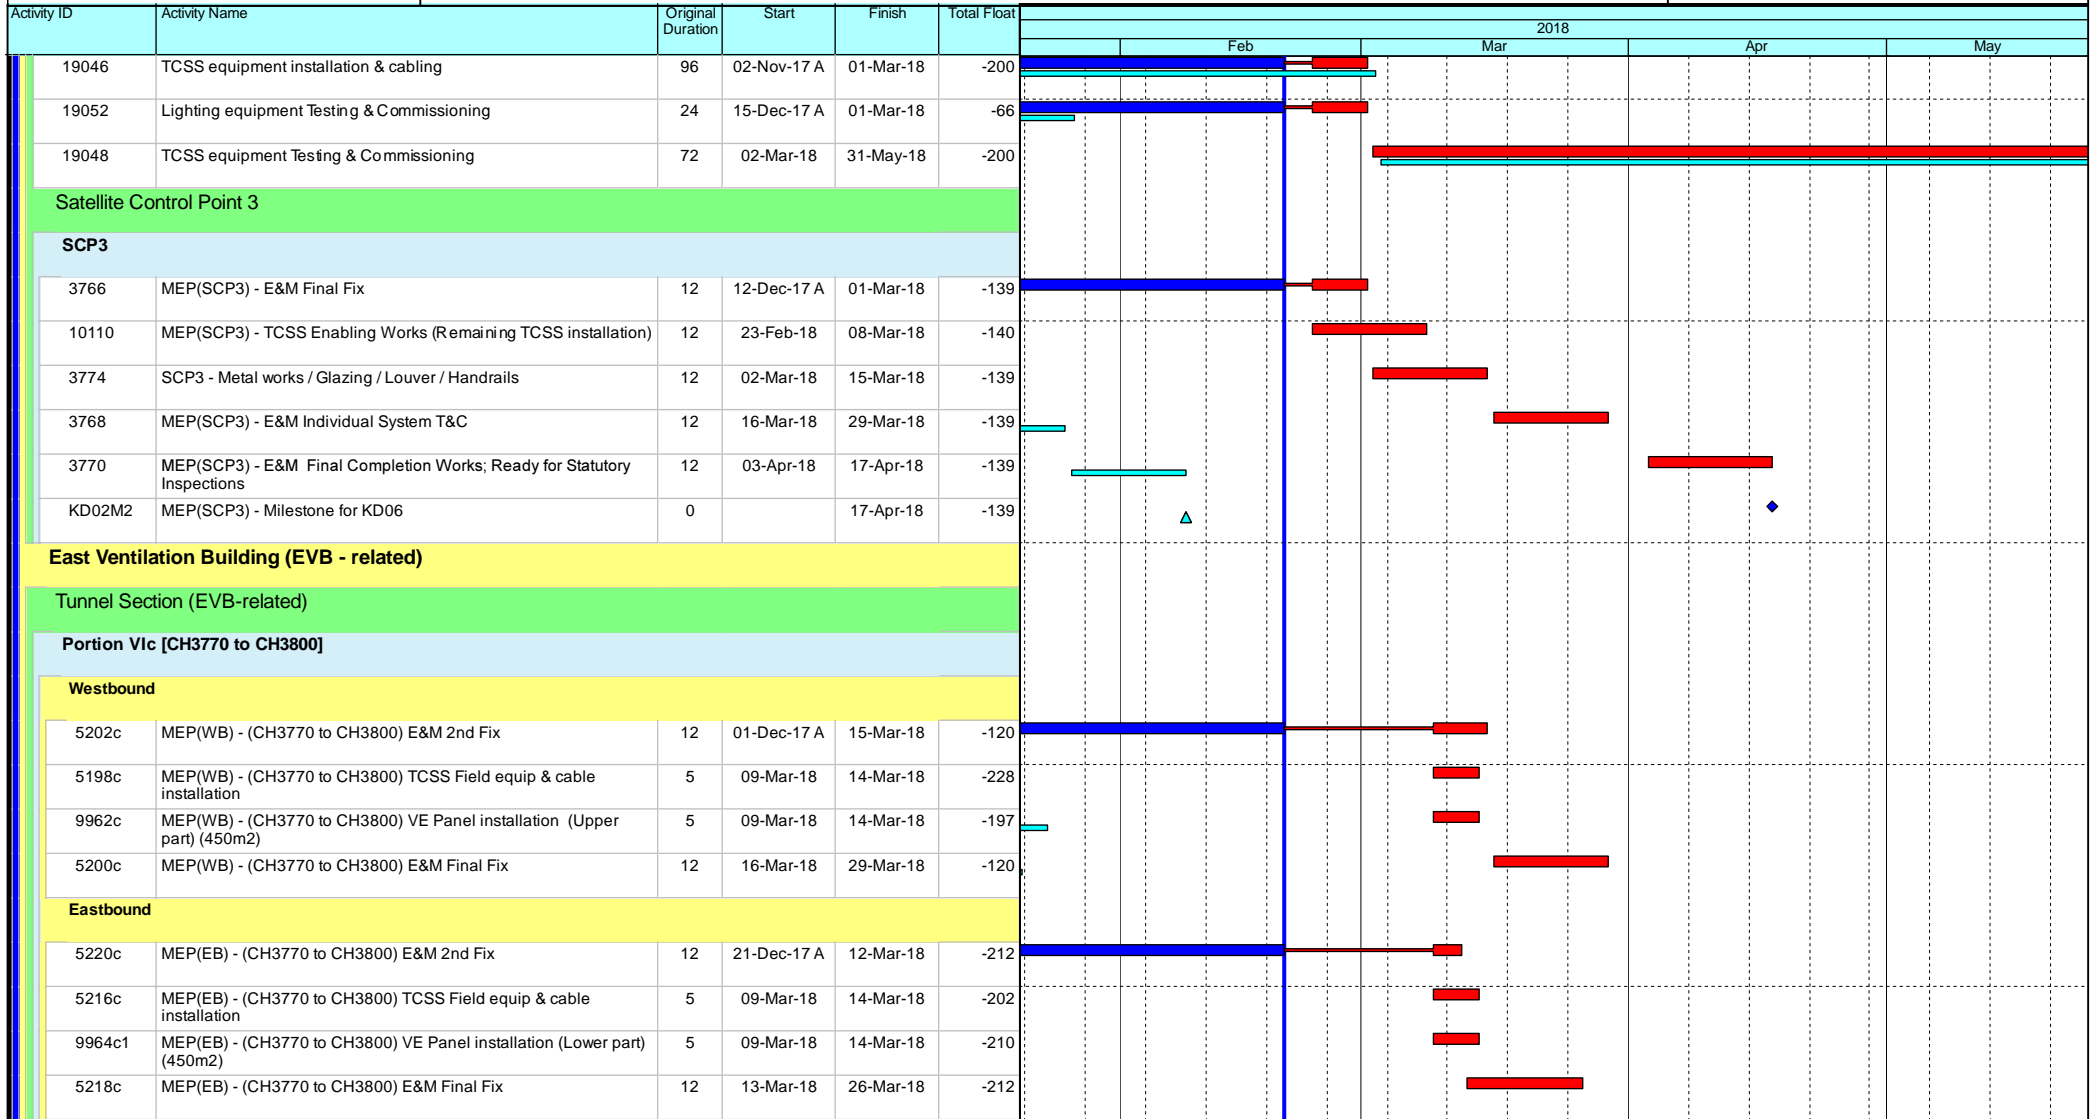

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 22 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

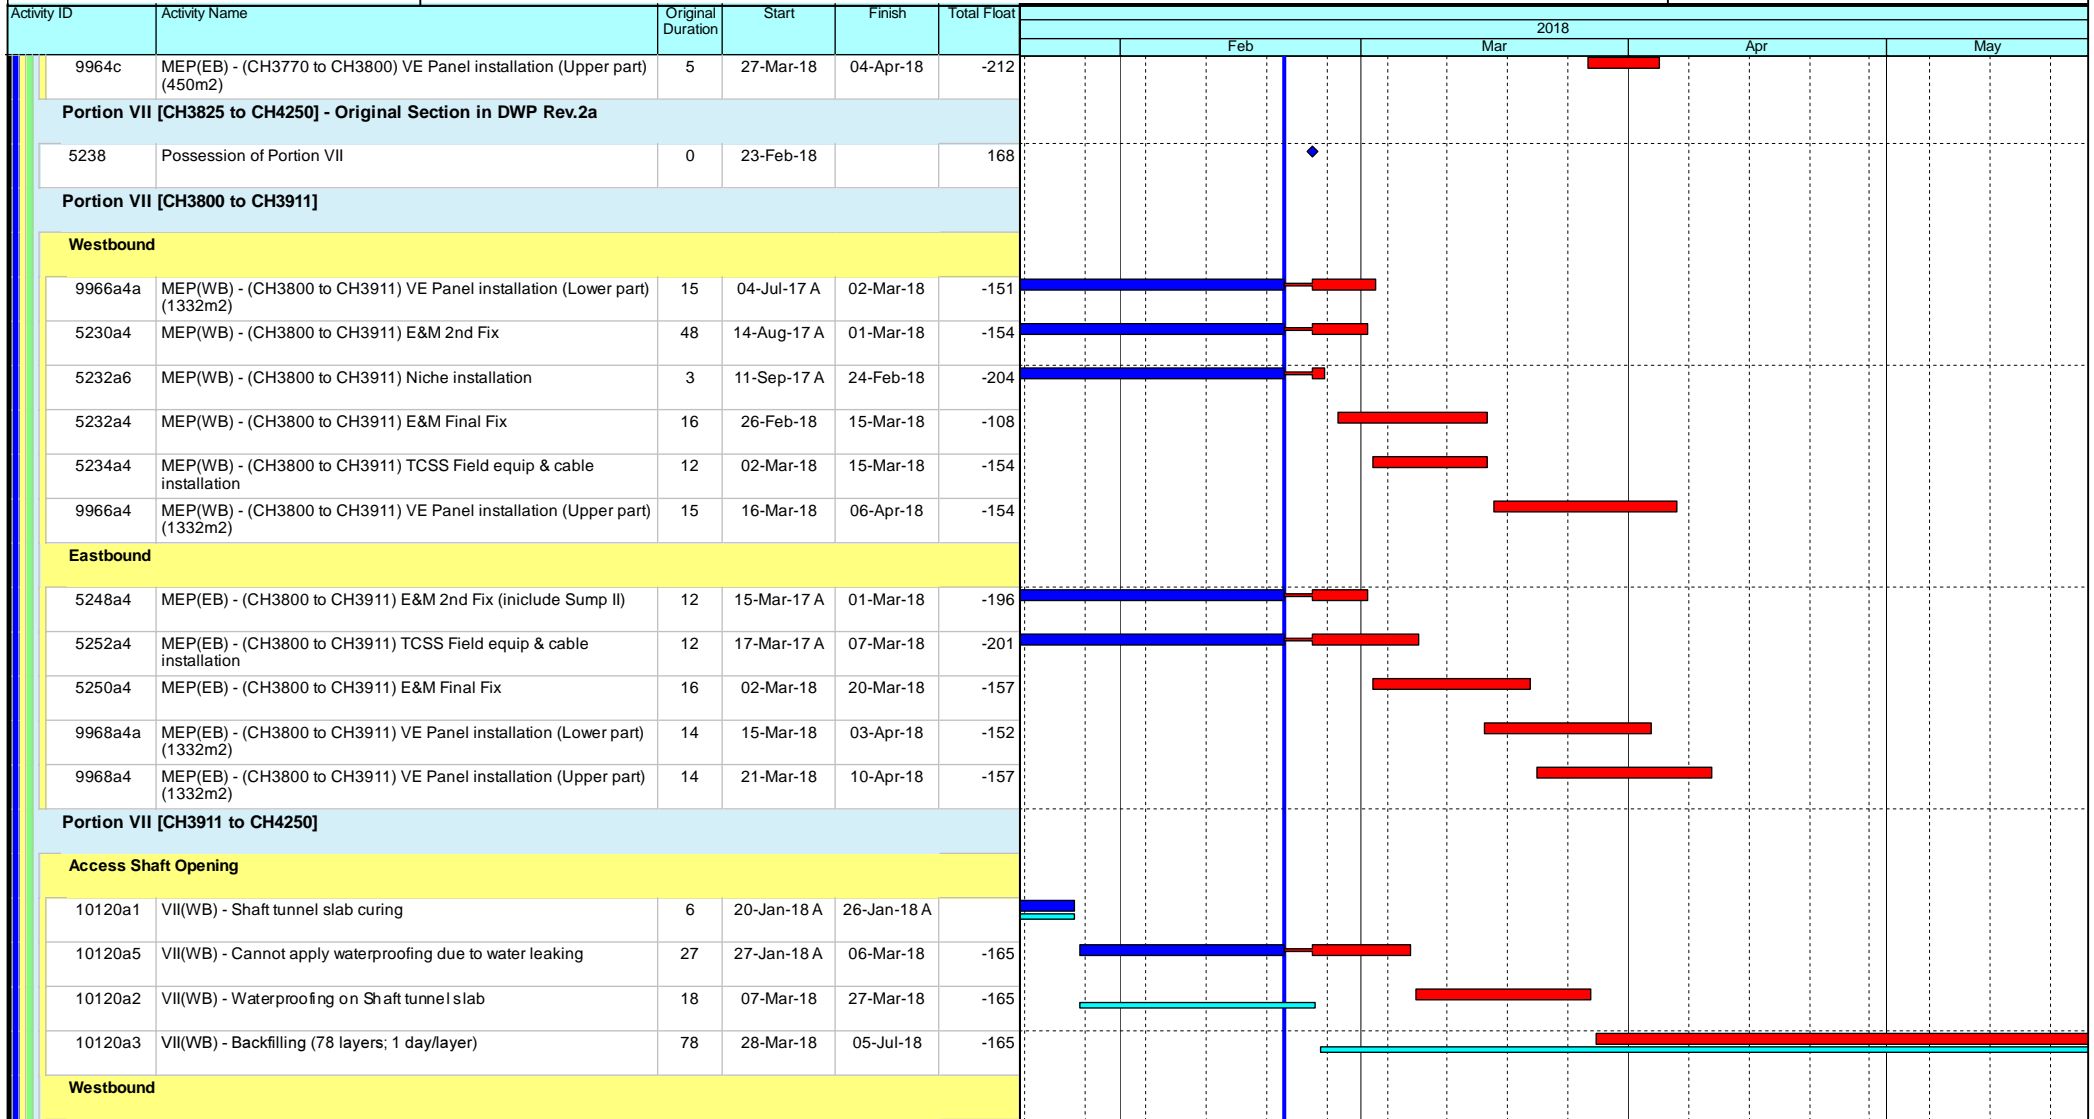

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 23 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018				
						Feb	Mar	Apr	May	
5234a2	MEP(WB) - (CH3911 to CH4250) TCSS Field equip & cable installation	15	15-Mar-17 A	09-Mar-18	-152					
5230a2	MEP(WB) - (CH3911 to CH4250) E&M 2nd Fix	48	14-Dec-17 A	01-Mar-18	-161					
5232a2	MEP(WB) - (CH3911 to CH4250) E&M Final Fix	16	02-Mar-18	20-Mar-18	-161					
9966a2a	MEP(WB) - (CH3911 to CH4250) VE Panel installation (Lower part) (4068m2)	23	03-Mar-18	29-Mar-18	-151					
9966a2	MEP(WB) - (CH3911 to CH4250) VE Panel installation (Upper part) (4068m2)	21	17-Mar-18	14-Apr-18	-161					
<b>Eastbound</b>										
12244a	VII(EB) - Anchorage installation for subsequent E&M 1st Fix and VE Panel frame support (include protection) (4086m2)	23	02-Sep-16 A	08-Mar-18	-151					
9968a2a	MEP(EB) - (CH3911 to CH4250) VE Panel installation (Lower part) (4086m2)	23	17-May-17 A	15-Mar-18	-152					
5250a2	MEP(EB) - (CH3911 to CH4250) E&M Final Fix	16	23-Feb-18	13-Mar-18	-150					
5252a2	MEP(EB) - (CH3911 to CH4250) TCSS Field equip & cable installation	15	23-Feb-18	12-Mar-18	-149					
9968a2	MEP(EB) - (CH3911 to CH4250) VE Panel installation (Upper part) (4086m2)	12	02-Mar-18	15-Mar-18	-152					
<b>Slip Road 8</b>										
13082a	VII(SR8) - Anchorage installation for subsequent E&M 1st Fix and VE Panel frame support (include protection) (1500m2)	24	09-Jan-17 A	15-Mar-18	-151					
13084a1	MEP(SR8) - (CH1000 to CH750) VE Panel installation (Lower part) (550m2)	6	27-Jun-17 A	22-Mar-18	-151					
13068a	MEP(SR8) - (CH1000 to CH750) E&M 1st Fix	12	23-Dec-17 A	15-Mar-18	-151					
13070a	MEP(SR8) - (CH1000 to CH750) E&M 2nd Fix (include Sump D)	12	09-Mar-18	22-Mar-18	-151					
13072a	MEP(SR8) - (CH1000 to CH750) E&M Final Fix	12	16-Mar-18	29-Mar-18	-151					
13074a	MEP(SR8) - (CH1000 to CH750) TCSS Field equip & cable installation	12	16-Mar-18	29-Mar-18	-151					
13084a	MEP(SR8) - (CH1000 to CH750) VE Panel installation (Upper part) (550m2)	6	23-Mar-18	29-Mar-18	-151					
<b>Portion VIIla [CH4250 to CH4600]</b>										
<b>Westbound</b>										
9970a	MEP(WB) - (CH4250 to CH4600) VE Panel installation (Lower part) (3900m2)	20	20-Sep-17 A	01-Mar-18	-140					
5282	MEP(WB) - (CH4250 to CH4600) E&M Final Fix	12	06-Jan-18 A	01-Mar-18	-147					
5284	MEP(WB) - (CH4250 to CH4600) TCSS Field equip & cable installation	11	23-Feb-18	07-Mar-18	-152					

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 24 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW







Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

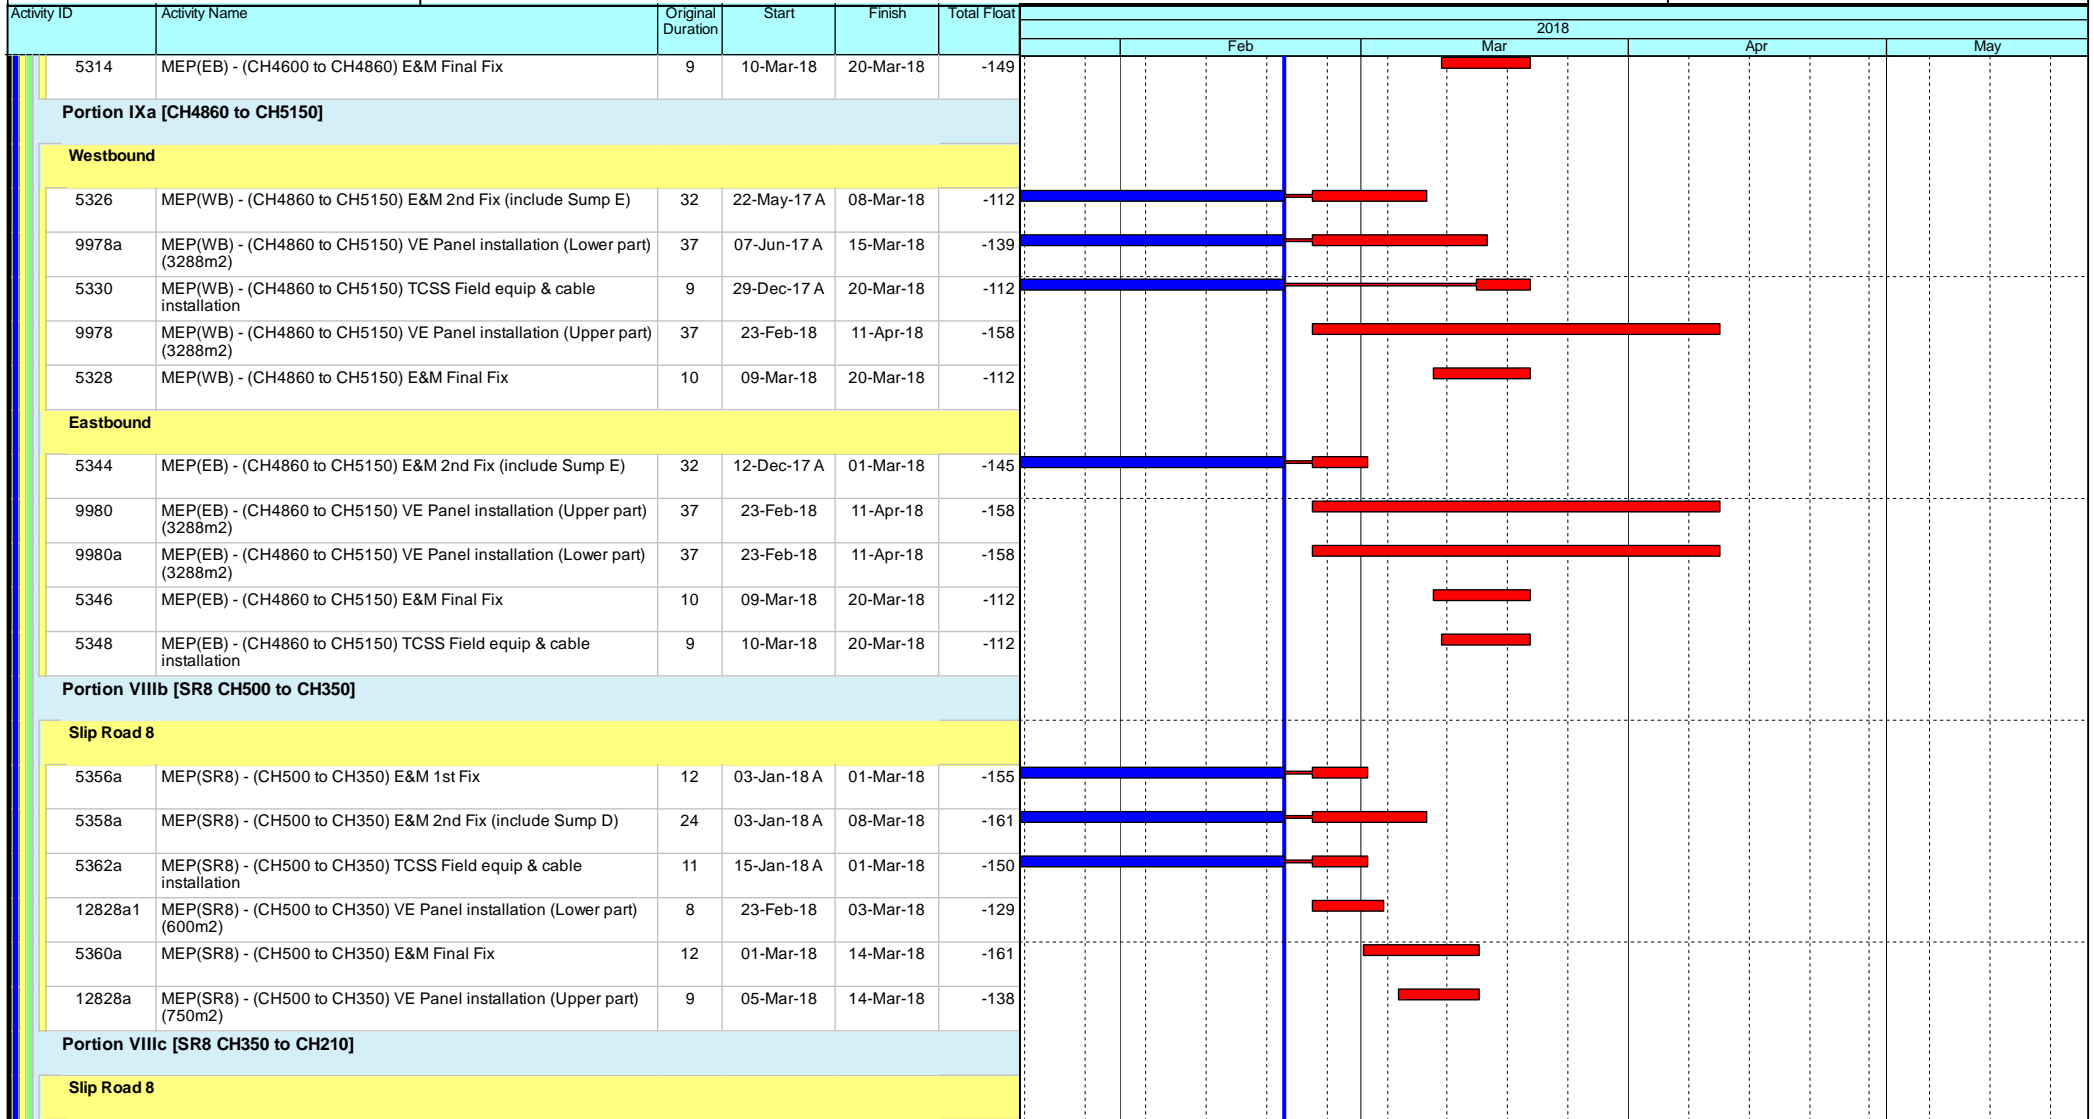

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING


Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 26 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

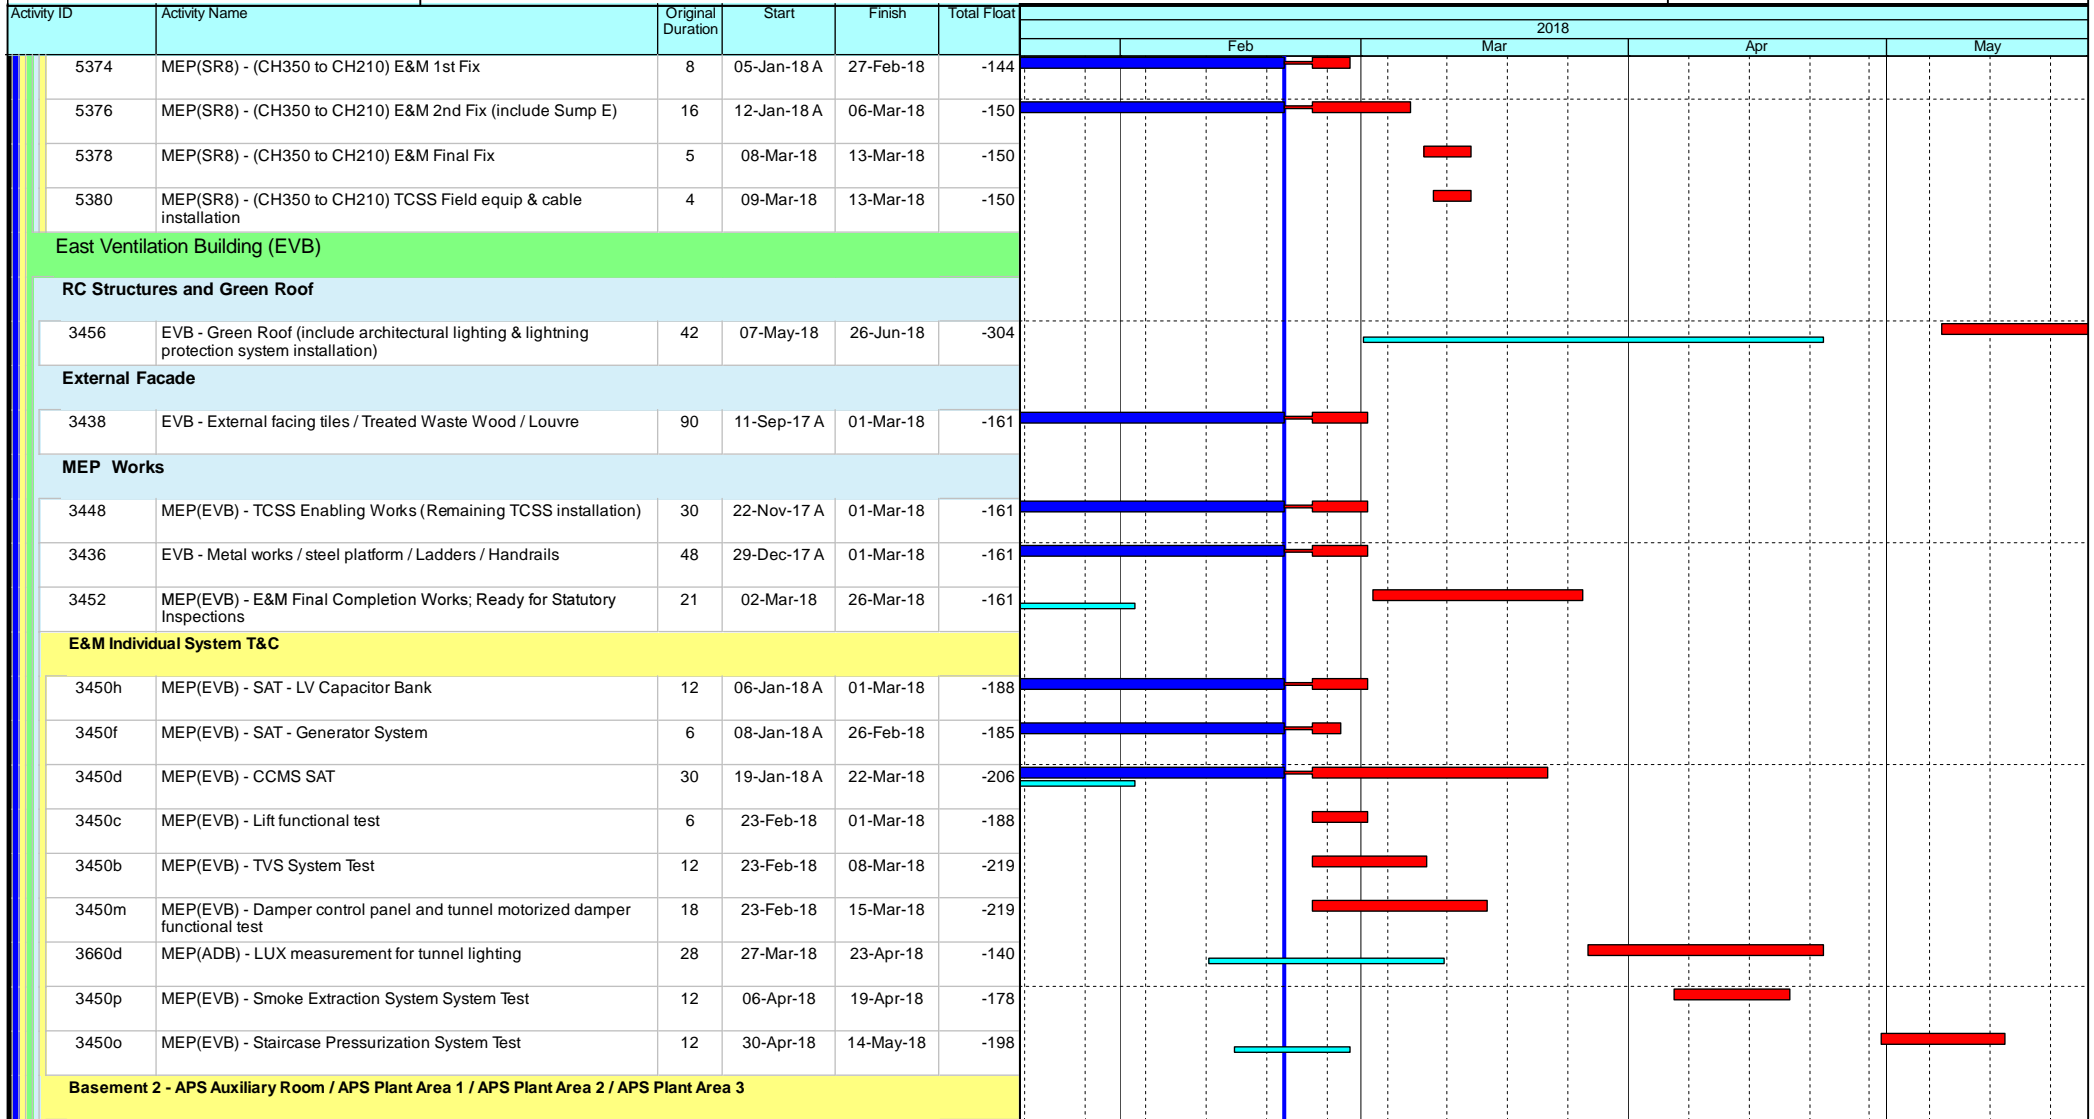

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 27 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018				
						Feb	Mar	Apr	May	
12304	APS(EVB) - HV charger for ESP	12	23-Feb-18	08-Mar-18	-185					
3560a	APS(EVB) - Delivery of HV power supply	0		23-Feb-18*	-185					
3560b	APS(EVB) - Installation of HV power supply (include transformer and controller for EVB)	18	23-Feb-18	15-Mar-18	-185					
3560	APS(EVB) - E&M final fixing	24	09-Mar-18	10-Apr-18	-185					
3560c	APS(EVB) - Testing of HV power supply for EVB	6	16-Mar-18	22-Mar-18	-89					
<b>Basement 2 - Sump Pit for ESP / Sump Pit for DENO2</b>										
3550	APS(EVB) - Plant 1 ESP/DeNO2 (Equipment installation / termination)	18	20-Jan-18 A	09-Feb-18 A						
3552a	APS(EVB) - Plant 2 ESP/DeNO2 (Equipment in place)	12	20-Jan-18 A	02-Feb-18 A						
3554a	APS(EVB) - Plant 3 ESP/DeNO2 (Equipment in place)	12	03-Feb-18 A	13-Feb-18 A						
3552	APS(EVB) - Plant 2 ESP/DeNO2 (Equipment installation / termination)	18	05-Feb-18 A	19-Feb-18 A						
3554	APS(EVB) - Plant 3 ESP/DeNO2 (Equipment installation / termination)	18	05-Feb-18 A	19-Feb-18 A						
<b>Basement 2 - Other Rooms / General Area &amp; Corridor</b>										
11602	MEP(EVB) - E&M 2nd fixing	24	06-Oct-17 A	01-Mar-18	-146					
11604	MEP(EVB) - E&M final fixing	24	13-Dec-17 A	08-Mar-18	-146					
<b>Basement 1 Mezzanine (GLA - D)</b>										
<b>Basement 1 Mezzanine (GL D - L)</b>										
<b>Plenum (B1M-03)</b>										
12988	MEP(EVB) - E&M 1st fixing	12	05-Oct-17 A	24-Feb-18	-156					
<b>Basement 1 (GLA - D)</b>										
<b>Other Rooms / General Area &amp; Corridor</b>										
11606	MEP(EVB) - ABWF Works	24	13-Sep-17 A	26-Feb-18	-124					
11608	MEP(EVB) - E&M 1st fixing	24	04-Oct-17 A	08-Mar-18	-133					
11610	MEP(EVB) - E&M 2nd fixing	24	18-Oct-17 A	15-Mar-18	-139					
11612	MEP(EVB) - E&M final fixing	24	16-Mar-18	17-Apr-18	-139					

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 28 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

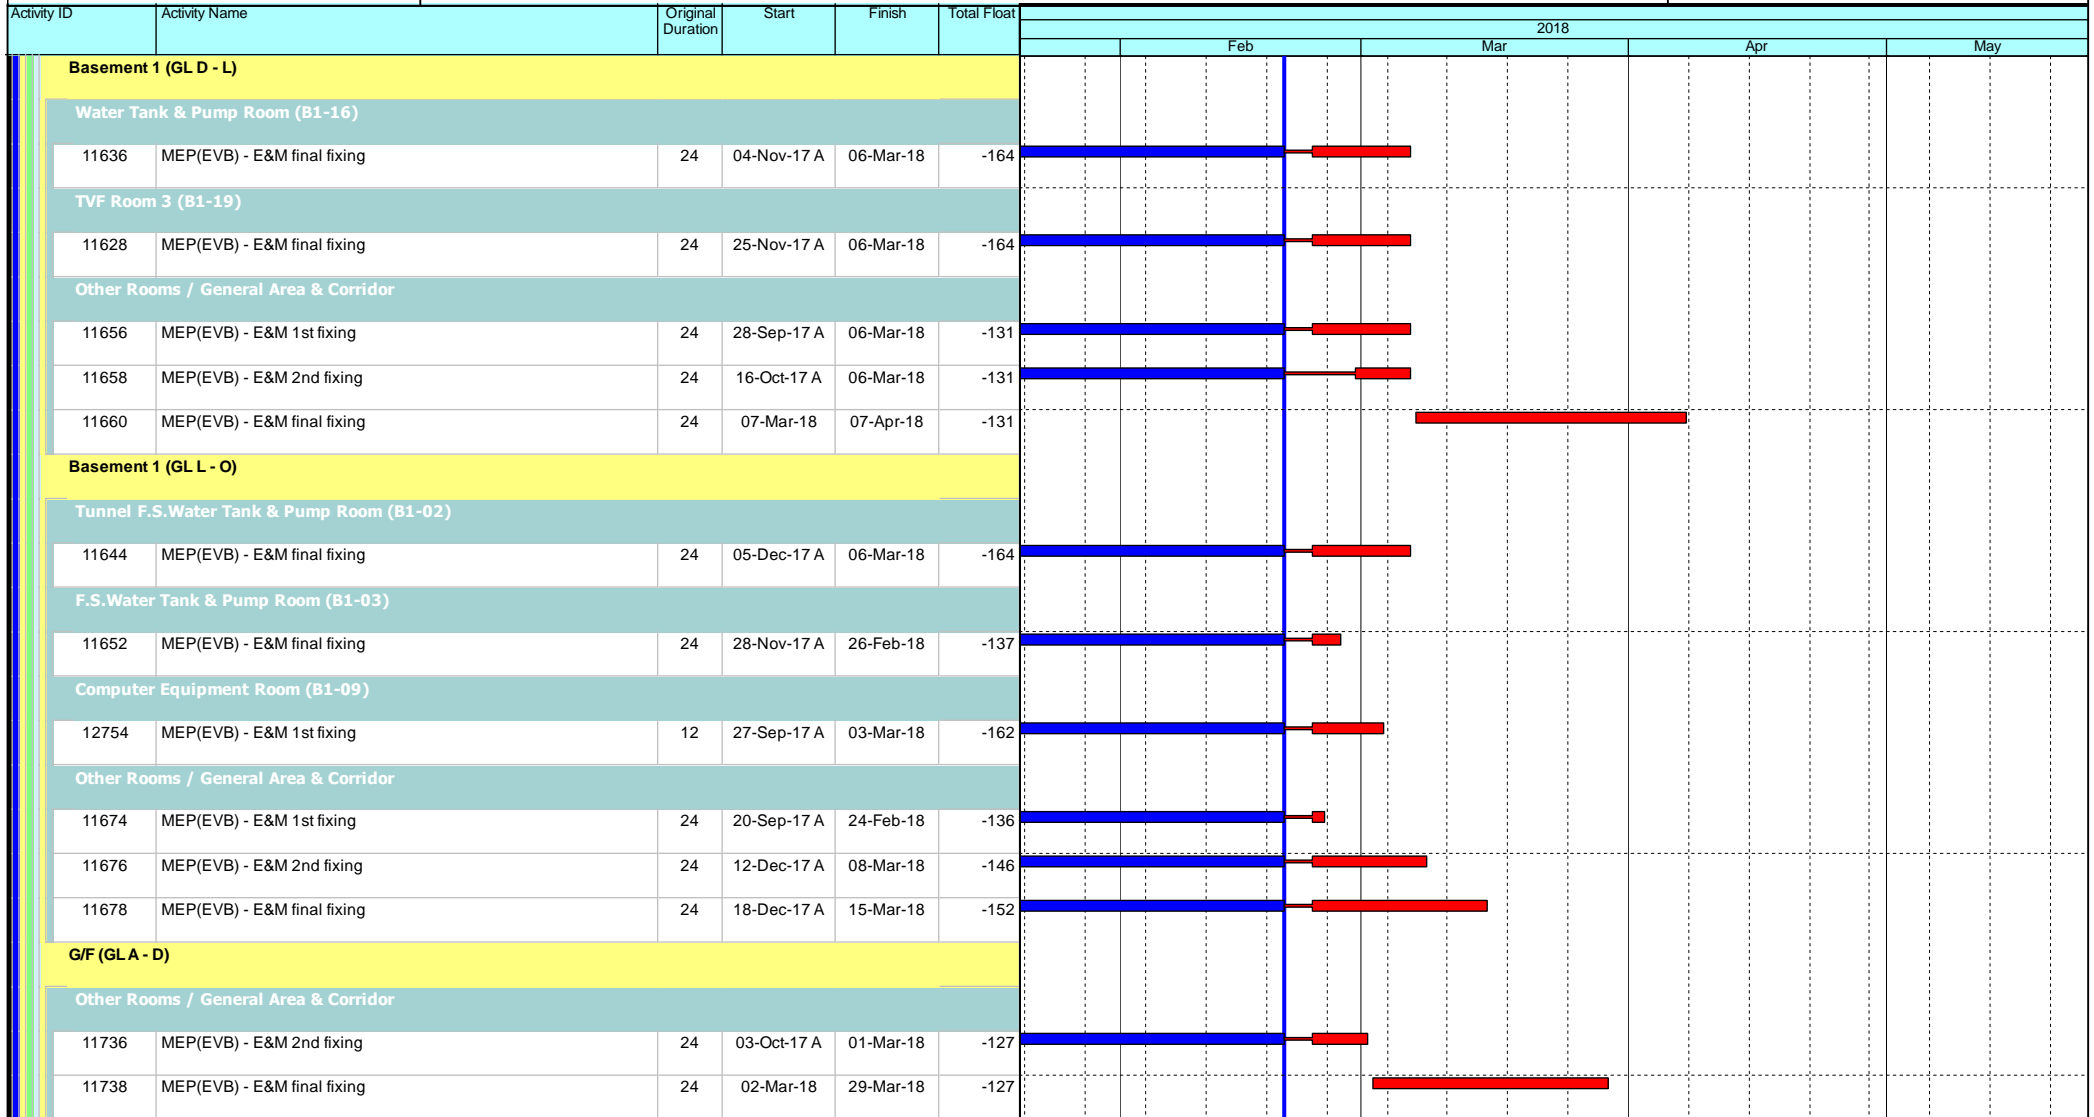

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 29 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

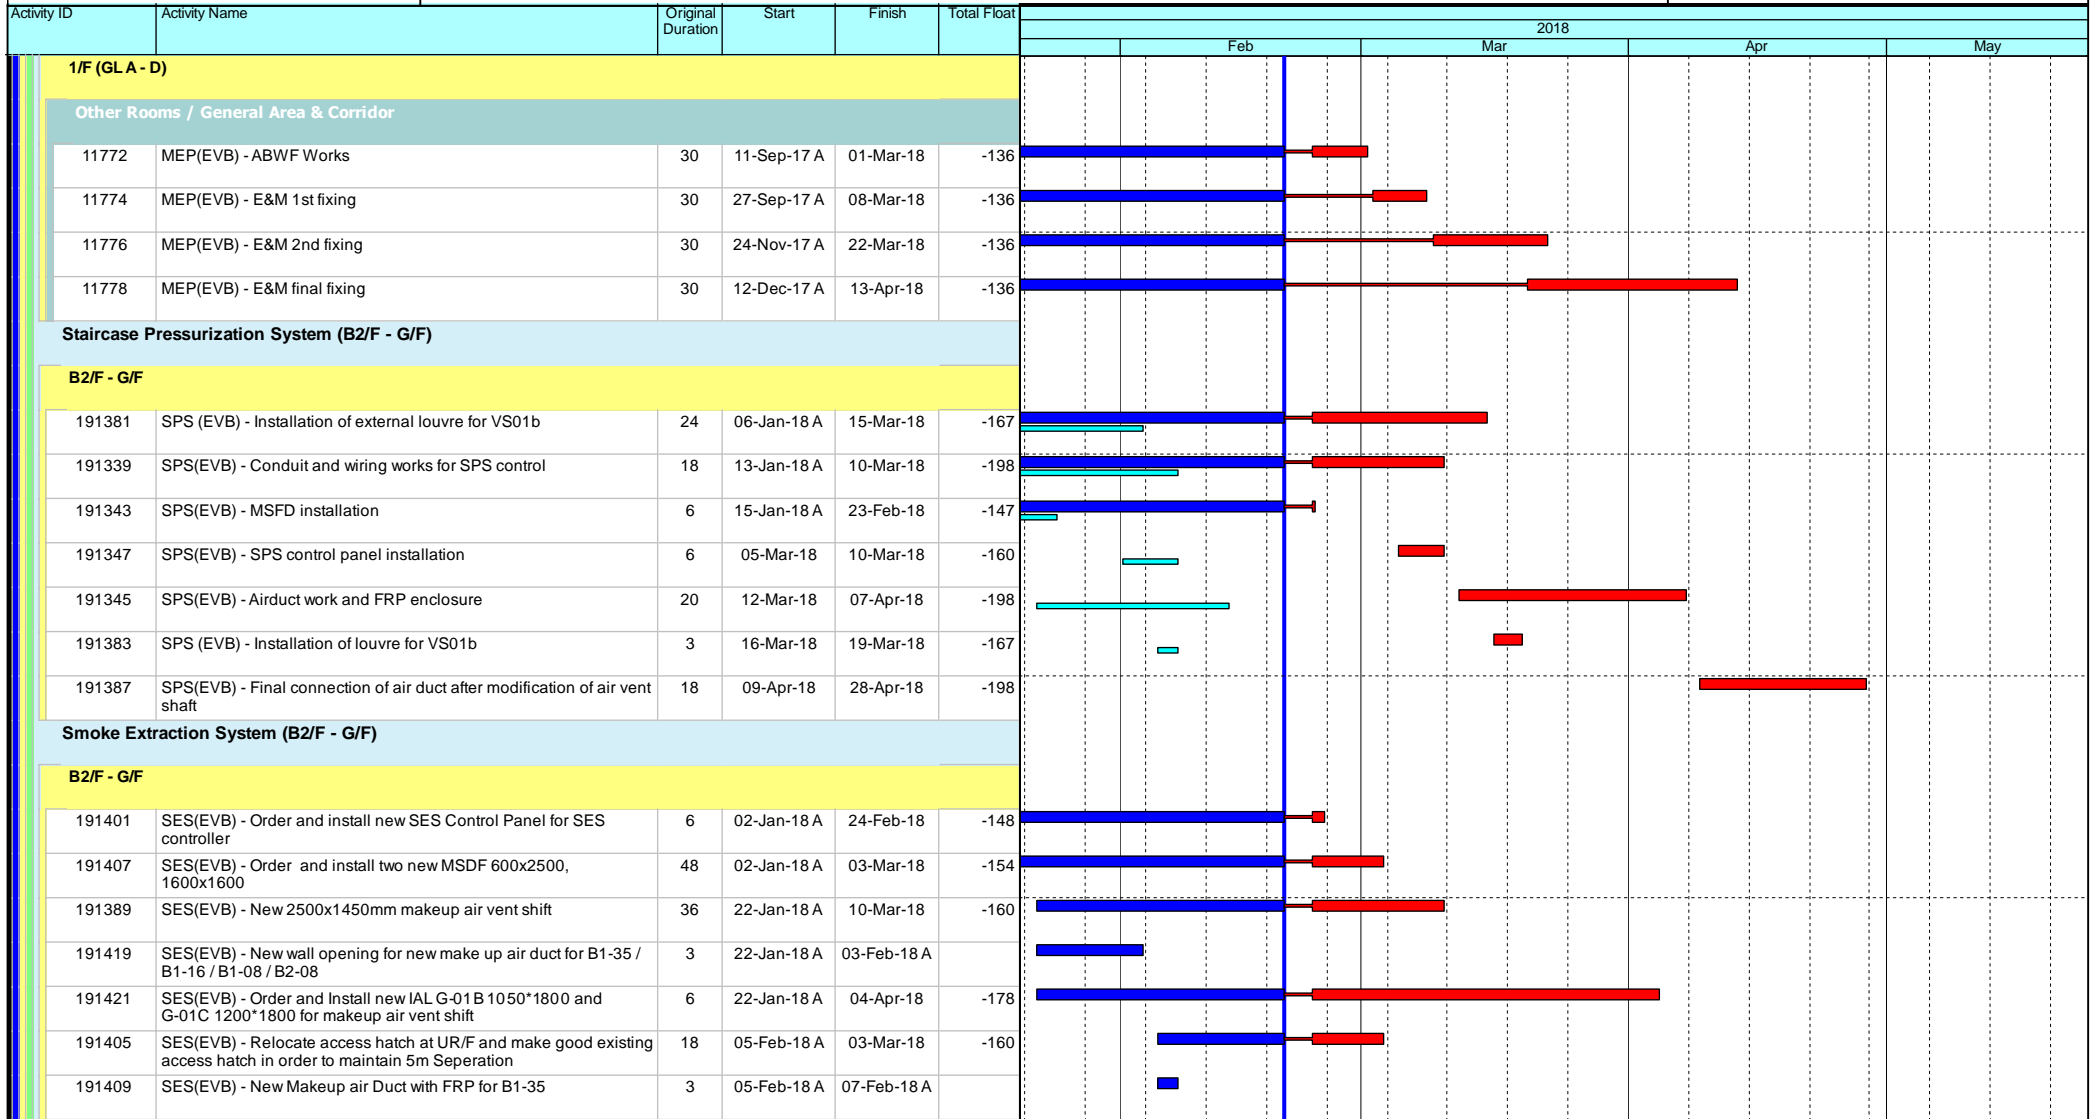

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 30 of 43



Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW



Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

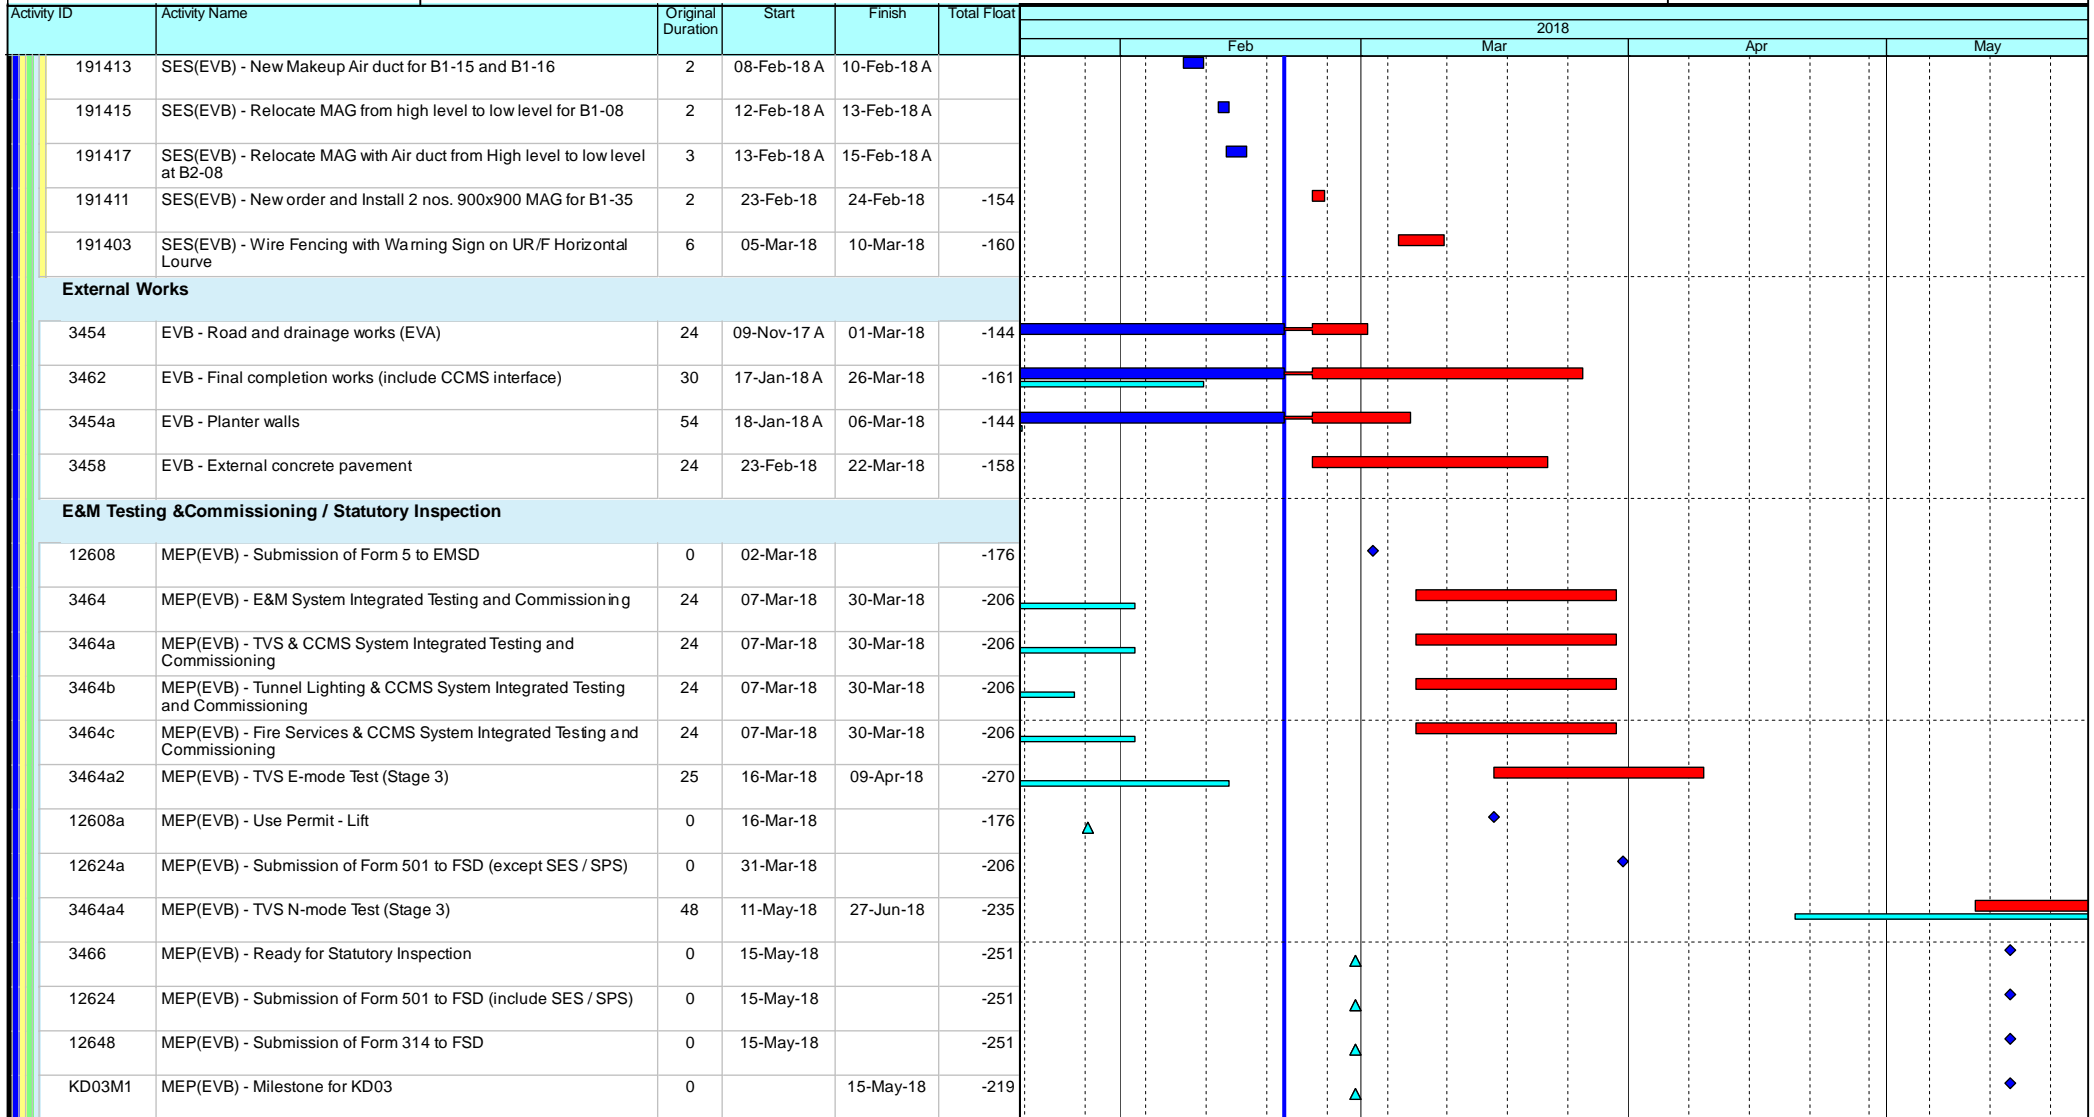

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 31 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

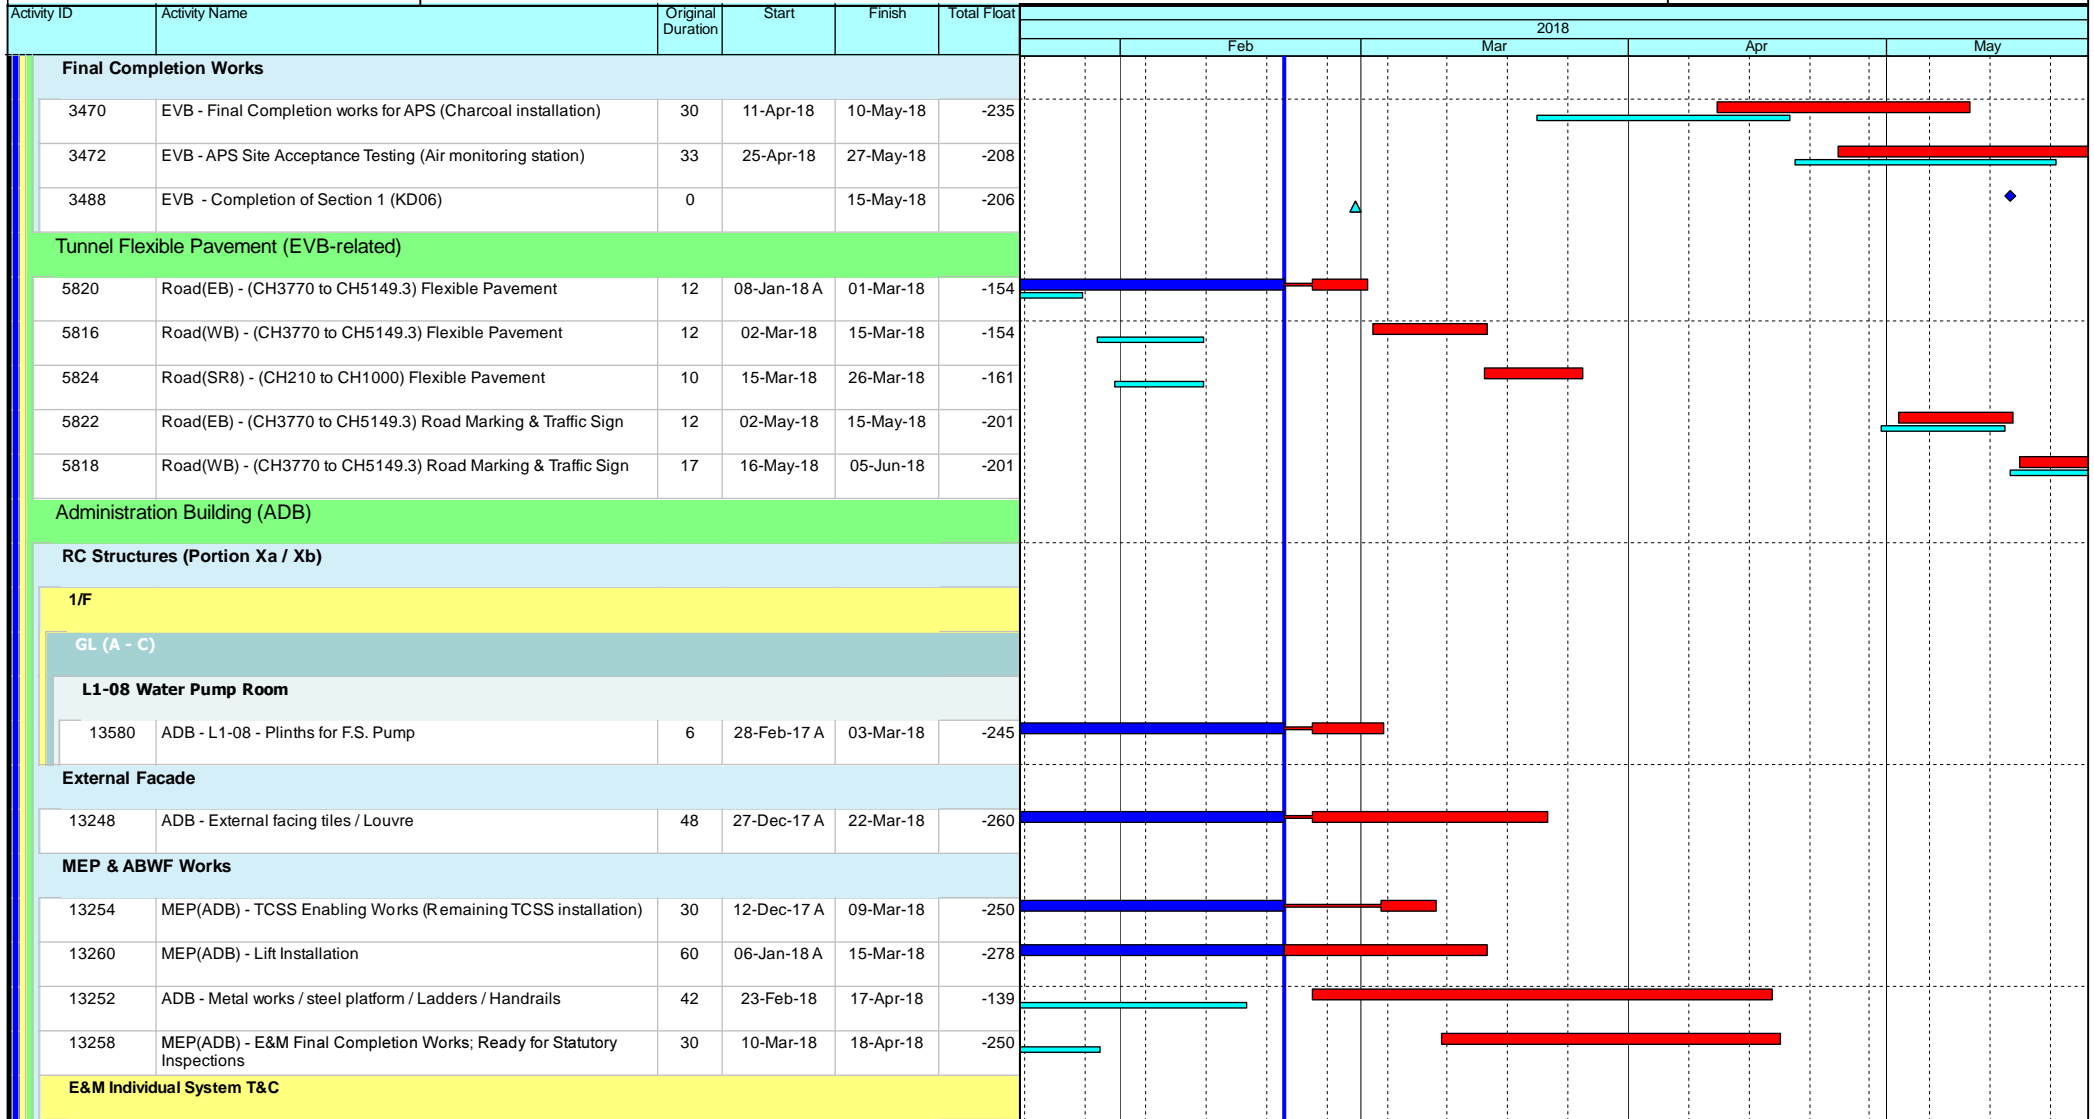

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 32 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

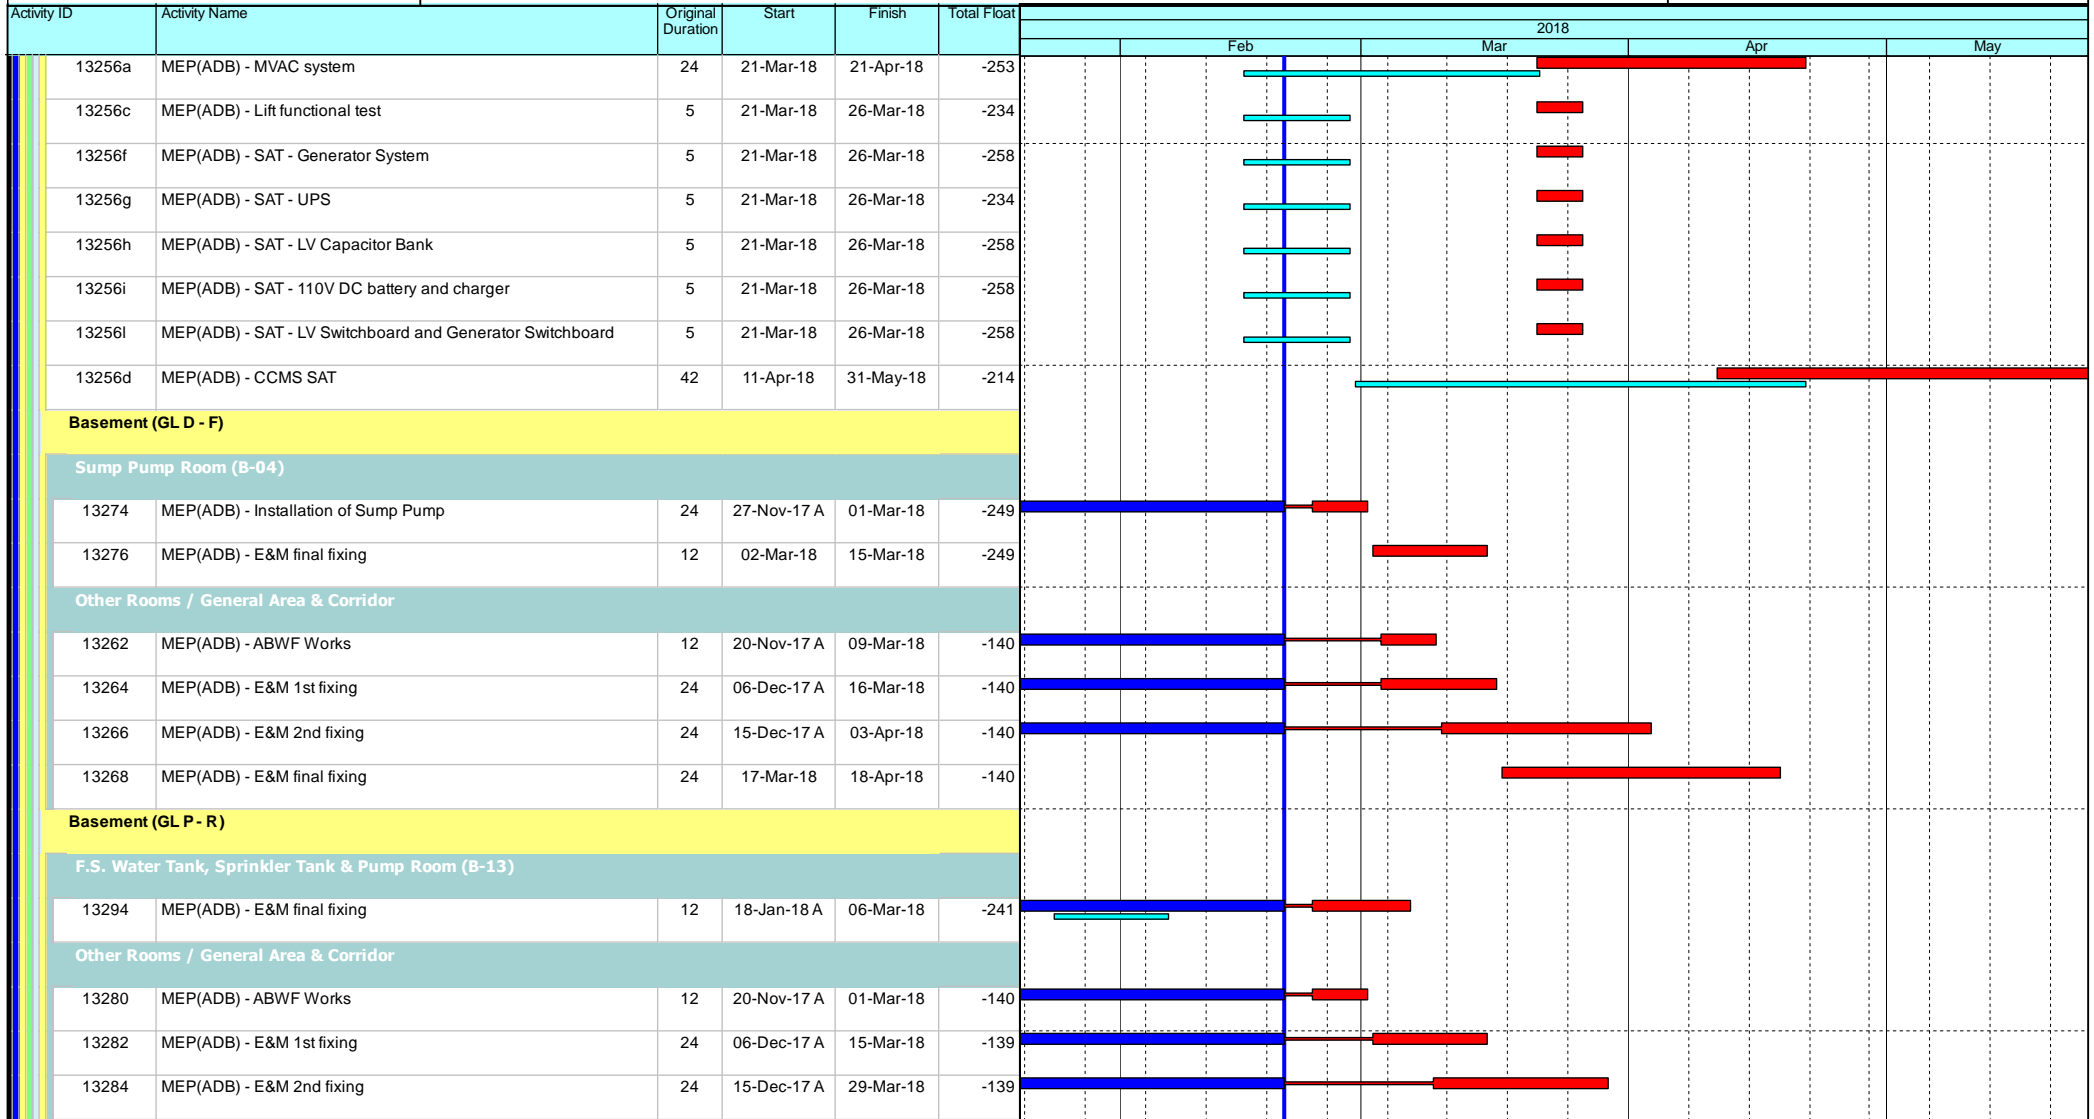

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 33 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

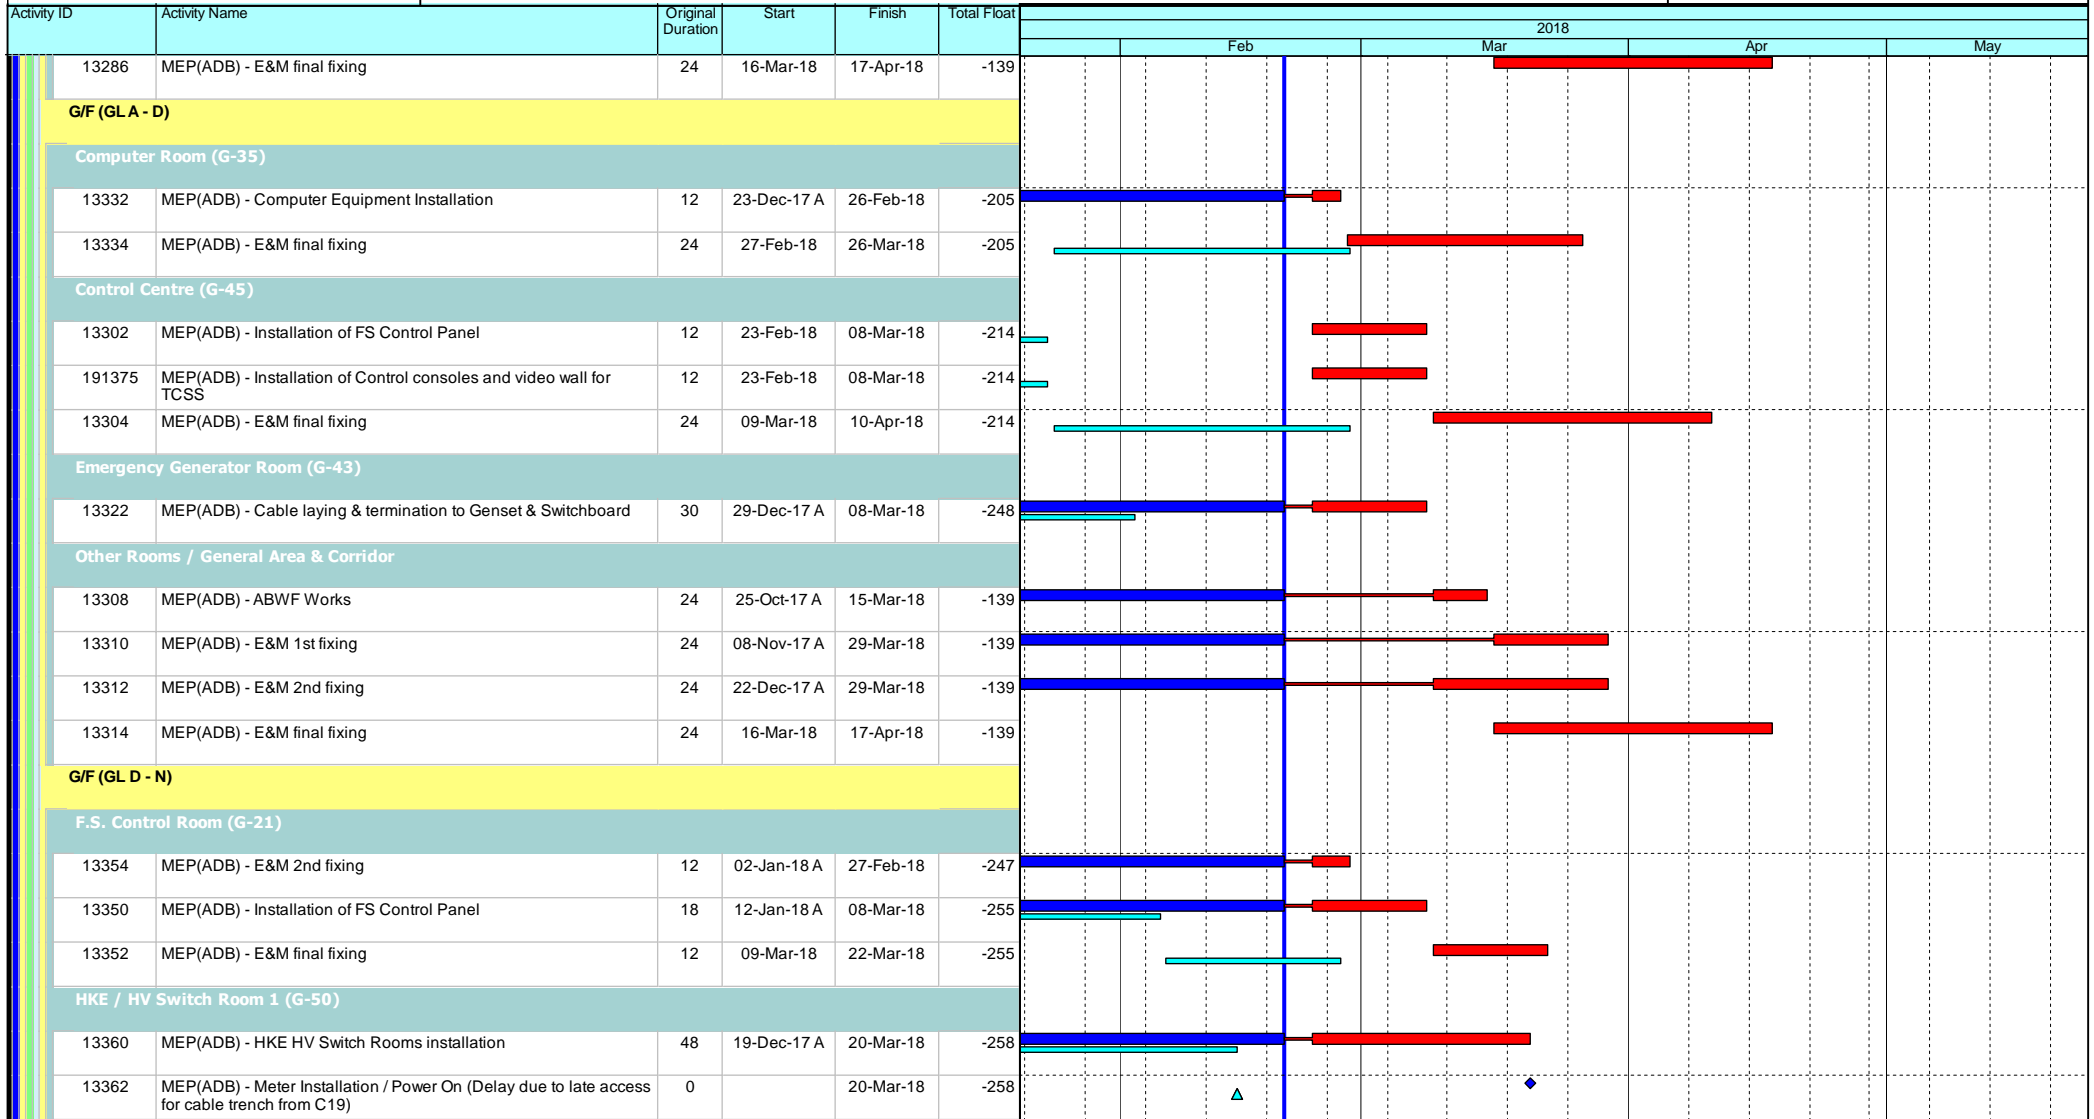

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 34 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

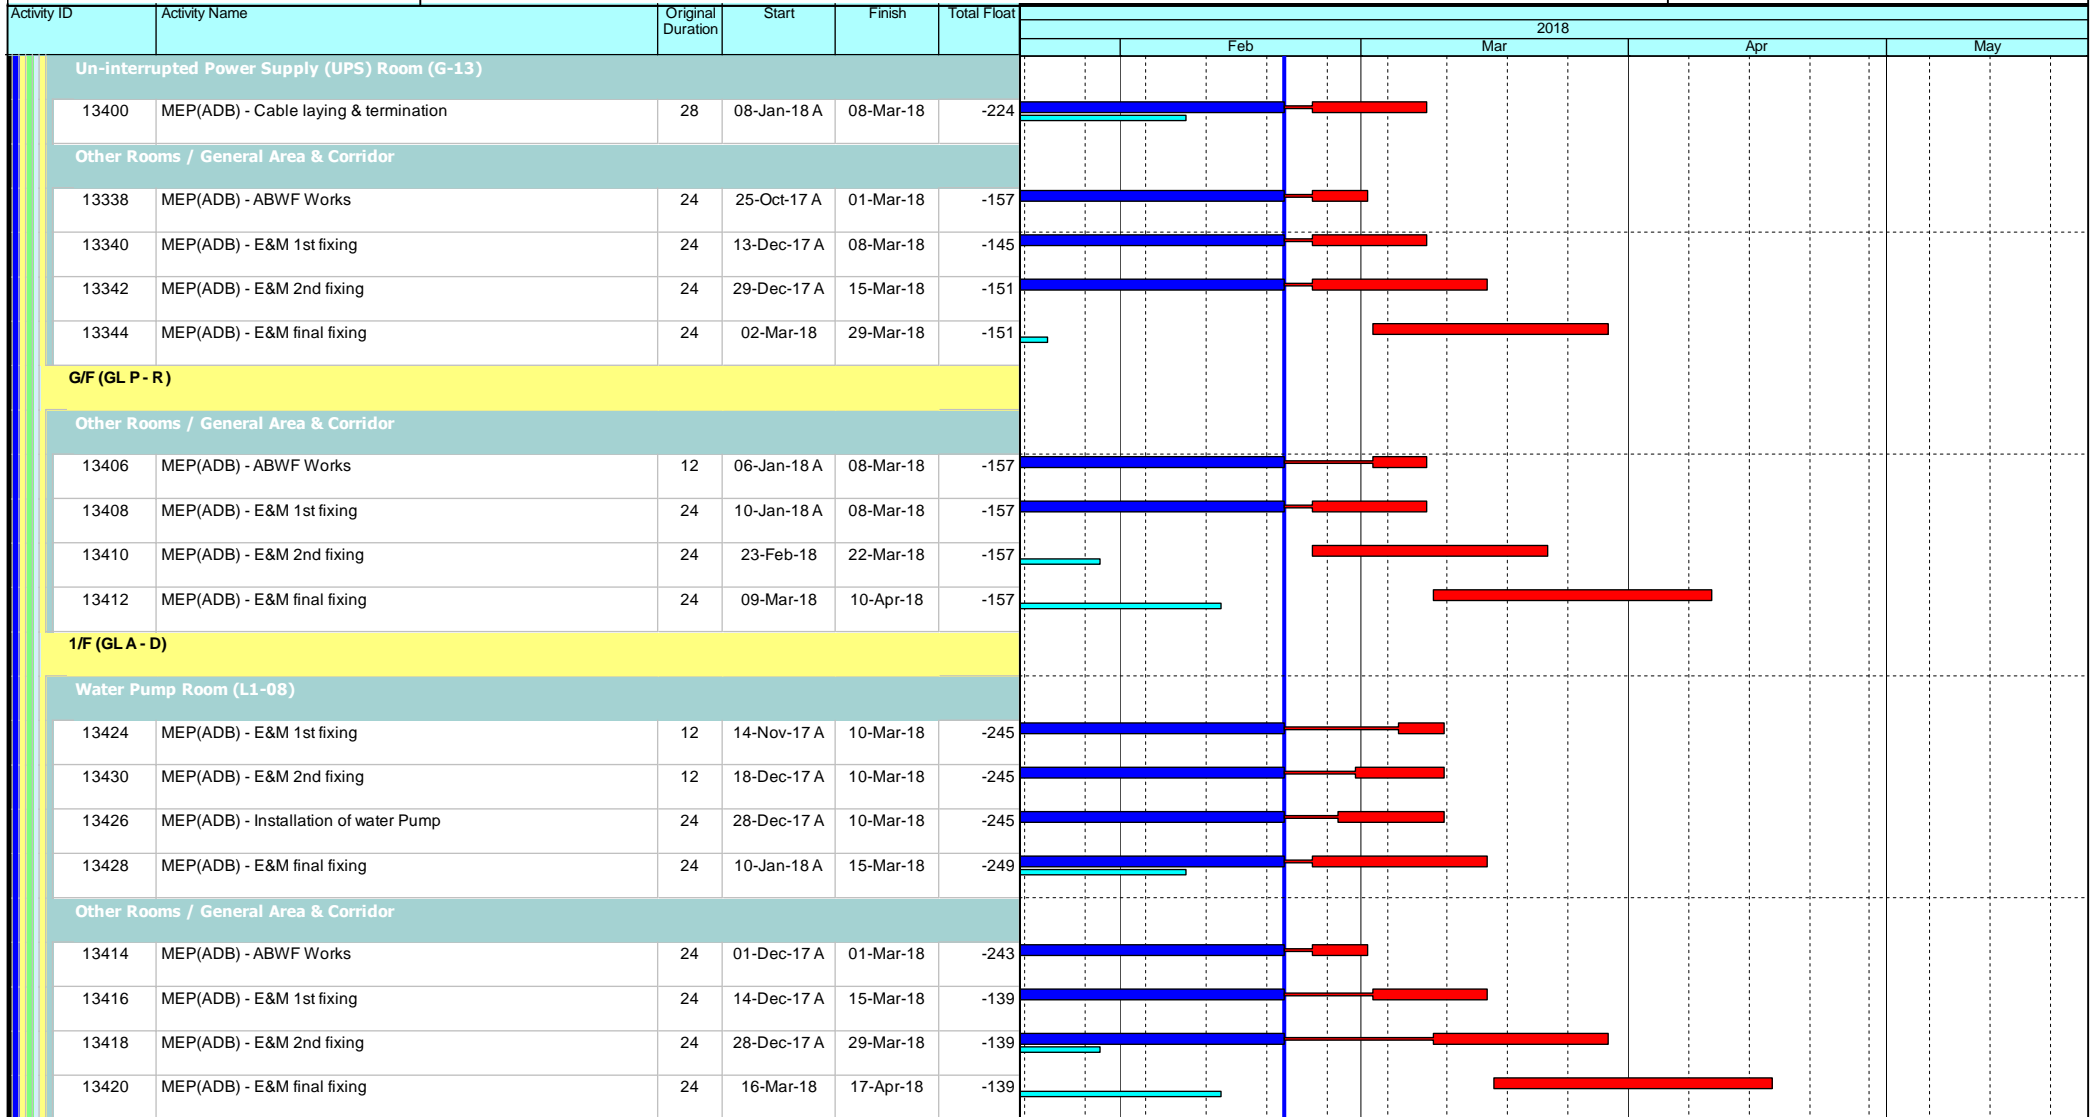

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
Baseline: SA01  
Layout: Update Three Month Rolling  
U048  
Page 35 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

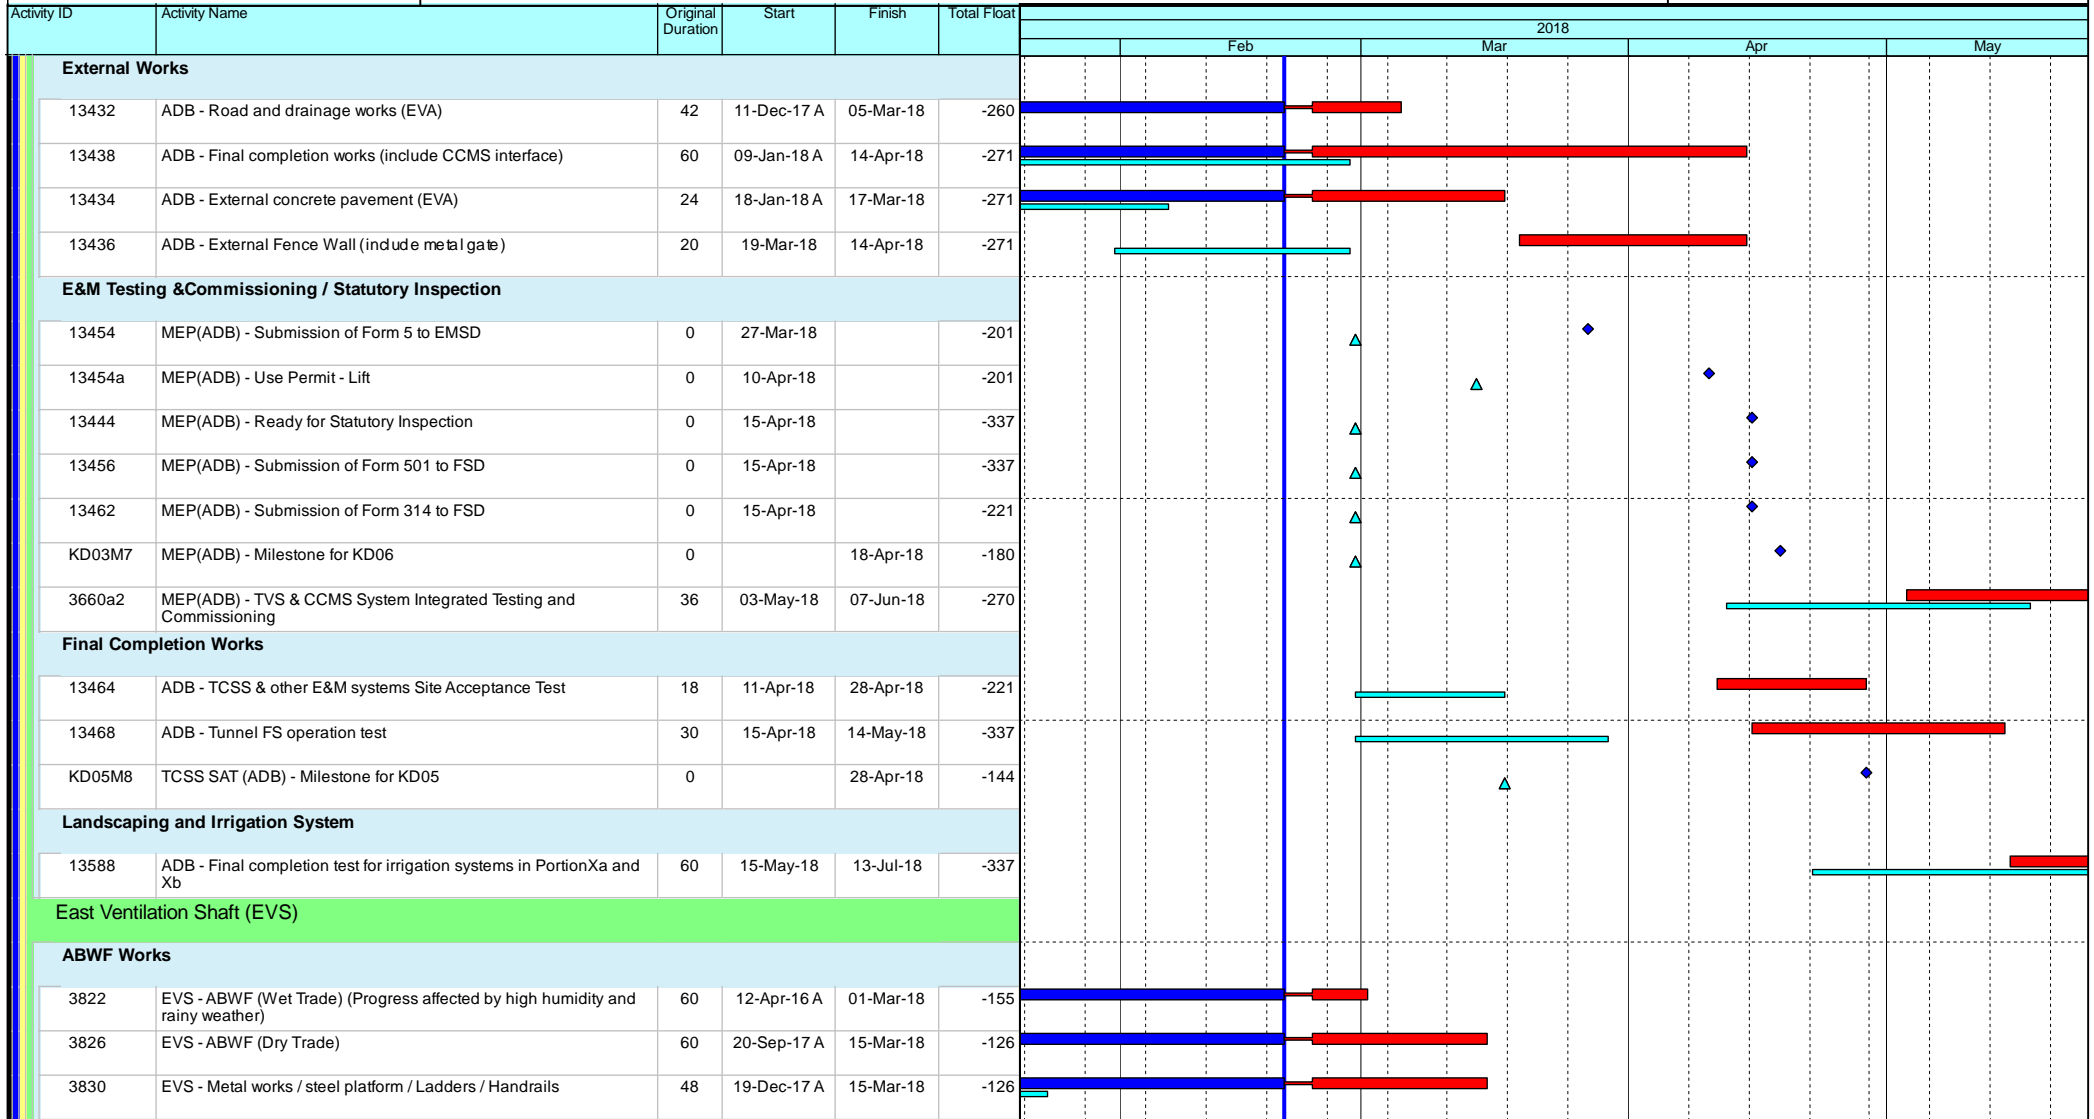

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 36 of 43



Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW



Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

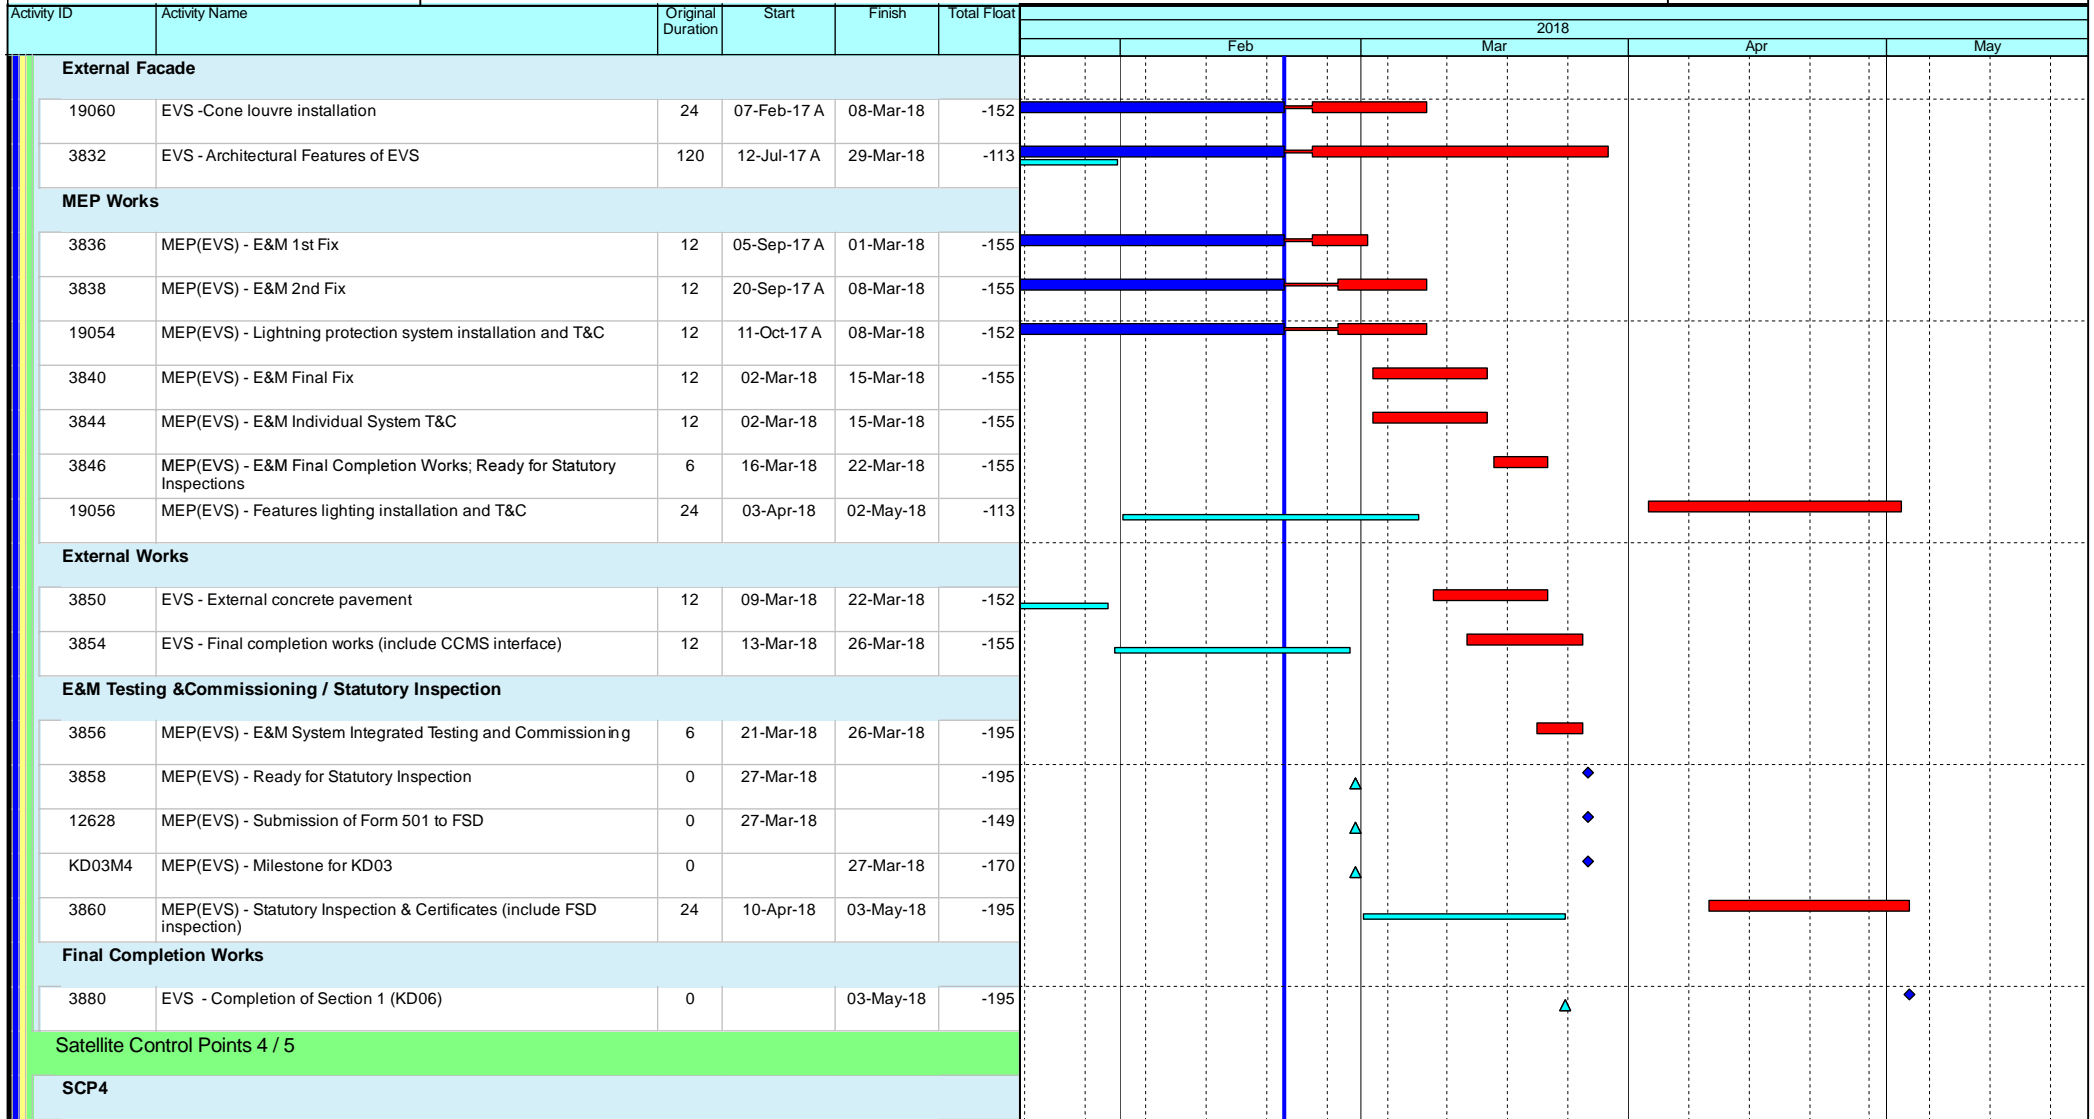

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 37 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Feb	Mar	Apr	May
3778	SCP4 - Initial Site Survey	6	23-Feb-18	01-Mar-18	-196				
3778a	SCP4 - Construction details from AECOM	0	23-Feb-18*		-196				
3780	SCP4 - Erect Hoarding	6	02-Mar-18	08-Mar-18	-196				
3782	SCP4 - Mobilisation and setup	12	09-Mar-18	22-Mar-18	-196				
3784	SCP4 - Construct SCP RC Structures	24	23-Mar-18	24-Apr-18	-196				
3786	SCP4 - ABWF Works	24	25-Apr-18	24-May-18	-196				
3798	SCP4 - External Works	24	25-Apr-18	24-May-18	-143				
3788	MEP(SCP4) - E&M 1st Fix	18	27-Apr-18	18-May-18	-196				
10112	MEP(SCP4) - TCSS Enabling Works (Remaining TCSS installation)	18	27-Apr-18	18-May-18	-196				
3790	MEP(SCP4) - E&M 2nd Fix	18	08-May-18	29-May-18	-155				
3824	SCP4 - Metal works / Glazing / Louver / Handrails	18	10-May-18	31-May-18	-149				
3792	MEP(SCP4) - E&M Final Fix	18	17-May-18	07-Jun-18	-155				
<b>SCP5</b>									
3828	SCP5 - Mobilization for Area B	0	23-Feb-18		-207				
3848	SCP5 - Initial Site Survey	6	23-Feb-18	01-Mar-18	-207				
3827	C19 allow access for SCP5 construction	0	23-Feb-18*		-207				
3827a	Construction details from AECOM	0	23-Feb-18*		168				
3852	SCP5 - Erect Hoarding	4	02-Mar-18	06-Mar-18	-207				
3868	SCP5 - Mobilisation and setup	2	07-Mar-18	08-Mar-18	-207				
3870a	SCP5 - Construct walls upto R/F - Falseworks & Formwork	4	09-Mar-18	13-Mar-18	-207				
3870b	SCP5 - Construct walls upto R/F - Rebar fixing	3	14-Mar-18	16-Mar-18	-207				
3870c	SCP5 - Construct walls upto R/F - Close formwork	4	17-Mar-18	21-Mar-18	-207				
3870d	SCP5 - Construct beams & slab upto R/F - Scaffolding, falsework & formwork	4	22-Mar-18	26-Mar-18	-207				
3870e	SCP5 - Construct beams & slab upto R/F - Rebar fixing	3	27-Mar-18	29-Mar-18	-207				

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 38 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

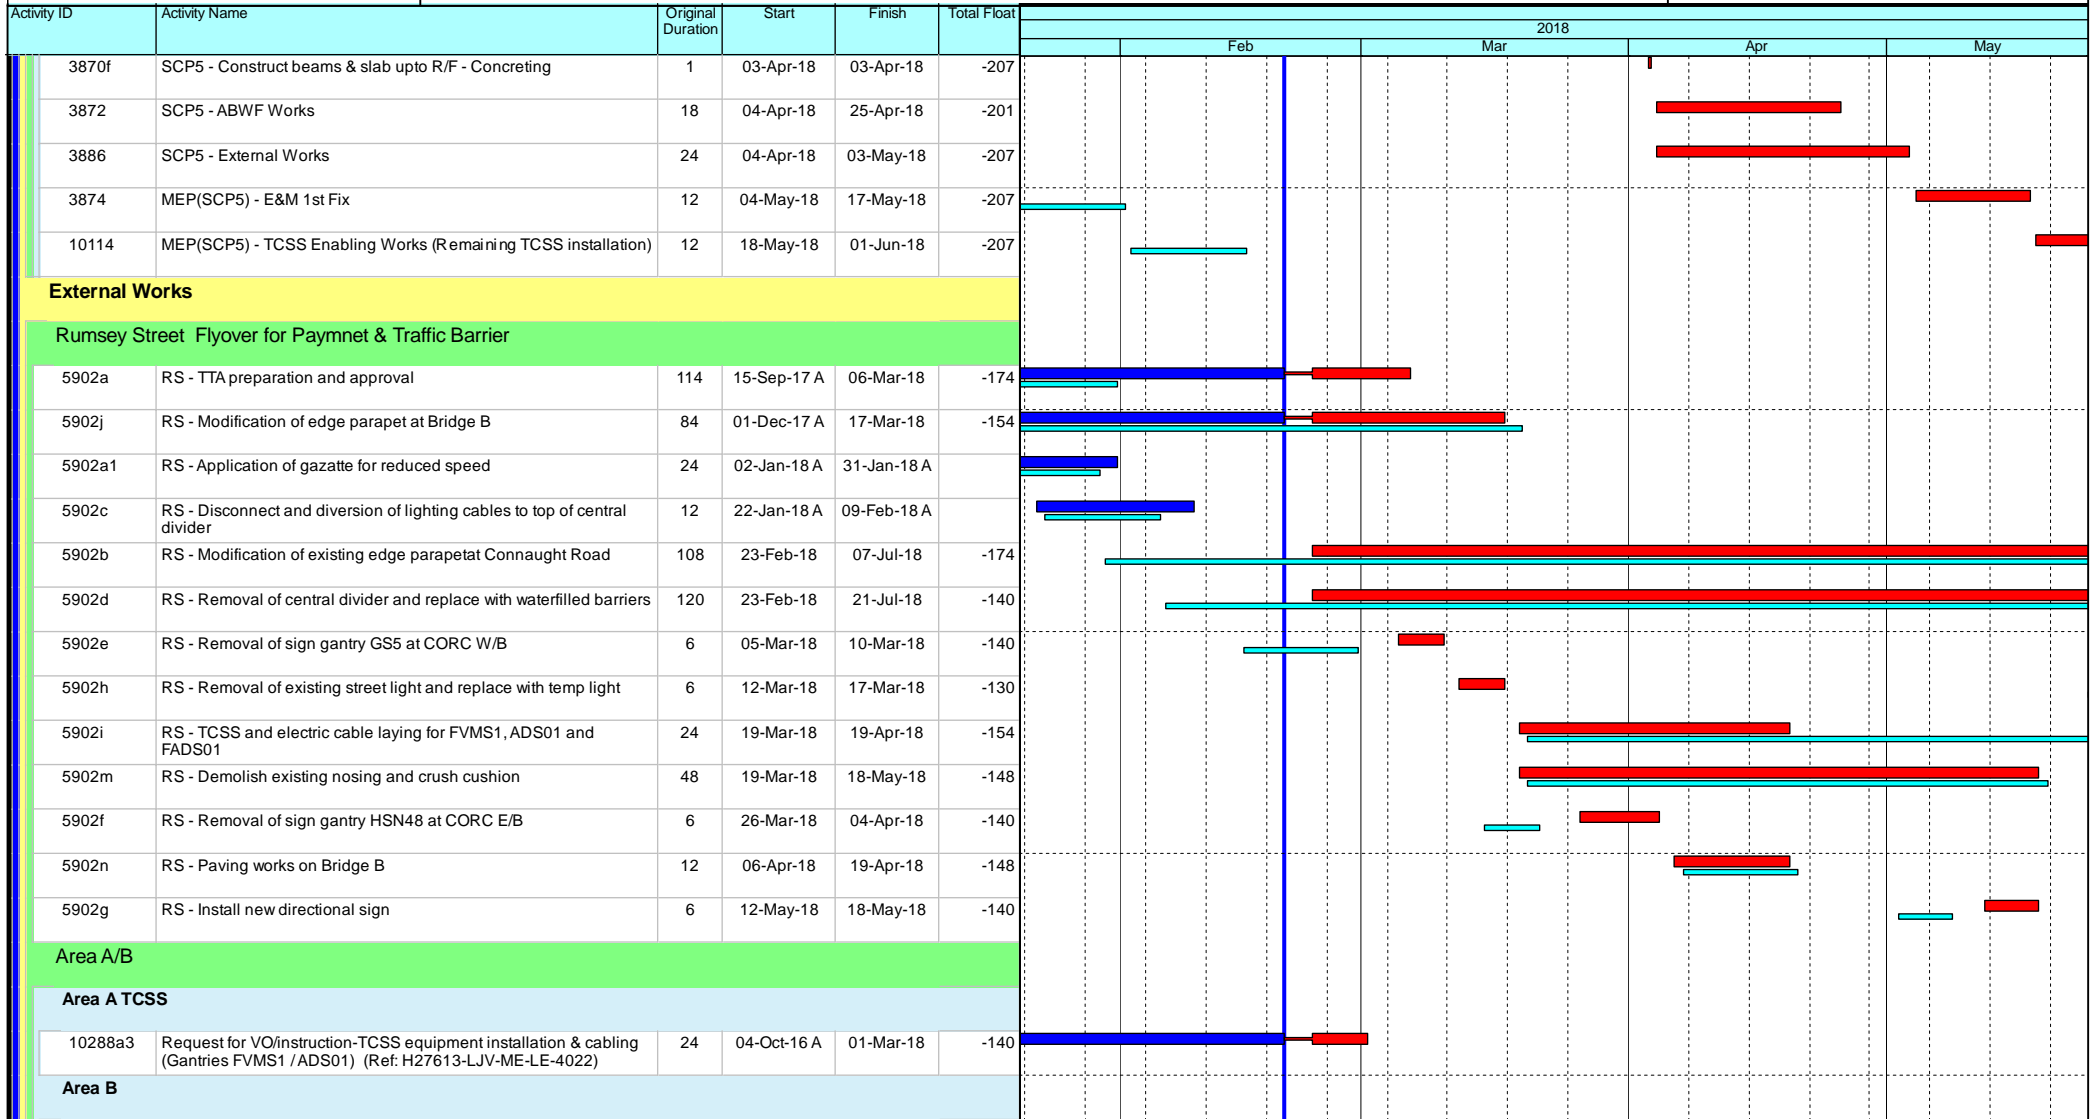

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 39 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

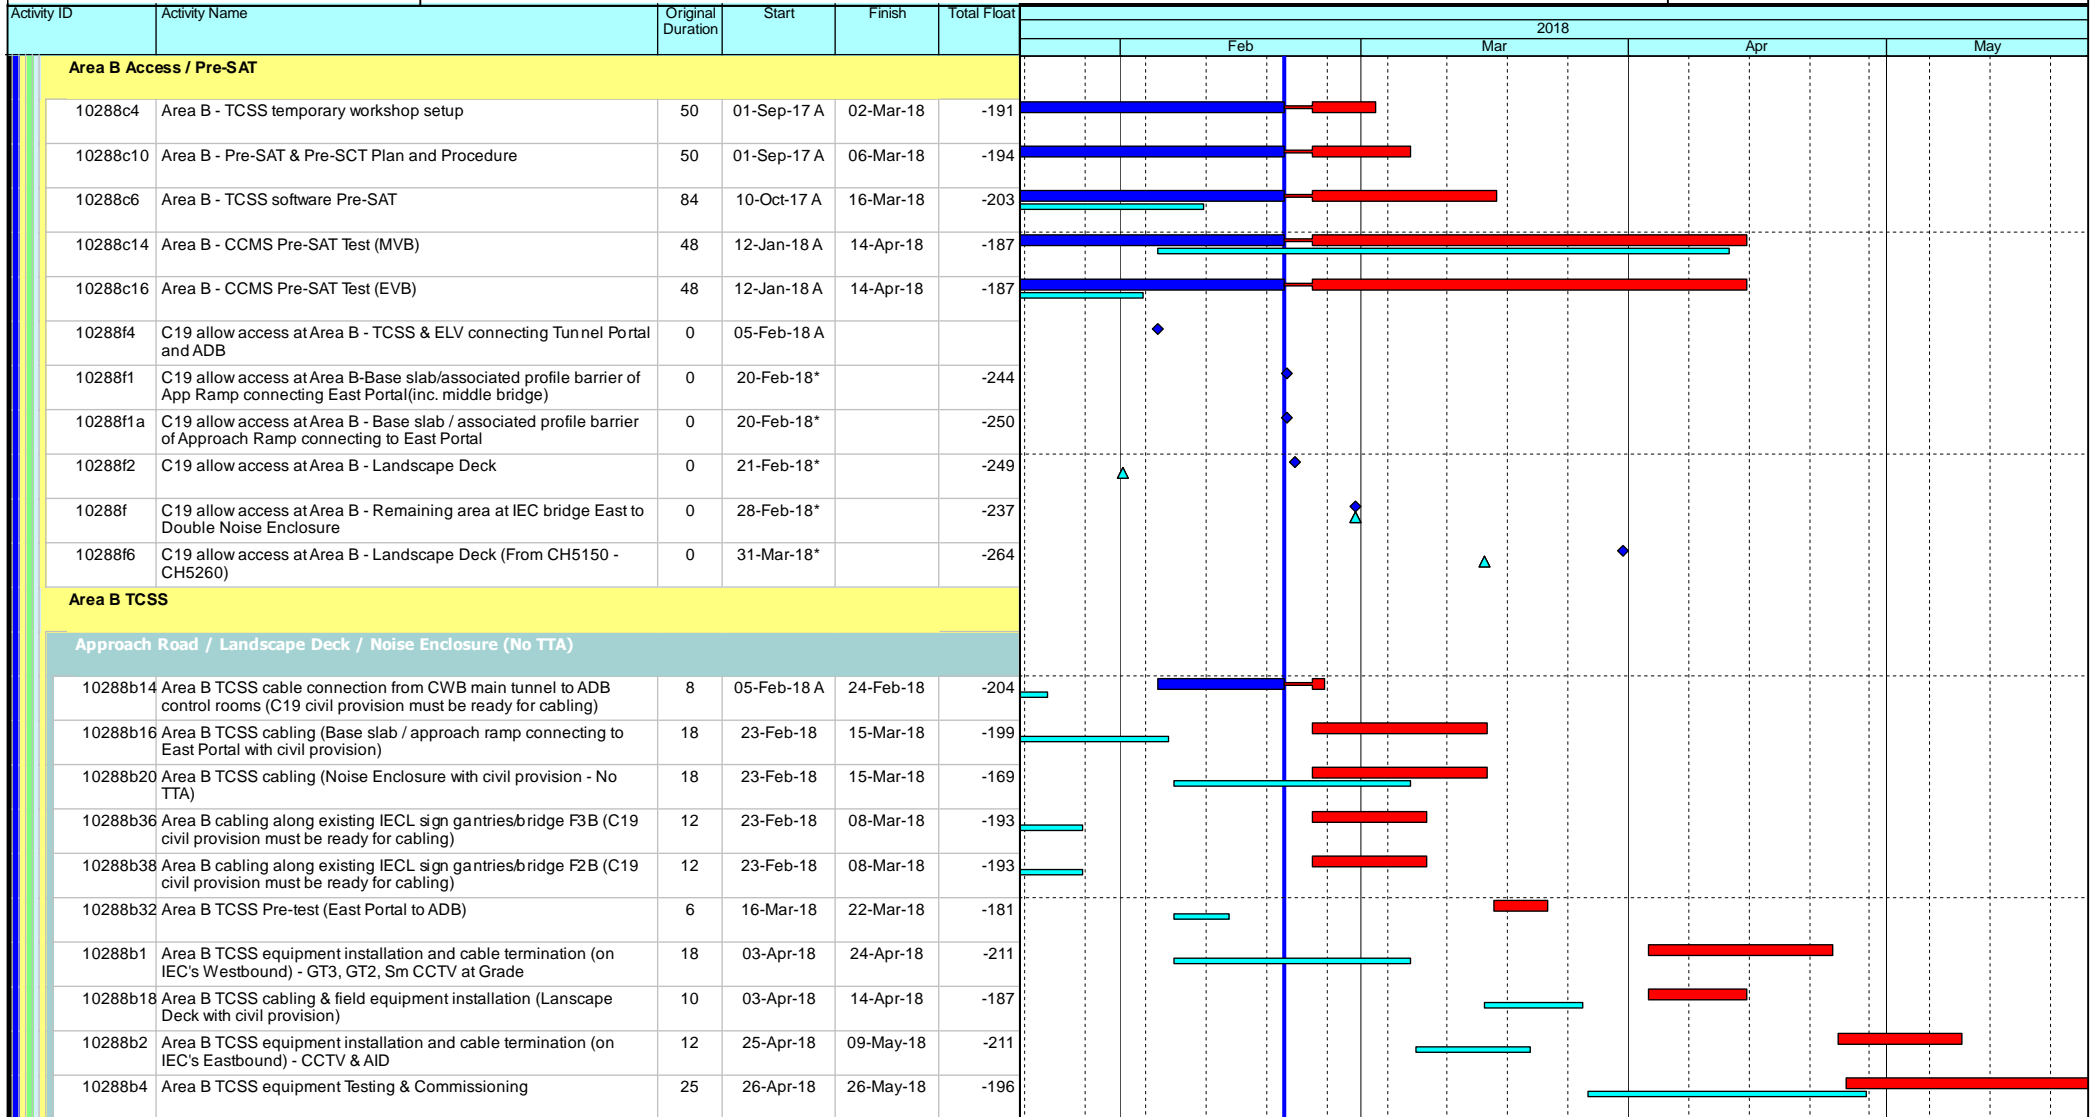

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 40 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Feb	Mar	Apr	May
10288b22	Area B TCSS equipment installation and cable termination (on IEC's Westbound) - DS06B	9	10-May-18	19-May-18	-211				
<b>Noise Enclosure (Live Traffic, TTA) - Night Shift</b>									
10288b6b	Area B FADS06 sign face installation	4	02-Apr-18*	05-Apr-18	-249				
10288b6	Area B TCSS equipment installation and cable termination (on IEC's Westbound) - FADS06	10	06-Apr-18	17-Apr-18	-198				
10288b6c	Area B DS06A sign face installation	1	15-Apr-18*	15-Apr-18	-255				
10288b6a	Area B TCSS equipment installation and cable termination (on IEC's Westbound) - DS06A	6	16-Apr-18	21-Apr-18	-202				
10288b10	Area B TCSS equipment installation and cable termination (on IEC's Eastbound) - FADS08A	6	18-Apr-18	24-Apr-18	-190				
10288b8	Area B TCSS equipment Testing & Commissioning	20	23-Apr-18	16-May-18	-202				
<b>Existing IEC (Live Traffic, TTA) - Night Shift</b>									
10288b24	ADS06 A-frame and main beam completion by C19	0		18-Mar-18*	-231				
10288b30	Area B TCSS cabling (Existing IEC with civil provision)	24	19-Mar-18	19-Apr-18	-186				
10288b24	Area B TCSS equipment installation and cable termination (on IEC's Westbound) - ADS06	10	19-Mar-18	29-Mar-18	-166				
10288b24	Area B TCSS equipment installation and cable termination (on IEC's Westbound) - VMS7	14	25-Apr-18	11-May-18	-190				
10288b26	Area B TCSS equipment Testing & Commissioning	12	17-May-18	31-May-18	-202				
<b>Area B Tunnel Lighting</b>									
<b>Landscape Deck</b>									
10288c1	Area B Tunnel Lighting (Landscape Deck) - Brackets / Cable Containment / Conduit / Junction Box installation	18	23-Feb-18	15-Mar-18	-202				
10288d2	Area B Tunnel Lighting (Landscape Deck) - Bracket installation (Cable Trench)	18	23-Feb-18	15-Mar-18	-202				
10288d3	Area B Tunnel Lighting (Landscape Deck) - Cable laying (Cable Trench)	24	03-Apr-18	02-May-18	-191				
10288c8	Area B Tunnel Lighting (Landscape Deck) - Brackets/Cable Containment/Conduit/Junction Box installation (CH5150-CH5260)	30	03-Apr-18	09-May-18	-214				
10288c2	Area B Tunnel Lighting (Landscape Deck) - Tunnel Lighting installation (Base / Reinforcement lighting)	34	13-Apr-18	24-May-18	-214				
10288d1	Area B Tunnel Lighting (Landscape Deck) - Cable laying / Control cable wiring (High Level)	42	21-Apr-18	11-Jun-18	-214				
10288d5	Area B Tunnel Lighting (Landscape Deck) - Cable termination (Cable Trench)	17	03-May-18	23-May-18	-191				
10288d4	Area B Tunnel Lighting (Landscape Deck) - Cable termination (High Level)	38	05-May-18	20-Jun-18	-214				

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING



Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 41 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.

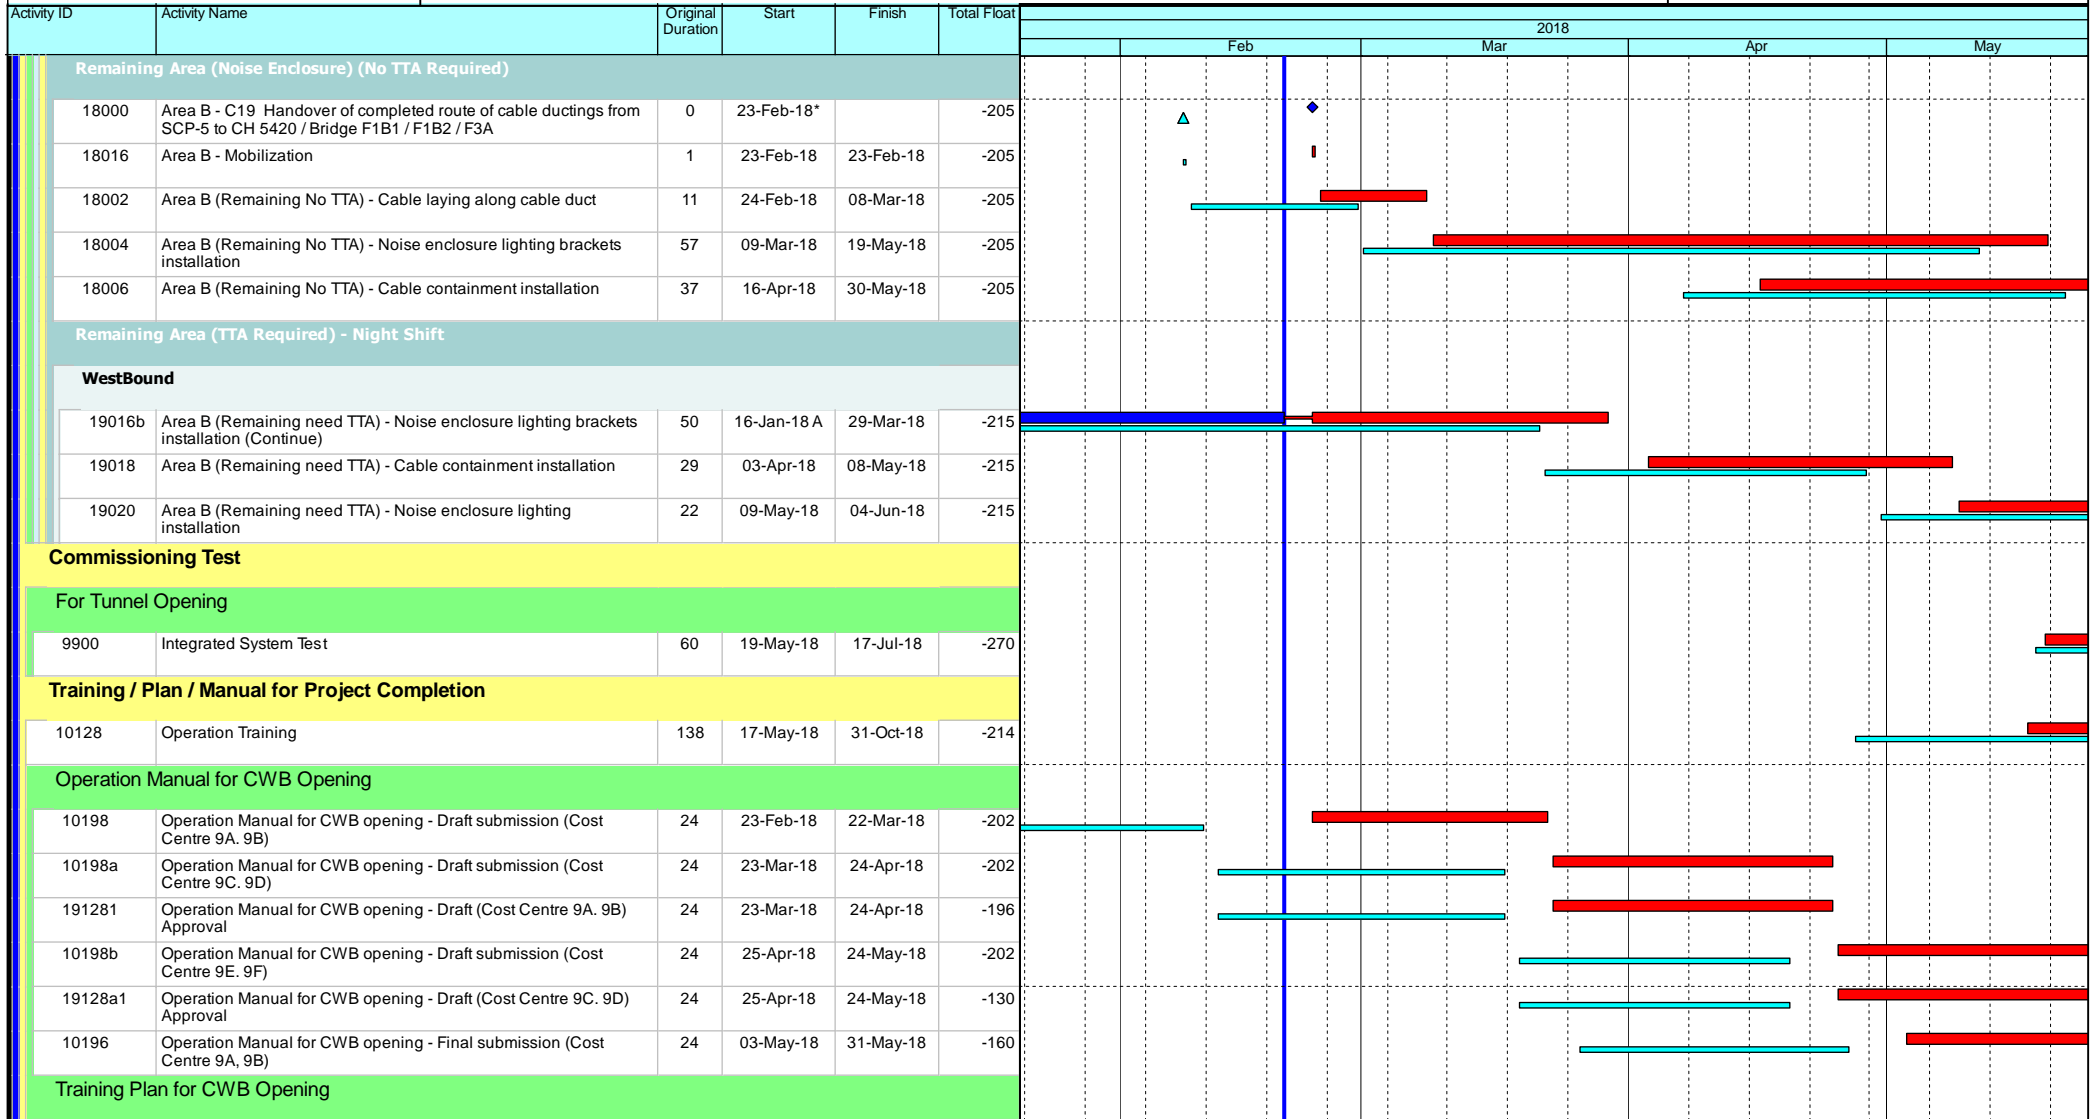

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048  
Baseline: SA01  
Layout: Update Three Month Rolling  
U048  
Page 42 of 43


Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW



Data Date: 20-Feb-18

## CWB(CC) - Commissioning Contract

**TASK filters: 3 Months\_4, 3MRP, No Original Sections, No Summary, Not HL.**

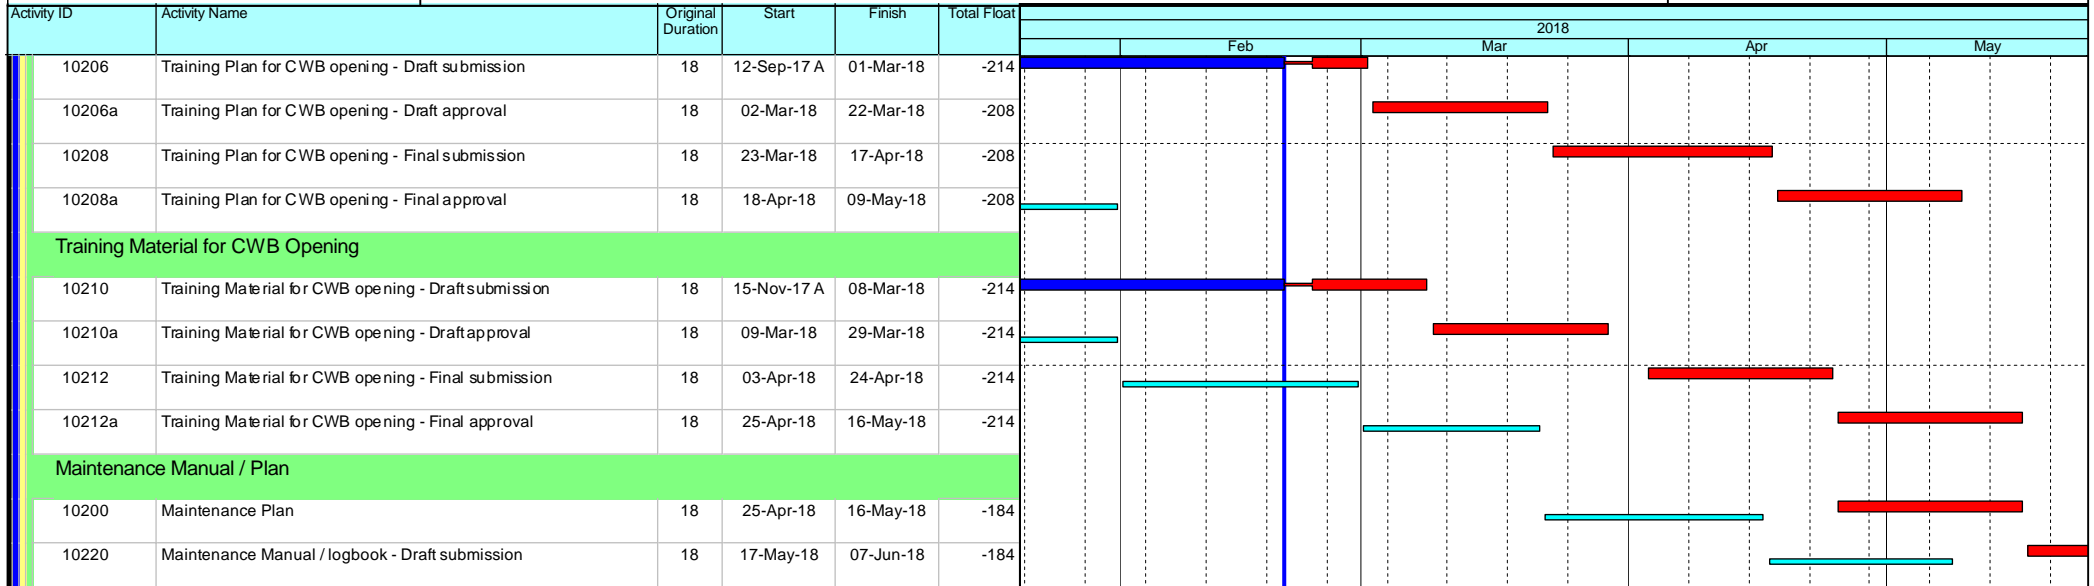

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048  
 Baseline: SA01  
 Layout: Update Three Month Rolling  
 U048  
 Page 43 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW
