


Contract No. HK/2009/01

Wan Chai Development Phase II – Central -Wan Chai Bypass at
Hong Kong Convention and Exhibition Centre


Construction Activities for Three Months Rolling

Construction Activities	January 2018	February 2018	March 2018
Reinstatement of Amenity Area			

Contract No. HK/2009/01

Wan Chai Development Phase II – Central -Wan Chai Bypass at
Hong Kong Convention and Exhibition Centre

Construction Activities for Three Months Rolling

Construction Activities	April 2018	May 2018	June 2018
Reinstatement of Amenity Area			

**CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2018			
					Apr	May	Jun	Jul
HK/2012/08 Revised Works Programme Rev.12.0(DD 20 November 2017)								
Dredging and Reclamation								
Marine Work Construction								
Zone D								
Seawall Construction - Zone D								
Seawall 10 & 11								
MAR20630	Zone D - Seawall 10 & 11: Install remaining seawall block	14	04-Apr-18*	17-Apr-18				
MAR20650	Zone D - Seawall 10 & 11: Backfill Type A	7	18-Apr-18	24-Apr-18				
MAR20670	Zone D - Seawall 10 & 11: Lay geotextile and filter	7	25-Apr-18	01-May-18				
Works for Section Completion								
Construction								
Section III A - Road A2, A4 & A5								
Roadwork & Utilities - Section 1 (L1806 - L1801)								
SIIIA10310b	Sec III A - section 1 carriageway - TTA stage 5: remaining sewerage pipe for M/H F8A - M/H F8B	18	20-Mar-18	13-Apr-18				
SIIIA10310e	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road -construct upstand wall above Dwall	25	10-Apr-18	09-May-18				
SIIIA10310f	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - roadside barrier	14	10-May-18	26-May-18				
SIIIA10310g	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - road formation	7	28-May-18	04-Jun-18				
SIIIA10310h	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - laying asphalt with transition slab	14	05-Jun-18	21-Jun-18				
SIIIA10312a	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L1805 - L1801)	15	23-Mar-18	13-Apr-18				
SIIIA10312b	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L1805-1807)	12	14-Apr-18	27-Apr-18				
SIIIA10313	Sec III A - roadwork and utilities section 1 carriageway - gully pipe (L1807 - L1801)	14	23-Apr-18	09-May-18				
SIIIA10320	Sec III A - roadwork and utilities section 1 carriageway - fresh watermain	7	10-May-18	17-May-18				
SIIIA10340	Sec III A - roadwork and utilities section 1 carriageway - utilities: HEC (80m) along carriageway	14	18-May-18	04-Jun-18				
SIIIA10360	Sec III A - roadwork and utilities section 1 carriageway - road kerb & formation	14	05-Jun-18	21-Jun-18				
Roadwork & Utilities - Section 6 (L1102 - L1411)								
SIIIA13470	Sec III A - roadwork and utilities section 6 carriageway - black top	7	28-Mar-18	09-Apr-18				
Section V - Remaining At-Grade Road & Road P2								
Roadwork & Utilities								
Section 2 (L1510 - L1504)								
SV12700	Sec V - Roadwork & Utilities Section 2 footpath - utilities: TCSS	16	20-Mar-18	11-Apr-18				
SV12740	Sec V - Roadwork & Utilities Section 2 footpath - paving block	18	12-Apr-18	03-May-18				
Section 3 (Culvert L - L1510)								
SIV12880	Sec V - Roadwork & Utilities Section 3 footpath - Paving block	21	27-Mar-18	24-Apr-18				
Section IV - Slip Road 3								
Roadwork & Utilities								

Data Date: 20-Feb-18	<ul style="list-style-type: none"> ◆ Current Milestone ■ Actual Work ■ Critical Remaining Work ■ Remaining Work ▬ Remaining Level of Effort
-------------------------	---

**3 Months Rolling Programme for Non-CRIII Area (April 2018 - June 2018)
(Ref. to Works Programme Rev.12)**

Date	Revision	Checked	Approved
13-Mar-18	12		

**CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2018					
					Apr	May	Jun	Jul		
Section 1 (L16608 - L1601)										
SIV11749	Sec IV - sign gantry DS20 & DS21 footing (type 2): removal of ELS and backfilling	10	21-Mar-18	04-Apr-18						
SIV11751	Sec IV - sign gantry DS21 footing (type 3): excavation	5	26-Mar-18	03-Apr-18						
SIV11752	Sec IV - sign gantry DS21 footing (type 3): footing structure	13	04-Apr-18	19-Apr-18						
SIV11763	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Drainage Works (L2004 - L2005, L2101 - L2101A)	21	20-Apr-18	15-May-18						
SIV11765	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Gully pipe (L2004)	7	17-May-18	25-May-18						
SIV11780	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Watermain	18	26-May-18	15-Jun-18						
SIV11800	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Utilities : TCSS crossroad duct	14	16-Jun-18	04-Jul-18						
SIV11860	Sec IV - Roadwork & Utilities at SR3 Section 1 footpath - Drainage Works: future connection pipes	7	26-May-18	02-Jun-18						
SIV11880	Sec IV - Roadwork & Utilities at SR3 Section 1 footpath - watermain	7	04-Jun-18	11-Jun-18						
SIV11900	Sec IV - Roadwork & Utilities at SR3 Section 1 footpath - utilities: HEC & TCSS	39	12-Jun-18	28-Jul-18						
Section 2 (L2301 - L2103)										
SIV12080	Sec IV - Roadwork & Utilities at SR3 Section 2 footpath - paving block	21	18-Apr-18	12-May-18						
Section 3 (M/H1.6 - L2301)										
SIV12120	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Drainage Works (M1.6-C1.1-C1.2): ELS,construct MH and	28	12-Apr-18	15-May-18						
SIV12121	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Drainage Works (M1.6-C1.1-C1.2): Backfilling & shift lane	6	16-May-18	23-May-18						
SIV12122	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Drainage Works (M1.6-C1.1-C1.2): Construct MH C1.2	5	24-May-18	29-May-18						
SIV12140	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Gully pipe (M/H 1.7 - L2301)	32	10-Apr-18	17-May-18						
SIV12150	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Road kerb	14	18-May-18	04-Jun-18						
SIV12155	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - formation	10	05-Jun-18	15-Jun-18						
SIV12160	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Black top	7	16-Jun-18	25-Jun-18						
SIV12170	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - Utilities: TCSS	21	10-May-18	04-Jun-18						
SIV12180	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - U channel	10	05-Jun-18	15-Jun-18						
SIV12220	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - Paving block	25	16-Jun-18	17-Jul-18						
Section VII - Remainder Works										
Road & Drainage Works (Culvert L - M/H1.7, Adjacent to SR3)										
SVII11620	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway : traffic diversion at Lung King Street	3	21-Apr-18	24-Apr-18						
SVII11640	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - Gully pipe (Culvert L -MH1.7)	27	25-Apr-18	28-May-18						
SVII11650	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - TCSS duct	7	29-May-18	05-Jun-18						
SVII11654	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - road kerb & formation	14	06-Jun-18	22-Jun-18						
SVII11680	Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - U channel	14	29-May-18	13-Jun-18						
SVII11700	Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - utilities: TCSS	14	14-Jun-18	30-Jun-18						
Retaining Wall RW5 Construction										
SVII10660	Sec VII - Retaining Wall RW5 (bay 1) - construct base slab and wall	22	02-May-18	28-May-18						
SVII10680	Sec VII - Retaining wall RW5 (bay 2) - construct base slab and wall	22	29-May-18	23-Jun-18						
SVII10800	Sec VII - Retaining wall RW5 (bay 3) - construct base slab and wall	22	02-May-18	28-May-18						
SVII10820	Sec VII - Retaining wall RW5 (bay 4) - construct base slab and wall	22	29-May-18	23-Jun-18						
Landing Steps Construction										
Landing Steps BSW13										
SVII10900	Sec VII - Landing steps (BSW13) - install vertical fender / step fender	15	31-May-18	16-Jun-18						

**CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West**

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2018			
					Apr	May	Jun	Jul
SVII10920	Sec VII - Landing steps (BSW13) - install s.s. handrail / tactile / sign board / bollard	25	19-Jun-18	18-Jul-18				
Promenade Seawall Parapet Construction & EVA								
SVII13122	Sec VII - Zone A1, A2 & B - seawall parapet: reinforced concrete coping	18	29-Mar-18	23-Apr-18				
SVII13140	Sec VII - Zone A1, A2 & B - seawall parapet: Construct seawall parapet	30	24-Apr-18	30-May-18				
SVII13160	Sec VII - Zone A1, A2 & B - EVA: watermain	14	31-May-18	15-Jun-18				
SVII13180	Sec VII - Zone A1, A2 & B - EVA: U-channel	14	16-Jun-18	04-Jul-18				
SVII13200	Sec VII - Zone D - seawall parapet: Remove temporary seawall block	21	21-Mar-18*	18-Apr-18				
SVII13220	Sec VII - Zone D - seawall parapet: Construct mass concrete	30	19-Apr-18	25-May-18				
SVII13222	Sec VII - Zone D - seawall parapet: reinforced concrete coping	18	26-May-18	15-Jun-18				
SVII13240	Sec VII - Zone D - seawall parapet: Construct seawall parapet	25	16-Jun-18	17-Jul-18				
Promenade Footpath								
Section 1								
SVII10440	Sec VII - section 1 footpath - drainage works : connection pipe & U -channel	10	10-May-18	21-May-18				
SVII10445	Sec VII - section 1 footpath - watermain	7	23-May-18	30-May-18				
SVII10460	Sec VII - section 1 footpath - lighting	7	31-May-18	07-Jun-18				
Section 2								
SVII12615	Sec VII - section 2 footpath - watermain	7	12-Apr-18	19-Apr-18				
SVII12630	Sec VII - section 2 footpath - utilities: TCSS	21	20-Apr-18	15-May-18				
SVII12670	Sec VII - section 2 footpath - paving block	30	16-May-18	21-Jun-18				
Section 3								
SVII12850	Sec VII - section 3 footpath - watermain	17	26-Mar-18*	18-Apr-18				
SVII12870	Sec VII - section 3 footpath - utilities (HEC, TCSS, HGC, PCCW)	40	19-Apr-18	06-Jun-18				
SVII12875	Sec VII - 3 footpath - drainage works :U chanel	14	07-Jun-18	23-Jun-18				
Section 4								
SVII13110	Sec VII - section 4 footpath - paving block	25	19-May-18	19-Jun-18				
Section 5								
SVII13275	Sec VII - section 5 footpath - watermain	14	07-Apr-18	23-Apr-18				
SVII13310	Sec VII - section 5 footpath - utilities: HEC, TCSS, HGC, PCCW	42	24-Apr-18	13-Jun-18				
SVII13330	Sec VII - section 5 footpath - paving block	22	14-Jun-18	11-Jul-18				
Section 6								
SVII13510	Sec VII - section 6 footpath - watermain	13	29-Mar-18	17-Apr-18				
SVII13514	Sec VII - section 6 footpath - U channel	20	18-Apr-18	11-May-18				
SVII13530	Sec VII - section 6 footpath - utilities: HEC, TCSS, HGC, PCCW	49	18-Apr-18	15-Jun-18				
SVII13550	Sec III A - section 6 footpath - paving block	25	16-Jun-18	17-Jul-18				
Section VIII - Landscape Softworks								
Soft Landscaping Works								
SVIII10040	Sec VIII - Trees Planting	141	03-Jun-18	21-Oct-18				
SVIII10060	Sec VIII - Shrubs Planting	141	03-Jun-18	21-Oct-18				

Activity ID	Activity Name	Rem Dur	Start	Finish	2018															
					April				May				June							
					18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	
3MRP (Mar 2018 - Jun 2018)																				
10 - SECTION X OF THE WORKS																				
10.3 - Middle Bridge (Bridge F)																				
10.3.2 - Bridge Construction																				
Bridge F1B2																				
1032-3880	Bridge F1B2 - Construct Int. Double Noise Encl. Bridge F1B2	9	13-Jan-18 A	29-Mar-18	[Green Bar] Bridge F1B2 - Construct Int. Double Noise Encl. Bridge F1B2															
1032-3900	Bridge F1B2 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking	7	31-Mar-18	10-Apr-18	[Green Bar] Bridge F1B2 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking															
Bridge F1B1																				
1032-1780	Bridge F1B1 - Construct Int. Double Noise Encl. Bridge F1B2	9	16-Jan-18 A	29-Mar-18	[Green Bar] Bridge F1B1 - Construct Int. Double Noise Encl. Bridge F1B2															
1032-1800	Bridge F1B1 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking	7	31-Mar-18	10-Apr-18	[Green Bar] Bridge F1B1 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking															
Bridge F5																				
1032-4080	Cutting of Deck Between Temp. TD & E/B > Pier F11-F14	6	19-Mar-18 A	26-Mar-18	[Green Bar] Cutting of Deck Between Temp. TD & E/B > Pier F11-F14															
1032-4120	Construction Parapet (Northside) > Pier F8-F11	2	15-Mar-18 A	21-Mar-18	[Green Bar] Construction Parapet (Northside) > Pier F8-F11															
1032-4140	Construction Parapet (Northside) > Pier F11-F14	8	22-Mar-18	31-Mar-18	[Green Bar] Construction Parapet (Northside) > Pier F11-F14															
1032-4160	Construct Noise Enclosure (Northside) > Pier F5 - F8	10	15-Mar-18 A	31-Mar-18	[Green Bar] Construct Noise Enclosure (Northside) > Pier F5 - F8															
1032-4180	Reinstate Deck Pier F8 - F14 (Northside) > Surfacing & Marking	5	03-Apr-18	09-Apr-18	[Green Bar] Reinstate Deck Pier F8 - F14 (Northside) > Surfacing & Marking															
1032-4200	Reinstate Deck Pier F5 - F8 (Northside) > Surfacing & Marking	5	10-Apr-18	14-Apr-18	[Green Bar] Reinstate Deck Pier F5 - F8 (Northside) > Surfacing & Marking															
All Middle Bridge F (Common)																				
1032-4240	Fresh Water Main 150DI at Bridge F Deck	20	27-Nov-17 A	14-Apr-18	[Green Bar] Fresh Water Main 150DI at Bridge F Deck															
1032-4356	Sign Gantry (DS06B,DS06A & FADS06) (Nigth work)	30	22-Feb-18 A	26-Apr-18	[Green Bar] Sign Gantry (DS06B,DS06A & FADS06) (Nigth work)															
10.5 - Temporary Bridge																				
10.5.3 - Temporary Bridge 'TD'																				
1053-1140	Demolition of Temporary Bridge "TD" at VI	32	14-Apr-18	22-May-18	[Green Bar] Demolition of Temporary Bridge "TD" at VI															
10.6 - Tunnel Approach Ramp																				
10.6.1 - Approach Ramp (Excluding Portion IIB)																				
Retaining Walls & Trough Structure B,C & D																				
1061-6860	Construct Retaining Wal E Pile Cap (7 nos)	29	06-Mar-17 A	25-Apr-18	[Green Bar] Construct Retaining Wal E Pile Cap (7 nos)															
1061-6900	Construct Retaining Wal E1 (Ch 5332 - 5371)	15	12-Mar-18 A	14-May-18	[Green Bar] Construct Retaining Wal E1 (Ch 5332 - 5371)															
1061-6990	Parapet at Wall above Retaining Wall E1	15	14-Mar-18 A	31-May-18	[Green Bar] Parapet at Wall above Retaining Wall E1															
1061-7020	Falseworks System for Landscape Deck	8	29-Jan-18 A	28-Mar-18	[Red Bar] Falseworks System for Landscape Deck															
1061-7040	Excavate for Foundation of Retaing Wall D	7	29-Mar-18	09-Apr-18	[Red Bar] Excavate for Foundation of Retaing Wall D															
1061-7060	Construct Retaining Wal D Footing (Ch 190 - 170)	15	10-Apr-18	26-Apr-18	[Green Bar] Construct Retaining Wal D Footing (Ch 190 - 170)															
1061-7080	Construct Retaining Wal D (Ch 190 - 170)	18	27-Apr-18	18-May-18	[Green Bar] Construct Retaining Wal D (Ch 190 - 170)															
1061-7100	Backfilling Works	12	19-May-18	01-Jun-18	[Green Bar] Backfilling Works															
1061-7120	Excavate to Founding Level Trough B Structure	12	31-Mar-18	16-Apr-18	[Red Bar] Excavate to Founding Level Trough B Structure															

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Mar.2018 to 19.Jun.2018)

Activity ID	Activity Name	Rem Dur	Start	Finish	2018													
					April						May				June			
					18	25	01	08	15	22	29	06	13	20	27	03	10	17
1061-7140	Construct Trough Structure B Base Slab	18	17-Apr-18	08-May-18	Construct Trough Structure B Base Slab													
1061-7160	Construct Trough Structure B Side Walls	18	09-May-18	29-May-18	Construct Trough Structure B Side Walls													
1061-7180	Excavate to Founding Level Trough C Structure	12	10-Apr-18	23-Apr-18	Excavate to Founding Level Trough C Structure													
1061-7200	Construct Trough Structure C Base Slab	15	24-Apr-18	11-May-18	Construct Trough Structure C Base Slab													
1061-7220	Construct Trough Structure C Side Walls	18	10-May-18	30-May-18	Construct Trough Structure C Side Walls													
1061-7240	Road & other Misc Works at Trough D	12	02-Jun-18	15-Jun-18	Road & other Misc													
Landscape Deck																		
1061-7460	Ch 5331 - 5419 > Beam & Deck	14	19-Feb-18 A	07-Apr-18	Ch 5331 - 5419 > Beam & Deck													
1061-7480	Ch 5303 - 5419 > Noise Panel Installations	32	19-Apr-18	26-May-18	Ch 5303 - 5419 > Noise Panel Installations													
10.6.2 - Approach Ramp (Within Portion IIB)																		
Structure																		
Bay 1																		
Wall - Upper Portion																		
A1220	Remove S1 and S2 Strut + Waling	4	03-Apr-18	07-Apr-18	Remove S1 and S2 Strut + Waling													
A1260	Vertical Water Proofing	2	09-Apr-18	10-Apr-18	Vertical Water Proofing													
Bay 2																		
Wall - Upper Portion																		
A1380	Remove S1 and S2 Strut + Waling	4	03-Apr-18	07-Apr-18	Remove S1 and S2 Strut + Waling													
A1420	Vertical Water Proofing	2	09-Apr-18	10-Apr-18	Vertical Water Proofing													
Bay 3																		
Wall - Upper Portion																		
A1540	Remove S1 and S2 Strut + Waling	4	03-Apr-18	07-Apr-18	Remove S1 and S2 Strut + Waling													
A1580	Vertical Water Proofing	2	09-Apr-18	10-Apr-18	Vertical Water Proofing													
Bay 4																		
Wall - Upper Portion																		
A1710	Remove S1 and S2 Strut + Waling	4	03-Apr-18	07-Apr-18	Remove S1 and S2 Strut + Waling													
A1750	Vertical Water Proofing	2	09-Apr-18	10-Apr-18	Vertical Water Proofing													
Bay 5																		
Wall - Lower Portion																		
A1830	Erect and Formwork	3	19-Mar-18 A	22-Mar-18	Erect and Formwork													
A1840	Concreting	1	23-Mar-18	23-Mar-18	Concreting													
A1850	Vertical Water Proofing	1	24-Mar-18	24-Mar-18	Vertical Water Proofing													
A1860	Backfilling	3	26-Mar-18	28-Mar-18	Backfilling													
Wall - Upper Portion																		
A1870	Remove S1 and S2 Strut + Waling	4	03-Apr-18	07-Apr-18	Remove S1 and S2 Strut + Waling													

- █ Remaining Level of Effort
- █ Actual Level of Effort
- █ Critical Remaining Work
- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work
- ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Mar.2018 to 19.Jun.2018)

Activity ID	Activity Name	Rem Dur	Start	Finish	2018															
					April				May				June							
					18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	
A1880	Erect Working Platform and Rebar Fixing	2	24-Mar-18	26-Mar-18																
A1890	Erect and Formwork	3	27-Mar-18	29-Mar-18																
A1900	Concreting	1	31-Mar-18	31-Mar-18																
A1910	Vertical Water Proofing	2	09-Apr-18	10-Apr-18																
Landscape Deck																				
1062-1240	Construct LD Column - Portion IIB (10nos)	9	12-Mar-18 A	29-Mar-18																
1062-1260	Construct Landscape Deck Beam/Slab Bay C1 & C2	18	14-Mar-18 A	12-Apr-18																
1062-1280	Construct Noise Panel Trough A (within Portion IIB)	30	20-Apr-18	25-May-18																
Road Works																				
1062-1300	Approach Ramp Road Drainage (within Portion IIB)	24	12-May-18	08-Jun-18																
1062-1320	Approach Ramp Profile Barrier (within Portion IIB)	24	12-May-18	08-Jun-18																
1062-1340	Approach Ramp Street Furniture (within Portion IIB)	24	12-May-18	08-Jun-18																
1062-1360	Approach Ramp TCSS/E&M Ducts and Supports (within Portion IIB)	24	12-May-18	08-Jun-18																
1062-1380	Approach Ramp Road Surfacing & Marking (within Portion IIB)	10	09-Jun-18	21-Jun-18																

Remaining Level of Effort Remaining Work
 Actual Level of Effort Critical Remaining Work
 Actual Work Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.Mar.2018 to 19.Jun.2018)

Activity ID	Activity Name	Original Duration	Start	Finish	2018												
					Feb	Mar	Apr	May	Jun								
Total		1876d	21-Mar-13 A	21-Jun-18													
DWP-08 - (2) - Update Progress As of 20 Feb 18		1876d	21-Mar-13 A	21-Jun-18													
Works in KD8		24d	05-Feb-18 A	27-Feb-18 A													
TS3W - Remove Temporary Reclamation		24d	05-Feb-18 A	27-Feb-18 A													
Stage 7 - Remove D-wall W4D13, 14 & W4D12, W4D15 - 16 + W3D8 - W3D11 & Seawall Reinstatement		24d	05-Feb-18 A	27-Feb-18 A													
Reinstatement of Remaining Vertical Seawall by Land Plants		24d	05-Feb-18 A	27-Feb-18 A													
MW_1610	Pour concrete behind 5th layer of facing stone	1d	05-Feb-18 A	05-Feb-18 A													
MW_1630	Erect Formwork for coping	3d	06-Feb-18 A	09-Feb-18 A													
MW_1640	Pour concrete for coping	1d	10-Feb-18 A	10-Feb-18 A													
MW_1660	Lay footpath paving blocks	4d	11-Feb-18 A	14-Feb-18 A													
MW_1650	Backfill up to formation level (6 layers)	13d	26-Feb-18 A	27-Feb-18 A													
Works in KD6		132d	30-Aug-17 A	20-Mar-18													
Works in SR8 (Open Cut Method)		132d	30-Aug-17 A	20-Mar-18													
SR8 (Zone C) - Ch. 528 to Ch. 368		74d	30-Aug-17 A	20-Mar-18													
Zone C - Tunnel Structure		74d	30-Aug-17 A	20-Mar-18													
Egress Passage - EP01		74d	30-Aug-17 A	20-Mar-18													
A9050	Steel Railing - Fabrication & Installation	74d	30-Aug-17 A	20-Mar-18													
SR8 (Zone B) - Ch.385.000 to Ch.317.500 - (Inside Victoria Park to Tunnel Portal)		16d	21-Feb-18 A	16-Mar-18													
SR8 (Zone B) Tunnel - ELS / CCT / BF Works (7 Bays Ch. 385.000 to Ch.317.500)		16d	21-Feb-18 A	16-Mar-18													
Portal Structure		16d	21-Feb-18 A	16-Mar-18													
Pump House		7d	21-Feb-18 A	28-Feb-18 A													
Remaining Works inside Pump Sump E		7d	21-Feb-18 A	28-Feb-18 A													
Pump Sump E Hand Rail		7d	21-Feb-18 A	28-Feb-18 A													
EXW_2530	Installation of handrail (agreed with CC contract)	7d	21-Feb-18 A	28-Feb-18 A													
Remaining Works in Zone B		15d	28-Feb-18 A	16-Mar-18													
Egress Passage		15d	28-Feb-18 A	16-Mar-18													
EXW_2550	Railing installation (2 nos. - 10m)	15d	28-Feb-18 A	16-Mar-18													
Works in KD9 (Include Re-provisioning Works of KD4,KD5)		185d	23-Oct-17 A	15-May-18													
External Works Under KD9		185d	25-Oct-17 A	15-May-18													
Zone 1		90d	15-Dec-17 A	27-Mar-18													
Drainage Alignment Confirmation for MH72, 73, 74 due to Tree T1106		90d	15-Dec-17 A	27-Mar-18													
EXW_1125	Drawing Confirmation and construction for MH2-74A and associated drainage	8d	15-Dec-17 A	25-Mar-18													
EXW_1145	Pedestrian walkway open to public during Christmas and CNY	90d	23-Jan-18 A	27-Mar-18													
Zone 2		35d	25-Oct-17 A	04-Apr-18													
EXW_1890	Irrigation system construction	15d	25-Oct-17 A	04-Apr-18													
EXW_1880	Boundary fence Installation	30d	01-Nov-17 A	04-Apr-18													
Zone 3		35d	03-Mar-18	16-Apr-18													
Traffic Island		35d	03-Mar-18	16-Apr-18													
EXW_2050	Directional sign DS17 steel frame	7d	03-Mar-18*	10-Mar-18													
EXW_2060	New VMS6 steel frame	7d	12-Mar-18	19-Mar-18													
EXW_2070	TCSS and lighting at island	7d	20-Mar-18	26-Mar-18													
EXW_2080	JTIS (3 nos. footings, 1 no. concrete plinth)	14d	27-Mar-18	16-Apr-18													
Zone 4 up to Elderly Facilities		90d	30-Jan-18 A	15-May-18													

Activity ID	Activity Name	Original Duration	Start	Finish	2018											
					Feb	Mar	Apr	May	Jun							
Elderly Facilities V/039 Received on 22 Jun 2017																
EXW_2270	Facilities fabrication	90d	30-Jan-18 A	15-May-18	Facilities fabrication											
Additional Walkway & Arbour V/040 Received on 22 Aug 2017																
EXW_2300	Arbour confirmation and fabrication	60d	15-Feb-18 A	16-Mar-18	Arbour confirmation and fabrication											
EXW_2310	Associated drainage works for the walkway	20d	17-Mar-18	12-Apr-18	Associated drainage works for the walkway											
Reverting Traffic for IEC,VP Rd & TF St & Seawall Reinstatement (KD9)																
TTA Revert Traffic Back to Original Alignment																
East Bound TTA - IEC East Bound, Victoria Park Road & footpath along Sea Side																
TTM Stage 1 - IEC (East Bound)																
Reinstatement Existing Structure																
EB_1020	Install metal parapet on parapet wall (30m)	6d	28-Feb-18	05-Mar-18	Install metal parapet on parapet wall (30m)											
TTM Stage 2 - Revert Traffic back to Original Victoria Road																
Existing Bridge Parapet Reinstatement																
EB_1180	Install metal parapet on parapet wall (40m)	4d	06-Mar-18	09-Mar-18	Install metal parapet on parapet wall (40m)											
TTM Stage 3 - Reinstatement of Footpath along Seafront																
Reinstatement Works in Traffic Deck Part A																
EB_1540	Break two concrete footings	2d	31-Jan-18 A	16-Mar-18	Break two concrete footings											
EB_1520	Break pipe piles and cut sheet pile	6d	10-Feb-18 A	26-Feb-18 A	Break pipe piles and cut sheet pile											
EB_1530	Backfill Subbase material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)	3d	17-Mar-18	19-Mar-18	Backfill Subbase material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)											
Reinstatement of Existing Gas Main																
EB_1560	Excavation for DN400mm Gas main	3d	20-Mar-18	22-Mar-18	Excavation for DN400mm Gas main											
EB_1570	Laying DN400mm gas main by HKCG at VPR footpath	14d	23-Mar-18	05-Apr-18	Laying DN400mm gas main by HKCG at VPR footpath											
West Bound - IEC West Bound & Tsing fung Street																
TTM Stage 2 - Revert Traffic back to Original Tsing Fung Street																
Existing Bridge Parapet Reinstatement																
IECW_1140	Install metal parapet on parapet wall (60m)	5d	28-Feb-18	04-Mar-18	Install metal parapet on parapet wall (60m)											
TTM Stage 3 - Reinstatement of Victoria Park																
Reinstatement Works in Traffic Deck																
IECW_1390	Cut pipe piles and sheet pile	5d	18-Jan-18 A	13-Mar-18	Cut pipe piles and sheet pile											
IECW_1400	Backfill General Fill Material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)	3d	14-Mar-18	16-Mar-18	Backfill General Fill Material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)											
Reinstatement Works inside Victoria Park																
IECW_1440	Reinstatement of Boundary Fence	21d	29-Jan-18 A	17-Mar-18	Reinstatement of Boundary Fence											
IECW_1460	Cutting sheet pile to 1.5m below finish slope profile (MS 169B)	10d	19-Mar-18	28-Mar-18	Cutting sheet pile to 1.5m below finish slope profile (MS 169B)											
IECW_1470	Slope Reinstatement of Victoria Park	21d	26-Mar-18	23-Apr-18	Slope Reinstatement of Victoria Park											
Completion of Minor Outstanding / Remaining Works for KD9																
West Bound - Completion of Minor Outstanding / Remaining Works for KD9																
Minor Reinstatement Works for Tsing Fung Street																
IECW_1530	Laying Public Lighting duct	6d	18-Mar-18	23-Mar-18	Laying Public Lighting duct											
IECW_1540	Installation of public lighting post and connection by HyD	7d	24-Mar-18	30-Mar-18	Installation of public lighting post and connection by HyD											
IECW_1550	Well compact road formation level and subbase for SRT	6d	24-Mar-18	29-Mar-18	Well compact road formation level and subbase for SRT											
Minor Reinstatement Works in IEC West Bound																
IECW_1600	Replacement of new movement joint at IEC W/B (Sun midnight only)	8d	28-Feb-18	07-Mar-18	Replacement of new movement joint at IEC W/B (Sun midnight only)											
IECW_1630	Repairing of 300 dia. concrete pipeline by lining under slow lane of IEC W/B	2d	28-Feb-18*	01-Mar-18	Repairing of 300 dia. concrete pipeline by lining under slow lane of IEC W/B											
IECW_1610	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)	59d	08-Mar-18	05-May-18	Repairing of extg conc deck surface after milling of ten											

Activity ID	Activity Name	Original Duration	Start	Finish	2018					
					Feb	Mar	Apr	May	Jun	
Works in Victoria Park (KD4, KD5, KD9)										
Re-Provisioning Works										
Nursery Compound										
Nursery compound										
ABWF										
Finishes & Waterproofing										
VP_NC_1500	External wall tile cleaning	3d	23-Oct-17 A	20-Mar-18	External wall tile cleaning					
VP_NC_1420	Painting to wall & ceiling in general (final coat)	4d	15-Mar-18*	19-Mar-18	Painting to wall & ceiling in general (final coat)					
Switch room Cut-out Frame & Chequer Plate										
VP_NC_1690	Installation	1d	13-Feb-18 A	14-Feb-18 A	Installation					
Signage										
VP_NC_1720	Installation	7d	21-Feb-18 A	28-Feb-18 A	Installation					
Metal Fence										
VP_NC_1820	Installation	30d	15-Jan-18 A	29-Mar-18	Installation					
E&M										
VP_NC_1890	Form WR1 submission	7d	09-Feb-18 A	13-Feb-18 A	Form WR1 submission					
VP_NC_1900	Expected power on date	7d	14-Feb-18 A	14-Feb-18 A	Expected power on date					
Fire Services										
VP_NC_1960	Pump and water pipe installation	10d	22-Dec-17 A	10-Mar-18	Pump and water pipe installation					
VP_NC_1980	Hose Reel installation, Breakglass and Alarm	3d	10-Feb-18 A	13-Feb-18 A	Hose Reel installation, Breakglass and Alarm					
VP_NC_1930	FS pipe connection from u/g to water meter room	2d	24-Feb-18 A	28-Feb-18 A	FS pipe connection from u/g to water meter room					
Plumbing and Flushing Water Supplies										
VP_NC_2080	Cleaning of potable water pipe and sampling to WSD	7d	17-Feb-18 A	26-Feb-18 A	Cleaning of potable water pipe and sampling to WSD					
VP_NC_2100	WSD Inspection	14d	28-Feb-18	15-Mar-18	WSD Inspection					
GRP Water Tank Installation										
VP_NC_2130	Final As-fitted drawing submission to WSD	7d	30-Jan-18 A	06-Feb-18 A	Final drawing submission to WSD					
External Works Aside Nursery Compound										
Drainage										
VP_NC_2150	U channel at toilet	2d	30-Jan-18 A	31-Jan-18 A	U channel					
VP_NC_2190	SS angle to shower room u channel	1d	31-Jan-18 A	31-Jan-18 A	SS angle to shower room u channel					
VP_NC_2140	Drainage work at External area	15d	28-Feb-18	16-Mar-18	Drainage work at External area					
Water Works										
VP_NC_2220	FS Fresh & Salt Water, Fresh Water and Irrigation System	15d	07-Feb-18 A	27-Feb-18 A	FS Fresh & Salt Water, Fresh Water and Irrigation System					
External Works Around Nursery Compound										
VP_NC_2250	Reinstatement of Existing Boundary Fence Wall Around Nursery Compound	45d	28-Feb-18	24-Apr-18	Reinstatement of Existing Boundary Fence Wall Around Nursery Compound					
KD10 - Preservation and Protection of Trees										
PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	21-Jun-18	Preservation and Protection of Existing Trees					
KD15 & KD8 - Mooring Components Upkeep (CBTS and ATS)										
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	28-Feb-18	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS					

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018											
						Apr			May			Jun			Jul		
Update 2018-04-20 CWB(CC) - Commissioning Contract (SA)																	
PRELIMINARIES AND GENERAL REQUIREMENTS																	
Salient Key Dates and Milestones																	
Anticipated Completion Dates																	
KD03	KD3 - Achievement of Stage 3 (1385 days) - include EOT No.7 (207 days)	0		16-May-18*	-152	◆											
KD02	KD2 - Achievement of Stage 2 (1634 days) - include EOT No.9 (402 days)	0		30-May-18*	83	▲											
KD04	KD4 - Achievement of Stage 4 (1710 days) - include EOT No.9 (414 days)	0		30-Jun-18*	78	▲											
Possession Dates and Vacation Dates																	
PO-IIa	Possession of Portion IIa (Day 1) - WVB below +6.5mPD	1329	28-Feb-14 A	18-May-18	-194	[Bar chart showing work from Feb to May]											
PO-III	Possession of Portion III (Day 120) - CH1805-2600	1209	28-Jun-14 A	18-May-18	-246	[Bar chart showing work from Jun to May]											
PO-Ib	Possession of Portion Ib (Day 242) - CH1580-1805	1087	28-Oct-14 A	18-May-18	-186	[Bar chart showing work from Oct to May]											
PO-IXd	Possession of Portion IXd (Day 266) - CH4600-4860	1063	21-Nov-14 A	18-May-18	-211	[Bar chart showing work from Nov to May]											
PO-XI	Possession of Portion XI (Day 296) - EVS	1033	21-Dec-14 A	18-May-18	121	[Bar chart showing work from Dec to May]											
PO-IIc	Possession of Portion IIc (Day 336) - CH1360-1580	993	30-Jan-15 A	18-May-18	-194	[Bar chart showing work from Jan to May]											
PO-IIb	Possession of Portion IIb (Day 336) - WVB above +6.5mPD	669	30-Jan-15 A	18-May-18	-194	[Bar chart showing work from Jan to May]											
PO-IXa	Possession of Portion IXa (Day 392) - CH4860-5150	937	27-Mar-15 A	18-May-18	-211	[Bar chart showing work from Mar to May]											
PO-Va	Possession of Portion V (Day 607) - CH2950-3210	722	28-Oct-15 A	18-May-18	-246	[Bar chart showing work from Oct to May]											
PO-VII_a1	Possession of Portion VII (Day 762) - CH3911-4250 (below -6.0mPD)	659	30-Dec-15 A	18-May-18	-194	[Bar chart showing work from Dec to May]											
PO-Vc	Possession of Portion V (Day 607) - CH3210-3250	658	15-Jan-16 A	18-May-18	-158	[Bar chart showing work from Jan to May]											
PO-VIb_b1	Possession of Portion VIb (Day 761) - CH3428-3625 (E/B)	619	18-Feb-16 A	18-May-18	-178	[Bar chart showing work from Feb to May]											
PO-VIb_b2	Possession of Portion VIb (Day 761) - CH3428-3625 (W/B)	568	29-Feb-16 A	18-May-18	-136	[Bar chart showing work from Feb to May]											
PO-Xa_1	Possession of Portion Xa (Day 650) - ADB Southern Portion (AECOM letter ref: 2015007890T)	589	07-Mar-16 A	18-May-18	-335	[Bar chart showing work from Mar to May]											
PO-Xb_1	Possession of Portion Xb (Day 804) - ADB Northern Portion	589	07-Mar-16 A	18-May-18	-335	[Bar chart showing work from Mar to May]											
PO-Vb1	Possession of Portion V (Day 607) - SR3	587	11-Mar-16 A	18-May-18	121	[Bar chart showing work from Mar to May]											

- ◆ Current Milestone
- Level of Effort
- ▲ Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING

Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 1 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Apr	May	Jun	Jul
PO-Ia	Possession of Portion Ia (Day 789) - SCB / SCP1 / SCP2 / Rumsey Street Flyover	600	28-Mar-16 A	18-May-18	-294				
PO-VII_a2	Possession of Portion VII (Day 762) - CH3800-3911 (below -6.0mPD)	567	31-Mar-16 A	18-May-18	-194				
PO-IXc_1	Possession of Portion IXc (Day 712) - EVB above 3.6mPD - Relinquished on 12 Apr 2016	445	29-Jul-16 A	18-May-18	-323				
PO-IXb_1	Possession of Portion IXb (Day 712) - EVB (below +3.6mPD to tunnel top slab) - Relinquished on 12 Apr 2016	445	05-Aug-16 A	18-May-18	-323				
PO-VIa_a	Possession of Portion VIa (Day 823) - CH3250-3283	425	15-Aug-16 A	18-May-18	-137				
PO-Vb2_a	Possession of Portion V (Day 607) - SR2	456	15-Aug-16 A	18-May-18	-208				
PO-VIc_a	Possession of Portion VIc (Day 761) - CH3770-3800 (Access Shaft Opening)	391	23-Sep-16 A	18-May-18	-178				
PO-VIb_c	Possession of Portion VIb (Day 761) - CH3625-3770	391	23-Sep-16 A	18-May-18	-178				
PO-IVa1	Possession of Portion IVa (Day 930) - CH2600-2720	323	30-Nov-16 A	18-May-18	-178				
PO-IVb2	Possession of Portion IVb (Day 930) - MVB (GLD-H)	233	28-Feb-17 A	18-May-18	-346				
PO-VIIIa_a	Possession of Portion VIIIa (Day 929) - CH4530-4591 W/B	233	28-Feb-17 A	18-May-18	-246				
PO-VIIIa	Possession of Portion VIIIa (Day 929) - CH4250-4600 (Remaining)	241	12-Mar-17 A	18-May-18	-246				
PO-VIIIb	Possession of Portion VIIIb (Day 929) - SR8 (CH700-350)	233	12-Mar-17 A	18-May-18	-193				
PO-VIIIc	Possession of Portion VIIIc (Day 1039) - SR8 (CH350-310) / SCP4	233	12-Mar-17 A	18-May-18	-194				
PO-IVa2_a	Possession of Portion IVa (Day 930) - CH2720-2950	241	12-Mar-17 A	18-May-18	-178				
PO-IVb1	Possession of Portion IVb (Day 930) - MVB (GLA-C)	239	14-Mar-17 A	18-May-18	-346				
PO-IVa2_b	Possession of Portion IVa (Day 930) - SR1	203	30-Mar-17 A	18-May-18	-178				
PO-Vb2_b	Possession of Portion V (Day 607) - SCP3	182	03-Jul-17 A	18-May-18	-208				
PO-VIb_a	Possession of Portion VIb (Day 761) - CH3400-3428	80	31-Jul-17 A	18-May-18	-136				
PO-VIa_b	Possession of Portion VIa (Day 823) - CH3283-3400	80	31-Jul-17 A	18-May-18	-246				
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-Apr-18	08-Aug-18	-197				
Submissions and Approvals									
Initial General Submission									
10168	Submission of CMC 3DVR	30	20-Apr-18	19-May-18	120				

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING

Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 2 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018																	
						Apr			May			Jun			Jul								
DETAILED DESIGN OF WORKS																							
Permanent Works Design and Engineering																							
Green Roof on EVB																							
2166	EVB Roof - Engineer review & Approval; Consent to Proceed Construction	24	22-Mar-16 A	06-Apr-18 A																			
Green Wall on ADB																							
10238	ADB Green Wall - Engineer review & Approval; Consent to Proceed Construction	24	07-Mar-16 A	26-Apr-18	-276																		
Landscaping & Associated Irigation System																							
10268	Landscaping - Engineer review & Approval; Consent to Proceed Construction	24	07-Mar-16 A	04-May-18	-257																		
PROCUREMENT, MANUFACTURING & DELIVERIES																							
Procurement; Manufacturing; Deliveries																							
Green Roof on EVB																							
Procurement & Fabrication																							
2232	EVB Green Roof - Confirm design of embed items	0	22-Mar-18 A																				
2234	EVB Green Roof - Embed fabrication & delivery	20	23-Mar-18 A	19-Apr-18 A																			
2236	EVB Green Roof - Commence embed installation	0	20-Apr-18		-343																		
2238	EVB Green Roof - Green Roof Fabrication & delivery	20	20-Apr-18	09-May-18	-343																		
2240	EVB Green Roof - Commence installation	0	10-May-18		-343																		
Landscaping and Associated Irigation System																							
Shop Drawings																							
10272	Landscaping - Shop Drawings submission to the Engineer	30	06-Oct-17 A	01-May-18	-347																		
12848	Landscaping - Shop Drawings review by the Engineer	30	02-May-18	31-May-18	-347																		
10274	Landscaping - Obtain Approval for Shop Drawings	0		31-May-18	-347																		
Procurement & Fabrication																							
10276	Landscaping - Confirm design of embed items	0	01-Jun-18		-347																		

- Current Milestone
- Remaining Work
- Level of Effort
- Project Baseline
- Baseline Milestone
- Actual Work
- Critical Remaining Work

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 3 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

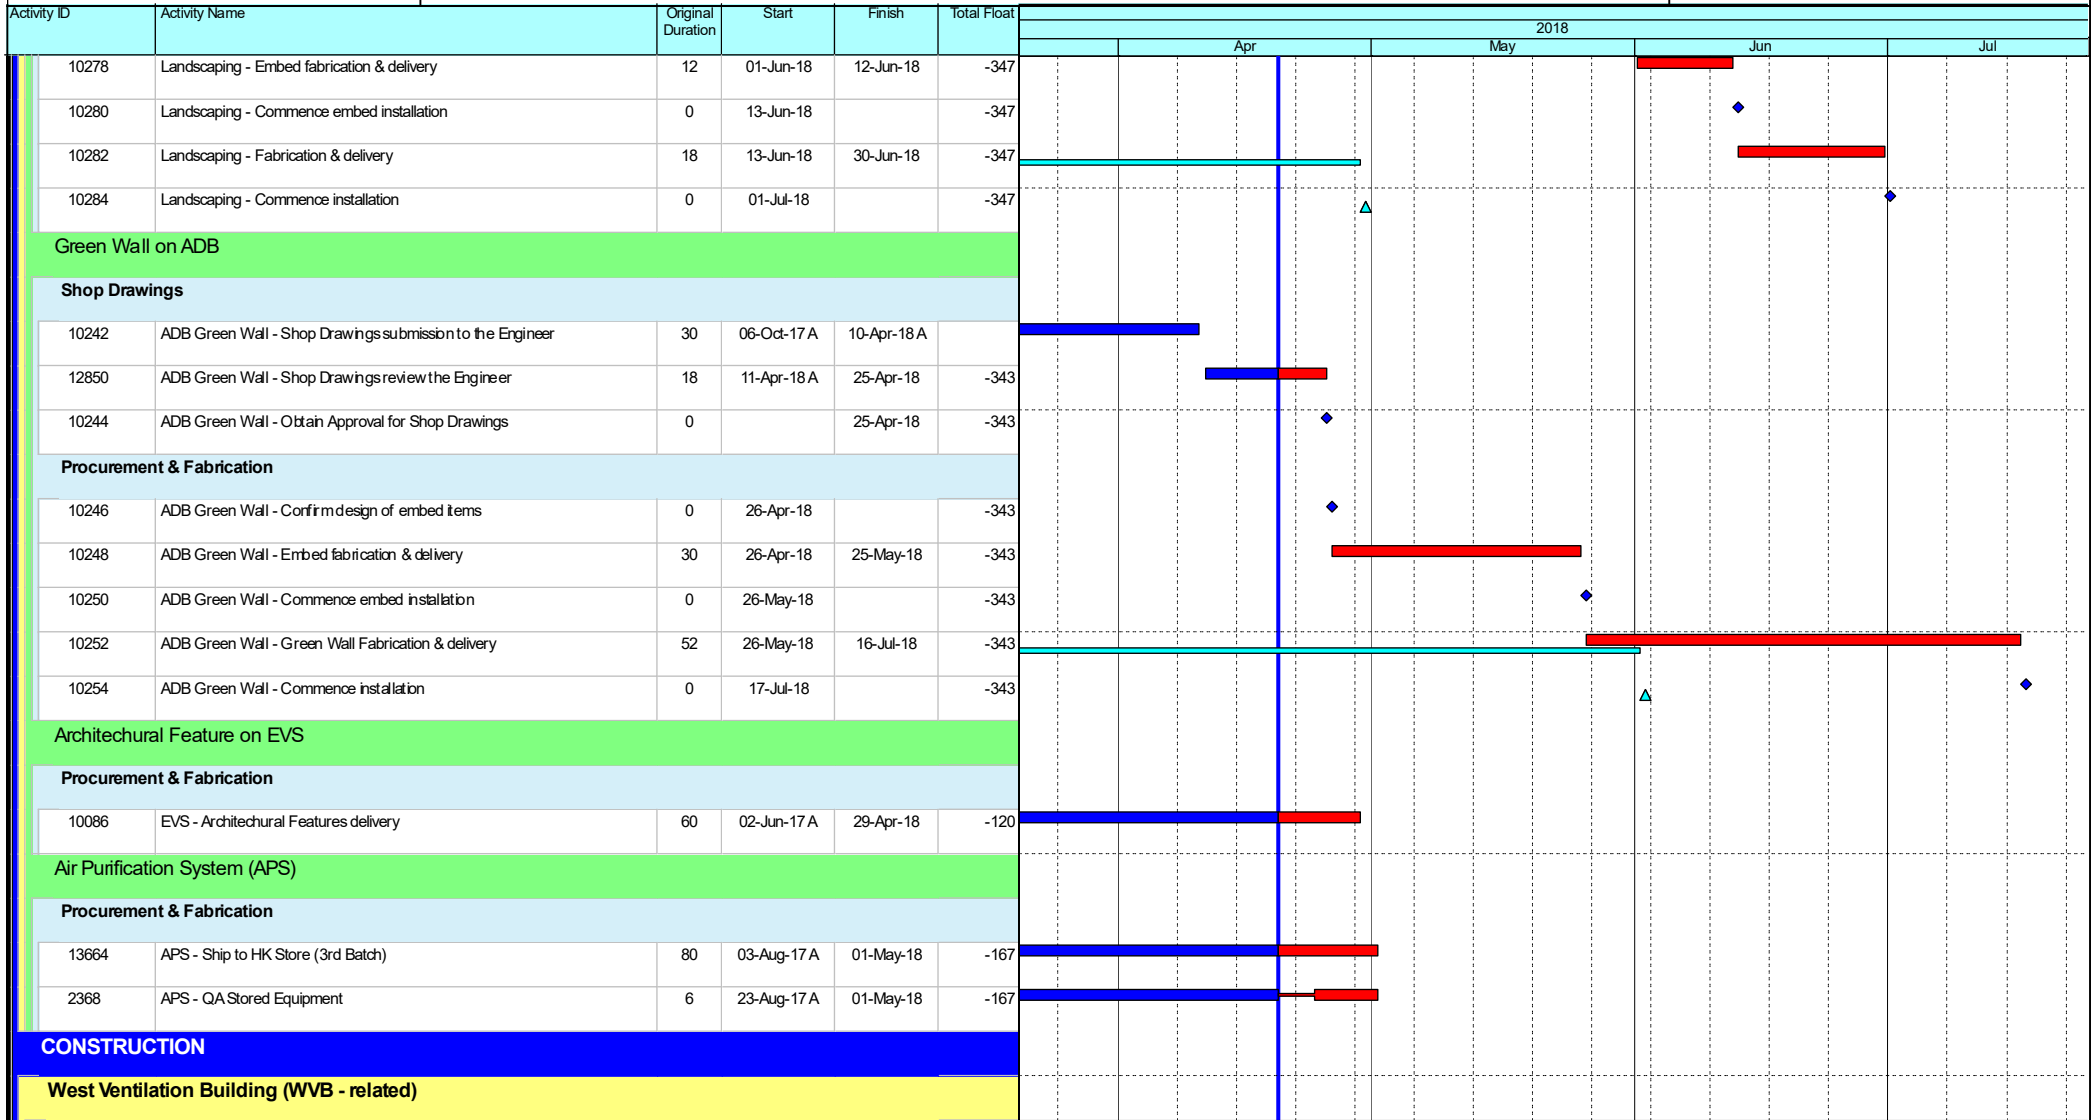

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
Baseline: SA01
Layout: Update Three Month Rolling
U050
Page 4 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

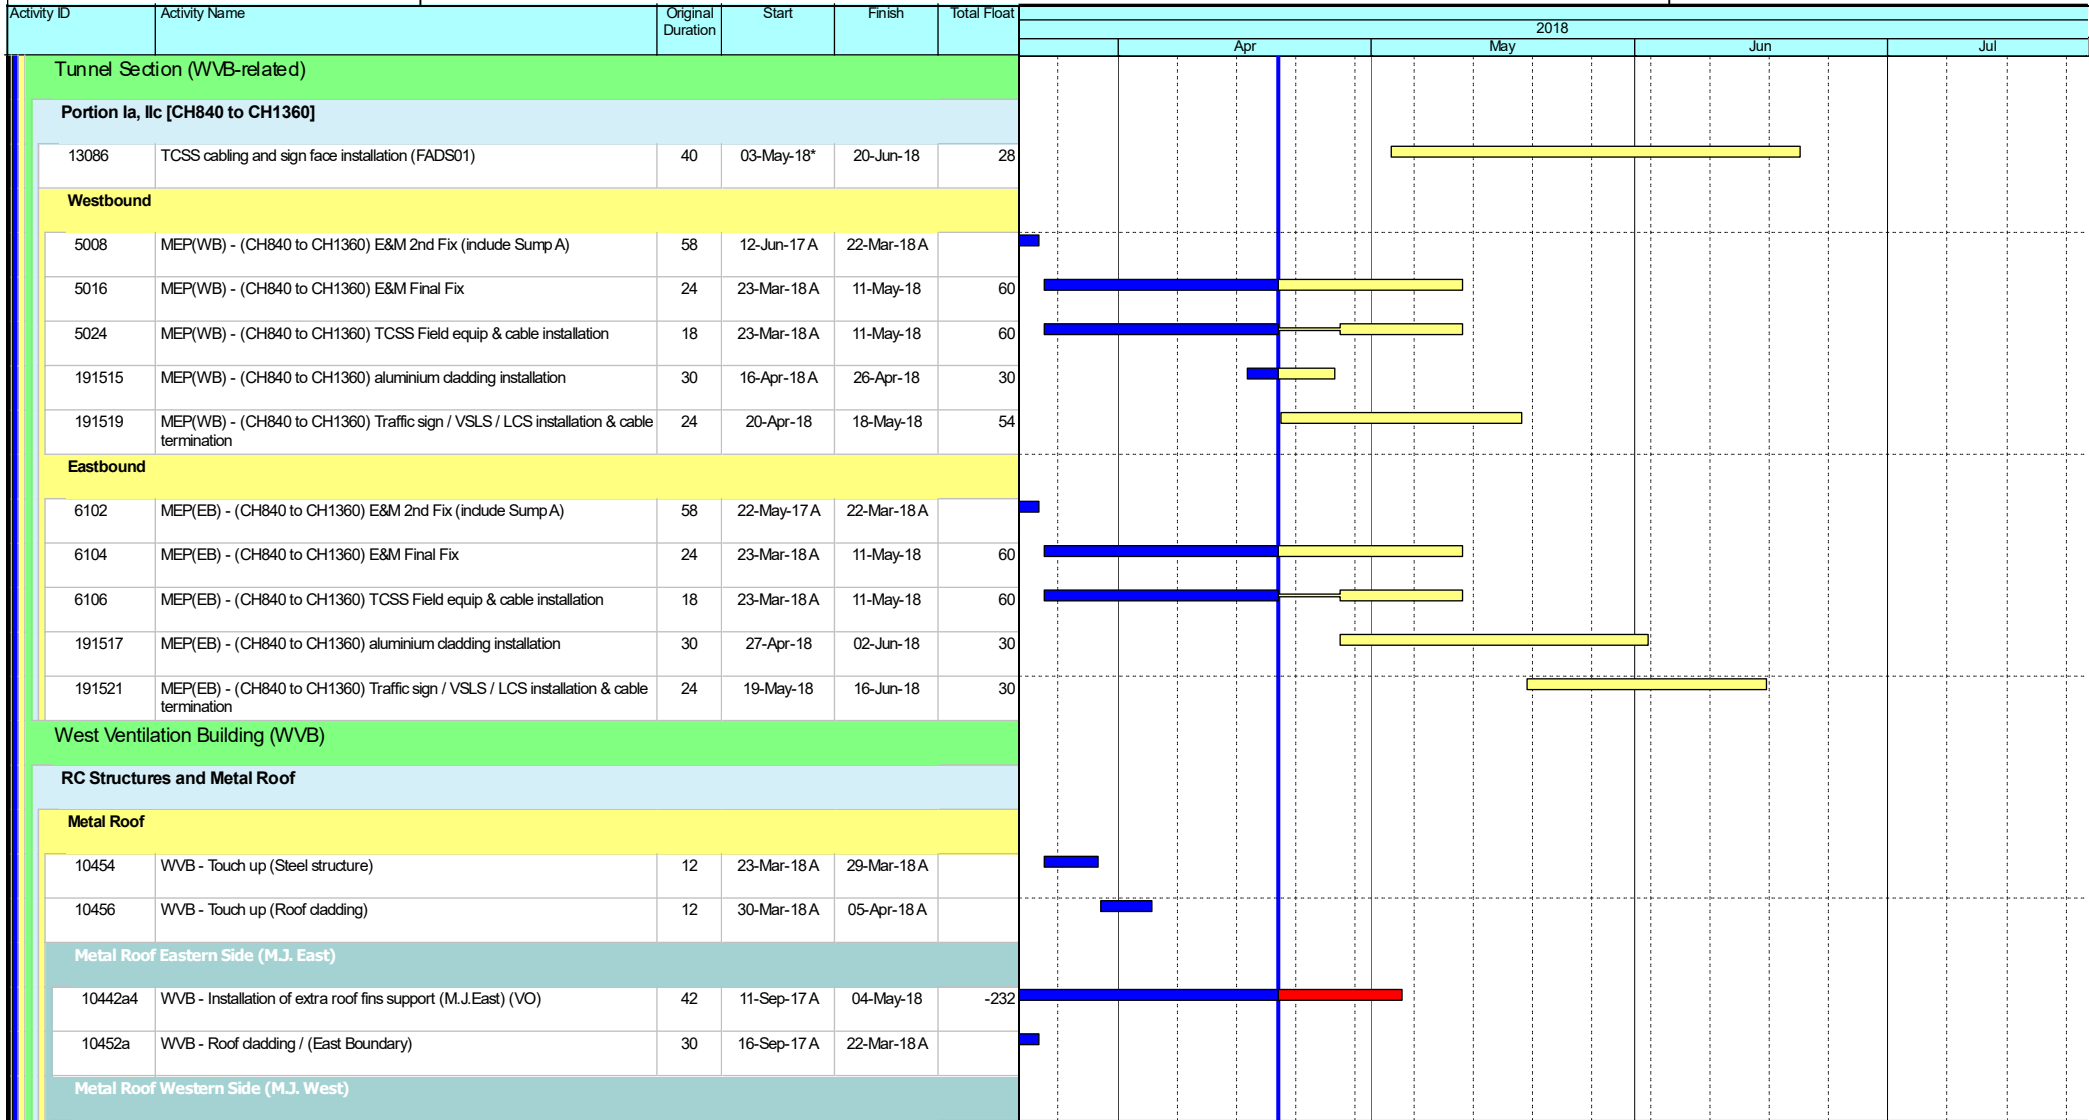

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 5 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

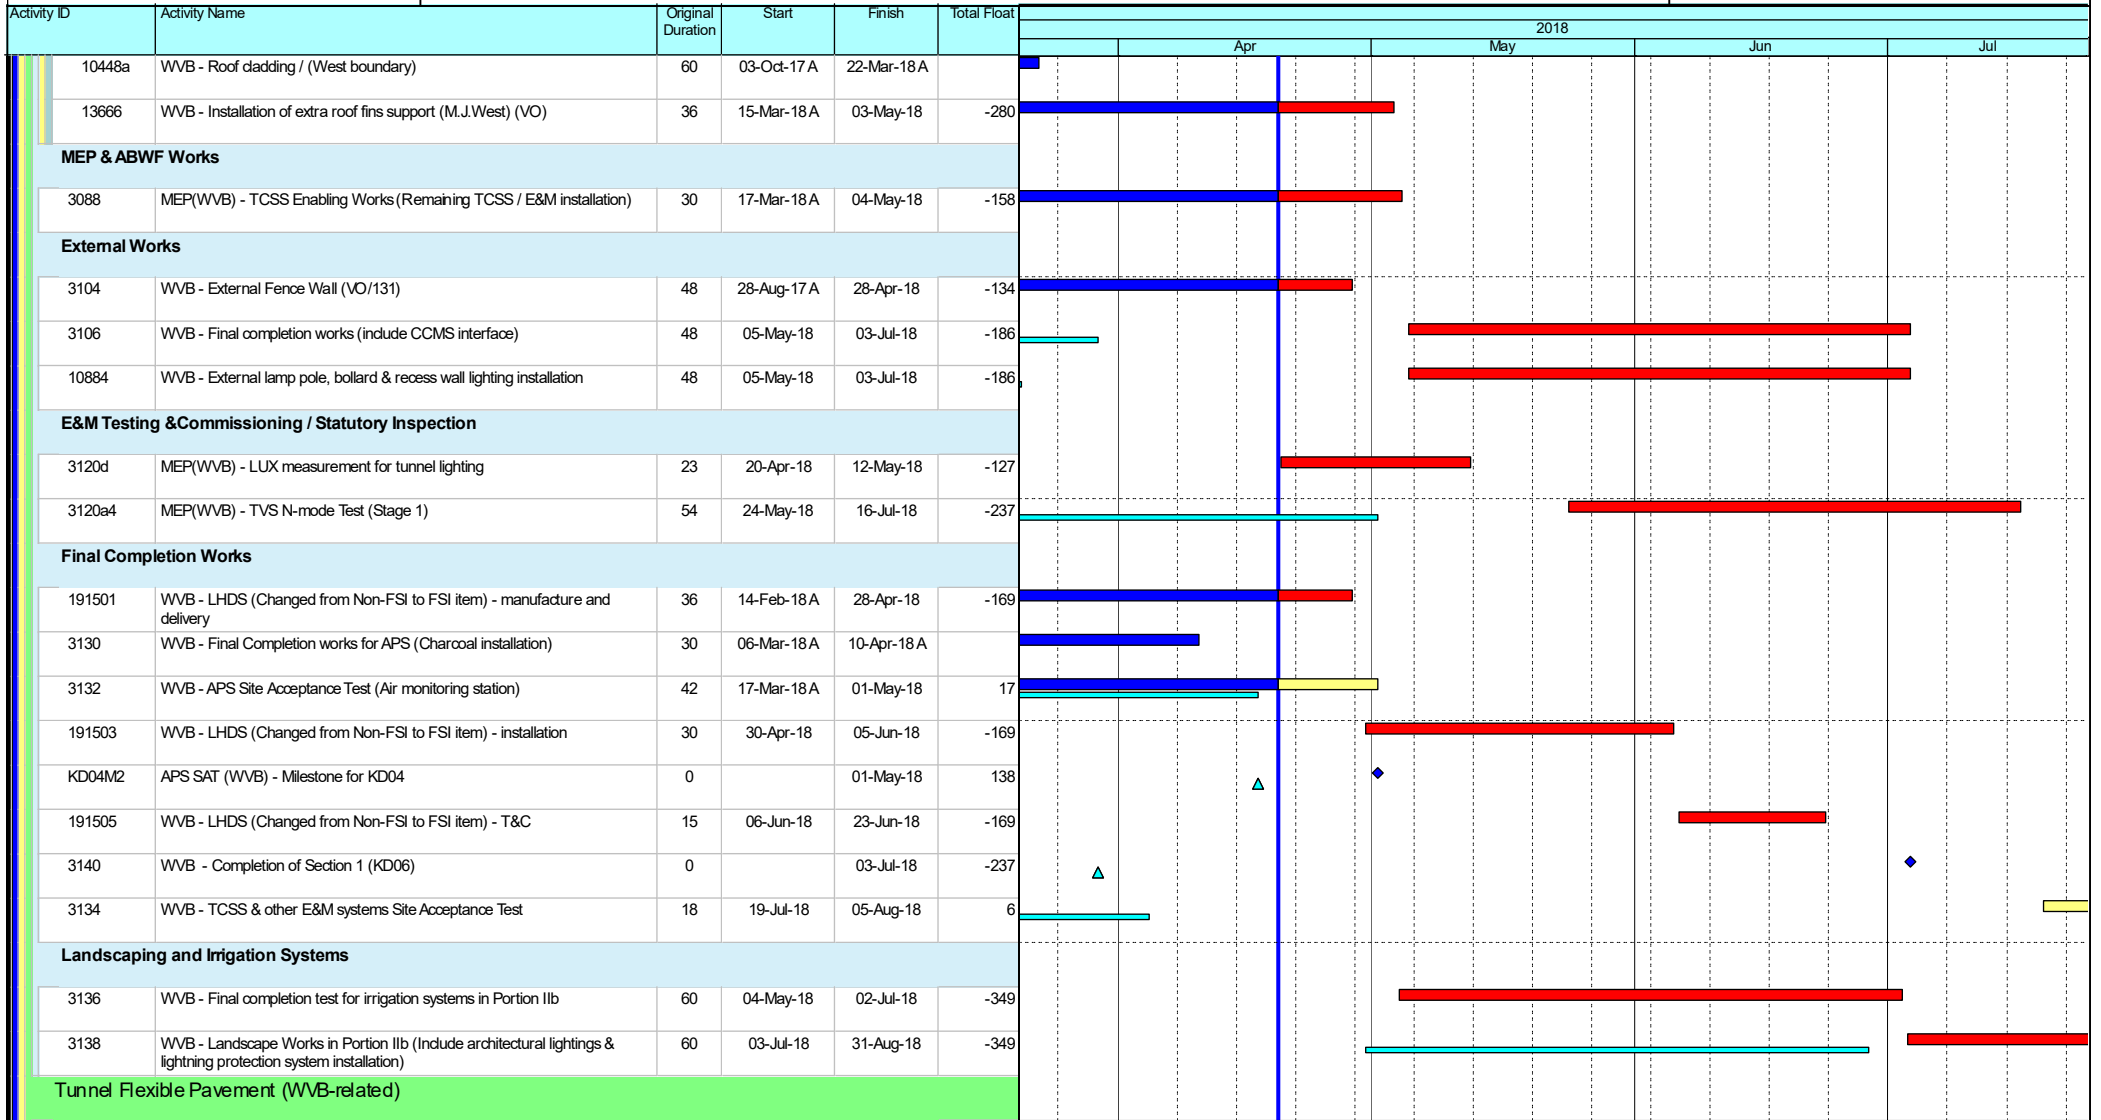

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 6 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

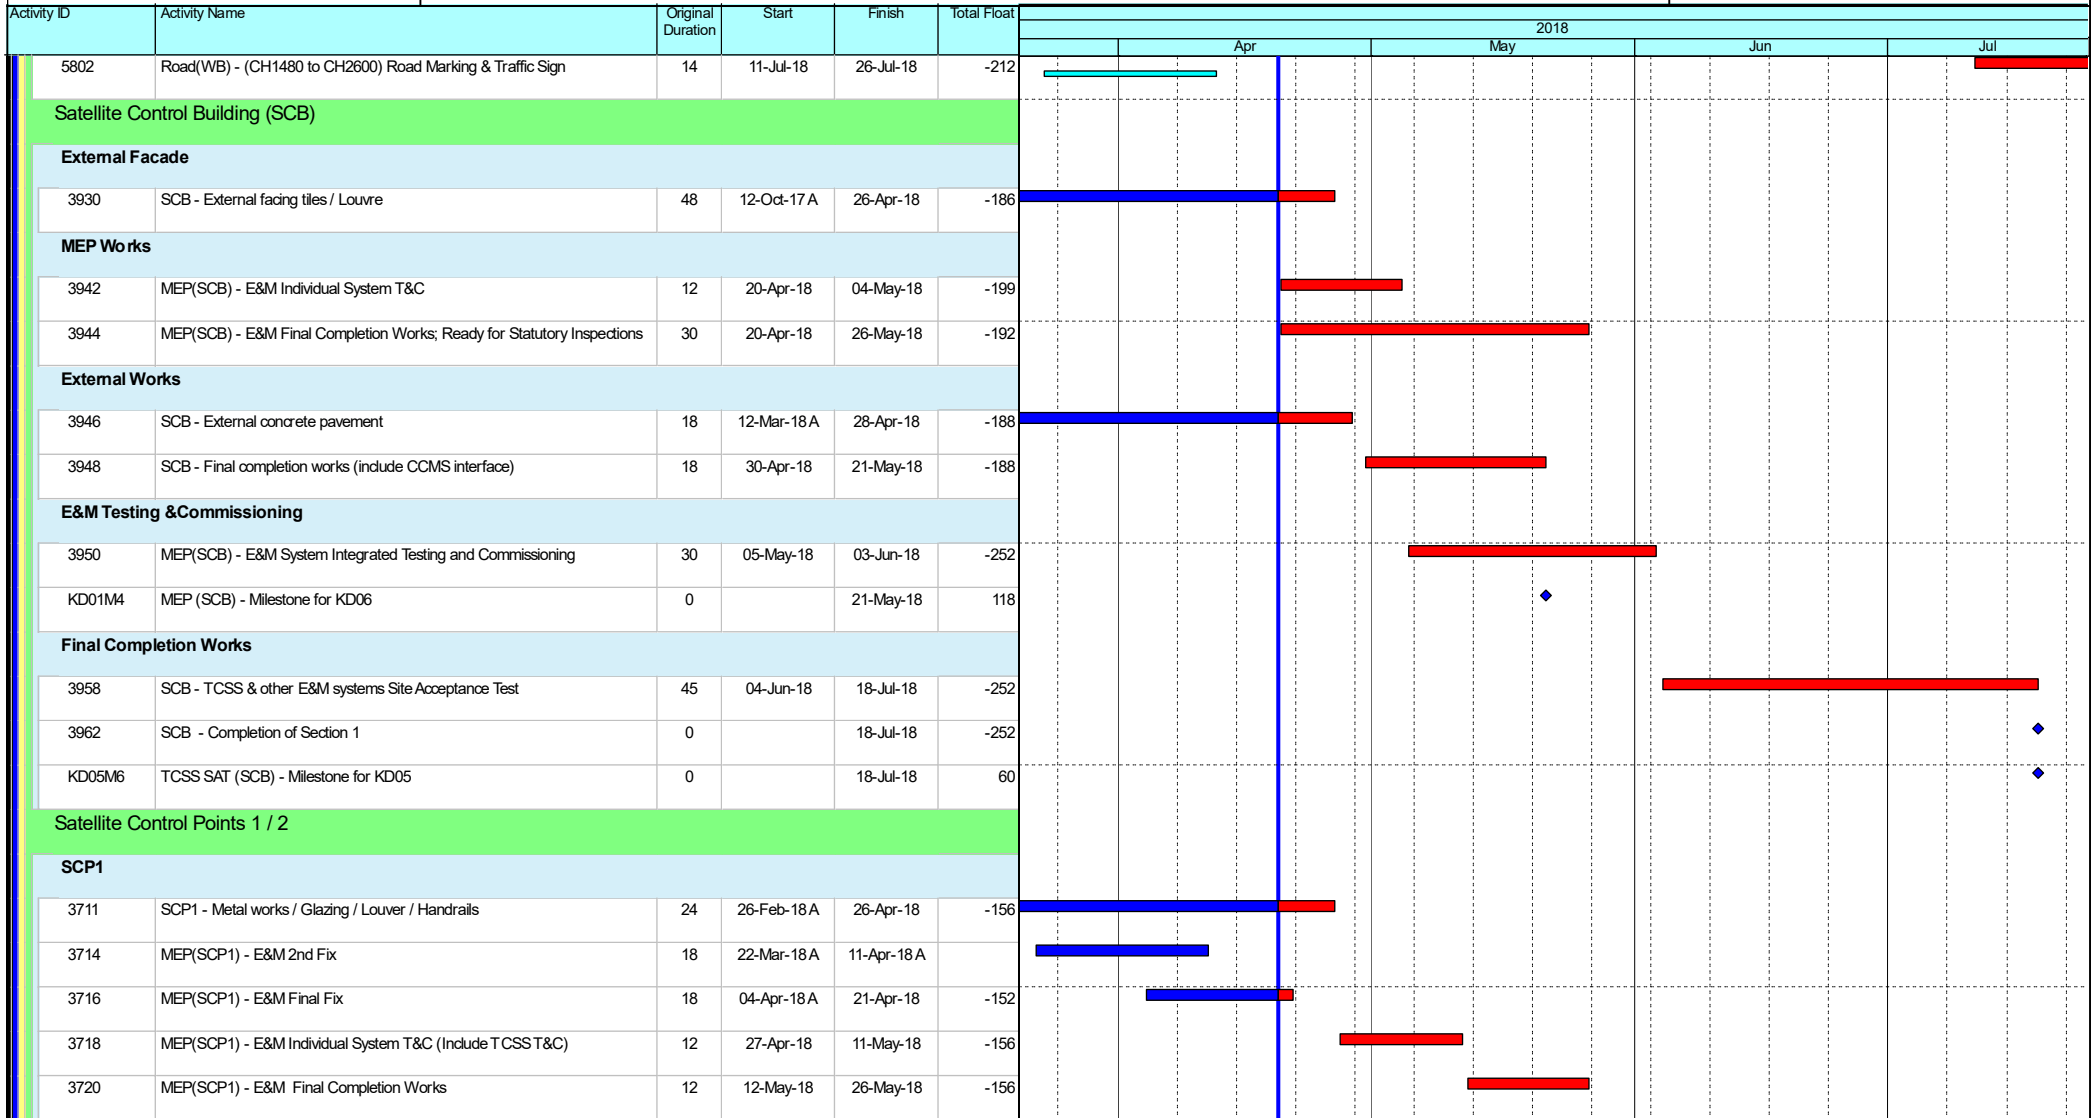



Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING

Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 7 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

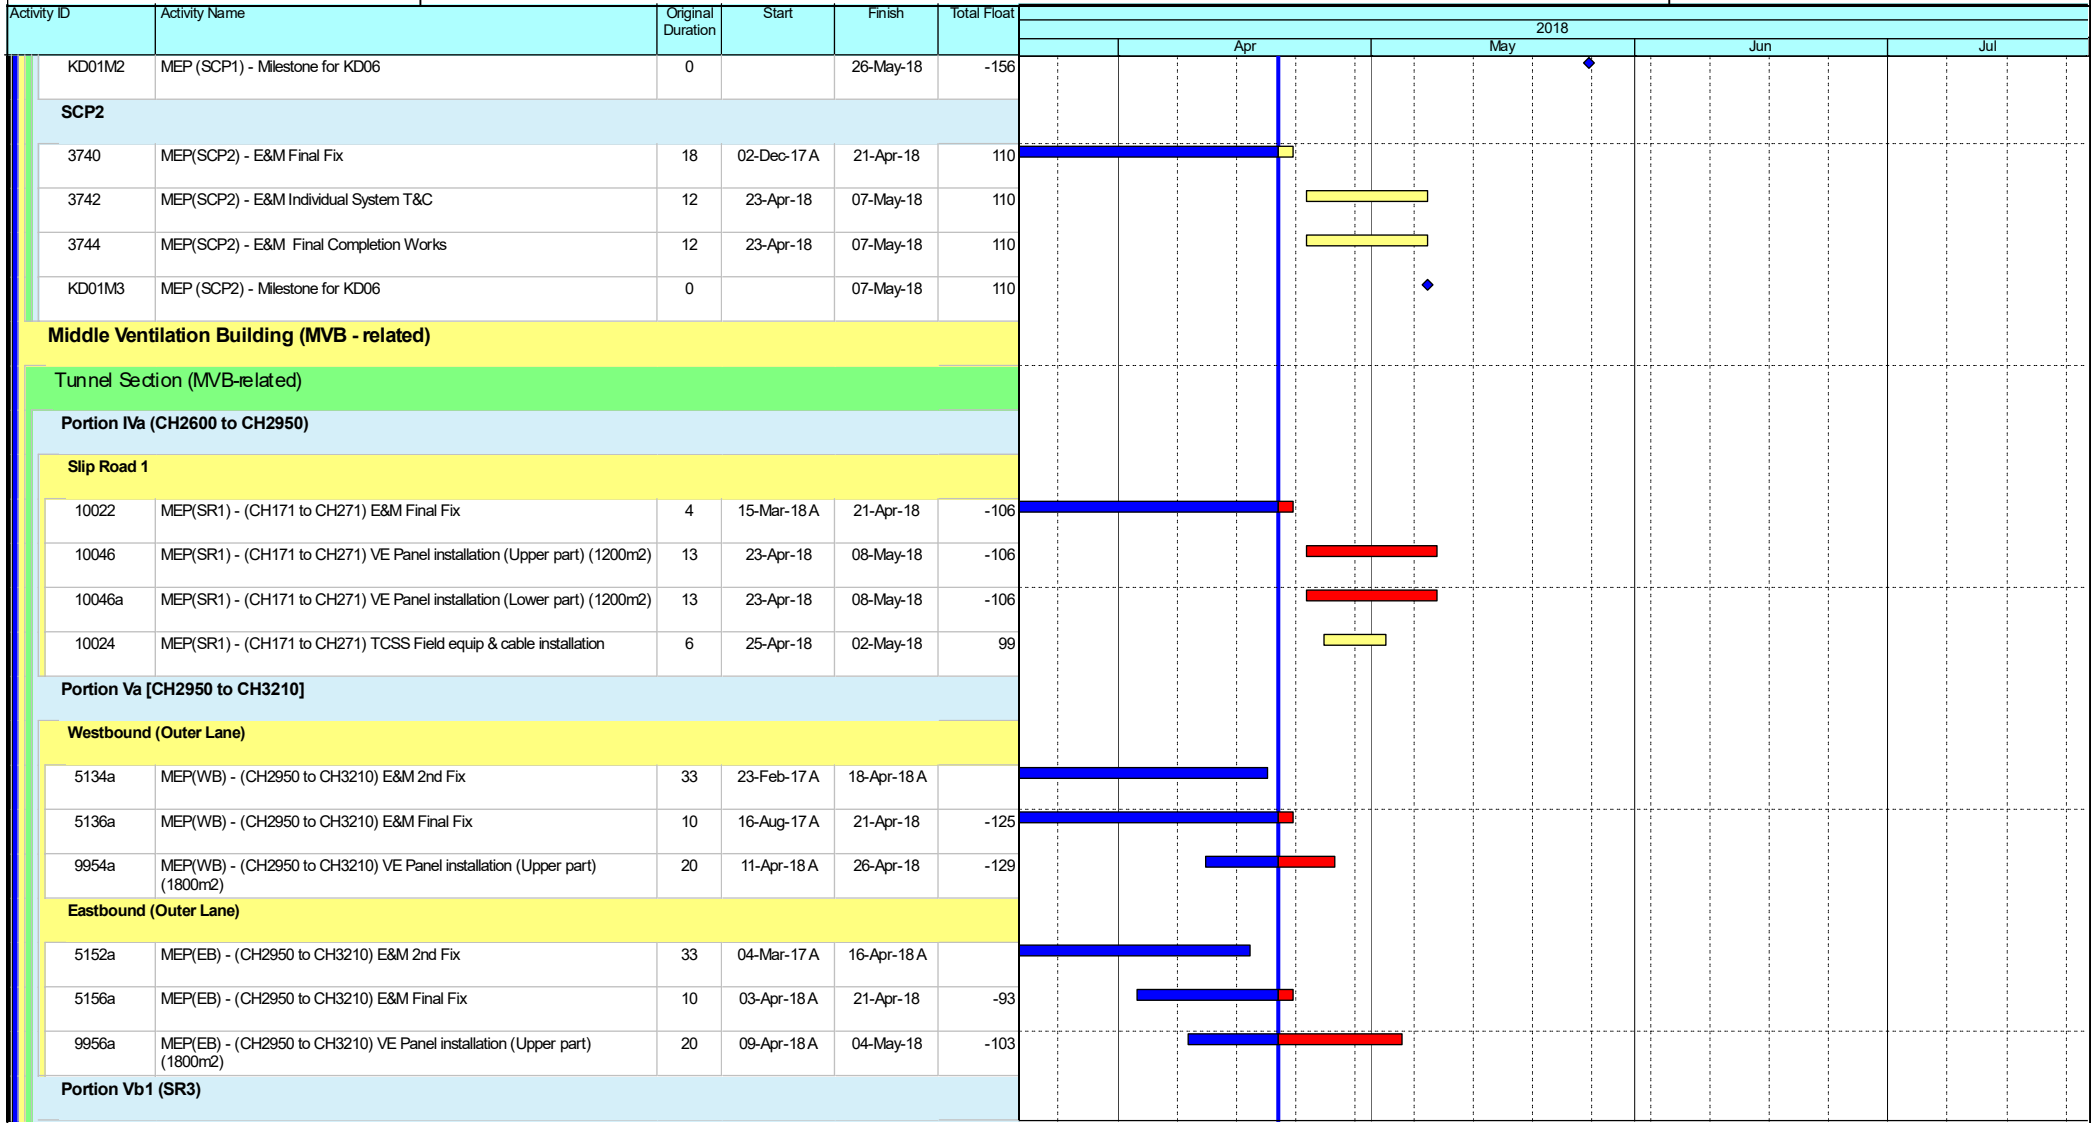

Leighton Contractors (Asia) Limited

Programme Update 50 (April 2018)

THREE MONTH ROLLING



Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 8 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

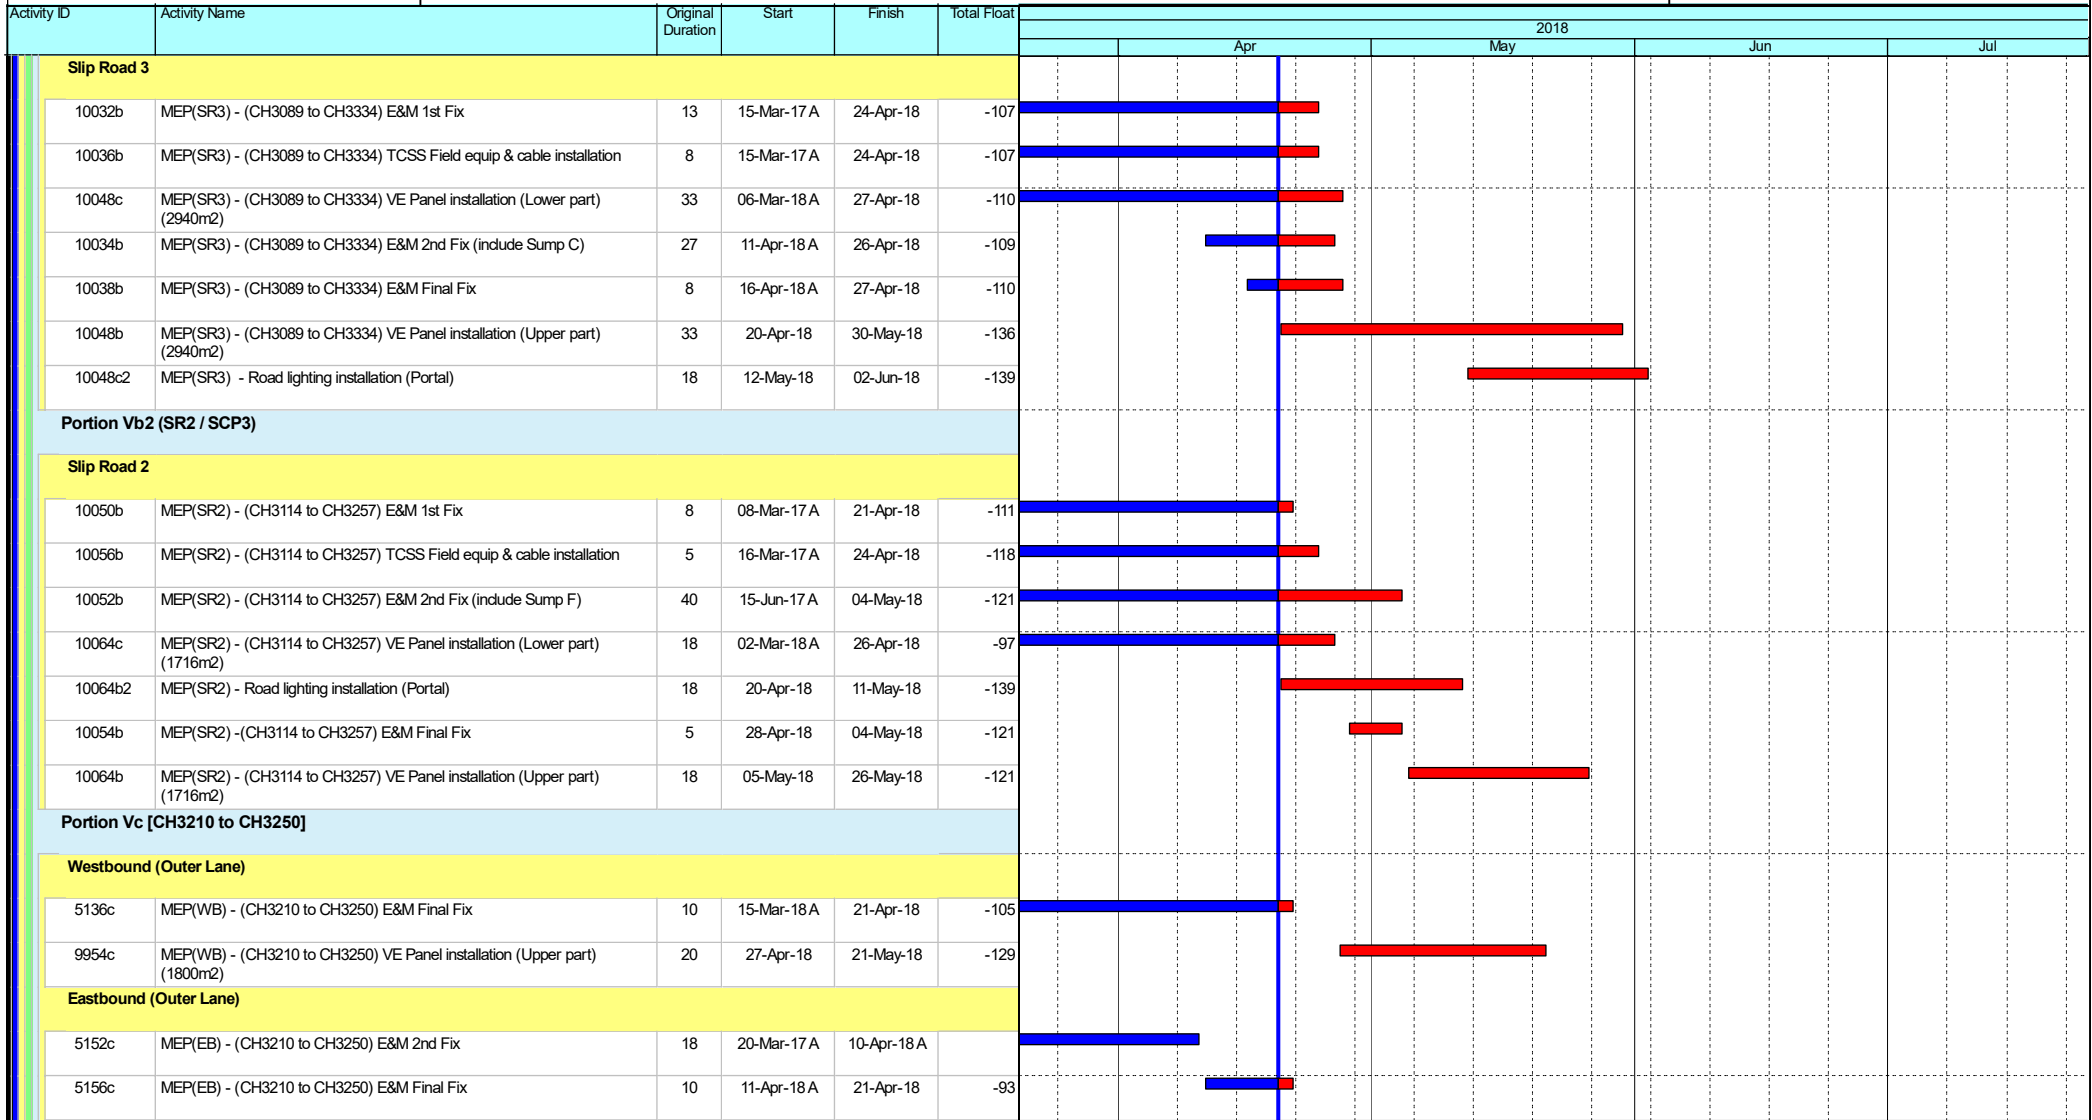

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING


Project ID: H2613-U050
Baseline: SA01
Layout: Update Three Month Rolling
U050
Page 9 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.



Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING

Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 10 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018					
						Apr	May	Jun	Jul		
Middle Ventilation Building (MVB)											
Establishment Works											
3220	MVB - Construct road and road drainage works in Area D & E	60	09-Nov-17 A	10-Apr-18 A							
External Facade											
3238	MVB - External facing tiles / Louvre	90	06-Nov-17 A	28-Apr-18	-162						
MEP Works											
3280	MEP(MVB) - Lift Installation	70	10-Nov-17 A	27-Apr-18	-290						
3236	MVB - Metal works / steel platform / Ladders / Handrails	48	06-Dec-17 A	26-Apr-18	-160						
3248	MEP(MVB) - TCSS Enabling Works (Remaining TCSS installation)	24	03-Jan-18 A	21-Apr-18	-277						
3252	MEP(MVB) - E&M Final Completion Works; Ready for Statutory Inspections	24	23-Apr-18	21-May-18	-180						
E&M Individual System T&C											
3250d	MEP(MVB) - CCMS SAT	12	07-Apr-18 A	02-May-18	-279						
3250a	MEP(MVB) - MVAC system	12	20-Apr-18	04-May-18	-275						
3250b	MEP(MVB) - TVS System Test	12	20-Apr-18	04-May-18	-275						
3250g	MEP(MVB) - SAT - UPS	6	23-Apr-18	28-Apr-18	-277						
3250h	MEP(MVB) - SAT - LV Capacitor Bank	6	23-Apr-18	28-Apr-18	-277						
3250m	MEP(MVB) - Damper control panel and tunnel motorized damper functional test	6	23-Apr-18	28-Apr-18	-277						
3250c	MEP(MVB) - Lift functional test	6	28-Apr-18	05-May-18	-233						
Basement 3 - APS Auxiliary Room / APS Plant Area 1 / APS Plant Area 2 (GL D - H)											
3302	APS(MVB) - E&M final fixing	24	01-Mar-18 A	23-Apr-18	-187						
Basement 3 - Other Rooms / General Area & Corridor											
3407	MEP(MVB) - E&M final fixing	18	12-Mar-18 A	21-Apr-18	-156						
Basement 3M - Sump Pit for ESP / Sump Pit for DENO2 (GL D - H)											
3296	APS(MVB) - Plant 4 ESP/DeNO2	24	13-Jan-18 A	02-May-18	-183						

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING

Project ID: H2613-U050
Baseline: SA01
Layout: Update Three Month Rolling
U050
Page 11 of 33


Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018											
						Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
Basement 3M - TVF Room																	
3307	APS(MVB) - Installation of TVF & Silencer	24	29-Dec-17 A	10-Apr-18 A													
3309	APS(MVB) - E&M Final Fix	18	07-Mar-18 A	21-Apr-18	-197												
Basement 3M - Other Rooms / General Area & Corridor																	
3311	MEP(MVB) - ABWF Works	18	02-Nov-17 A	11-Apr-18 A													
3313	MEP(MVB) - E&M 1st fixing	24	23-Nov-17 A	24-Apr-18	-158												
3315	MEP(MVB) - E&M 2nd fixing	24	20-Dec-17 A	26-Apr-18	-160												
3317	MEP(MVB) - E&M final fixing	24	07-Feb-18 A	04-May-18	-166												
Basement 2 (GL D - H)																	
Basement 2 - Other Rooms / General Area & Corridor																	
19028	MEP(MVB) - ABWF Works	12	15-Nov-17 A	03-Apr-18 A													
19030	MEP(MVB) - E&M 1st fixing	18	28-Nov-17 A	24-Apr-18	-158												
19032	MEP(MVB) - E&M 2nd fixing	18	19-Dec-17 A	26-Apr-18	-160												
19034	MEP(MVB) - E&M final fixing	18	12-Feb-18 A	02-May-18	-164												
Basement 2M (GL D - H)																	
Basement 2M - Other Rooms / General Area & Corridor																	
19045	MEP(MVB) - ABWF Works	12	18-Nov-17 A	02-Apr-18 A													
19047	MEP(MVB) - E&M 1st fixing	18	02-Dec-17 A	26-Apr-18	-160												
19049	MEP(MVB) - E&M 2nd fixing	18	19-Dec-17 A	02-May-18	-164												
19051	MEP(MVB) - E&M final fixing	18	07-Mar-18 A	04-May-18	-166												
Basement 1 (GL D - H)																	
Other Rooms / General Area & Corridor																	
11312	MEP(MVB) - ABWF Works	18	19-Aug-17 A	11-Apr-18 A													
11314	MEP(MVB) - E&M 1st fixing	24	13-Oct-17 A	24-Apr-18	-158												



Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
Baseline: SA01
Layout: Update Three Month Rolling
U050
Page 12 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

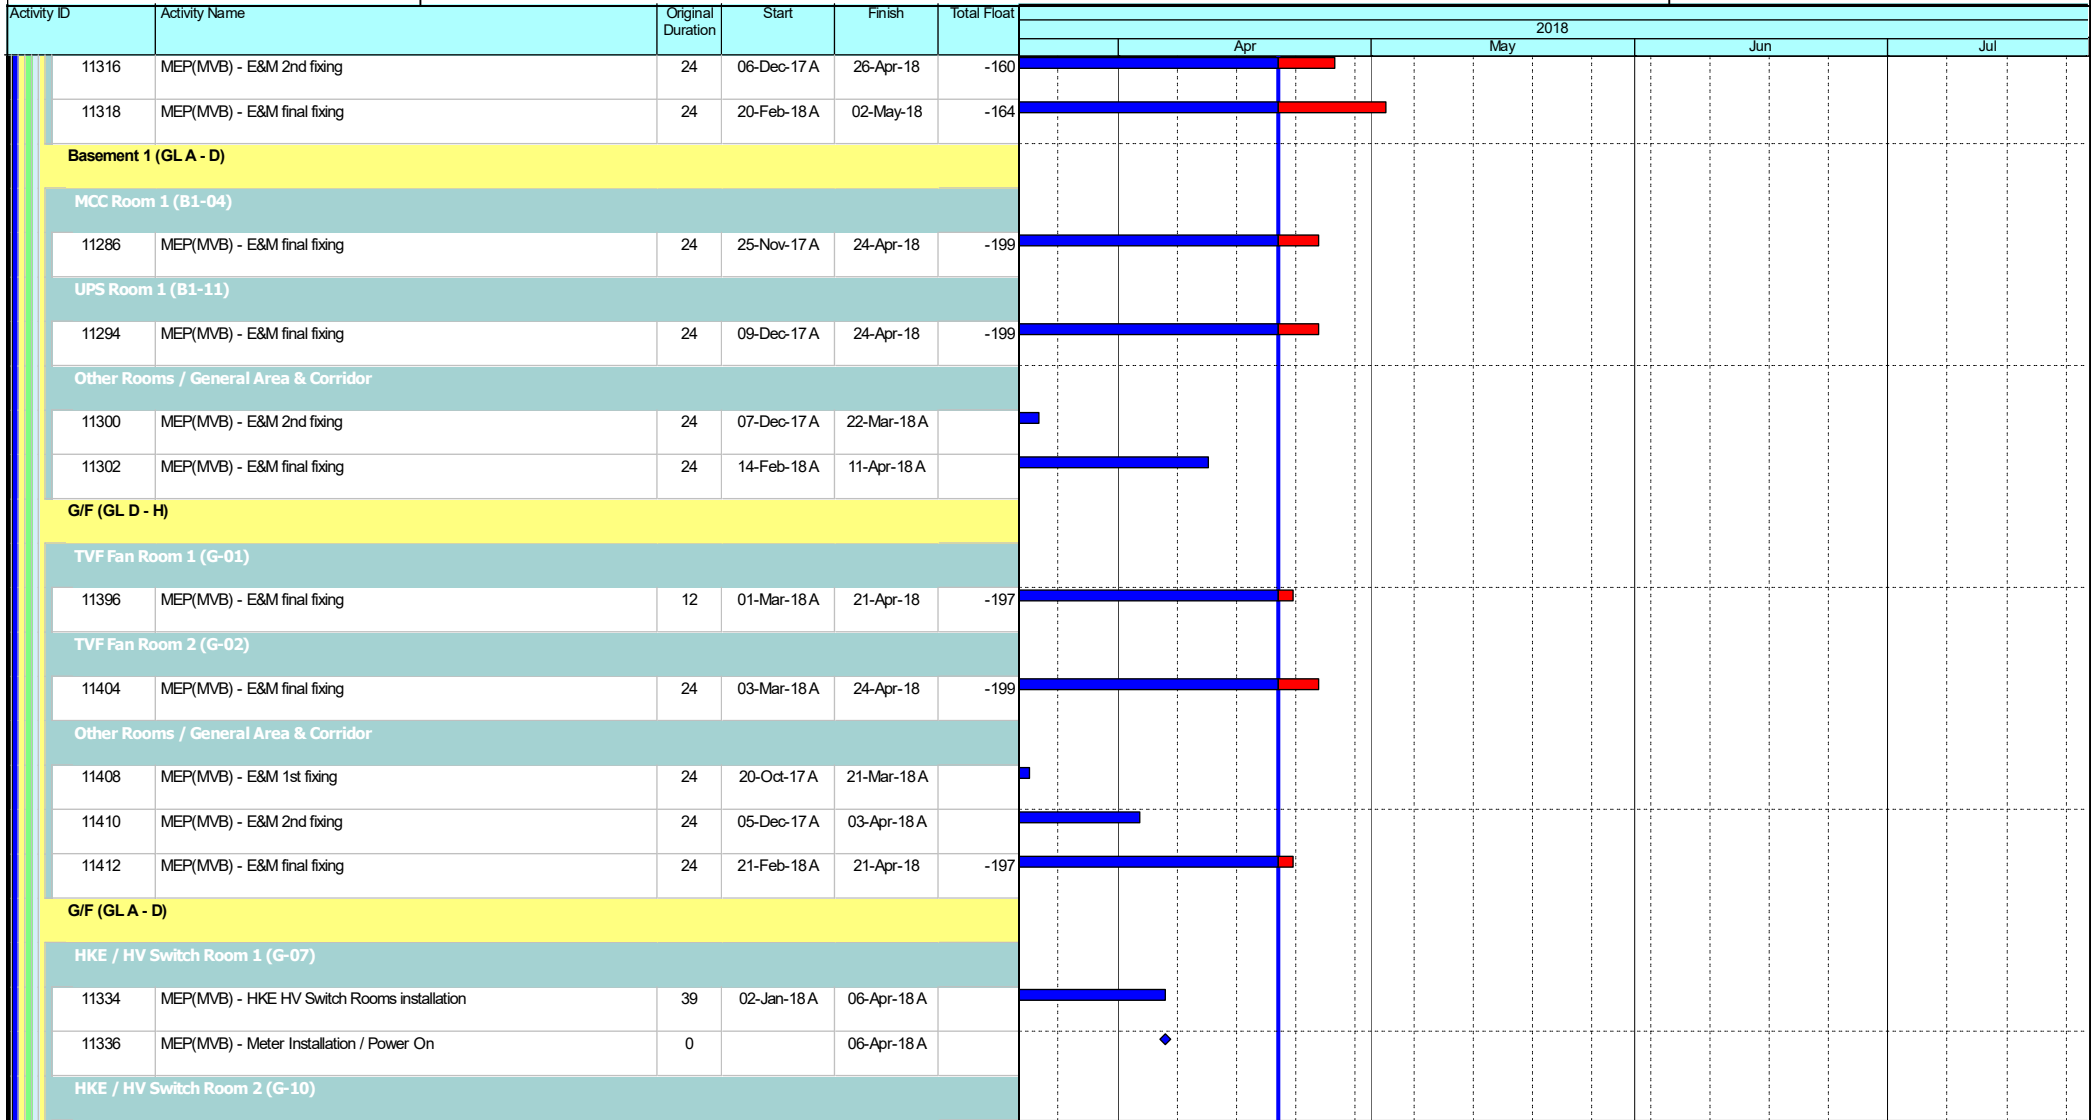

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
Baseline: SA01
Layout: Update Three Month Rolling
U050
Page 13 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

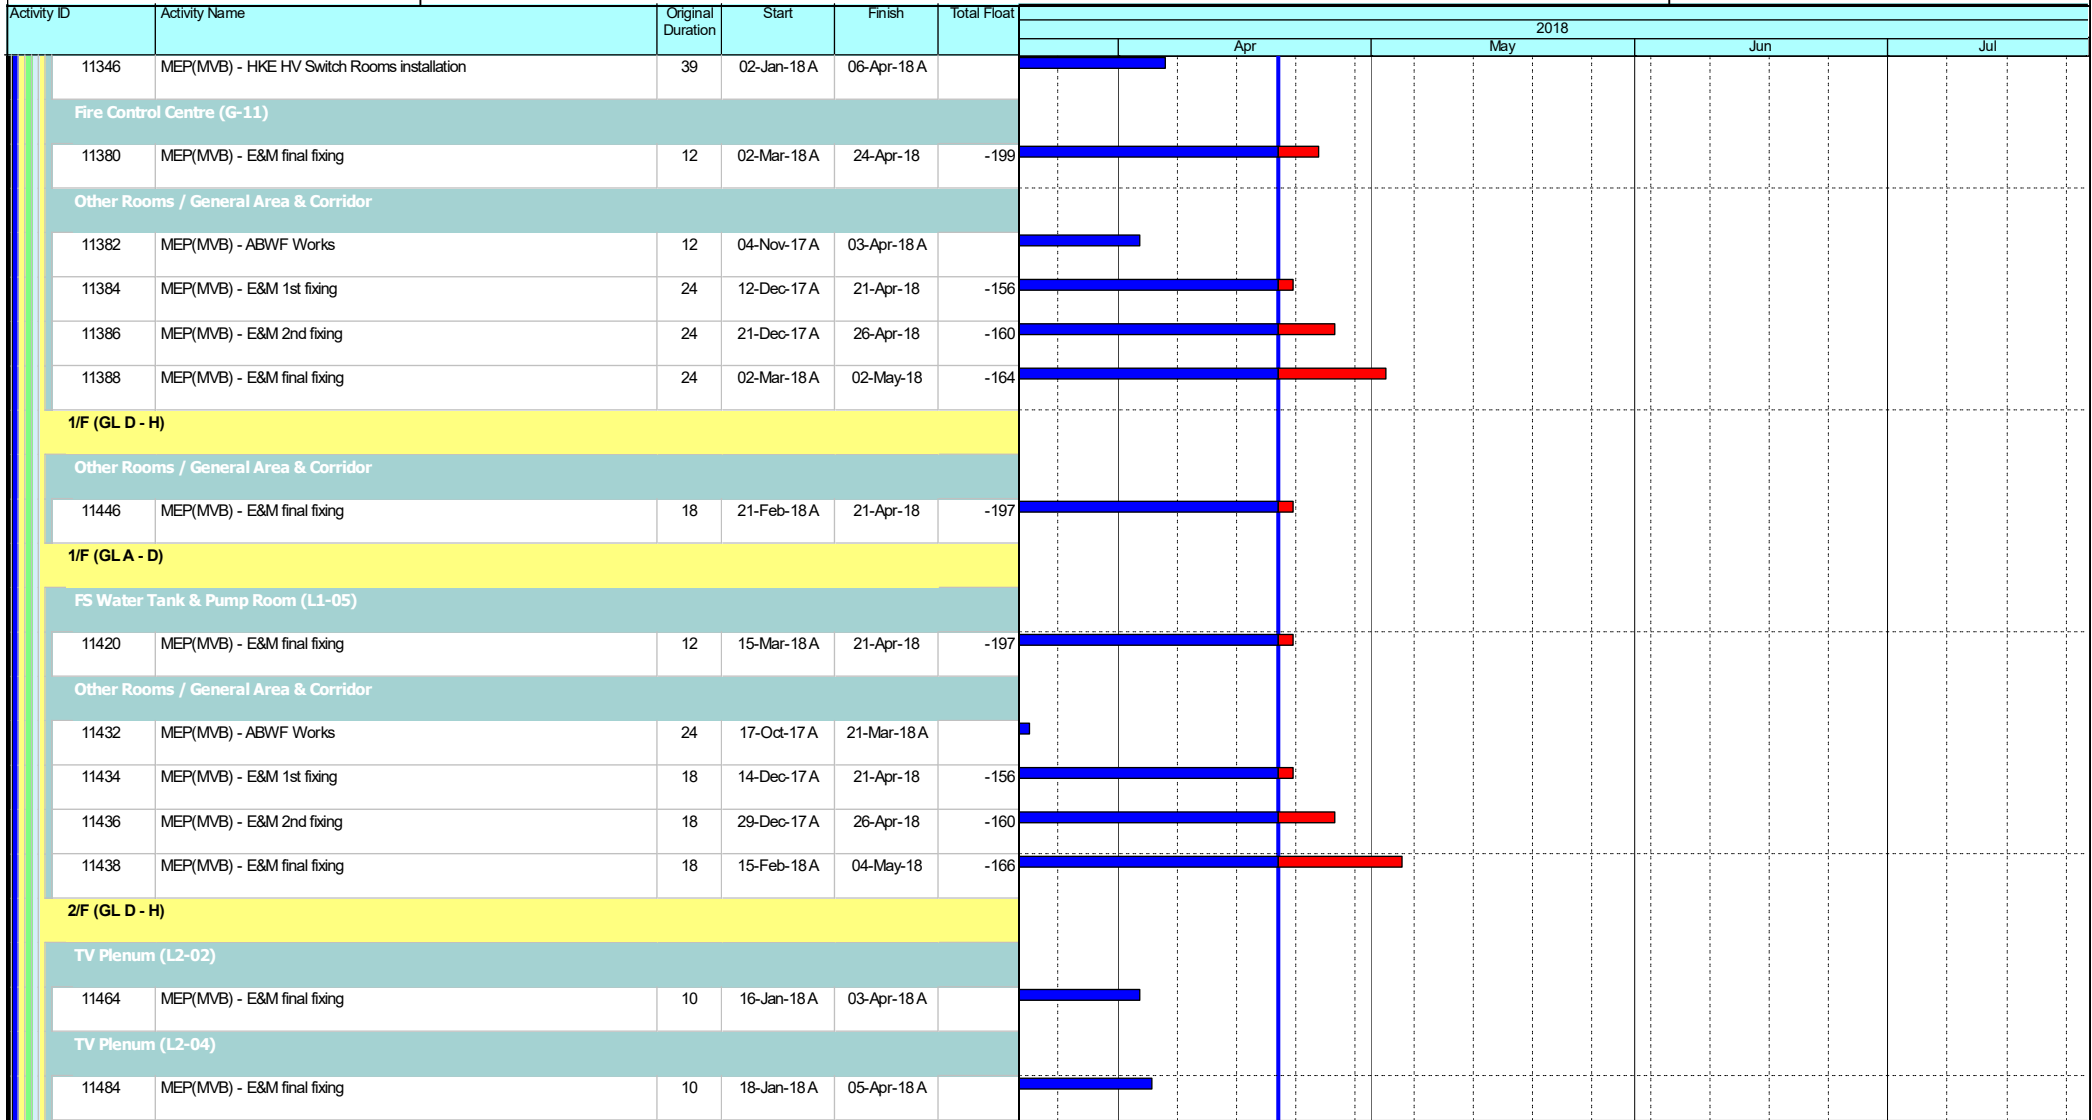

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 14 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

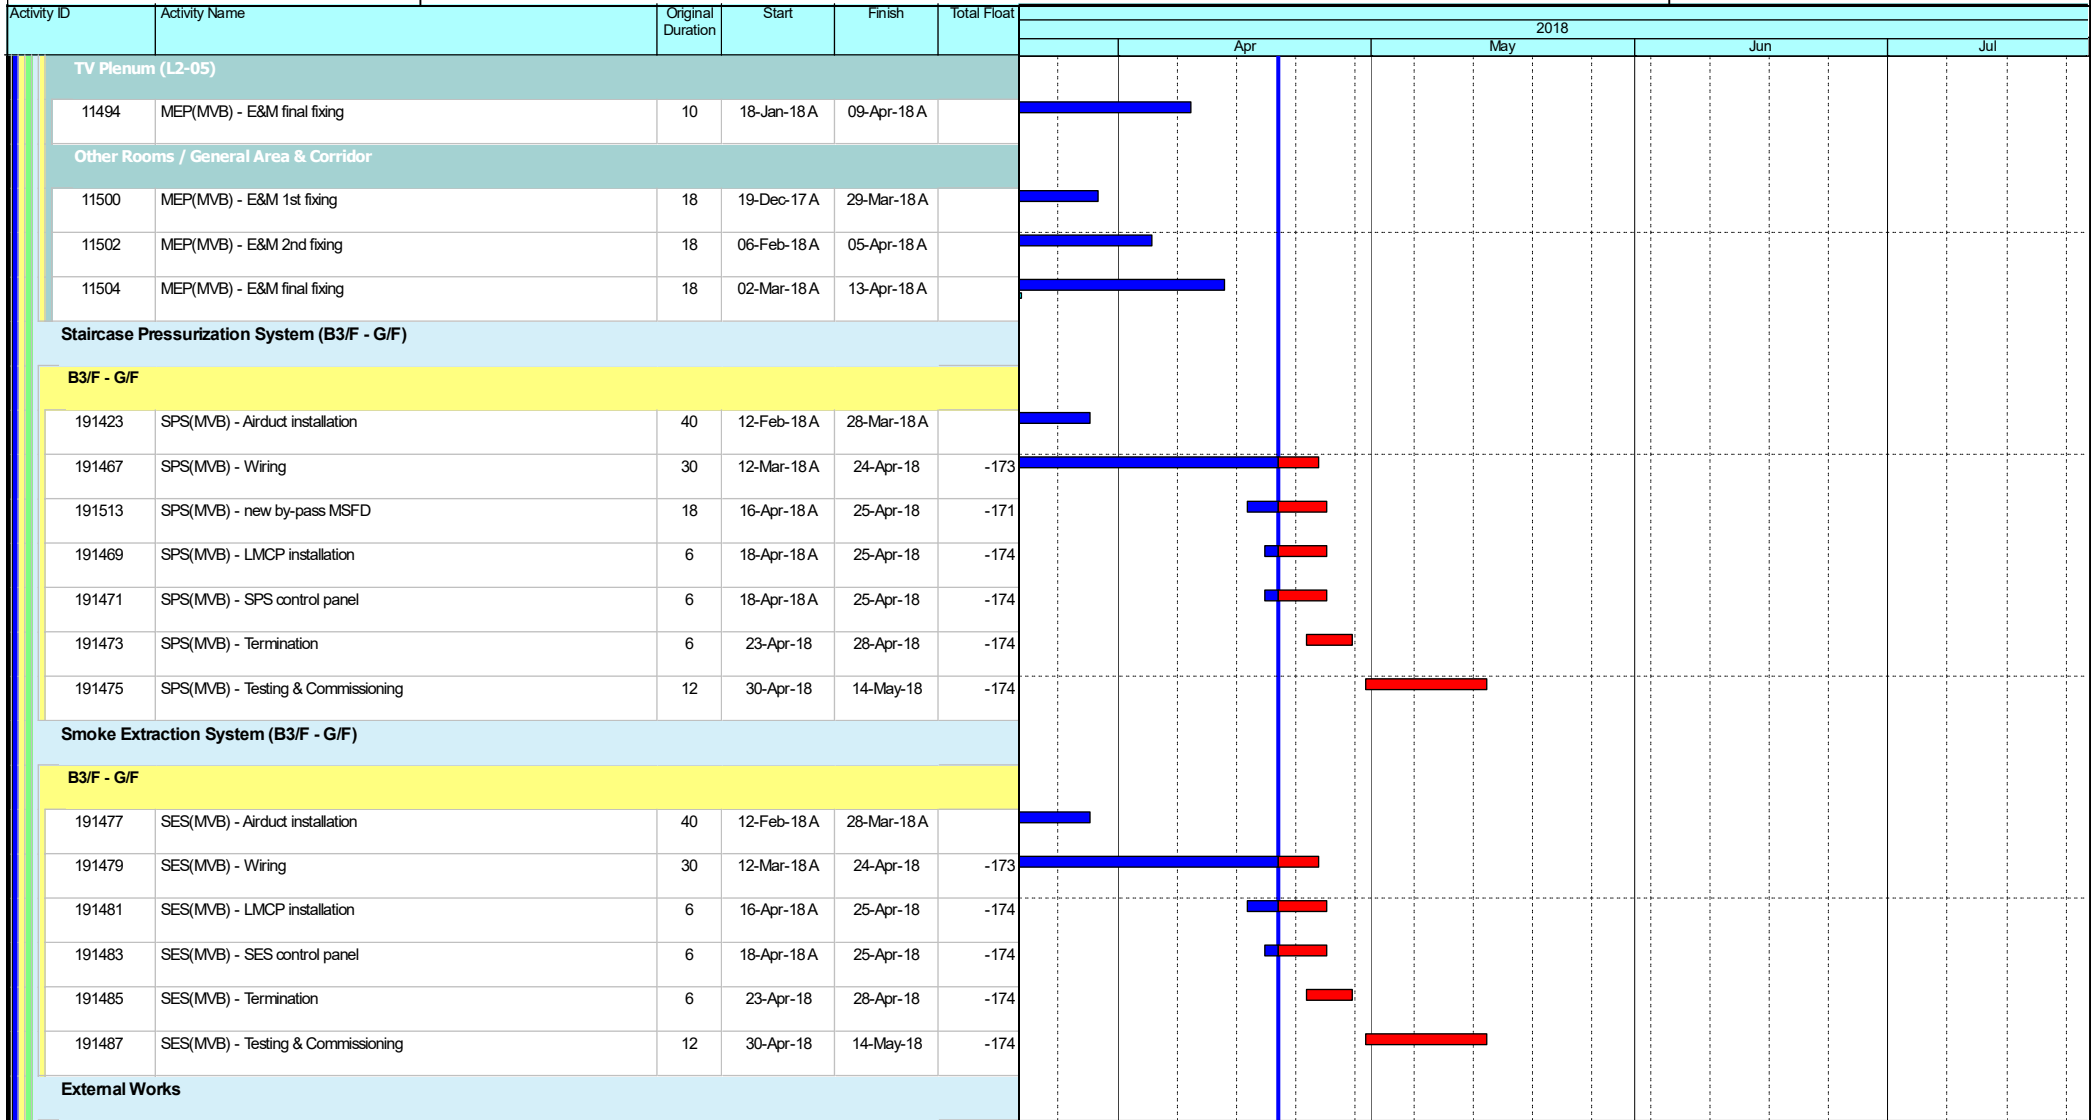

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 15 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

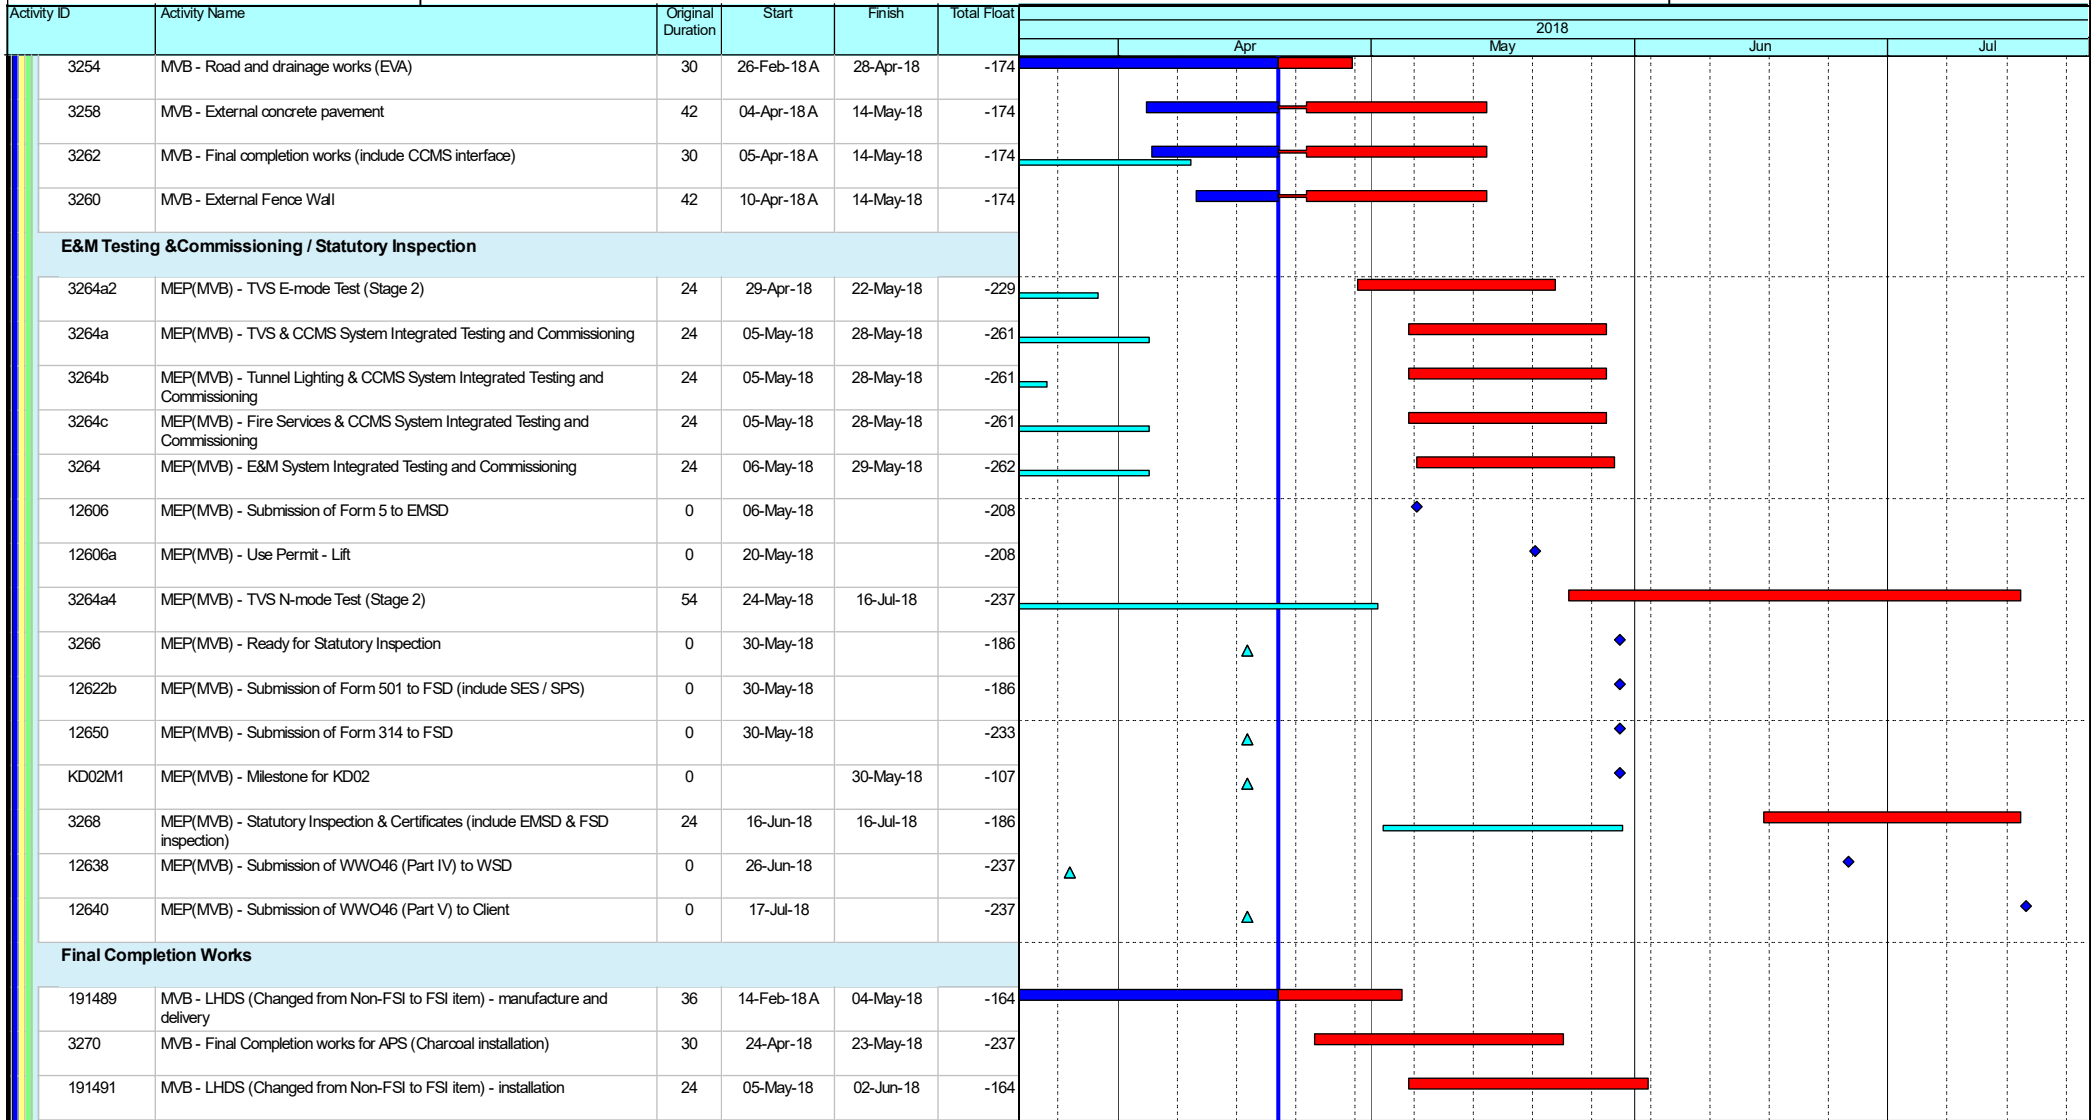

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING

Project ID: H2613-U050
Baseline: SA01
Layout: Update Three Month Rolling
U050
Page 16 of 33


Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Apr	May	Jun	Jul
3288	MVB - Completion of Section 1 (KD06)	0		30-May-18	-107				
3272	MVB - APS Site Acceptance Testing (Air monitoring station)	30	01-Jun-18	30-Jun-18	17				
191493	MVB - LHDS (Changed from Non-FSI to FSI item) - T&C	12	04-Jun-18	16-Jun-18	-164				
KD04M3	APS SAT (MVB) - Milestone for KD04	0		30-Jun-18	78				
Landscaping and Irrigation System									
3276	MVB - Final completion test for irrigation systems in Portion IVa and IVb	60	03-May-18	01-Jul-18	-348				
3278	MVB - Landscape Works in Portion IVa and IVb	60	02-Jul-18	30-Aug-18	-348				
Tunnel Flexible Pavement (MVB-related)									
5808	Road(WB) - (CH2600 to CH3770) Flexible Pavement	12	15-Mar-18 A	03-Apr-18 A					
Portion IVa Road Surface Area									
19046	TCSS equipment installation & cabling	96	02-Nov-17 A	26-Apr-18	-211				
19052	Lighting equipment Testing & Commissioning	24	15-Dec-17 A	26-Apr-18	-85				
191523	WDII area access	0	20-Apr-18*		-208				
191525	WDII area - TCSS equipment / signage / lumimeter installation, cabling & termination	24	20-Apr-18	18-May-18	-208				
19048	TCSS equipment Testing & Commissioning	70	27-Apr-18	21-Jul-18	-211				
191527	WDII area - TCSS SCT	24	19-May-18	16-Jun-18	-208				
191529	WDII area - TCSS SAT	24	19-Jun-18	17-Jul-18	-208				
Satellite Control Point 3									
SCP3									
3766	MEP(SCP3) - E&M Final Fix	12	12-Dec-17 A	21-Apr-18	-164				
10110	MEP(SCP3) - TCSS Enabling Works (Remaining TCSS installation)	12	20-Apr-18	04-May-18	-158				
3774	SCP3 - Metal works / Glazing / Louver / Handrails	12	23-Apr-18	07-May-18	-164				
3768	MEP(SCP3) - E&M Individual System T&C	12	08-May-18	21-May-18	-164				
3770	MEP(SCP3) - E&M Final Completion Works; Ready for Statutory Inspections	12	23-May-18	05-Jun-18	-164				



Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
Baseline: SA01
Layout: Update Three Month Rolling
U050
Page 17 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

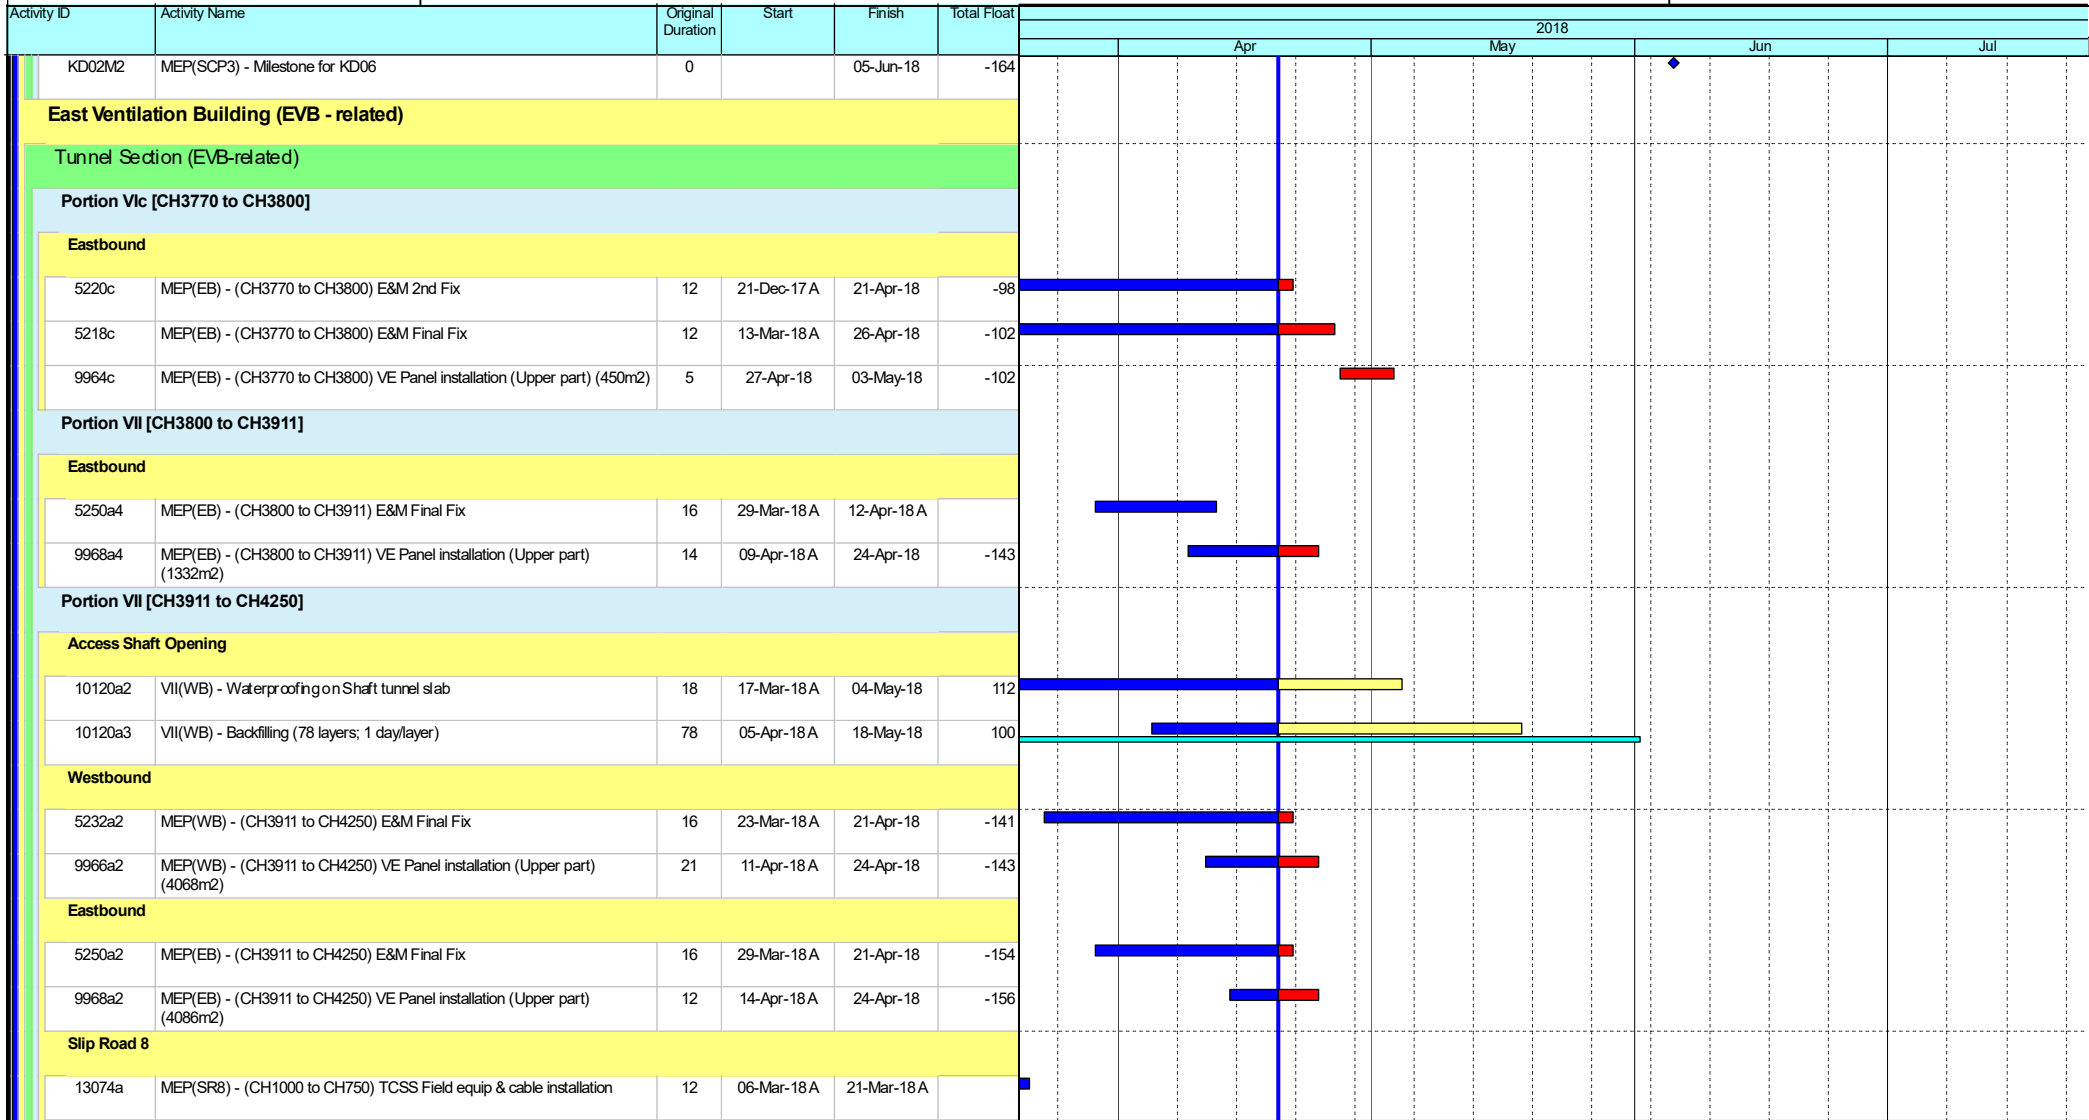

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 18 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

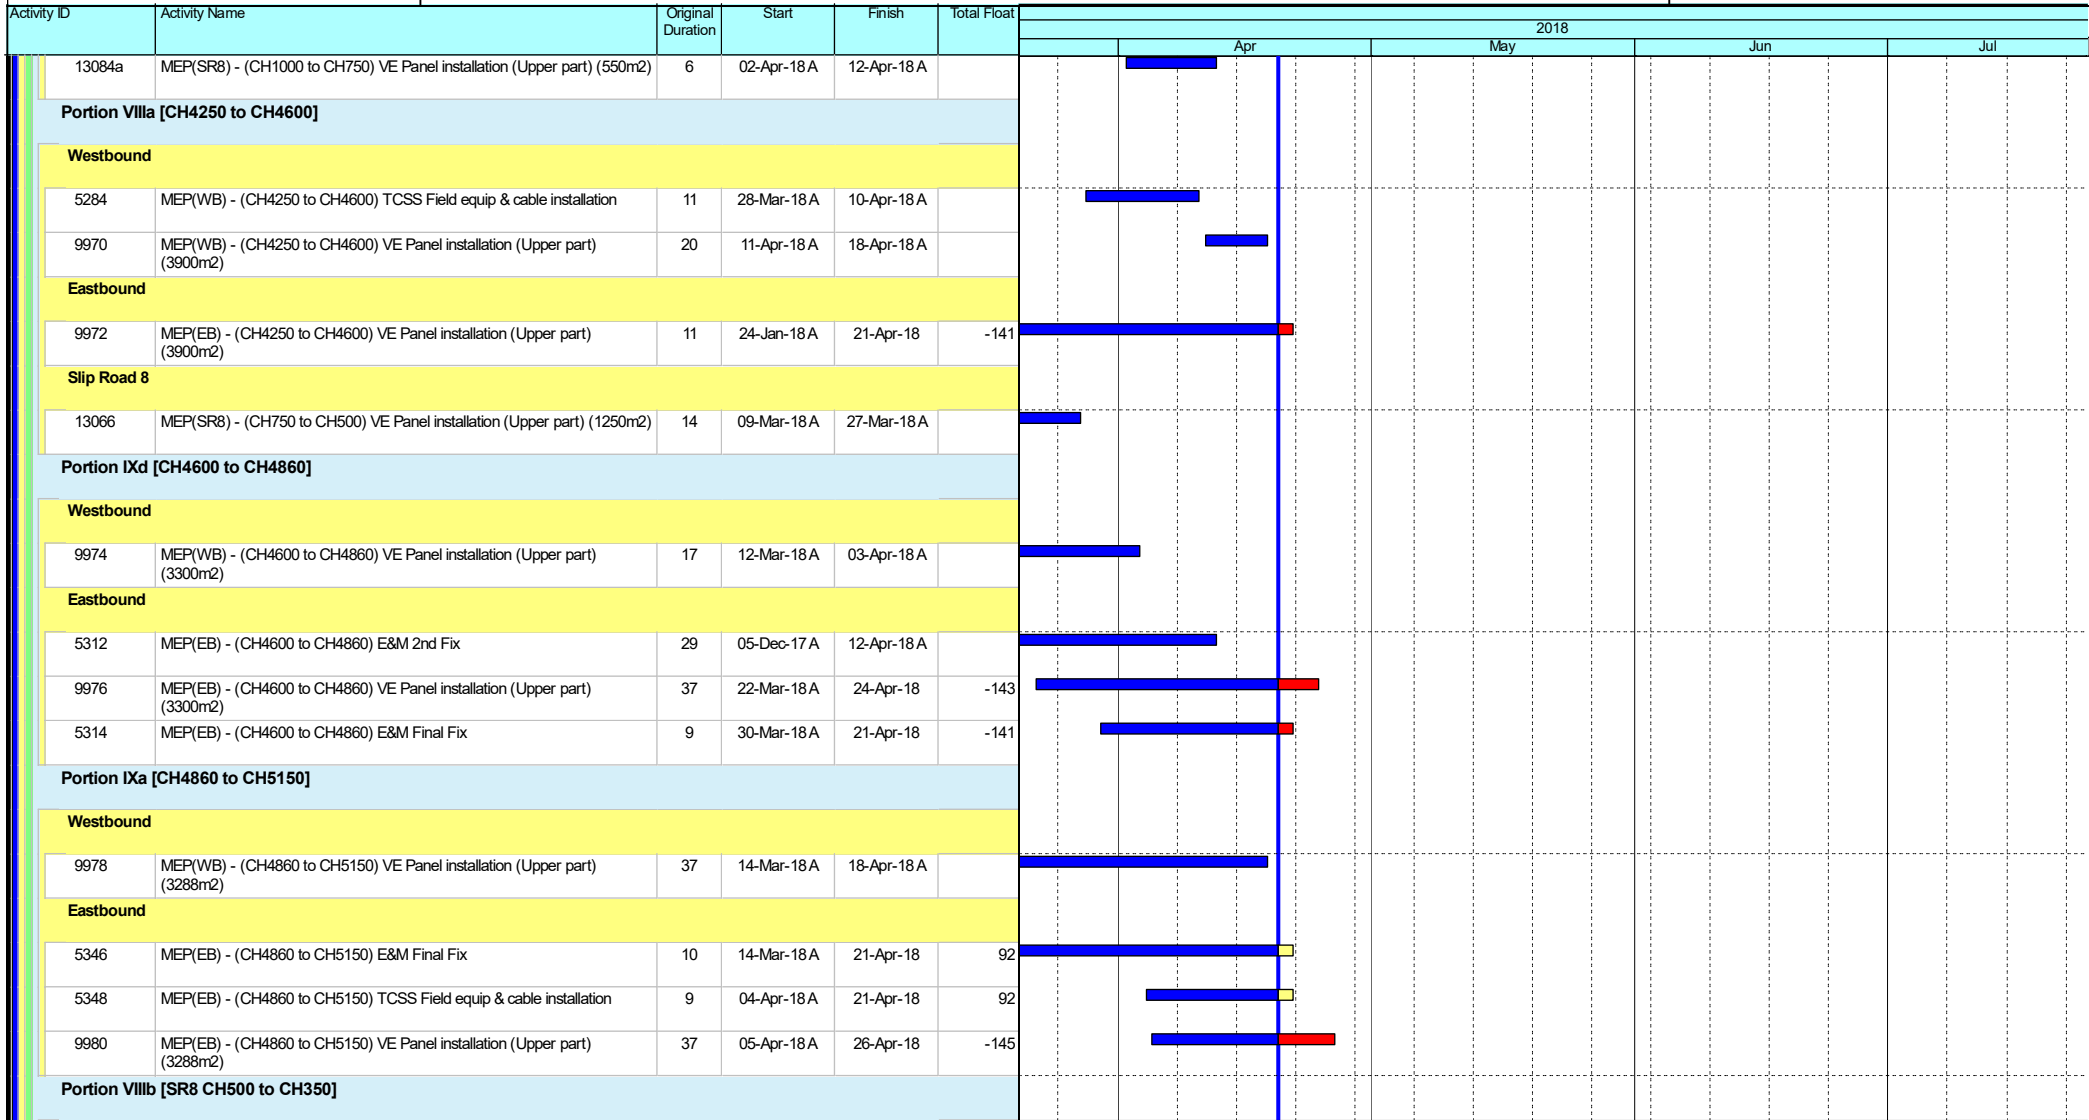

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 19 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

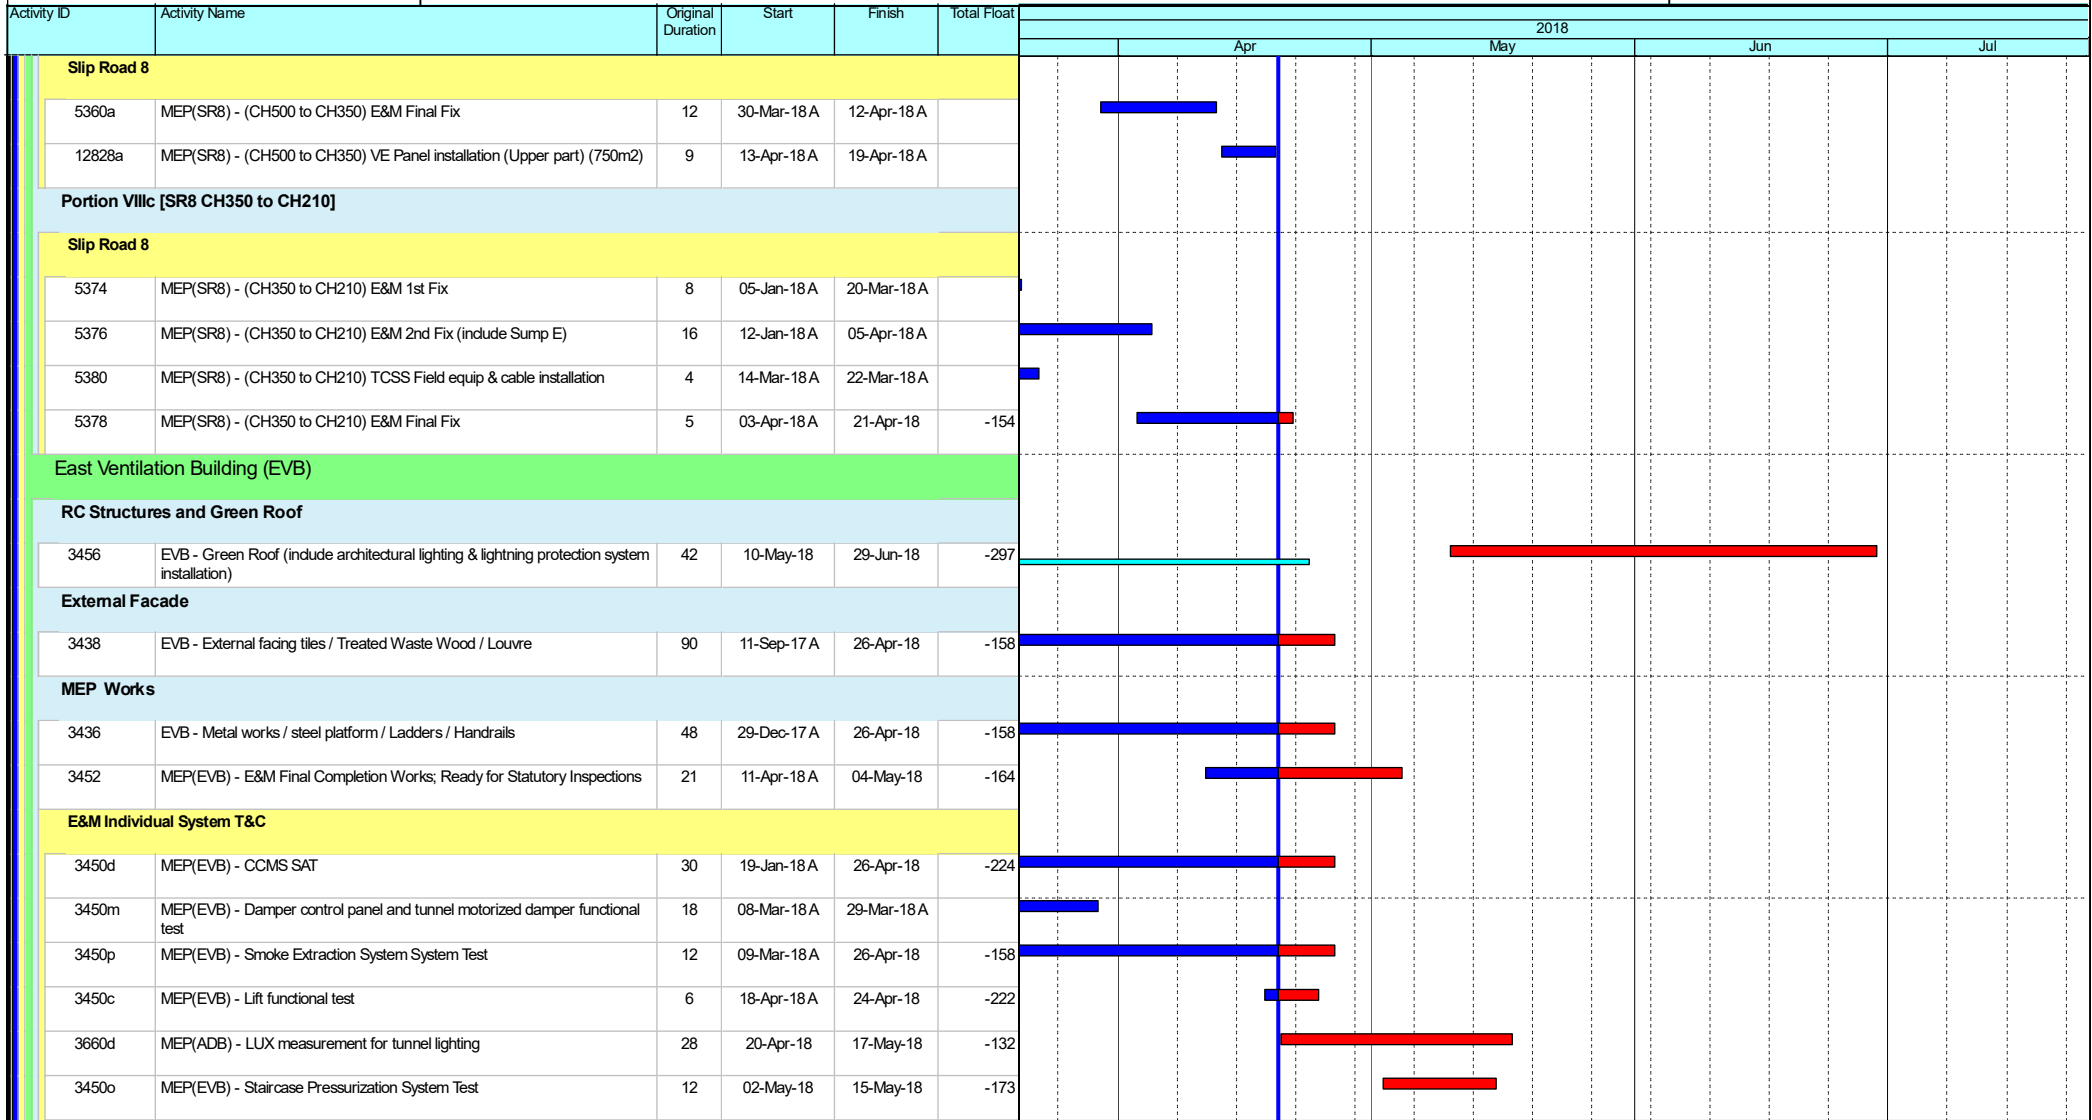

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING

Project ID: H2613-U050
Baseline: SA01
Layout: Update Three Month Rolling
U050
Page 20 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018												
						Apr	May	Jun	Jul									
Basement 2 - APSAuxiliary Room / APS Plant Area 1 / APS Plant Area 2 / APS Plant Area 3																		
3560	APS(EVB) - E&M final fixing	24	07-Mar-18 A	05-Apr-18 A		█												
Basement 1 (GL D - L)																		
Water Tank & Pump Room (B1-16)																		
11636	MEP(EVB) - E&M final fixing	24	04-Nov-17 A	21-Apr-18	-154	█	█	█	█	█	█	█	█	█	█	█	█	█
TVF Room 3 (B1-19)																		
11628a	MEP(EVB) - Thermal enclosure for actuator manufacture and delivery	21	22-Feb-18 A	06-Apr-18 A		█												
11628a2	MEP(EVB) - Thermal enclosure for actuator Installation and termination	10	07-Apr-18 A	16-Apr-18 A			█											
11628a4	MEP(EVB) - Thermal enclosure for actuator T&C	6	17-Apr-18 A	21-Apr-18	-195			█	█									
1/F (GL A - D)																		
Other Rooms / General Area & Corridor																		
11776	MEP(EVB) - E&M 2nd fixing	30	24-Nov-17 A	30-Mar-18 A		█												
11778	MEP(EVB) - E&M final fixing	30	12-Dec-17 A	11-Apr-18 A		█	█											
Staircase Pressurization System (B2/F - G/F)																		
B2/F - G/F																		
191345	SPS(EVB) - Airduct work and FRP enclosure	20	15-Mar-18 A	21-Apr-18	-166	█	█	█	█	█	█	█	█	█	█	█	█	█
191387	SPS(EVB) - Final connection of air duct after modification of air vent shaft	18	28-Mar-18 A	30-Apr-18	-173		█	█	█	█	█	█	█	█	█	█	█	█
External Works																		
3454	EVB - Road and drainage works (EVA)	24	09-Nov-17 A	24-Apr-18	-156	█	█	█	█	█	█	█	█	█	█	█	█	█
3462	EVB - Final completion works (include CCMS interface)	30	17-Jan-18 A	14-May-18	-172	█	█	█	█	█	█	█	█	█	█	█	█	█
3458	EVB - External concrete pavement	24	24-Feb-18 A	26-Apr-18	-158	█	█	█	█	█	█	█	█	█	█	█	█	█
E&M Testing & Commissioning / Statutory Inspection																		
3464a	MEP(EVB) - TVS & CCMS System Integrated Testing and Commissioning	36	26-Mar-18 A	07-May-18	-211	█	█	█	█	█	█	█	█	█	█	█	█	█
3464b	MEP(EVB) - Tunnel Lighting & CCMS System Integrated Testing and Commissioning	24	26-Mar-18 A	07-May-18	-211	█	█	█	█	█	█	█	█	█	█	█	█	█

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 21 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

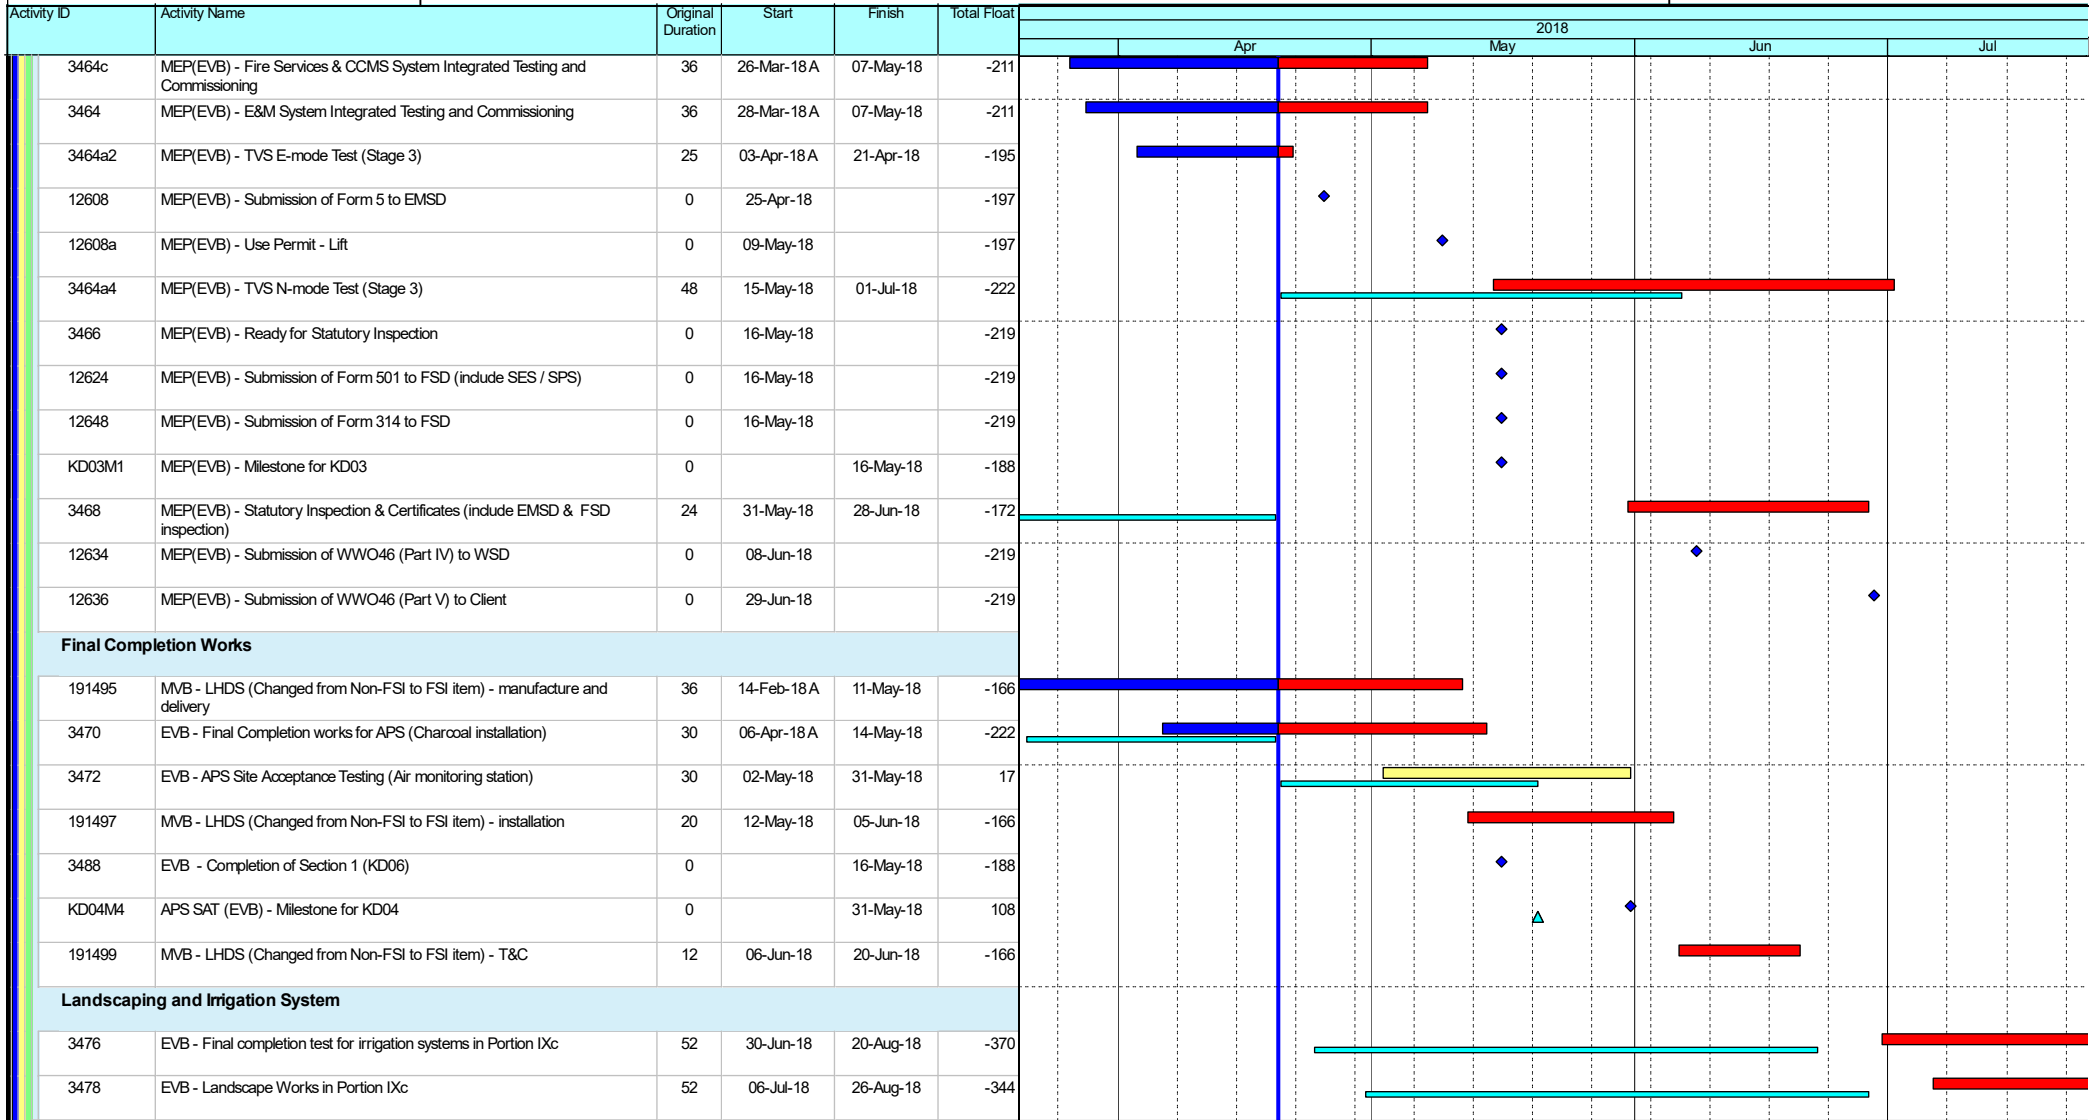

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 22 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

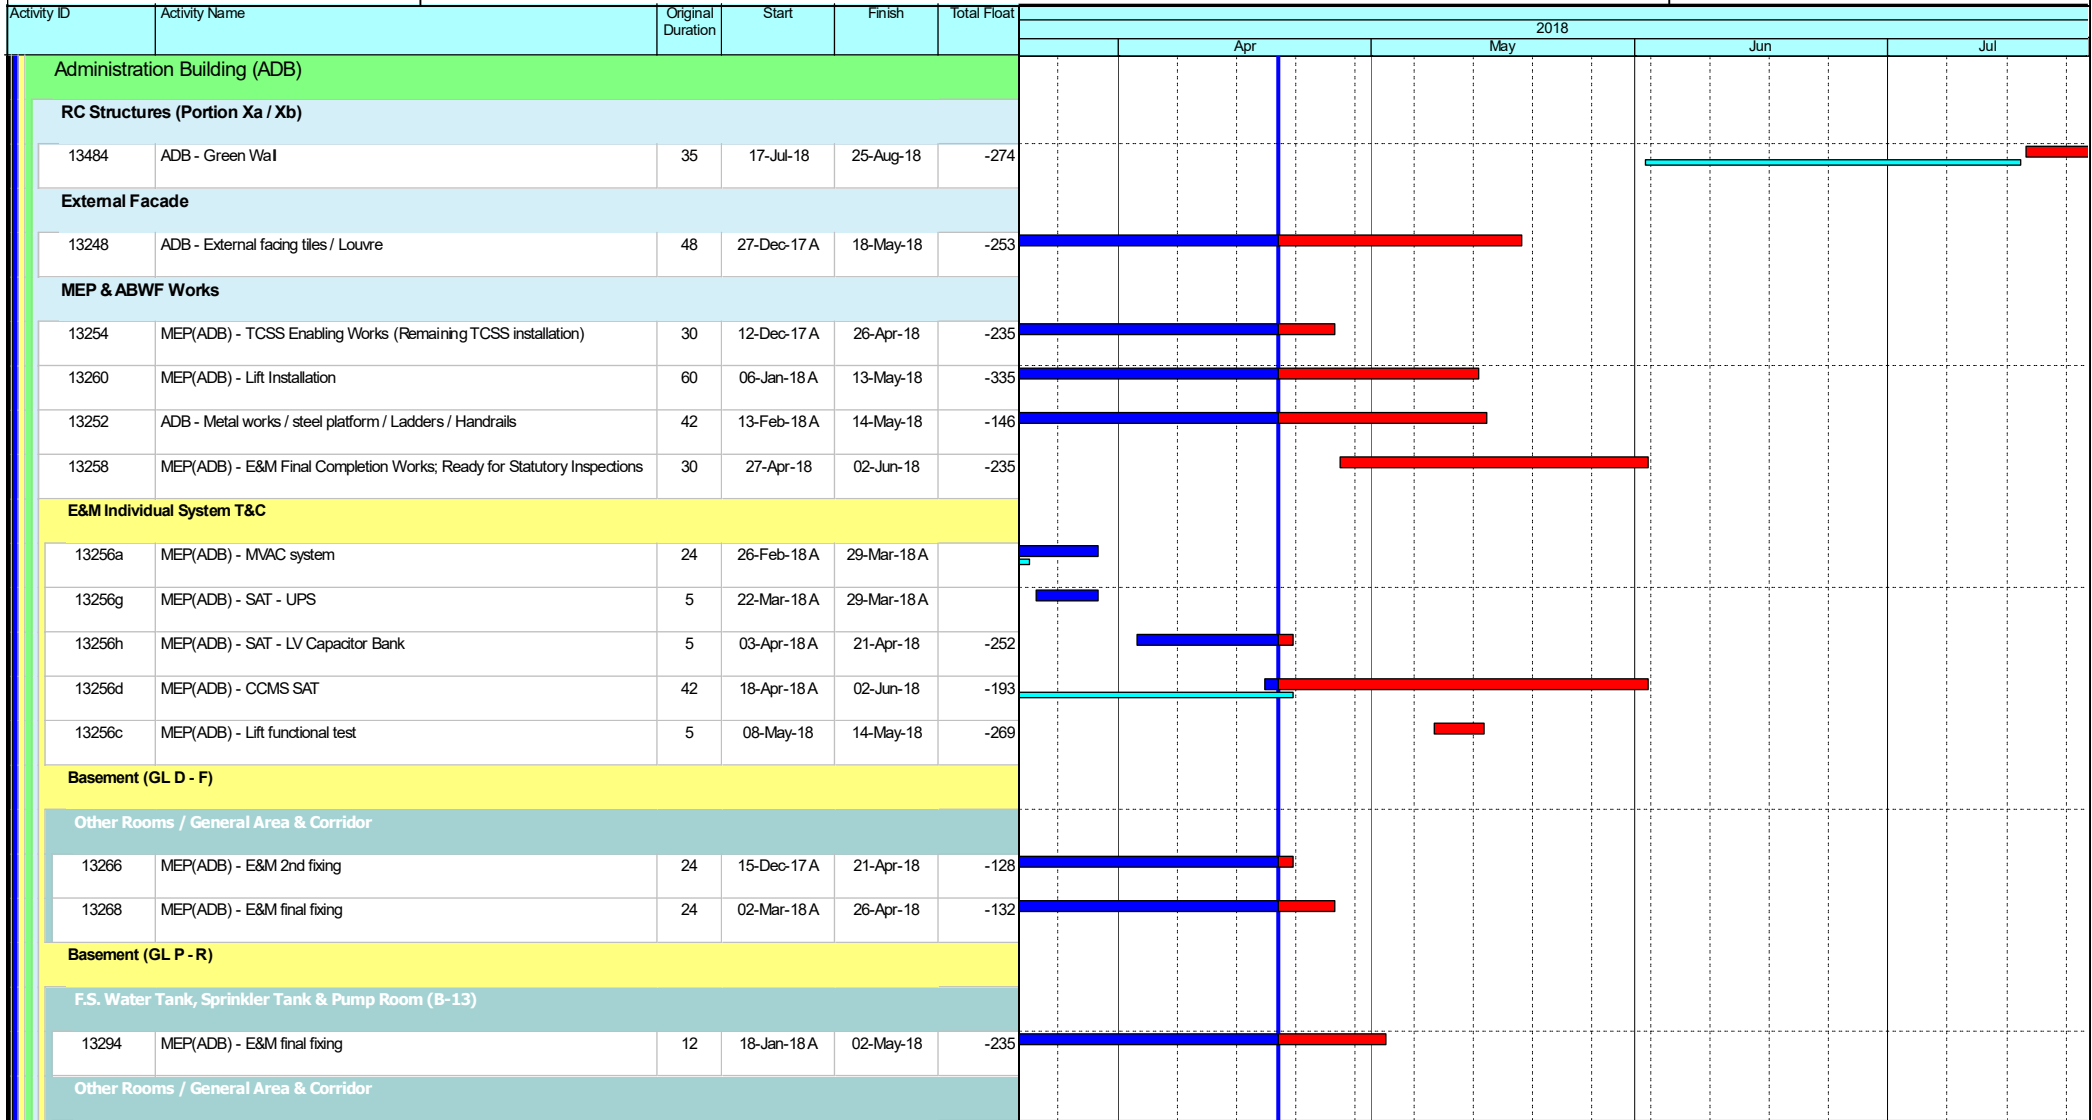

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
Baseline: SA01
Layout: Update Three Month Rolling
U050
Page 23 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

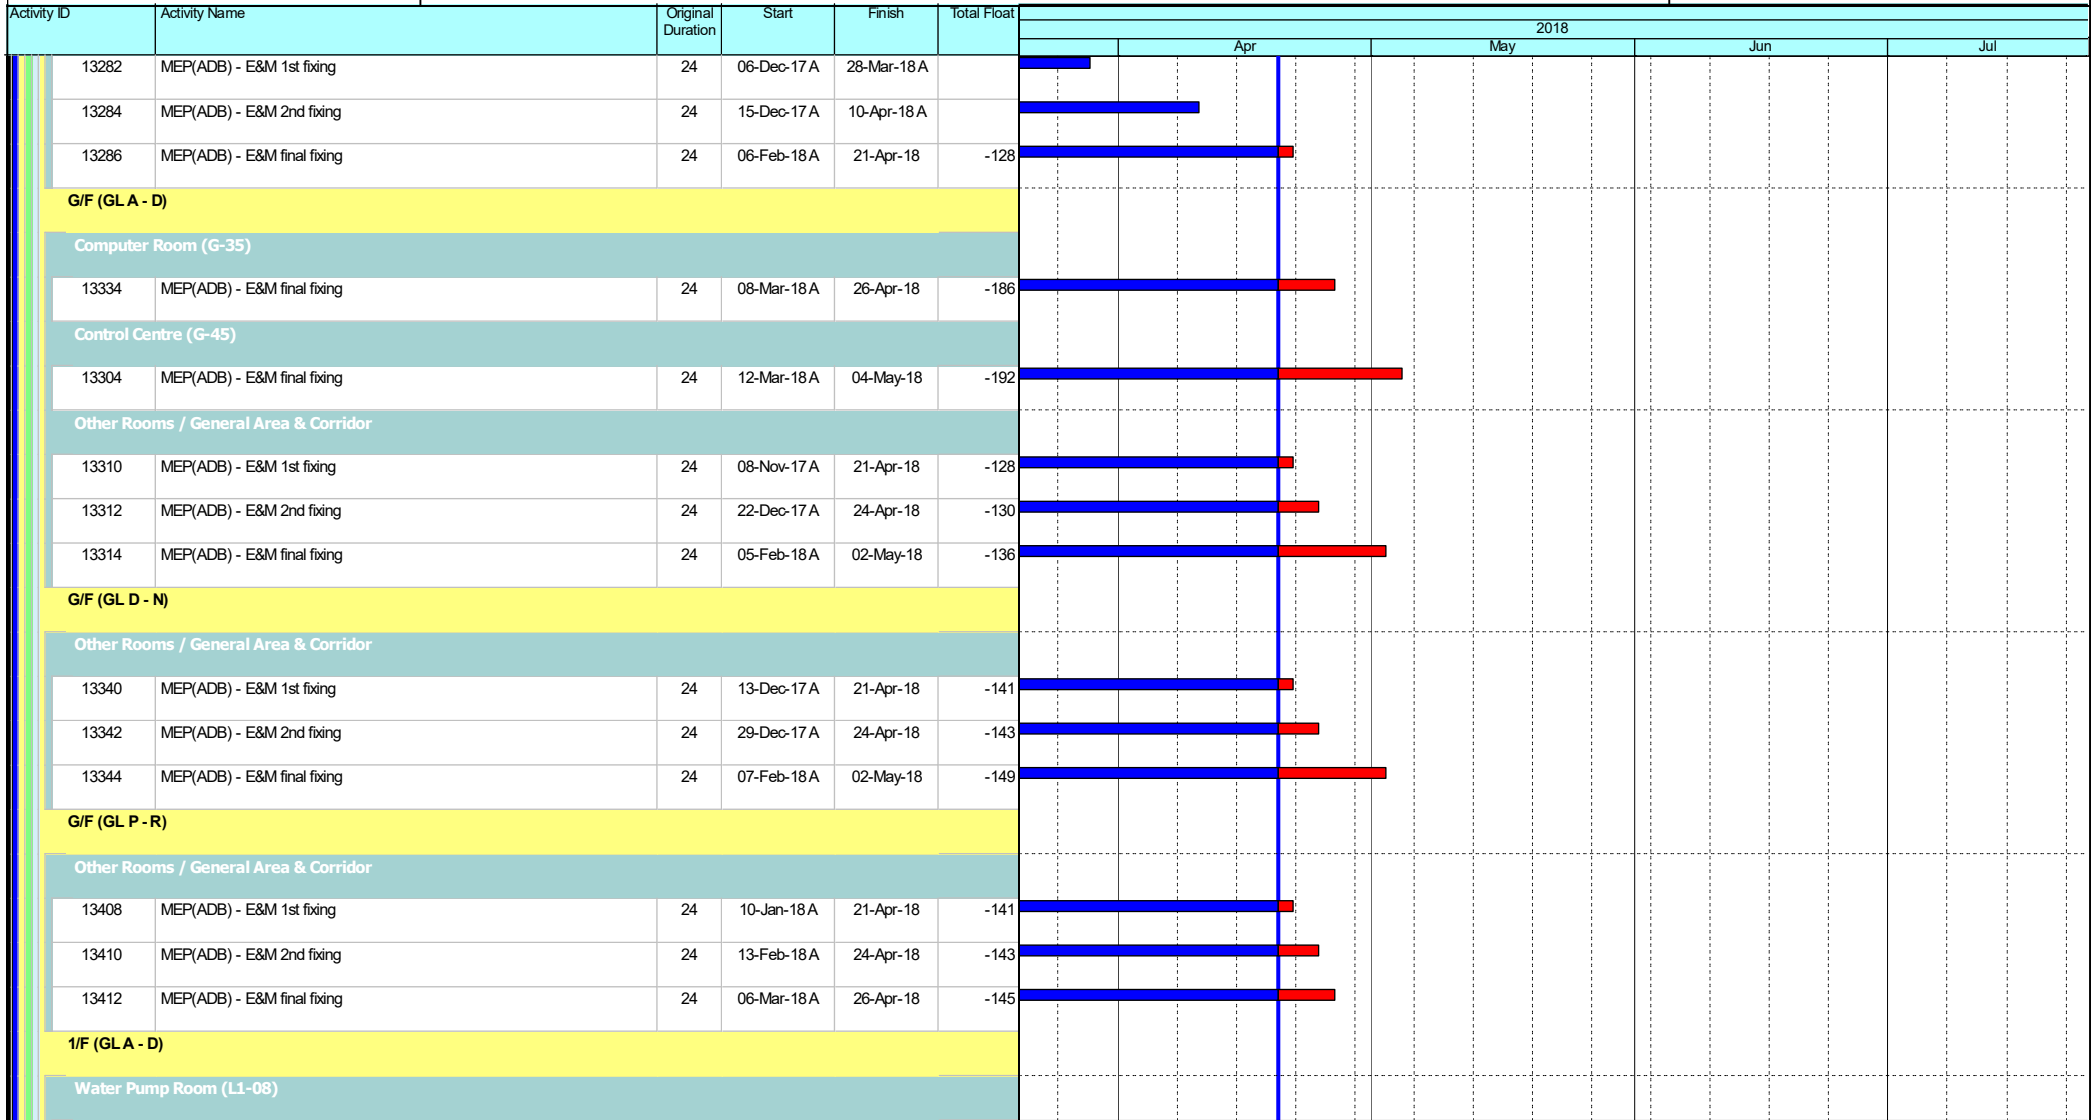

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING

Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 24 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Apr	May	Jun	Jul
13430	MEP(ADB) - E&M 2nd fixing	12	18-Dec-17 A	21-Apr-18	-227				
13426	MEP(ADB) - Installation of water Pump	24	28-Dec-17 A	04-May-18	-237				
13428	MEP(ADB) - E&M final fixing	24	10-Jan-18 A	11-May-18	-243				
Other Rooms / General Area & Corridor									
13420	MEP(ADB) - E&M final fixing	24	22-Feb-18 A	27-Mar-18 A					
External Works									
13432	ADB - Road and drainage works (EVA)	42	11-Dec-17 A	27-Apr-18	-253				
13438	ADB - Final completion works (include CCMS interface)	60	09-Jan-18 A	24-May-18	-253				
13434	ADB - External concrete pavement (EVA)	24	18-Jan-18 A	16-May-18	-247				
13436	ADB - External Fence Wall (include metal gate)	21	28-Apr-18	24-May-18	-253				
E&M Testing & Commissioning / Statutory Inspection									
3660a2	MEP(ADB) - TVS & CCMS System Integrated Testing and Commissioning	36	12-May-18	16-Jun-18	-250				
13454	MEP(ADB) - Submission of Form 5 to EMSD	0	14-May-18		-216				
13444	MEP(ADB) - Ready for Statutory Inspection	0	25-May-18		-253				
13456	MEP(ADB) - Submission of Form 501 to FSD	0	25-May-18		-253				
13462	MEP(ADB) - Submission of Form 314 to FSD	0	25-May-18		-182				
KD03M7	MEP(ADB) - Milestone for KD06	0		25-May-18	-197				
13454a	MEP(ADB) - Use Permit - Lift	0	28-May-18		-216				
13446	MEP(ADB) - Statutory Inspection & Certificates (include EMSD & FSD inspection)	24	12-Jun-18	11-Jul-18	-182				
13458	MEP(ADB) - Submission of WWO46 (Part IV) to WSD	0	21-Jun-18		-232				
13460	MEP(ADB) - Submission of WWO46 (Part V) to Client	0	12-Jul-18		-232				
Final Completion Works									
191507	ADB - MFCP manufacture & delivery	44	05-Apr-18 A	19-May-18	-212				
13464	ADB - TCSS & other E&M systems Site Acceptance Test	18	05-May-18	22-May-18	-205				

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
Baseline: SA01
Layout: Update Three Month Rolling
U050
Page 25 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

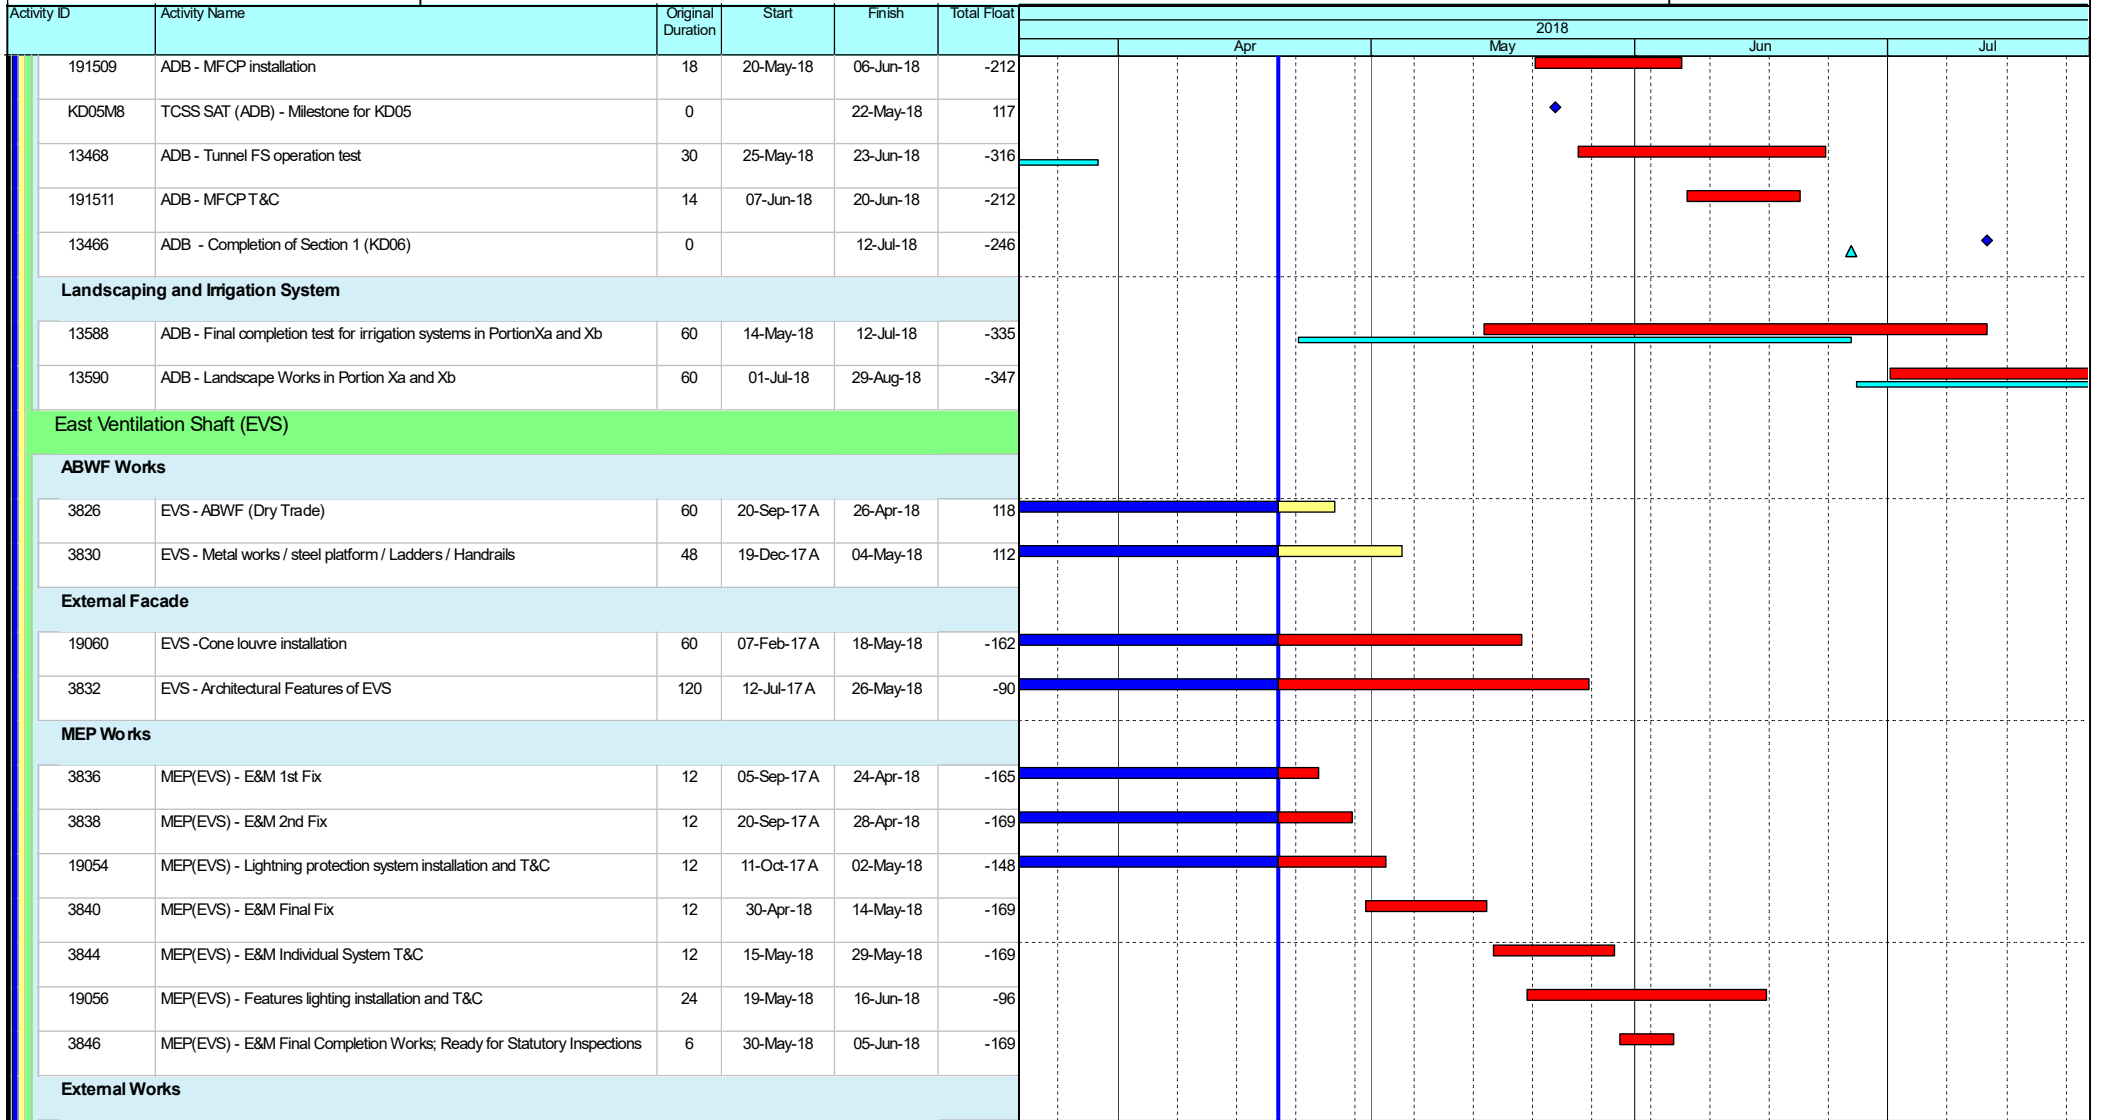

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
Baseline: SA01
Layout: Update Three Month Rolling
U050
Page 26 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

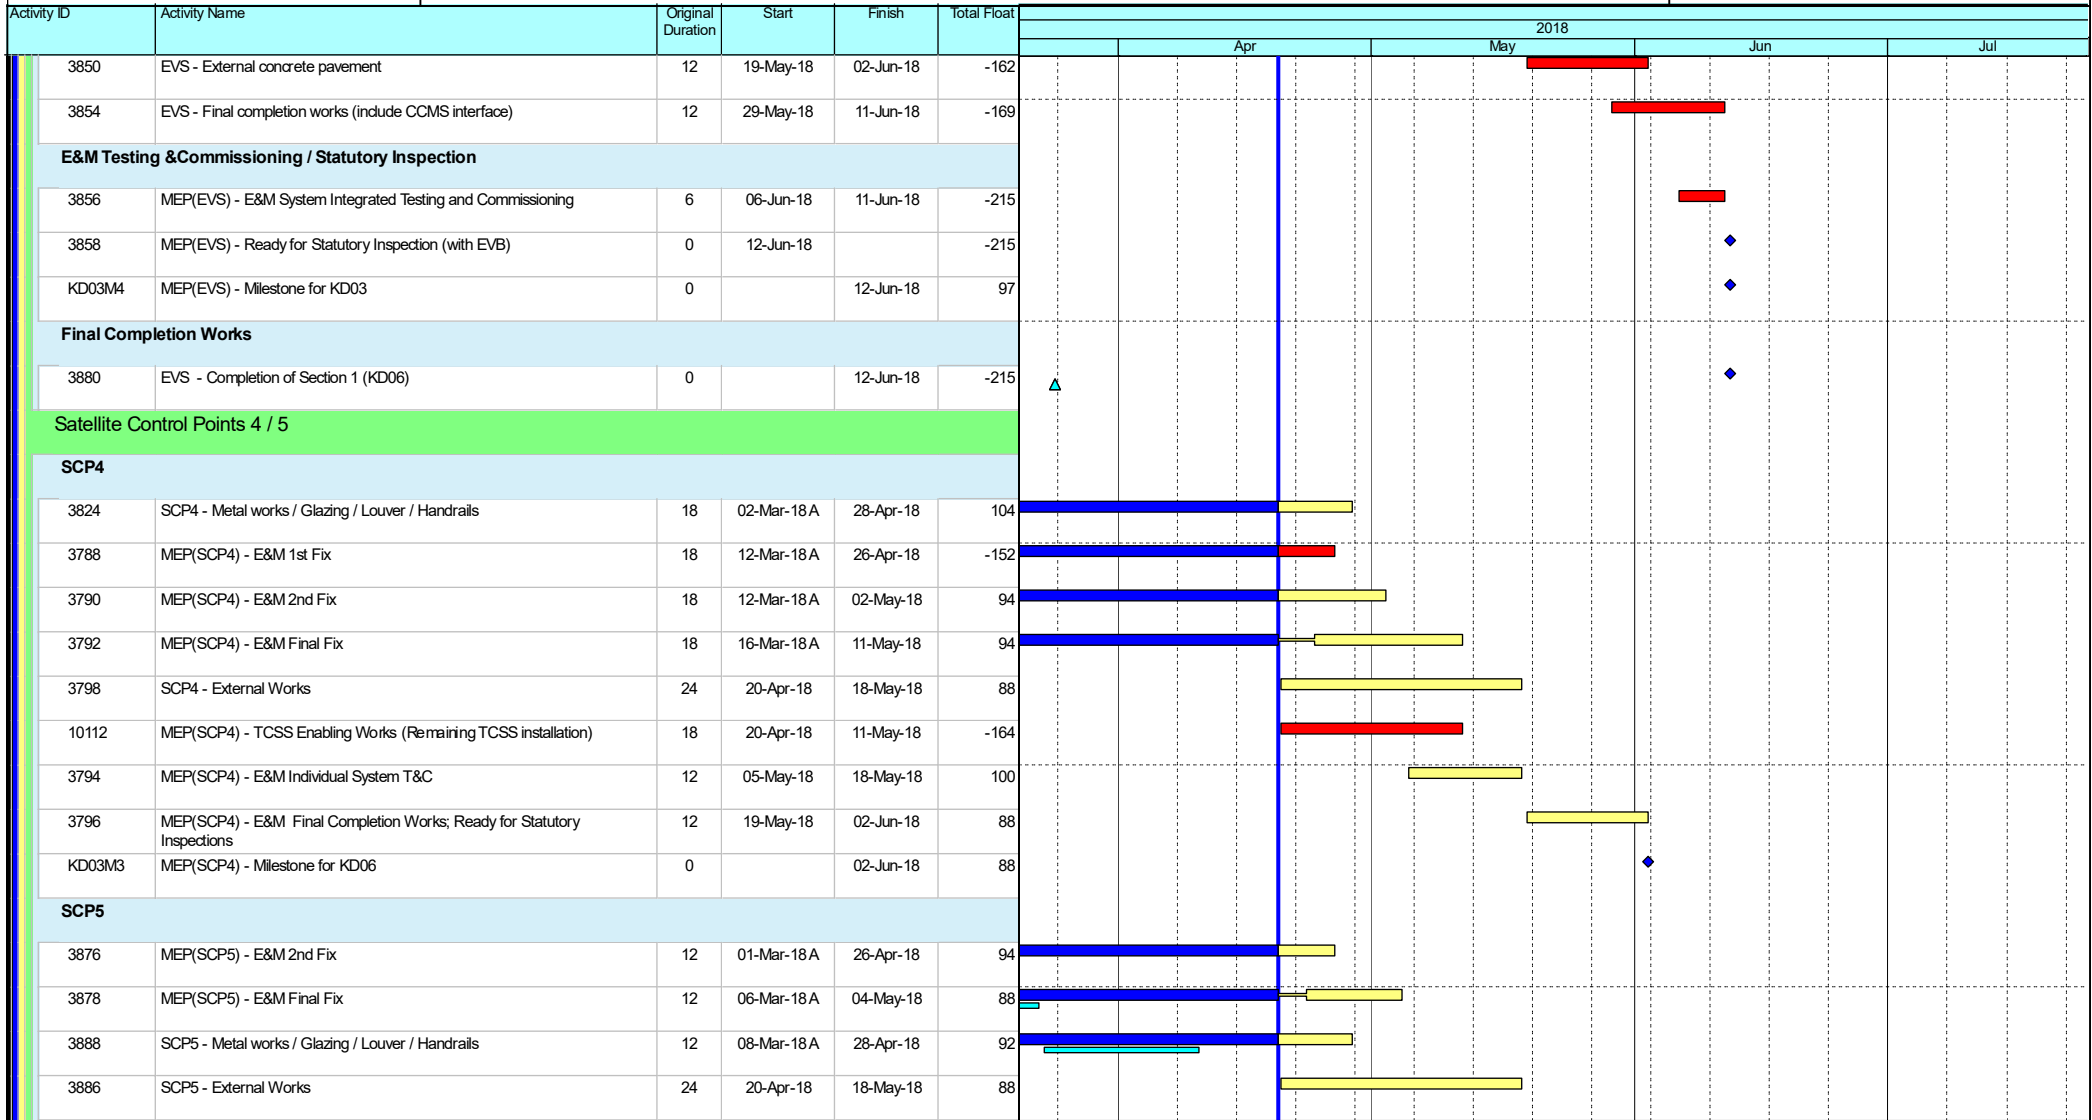

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
Baseline: SA01
Layout: Update Three Month Rolling
U050
Page 27 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

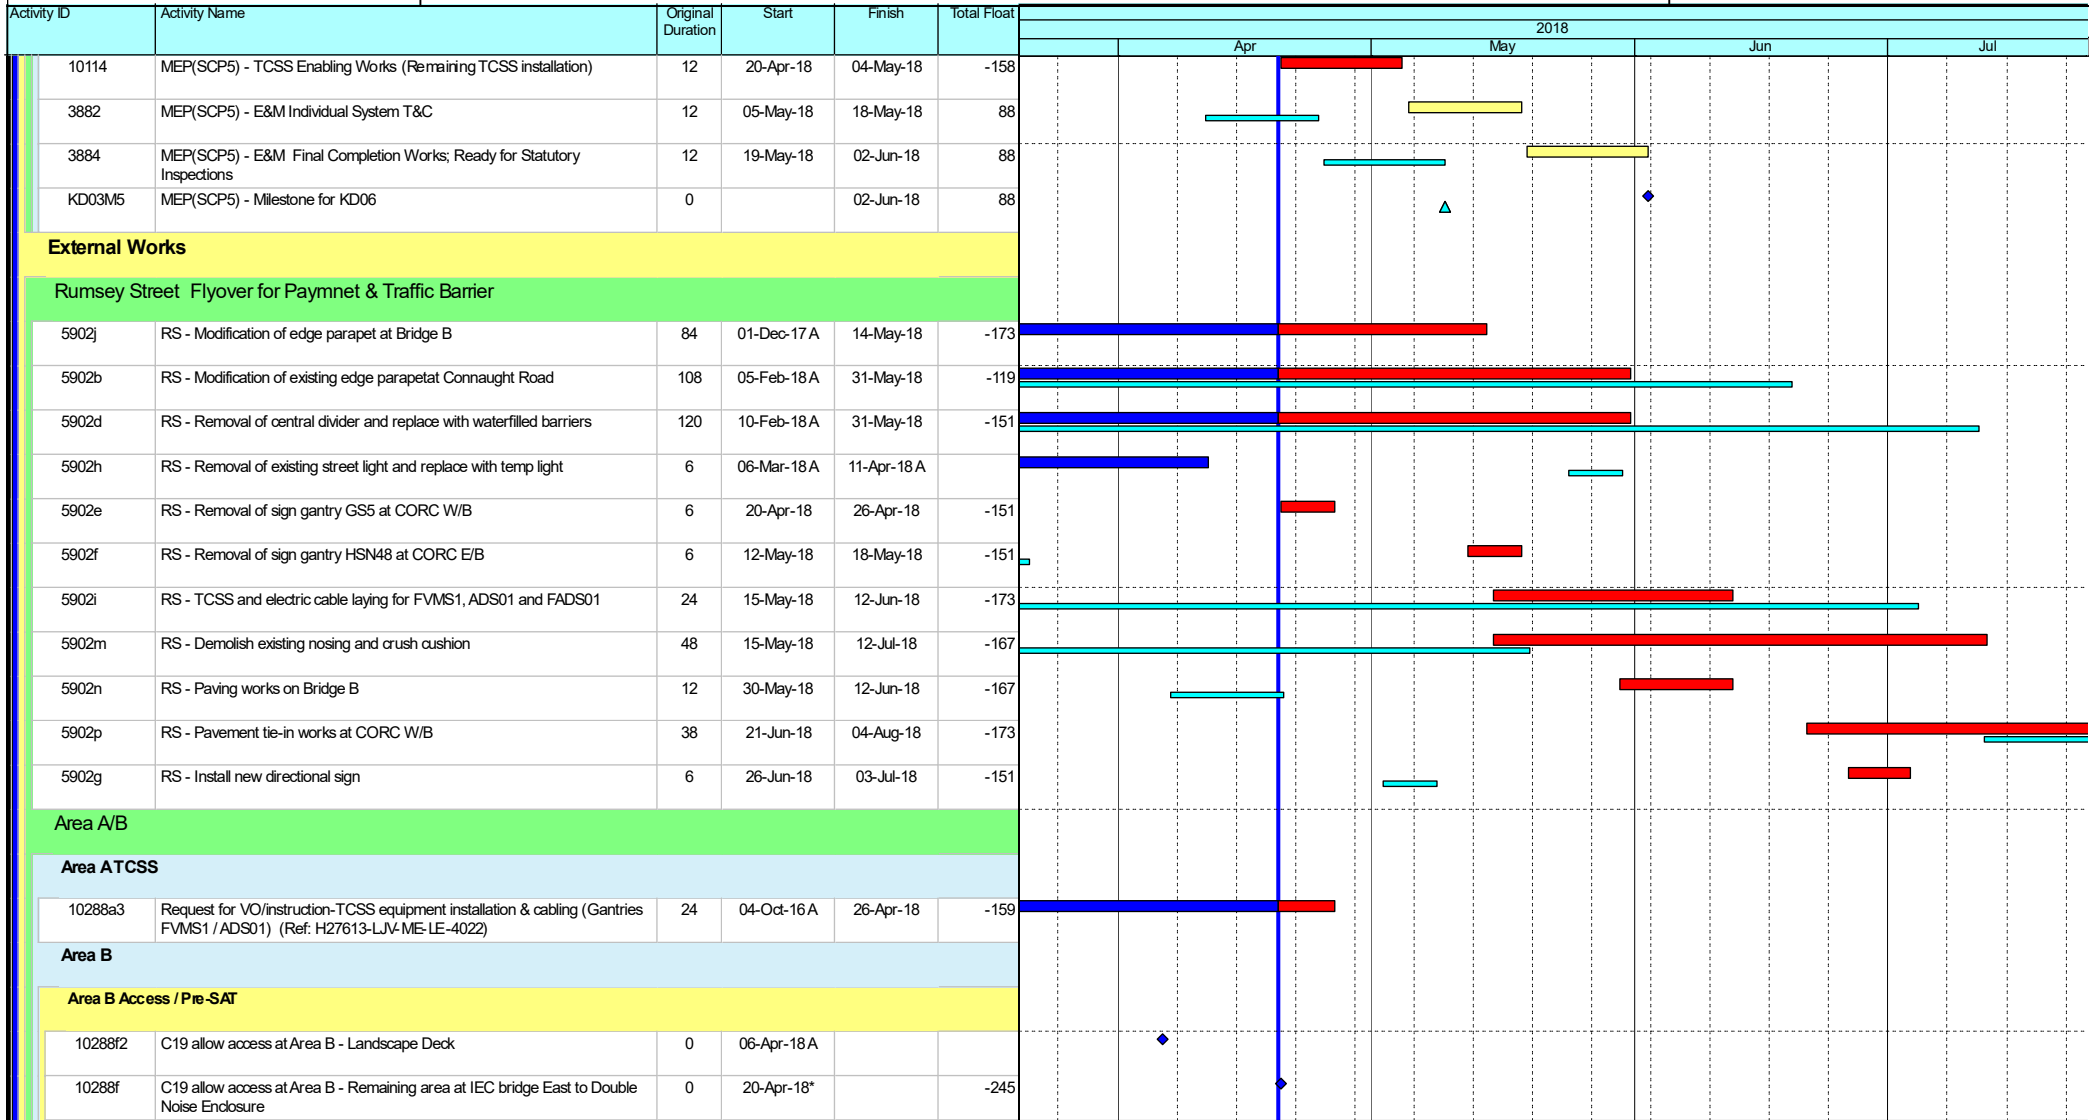

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 28 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

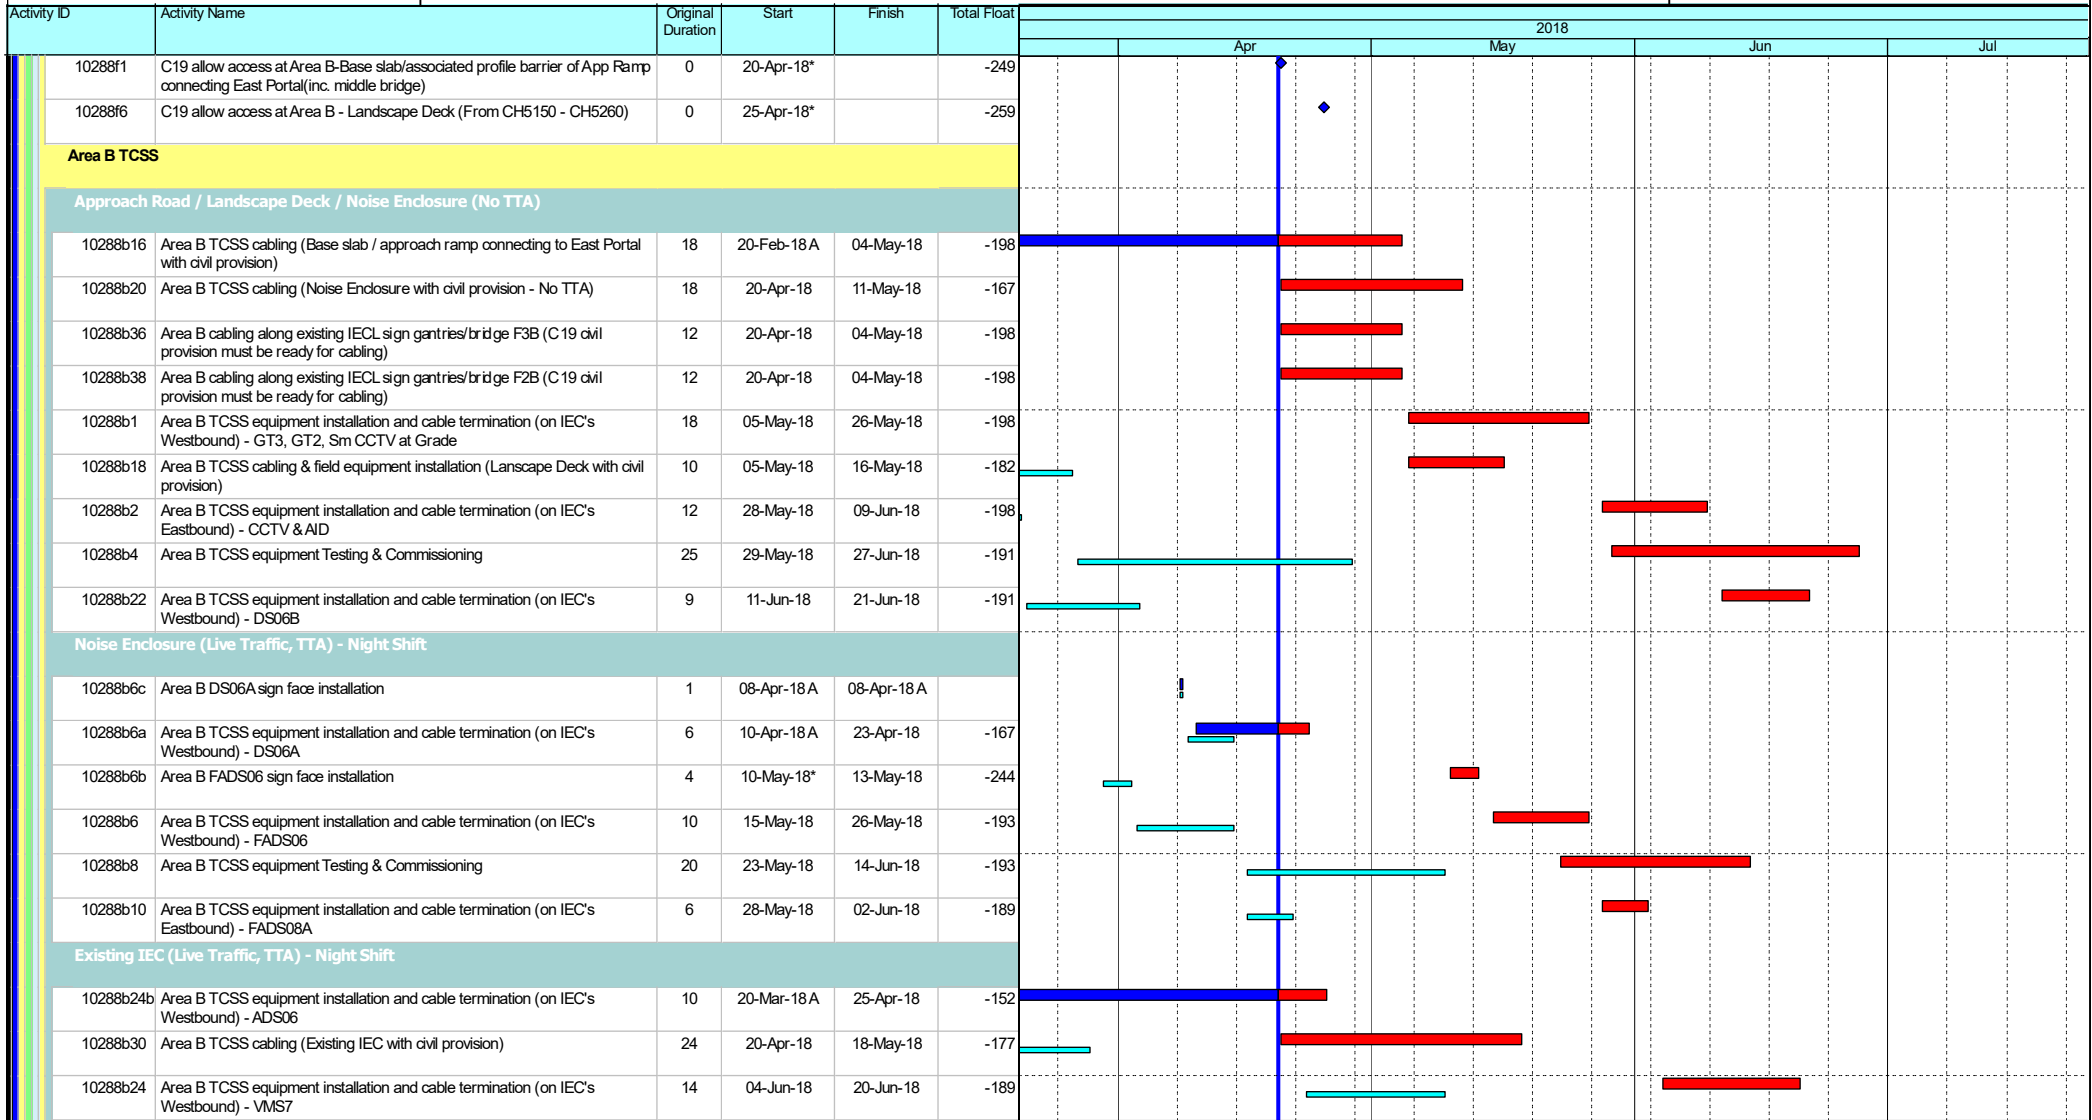

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 29 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

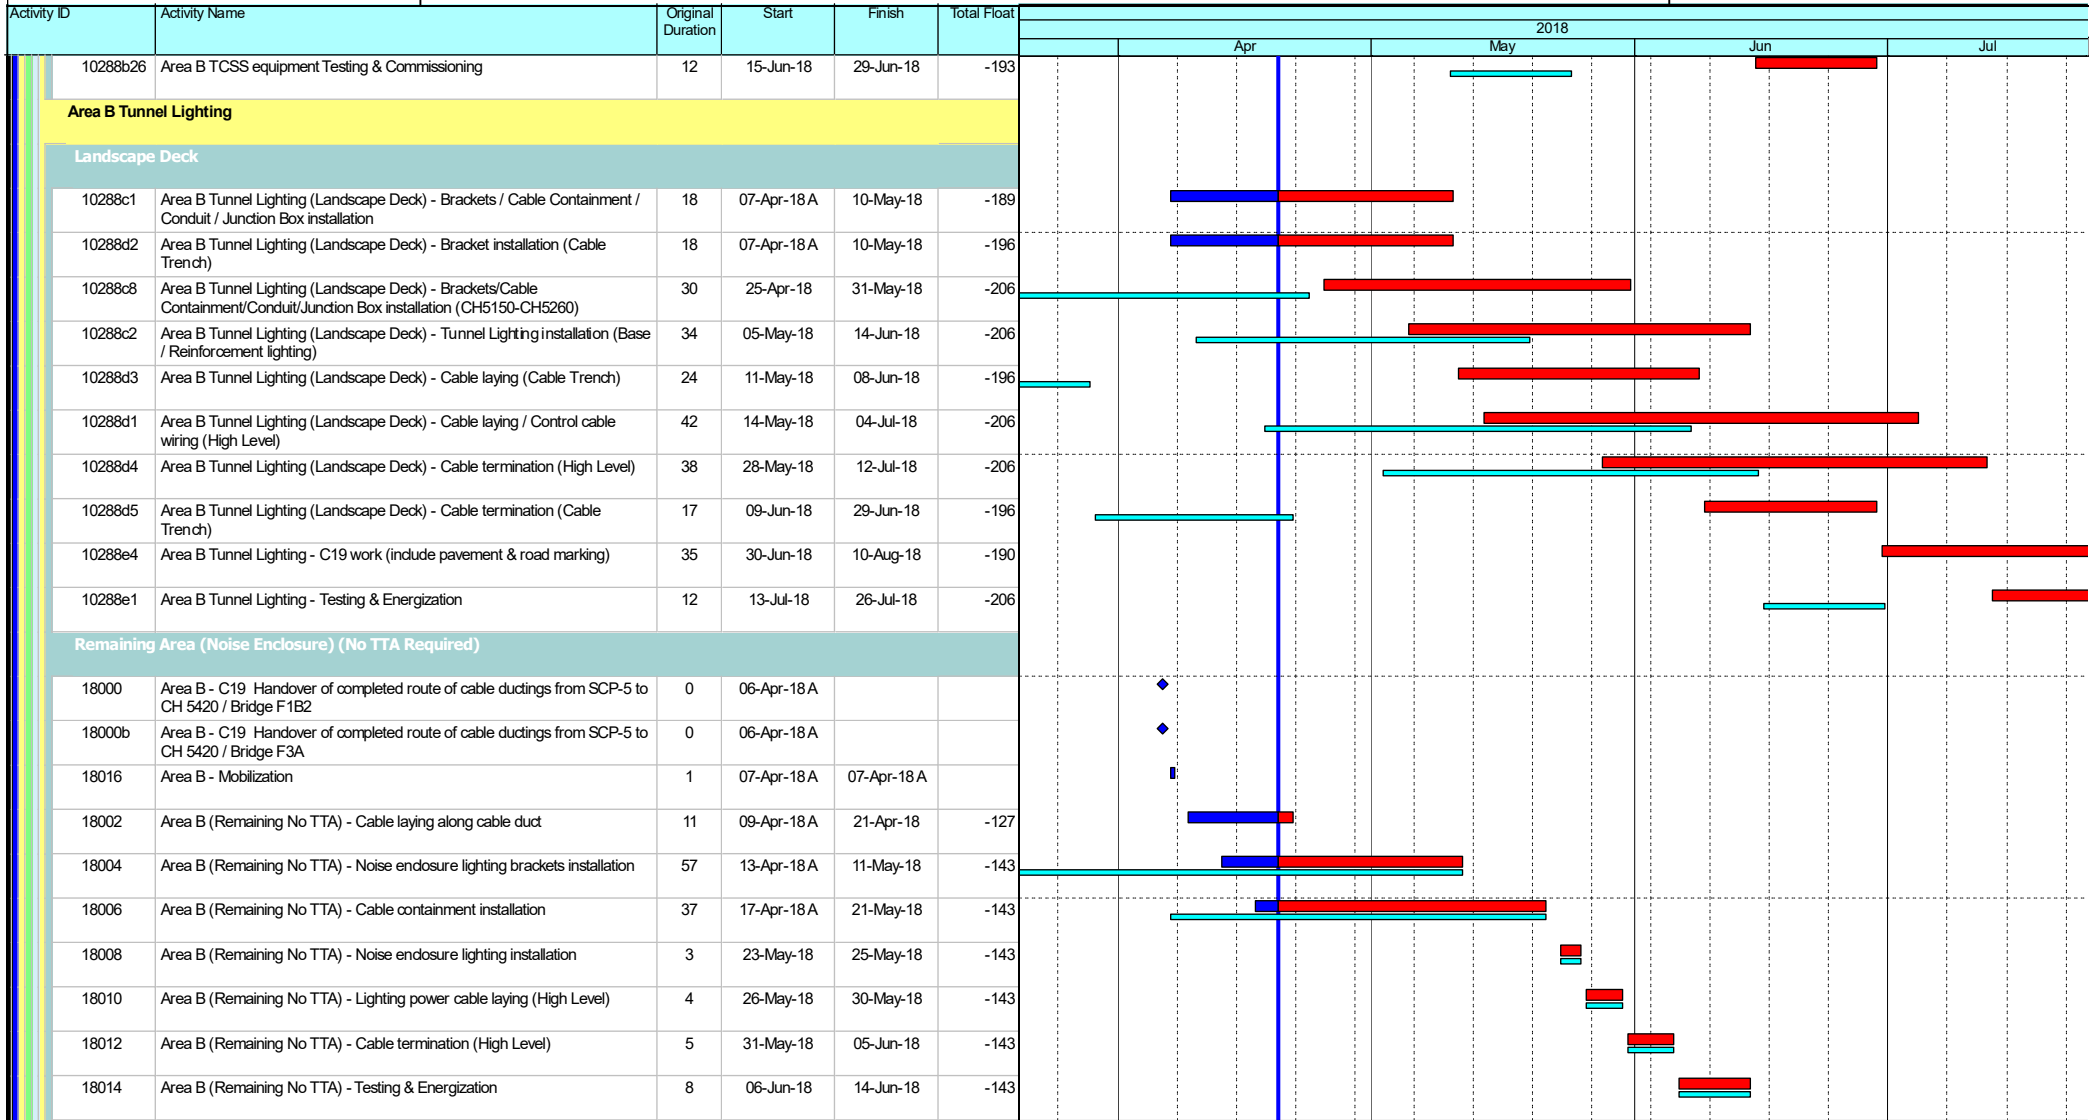

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 30 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

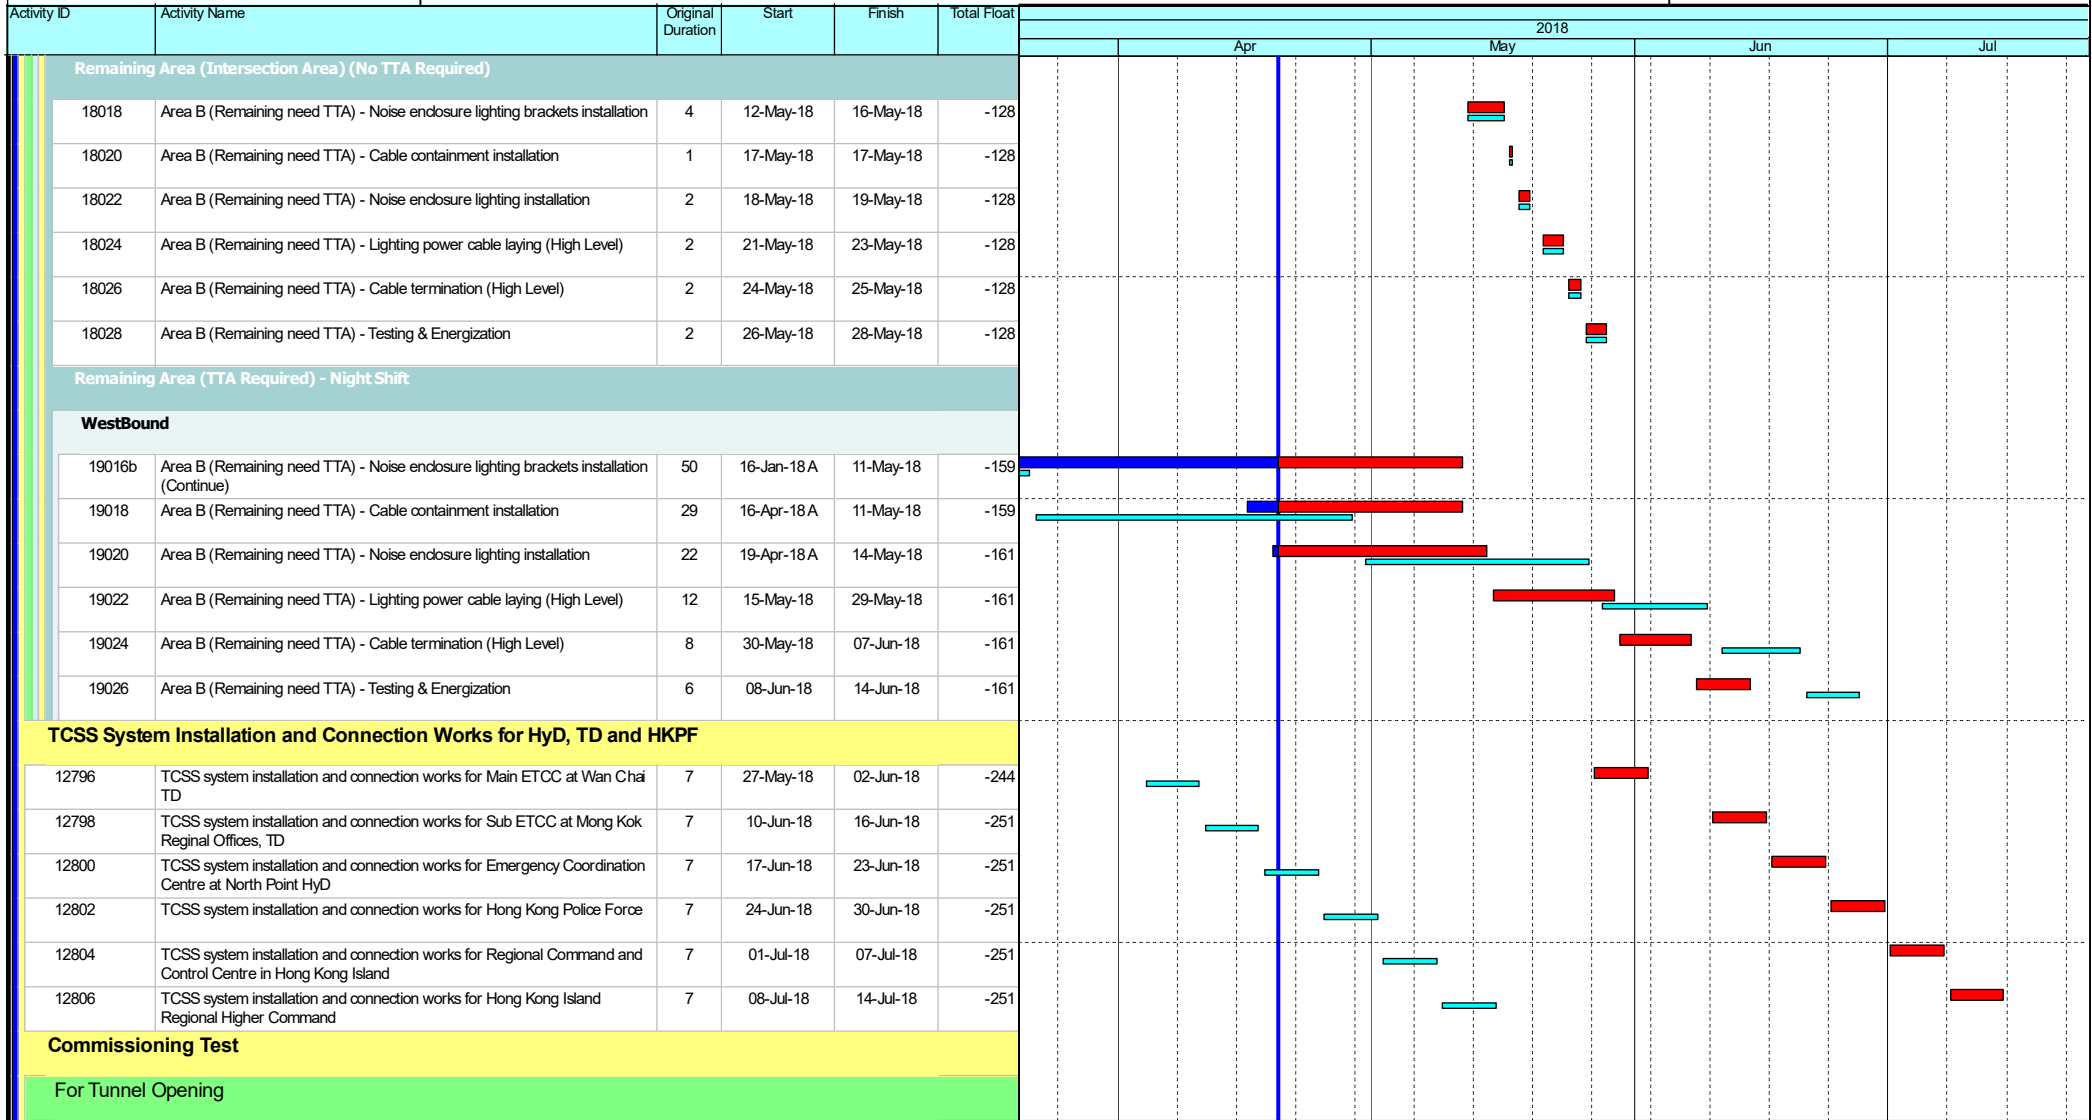

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING



Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 31 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

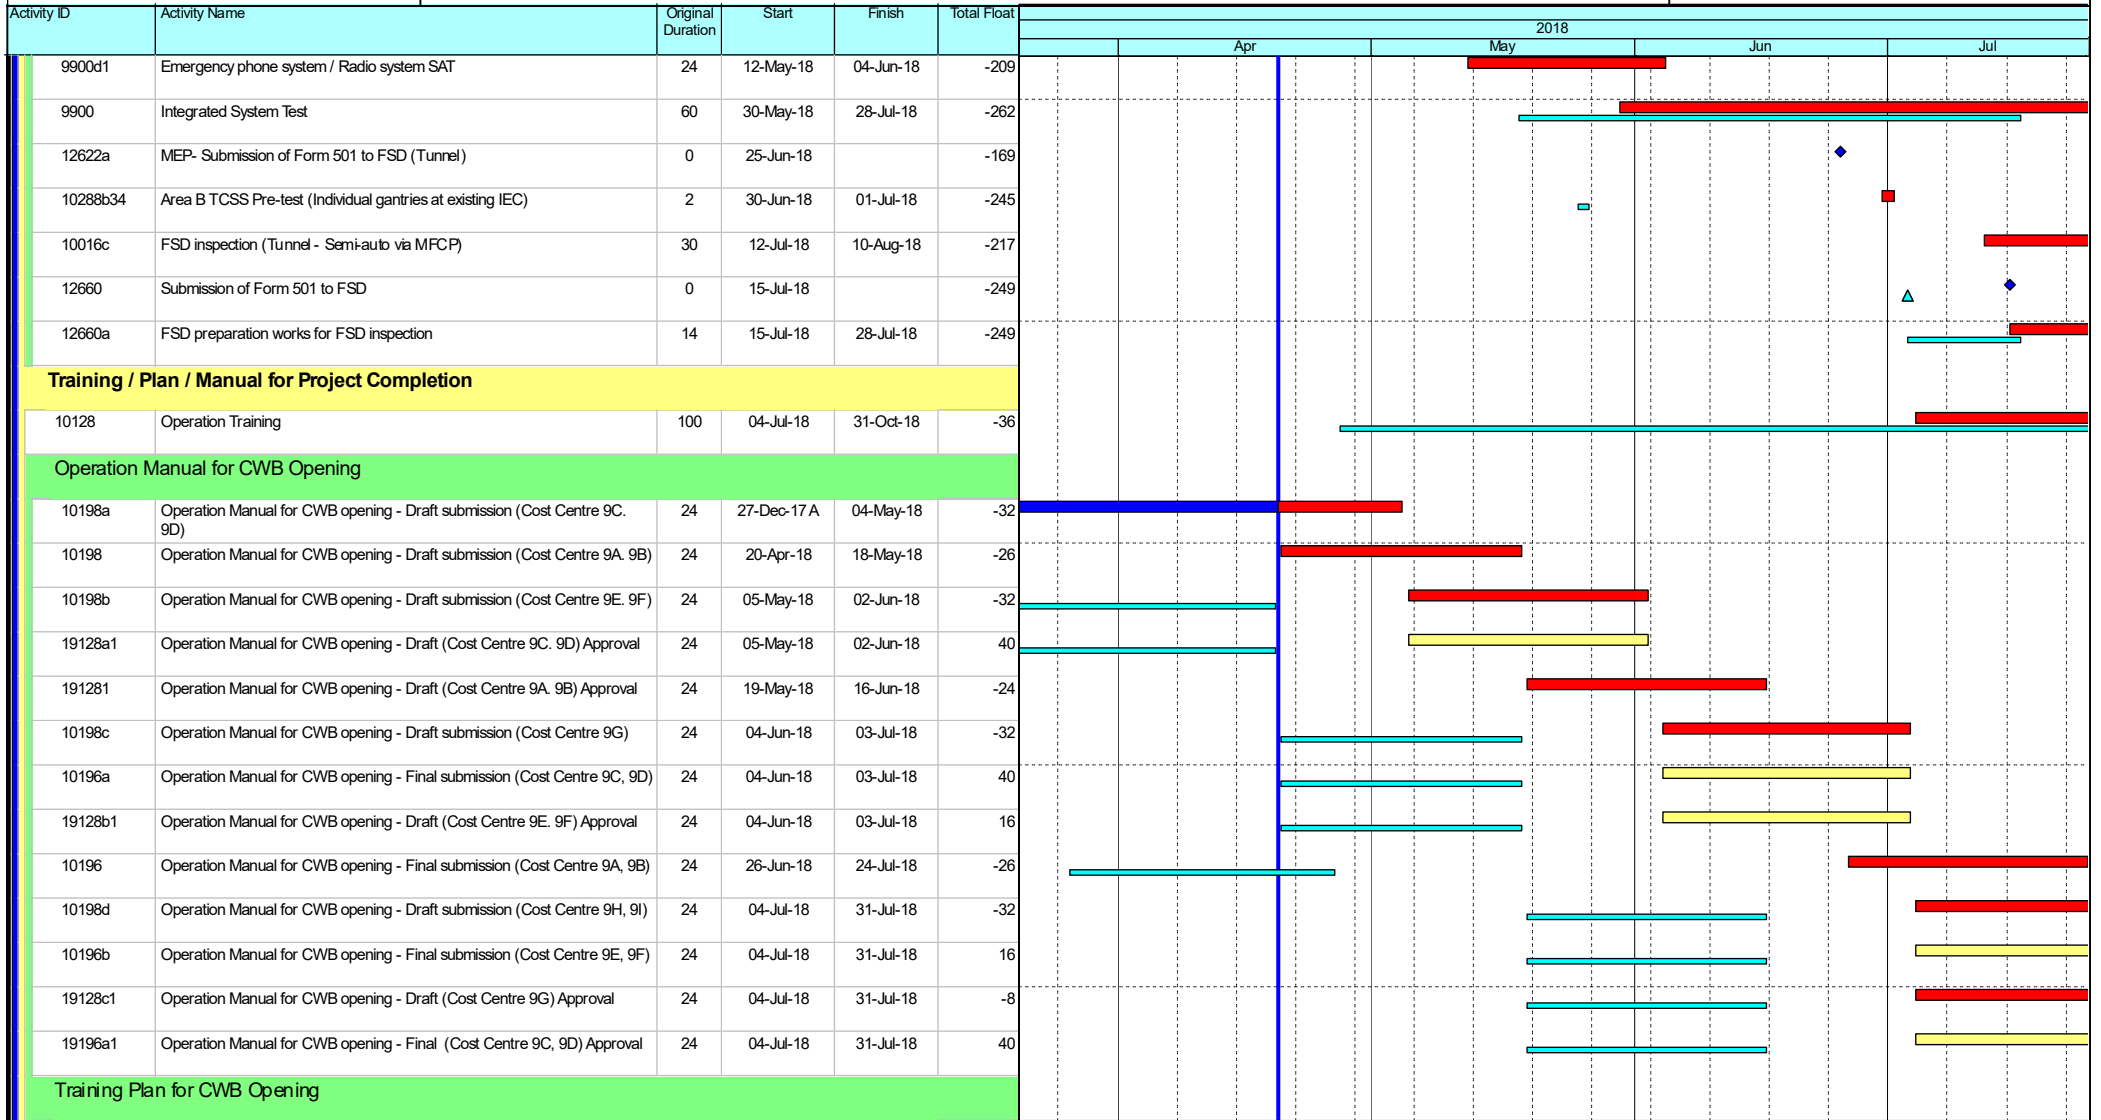

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING


Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 32 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW

Data Date: 20-Apr-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

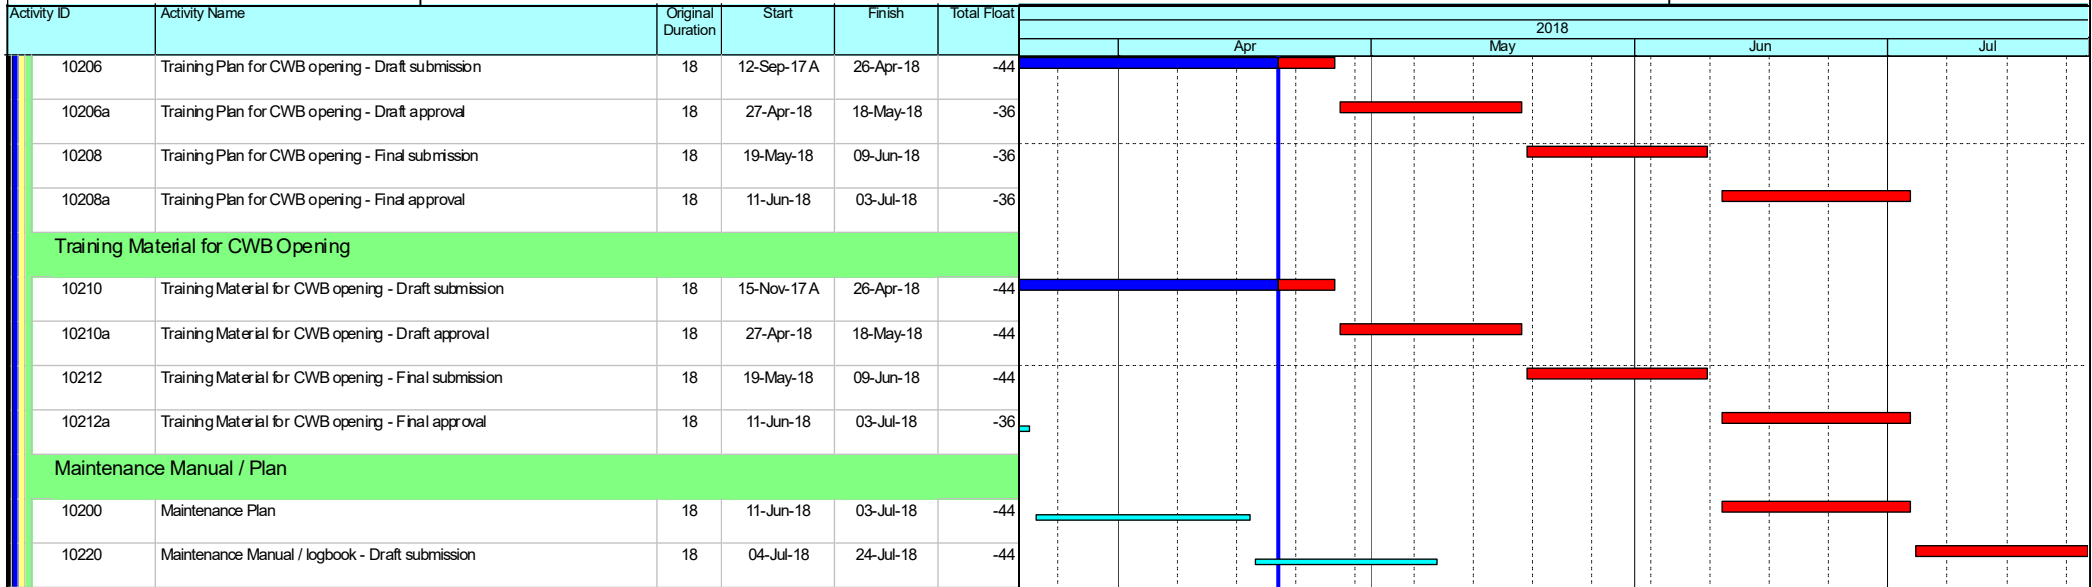

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 50 (April 2018) THREE MONTH ROLLING

Project ID: H2613-U050
 Baseline: SA01
 Layout: Update Three Month Rolling
 U050
 Page 33 of 33

Date	Revision	Checked	Approv...
20-Mar-18	U049	AT	CW
20-Apr-18	U050	AT	CW
