

**CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West**


Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018												2019								
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
HK/2012/08 Revised Works Programme Rev.12.0(DD 20 November 2017)																										
Key Dates and Milestone Dates																										
Sections of Works Completion (Included Not Granted EOT Entitlement of The Contractor)																										
KD10840	Completion of Section IIIA	0		08-Sep-18*	0%																					
KD10860	Completion of Section IV	0		30-Aug-18*	0%																					
KD10880	Completion of Section V	0		26-Sep-18*	0%																					
KD11010	Completion of Section VII	0		14-Sep-18*	0%																					
KD11020	Completion of Section VIII	0		21-Sep-18*	0%																					
KD11040	Completion of Section IX	0		21-Sep-19*	0%																					
KD11060	Completion of Section X	0		21-Sep-18*	0%																					
Planned Sections of Works Completion																										
KD10080	Planned Section IIIA Completion - Road A2,A4, A5	0		08-Sep-18	0%																					
KD10100	Planned Section IV Completion - Slip Road 3	0		30-Aug-18	0%																					
KD10140	Planned Section V Completion - Remaining At-Grade Road	0		26-Sep-18	0%																					
KD10280	Planned Section VII Completion - Remainder Works	0		14-Sep-18	0%																					
KD10300	Planned Section VIII Completion - Landscape Softwork	0		21-Sep-18	0%																					
KD10320	Planned Section IX Completion - Establishment Works	0		21-Sep-19	0%																					
KD10340	Planned Section X Completion - Tree Protection & Preservation	0		21-Sep-18	0%																					
Dredging and Reclamation																										
Marine Work Construction																										
Zone CRIII																										
Seawall Construction - Zone CRIII																										
Zone CRIII Seawall- 2nd Stage																										
Seawall 2 & 12																										
MAR21371	Zone CRIII - seawall 2 & 12 - Backfilling remaining portion (type A, geotextile and filter)	0	19-Jan-18 A	27-Jan-18 A	100%	■																				
Zone D																										
Seawall Construction - Zone D																										
Seawall 10 & 11																										
MAR20630	Zone D - Seawall 10 & 11: Install remaining seawall block	14	20-Feb-18*	05-Mar-18	0%		■																			
MAR20650	Zone D - Seawall 10 & 11: Backfill Type A	7	06-Mar-18	12-Mar-18	0%			■																		
MAR20670	Zone D - Seawall 10 & 11: Lay geotextile and filter	7	13-Mar-18	19-Mar-18	0%			■																		
Works for Section Completion																										
Construction																										
Section III A - Road A2, A4 & A5																										
Roadwork & Utilities - Section 1 (L1806 - L1801)																										

Data Date: 20-Feb-18



- ◆ Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Remaining Level of Effort

**Updated Works Programme Rev.12
(Ref. to Rev.12 as of 20 February 2018)**

Date	Revision	Checked	Approved
20-Feb-18	12		

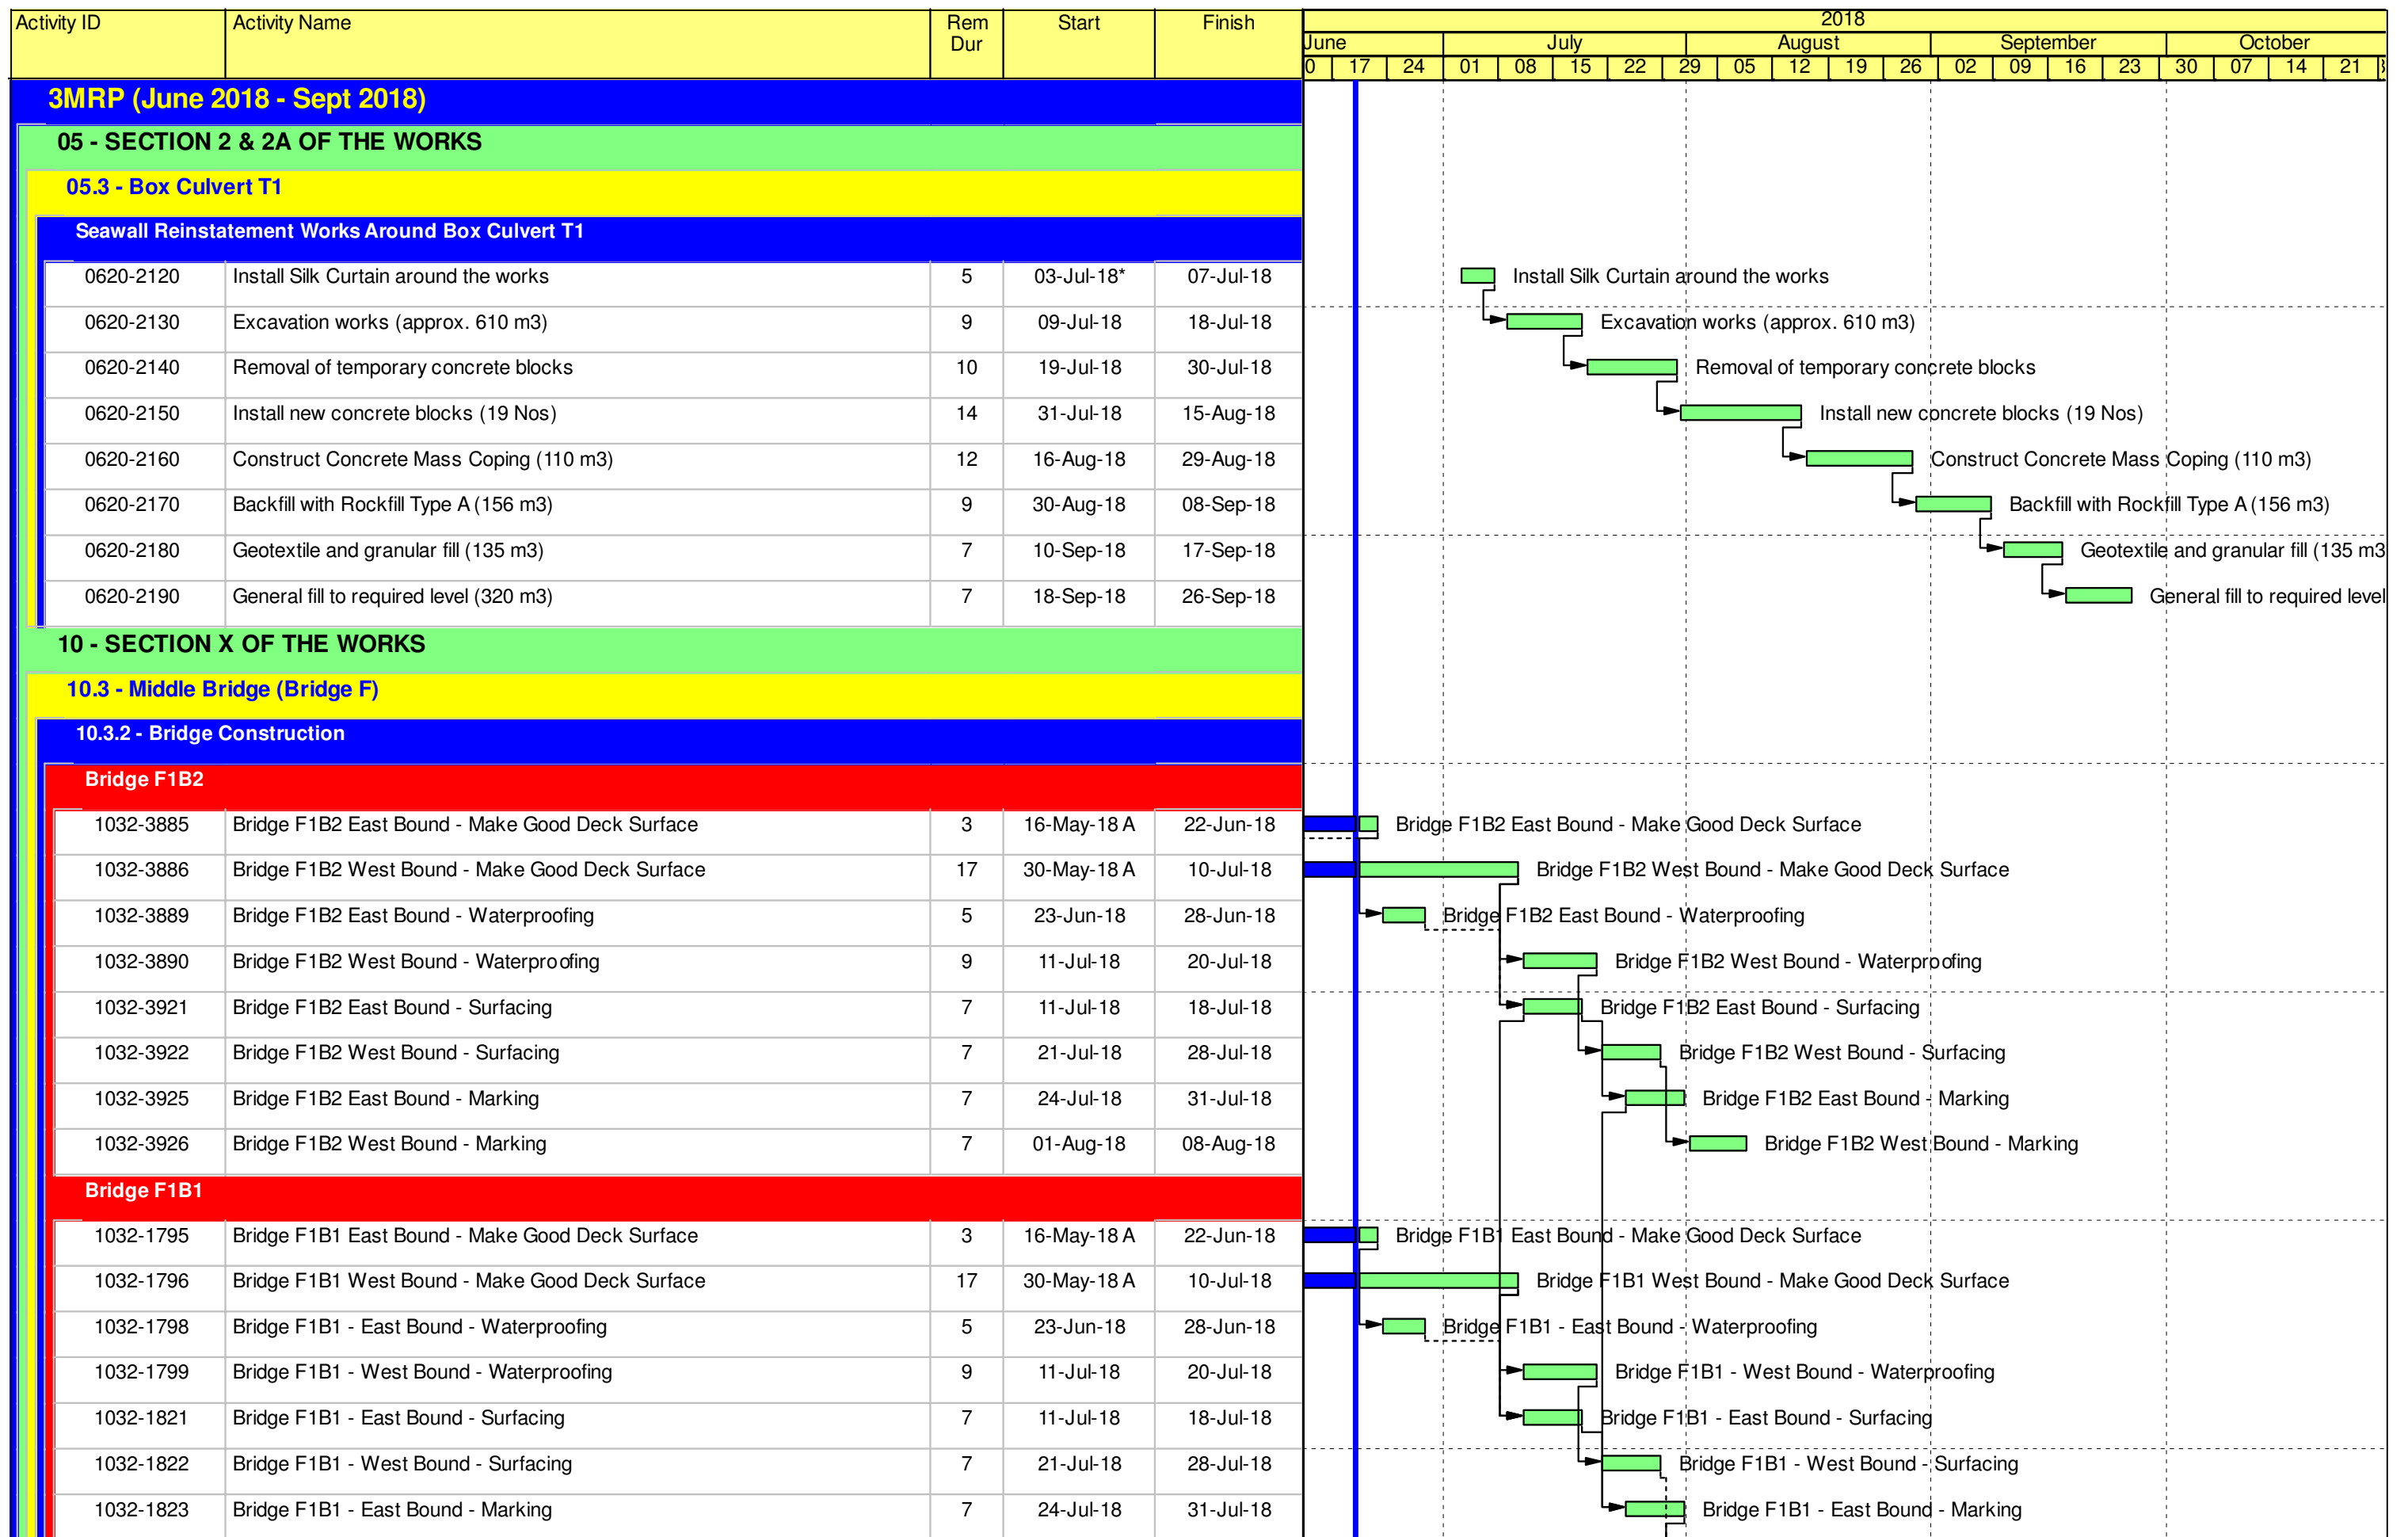

Contract HY/2009/19
Three Months Rolling Programme (20.June.2018 to 20.Sept.2018)

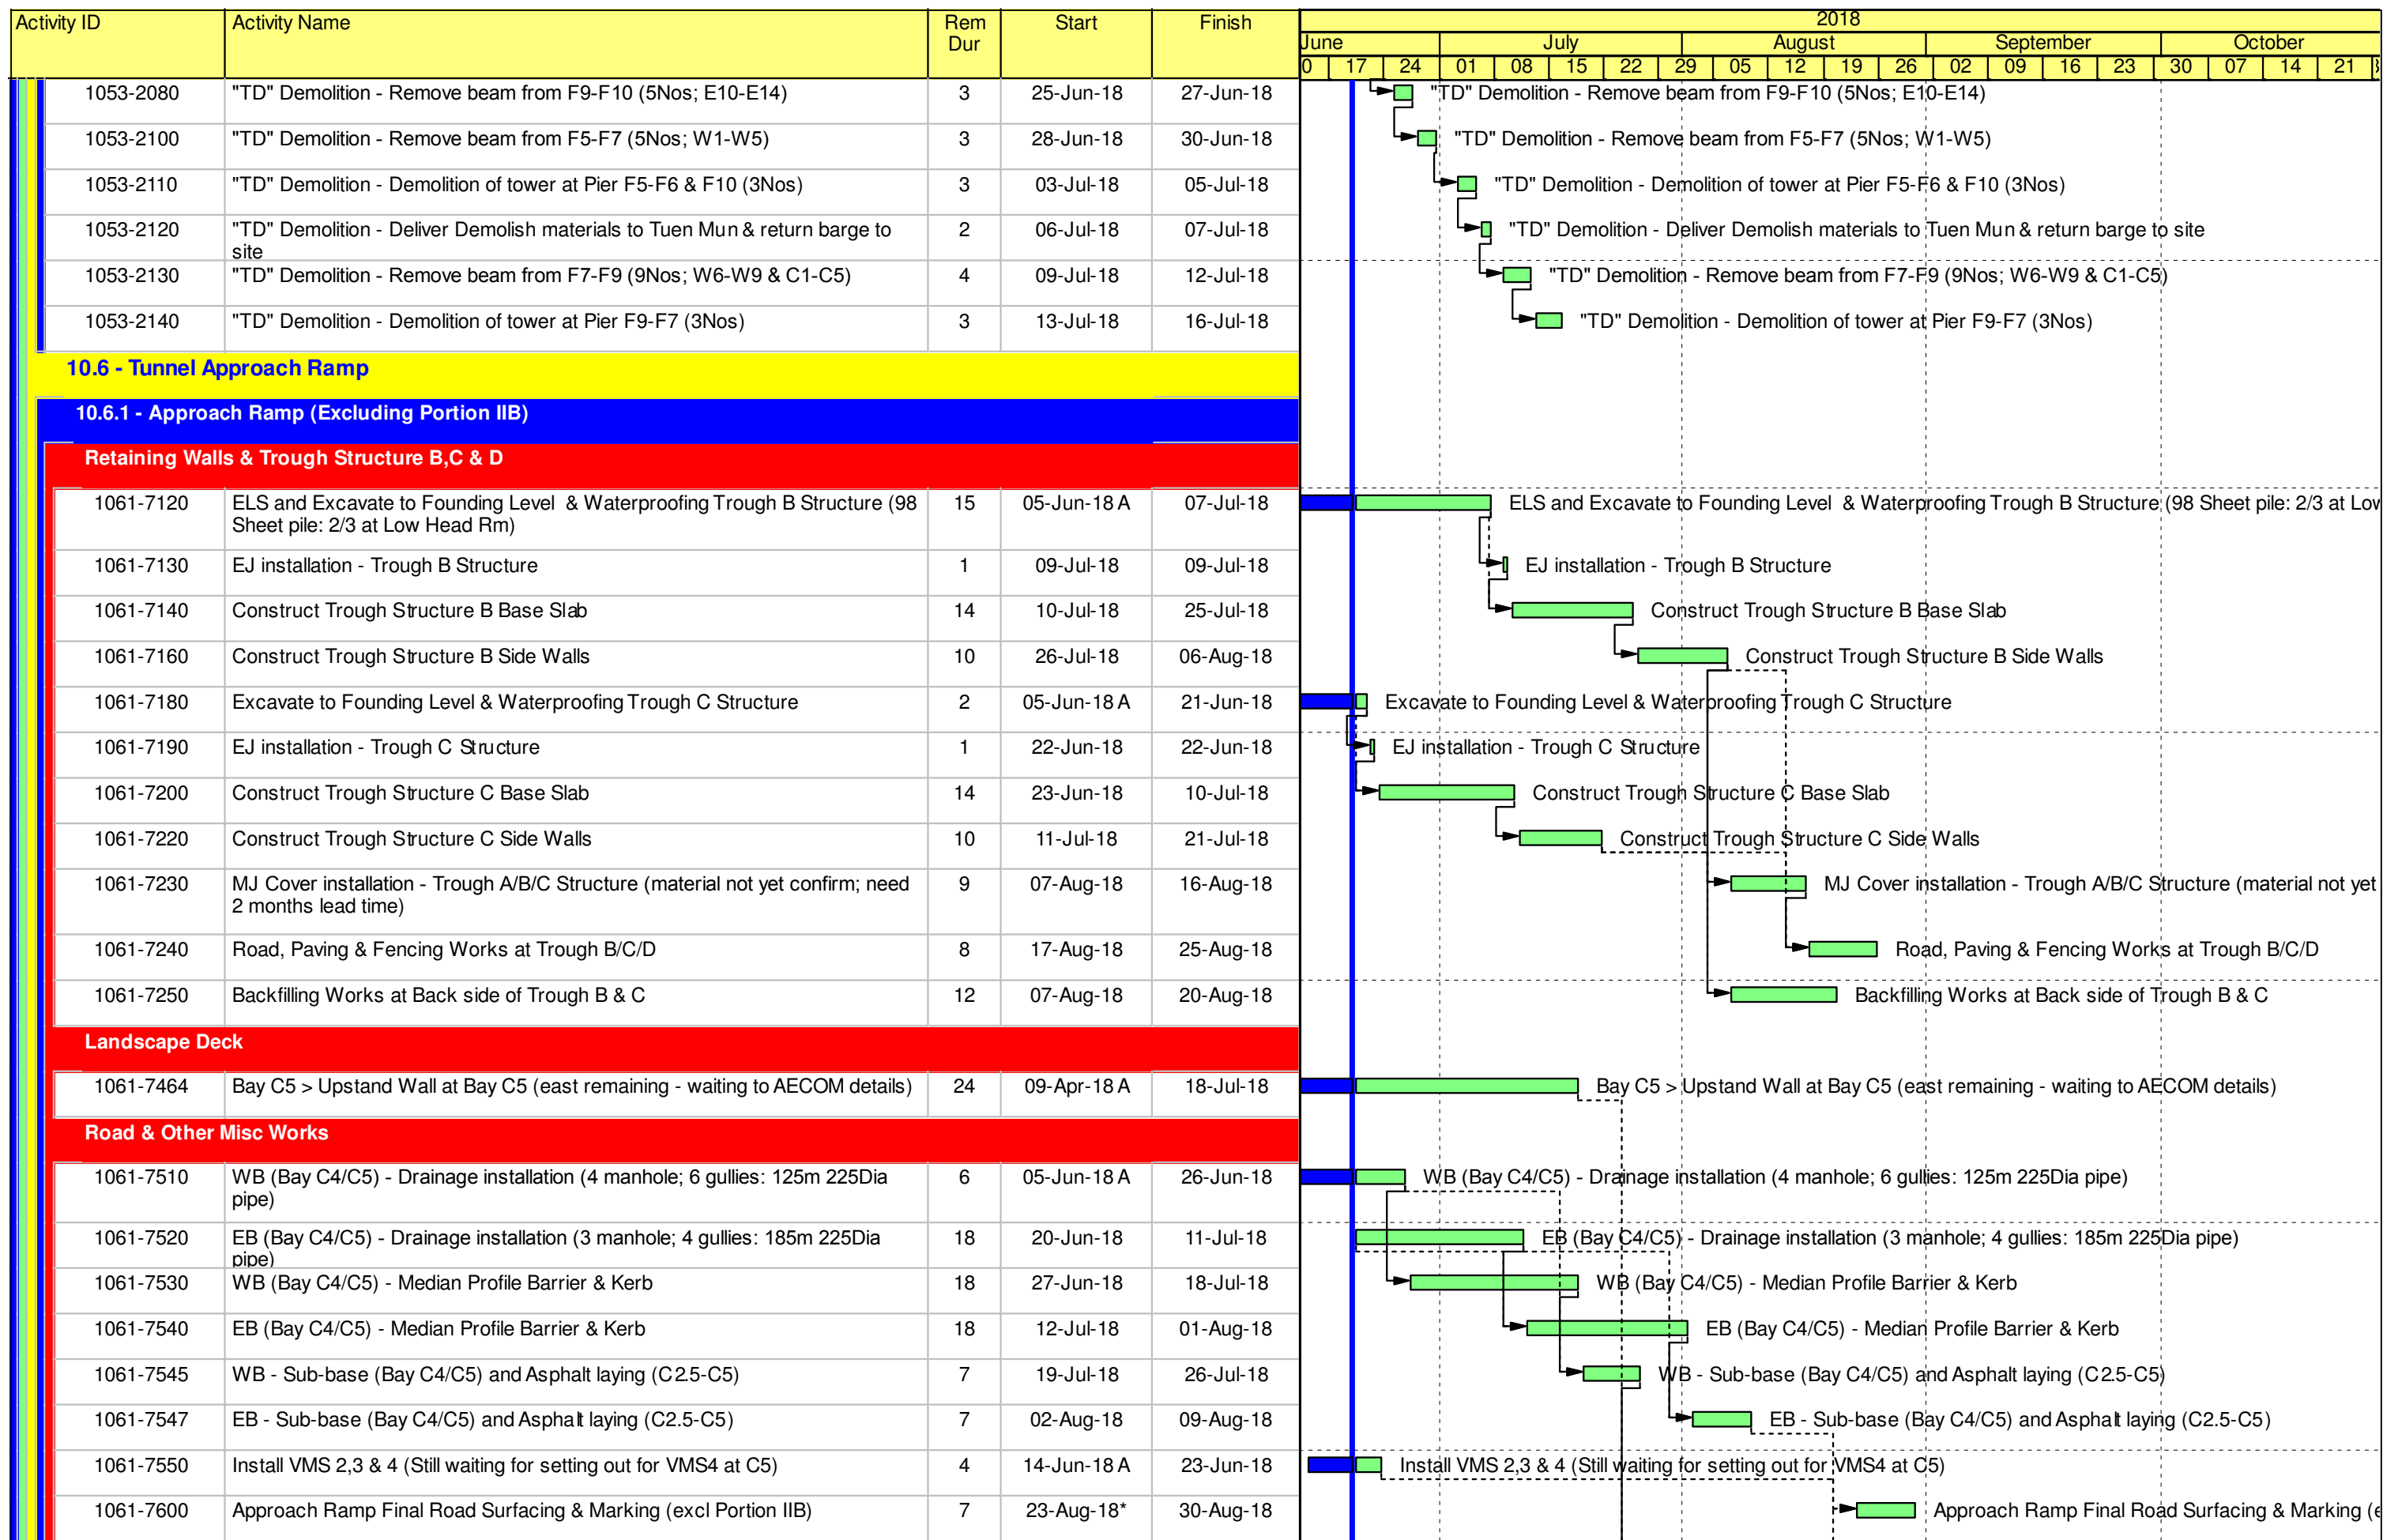

Contract HY/2009/19
Three Months Rolling Programme (20.June.2018 to 20.Sept.2018)

Activity ID	Activity Name	Rem Dur	Start	Finish	2018																			
					June			July				August				September				October				
					0	17	24	01	08	15	22	29	05	12	19	26	02	09	16	23	30	07	14	21
1062-1291	Slip Road 13 (West - Near Site Office) Trimming Ex Surface & Drainage Works	13	07-Jun-18 A	05-Jul-18	Slip Road 13 (West - Near Site Office) Trimming Ex Surface & Drainage Works																			
1062-1292	Slip Road 13 (West - Near Site Office) Backfilling & Compaction	8	06-Jul-18	14-Jul-18	Slip Road 13 (West - Near Site Office) Backfilling & Compaction																			
1062-1293	Slip Road 13 (West - Near Site Office) Road Kerb & Other Misc Works	8	16-Jul-18	24-Jul-18	Slip Road 13 (West - Near Site Office) Road Kerb & Other Misc Works																			
1062-1294	Slip Road 13 (North - Sea Side) Drainage & Other Underground Civil Provision Works	14	25-Jun-18	11-Jul-18	Slip Road 13 (North - Sea Side) Drainage & Other Underground Civil Provision Works																			
1062-1295	Slip Road 13 (North - Sea Side) Backfilling & Compaction	8	12-Jul-18	20-Jul-18	Slip Road 13 (North - Sea Side) Backfilling & Compaction																			
1062-1296	Slip Road 13 (North - Sea Side) Road Kerb & Other Misc Works	8	21-Jul-18	30-Jul-18	Slip Road 13 (North - Sea Side) Road Kerb & Other Misc Works																			
1062-1297	Slip Road Surfacing	5	31-Jul-18	04-Aug-18	Slip Road Surfacing																			
1062-1298	Road Marking, Fencing & Other Finishing Works	17	06-Aug-18	24-Aug-18	Road Marking, Fencing & Other Finishing Works																			
10.7 - Section X - Miscellaneous Works																								
10.7.2 - Oil Street/Watson Road (Portion III)																								
1072-1285	Pre-cast Clay Paving EVA to EVB (remaining paver to arrive on site by mid Aug)	57	10-May-18 A	25-Aug-18	Pre-cast Clay Paving EVA to EVB (remaining paver to arrive on site by mid Aug)																			
1072-1287	Road Reinstatement > Watson Road cul-de sac	12	22-May-18 A	04-Jul-18	Road Reinstatement > Watson Road cul-de sac																			
11 - SECTION 11 OF THE WORKS																								
11.0 - Portion XIIC																								
1110-2500	EB - Modification of Road Marking at Hing Fat Slip Road (Night Work)	1	26-Aug-18*	26-Aug-18	EB - Modification of Road Marking at Hing Fat Slip Road																			
11.1 - Portion XIIA - Stage 1																								
11.1.4 - Footing and frame/pole for directional sign FVMSH2, ADS16 and OHVD (Portion XIIA)																								
1110-2970	FVMSH2	18	07-May-18 A	11-Jul-18	FVMSH2																			
1110-2980	DS15 (Frame)	6	19-Jun-18 A	26-Jun-18	DS15 (Frame)																			
1110-2985	DS18	10	20-Jun-18	30-Jun-18	DS18																			
1110-2987	OHVD at Tsing Fung Street Flyover	17	05-Jul-18*	24-Jul-18	OHVD at Tsing Fung Street Flyover																			
11.2 - Portion XIIA - Stage 2 - Along Gordon House - Cross road ducting at Hing Fat St (public hol)																								
1110-3020	Miscellaneous Road Works at Portion XIIA (5 TTA arrangement - works only on Sunday & public holiday; 12days)	56	04-Jul-18	06-Sep-18	Miscellaneous Road Works at Portion XIIA (5 TTA arrangement - works only on Sunday & public holiday; 12days)																			
11.3 - Portion XIIA - Stage 3 - Preparation & works night before road opening																								
1110-3030	Misc Works prior to CWB opening incl preparation - Stage 2	12	06-Sep-18	19-Sep-18	Misc Works prior to CWB opening																			

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone

Contract HY/2009/19
Three Months Rolling Programme (20.June.2018 to 20.Sept.2018)

Activity ID	Activity Name	Original Duration	Start	Finish	2018			
					Jun	Jul	Aug	Sep
Total		2356d	21-Mar-13 A	01-Sep-19				
DWP-08 - (2) - Update Progress As of 20 Jun 18		2356d	21-Mar-13 A	01-Sep-19				
Works in KD9 (Include Re-provisioning Works of KD4,KD5)		247d	30-Jan-18 A	23-Sep-18				
External Works Under KD9		151d	30-Jan-18 A	17-Sep-18				
Zone 1		60d	18-Apr-18 A	27-May-18 A				
Drainage Alignment Confirmation for MH72, 73, 74 due to Tree T1106		60d	18-Apr-18 A	27-May-18 A				
EXW_1155	Confirmation, TTA application and construction of re-routing of drainage works near RW8E side	60d	18-Apr-18 A	27-May-18 A	TTA application and construction of re-routing of drainage works near RW8E side			
Zone 4 up to Elderly Facilities		125d	30-Jan-18 A	17-Sep-18				
Elderly Facilities V/039 Received on 22 Jun 2017		100d	30-Jan-18 A	17-Sep-18				
EXW_2270	Facilities fabrication	90d	30-Jan-18 A	13-Aug-18	Facilities fabrication			
EXW_2280	Ground levelling, drainage works and safety met installation	30d	14-Aug-18	17-Sep-18	Ground levelling			
Additional Walkway & Arbour V/040 Received on 22 Aug 2017		93d	28-Mar-18 A	28-Jul-18				
EXW_2310	Associated drainage works for the walkway	20d	28-Mar-18 A	23-May-18 A	Works for the walkway			
EXW_2320	Arbour installation and walkway construction	30d	03-May-18 A	28-Jul-18	Arbour installation and walkway construction			
Reverting Traffic for IEC,VP Rd & TF St & Seawall Reinstatement (KD9)		164d	26-Mar-18 A	23-Sep-18				
TTA Revert Traffic Back to Original Alignment		105d	26-Mar-18 A	28-Jul-18				
East Bound TTA - IEC East Bound, Victoria Park Road & footpath along Sea Side		93d	28-Mar-18 A	28-Jul-18				
TTM Stage 1 - IEC (East Bound)		6d	21-Jun-18	26-Jun-18				
Reinstatement Existing Structure		6d	21-Jun-18	26-Jun-18				
EB_1020	Install metal parapet on parapet wall (30m)	6d	21-Jun-18	26-Jun-18	Install metal parapet on parapet wall (30m)			
TTM Stage 2 - Revert Traffic back to Original Victoria Road		4d	27-Jun-18	30-Jun-18				
Existing Bridge Parapet Reinstatement		4d	27-Jun-18	30-Jun-18				
EB_1180	Install metal parapet on parapet wall (40m)	4d	27-Jun-18	30-Jun-18	Install metal parapet on parapet wall (40m)			
TTM Stage 3 - Reinstatement of Footpath along Seafront		93d	28-Mar-18 A	28-Jul-18				
Reinstatement of Existing Utilities at Existing Footpath		86d	28-Mar-18 A	24-Jul-18				
EB_1600	Lay HGC, PCCW, Whart T&T and NWT telecom ducts and construct drawpits	10d	28-Mar-18 A	24-Jul-18	Lay HGC, PCCW, Whart T&T and NWT telecom ducts and construct drawpits			
EB_1620	Reinstate permanent water main	5d	18-Apr-18 A	17-Jul-18	Reinstate permanent water main			
EB_1580	Water main Connection by WSD	2d	20-Jun-18 A	20-Jun-18 A	Water main Connection by WSD			
Reinstatement of Permanent Footpath at Seafront		49d	27-May-18 A	26-Jul-18				
EB_1630	Backfilling Subbase	3d	27-May-18 A	29-May-18 A	Subbase			
EB_1640	Concreting of Permanent Footpath	4d	29-May-18 A	25-Jul-18	Concreting of Permanent Footpath			
EB_1650	Pedestrian diversion on Permanent Footpath	1d	26-Jul-18	26-Jul-18	Pedestrian diversion on Permanent Footpath			
Reinstatement Works in Traffic Deck Part B		3d	07-May-18 A	28-Jul-18				
EB_1700	Backfill Type B Material up to 2m below F.F.L (Compaction by proof rolling method of 0.2m each layer)	3d	07-May-18 A	28-Jul-18	Backfill Type B Material up to 2m below F.F.L (Compaction by proof rolling method of 0.2m each layer)			
West Bound - IEC West Bound & Tsing fung Street		74d	26-Mar-18 A	06-Jul-18				
TTM Stage 2 - Revert Traffic back to Original Tsing Fung Street		5d	21-Jun-18	25-Jun-18				
Existing Bridge Parapet Reinstatement		5d	21-Jun-18	25-Jun-18				
IECW_1140	Install metal parapet on parapet wall (60m)	5d	21-Jun-18	25-Jun-18	Install metal parapet on parapet wall (60m)			
TTM Stage 3 - Reinstatement of Victoria Park		21d	26-Mar-18 A	06-Jul-18				
Reinstatement Works inside Victoria Park		21d	26-Mar-18 A	06-Jul-18				
IECW_1470	Slope Reinstatement of Victoria Park	21d	26-Mar-18 A	06-Jul-18	Slope Reinstatement of Victoria Park			
Completion of Minor Outstanding / Remaining Works for KD9		110d	18-May-18 A	23-Sep-18				
East Bound - Minor Outstanding Works in Footpath after Substantial Completion of KD9		88d	18-May-18 A	01-Sep-18				



中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Date	Revision	Checked	Approved
20-Jun-18	DWP-08 (2) - 3 Months Rolling	TL	TL

Activity ID	Activity Name	Original Duration	Start	Finish	2018											
					Jun			Jul			Aug			Sep		
					1	2	3	4	5	6	7	8	9	10	11	12
Minor Reinstatement Works for Existing Sign Gantry					75d 30-May-18 A 27-Aug-18											
EB_1750	Laying Public Lighting duct	3d	30-May-18 A	25-Aug-18	Laying Public Lighting duct											
EB_1780	Erect Sign Gantry Steel Supports and Sign Gantry Beam across VPR and IEC E/B	4d	29-Jul-18	01-Aug-18	Erect Sign Gantry Steel Supports and Sign Gantry Beam across VPR and IEC E/B											
EB_1790	Installation of E & M at Sign Gantry (night work)	1d	02-Aug-18	02-Aug-18	Installation of E & M at Sign Gantry (night work)											
EB_1760	Connection of Public Lighting by HyD (Lighting)	2d	26-Aug-18	27-Aug-18	Connection of Public Lighting by HyD (Lighting)											
Minor Reinstatement Works for Central Median of IEC & Footbridge					6d 02-Aug-18 07-Aug-18											
EB_1800	Reconstruction of central divider (6m long, night work)	6d	02-Aug-18	07-Aug-18	Reconstruction of central divider (6m long, night work)											
EB_1810	Dismantlement of temp directional sign mounted on extg footbridge	1d	03-Aug-18	03-Aug-18	Dismantlement of temp directional sign mounted on extg footbridge											
Minor Reinstatement Works for Footpath					88d 18-May-18 A 01-Sep-18											
EB_1820	Place kerblines along VPR footpath	3d	18-May-18 A	23-Aug-18	Place kerblines along VPR footpath											
EB_1850	Backfilling subbase material	2d	27-May-18 A	29-May-18 A	subbase material											
EB_1830	Reinstatement of District Council Welcome Sign and opening plaque at Planter area	1d	24-Aug-18	24-Aug-18	Reinstatement of District Council Welcome Sign and opening plaque											
EB_1840	Re-provision of Tree	8d	25-Aug-18	01-Sep-18	Re-provision of Tree											
Minor Reinstatement Works for Bus Stop					56d 23-May-18 A 29-Aug-18											
EB_1860	Reinstatement of Permanent Bus Stop	5d	23-May-18 A	26-Jun-18 A	Reinstatement of Permanent Bus Stop											
EB_1870	Relocation of Bus Stop	1d	27-Jun-18 A	27-Jun-18 A	Relocation of Bus Stop											
EB_1880	Reinstate Planter(Previous Temporary Bus Stop)	5d	25-Aug-18	29-Aug-18	Reinstate Planter(Previous Temporary Bus Stop)											
Minor Reinstatement Works for Loop Detector					4d 04-Aug-18 07-Aug-18											
EB_1900	Construction of concrete plinth and fix counter housing for Loop Detector (ILDS)	3d	04-Aug-18	06-Aug-18	Construction of concrete plinth and fix counter housing for Loop Detector (ILDS)											
EB_1890	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)	1d	07-Aug-18	07-Aug-18	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)											
West Bound - Completion of Minor Outstanding / Remaining Works for KD9					95d 21-Jun-18 23-Sep-18											
Minor Reinstatement Works for Victoria Park					37d 07-Jul-18 12-Aug-18											
IECW_1500	Re-provision of Tree	32d	07-Jul-18	07-Aug-18	Re-provision of Tree											
IECW_1510	Laying Irrigation Main	10d	22-Jul-18	31-Jul-18	Laying Irrigation Main											
IECW_1520	Construct Landscape Footpath and Lightings	7d	06-Aug-18	12-Aug-18	Construct Landscape Footpath and Lightings											
Minor Reinstatement Works in IEC West Bound					95d 21-Jun-18 23-Sep-18											
IECW_1600	Replacement of new movement joint at IEC W/B (Sun midnight only)	8d	21-Jun-18	28-Jun-18	Replacement of new movement joint at IEC W/B (Sun midnight only)											
IECW_1610	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)	57d	29-Jun-18	24-Aug-18	Repairing of extg conc deck surface after milling of temp asphalt											
IECW_1640	Erection of new precast concrete panels (12 nos.) at abutment M facing to VPR	2d	25-Aug-18	26-Aug-18	Erection of new precast concrete panels (12 nos.) at abutment M											
IECW_1620	Repairing of concrete defects on extg concrete deck and abutment M	30d	25-Aug-18	23-Sep-18	Repairing of concrete defects on extg concrete deck and abutment M											
Works in Victoria Park (KD4, KD5, KD9)					169d 01-Mar-18 A 07-Aug-18											
Re-Provisioning Works					169d 01-Mar-18 A 07-Aug-18											
Nursery Compound					169d 01-Mar-18 A 07-Aug-18											
Nursery compound					169d 01-Mar-18 A 07-Aug-18											
ABWF					27d 05-Apr-18 A 07-Aug-18											
Metal Fence					27d 05-Apr-18 A 07-Aug-18											
VP_NC_1820	Installation	30d	05-Apr-18 A	07-Aug-18	Installation											
Fire Services					14d 21-Jun-18 07-Jul-18											
VP_NC_2030	FS inspection	14d	21-Jun-18	07-Jul-18	FS inspection											
Plumbing and Flushing Water Supplies					14d 21-Jun-18 07-Jul-18											
VP_NC_2100	WSD Inspection	14d	21-Jun-18	07-Jul-18	WSD Inspection											
External Works Aside Nursery Compound					56d 01-Mar-18 A 14-Jul-18											
External Works Around Nursery Compound					56d 01-Mar-18 A 14-Jul-18											

Activity ID	Activity Name	Original Duration	Start	Finish	2018											
					Jun			Jul			Aug			Sep		
					1	2	3	4	5	6	7	8	9	10	11	12
VP_NC_2250	Reinstatement of Existing Boundary Fence Wall Around Nursery Compound	45d	01-Mar-18 A	26-May-18 A	Existing Boundary Fence Wall Around Nursery Compound											
VP_NC_2260	EVA Construction	15d	28-May-18 A	14-Jul-18	EVA Construction											
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks		390d	08-Aug-18	01-Sep-19												
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)		365d	08-Aug-18	07-Aug-19												
EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365d	08-Aug-18	07-Aug-19												
KD13 - Section 7C: Portion IVA, VA, VIII, IX, XII (excl. DBH>500mm)		365d	02-Sep-18	01-Sep-19												
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365d	02-Sep-18	01-Sep-19												
KD18 - Section 11: Transplanted Trees DBH>500mm in Portion VA and XII		365d	08-Aug-18	07-Aug-19												
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365d	08-Aug-18	07-Aug-19												
KD10 - Preservation and Protection of Trees		1088d	21-Mar-13 A	27-Sep-18												
PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	27-Sep-18												
KD15 & KD8 - Mooring Components Upkeep (CBTS and ATS)		979d	15-May-14 A	21-Jun-18												
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	21-Jun-18	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS											

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018																
						May			Jun			Jul			Aug							
Update 2018-05-20 CWB(CC) - Commissioning Contract (SA)																						
PRELIMINARIES AND GENERAL REQUIREMENTS																						
Salient Key Dates and Milestones																						
Anticipated Completion Dates																						
KD03	KD3 - Achievement of Stage 3 (1385 days) - include EOT No.7 (207 days)	0		04-Jun-18*	-171																	
KD02	KD2 - Achievement of Stage 2 (1634 days) - include EOT No.9 (402 days)	0		29-Jun-18*	53																	
KD04	KD4 - Achievement of Stage 4 (1710 days) - include EOT No.9 (414 days)	0		30-Jun-18*	78																	
Possession Dates and Vacation Dates																						
PO-IIa	Possession of Portion IIa (Day 1) - WVB below +6.5mPD	1329	28-Feb-14 A	17-Jun-18	-216																	
PO-III	Possession of Portion III (Day 120) - CH1805-2600	1209	28-Jun-14 A	17-Jun-18	-224																	
PO-Ib	Possession of Portion Ib (Day 242) - CH1580-1805	1087	28-Oct-14 A	17-Jun-18	-216																	
PO-IXd	Possession of Portion IXd (Day 266) - CH4600-4860	1063	21-Nov-14 A	17-Jun-18	-224																	
PO-XI	Possession of Portion XI (Day 296) - EVS	1033	21-Dec-14 A	17-Jun-18	91																	
PO-IIc	Possession of Portion IIc (Day 336) - CH1360-1580	993	30-Jan-15 A	17-Jun-18	-216																	
PO-IIb	Possession of Portion IIb (Day 336) - WVB above +6.5mPD	669	30-Jan-15 A	17-Jun-18	-216																	
PO-IXa	Possession of Portion IXa (Day 392) - CH4860-5150	937	27-Mar-15 A	17-Jun-18	-224																	
PO-Va	Possession of Portion V (Day 607) - CH2950-3210	722	28-Oct-15 A	17-Jun-18	-206																	
PO-VII_a1	Possession of Portion VII (Day 762) - CH3911-4250 (below -6.0mPD)	659	30-Dec-15 A	17-Jun-18	-190																	
PO-Vc	Possession of Portion V (Day 607) - CH3210-3250	658	15-Jan-16 A	17-Jun-18	-188																	
PO-VIb_b1	Possession of Portion VIb (Day 761) - CH3428-3625 (E/B)	619	18-Feb-16 A	17-Jun-18	-172																	
PO-VIb_b2	Possession of Portion VIb (Day 761) - CH3428-3625 (W/B)	568	29-Feb-16 A	17-Jun-18	-166																	
PO-Xa_1	Possession of Portion Xa (Day 650) - ADB Southern Portion (AECOM letter ref: 2015007890T)	589	07-Mar-16 A	17-Jun-18	-353																	
PO-Xb_1	Possession of Portion Xb (Day 804) - ADB Northern Portion	589	07-Mar-16 A	17-Jun-18	-353																	
PO-Vb1	Possession of Portion V (Day 607) - SR3	587	11-Mar-16 A	17-Jun-18	91																	

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline
- ▲ Baseline Milestone

Leighton Contractors (Asia) Limited

Programme Update 51 (May 2018)

THREE MONTH ROLLING

Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 1 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
PO-Ia	Possession of Portion Ia (Day 789) - SCB / SCP1 / SCP2 / Rumsey Street Flyover	600	28-Mar-16 A	17-Jun-18	-324				
PO-VII_a2	Possession of Portion VII (Day 762) - CH3800-3911 (below -6.0mPD)	567	31-Mar-16 A	17-Jun-18	-190				
PO-IXc_1	Possession of Portion IXc (Day 712) - EVB above 3.6mPD - Relinquished on 12 Apr 2016	445	29-Jul-16 A	17-Jun-18	-353				
PO-IXb_1	Possession of Portion IXb (Day 712) - EVB (below +3.6mPD to tunnel top slab) - Relinquished on 12 Apr 2016	445	05-Aug-16 A	17-Jun-18	-353				
PO-VIa_a	Possession of Portion VIa (Day 823) - CH3250-3283	425	15-Aug-16 A	17-Jun-18	-167				
PO-Vb2_a	Possession of Portion V (Day 607) - SR2	456	15-Aug-16 A	17-Jun-18	-183				
PO-VIc_a	Possession of Portion VIc (Day 761) - CH3770-3800 (Access Shaft Opening)	391	23-Sep-16 A	17-Jun-18	-172				
PO-VIb_c	Possession of Portion VIb (Day 761) - CH3625-3770	391	23-Sep-16 A	17-Jun-18	-172				
PO-IVa1	Possession of Portion IVa (Day 930) - CH2600-2720	323	30-Nov-16 A	17-Jun-18	-172				
PO-IVb2	Possession of Portion IVb (Day 930) - MVB (GLD-H)	233	28-Feb-17 A	17-Jun-18	-367				
PO-VIIIa_a	Possession of Portion VIIIa (Day 929) - CH4530-4591 W/B	233	28-Feb-17 A	17-Jun-18	-224				
PO-VIIIa	Possession of Portion VIIIa (Day 929) - CH4250-4600 (Remaining)	241	12-Mar-17 A	17-Jun-18	-224				
PO-VIIIb	Possession of Portion VIIIb (Day 929) - SR8 (CH700-350)	233	12-Mar-17 A	17-Jun-18	-187				
PO-VIIIc	Possession of Portion VIIIc (Day 1039) - SR8 (CH350-310) / SCP4	233	12-Mar-17 A	17-Jun-18	-190				
PO-IVa2_a	Possession of Portion IVa (Day 930) - CH2720-2950	241	12-Mar-17 A	17-Jun-18	-172				
PO-IVb1	Possession of Portion IVb (Day 930) - MVB (GLA-C)	239	14-Mar-17 A	17-Jun-18	-367				
PO-IVa2_b	Possession of Portion IVa (Day 930) - SR1	203	30-Mar-17 A	17-Jun-18	-172				
PO-Vb2_b	Possession of Portion V (Day 607) - SCP3	182	03-Jul-17 A	17-Jun-18	-183				
PO-VIb_a	Possession of Portion VIb (Day 761) - CH3400-3428	80	31-Jul-17 A	17-Jun-18	-166				
PO-VIa_b	Possession of Portion VIa (Day 823) - CH3283-3400	80	31-Jul-17 A	17-Jun-18	-206				
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-May-18	07-Sep-18	-185				
Submissions and Approvals									
Initial General Submission									
10168	Submission of CMC 3DVR	30	20-May-18	18-Jun-18	90				

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 2 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

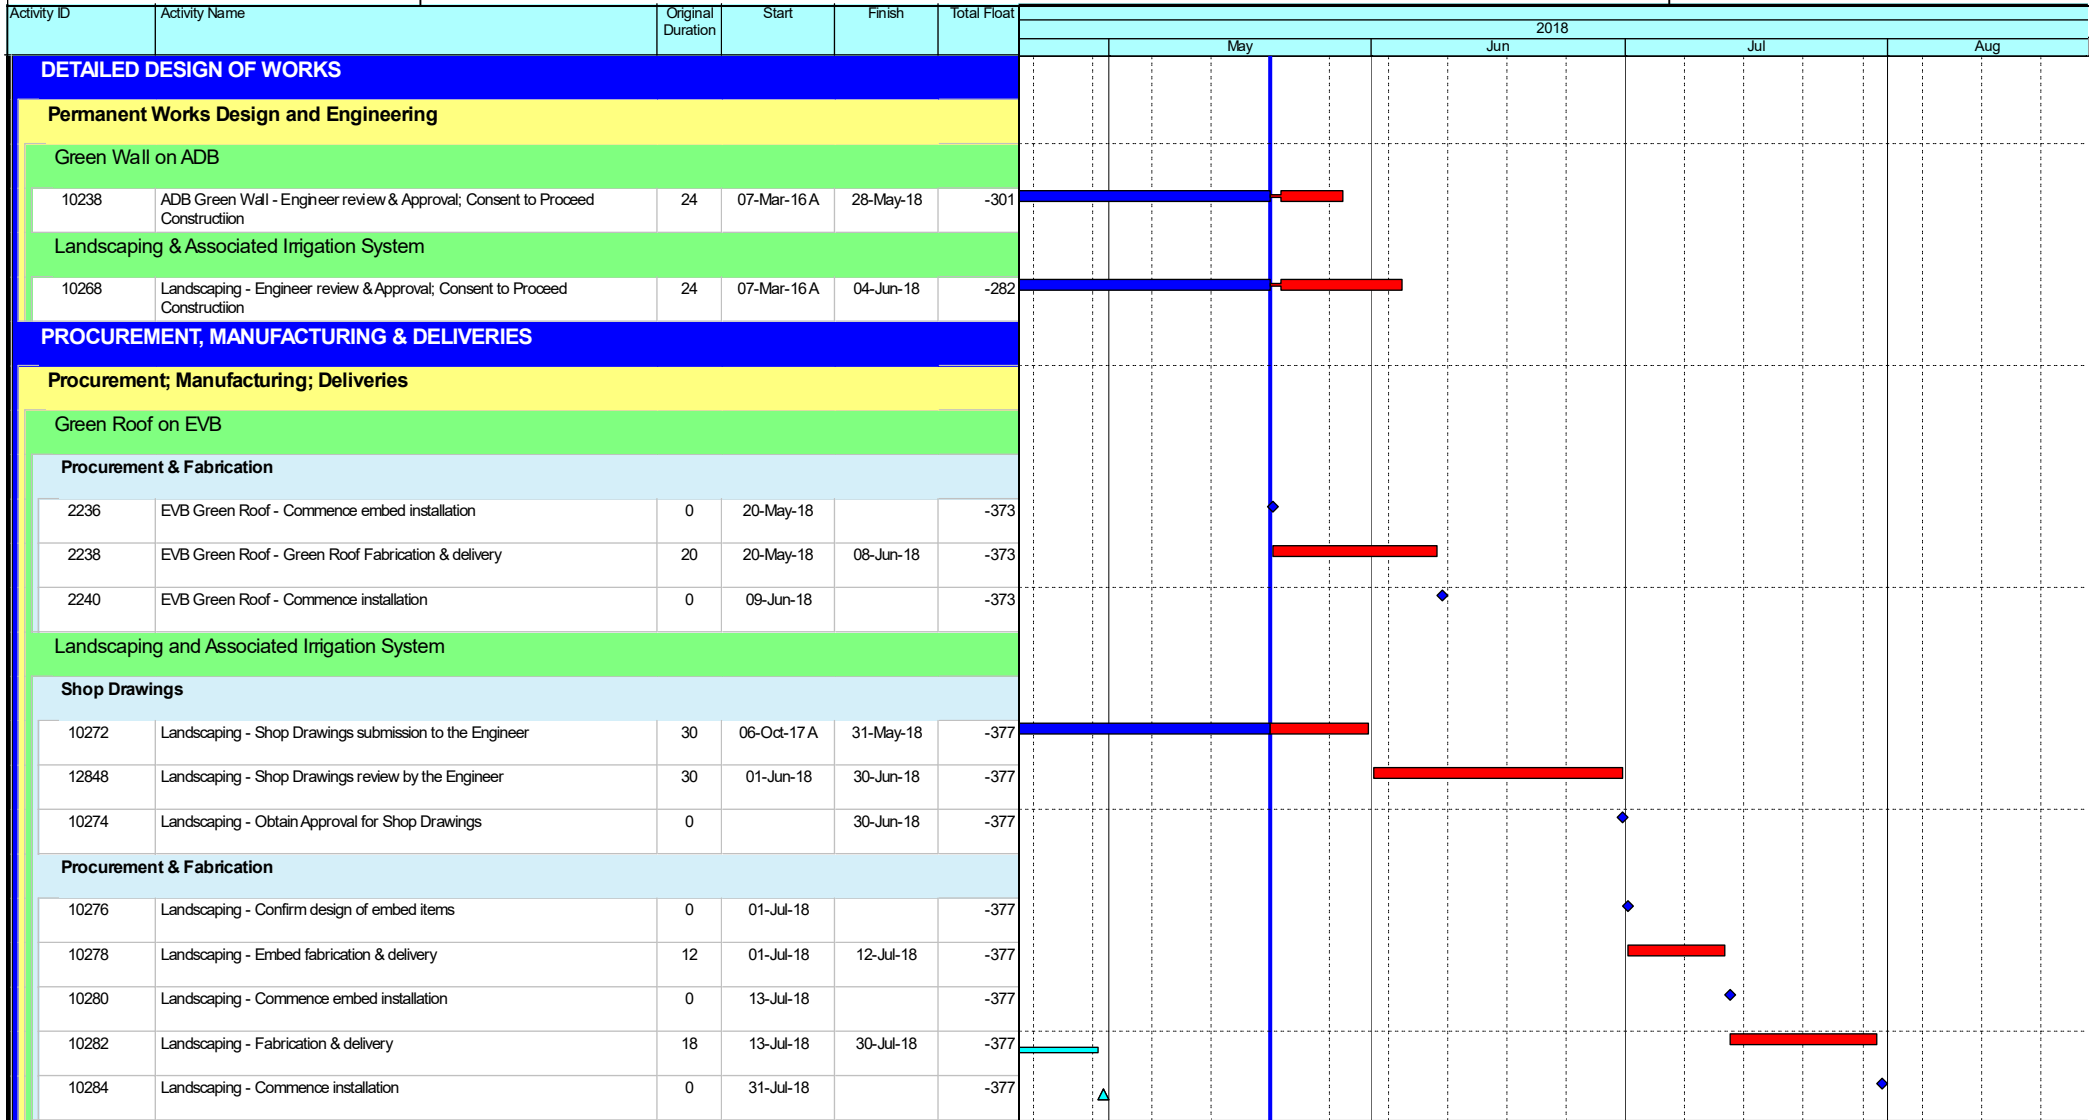

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
Baseline: SA01
Layout: Update Three Month Rolling
U051
Page 3 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
Green Wall on ADB									
Shop Drawings									
12850	ADB Green Wall - Shop Drawings review the Engineer	18	11-Apr-18 A	26-May-18	-374				
10244	ADB Green Wall - Obtain Approval for Shop Drawings	0		26-May-18	-374				
Procurement & Fabrication									
10246	ADB Green Wall - Confirm design of embed items	0	27-May-18		-374				
10248	ADB Green Wall - Embed fabrication & delivery	30	27-May-18	25-Jun-18	-374				
10250	ADB Green Wall - Commence embed installation	0	26-Jun-18		-374				
10252	ADB Green Wall - Green Wall Fabrication & delivery	52	26-Jun-18	16-Aug-18	-374				
10254	ADB Green Wall - Commence installation	0	17-Aug-18		-374				
Architectural Feature on EVS									
Procurement & Fabrication									
10086	EVS - Architectural Features delivery	60	02-Jun-17 A	29-May-18	-150				
Air Purification System (APS)									
Procurement & Fabrication									
13664	APS - Ship to HK Store (3rd Batch)	80	03-Aug-17 A	30-May-18	-155				
2368	APS - QA Stored Equipment	6	23-Aug-17 A	30-May-18	-155				
CONSTRUCTION									
West Ventilation Building (WVB - related)									
Tunnel Section (WVB-related)									
Portion 1a, 1lc [CH840 to CH1360]									
13086	TCSS cabling and sign face installation (FADS01)	40	21-May-18*	09-Jul-18	44				
Westbound									
5016	MEP(WB) - (CH840 to CH1360) E&M Final Fix	24	23-Mar-18 A	04-Jun-18	72				

	Current Milestone		Remaining Work
	Level of Effort		Project Baseline
	Baseline Milestone		Actual Work
	Critical Remaining Work		

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
Baseline: SA01
Layout: Update Three Month Rolling
U051
Page 4 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
5024	MEP(WB) - (CH840 to CH1360) TCSS Field equip & cable installation	18	23-Mar-18 A	04-Jun-18	72				
191519	MEP(WB) - (CH840 to CH1360) Traffic sign / VLSL / LCS installation & cable termination	24	10-Apr-18 A	01-May-18 A					
191515	MEP(WB) - (CH840 to CH1360) aluminium cladding installation	30	16-Apr-18 A	28-May-18	78				
Eastbound									
6104	MEP(EB) - (CH840 to CH1360) E&M Final Fix	24	23-Mar-18 A	04-Jun-18	72				
6106	MEP(EB) - (CH840 to CH1360) TCSS Field equip & cable installation	18	23-Mar-18 A	04-Jun-18	72				
191521	MEP(EB) - (CH840 to CH1360) Traffic sign / VLSL / LCS installation & cable termination	24	10-Apr-18 A	01-May-18 A					
191517	MEP(EB) - (CH840 to CH1360) aluminium cladding installation	30	03-May-18 A	30-May-18	76				
West Ventilation Building (WVB)									
RC Structures and Metal Roof									
Metal Roof									
Metal Roof Eastern Side (M.J. East)									
10442a4	WVB - Installation of extra roof fins support (M.J.East) (VO)	42	11-Sep-17 A	04-Jun-18	-257				
Metal Roof Western Side (M.J. West)									
13666	WVB - Installation of extra roof fins support (M.J.West) (VO)	36	15-Mar-18 A	02-Jun-18	-305				
MEP & ABWF Works									
3088	MEP(WVB) - TCSS Enabling Works (Remaining TCSS / E&M installation)	30	17-Mar-18 A	04-Jun-18	3				
External Works									
3104	WVB - External Fence Wall (VO/131)	48	28-Aug-17 A	30-May-18	-81				
3106	WVB - Final completion works (include CCMS interface)	48	05-Jun-18	01-Aug-18	-133				
10884	WVB - External lamp pole, bollard & recess wall lighting installation	48	05-Jun-18	01-Aug-18	-133				
E&M Testing & Commissioning / Statutory Inspection									
3120d	MEP(WVB) - LUX measurement for tunnel lighting	23	20-May-18	11-Jun-18	-157				
3120a4	MEP(WVB) - TVS N-mode Test (Stage 1)	54	24-Jun-18	16-Aug-18	-223				

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
Baseline: SA01
Layout: Update Three Month Rolling
U051
Page 5 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018				
						May	Jun	Jul	Aug	
Final Completion Works										
191501	WVB - LHDS (Changed from Non-FSI to FSI item) - manufacture and delivery	36	14-Feb-18 A	12-May-18 A						
3132	WVB - APS Site Acceptance Test (Air monitoring station)	42	17-Mar-18 A	31-May-18	17					
191503	WVB - LHDS (Changed from Non-FSI to FSI item) - installation	30	14-May-18 A	13-Jun-18	-155					
KD04M2	APS SAT (WVB) - Milestone for KD04	0		31-May-18	108					
191505	WVB - LHDS (Changed from Non-FSI to FSI item) - T&C	8	14-Jun-18	23-Jun-18	-155					
3134	WVB - TCSS & other E&M systems Site Acceptance Test	18	10-Jul-18	27-Jul-18	51					
KD05M2	TCSS SAT (WVB) - Milestone for KD05	0		27-Jul-18	51					
3140	WVB - Completion of Section 1 (KD06)	0		01-Aug-18	-171					
Landscaping and Irrigation Systems										
3136	WVB - Final completion test for irrigation systems in Portion IIb	60	03-Jun-18	01-Aug-18	-379					
3138	WVB - Landscape Works in Portion IIb (Include architectural lightings & lightning protection system installation)	60	02-Aug-18	30-Sep-18	-379					
Tunnel Flexible Pavement (WVB-related)										
5802	Road(WB) - (CH1480 to CH2600) Road Marking & Traffic Sign	14	11-Jul-18	26-Jul-18	-212					
5806	Road(EB) - (CH1480 to CH2600) Road Marking & Traffic Sign	14	27-Jul-18	11-Aug-18	-212					
Satellite Control Building (SCB)										
External Facade										
3930	SCB - External facing tiles / Louvre	48	12-Oct-17 A	03-May-18 A						
MEP Works										
3944	MEP(SCB) - E&M Final Completion Works; Ready for Statutory Inspections	30	18-Apr-18 A	07-May-18 A						
External Works										
3948	SCB - Final completion works (include CCMS interface)	18	04-Apr-18 A	24-Apr-18 A						
E&M Testing & Commissioning										
3950	MEP (SCB) - E&M System Integrated Testing and Commissioning	30	18-Apr-18 A	09-May-18 A						

- Current Milestone
- Level of Effort
- Remaining Work
- Project Baseline
- Baseline Milestone
- Actual Work
- Critical Remaining Work

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 6 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018				
						May	Jun	Jul	Aug	
KD01M4	MEP (SCB) - Milestone for KD06	0		24-Apr-18 A						
Final Completion Works										
3958	SCB - TCSS & other E&M systems Site Acceptance Test	45	20-May-18	03-Jul-18	-142		[Red Bar]			
3962	SCB - Completion of Section 1	0		03-Jul-18	-142					◆
KD05M6	TCSS SAT (SCB) - Milestone for KD05	0		03-Jul-18	75					◆
Satellite Control Points 1 / 2										
SCP1										
3716	MEP (SCP1) - E&M Final Fix	18	04-Apr-18 A	23-May-18	73	[Blue Bar]				
3718	MEP (SCP1) - E&M Individual System T&C (Include TCSS T&C)	12	24-May-18	06-Jun-18	73		[Yellow Bar]			
3720	MEP (SCP1) - E&M Final Completion Works	12	07-Jun-18	21-Jun-18	73			[Yellow Bar]		
KD01M2	MEP (SCP1) - Milestone for KD06	0		21-Jun-18	73					◆
SCP2										
3740	MEP (SCP2) - E&M Final Fix	18	02-Dec-17 A	23-May-18	85	[Blue Bar]				
3742	MEP (SCP2) - E&M Individual System T&C	12	24-May-18	06-Jun-18	85		[Yellow Bar]			
3744	MEP (SCP2) - E&M Final Completion Works	12	24-May-18	06-Jun-18	85		[Yellow Bar]			
KD01M3	MEP (SCP2) - Milestone for KD06	0		06-Jun-18	85					◆
Middle Ventilation Building (MVB - related)										
Tunnel Section (MVB-related)										
Portion IVa (CH2600 to CH2950)										
Slip Road 1										
10022	MEP(SR1) - (CH171 to CH271) E&M Final Fix	4	15-Mar-18 A	23-May-18	-131	[Blue Bar]				
10046	MEP(SR1) - (CH171 to CH271) VE Panel installation (Upper part) (1200m2)	13	24-May-18	07-Jun-18	-131		[Red Bar]			
10046a	MEP(SR1) - (CH171 to CH271) VE Panel installation (Lower part) (1200m2)	13	24-May-18	07-Jun-18	-131		[Red Bar]			
10024	MEP(SR1) - (CH171 to CH271) TCSS Field equip & cable installation	6	26-May-18	01-Jun-18	74		[Yellow Bar]			

- ◆ Current Milestone
- ▬ Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 7 of 34








Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
10046b	VO 238 - SR1 - Anticipated handover from WDII	0	01-Jun-18*		-183				
10046c	VO 238 - SR1 - Construction of D-wall plinth and install wall brackets	12	01-Jun-18	14-Jun-18	-183				
10046d	VO 238 - SR1 - Installation of granite stone panels / precast concrete panels	40	15-Jun-18	02-Aug-18	-183				
10046e	VO 238 - SR1 - Application of Evonik Protectosil SC60	6	03-Aug-18	09-Aug-18	-183				
Portion Va [CH2950 to CH3210]									
Westbound (Outer Lane)									
5136a	MEP(WB) - (CH2950 to CH3210) E&M Final Fix	10	16-Aug-17 A	23-May-18	-150				
9954a	MEP(WB) - (CH2950 to CH3210) VE Panel installation (Upper part) (1800m2)	20	11-Apr-18 A	28-May-18	-154				
Eastbound (Outer Lane)									
5156a	MEP(EB) - (CH2950 to CH3210) E&M Final Fix	10	03-Apr-18 A	23-May-18	-118				
9956a	MEP(EB) - (CH2950 to CH3210) VE Panel installation (Upper part) (1800m2)	20	09-Apr-18 A	04-Jun-18	-128				
Portion Vb1 (SR3)									
Slip Road 3									
10032b	MEP(SR3) - (CH3089 to CH3334) E&M 1st Fix	13	15-Mar-17 A	25-May-18	-132				
10036b	MEP(SR3) - (CH3089 to CH3334) TCSS Field equip & cable installation	8	15-Mar-17 A	25-May-18	-132				
10048c	MEP(SR3) - (CH3089 to CH3334) VE Panel installation (Lower part) (2940m2)	33	06-Mar-18 A	29-May-18	-135				
10034b	MEP(SR3) - (CH3089 to CH3334) E&M 2nd Fix (include Sump C)	27	11-Apr-18 A	28-May-18	-134				
10038b	MEP(SR3) - (CH3089 to CH3334) E&M Final Fix	8	16-Apr-18 A	29-May-18	-135				
10048b	MEP(SR3) - (CH3089 to CH3334) VE Panel installation (Upper part) (2940m2)	33	21-May-18	29-Jun-18	-161				
10048d	VO 238 - Prepare and finalize design of grouting pad	11	21-May-18*	02-Jun-18	-184				
10048e	VO 238 - Construction of grouting pad	5	04-Jun-18	08-Jun-18	-184				
10048f	VO 238 - Drill and fix wall bracket	11	09-Jun-18	22-Jun-18	-184				
10048c2	MEP(SR3) - Road lighting installation (Portal)	18	12-Jun-18	04-Jul-18	-164				
10048h	VO 238 - Installation of precast concrete	22	23-Jun-18	19-Jul-18	-184				

-  Current Milestone
-  Level of Effort
-  Baseline Milestone
-  Actual Work
-  Critical Remaining Work
-  Remaining Work
-  Project Baseline

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 8 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

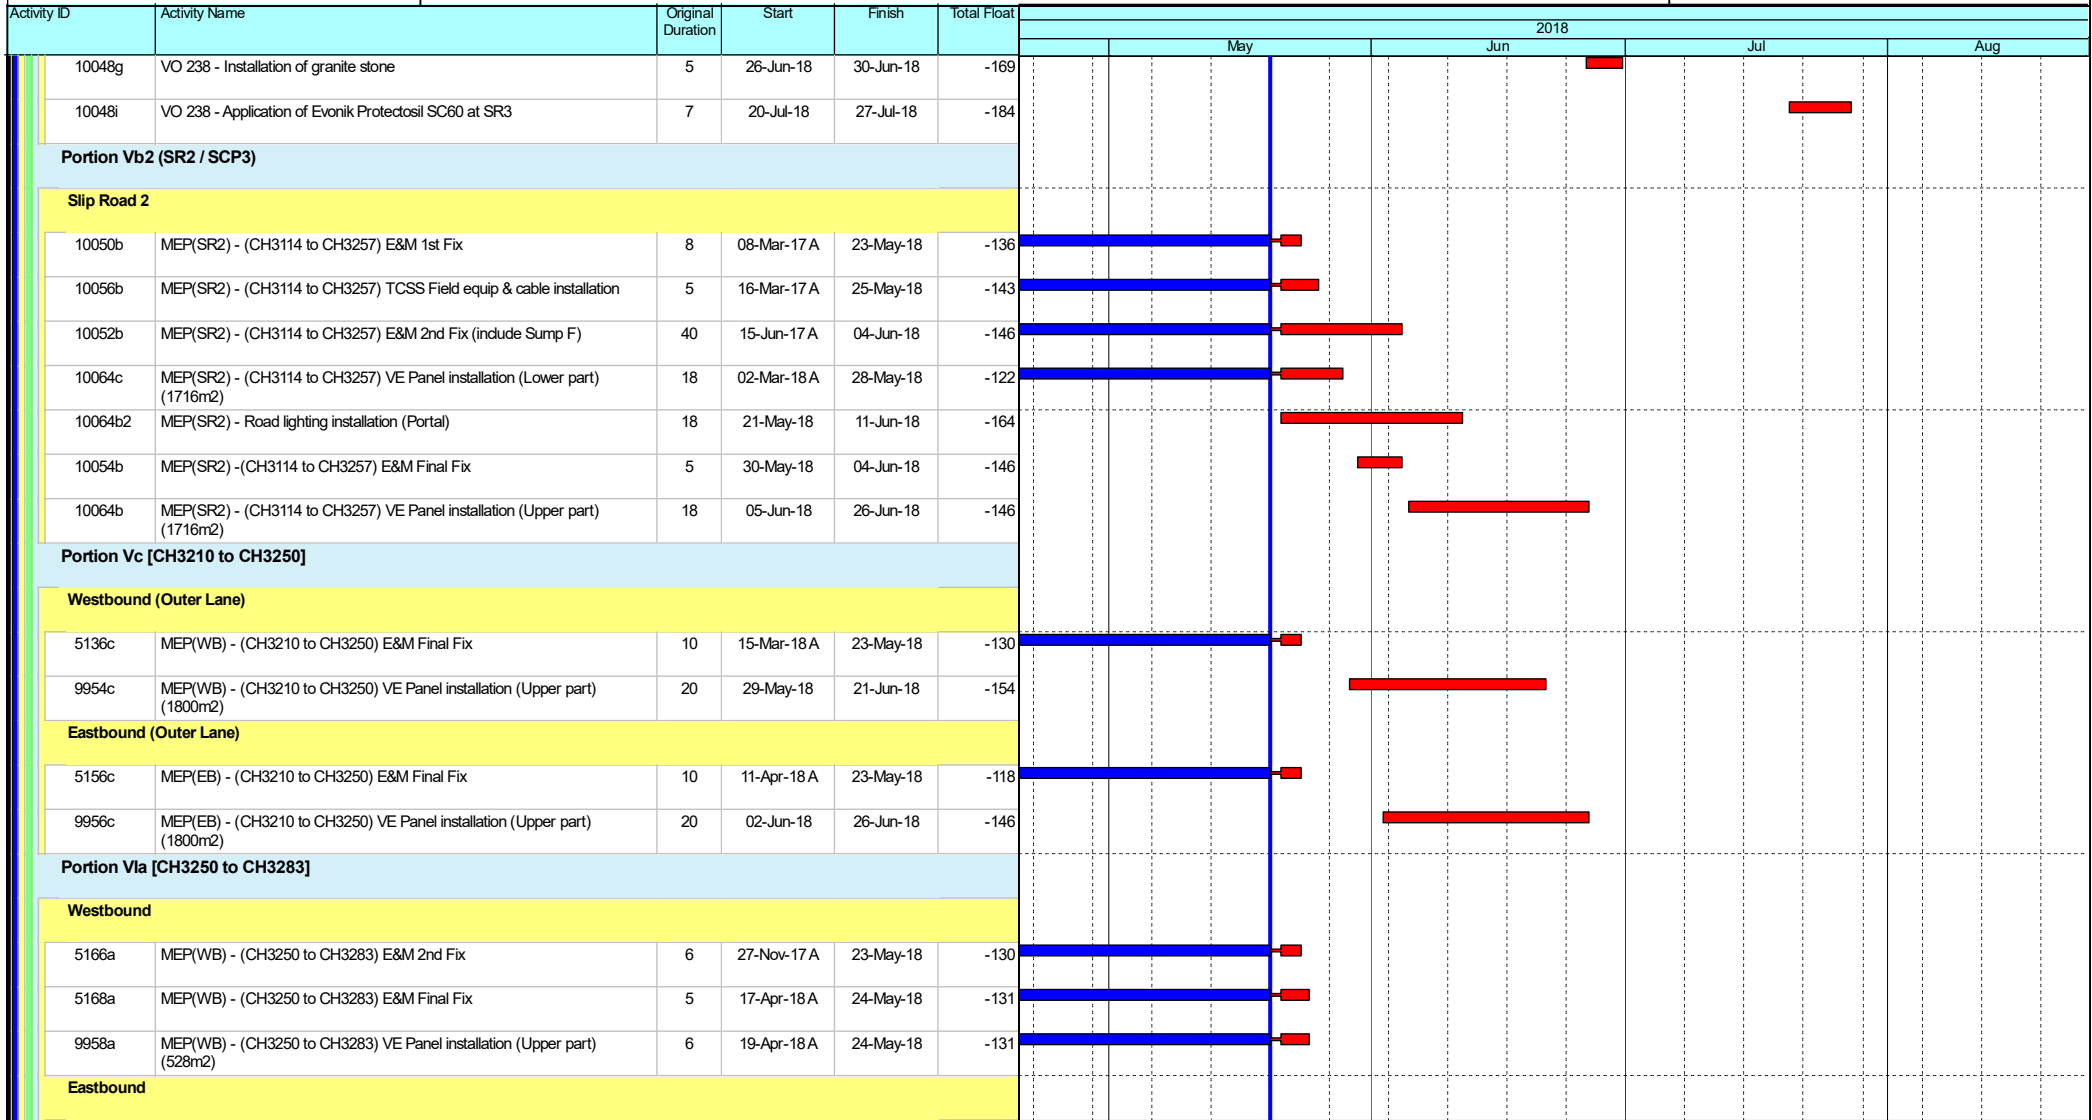

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
Baseline: SA01
Layout: Update Three Month Rolling
U051
Page 9 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
5182a	MEP(EB) - (CH3250 to CH3283) E&M 1st Fix	6	11-Nov-17 A	23-May-18	-118				
5184a	MEP(EB) - (CH3250 to CH3283) E&M 2nd Fix	6	06-Mar-18 A	24-May-18	-119				
5186a	MEP(EB) - (CH3250 to CH3283) E&M Final Fix	5	22-Mar-18 A	25-May-18	-120				
9960a	MEP(EB) - (CH3250 to CH3283) VE Panel installation (Upper part) (528m2)	6	18-Apr-18 A	26-May-18	-121				
Portion VIa [CH3283 to CH3400]									
Westbound									
5166b	MEP(WB) - (CH3283 to CH3400) E&M 2nd Fix	17	07-Dec-17 A	28-May-18	-128				
5168b	MEP(WB) - (CH3283 to CH3400) E&M Final Fix	12	04-Apr-18 A	28-May-18	78				
9958b	MEP(WB) - (CH3283 to CH3400) VE Panel installation (Upper part) (1872m2)	21	10-Apr-18 A	01-Jun-18	-138				
Eastbound									
5186b	MEP(EB) - (CH3283 to CH3400) E&M Final Fix	12	06-Mar-18 A	28-May-18	-168				
9960b	MEP(EB) - (CH3283 to CH3400) VE Panel installation (Upper part) (1872m2)	21	16-Apr-18 A	04-Jun-18	-128				
Portion VIb [CH3400 to CH3428]									
Eastbound									
5218b1	MEP(EB) - (CH3400 to CH3428) E&M Final Fix	12	03-Apr-18 A	23-May-18	82				
Middle Ventilation Building (MVB)									
External Facade									
3238	MVB - External facing tiles / Louvre	90	06-Nov-17 A	30-May-18	-177				
MEP Works									
3280	MEP(MVB) - Lift Installation	70	10-Nov-17 A	23-May-18	-316				
3236	MVB - Metal works / steel platform / Ladders / Handrails	48	06-Dec-17 A	28-May-18	-151				
3248	MEP(MVB) - TCSS Enabling Works (Remaining TCSS installation)	24	03-Jan-18 A	23-May-18	-296				
3280a	MEP(MVB) - lift shaft water leakage (Fix by C19) - Tentative fixed date on 31-May-2018	70	17-May-18 A	23-May-18	-316				
3252	MEP(MVB) - E&M Final Completion Works; Ready for Statutory Inspections	24	31-May-18	28-Jun-18	-177				

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 10 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018					
						May	Jun	Jul	Aug		
E&M Individual System T&C											
3250d	MEP(MVB) - CCMS SAT	12	07-Apr-18 A	11-May-18 A							
3250a	MEP(MVB) - MVAC system	12	23-Apr-18 A	05-May-18 A							
3250h	MEP(MVB) - SAT - LV Capacitor Bank	6	25-Apr-18 A	28-Apr-18 A							
3250b	MEP(MVB) - TVS System Test	12	03-May-18 A	05-May-18 A							
3250m	MEP(MVB) - Damper control panel and tunnel motorized damper functional test	6	09-May-18 A	23-May-18	-296						
3250g	MEP(MVB) - SAT - UPS	6	10-May-18 A	15-May-18 A							
3250c	MEP(MVB) - Lift functional test	6	24-May-18	30-May-18	-253						
Basement 3 - APS Auxiliary Room / APS Plant Area 1 / APS Plant Area 2 (GL D - H)											
3302	APS(MVB) - E&M final fixing	24	01-Mar-18 A	24-May-18	-175						
Basement 3 - Other Rooms / General Area & Corridor											
3407	MEP(MVB) - E&M final fixing	18	12-Mar-18 A	23-May-18	-147						
Basement 3M - Sump Pit for ESP / Sump Pit for DENO2 (GL D - H)											
3296	APS(MVB) - Plant 4 ESP/DeNO2	24	13-Jan-18 A	30-May-18	-170						
Basement 3M - TVF Room											
3309	APS(MVB) - E&M Final Fix	18	07-Mar-18 A	23-May-18	-164						
Basement 3M - Other Rooms / General Area & Corridor											
3313	MEP(MVB) - E&M 1st fixing	24	23-Nov-17 A	25-May-18	-149						
3315	MEP(MVB) - E&M 2nd fixing	24	20-Dec-17 A	28-May-18	-151						
3317	MEP(MVB) - E&M final fixing	24	07-Feb-18 A	04-Jun-18	-157						
Basement 2 (GL D - H)											
Basement 2 - Other Rooms / General Area & Corridor											
19030	MEP(MVB) - E&M 1st fixing	18	28-Nov-17 A	25-May-18	-149						
19032	MEP(MVB) - E&M 2nd fixing	18	19-Dec-17 A	28-May-18	-151						

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
Baseline: SA01
Layout: Update Three Month Rolling
U051
Page 11 of 34


Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
19034	MEP(MVB) - E&M final fixing	18	12-Feb-18 A	01-Jun-18	-155				
Basement 2M (GL D - H)									
Basement 2M - Other Rooms / General Area & Corridor									
19047	MEP(MVB) - E&M 1st fixing	18	02-Dec-17 A	28-May-18	-151				
19049	MEP(MVB) - E&M 2nd fixing	18	19-Dec-17 A	01-Jun-18	-155				
19051	MEP(MVB) - E&M final fixing	18	07-Mar-18 A	04-Jun-18	-157				
Basement 1 (GL D - H)									
Other Rooms / General Area & Corridor									
11314	MEP(MVB) - E&M 1st fixing	24	13-Oct-17 A	25-May-18	-149				
11316	MEP(MVB) - E&M 2nd fixing	24	06-Dec-17 A	28-May-18	-151				
11318	MEP(MVB) - E&M final fixing	24	20-Feb-18 A	01-Jun-18	-155				
Basement 1 (GL A - D)									
MCC Room 1 (B1-04)									
11286	MEP(MVB) - E&M final fixing	24	25-Nov-17 A	25-May-18	-166				
UPS Room 1 (B1-11)									
11294	MEP(MVB) - E&M final fixing	24	09-Dec-17 A	25-May-18	-166				
G/F (GL D - H)									
TVF Fan Room 1 (G-01)									
11396	MEP(MVB) - E&M final fixing	12	01-Mar-18 A	23-May-18	-164				
TVF Fan Room 2 (G-02)									
11404	MEP(MVB) - E&M final fixing	24	03-Mar-18 A	25-May-18	-166				
Other Rooms / General Area & Corridor									
11412	MEP(MVB) - E&M final fixing	24	21-Feb-18 A	23-May-18	-164				
G/F (GL A - D)									



Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
Baseline: SA01
Layout: Update Three Month Rolling
U051
Page 12 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018					
						May	Jun	Jul	Aug		
Fire Control Centre (G-11)											
11380	MEP(MVB) - E&M final fixing	12	02-Mar-18 A	25-May-18	-166						
Other Rooms / General Area & Corridor											
11384	MEP(MVB) - E&M 1st fixing	24	12-Dec-17 A	23-May-18	-147						
11386	MEP(MVB) - E&M 2nd fixing	24	21-Dec-17 A	28-May-18	-151						
11388	MEP(MVB) - E&M final fixing	24	02-Mar-18 A	01-Jun-18	-155						
1/F (GL D - H)											
Other Rooms / General Area & Corridor											
11446	MEP(MVB) - E&M final fixing	18	21-Feb-18 A	23-May-18	-164						
1/F (GL A - D)											
FS Water Tank & Pump Room (L1-05)											
11420	MEP(MVB) - E&M final fixing	12	15-Mar-18 A	23-May-18	-164						
Other Rooms / General Area & Corridor											
11434	MEP(MVB) - E&M 1st fixing	18	14-Dec-17 A	23-May-18	-147						
11436	MEP(MVB) - E&M 2nd fixing	18	29-Dec-17 A	28-May-18	-151						
11438	MEP(MVB) - E&M final fixing	18	15-Feb-18 A	04-Jun-18	-157						
Staircase Pressurization System (B3/F - G/F)											
B3/F - G/F											
191513	SPS(MVB) - new by-pass MSFD	18	16-Apr-18 A	23-Apr-18 A							
191469	SPS(MVB) - LMCP installation	6	18-Apr-18 A	20-Apr-18 A							
191471	SPS(MVB) - SPS control panel	6	18-Apr-18 A	23-Apr-18 A							
191473	SPS(MVB) - Termination	6	24-Apr-18 A	25-Apr-18 A							
191475	SPS(MVB) - Testing & Commissioning	12	26-Apr-18 A	04-May-18 A							
Smoke Extraction System (B3/F - G/F)											

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 13 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018					
						May	Jun	Jul	Aug		
B3/F - G/F											
191479	SES(MVB) - Wiring	30	12-Mar-18 A	25-May-18	-164						
191481	SES(MVB) - LMCP installation	6	16-Apr-18 A	26-May-18	-165						
191483	SES(MVB) - SES control panel	6	18-Apr-18 A	26-May-18	-165						
191485	SES(MVB) - Termination	6	24-May-18	30-May-18	-165						
191487	SES(MVB) - Testing & Commissioning	12	31-May-18	13-Jun-18	-165						
External Works											
3254	MVB - Road and drainage works (EVA)	30	26-Feb-18 A	28-May-18	-164						
3258	MVB - External concrete pavement	42	04-Apr-18 A	11-Jun-18	-163						
3262	MVB - Final completion works (include CCMS interface)	30	05-Apr-18 A	11-Jun-18	-163						
3260	MVB - External Fence Wall	42	10-Apr-18 A	11-Jun-18	-163						
E&M Testing & Commissioning / Statutory Inspection											
3264	MEP(MVB) - E&M System Integrated Testing and Commissioning	24	24-May-18	16-Jun-18	-234						
3264a	MEP(MVB) - TVS & CCMS System Integrated Testing and Commissioning	24	24-May-18	16-Jun-18	-234						
3264b	MEP(MVB) - Tunnel Lighting & CCMS System Integrated Testing and Commissioning	24	24-May-18	16-Jun-18	-234						
3264c	MEP(MVB) - Fire Services & CCMS System Integrated Testing and Commissioning	24	24-May-18	16-Jun-18	-234						
3264a2	MEP(MVB) - TVS E-mode Test (Stage 2)	18	24-May-18	10-Jun-18	-234						
12606	MEP(MVB) - Submission of Form 5 to EMSD	0	31-May-18		-198						
12606a	MEP(MVB) - Use Permit - Lift	0	14-Jun-18		-198						
3264a4	MEP(MVB) - TVS N-mode Test (Stage 2)	54	24-Jun-18	16-Aug-18	-223						
3266	MEP(MVB) - Ready for Statutory Inspection	0	29-Jun-18		-177						
12622b	MEP(MVB) - Submission of Form 501 to FSD (include SES / SPS) (Building)	0	29-Jun-18		-177						
12650	MEP(MVB) - Submission of Form 314 to FSD	0	29-Jun-18		-225						
KD02M1	MEP(MVB) - Milestone for KD02	0		29-Jun-18	-137						

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 14 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

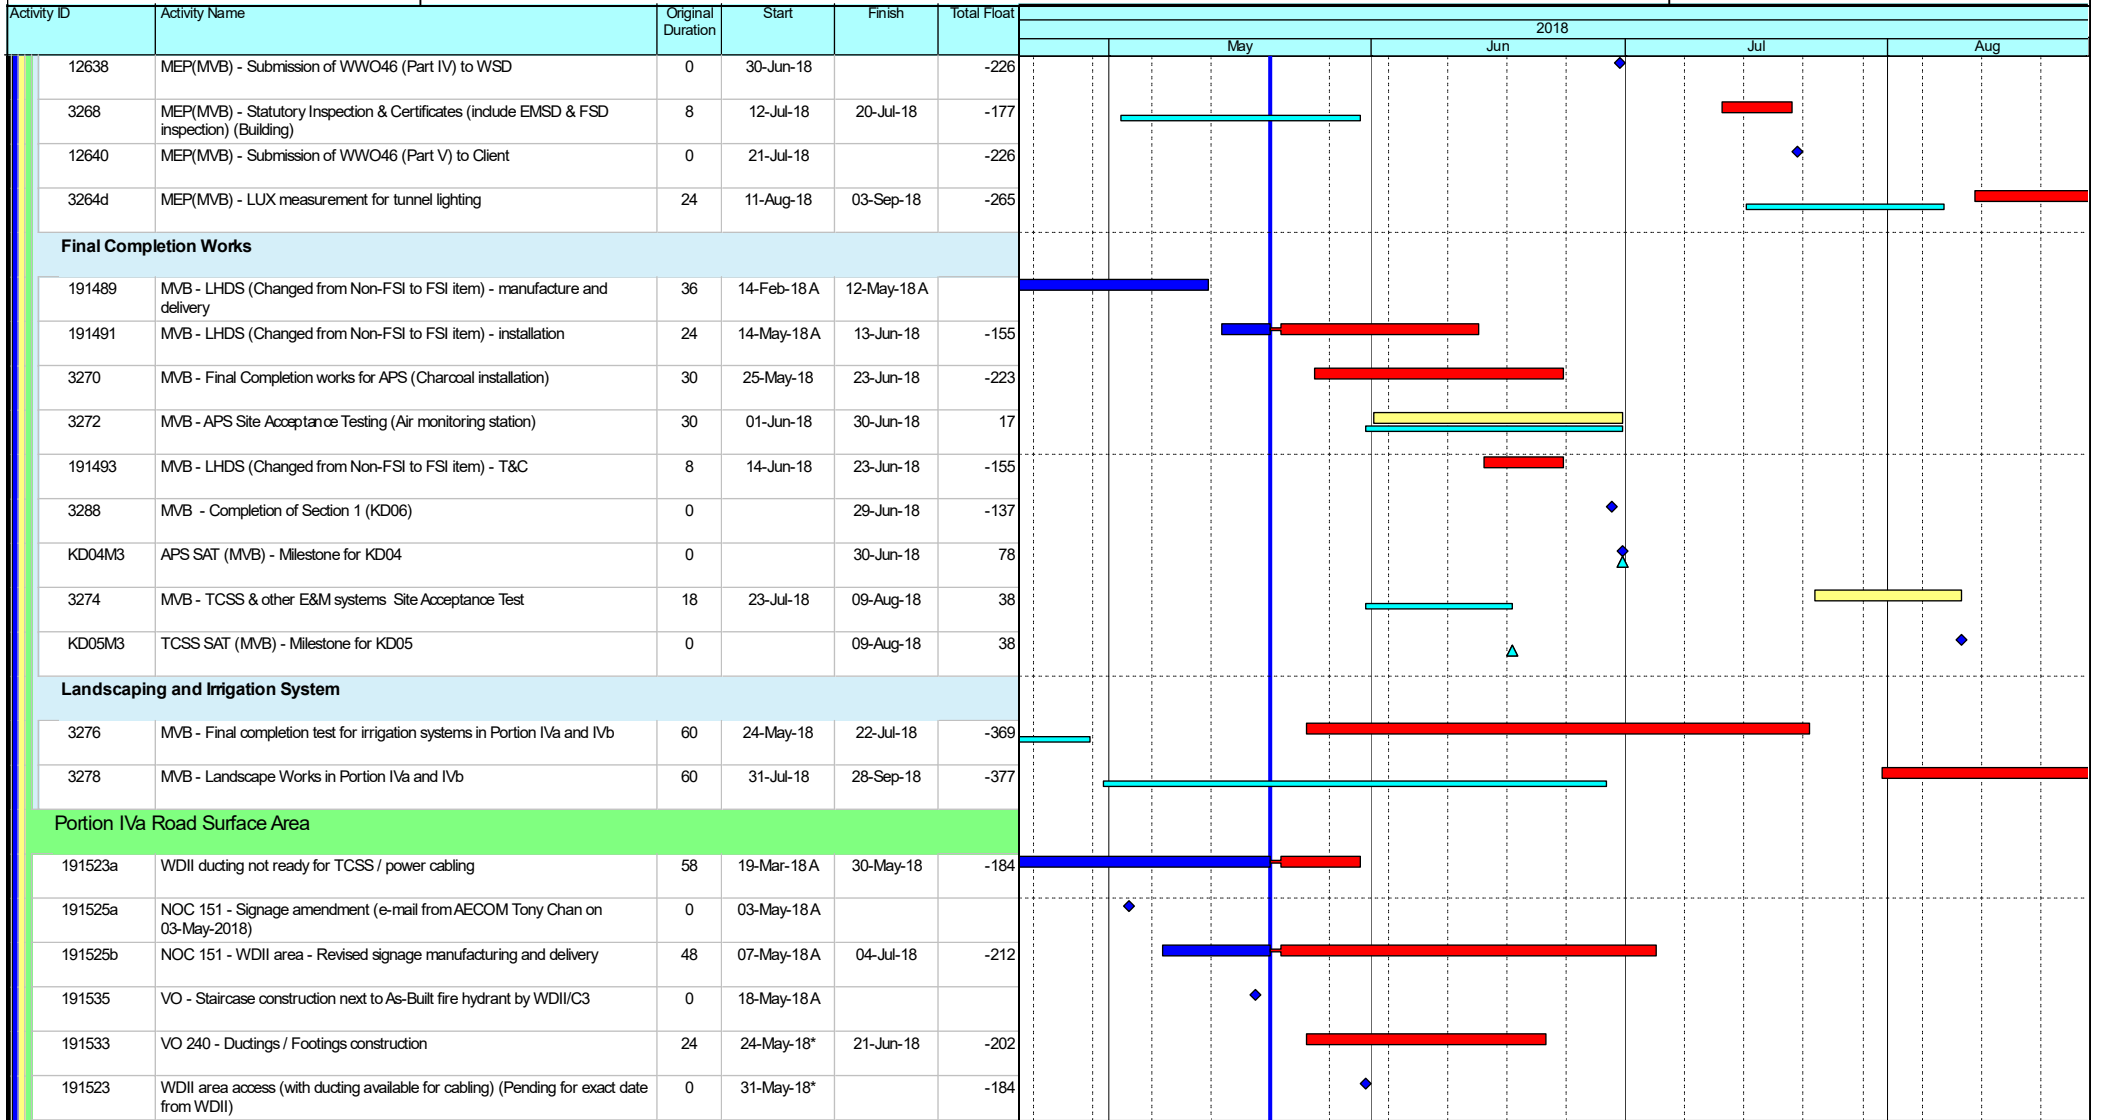

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 15 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
191537	VO - Staircase construction and railing installation	12	11-Jun-18*	25-Jun-18	-174				
191525	WDII area - TCSS equipment / signage / lumimeter installation, cabling & termination	24	05-Jul-18	01-Aug-18	-212				
191527	WDII area - TCSS SCT	24	02-Aug-18	29-Aug-18	-212				
Satellite Control Point 3									
SCP3									
3766	MEP(SCP3) - E&M Final Fix	12	12-Dec-17 A	23-May-18	73				
3774	SCP3 - Metal works / Glazing / Louver / Handrails	12	19-Apr-18 A	04-May-18 A					
10110	MEP(SCP3) - TCSS Enabling Works (Remaining TCSS installation)	12	21-May-18	04-Jun-18	3				
3768	MEP(SCP3) - E&M Individual System T&C	12	24-May-18	06-Jun-18	73				
3770	MEP(SCP3) - E&M Final Completion Works; Ready for Statutory Inspections	12	07-Jun-18	21-Jun-18	73				
KD02M2	MEP(SCP3) - Milestone for KD06	0		21-Jun-18	73				
East Ventilation Building (EVB - related)									
Tunnel Section (EVB-related)									
Portion VIc [CH3770 to CH3800]									
Eastbound									
5220c	MEP(EB) - (CH3770 to CH3800) E&M 2nd Fix	12	21-Dec-17 A	23-May-18	-123				
5218c	MEP(EB) - (CH3770 to CH3800) E&M Final Fix	12	13-Mar-18 A	28-May-18	-127				
9964c	MEP(EB) - (CH3770 to CH3800) VE Panel installation (Upper part) (450m2)	5	29-May-18	02-Jun-18	-127				
Portion VII [CH3800 to CH3911]									
Eastbound									
9968a4	MEP(EB) - (CH3800 to CH3911) VE Panel installation (Upper part) (1332m2)	14	09-Apr-18 A	25-May-18	-138				
Portion VII [CH3911 to CH4250]									
Access Shaft Opening									
10120a2	VII(WB) - Waterproofing on Shaft tunnel slab	18	17-Mar-18 A	18-May-18 A					

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 16 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
10120a3	VI(WB) - Backfilling (78 layers; 1 day/layer)	78	05-Apr-18 A	23-May-18	97				
Westbound									
5232a2	MEP(WB) - (CH3911 to CH4250) E&M Final Fix	16	23-Mar-18 A	23-May-18	-136				
9966a2	MEP(WB) - (CH3911 to CH4250) VE Panel installation (Upper part) (4068m2)	21	11-Apr-18 A	25-May-18	-138				
Eastbound									
5250a2	MEP(EB) - (CH3911 to CH4250) E&M Final Fix	16	29-Mar-18 A	23-May-18	-151				
9968a2	MEP(EB) - (CH3911 to CH4250) VE Panel installation (Upper part) (4086m2)	12	14-Apr-18 A	25-May-18	-153				
Portion VIIa [CH4250 to CH4600]									
Eastbound									
9972	MEP(EB) - (CH4250 to CH4600) VE Panel installation (Upper part) (3900m2)	11	24-Jan-18 A	23-May-18	-136				
Portion IXd [CH4600 to CH4860]									
Eastbound									
9976	MEP(EB) - (CH4600 to CH4860) VE Panel installation (Upper part) (3300m2)	37	22-Mar-18 A	25-May-18	-138				
5314	MEP(EB) - (CH4600 to CH4860) E&M Final Fix	9	30-Mar-18 A	23-May-18	-136				
Portion IXa [CH4860 to CH5150]									
Eastbound									
5346	MEP(EB) - (CH4860 to CH5150) E&M Final Fix	10	14-Mar-18 A	23-May-18	67				
5348	MEP(EB) - (CH4860 to CH5150) TCSS Field equip & cable installation	9	04-Apr-18 A	23-May-18	67				
9980	MEP(EB) - (CH4860 to CH5150) VE Panel installation (Upper part) (3288m2)	37	05-Apr-18 A	28-May-18	-140				
Portion VIIIc [SR8 CH350 to CH210]									
Slip Road 8									
5378	MEP(SR8) - (CH350 to CH210) E&M Final Fix	5	03-Apr-18 A	23-May-18	-151				
East Ventilation Building (EVB)									
RC Structures and Green Roof									

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 17 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
3456	EVB - Green Roof (include architectural lighting & lightning protection system installation)	42	09-Jun-18	30-Jul-18	-297				
External Facade									
3438	EVB - External facing tiles / Treated Waste Wood / Louvre	90	11-Sep-17 A	28-May-18	-155				
MEP Works									
3436	EVB - Metal works / steel platform / Ladders / Handrails	48	29-Dec-17 A	28-May-18	-155				
3452	MEP(EVB) - E&M Final Completion Works; Ready for Statutory Inspections	21	11-Apr-18 A	04-Jun-18	-161				
E&M Individual System T&C									
3450d	MEP(EVB) - CCMS SAT	30	19-Jan-18 A	28-May-18	-249				
3450p	MEP(EVB) - Smoke Extraction System System Test	12	09-Mar-18 A	14-May-18 A					
3450c	MEP(EVB) - Lift functional test	6	18-Apr-18 A	10-May-18 A					
3450o	MEP(EVB) - Staircase Pressurization System Test	15	20-May-18	03-Jun-18	-202				
3660d	MEP(ADB) - LUX measurement for tunnel lighting	28	20-May-18	16-Jun-18	-162				
Basement 1 (GL D - L)									
Water Tank & Pump Room (B1-16)									
11636	MEP(EVB) - E&M final fixing	24	04-Nov-17 A	03-May-18 A					
TVF Room 3 (B1-19)									
11628a4	MEP(EVB) - Thermal enclosure for actuator T&C	6	17-Apr-18 A	21-May-18	-192				
Staircase Pressurization System (B2/F - G/F)									
B2/F - G/F									
191531b	VO/232 - Lift Pressurization System (LPS) installation	49	12-Mar-18 A	12-May-18 A					
191345	SPS(EVB) - Airduct work and FRP enclosure	20	15-Mar-18 A	04-May-18 A					
191387	SPS(EVB) - Final connection of air duct after modification of air vent shaft	18	28-Mar-18 A	05-May-18 A					
191531c	Take down part of LPS system for injection - leakage from C19 concrete wall	1	10-May-18 A	10-May-18 A					
191531e	Change rusted pipes	3	11-May-18 A	14-May-18 A					

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline
- ▲ Baseline Milestone

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 18 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

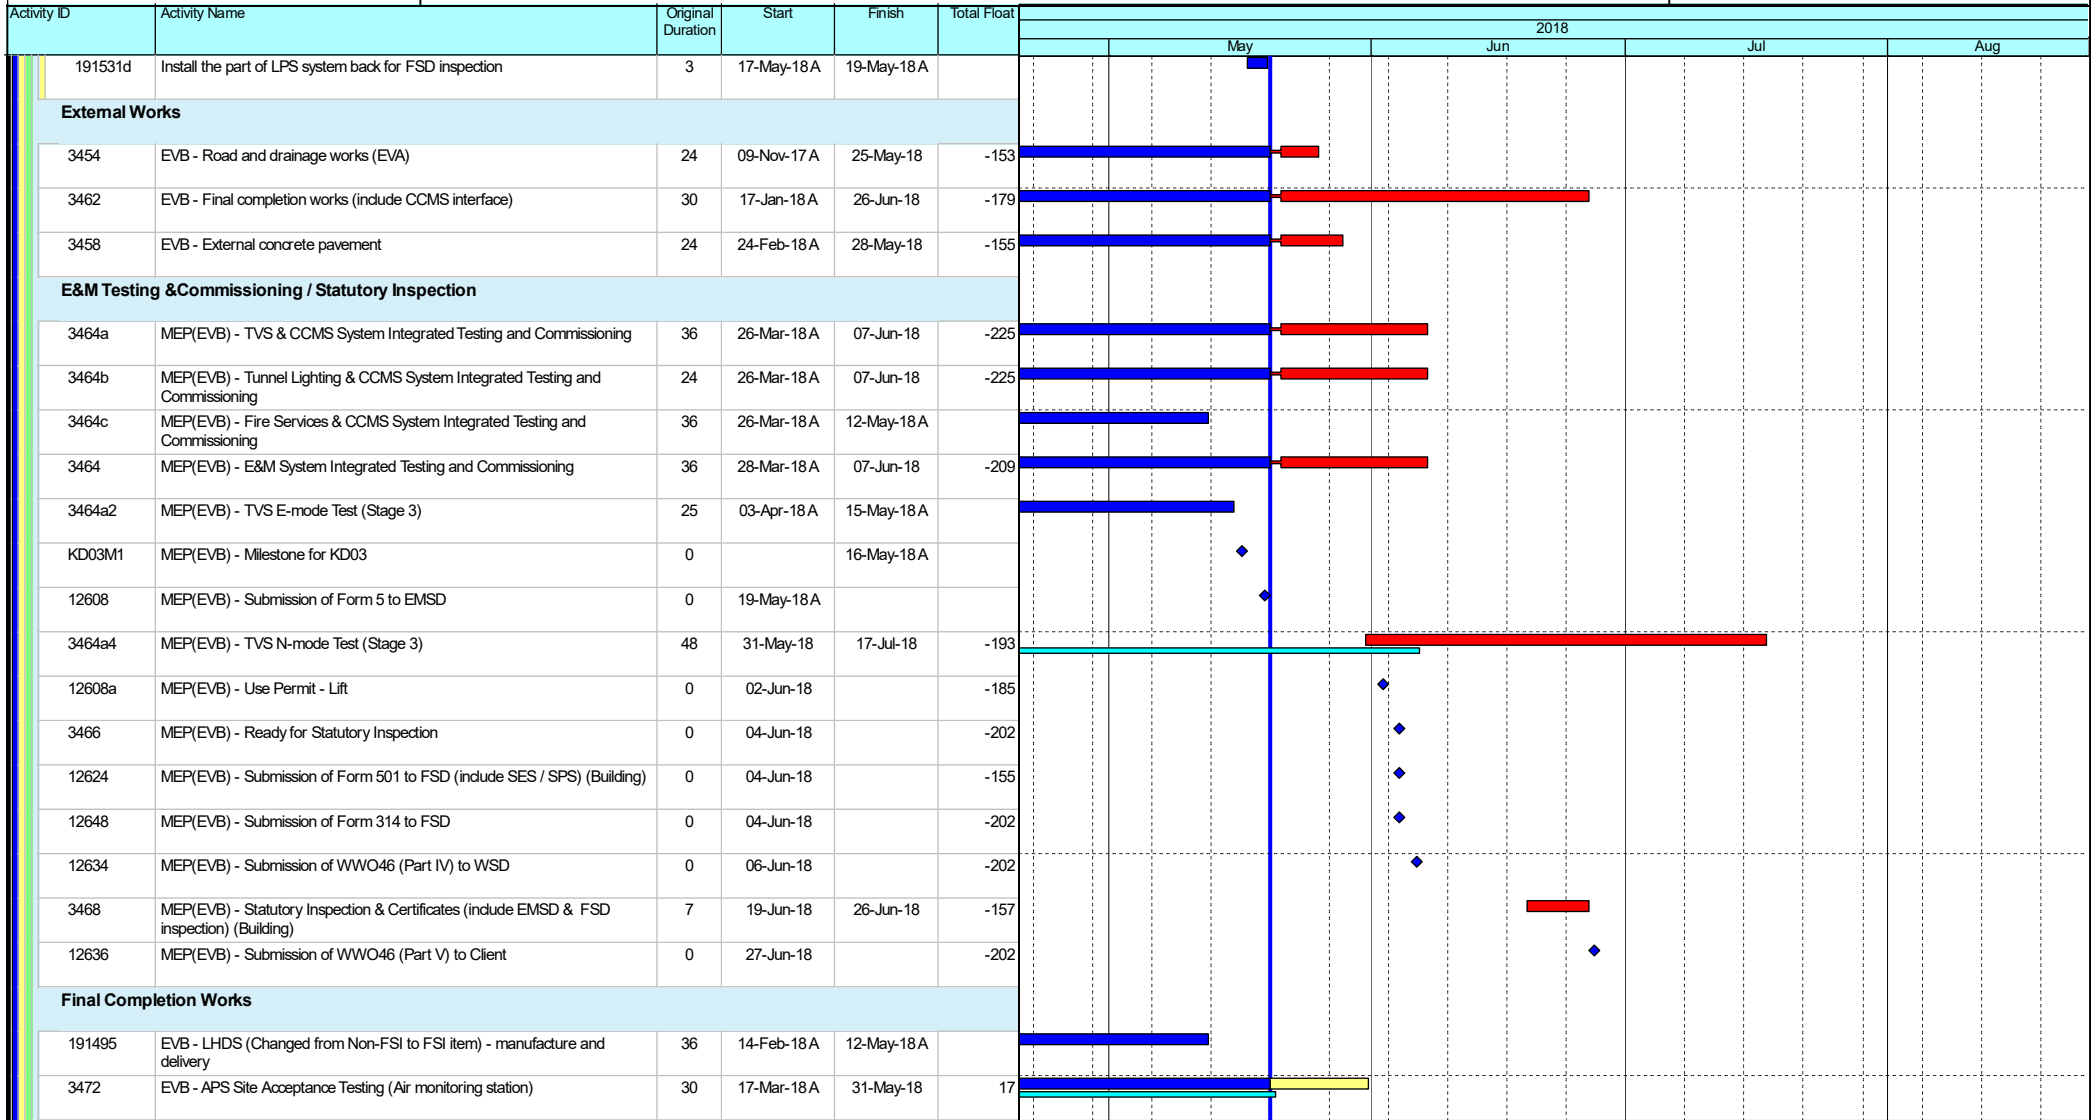

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling U051
 Page 19 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
3470	EVB - Final Completion works for APS (Charcoal installation)	30	06-Apr-18 A	12-May-18 A					
191497	EVB - LHDS (Changed from Non-FSI to FSI item) - installation	20	14-May-18 A	13-Jun-18	-155				
KD04M4	APS SAT (EVB) - Milestone for KD04	0		31-May-18	108				
3488	EVB - Completion of Section 1 (KD06)	0		04-Jun-18	-112				
3474	EVB - TCSS & other E&M systems Site Acceptance Test	18	08-Jun-18	25-Jun-18	65				
191499	EVB - LHDS (Changed from Non-FSI to FSI item) - T&C	8	14-Jun-18	23-Jun-18	-155				
KD05M4	TCSS SAT (EVB) - Milestone for KD05	0		25-Jun-18	83				
Landscaping and Irrigation System									
3476	EVB - Final completion test for irrigation systems in Portion IXc	52	31-Jul-18	20-Sep-18	-370				
3478	EVB - Landscape Works in Portion IXc	52	06-Aug-18	26-Sep-18	-375				
Tunnel Flexible Pavement (EVB-related)									
5822	Road(EB) - (CH3770 to CH5149.3) Road Marking & Traffic Sign	12	13-Aug-18	25-Aug-18	-212				
Administration Building (ADB)									
RC Structures (Portion Xa / Xb)									
13484	ADB - Green Wall	35	17-Aug-18	27-Sep-18	-301				
External Facade									
13248	ADB - External facing tiles / Louvre	48	27-Dec-17 A	19-Jun-18	-248				
MEP & ABWF Works									
13254	MEP(ADB) - TCSS Enabling Works (Remaining TCSS installation)	30	12-Dec-17 A	28-May-18	-260				
13260	MEP(ADB) - Lift Installation	60	06-Jan-18 A	31-May-18	-353				
13252	ADB - Metal works / steel platform / Ladders / Handrails	42	13-Feb-18 A	13-Jun-18	79				
13258	MEP(ADB) - E&M Final Completion Works; Ready for Statutory Inspections	30	29-May-18	04-Jul-18	-260				
E&M Individual System T&C									
13256h	MEP(ADB) - SAT - LV Capacitor Bank	5	03-Apr-18 A	23-May-18	-277				

- Current Milestone
- Remaining Work
- Level of Effort
- Project Baseline
- Baseline Milestone
- Actual Work
- Critical Remaining Work

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 20 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

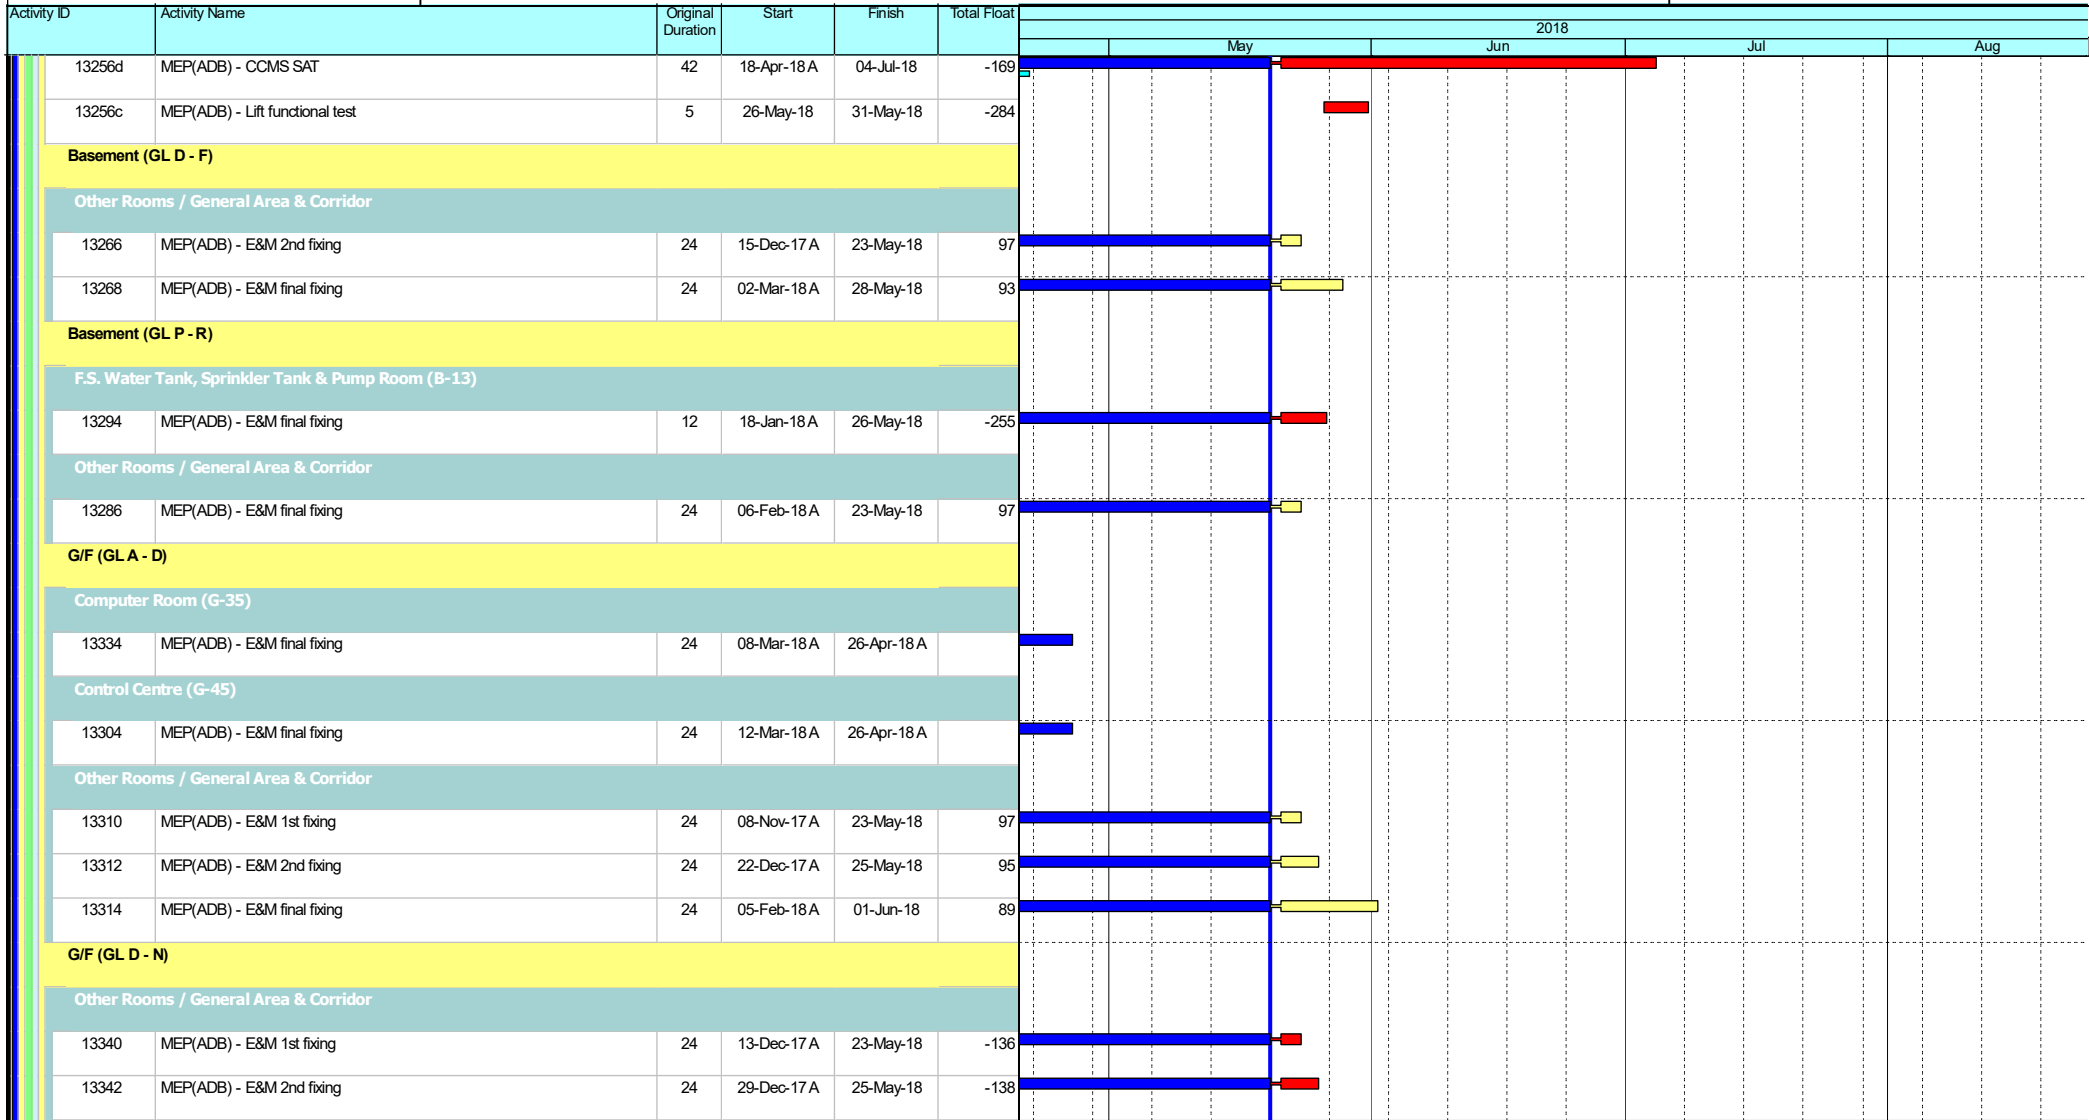

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 21 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
13344	MEP(ADB) - E&M final fixing	24	07-Feb-18 A	01-Jun-18	-144				
G/F (GL P - R)									
Other Rooms / General Area & Corridor									
13408	MEP(ADB) - E&M 1st fixing	24	10-Jan-18 A	23-May-18	-136				
13410	MEP(ADB) - E&M 2nd fixing	24	13-Feb-18 A	25-May-18	-138				
13412	MEP(ADB) - E&M final fixing	24	06-Mar-18 A	28-May-18	-140				
1/F (GL A - D)									
Water Pump Room (L1-08)									
13430	MEP(ADB) - E&M 2nd fixing	12	18-Dec-17 A	23-May-18	-252				
13426	MEP(ADB) - Installation of water Pump	24	28-Dec-17 A	23-May-18	-252				
13428	MEP(ADB) - E&M final fixing	24	10-Jan-18 A	26-May-18	-255				
External Works									
13432	ADB - Road and drainage works (EVA)	42	11-Dec-17 A	28-May-18	-91				
13438	ADB - Final completion works (include CCMS interface)	60	09-Jan-18 A	30-Jun-18	-107				
13434	ADB - External concrete pavement (EVA)	24	18-Jan-18 A	30-Jun-18	-107				
3254b	VO/209 - Design submission for approval (re-submitted and rejected twice) (Form 542)	0	05-Mar-18 A	03-May-18 A					
3254c	VO/209 - Design re-submission for approval (Form 542)	0	15-May-18 A						
13436	ADB - External Fence Wall (include metal gate)	21	18-May-18 A	30-Jun-18	-107				
3254d	VO/209 - Design approval (Tentative)	0		25-May-18*	-107				
3254e	VO/209 - WWO46 Part I & II approval	12	26-May-18	08-Jun-18	-107				
3254f	VO/209 - VO Works installation (Street fire hydrant and water connection at EVA of ADB)	12	09-Jun-18	23-Jun-18	-107				
E&M Testing & Commissioning / Statutory Inspection									
13458	MEP(ADB) - Submission of WWO46 (Part IV) to WSD	0	26-May-18		-191				
13444	MEP(ADB) - Ready for Statutory Inspection (Building)	0	28-May-18		-255				

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
Baseline: SA01
Layout: Update Three Month Rolling
U051
Page 22 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
13456	MEP(ADB) - Submission of Form 501 to FSD (Building)	0	28-May-18		-255				
13462	MEP(ADB) - Submission of Form 314 to FSD	0	28-May-18		-148				
13454	MEP(ADB) - Submission of Form 5 to EMSD	0	01-Jun-18		-184				
3660a2	MEP(ADB) - TVS & CCMS System Integrated Testing and Commissioning	36	06-Jun-18	11-Jul-18	-217				
13446	MEP(ADB) - Statutory Inspection & Certificates (include EMSD & FSD inspection) (Building)	7	08-Jun-18	15-Jun-18	-149				
KD03M7	MEP(ADB) - Milestone for KD06	0		13-Jun-18	95				
13454a	MEP(ADB) - Use Permit - Lift (Non-FS)	0	15-Jun-18		94				
13460	MEP(ADB) - Submission of WWO46 (Part V) to Client	0	16-Jun-18		-191				
13446a	MEP(ADB) - Statutory Inspection & Certificates (FSD inspection) (SFH & EVA)	2	03-Jul-18	04-Jul-18	-2				
Final Completion Works									
191507	ADB - MFCP manufacture & delivery	44	05-Apr-18 A	19-May-18 A					
13464	ADB - TCSS & other E&M systems Site Acceptance Test	18	02-May-18 A	29-May-18	-212				
191509	ADB - MFCP installation	18	20-May-18	06-Jun-18	-196				
13468	ADB - Tunnel FS operation test	30	28-May-18	26-Jun-18	-319				
KD05M8	TCSS SAT (ADB) - Milestone for KD05	0		29-May-18	110				
191511	ADB - MFCPT&C	14	07-Jun-18	20-Jun-18	-196				
13466	ADB - Completion of Section 1 (KD06)	0		30-Jul-18	48				
Landscaping and Irrigation System									
13588	ADB - Final completion test for irrigation systems in PortionXa and Xb	60	01-Jun-18	30-Jul-18	-353				
13590	ADB - Landscape Works in Portion Xa and Xb	60	31-Jul-18	28-Sep-18	-377				
East Ventilation Shaft (EVS)									
ABWF Works									
3826	EVS - ABWF (Dry Trade)	60	20-Sep-17 A	28-May-18	93				
3830	EVS - Metal works / steel platform / Ladders / Handrails	48	19-Dec-17 A	04-Jun-18	87				

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline
- ▲ Baseline Milestone

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 23 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018					
						May	Jun	Jul	Aug		
External Facade											
19060	EVS - Cone louvre installation	60	07-Feb-17 A	19-Jun-18	-121						
3832	EVS - Architectural Features of EVS	120	12-Jul-17 A	26-Jun-18	-115						
MEP Works											
3836	MEP(EVS) - E&M 1st Fix	12	05-Sep-17 A	25-May-18	-113						
3838	MEP(EVS) - E&M 2nd Fix	12	20-Sep-17 A	30-May-18	-117						
19054	MEP(EVS) - Lightning protection system installation and T&C	12	11-Oct-17 A	01-Jun-18	-95						
3840	MEP(EVS) - E&M Final Fix	12	31-May-18	13-Jun-18	-117						
3844	MEP(EVS) - E&M Individual System T&C	12	14-Jun-18	28-Jun-18	-117						
19056	MEP(EVS) - Features lighting installation and T&C	24	20-Jun-18	18-Jul-18	-121						
3846	MEP(EVS) - E&M Final Completion Works; Ready for Statutory Inspections	6	29-Jun-18	06-Jul-18	-117						
External Works											
3850	EVS - External concrete pavement	12	20-Jun-18	04-Jul-18	-109						
3854	EVS - Final completion works (include CCMS interface)	12	28-Jun-18	12-Jul-18	-116						
E&M Testing & Commissioning / Statutory Inspection											
3856	MEP(EVS) - E&M System Integrated Testing and Commissioning	6	07-Jul-18	12-Jul-18	-152						
3858	MEP(EVS) - Ready for Statutory Inspection (with EVB)	0	13-Jul-18		-151						
KD03M4	MEP(EVS) - Milestone for KD03	0		13-Jul-18	66						
Final Completion Works											
3880	EVS - Completion of Section 1 (KD06)	0		13-Jul-18	-151						
Satellite Control Points 4 / 5											
SCP4											
3824	SCP4 - Metal works / Glazing / Louver / Handrails	18	02-Mar-18 A	05-May-18 A							
3788	MEP(SCP4) - E&M 1st Fix	18	12-Mar-18 A	25-May-18	11						

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 24 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

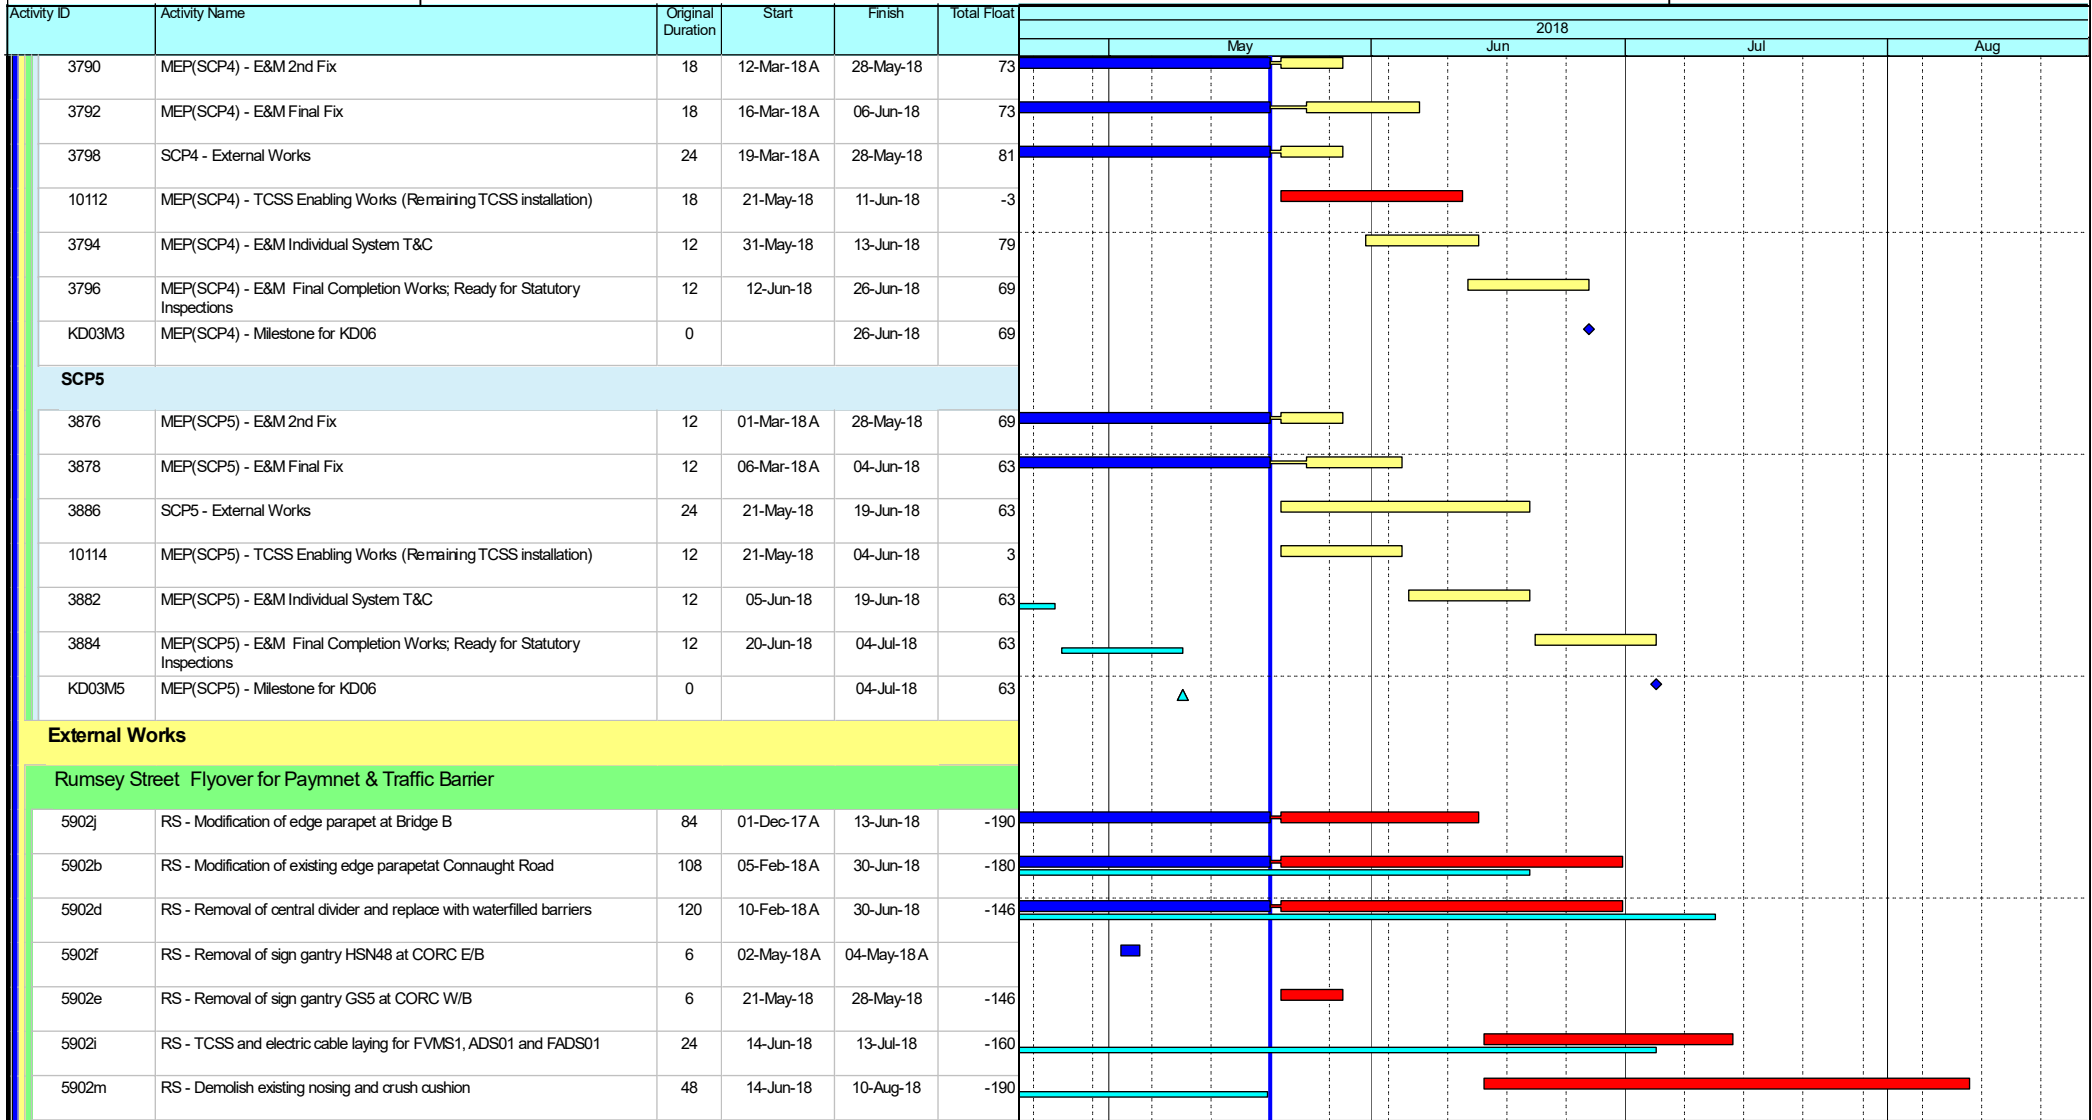

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 25 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
5902g	RS - Install new directional sign	6	20-Jun-18	26-Jun-18	-146				
5902n	RS - Paving works on Bridge B	12	29-Jun-18	13-Jul-18	-190				
5902p	RS - Pavement tie-in works at CORC W/B	36	14-Jul-18	24-Aug-18	-190				
VO/217 - TCSS and JTIS for sign face ADS16 at Hing Fat Street									
5906d	VO/217 - Ducts/drawpits at parking spaces section 1, 2 & 3	18	03-Apr-18 A	24-Apr-18 A					
5906b	VO/217 - Cross road duct	36	16-Apr-18 A	29-May-18	-177				
5906c	VO/217 - Ducts/drawpits at left side F/P section 1 & 2	6	16-Apr-18 A	21-Apr-18 A					
5906g	VO/217 - Ducts/drawpits at right side F/P	6	23-Apr-18 A	28-Apr-18 A					
5906e	VO/217 - Ducts/drawpits at exit of parking area	24	25-Apr-18 A	24-May-18	96				
5906f	VO/217 - Ducts/drawpits at north of carpark F/P	10	30-Apr-18 A	11-May-18 A					
5906h	VO/217 - Cross road ducts at J/O HIFS and TSFS left / right lane	24	12-May-18 A	09-Jun-18	-177				
Area A/B									
Area ATCSS									
10288a3	Request for VO/instruction-TCSS equipment installation & cabling (Gantries FVMS1/ADS01) (Ref: H27613-LJV-ME-LE-4022)	24	04-Oct-16 A	28-May-18	-146				
Area B									
Area B Access / Pre-SAT									
10288f	C19 allow access at Area B - Remaining area at IEC bridge East to Double Noise Enclosure	0	03-May-18 A						
10288f6	C19 allow access at Area B - Landscape Deck (From CH5150 - CH5260) - Remaining	0	14-May-18 A						
10288f8	C19 allow access at Area B - Landscape Deck (From CH5150 - CH5260) - W/B	0	16-May-18 A						
Area B TCSS									
Approach Road / Landscape Deck / Noise Enclosure (No TTA)									
10288b16	Area B TCSS cabling (Base slab / approach ramp connecting to East Portal with civil provision)	18	20-Feb-18 A	04-Jun-18	-173				
10288b40	Area B TCSS equipment installation (on IEC's Westbound) - DS06B	9	14-May-18 A	15-May-18 A					
10288b20	Area B TCSS cabling (Noise Enclosure with civil provision - No TTA)	18	21-May-18	11-Jun-18	-136				

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline
- ▲ Baseline Milestone

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
Baseline: SA01
Layout: Update Three Month Rolling
U051
Page 26 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
						Gantt Chart			
10288b36	Area B cabling along existing IECL sign gantries/bridge F3B (C19 civil provision must be ready for cabling)	12	21-May-18	04-Jun-18	-173	[Gantt bar: 21-May-18 to 04-Jun-18]			
10288b38	Area B cabling along existing IECL sign gantries/bridge F2B (C19 civil provision must be ready for cabling)	12	21-May-18	04-Jun-18	-173	[Gantt bar: 21-May-18 to 04-Jun-18]			
10288b1	Area B TCSS equipment installation and cable termination (on IEC's Westbound) - GT3, GT2, Sm CCTV at Grade	18	05-Jun-18	26-Jun-18	-173	[Gantt bar: 05-Jun-18 to 26-Jun-18]			
10288b18	Area B TCSS cabling & field equipment installation (Landscape Deck with civil provision)	10	05-Jun-18	15-Jun-18	-151	[Gantt bar: 05-Jun-18 to 15-Jun-18]			
10288b2	Area B TCSS equipment installation and cable termination (on IEC's Eastbound) - CCTV & AID	12	27-Jun-18	11-Jul-18	-173	[Gantt bar: 27-Jun-18 to 11-Jul-18]			
10288b4	Area B TCSS equipment Testing & Commissioning	25	28-Jun-18	27-Jul-18	-160	[Gantt bar: 28-Jun-18 to 27-Jul-18]			
10288b22	Area B TCSS cable termination (on IEC's Westbound) - DS06B	9	12-Jul-18	21-Jul-18	-160	[Gantt bar: 12-Jul-18 to 21-Jul-18]			
Noise Enclosure (Live Traffic, TTA) - Night Shift									
10288b6a	Area B TCSS equipment installation and cable termination (on IEC's Westbound) - DS06A	6	10-Apr-18 A	24-May-18	-192	[Gantt bar: 10-Apr-18 A to 24-May-18]			
10288b6b	Area B FADS06 sign face installation	4	29-Apr-18 A	29-Apr-18 A		[Gantt bar: 29-Apr-18 A to 29-Apr-18 A]			
10288b6	Area B TCSS equipment installation and cable termination (on IEC's Westbound) - FADS06	10	28-May-18	07-Jun-18	-203	[Gantt bar: 28-May-18 to 07-Jun-18]			
10288b8	Area B TCSS equipment Testing & Commissioning	20	04-Jun-18	27-Jun-18	-203	[Gantt bar: 04-Jun-18 to 27-Jun-18]			
10288b10	Area B TCSS equipment installation and cable termination (on IEC's Eastbound) - FADS08A	6	08-Jun-18	14-Jun-18	-199	[Gantt bar: 08-Jun-18 to 14-Jun-18]			
Existing IEC (Live Traffic, TTA) - Night Shift									
10288b24b	Area B TCSS equipment installation and cable termination (on IEC's Westbound) - ADS06	10	20-Mar-18 A	26-May-18	-177	[Gantt bar: 20-Mar-18 A to 26-May-18]			
10288b30	Area B TCSS cabling (Existing IEC with civil provision)	24	21-May-18	19-Jun-18	-202	[Gantt bar: 21-May-18 to 19-Jun-18]			
10288b24	Area B TCSS equipment installation and cable termination (on IEC's Westbound) - VMS7	14	20-Jun-18	06-Jul-18	-202	[Gantt bar: 20-Jun-18 to 06-Jul-18]			
10288b26	Area B TCSS equipment Testing & Commissioning	12	28-Jun-18	12-Jul-18	-203	[Gantt bar: 28-Jun-18 to 12-Jul-18]			
Area B Tunnel Lighting									
Landscape Deck (Bay C1 to C5)									
10295c	VO 244 - Pending for C19 dismantle scaffold and cable trough construction	24	02-May-18 A	24-May-18	-183	[Gantt bar: 02-May-18 A to 24-May-18]			
10295d	VO 244 - Concrete screen wall construction continue	6	25-May-18	31-May-18	-183	[Gantt bar: 25-May-18 to 31-May-18]			
Landscape Deck (Bay C1 & C2A-2 Remaining Bay (W/B))									
10288c24	Hanger bracket / Cable tray / U-channel support for lighting installation	20	16-May-18 A	08-Jun-18	-185	[Gantt bar: 16-May-18 A to 08-Jun-18]			

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline
- ▲ Baseline Milestone

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 27 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

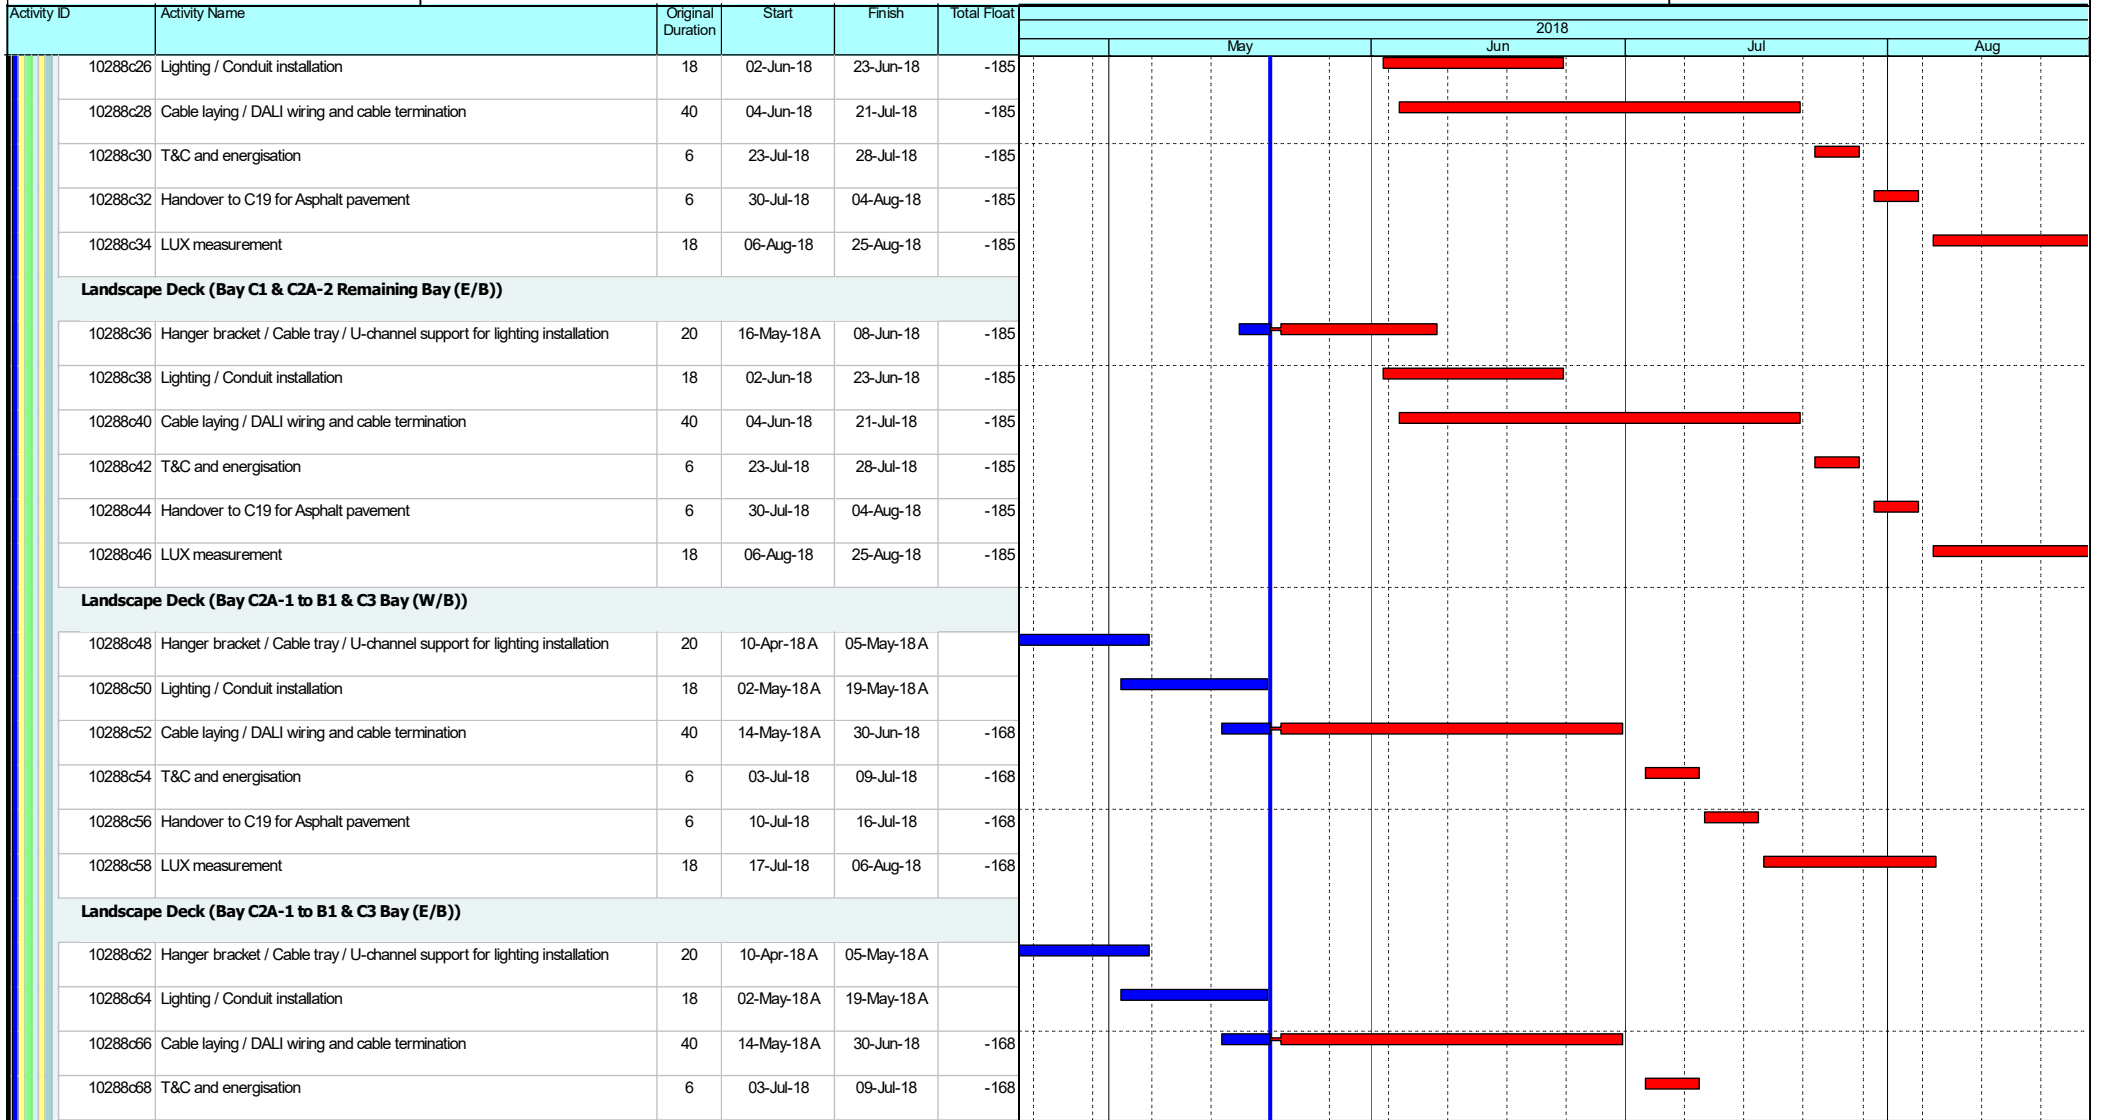

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
Baseline: SA01
Layout: Update Three Month Rolling
U051
Page 28 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						May	Jun	Jul	Aug
10288c70	Handover to C19 for Asphalt pavement	6	10-Jul-18	16-Jul-18	-168				
10288c72	LUX measurement	18	17-Jul-18	06-Aug-18	-168				
Landscape Deck (Bay C4 - E/B Slow Lane)									
10288c76	Hanger bracket / Cable tray / U-channel support for lighting installation	18	06-Jun-18	27-Jun-18	-193				
10288c88	Access date - Bay C4 - E/B Slow Lane	0	06-Jun-18*		-193				
10288c78	Lighting / Conduit installation	6	21-Jun-18	27-Jun-18	-191				
10288c78a	Handover to C19 for backfilling & paving	10	30-Jun-18	12-Jul-18	-193				
10288c80	Cable laying / DALI wiring and cable termination	28	13-Jul-18	14-Aug-18	-193				
10288c90	Lighting / Conduit installation (continue)	6	13-Jul-18	19-Jul-18	-171				
10288c82	T&C and energisation	6	15-Aug-18	21-Aug-18	-193				
10288c86	LUX measurement	18	15-Aug-18	04-Sep-18	-193				
Landscape Deck (Bay C4 - E/B Fast Lane)									
10288c92	Hanger bracket / Cable tray / U-channel support for lighting installation	22	26-Apr-18A	23-May-18	-194				
10288c10a	Access date - Bay C4 - E/B Fast Lane	0	26-Apr-18A		-194				
10288c94	Lighting / Conduit installation	11	17-May-18A	30-May-18	-194				
10288c78a	Handover to C19 for remaining works at Bay C4 & C5	34	31-May-18	11-Jul-18	-194				
10288c96	Cable laying / DALI wiring and cable termination	30	12-Jul-18	15-Aug-18	-194				
10288c10c	Lighting / Conduit installation (continue)	6	12-Jul-18	18-Jul-18	-170				
10288c98	T&C and energisation	6	16-Aug-18	22-Aug-18	-194				
10288c10f	LUX measurement	18	16-Aug-18	05-Sep-18	-194				
Landscape Deck (Bay C4 - W/B)									
10288c10e	Hanger bracket / Cable tray / U-channel support for lighting installation	22	26-Apr-18A	23-May-18	-194				
10288c11e	Access date - Bay C4 - W/B	0	26-Apr-18A		-194				
10288c10g	Lighting / Conduit installation	11	17-May-18A	30-May-18	-194				

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline
- ▲ Baseline Milestone

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 29 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

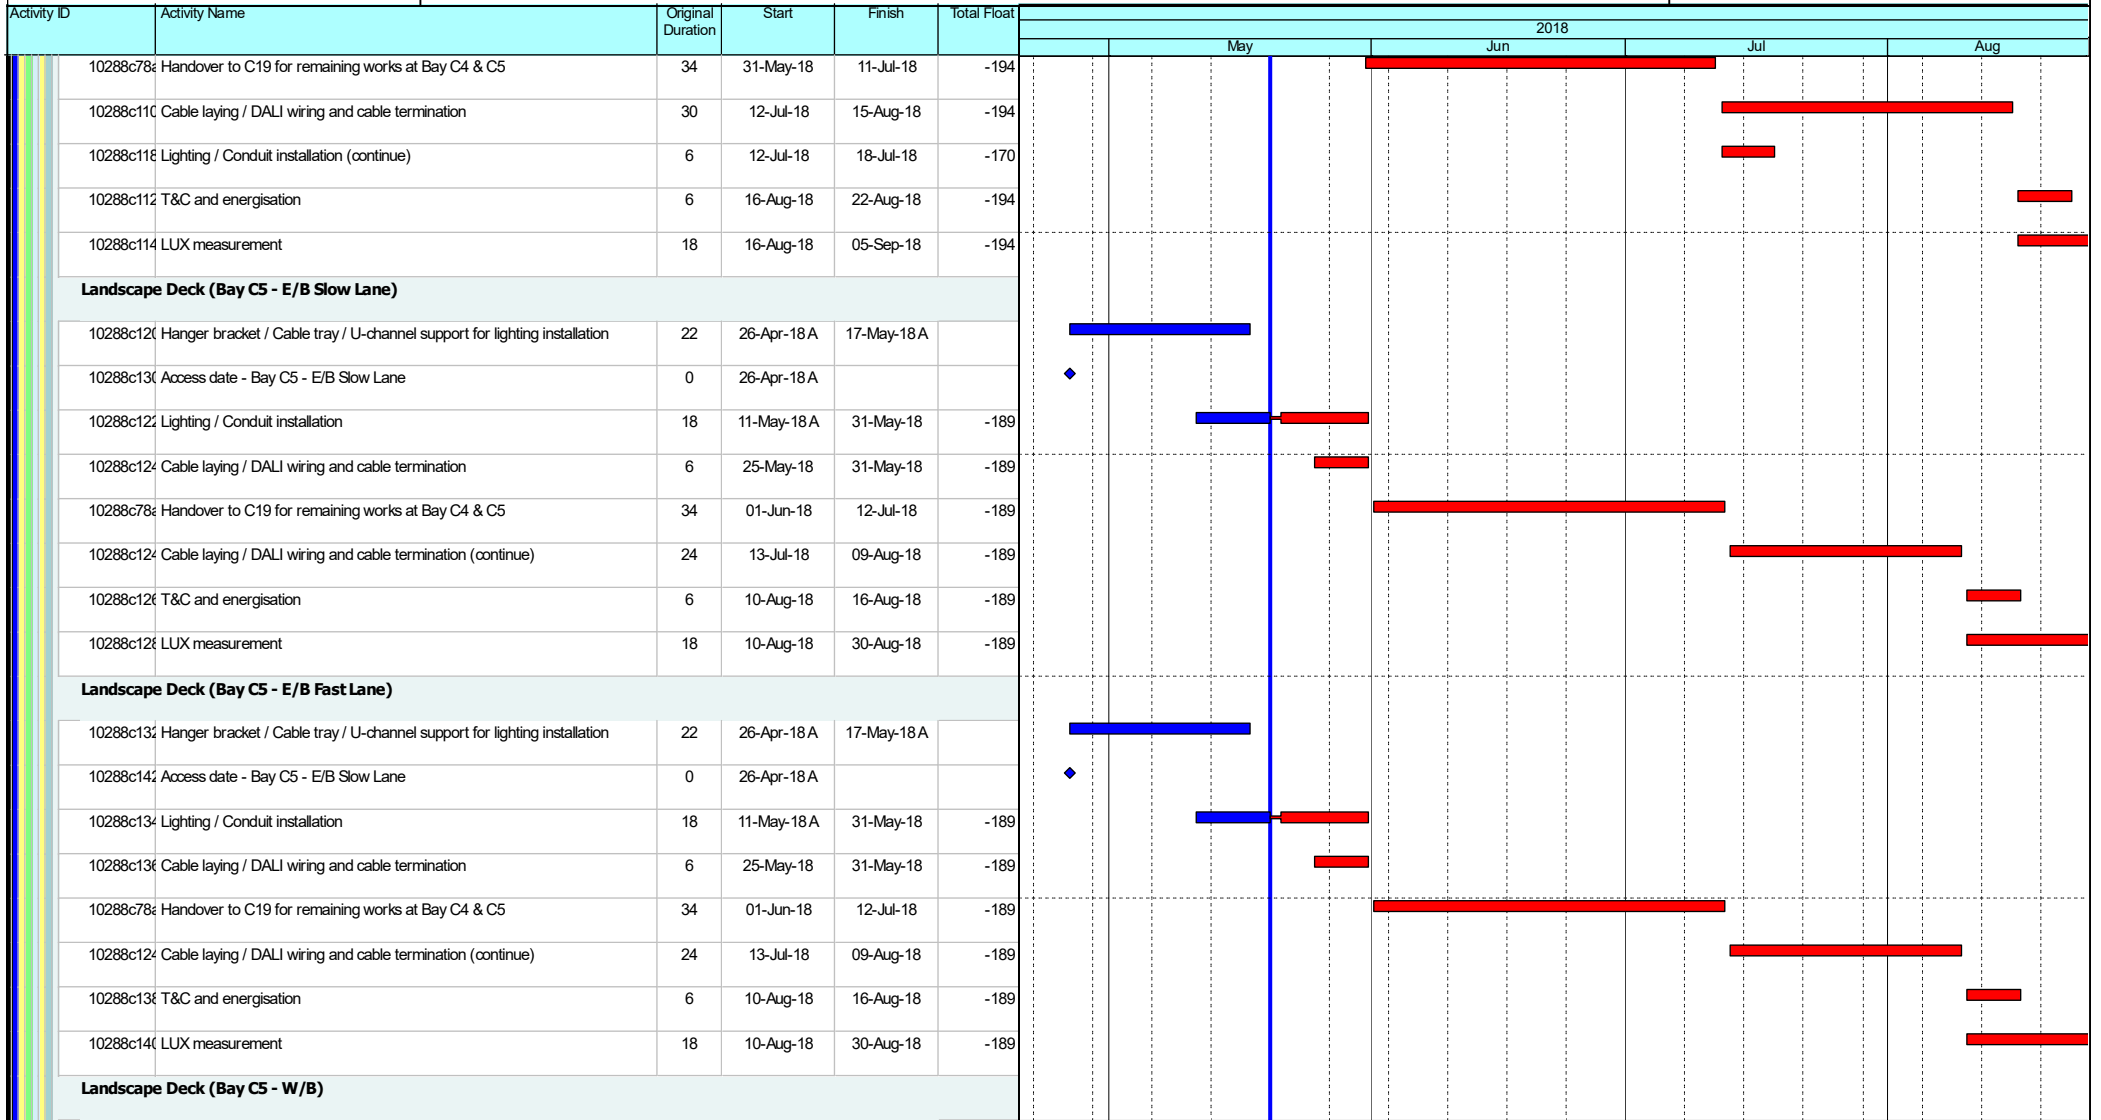

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING


Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 30 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

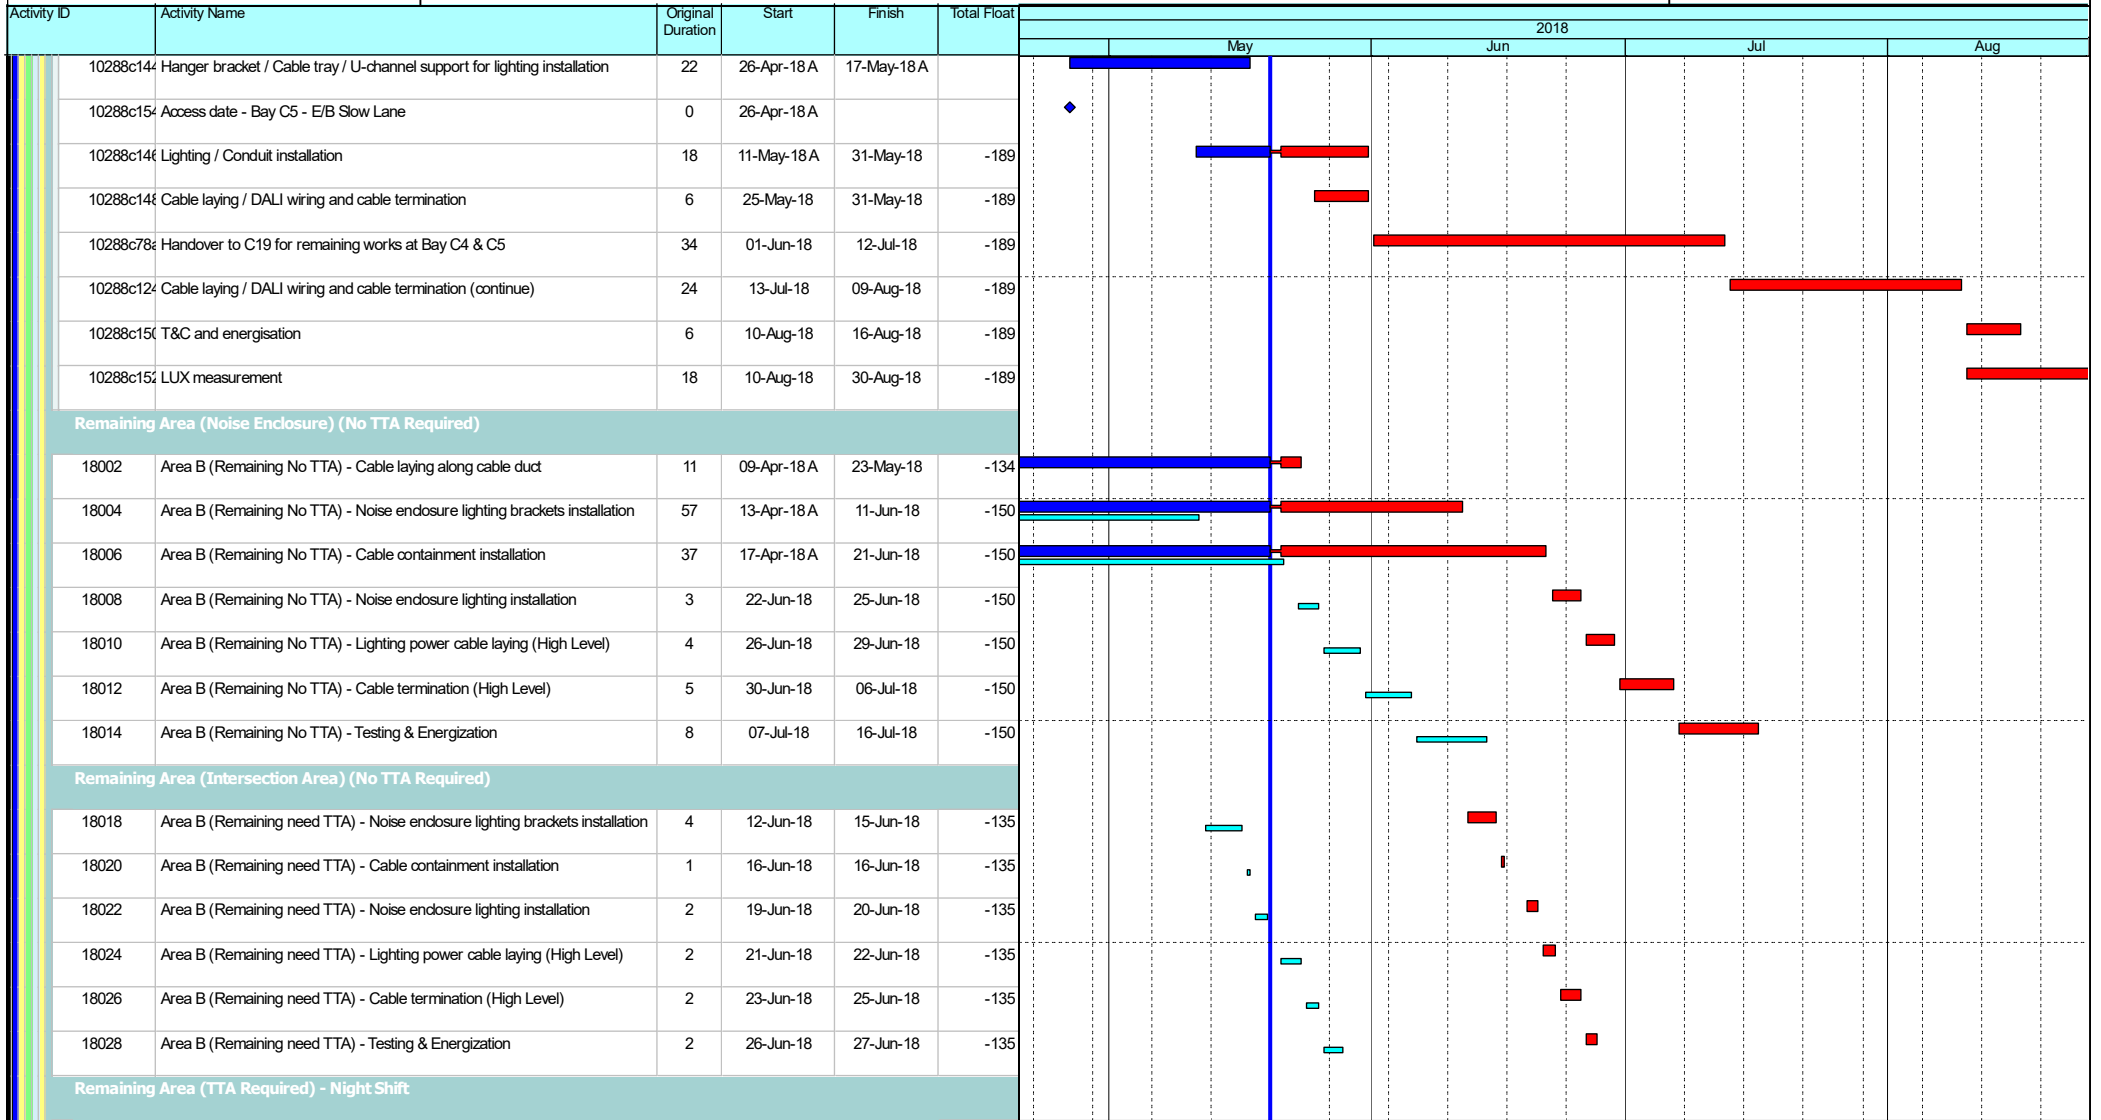

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING



Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 31 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

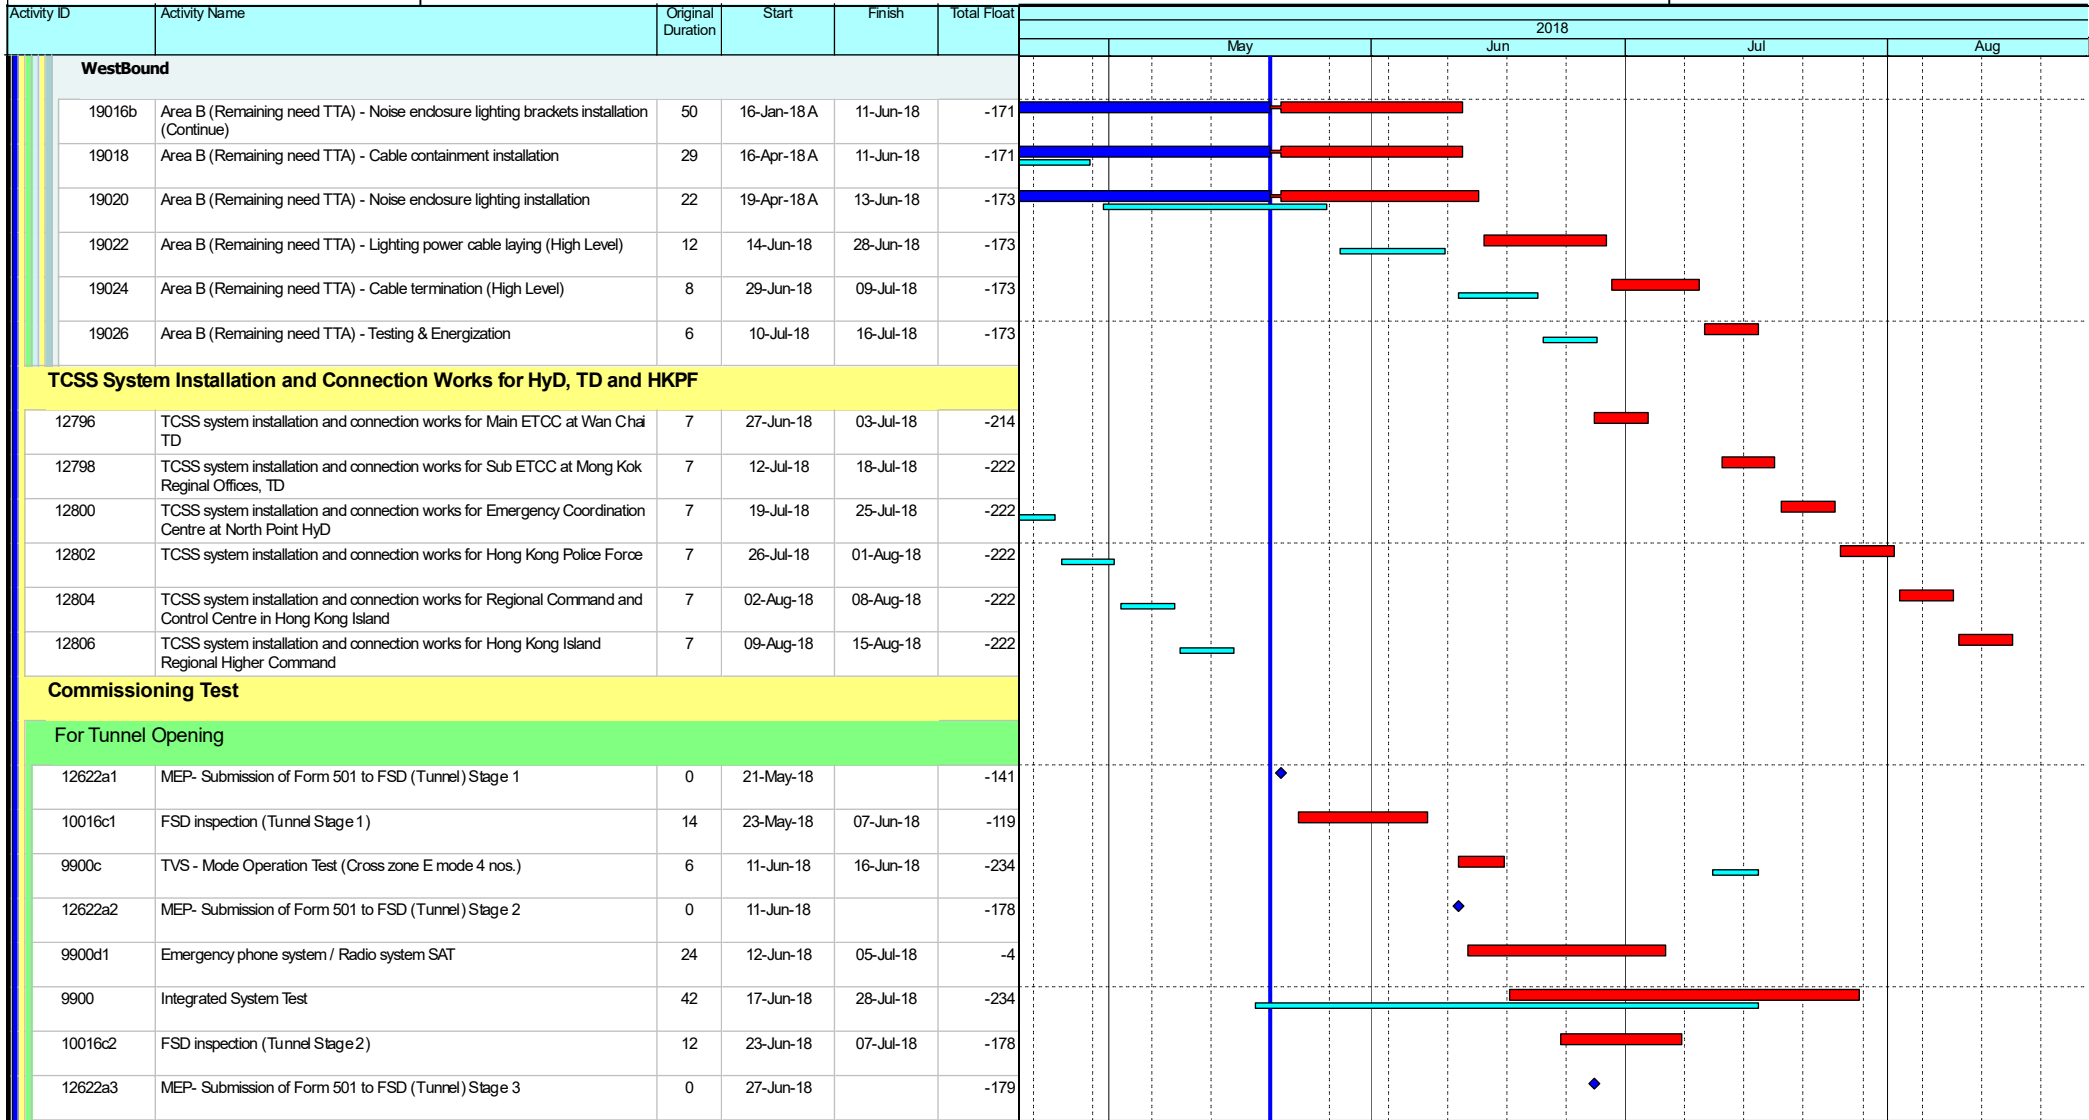

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
Baseline: SA01
Layout: Update Three Month Rolling
U051
Page 32 of 34

Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-May-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018											
						May			Jun			Jul			Aug		
Training Plan for CWB Opening																	
10206	Training Plan for CWB opening - Draft submission	18	12-Sep-17 A	28-May-18	-69												
10206a	Training Plan for CWB opening - Draft approval	18	29-May-18	19-Jun-18	-61												
10208	Training Plan for CWB opening - Final submission	18	20-Jun-18	11-Jul-18	-61												
10208a	Training Plan for CWB opening - Final approval	18	12-Jul-18	01-Aug-18	-61												
Training Material for CWB Opening																	
10210	Training Material for CWB opening - Draft submission	18	15-Nov-17 A	28-May-18	-69												
10210a	Training Material for CWB opening - Draft approval	18	29-May-18	19-Jun-18	-69												
10212	Training Material for CWB opening - Final submission	18	20-Jun-18	11-Jul-18	-69												
10212a	Training Material for CWB opening - Final approval	18	12-Jul-18	01-Aug-18	-61												
Maintenance Manual / Plan																	
10200	Maintenance Plan	18	12-Jul-18	01-Aug-18	-69												
10220	Maintenance Manual / logbook - Draft submission	18	02-Aug-18	22-Aug-18	-69												

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 51 (May 2018) THREE MONTH ROLLING

Project ID: H2613-U051
 Baseline: SA01
 Layout: Update Three Month Rolling
 U051
 Page 34 of 34


Date	Revision	Checked	Approv...
20-Apr-18	U050	AT	CW
20-May-18	U051	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Aug	Sep	Oct	Nov
PO-VII_a1	Possession of Portion VII (Day 762) - CH3911-4250 (below -6.0mPD)	659	30-Dec-15 A	17-Sep-18	-263				
PO-Vc	Possession of Portion V (Day 607) - CH3210-3250	658	15-Jan-16 A	17-Sep-18	-241				
PO-VIb_b1	Possession of Portion VIb (Day 761) - CH3428-3625 (E/B)	619	18-Feb-16 A	17-Sep-18	-263				
PO-VIb_b2	Possession of Portion VIb (Day 761) - CH3428-3625 (W/B)	568	29-Feb-16 A	17-Sep-18	-226				
PO-Xa_1	Possession of Portion Xa (Day 650) - ADB Southern Portion (AECOM letter ref: 2015007890T)	589	07-Mar-16 A	17-Sep-18	-433				
PO-Xb_1	Possession of Portion Xb (Day 804) - ADB Northern Portion	589	07-Mar-16 A	17-Sep-18	-433				
PO-Vb1	Possession of Portion V (Day 607) - SR3	587	11-Mar-16 A	17-Sep-18	-1				
PO-Ia	Possession of Portion Ia (Day 789) - SCB / SCP1 / SCP2 / Rumsey Street Flyover	600	28-Mar-16 A	17-Sep-18	-416				
PO-VII_a2	Possession of Portion VII (Day 762) - CH3800-3911 (below -6.0mPD)	567	31-Mar-16 A	17-Sep-18	-263				
PO-IXc_1	Possession of Portion IXc (Day 712) - EVB above 3.6mPD - Relinquished on 12 Apr 2016	445	29-Jul-16 A	17-Sep-18	-409				
PO-IXb_1	Possession of Portion IXb (Day 712) - EVB (below +3.6mPD to tunnel top slab) - Relinquished on 12 Apr 2016	445	05-Aug-16 A	17-Sep-18	-409				
PO-VIa_a	Possession of Portion VIa (Day 823) - CH3250-3283	425	15-Aug-16 A	17-Sep-18	-226				
PO-Vb2_a	Possession of Portion V (Day 607) - SR2	456	15-Aug-16 A	17-Sep-18	-266				
PO-VIc_a	Possession of Portion VIc (Day 761) - CH3770-3800 (Access Shaft Opening)	391	23-Sep-16 A	17-Sep-18	-263				
PO-VIb_c	Possession of Portion VIb (Day 761) - CH3625-3770	391	23-Sep-16 A	17-Sep-18	-263				
PO-IVa1	Possession of Portion IVa (Day 930) - CH2600-2720	323	30-Nov-16 A	17-Sep-18	-249				
PO-IVb2	Possession of Portion IVb (Day 930) - MVB (GLD-H)	233	28-Feb-17 A	17-Sep-18	-457				
PO-VIIIa_a	Possession of Portion VIIIa (Day 929) - CH4530-4591 W/B	233	28-Feb-17 A	17-Sep-18	-267				
PO-VIIIa	Possession of Portion VIIIa (Day 929) - CH4250-4600 (Remaining)	241	12-Mar-17 A	17-Sep-18	-267				
PO-VIIIb	Possession of Portion VIIIb (Day 929) - SR8 (CH700-350)	233	12-Mar-17 A	17-Sep-18	-249				
PO-VIIIc	Possession of Portion VIIIc (Day 1039) - SR8 (CH350-310) / SCP4	233	12-Mar-17 A	17-Sep-18	-236				
PO-IVa2_a	Possession of Portion IVa (Day 930) - CH2720-2950	241	12-Mar-17 A	17-Sep-18	-249				
PO-IVb1	Possession of Portion IVb (Day 930) - MVB (GLA-C)	239	14-Mar-17 A	17-Sep-18	-457				
PO-IVa2_b	Possession of Portion IVa (Day 930) - SR1	203	30-Mar-17 A	17-Sep-18	-249				



Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 2 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Aug	Sep	Oct	Nov
PO-Vb2_b	Possession of Portion V (Day 607) - SCP3	182	03-Jul-17 A	17-Sep-18	-266				
PO-Vlb_a	Possession of Portion Vlb (Day 761) - CH3400-3428	80	31-Jul-17 A	17-Sep-18	-226				
PO-Vla_b	Possession of Portion Vla (Day 823) - CH3283-3400	80	31-Jul-17 A	17-Sep-18	-249				
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-Aug-18	08-Dec-18	-268				
Submissions and Approvals									
Initial General Submission									
10168	Submission of CMC 3DVR	30	20-Aug-18	18-Sep-18	-2				
DETAILED DESIGN OF WORKS									
Permanent Works Design and Engineering									
Green Wall on ADB									
10238	ADB Green Wall - Engineer review & Approval; Consent to Proceed Construction	24	07-Mar-16 A	25-Aug-18	-376				
Landscaping & Associated Irrigation System									
10268	Landscaping - Engineer review & Approval; Consent to Proceed Construction	24	07-Mar-16 A	01-Sep-18	-357				
PROCUREMENT, MANUFACTURING & DELIVERIES									
Procurement; Manufacturing; Deliveries									
Landscaping and Associated Irrigation System									
Shop Drawings									
10272	Landscaping - Shop Drawings submission to the Engineer	30	06-Oct-17 A	31-Aug-18	-469				
12848	Landscaping - Shop Drawings review by the Engineer	30	01-Sep-18	30-Sep-18	-469				
10274	Landscaping - Obtain Approval for Shop Drawings	0		30-Sep-18	-469				
Procurement & Fabrication									
10276	Landscaping - Confirm design of embed items	0	01-Oct-18		-469				
10278	Landscaping - Embed fabrication & delivery	12	01-Oct-18	12-Oct-18	-469				
10280	Landscaping - Commence embed installation	0	13-Oct-18		-469				

- Current Milestone
- Level of Effort
- Project Baseline
- Actual Work
- Critical Remaining Work
- Remaining Work
- Baseline Milestone

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 3 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

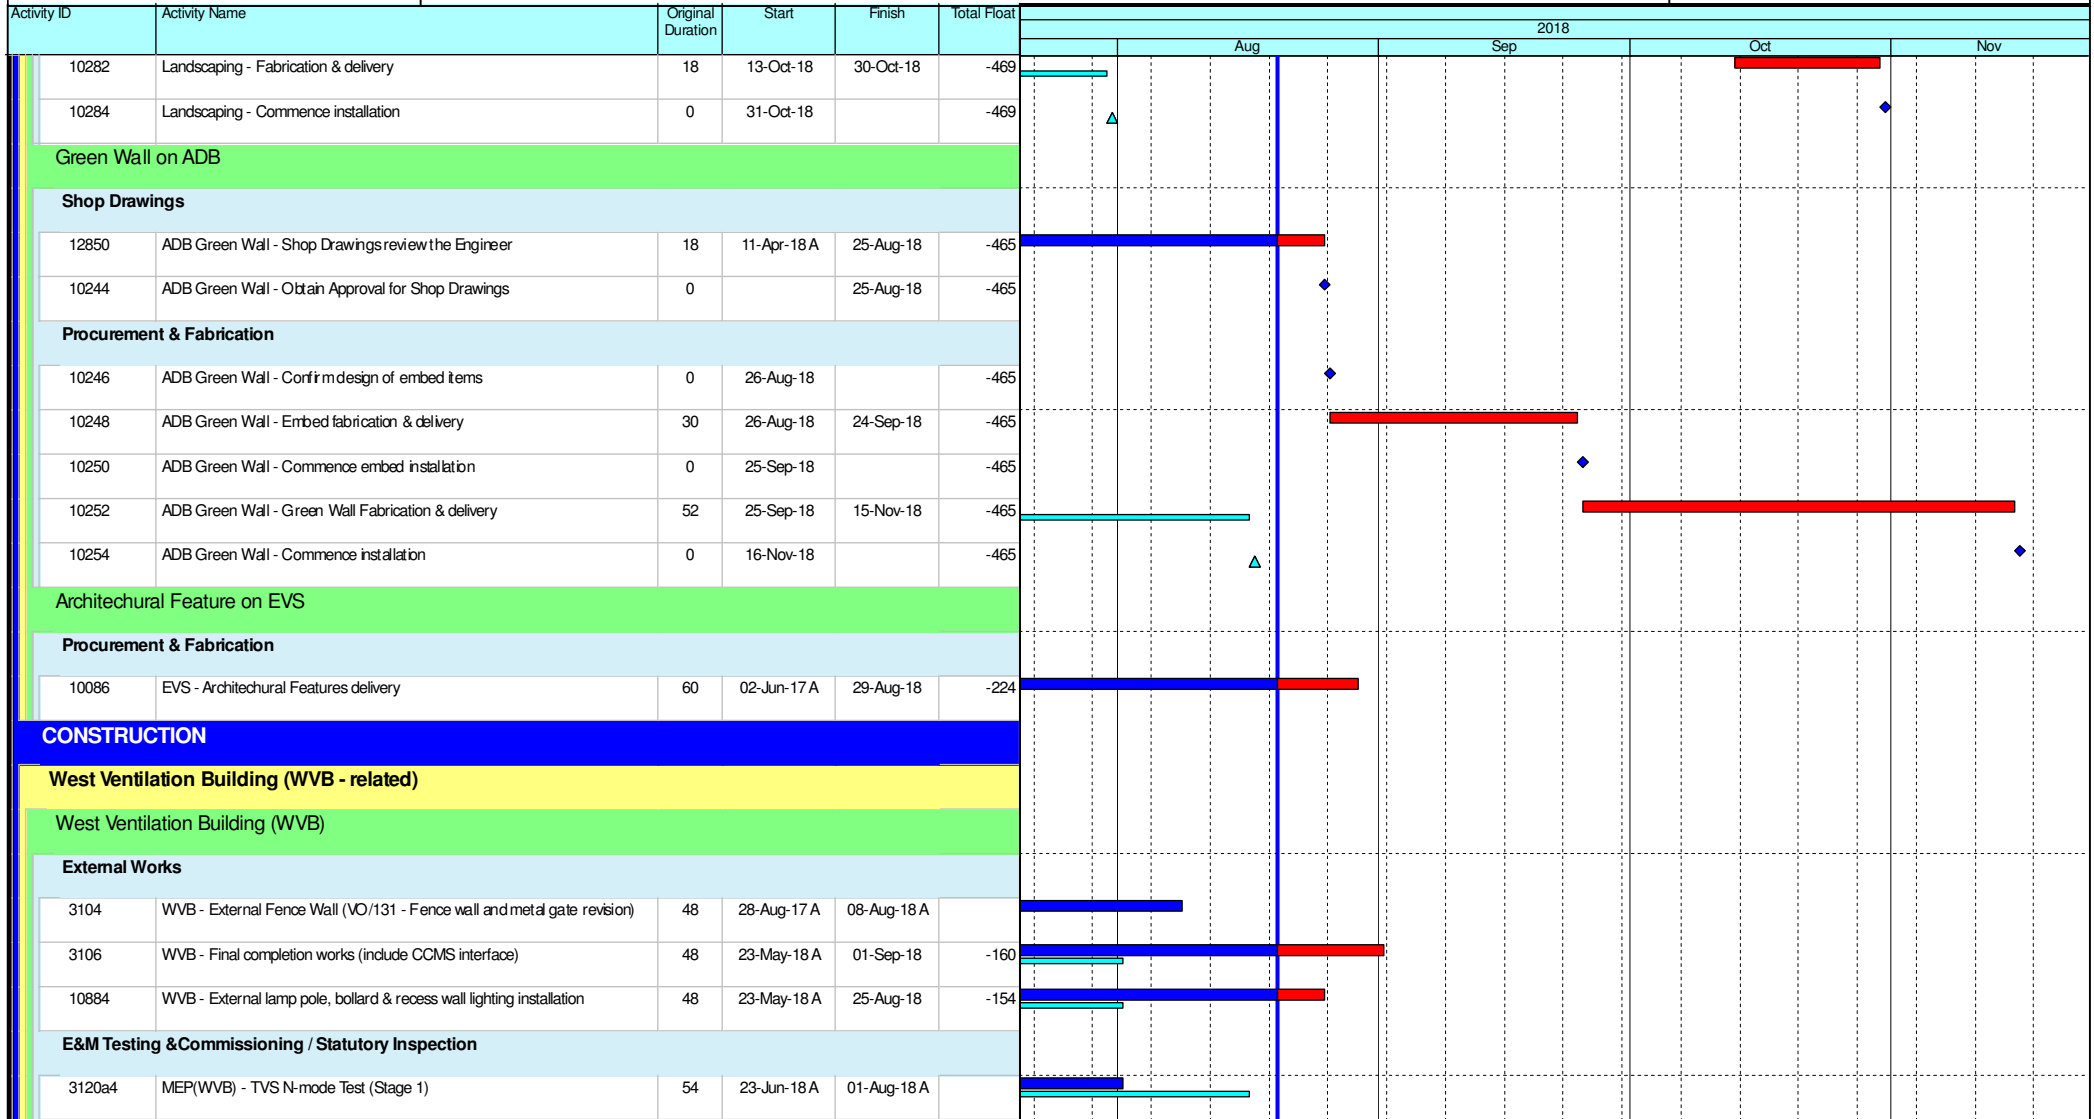

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 4 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

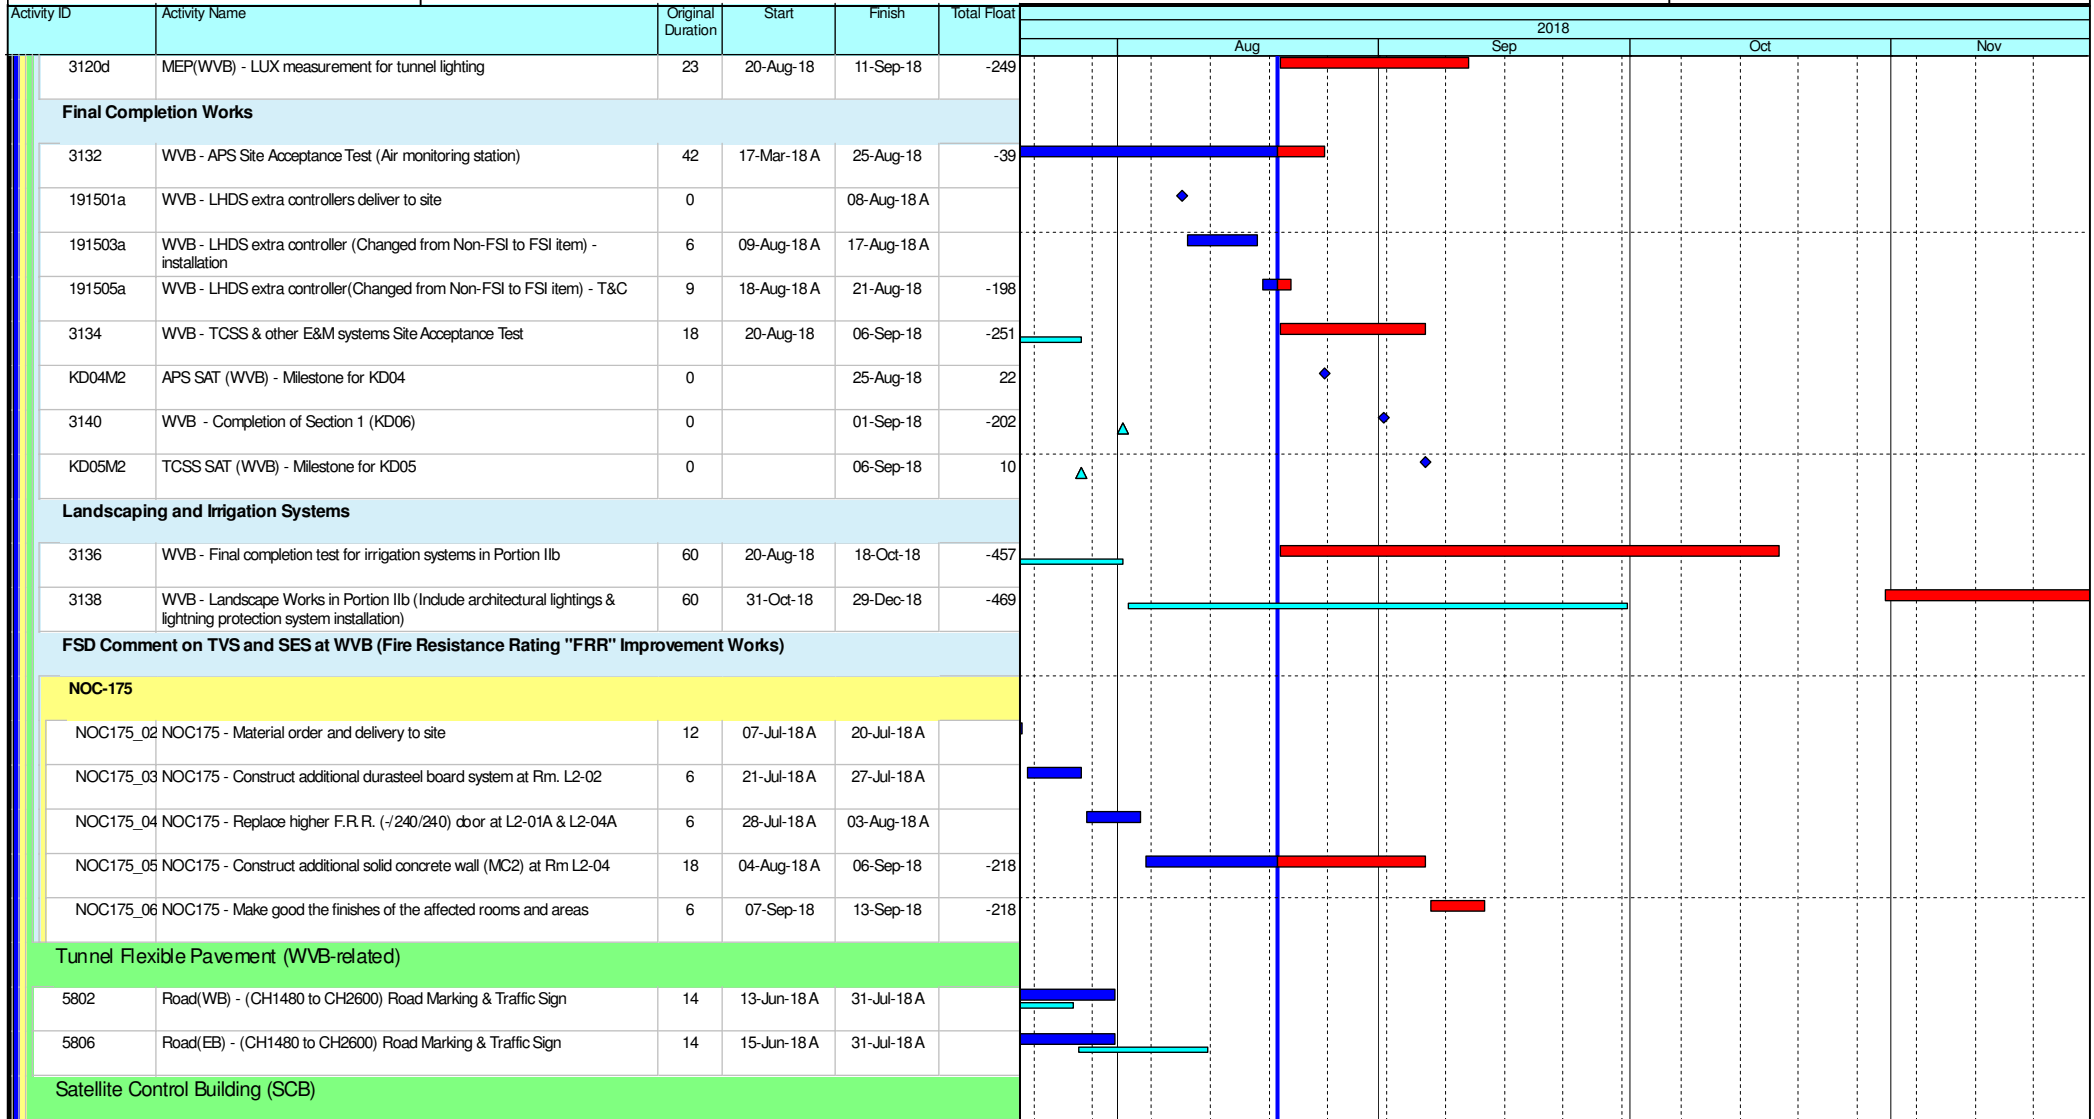

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 5 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018				
						Aug	Sep	Oct	Nov	
Final Completion Works										
3958	SCB - TCSS & other E&M systems Site Acceptance Test	90	10-May-18 A	25-Jul-18 A						
3962	SCB - Completion of Section 1	0		25-Jul-18 A						
KD05M6	TCSS SAT (SCB) - Milestone for KD05	0		25-Jul-18 A						
Satellite Control Points 1 / 2										
SCP1										
3720	MEP (SCP1) - E&M Final Completion Works	12	11-Jul-18 A	26-Jul-18 A						
KD01M2	MEP (SCP1) - Milestone for KD06	0		26-Jul-18 A						
SCP2										
3742	MEP (SCP2) - E&M Individual System T&C	12	10-Jul-18 A	26-Jul-18 A						
3744	MEP (SCP2) - E&M Final Completion Works	12	10-Jul-18 A	26-Jul-18 A						
KD01M3	MEP (SCP2) - Milestone for KD06	0		26-Jul-18 A						
Middle Ventilation Building (MVB - related)										
Tunnel Section (MVB-related)										
Portion IVa (CH2600 to CH2950)										
Slip Road 1										
10024	MEP(SR1) - (CH171 to CH271) TCSS Field equip & cable installation	6	24-May-18 A	27-Aug-18	2					
10046	MEP(SR1) - (CH171 to CH271) VE Panel installation (Upper part) (1200m2)	13	28-Jun-18 A	22-Aug-18	-182					
10046d	VO 238 - SR1 - Installation of granite stone panels / precast concrete panels	40	09-Jul-18 A	28-Jul-18 A						
10046c	VO 238 - SR1 - Construction of D-wall plinth and install wall brackets	12	10-Jul-18 A	23-Aug-18	-213					
10024a	MEP(SR1) - (CH171 to CH271) Access	0	20-Aug-18*		3					
10046e	VO 238 - SR1 - Application of Evonik Protectosil SC60	6	21-Sep-18	28-Sep-18	-213					
Portion Va [CH2950 to CH3210]										
Westbound (Outer Lane)										

- Current Milestone
- Remaining Work
- Level of Effort
- Project Baseline
- Baseline Milestone
- Actual Work
- Critical Remaining Work

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 6 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Aug	Sep	Oct	Nov
9954a	MEP(WB) - (CH2950 to CH3210) VE Panel installation (Upper part) (1800m2)	20	11-Apr-18 A	25-Aug-18	-185				
Eastbound (Outer Lane)									
9956a	MEP(EB) - (CH2950 to CH3210) VE Panel installation (Upper part) (1800m2)	20	09-Apr-18 A	25-Aug-18	-185				
Portion Vb1 (SR3)									
Slip Road 3									
10032b	MEP(SR3) - (CH3089 to CH3334) E&M 1st Fix	13	15-Mar-17 A	23-Aug-18	-183				
10036b	MEP(SR3) - (CH3089 to CH3334) TCSS Field equip & cable installation	8	15-Mar-17 A	23-Aug-18	-183				
10034b	MEP(SR3) - (CH3089 to CH3334) E&M 2nd Fix (include Sump C)	27	11-Apr-18 A	25-Aug-18	-185				
10038b	MEP(SR3) - (CH3089 to CH3334) E&M Final Fix	8	16-Apr-18 A	27-Aug-18	-186				
10048c2	MEP(SR3) - Road lighting installation (Portal)	18	12-Jun-18 A	01-Sep-18	-191				
10048b	MEP(SR3) - (CH3089 to CH3334) VE Panel installation (Upper part) (2940m2)	33	04-Jul-18 A	27-Aug-18	-186				
10048g	VO 238 - Installation of granite stone	5	11-Jul-18 A	30-Jul-18 A					
10048h	VO 238 - Installation of precast concrete	22	24-Jul-18 A	11-Sep-18	-206				
10048i	VO 238 - Application of Evonik Protectosil SC60 at SR3	7	12-Sep-18	19-Sep-18	-206				
Portion Vb2 (SR2 / SCP3)									
Slip Road 2									
10050b	MEP(SR2) - (CH3114 to CH3257) E&M 1st Fix	8	08-Mar-17 A	21-Aug-18	-181				
10056b	MEP(SR2) - (CH3114 to CH3257) TCSS Field equip & cable installation	5	16-Mar-17 A	23-Aug-18	-183				
10052b	MEP(SR2) - (CH3114 to CH3257) E&M 2nd Fix (include Sump F)	40	15-Jun-17 A	25-Aug-18	-185				
10054b	MEP(SR2) - (CH3114 to CH3257) E&M Final Fix	5	08-May-18 A	25-Aug-18	-185				
10064b2	MEP(SR2) - Road lighting installation (Portal)	18	12-Jun-18 A	01-Sep-18	-191				
10064b	MEP(SR2) - (CH3114 to CH3257) VE Panel installation (Upper part) (1716m2)	18	09-Jul-18 A	25-Aug-18	-185				
Portion Vc [CH3210 to CH3250]									
Westbound (Outer Lane)									

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 7 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Aug	Sep	Oct	Nov
9954c	MEP(WB) - (CH3210 to CH3250) VE Panel installation (Upper part) (1800m2)	20	10-Jul-18 A	30-Aug-18	-189				
Eastbound (Outer Lane)									
9956c	MEP(EB) - (CH3210 to CH3250) VE Panel installation (Upper part) (1800m2)	20	06-Jul-18 A	25-Aug-18	-185				
Portion VIa [CH3250 to CH3283]									
Westbound									
9958a	MEP(WB) - (CH3250 to CH3283) VE Panel installation (Upper part) (528m2)	6	19-Apr-18 A	21-Aug-18	-181				
Eastbound									
9960a	MEP(EB) - (CH3250 to CH3283) VE Panel installation (Upper part) (528m2)	6	18-Apr-18 A	21-Aug-18	-181				
Portion VIa [CH3283 to CH3400]									
Westbound									
9958b	MEP(WB) - (CH3283 to CH3400) VE Panel installation (Upper part) (1872m2)	21	10-Apr-18 A	25-Aug-18	-185				
Eastbound									
9960b	MEP(EB) - (CH3283 to CH3400) VE Panel installation (Upper part) (1872m2)	21	16-Apr-18 A	25-Aug-18	-185				
Middle Ventilation Building (MVB)									
External Facade									
3238	MVB - External facing tiles / Louvre	90	06-Nov-17 A	14-Aug-18 A					
MEP Works									
3236	MVB - Metal works / steel platform / Ladders / Handrails	48	06-Dec-17 A	10-Aug-18 A					
3248	MEP(MVB) - TCSS Enabling Works (Remaining TCSS installation)	24	03-Jan-18 A	23-Jul-18 A					
3252	MEP(MVB) - E&M Final Completion Works; Ready for Statutory Inspections	24	31-May-18 A	16-Aug-18 A					
3280a10	Rectification works for lift shaft structure by lift contractor / WDII / C3	6	03-Aug-18 A	09-Aug-18 A					
E&M Individual System T&C									
3250c	MEP(MVB) - Lift functional test	12	06-Jul-18 A	09-Aug-18 A					
Basement 2 (GL D - H)									

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 8 of 27








Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018				
						Aug	Sep	Oct	Nov	
Basement 2 - Other Rooms / General Area & Corridor										
19034	MEP(MVB) - E&M final fixing	18	12-Feb-18 A	25-Jul-18 A						
Basement 2M (GL D - H)										
Basement 2M - Other Rooms / General Area & Corridor										
19051	MEP(MVB) - E&M final fixing	18	07-Mar-18 A	03-Aug-18 A						
Basement 1 (GL D - H)										
Other Rooms / General Area & Corridor										
11318	MEP(MVB) - E&M final fixing	24	20-Feb-18 A	15-Aug-18 A						
Basement 1 (GL A - D)										
MCC Room 1 (B1-04)										
11286	MEP(MVB) - E&M final fixing	24	25-Nov-17 A	14-Aug-18 A						
G/F (GL D - H)										
TVF Fan Room 2 (G-02)										
11404	MEP(MVB) - E&M final fixing	24	03-Mar-18 A	25-Jul-18 A						
Other Rooms / General Area & Corridor										
11412	MEP(MVB) - E&M final fixing	24	21-Feb-18 A	07-Aug-18 A						
G/F (GL A - D)										
Fire Control Centre (G-11)										
11380	MEP(MVB) - E&M final fixing	12	02-Mar-18 A	26-Jul-18 A						
Other Rooms / General Area & Corridor										
11388	MEP(MVB) - E&M final fixing	24	02-Mar-18 A	02-Aug-18 A						
1/F (GL D - H)										
Other Rooms / General Area & Corridor										
11446	MEP(MVB) - E&M final fixing	18	21-Feb-18 A	16-Aug-18 A						

-  Current Milestone
-  Level of Effort
-  Baseline Milestone
-  Actual Work
-  Critical Remaining Work
-  Remaining Work
-  Project Baseline

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 9 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018				
						Aug	Sep	Oct	Nov	
1/F (GLA - D)										
FS Water Tank & Pump Room (L1-05)										
11420	MEP(MVB) - E&M final fixing	12	15-Mar-18 A	24-Jul-18 A						
Other Rooms / General Area & Corridor										
11438	MEP(MVB) - E&M final fixing	18	15-Feb-18 A	09-Aug-18 A						
Smoke Extraction System (B3/F - G/F)										
B3/F - G/F										
191485	SES(MVB) - Termination	6	16-Jun-18 A	23-Jul-18 A						
191487	SES(MVB) - Testing & Commissioning	12	24-Jul-18 A	07-Aug-18 A						
External Works										
3258	MVB - External concrete pavement	42	04-Apr-18 A	30-Aug-18	-158					
3262	MVB - Final completion works (include CCMS interface)	30	05-Apr-18 A	30-Aug-18	-158					
3260	MVB - External Fence Wall	42	10-Apr-18 A	30-Aug-18	-158					
E&M Testing & Commissioning / Statutory Inspection										
3264	MEP(MVB) - E&M System Integrated Testing and Commissioning	24	23-Jul-18 A	31-Aug-18	-261					
3264a	MEP(MVB) - TVS & CCMS System Integrated Testing and Commissioning	24	23-Jul-18 A	31-Aug-18	-261					
3264b	MEP(MVB) - Tunnel Lighting & CCMS System Integrated Testing and Commissioning	24	23-Jul-18 A	31-Aug-18	-261					
3264c	MEP(MVB) - Fire Services & CCMS System Integrated Testing and Commissioning	24	23-Jul-18 A	31-Aug-18	-261					
3264a4	MEP(MVB) - TVS N-mode Test (Stage 2)	54	10-Aug-18 A	31-Aug-18	-238					
12606	MEP(MVB) - Submission of Form 5 to EMSD	0	15-Aug-18 A							
3266	MEP(MVB) - Ready for Statutory Inspection	0	17-Aug-18 A							
12622b	MEP(MVB) - Submission of Form 501 to FSD (include SES / SPS) (Building)	0	17-Aug-18 A							
12650	MEP(MVB) - Submission of Form 314 to FSD	0	17-Aug-18 A							
KD02M1	MEP(MVB) - Milestone for KD02	0		17-Aug-18 A						

- ◆ Current Milestone
- ▬ Level of Effort
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline
- ▲ Baseline Milestone

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING


Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 10 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

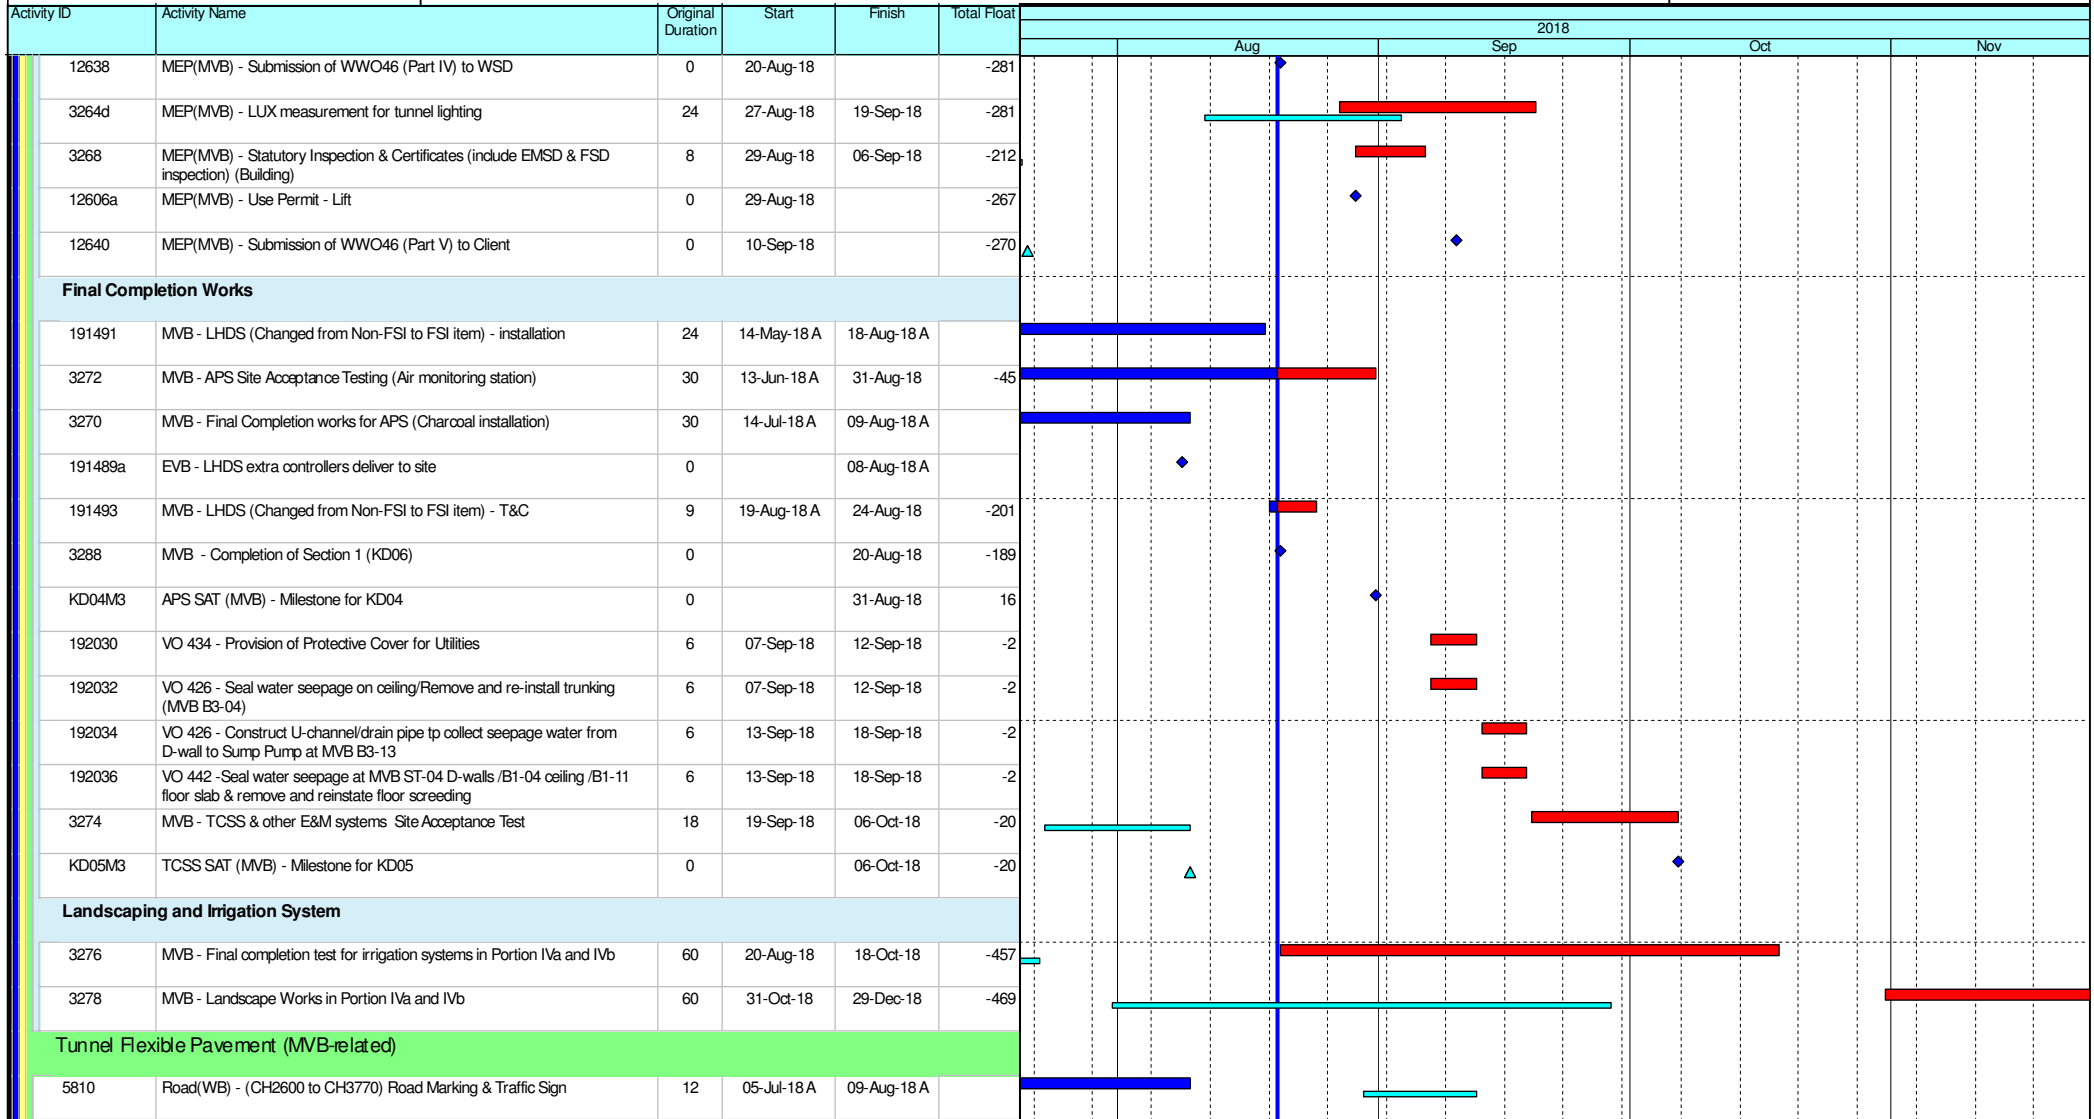

- ◆ Current Milestone
- Level of Effort
- ▲ Baseline Milestone
- ▬ Actual Work
- ▬ Critical Remaining Work
- ▬ Remaining Work
- ▬ Project Baseline

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 11 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

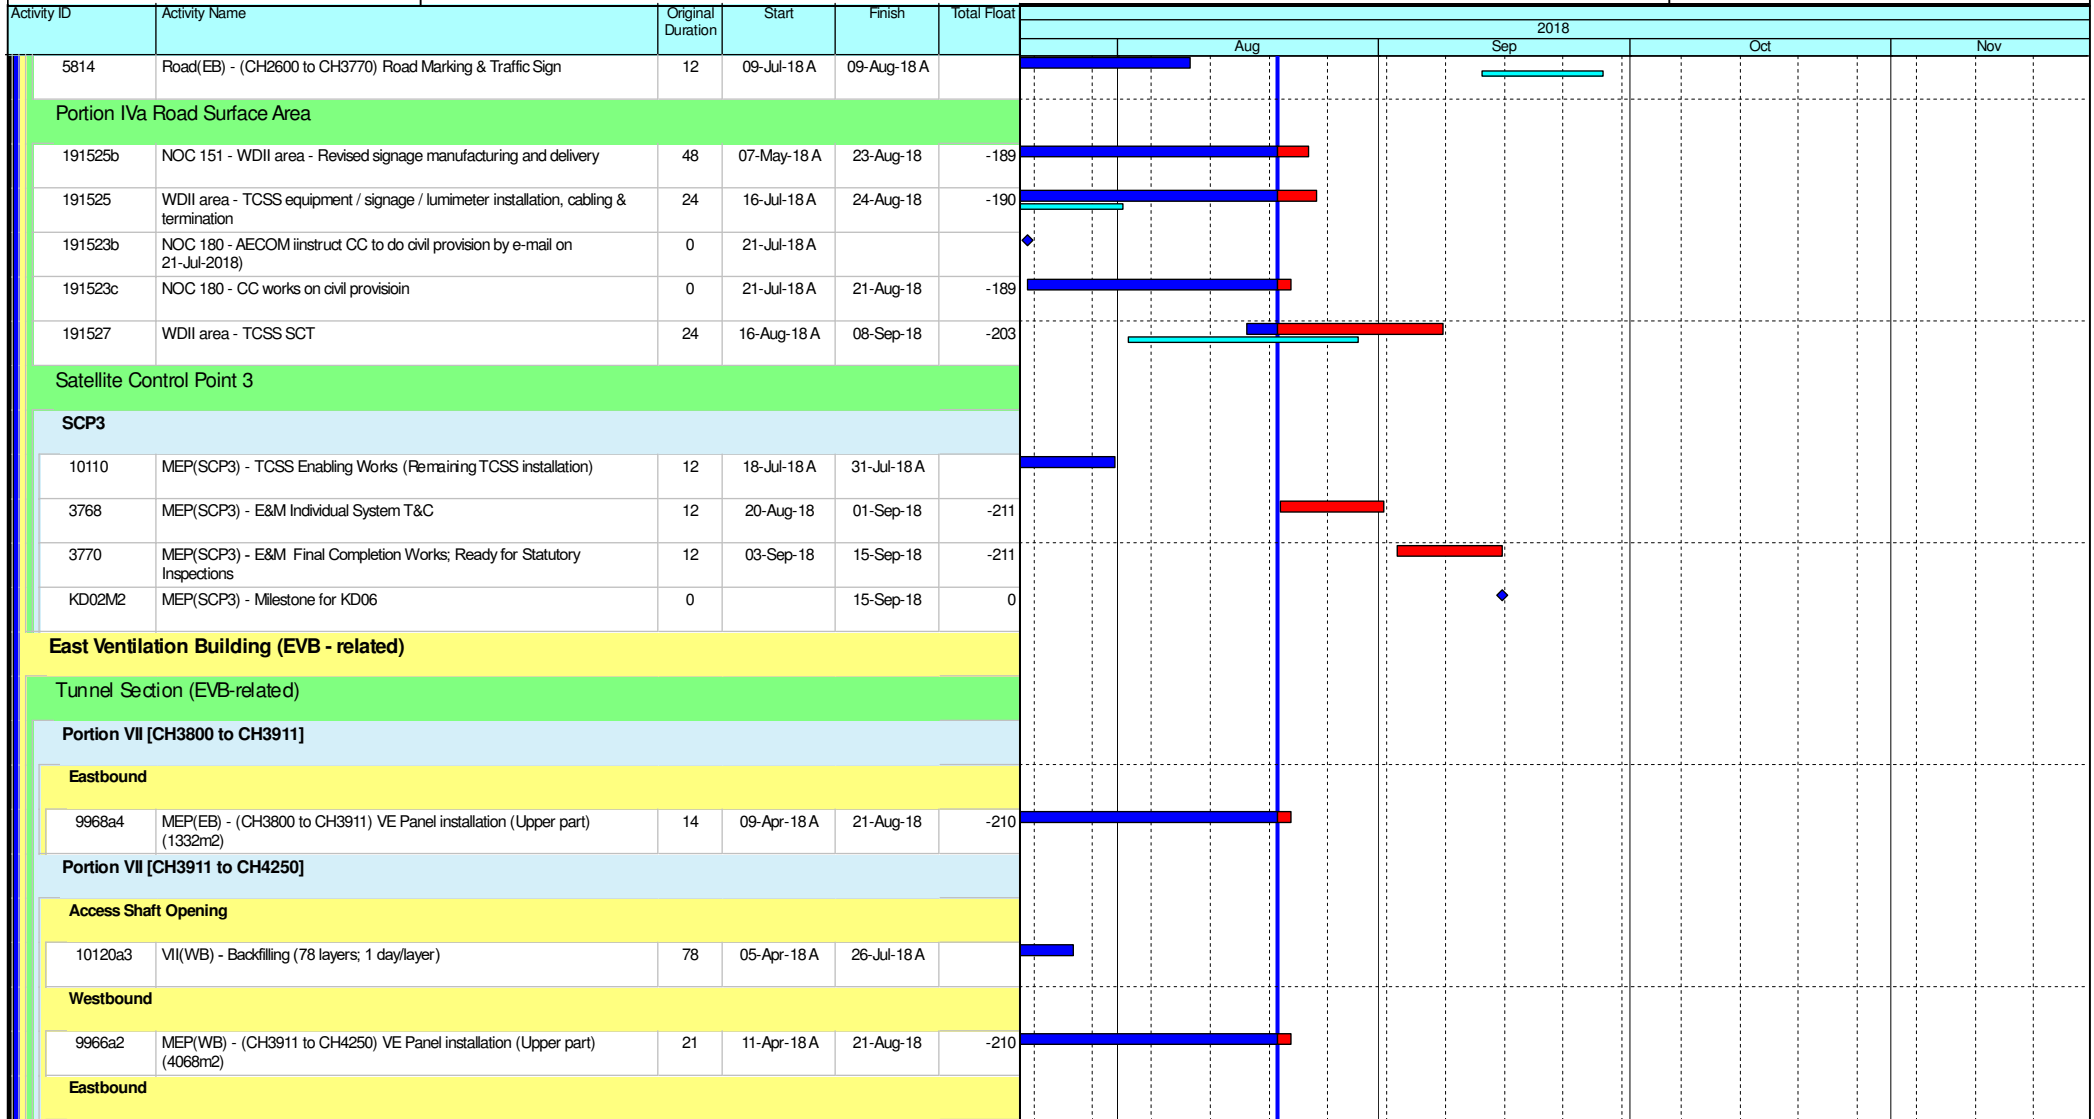

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 12 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Aug	Sep	Oct	Nov
9968a2	MEP(EB) - (CH3911 to CH4250) VE Panel installation (Upper part) (4086m2)	12	14-Apr-18 A	21-Aug-18	-210				
Portion VIIIa [CH4250 to CH4600]									
Eastbound									
9972	MEP(EB) - (CH4250 to CH4600) VE Panel installation (Upper part) (3900m2)	11	24-Jan-18 A	21-Aug-18	-210				
Portion IXd [CH4600 to CH4860]									
Eastbound									
9976	MEP(EB) - (CH4600 to CH4860) VE Panel installation (Upper part) (3300m2)	37	22-Mar-18 A	21-Aug-18	-210				
Portion IXa [CH4860 to CH5150]									
Eastbound									
5346	MEP(EB) - (CH4860 to CH5150) E&M Final Fix	10	14-Mar-18 A	27-Jul-18 A					
9980	MEP(EB) - (CH4860 to CH5150) VE Panel installation (Upper part) (3288m2)	37	05-Apr-18 A	23-Aug-18	-212				
East Ventilation Building (EVB)									
RC Structures and Green Roof									
3456	EVB - Green Roof (include architectural lighting & lightning protection system installation)	42	19-May-18 A	01-Sep-18	-330				
External Facade									
3438	EVB - External facing tiles / Treated Waste Wood / Louvre	90	11-Sep-17 A	22-Sep-18	-298				
192020	VO/335 - Material submission for approval	6	20-Aug-18	25-Aug-18	-30				
191613	VO/335 - Manufacture and delivery of smoke vent cover	24	27-Aug-18	22-Sep-18	-30				
191615	VO/335 - smoke vent cover installation and cable termination	18	24-Sep-18	16-Oct-18	-30				
191617	VO/335 - smoke vent cover T&C (Assume not affecting FSD inspection until further confirmation from AECOM / FSD)	6	18-Oct-18	24-Oct-18	-30				
MEP Works									
3452	MEP(EVB) - E&M Final Completion Works; Ready for Statutory Inspections	21	11-Apr-18 A	01-Sep-18	-220				
E&M Individual System T&C									
3660d	MEP(ADB) - LUX measurement for tunnel lighting	28	20-Aug-18	16-Sep-18	-254				

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 13 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

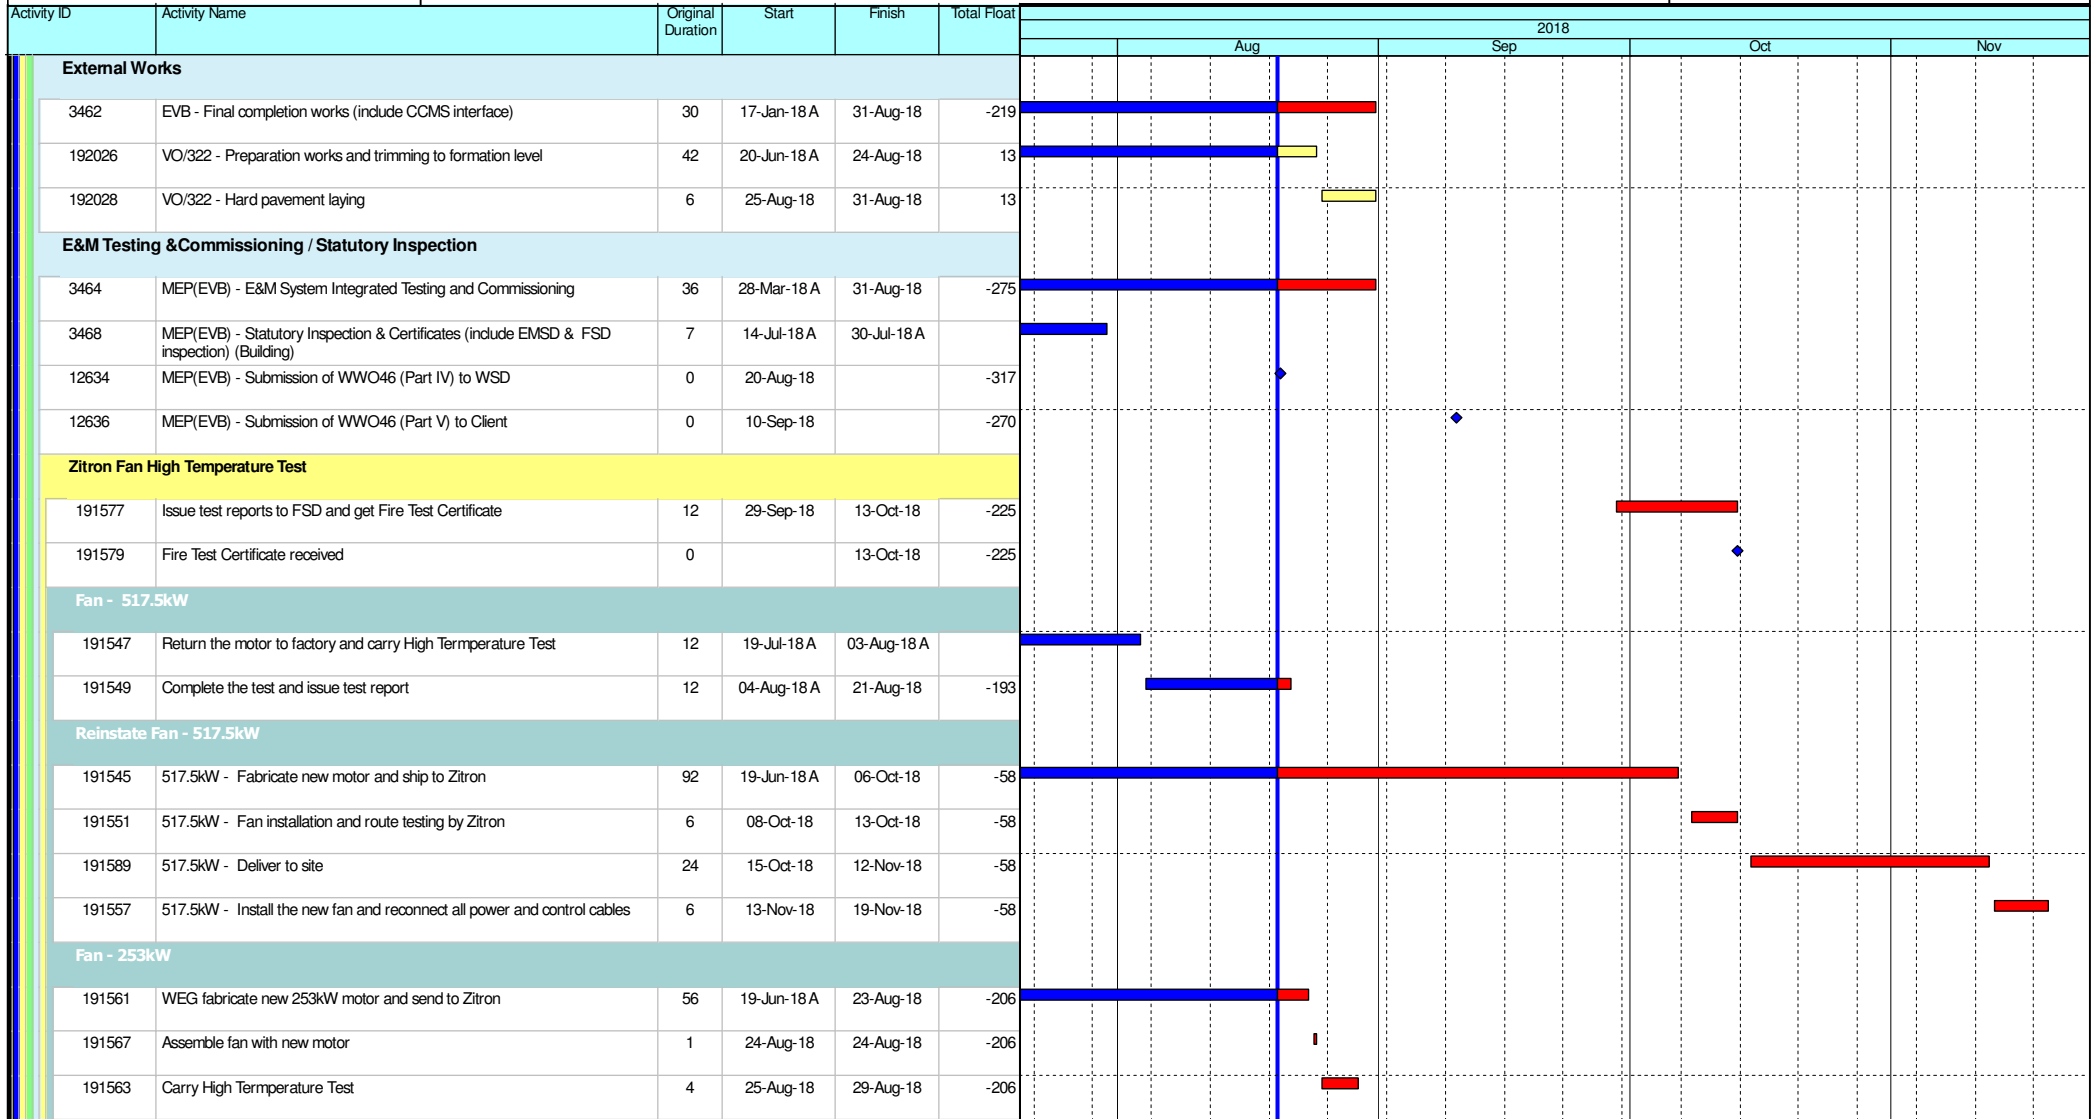

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 14 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

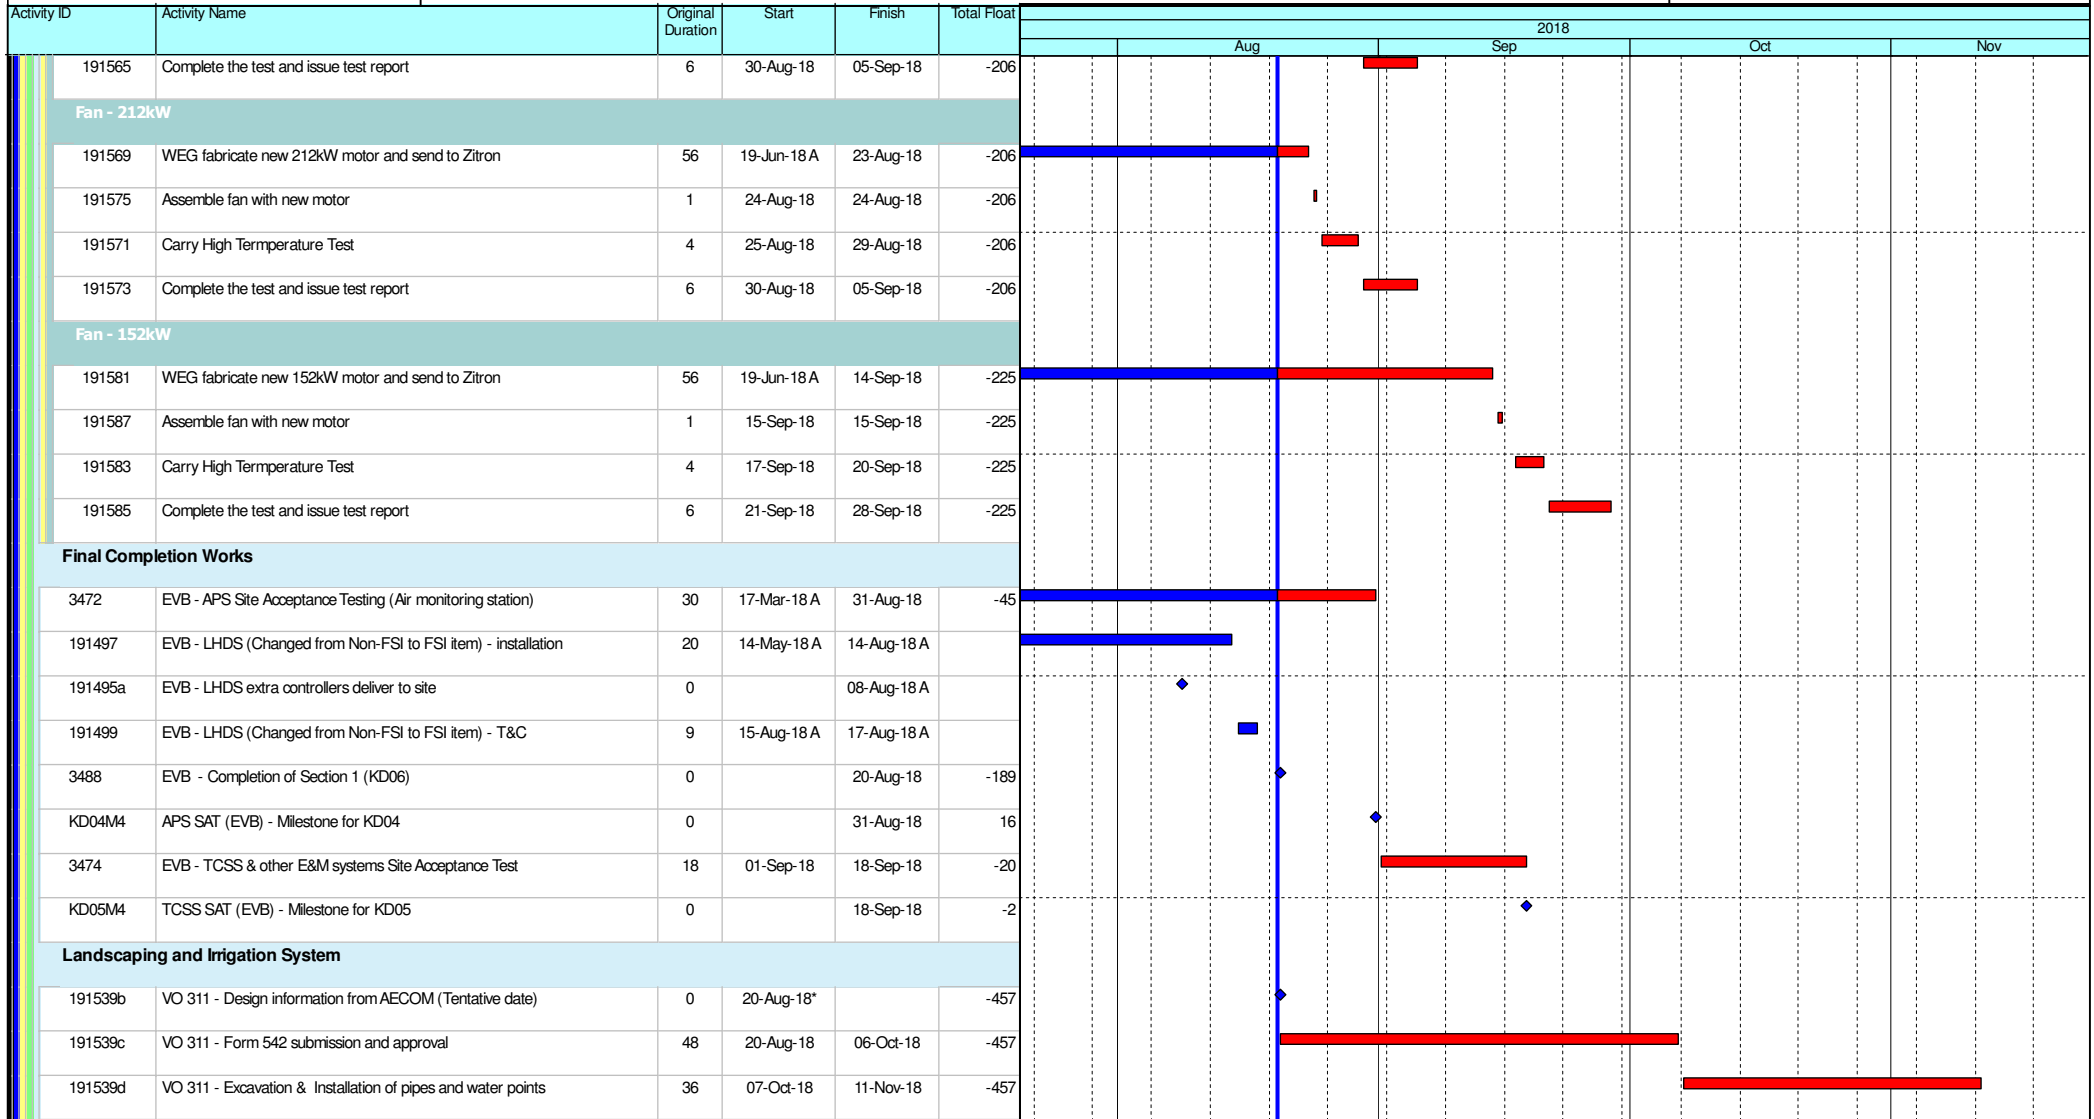

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 15 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

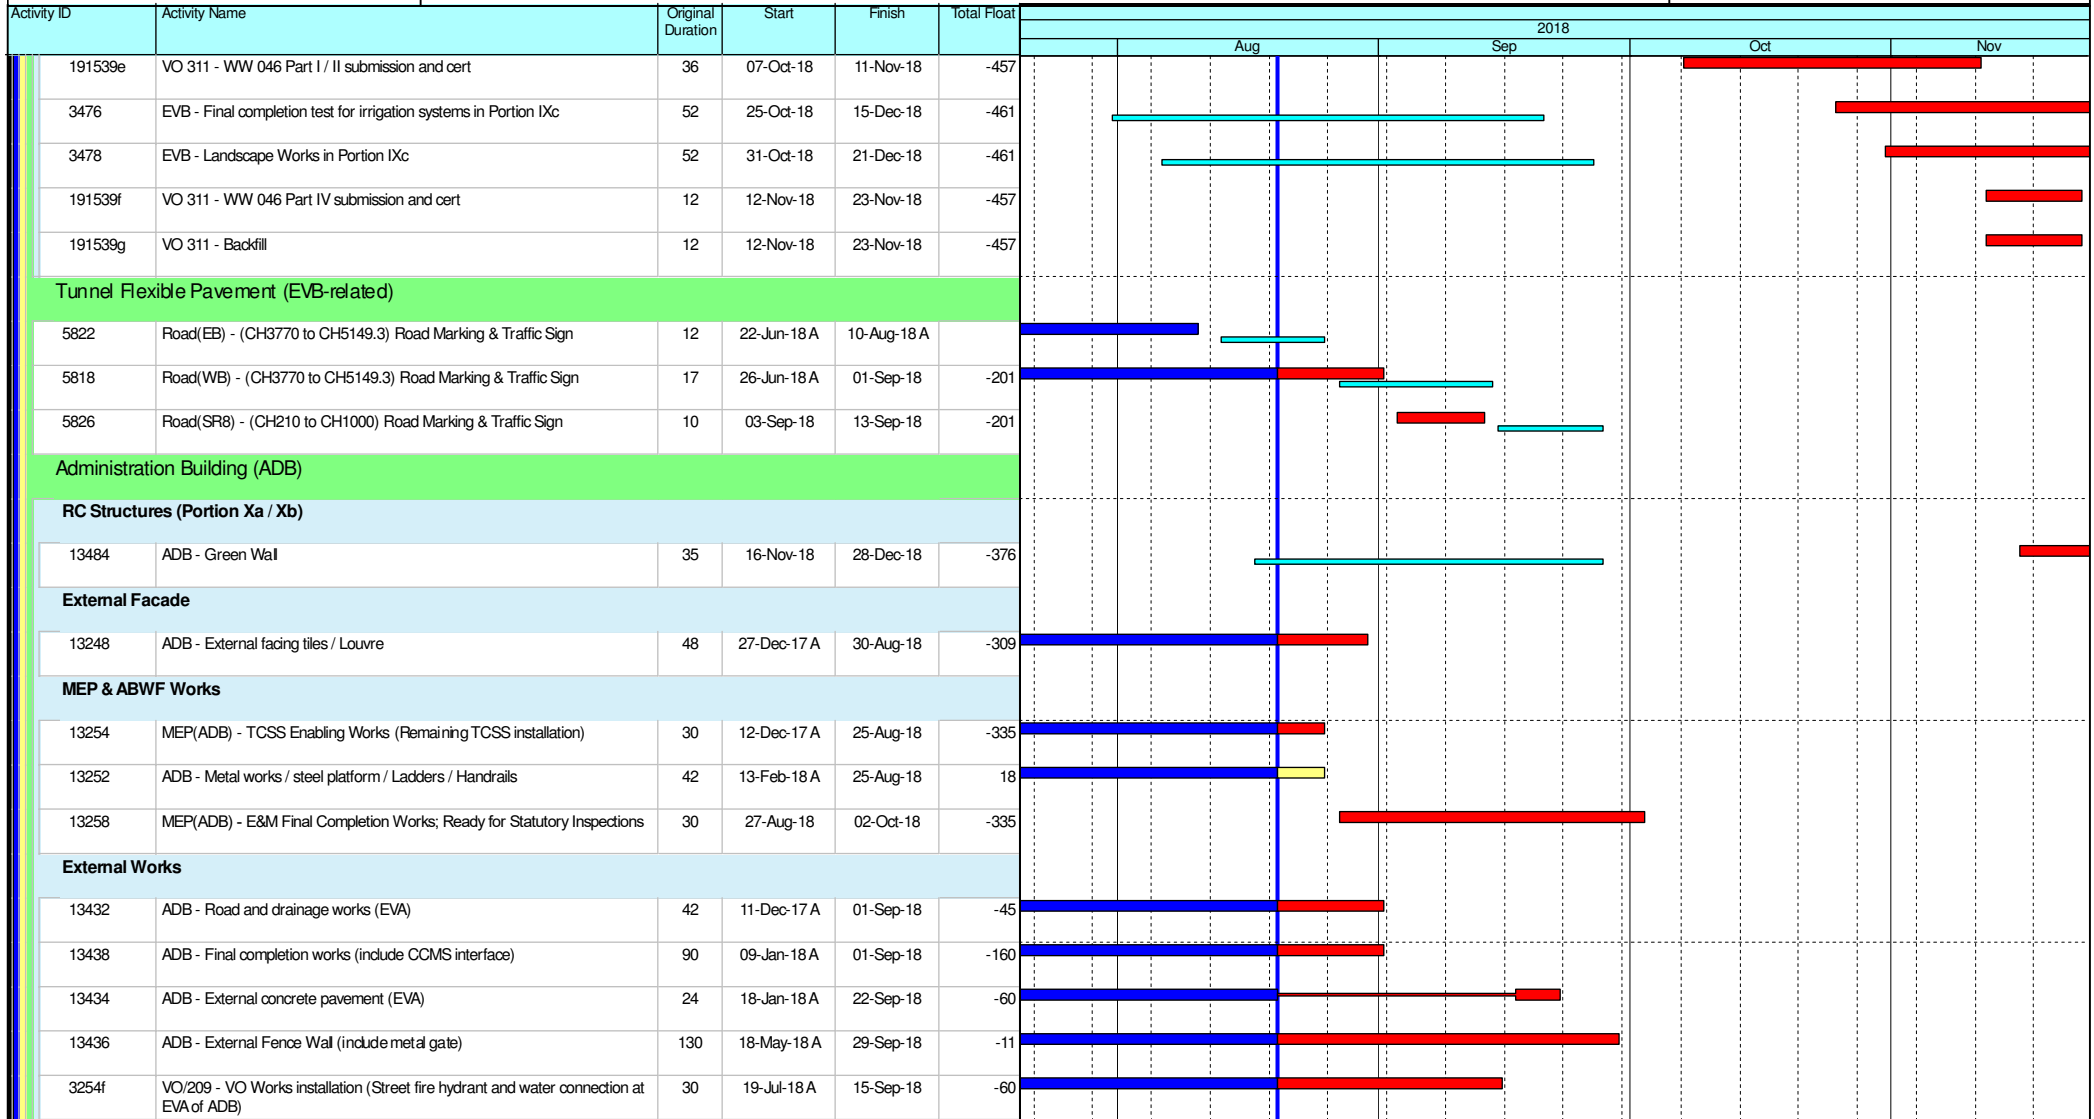

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 16 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

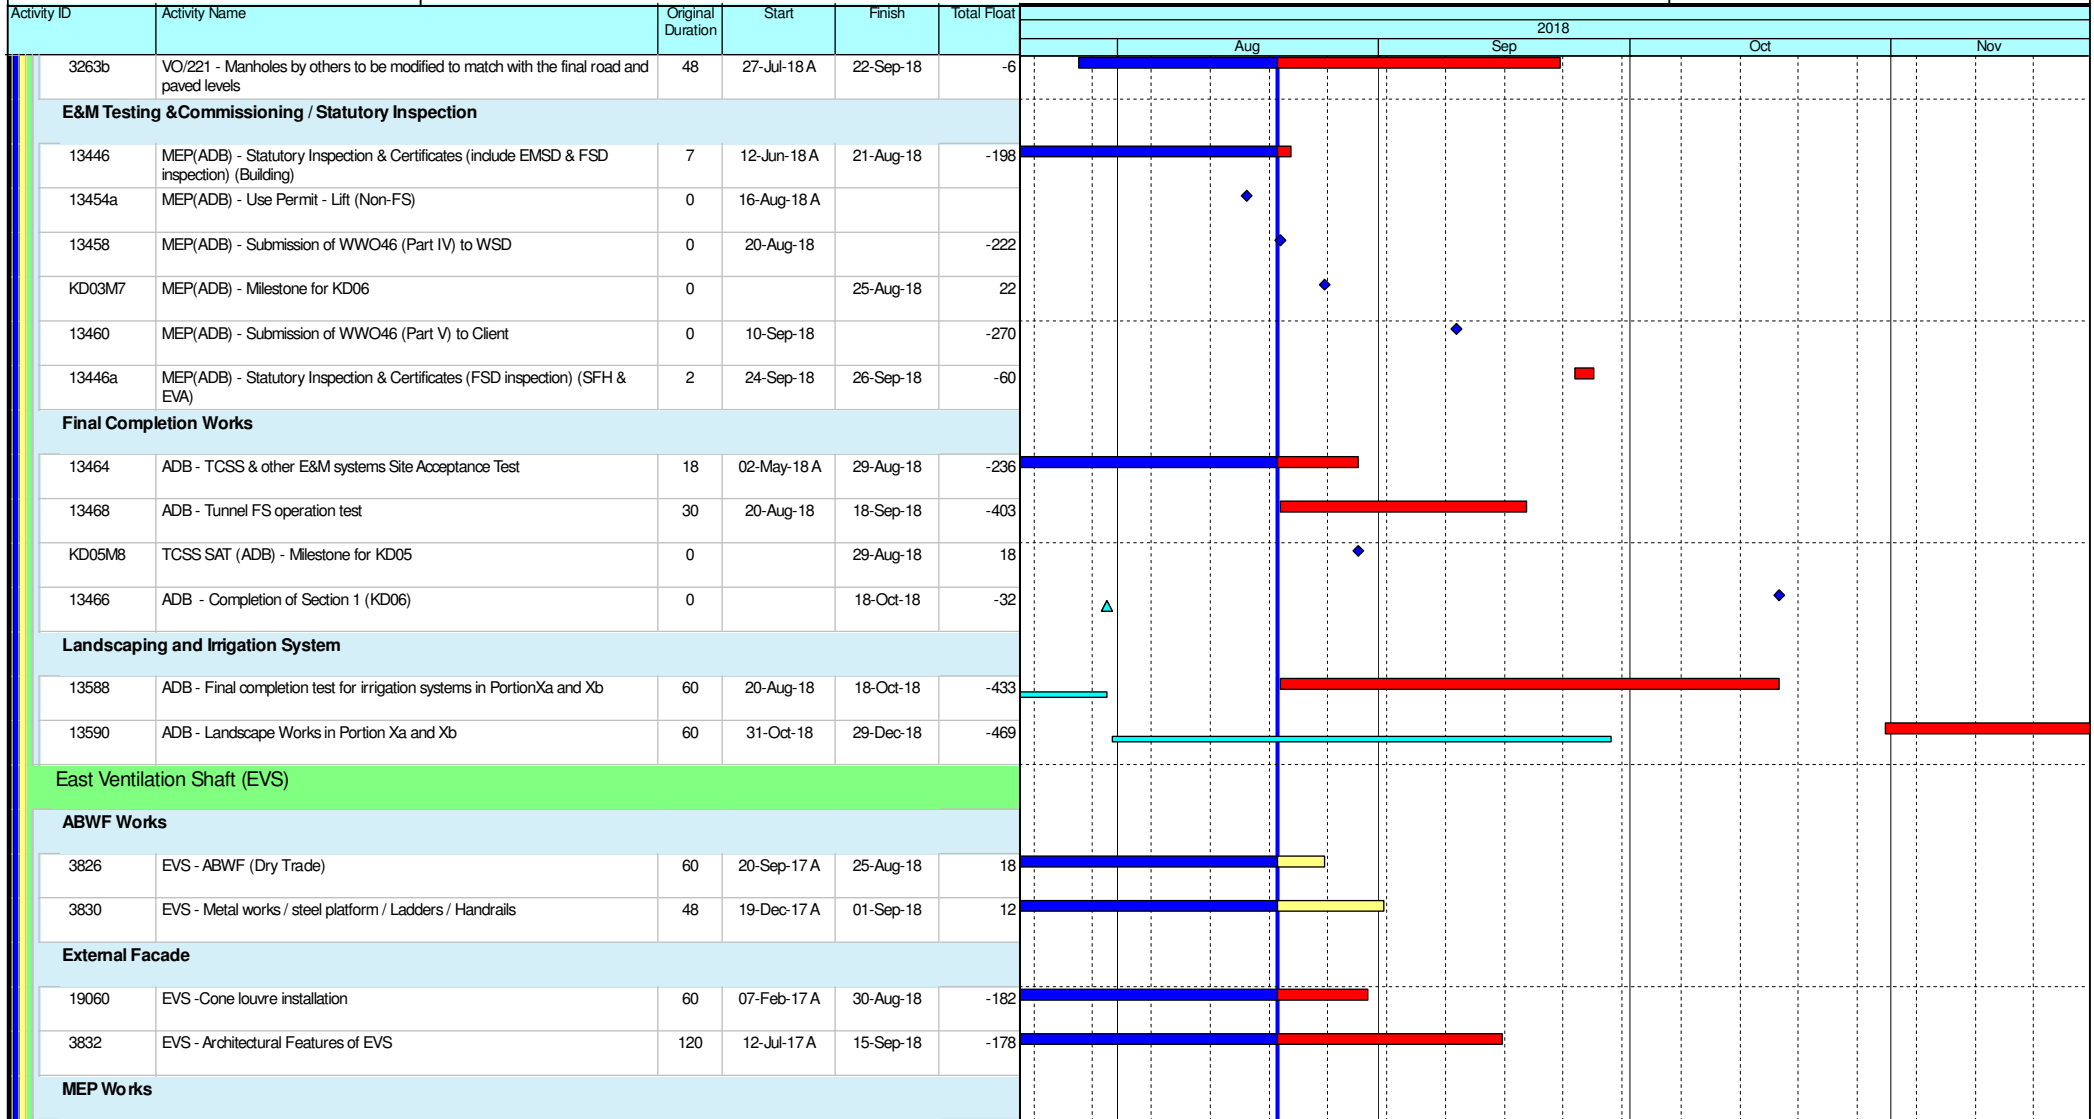

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 17 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

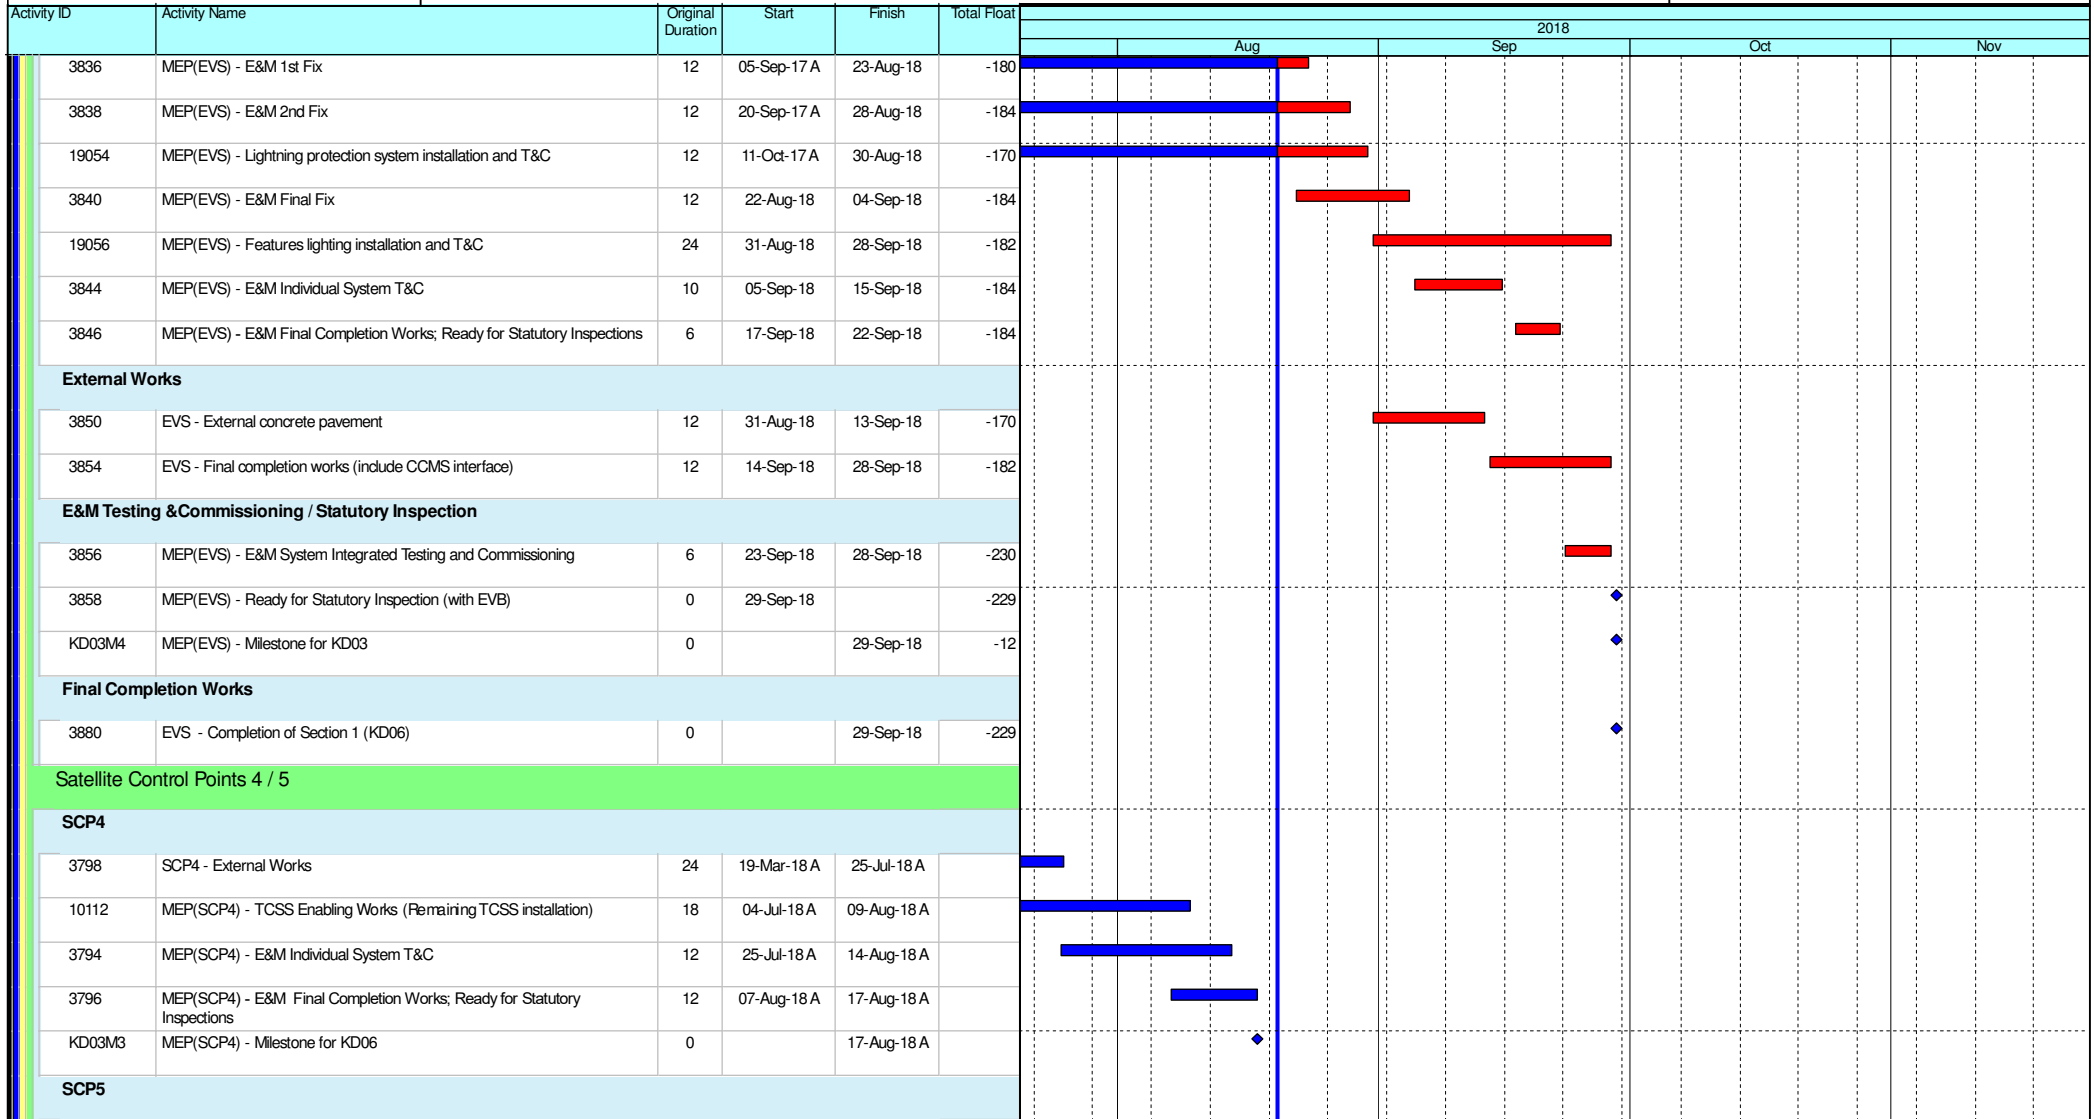

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 18 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Aug	Sep	Oct	Nov
3886	SCP5 - External Works	24	18-Jun-18 A	01-Sep-18	-211				
10114	MEP(SCP5) - TCSS Enabling Works (Remaining TCSS installation)	12	10-Jul-18 A	08-Aug-18 A					
3882	MEP(SCP5) - E&M Individual System T&C	12	20-Aug-18	01-Sep-18	-211				
3884	MEP(SCP5) - E&M Final Completion Works; Ready for Statutory Inspections	12	03-Sep-18	15-Sep-18	-211				
KD03M5	MEP(SCP5) - Milestone for KD06	0		15-Sep-18	0				
External Works									
Rumsey Street Flyover for Paymnet & Traffic Barrier									
5902b	RS - Modification of existing edge parapet at Connaught Road	108	05-Feb-18 A	31-Jul-18 A					
5902d	RS - Removal of central divider and replace with waterfilled barriers	120	10-Feb-18 A	31-Jul-18 A					
5902p	RS - Pavement tie-in works at CORC W/B	30	14-Aug-18 A	15-Sep-18	-215				
5902g	RS - Install new directional sign	6	17-Sep-18	22-Sep-18	-215				
5902r	RS - Road pavement tie-in E/B and W/B of CORC	6	24-Sep-18	02-Oct-18	-215				
5902q	RS - Road marking	6	24-Sep-18	02-Oct-18	-215				
5902m	RS - Demolish existing nosing and crush cushion	48	15-Oct-18	10-Dec-18	-141				
5904a	RS - Construct permanent parapet and nosing	102	15-Oct-18	21-Feb-19	-225				
5902n	RS - Paving works on Bridge B	12	30-Oct-18	12-Nov-18	-141				
Area A/B									
Area ATCSS									
10288a3	Request for VO/instruction-TCSS equipment installation & cabling (Gantries FVMS1 / ADS01) (Ref: H27613-LJV-ME-LE-4022)	24	04-Oct-16 A	25-Aug-18	-185				
Area B									
Area B TCSS									
Approach Road / Landscape Deck / Noise Enclosure (No TTA)									
10288b22	Area B TCSS cable termination (on IEC's Westbound) - DS06B	9	08-Jun-18 A	26-Jul-18 A					
10288b1	Area B TCSS equipment installation and cable termination (on IEC's Westbound) - GT3, GT2, Sm CCTV at Grade	18	13-Jun-18 A	15-Aug-18 A					

- Current Milestone
- Remaining Work
- Level of Effort
- Project Baseline
- Baseline Milestone
- Actual Work
- Critical Remaining Work

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 19 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

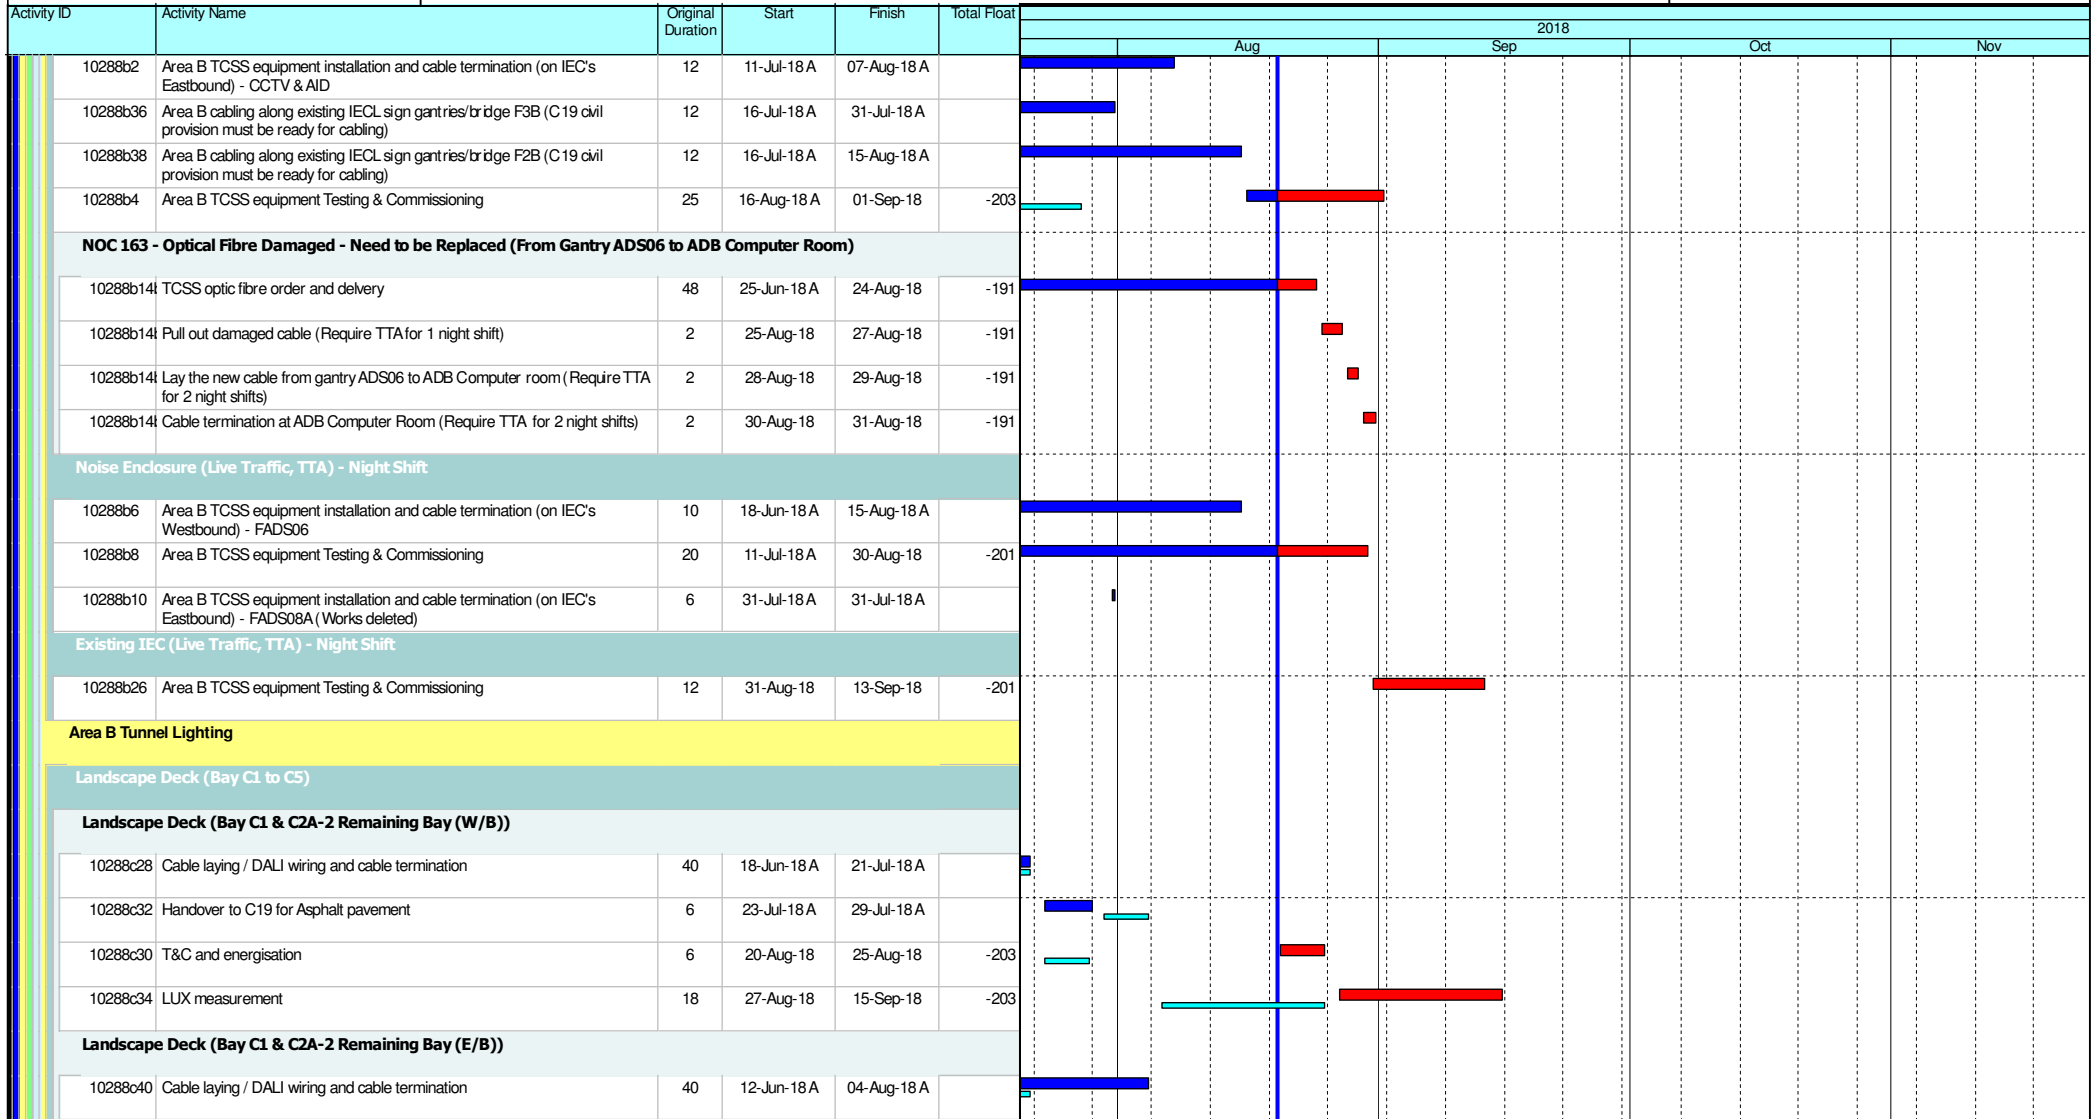

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 20 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

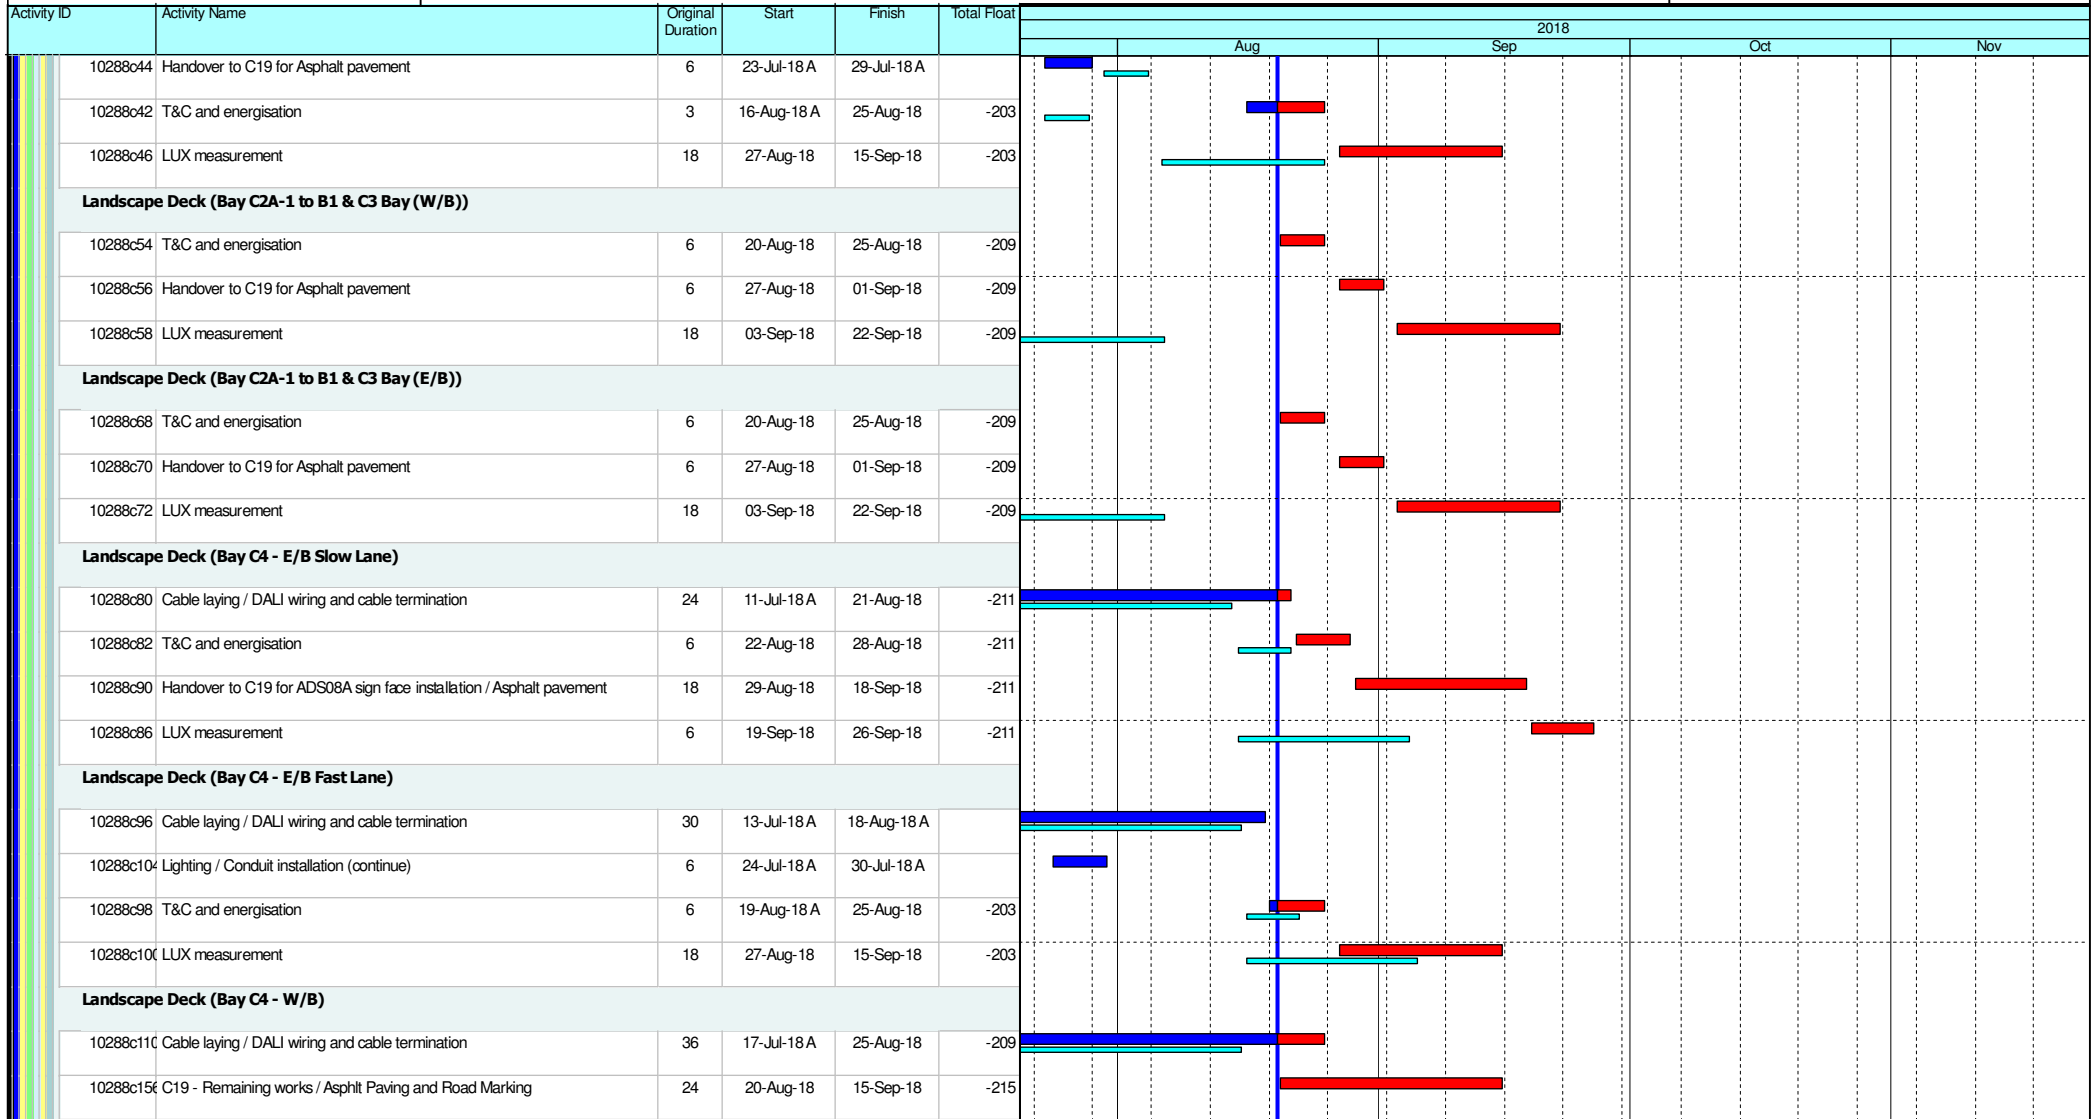

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 21 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

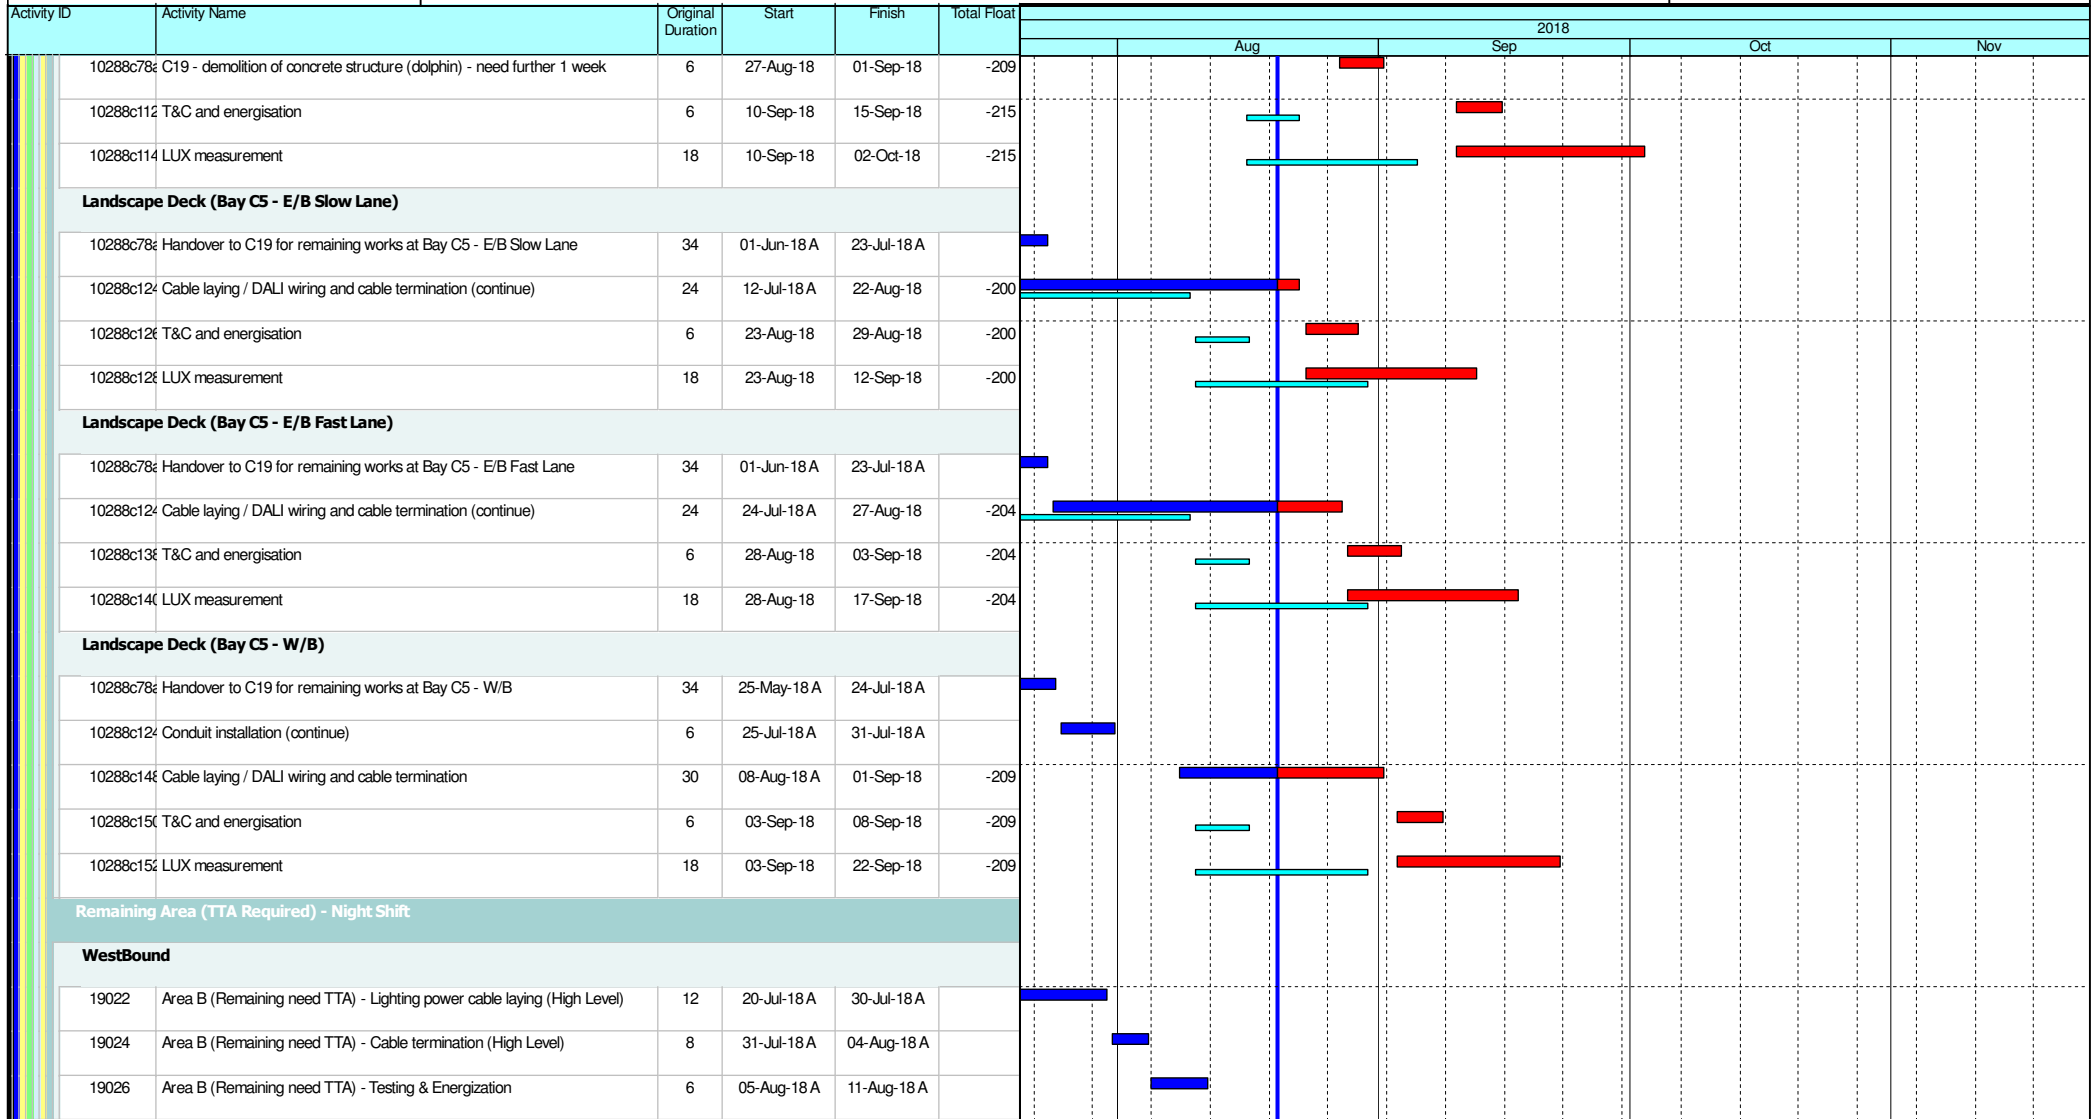

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 22 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

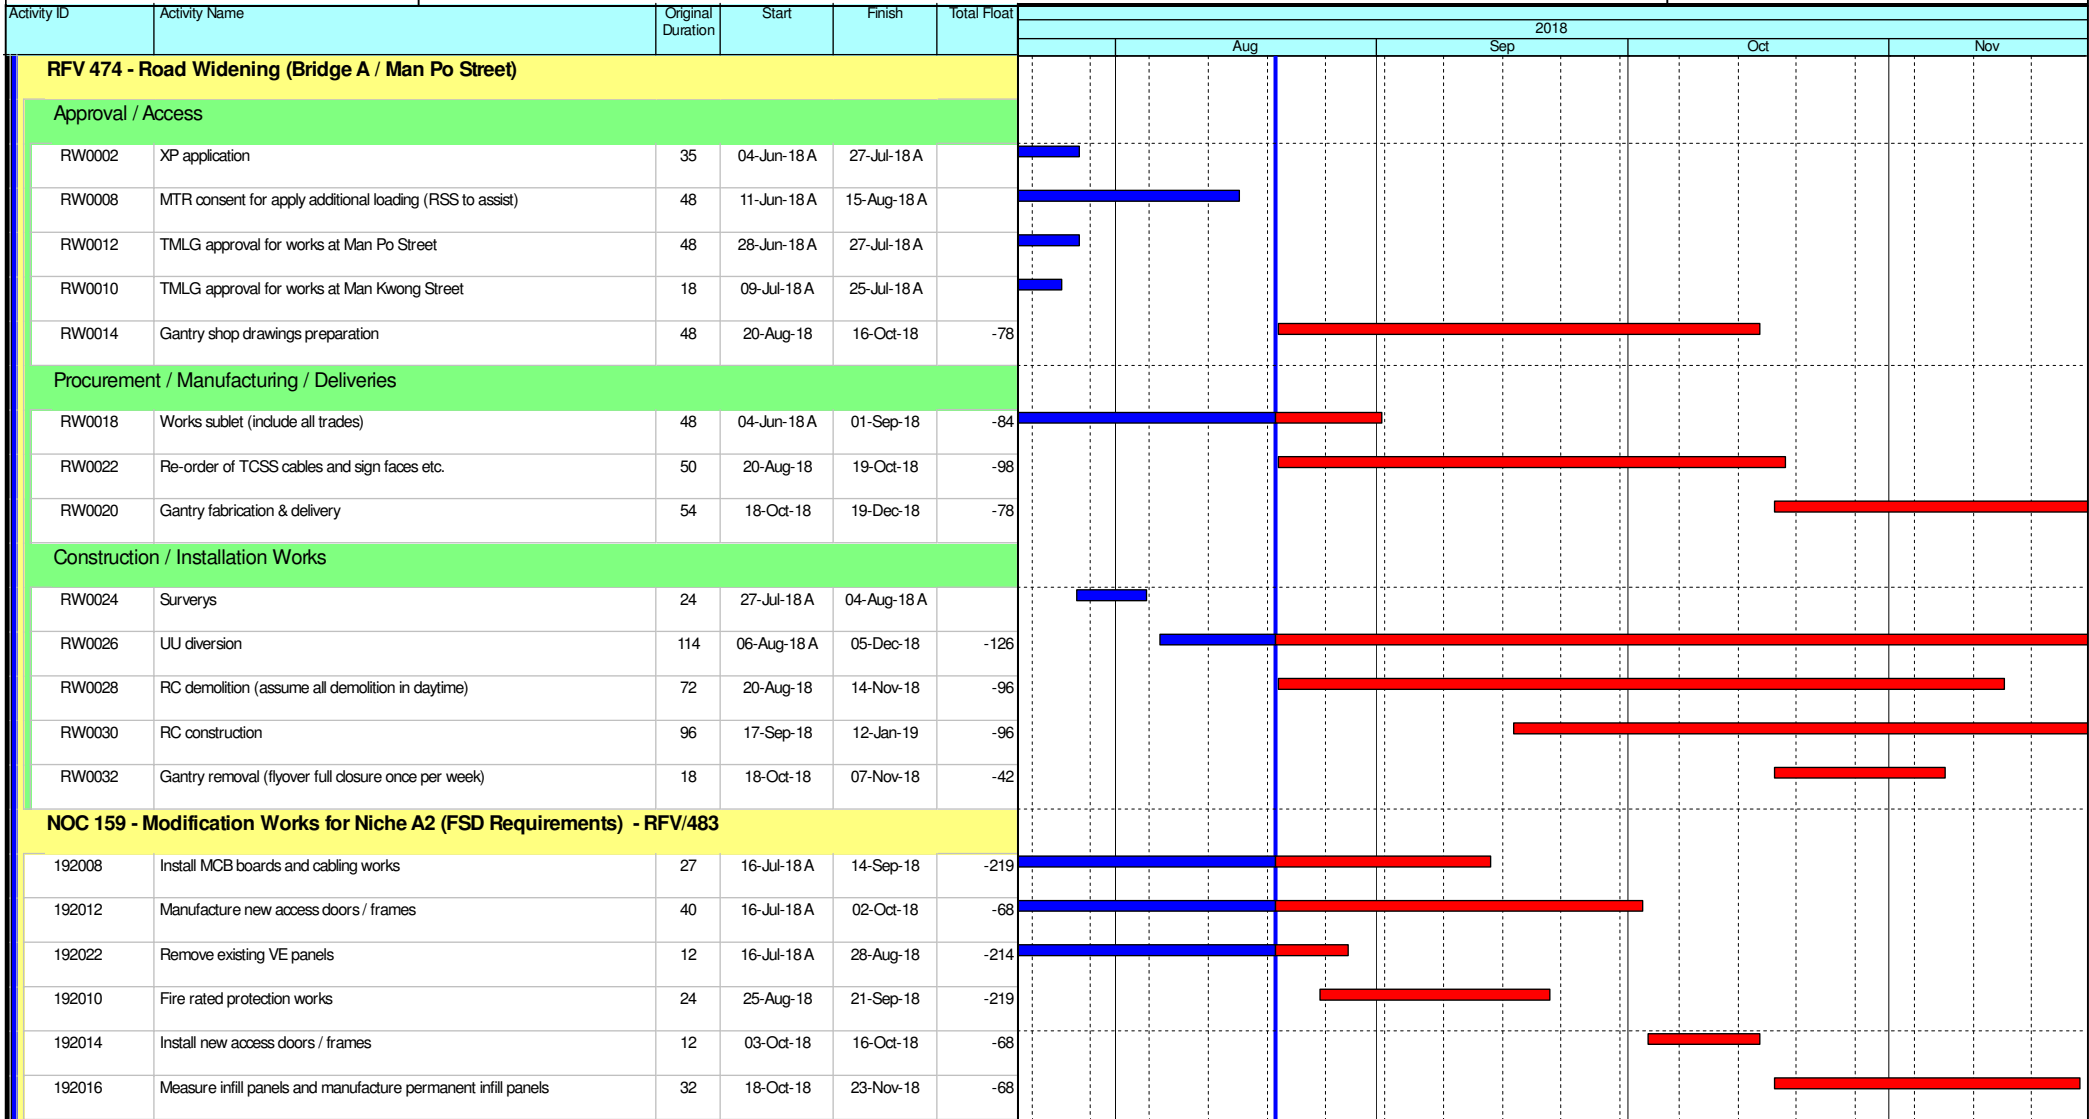

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 23 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

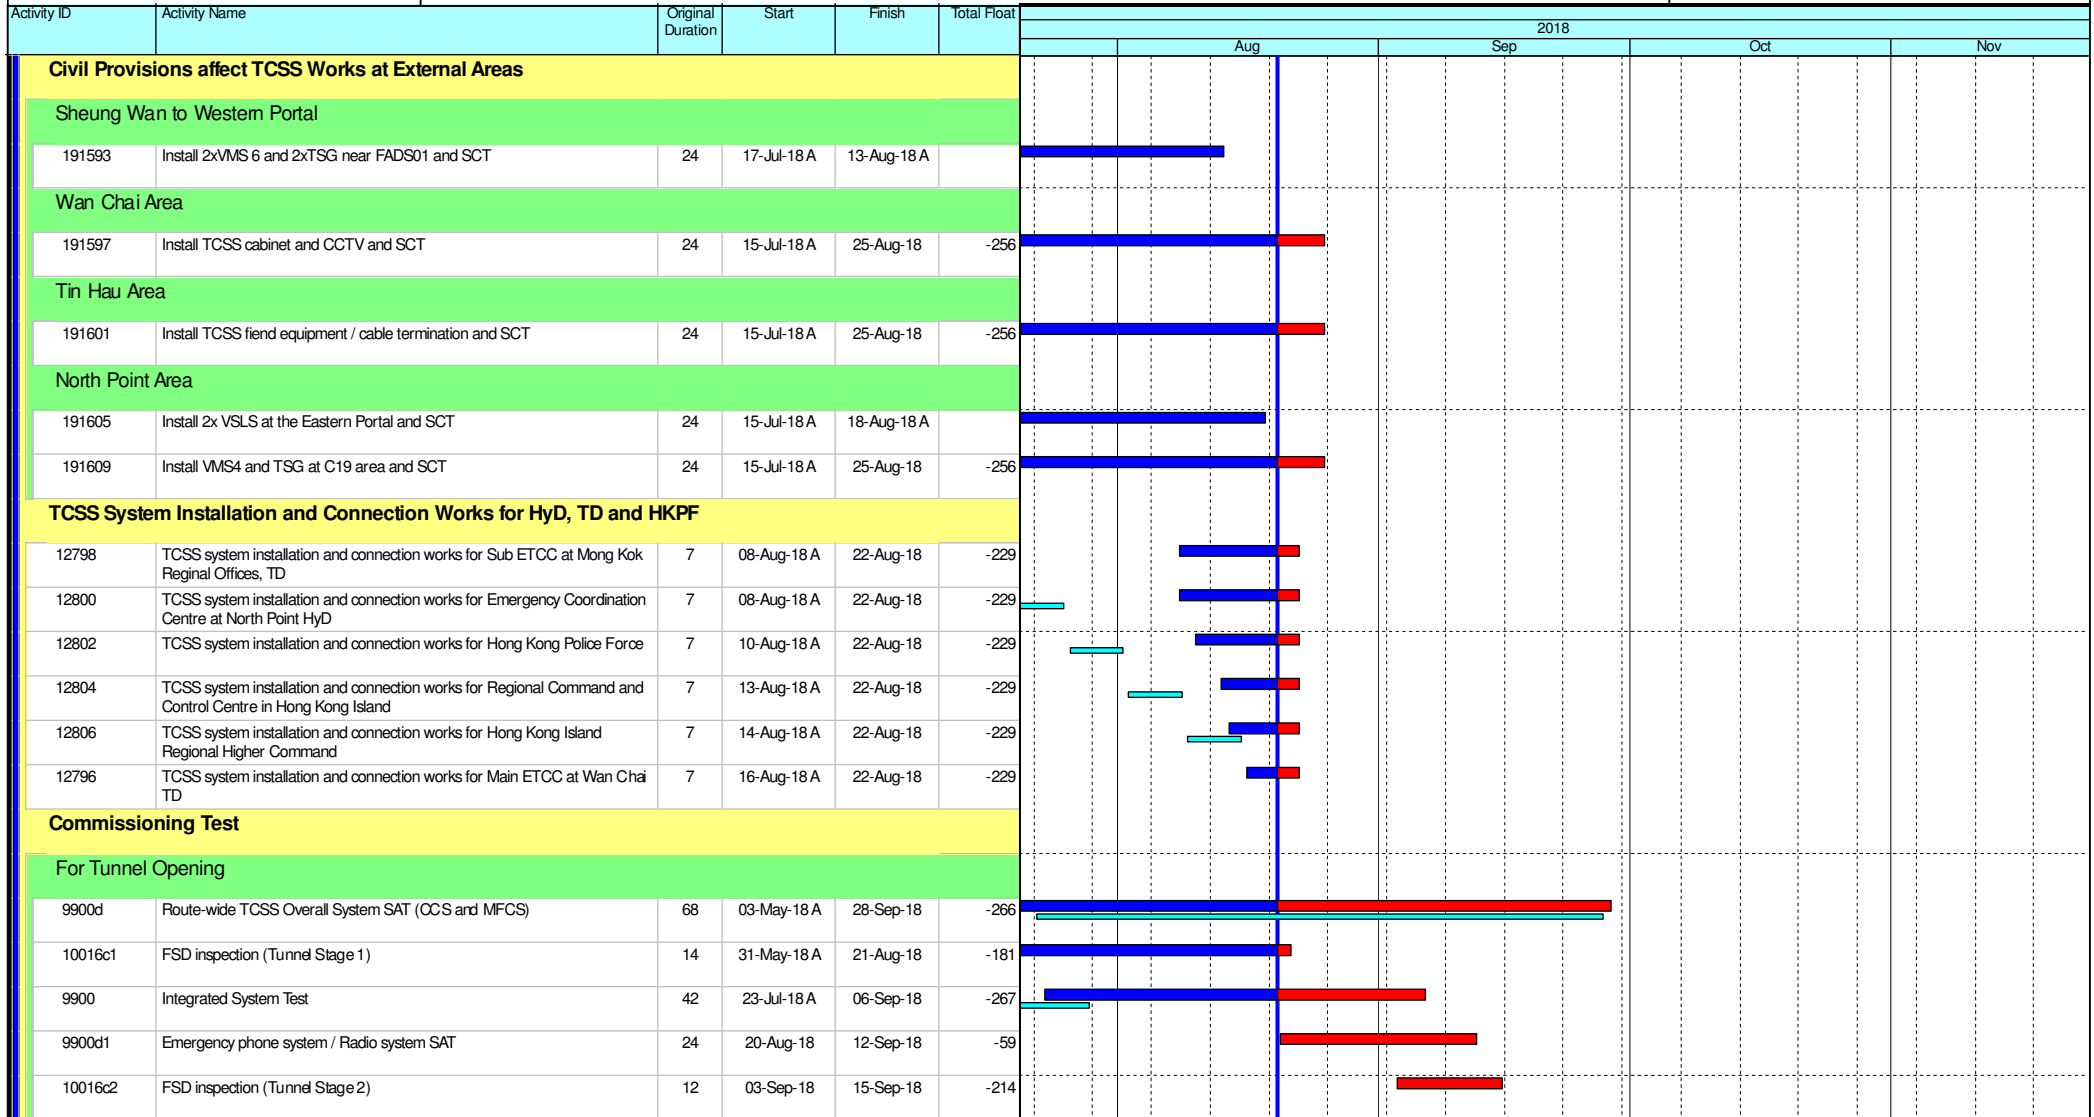

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 24 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

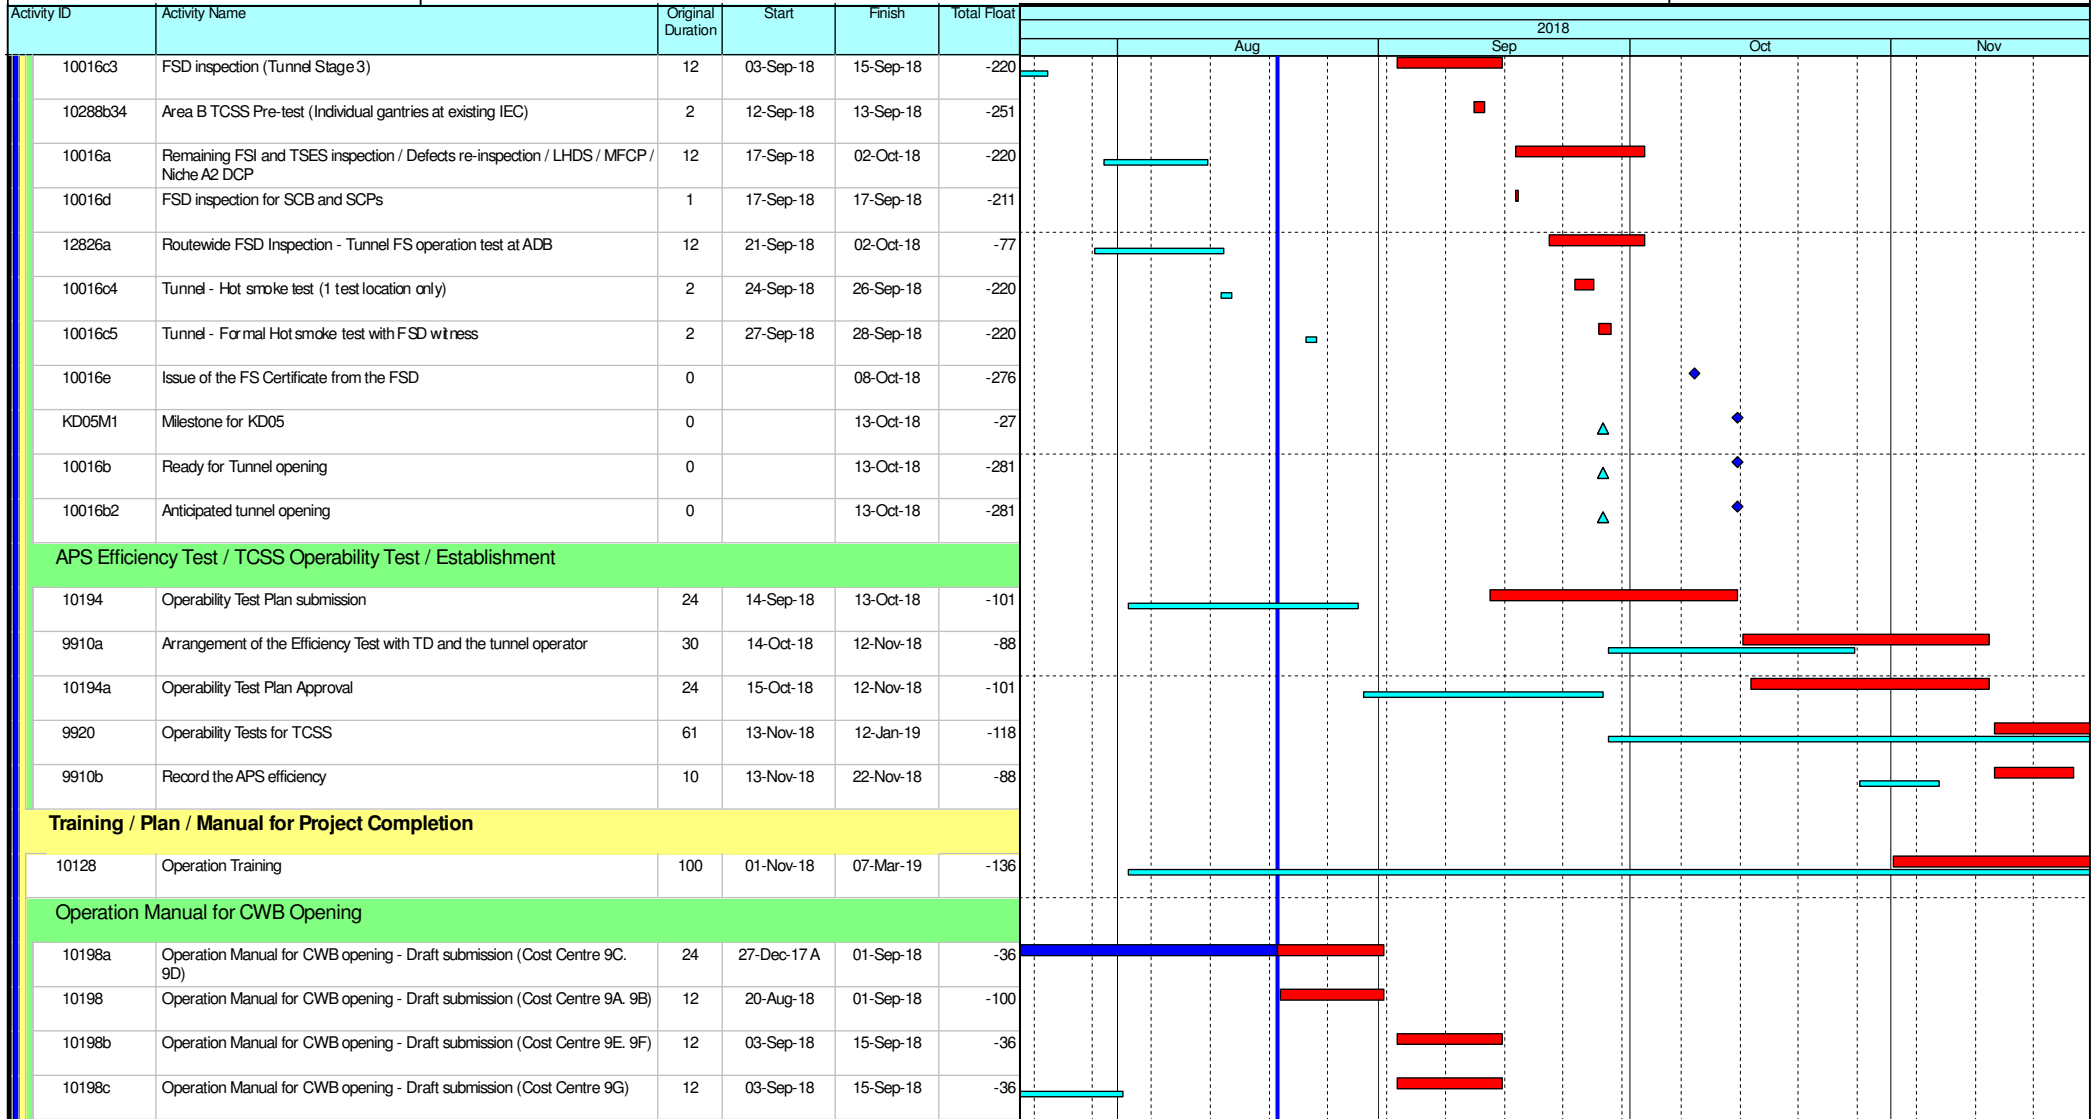

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING



Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 25 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

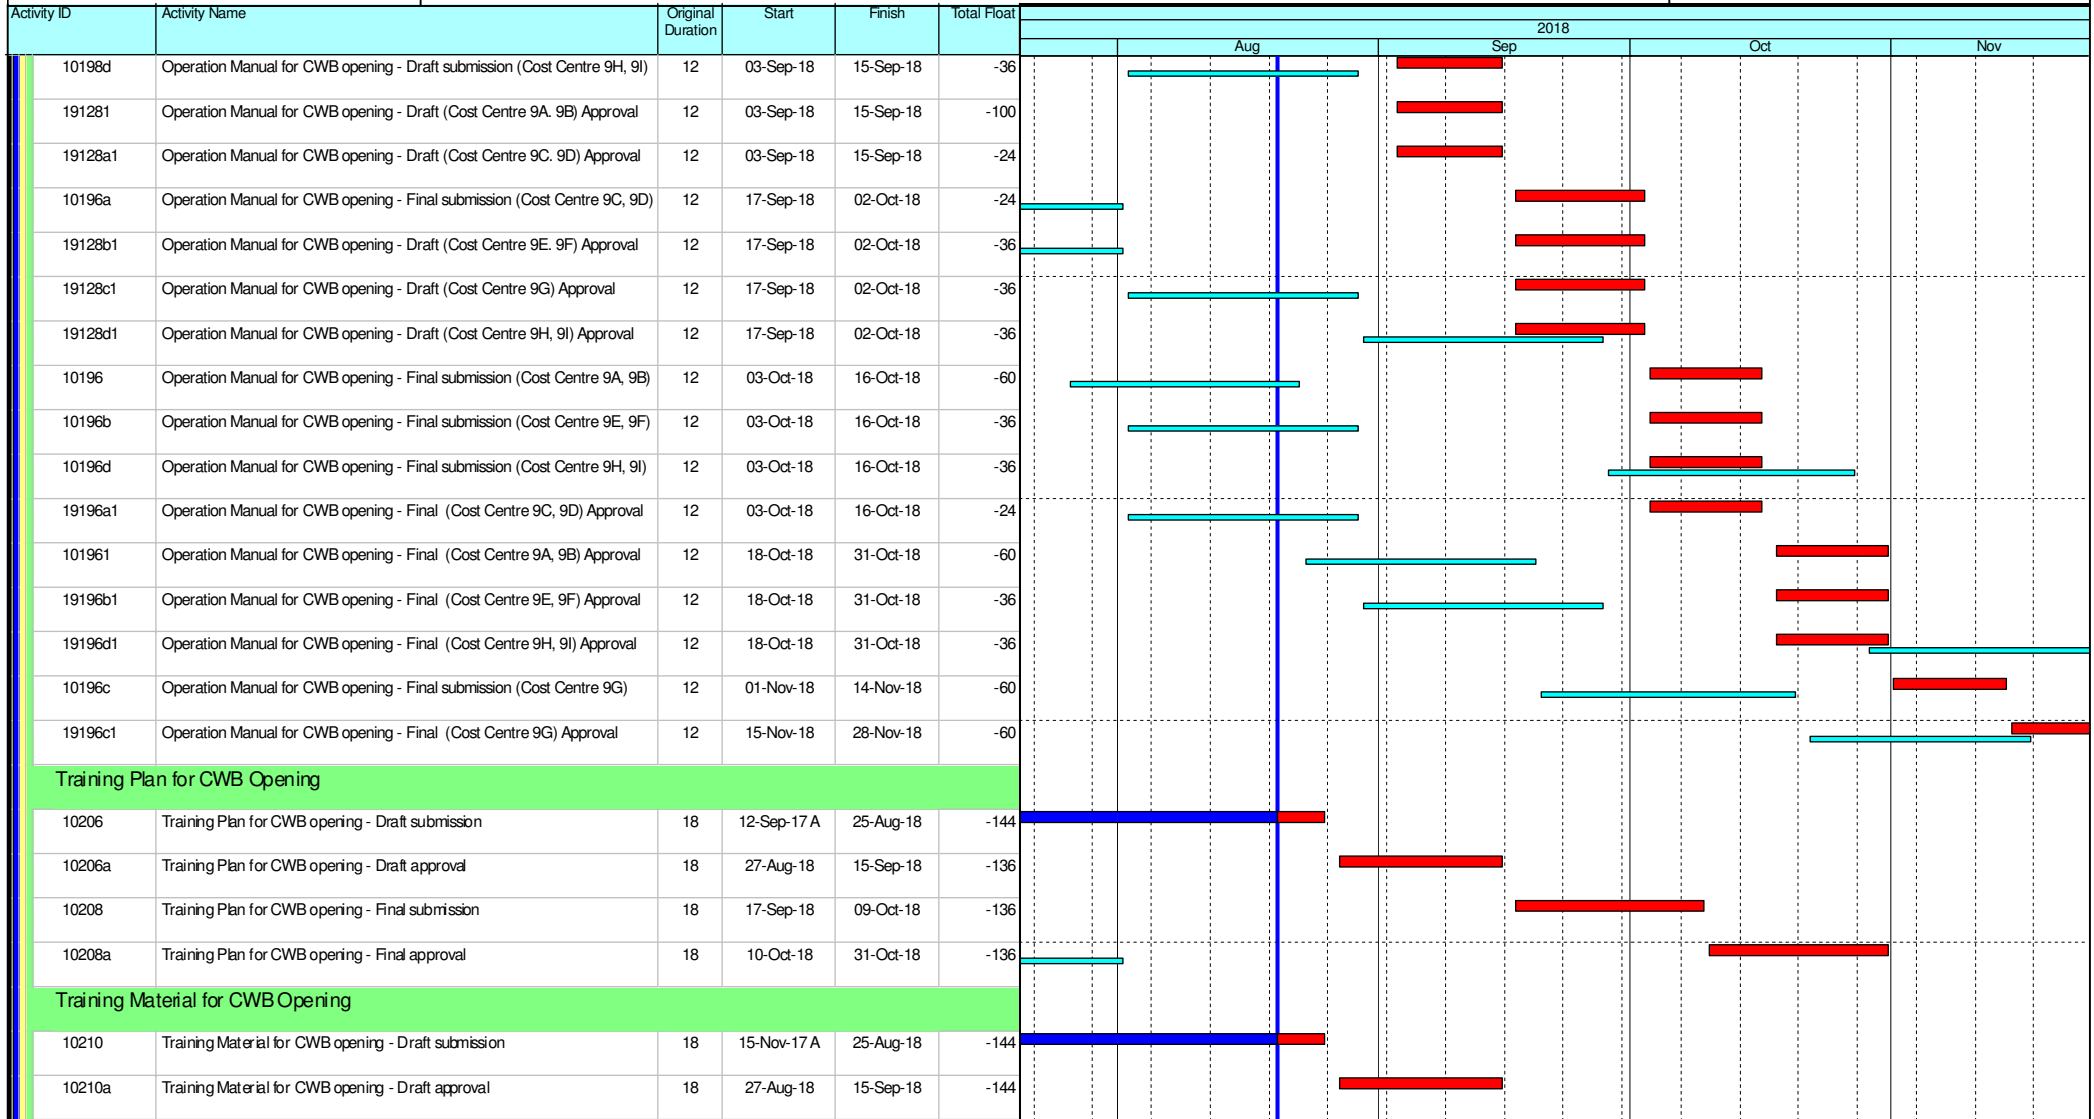

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 26 of 27








Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW

Data Date: 20-Aug-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018			
						Aug	Sep	Oct	Nov
10212	Training Material for CWB opening - Final submission	18	17-Sep-18	09-Oct-18	-144				
10212a	Training Material for CWB opening - Final approval	18	10-Oct-18	31-Oct-18	-136				
Maintenance Manual / Plan									
10200	Maintenance Plan	18	10-Oct-18	31-Oct-18	-144				
10220	Maintenance Manual / logbook - Draft submission	18	01-Nov-18	21-Nov-18	-144				

-  Current Milestone
-  Level of Effort
-  Baseline Milestone
-  Actual Work
-  Critical Remaining Work
-  Remaining Work
-  Project Baseline

Leighton Contractors (Asia) Limited Programme Update 54 (August 2018) THREE MONTH ROLLING

Project ID: H2613-U054
 Baseline: DWP4
 Layout: Update Three Month Rolling
 U054
 Page 27 of 27

Date	Revision	Checked	Approv...
20-Jul-18	U053	AT	CW
20-Aug-18	U054	AT	CW
