

CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central -Wan Chai Bypass at Wan Chai West

Activity ID	Activity Name	Early Start	Early Finish	Remaining Duration	Activity % Complete	2015			
						Mar	Apr	May	Jun
HK/2012/08 Revised Works Programme Rev.4 (Revised as of 28-Feb-15)									
Dredging and Reclamation									
Marine Work Construction									
Zone CRIII									
Dredging - Zone CRIII									
CRIII - Temporary Pipe Pile Wave Wall (1st Stage)									
MAR12360	CRIII - temp pipe pile wall (34-197) - install 610 dia. pipe pile [Remaining 28 nos. @750c/c]	18-Oct-14 A	27-May-15	70	0%				
Dredging at Zone CRIII									
1st Stage of Work (Types 2E, 1B(1), 1B(2), 1B(3))									
MAR15060	Zone CRIII - 1st stage - demolish existing tie beam & removal of L-shaped wall	09-Feb-15 A	27-May-15	70	0%				
MAR15080	Zone CRIII - 1st stage - removal of seawall block	12-Feb-15 A	29-May-15	72	0%				
MAR15120	Zone CRIII - 1st stage - Dredging to final formation level for Seawall 2E, 1B(2), 1B(1) & 1B(3)	25-Feb-15 A	03-Jun-15	76	0%				
MAR15140	Zone CRIII - 1st stage - Final Hydrographic Survey	04-Mar-15	05-Jun-15	75	0%				
Seawall Construction - Zone CRIII									
Zone CRIII Seawall (1st Stage)									
Seawall 2E									
MAR20620	Zone CRIII - fill rock mound for Seawall 2E & Trimming	05-Mar-15	12-Mar-15	7	0%				
MAR20640	Zone CRIII - lay toe block and level stone for Seawall 2E	13-Mar-15	21-Mar-15	8	0%				
MAR21070	Zone CRIII - deliver and install caisson seawall 2E	22-Mar-15	23-Mar-15	2	0%				
Seawall 1B(1)									
MAR20700	Zone CRIII - fill rock mound for Seawall 1B(1) & Trimming	05-Mar-15	12-Mar-15	7	0%				
MAR20720	Zone CRIII - lay toe block and level stone for Seawall 1B(1)	13-Mar-15	21-Mar-15	8	0%				
MAR21200	Zone CRIII - deliver and install caisson seawall 1B(1)	22-Mar-15	23-Mar-15	2	0%				
Seawall 1B(2)									
MAR20660	Zone CRIII - fill rock mound for Seawall 1B(2) & Trimming	25-Apr-15	02-May-15	6	0%				
MAR20680	Zone CRIII - lay toe block and level stone for Seawall 1B(2)	02-May-15	09-May-15	7	0%				
MAR21100	Zone CRIII - deliver and install caisson seawall 1B(2)	10-May-15	11-May-15	2	0%				

- Actual Work
- Remaining Work
- Critical Remain...
- Milestone

Project Star :22-Jan-13
Project End: 21-Jul-18
Date Date: 28-Feb-15

3 Months Rolling Programme (CRIII Area)
March 2015 to May 2015

Date	Revision	Checked	Approved
01-Mar-15	1		



Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	June 2015							July 2015							August 2015							September 2015							October 2015							November 2015							December 2015							January 2016							February 2016							March 2016							April 2016							May 2016							June 2016							July 2016							August 2016							September 2016						
					01	08	15	22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	01	08	15	22	29	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05	12	19																																											
HK/2012/08 Revised Works Programme Rev.4_1(Final)																																																																																																																				
Works for Section Completion																																																																																																																				
Construction																																																																																																																				
Section II A - CWB Tunnel & Slip Road Structures and Facilities																																																																																																																				
CWB CRIII & A1																																																																																																																				
CWB CRIII & A1 - Pumping Test Preparation/ Pumping Test																																																																																																																				
CWB A1 - Pumping Testing Preparation																																																																																																																				
SIIA11240	Sec II A - CWB A1 - install dewater/ recharge / observation well	17	11-May-15 A	20-Jul-15																																																																																																																
CWB CRIII & A1 - Pumping Test																																																																																																																				
SIIA10780	Sec II A - CWB CRIII - pumping test (CRIII, A1)	10	20-Jul-15	30-Jul-15																																																																																																																
CWB CRIII - ELS & Tunnel Structure																																																																																																																				
CWB CRIII - ELS																																																																																																																				
SIIA10820	Sec II A - CWB CRIII: Shoring & Excavation	42	18-Apr-15 A	18-Aug-15																																																																																																																
SIIA10960	Sec II A - CWB CRIII: Demolish Bulkhead at West End	45	19-Aug-15	12-Oct-15																																																																																																																
CWB CRIII - Tunnel Structure																																																																																																																				
SIIA10840	Sec II A - CWB CRIII: Base, wall, OHVD & roof (bay 1)	45	19-Aug-15	12-Oct-15																																																																																																																
SIIA10880	Sec II A - CWB CRIII: Base, wall, OHVD & roof (bay 3)	45	19-Aug-15	12-Oct-15																																																																																																																
CWB A1 - ELS & Tunnel Structure																																																																																																																				
CWB A1 - ELS Remaining																																																																																																																				
SIIA11286	Sec IIA - CWB A1 : Shoring & Excavation (Remaining)	37	07-Jul-15	18-Aug-15																																																																																																																
CWB A1 - Tunnel Structure Remaining																																																																																																																				
SIIA13045	Sec II A - CWB A1: Pile head + trough + base & wall + OHVD unit (1st bay)	45	19-Aug-15	12-Oct-15																																																																																																																
CWB A1 - Other Works																																																																																																																				
SIIA15480	Culvert L - [Summary] Bay 9 to Bay 11 on top of CWB A1 and divert flow	27	08-Jun-15 A	31-Jul-15																																																																																																																
SIIA15500	Zone A2(2) - Public Fill -4.0 to +4.0mPD (behind Type 4 & 13 for temp channel outlet)	28	01-Aug-15	28-Aug-15																																																																																																																
Section III - Road D11 & Part of Road P2, Area 4, Implement 1st Stage ITA																																																																																																																				
Roadwork & Utilities																																																																																																																				
General																																																																																																																				
SIII10040	Sec III - roadwork & utilities - storm water drain & subsoil drain	121	01-May-15 A	21-Nov-15																																																																																																																
SIII10060	Sec III - roadwork & utilities - Watermain & Irrigation Mains	100	07-Jul-15*	03-Nov-15																																																																																																																
SIII10080	Sec III - roadwork & utilities - gas main and valve chamber	100	17-Jul-15	13-Nov-15																																																																																																																
SIII10100	Sec III - roadwork & utilities - HEC cable duct and catchpit	100	27-Jul-15	23-Nov-15																																																																																																																
SIII10120	Sec III - roadwork & utilities - sub-base	100	06-Aug-15	03-Dec-15																																																																																																																
SIII10140	Sec III - roadwork & utilities - Road kerb	100	15-Aug-15	12-Dec-15																																																																																																																
SIII10160	Sec III - roadwork & utilities - flexible pavement	100	26-Aug-15	23-Dec-15																																																																																																																

Data Date: 30-Jun-15

- Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Remaining Level of Effort

Works Programme for Zone CRIII (June to August 2015)

Date	Revision	Checked	Approved
03-Jul-15			

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015					
						Jul	Aug	Sep	Oct		
Update 2015-06-20 CWB - Central Interchange (2014-06-20) Revised DWP R7 with RFI											
SECTION 3 - REMAINING WORKS IN PORTION IIIA & IIIB											
Surface Works - East of Man Yiu Street											
Road P1											
P1 Road East Bound											
VO089f	VO089 - Maintenance Section 1	906d	31-Jul-12 A	31-Aug-15	-162d						
VO089i	VO089 - Maintenance Section 2	299d	25-Aug-14 A	31-Aug-15	-162d						
14960	P1 E/B - Footpath (VO158) - Material approval & procurement	116d	10-Mar-15 A	31-Jul-15	-212d						
14904	P1 E/B - Street Furniture / Sign (VO/192)	75d	27-Mar-15 A	31-Jul-15	-136d						
14960a	P1 E/B - Footpath (VO158) - Block fabrication and Site work	76d	01-Aug-15	31-Oct-15	-212d						
P1 Road West Bound											
VO089b	VO089 - Maintenance Section 1	906d	31-Jul-12 A	31-Aug-15	-162d						
VO089d	VO089 - Maintenance Section 2	299d	25-Aug-14 A	31-Aug-15	-162d						
14958	P1 W/B - Footpath (VO158) - Material approval & procurement	116d	10-Mar-15 A	31-Jul-15	-212d						
1520	P1 W/B - U Channel / Landscape works / Drainage (VO/192)	25d	01-Jun-15 A	31-Jul-15	-136d						
1512a	P1 W/B - Bitumen laying (Final portion)	3d	06-Jul-15 A	08-Jul-15 A							
14958a	P1 W/B - Footpath (VO158) - Block fabrication and Site work	76d	01-Aug-15	31-Oct-15	-212d						
Man Yiu Street Northern Portion											
RFI453a	RFI 453 (Site Works)	199d	22-Nov-14 A	31-Jul-15	-212d						
RFI457a	RFI 457 (Site Works)	35d	27-Dec-14 A	31-Jul-15	-212d						
14962	MYS Nth - Footpath (VO/158) - Material approval & procurement	116d	10-Mar-15 A	31-Jul-15	-212d						
1514	MYS Nth - Drainage / Landscape (VO/192)	80d	04-Jun-15 A	31-Jul-15	-201d						
14962a	MYS Nth - Footpath (VO/158) - Block fabrication and Site work	76d	01-Aug-15	31-Oct-15	-212d						
VO134	VO134 - 29 Oct 2014	76d	01-Aug-15	31-Oct-15	-195d						
Man Yiu Street Southern Portion											

- Current Milestone
- Critical Remaining Work
- Level of Effort
- Remaining Work
- Baseline Milestone
- Project Baseline
- Actual Work


Leighton Contractors (Asia) Limited

Programme Update 58 (July 2015)

THREE MONTH ROLLING

Project ID: U058
 Baseline: DCP7-2c
 Layout: Update Three Month Rolling U058
 Page 1 of 5

Date	Revision	Checked	Appro...
20-Jun-15	U057	AT	BY
20-Jul-15	U058	AT	BY

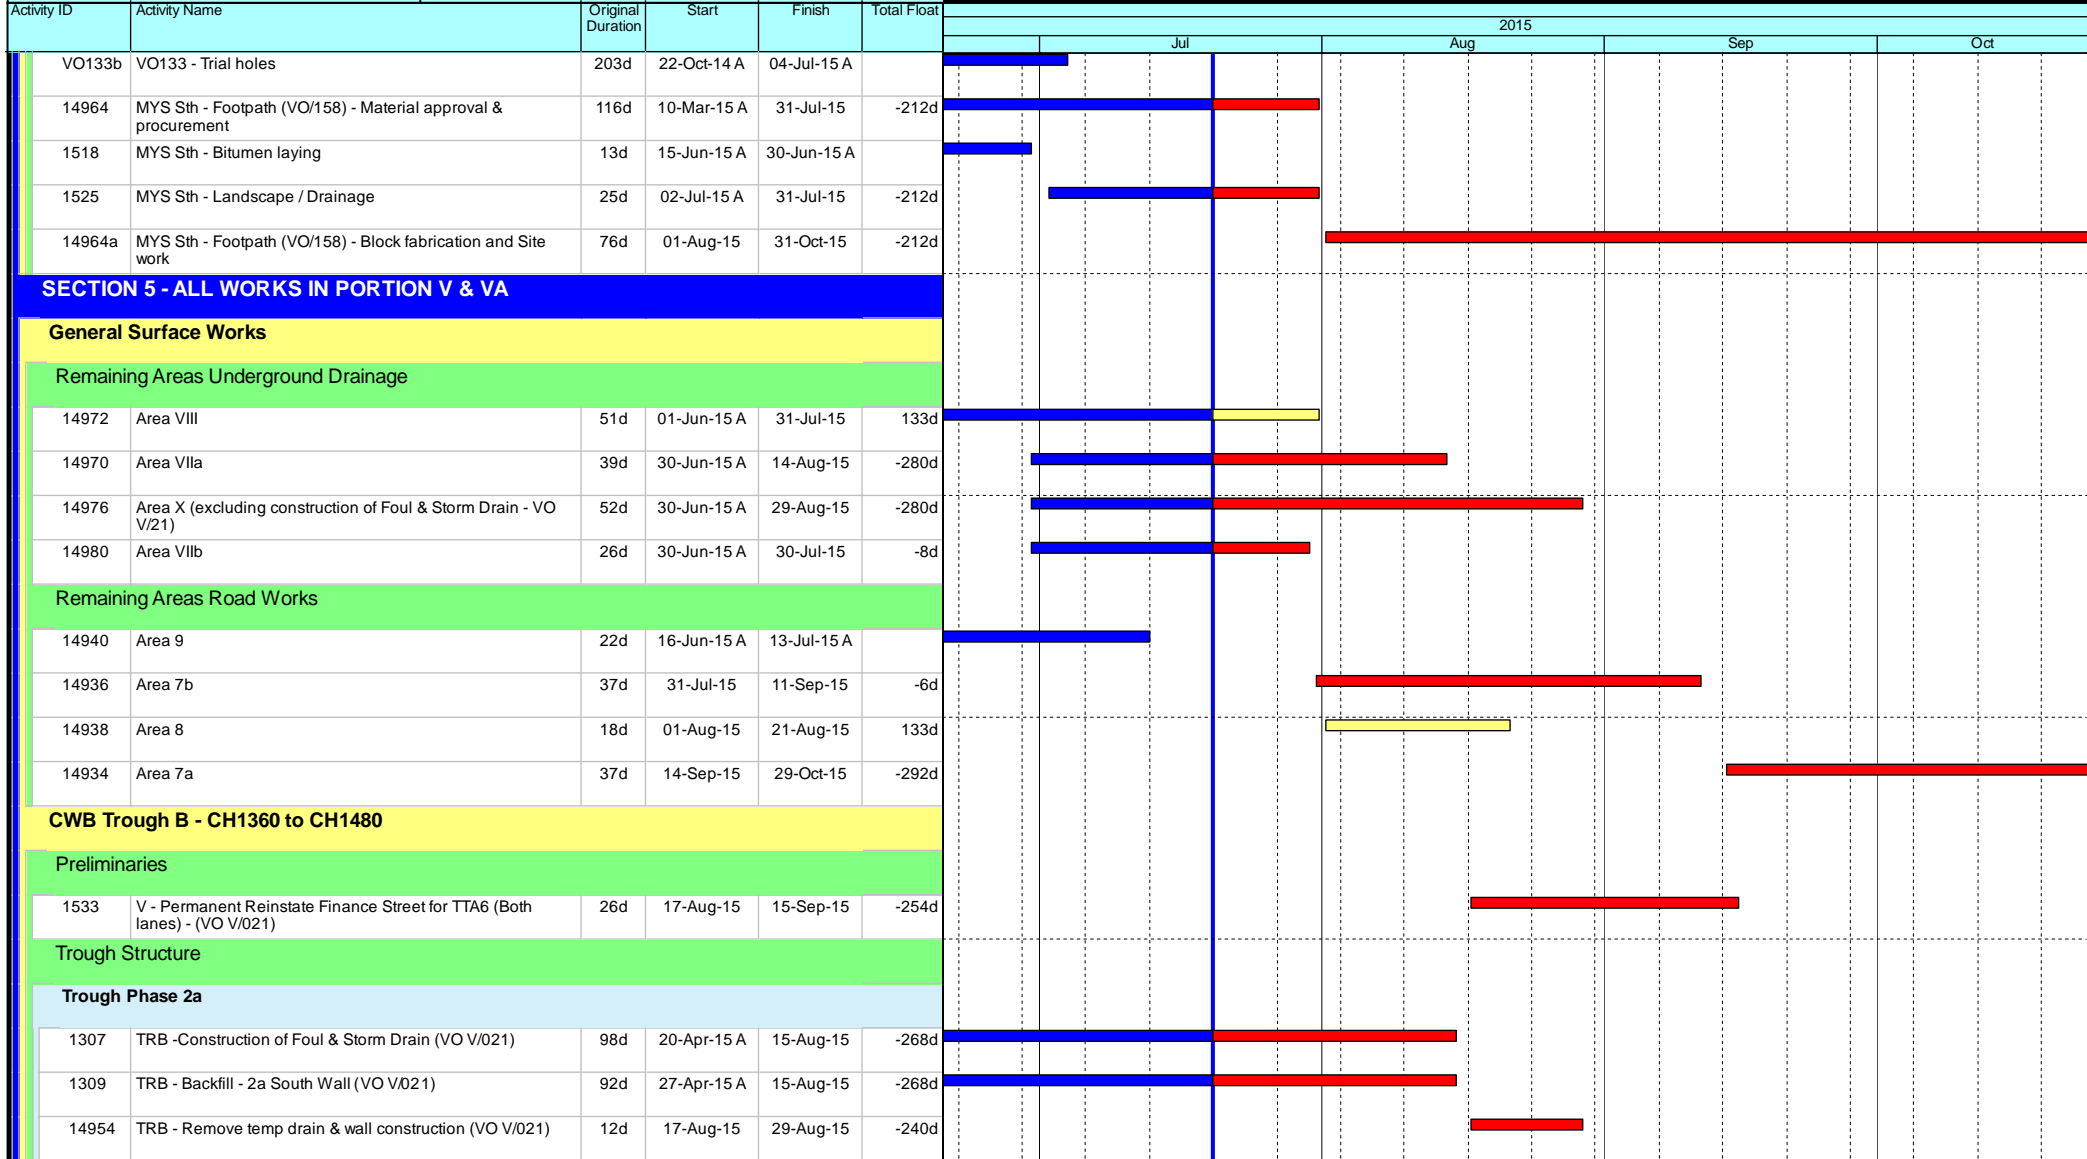

- Current Milestone
- Critical Remaining Work
- Level of Effort
- Remaining Work
- Baseline Milestone
- Project Baseline
- Actual Work


Leighton Contractors (Asia) Limited

Programme Update 58 (July 2015)

THREE MONTH ROLLING

Project ID: U058
 Baseline: DCP7-2c
 Layout: Update Three Month Rolling U058
 Page 2 of 5

Date	Revision	Checked	Appro...
20-Jun-15	U057	AT	BY
20-Jul-15	U058	AT	BY

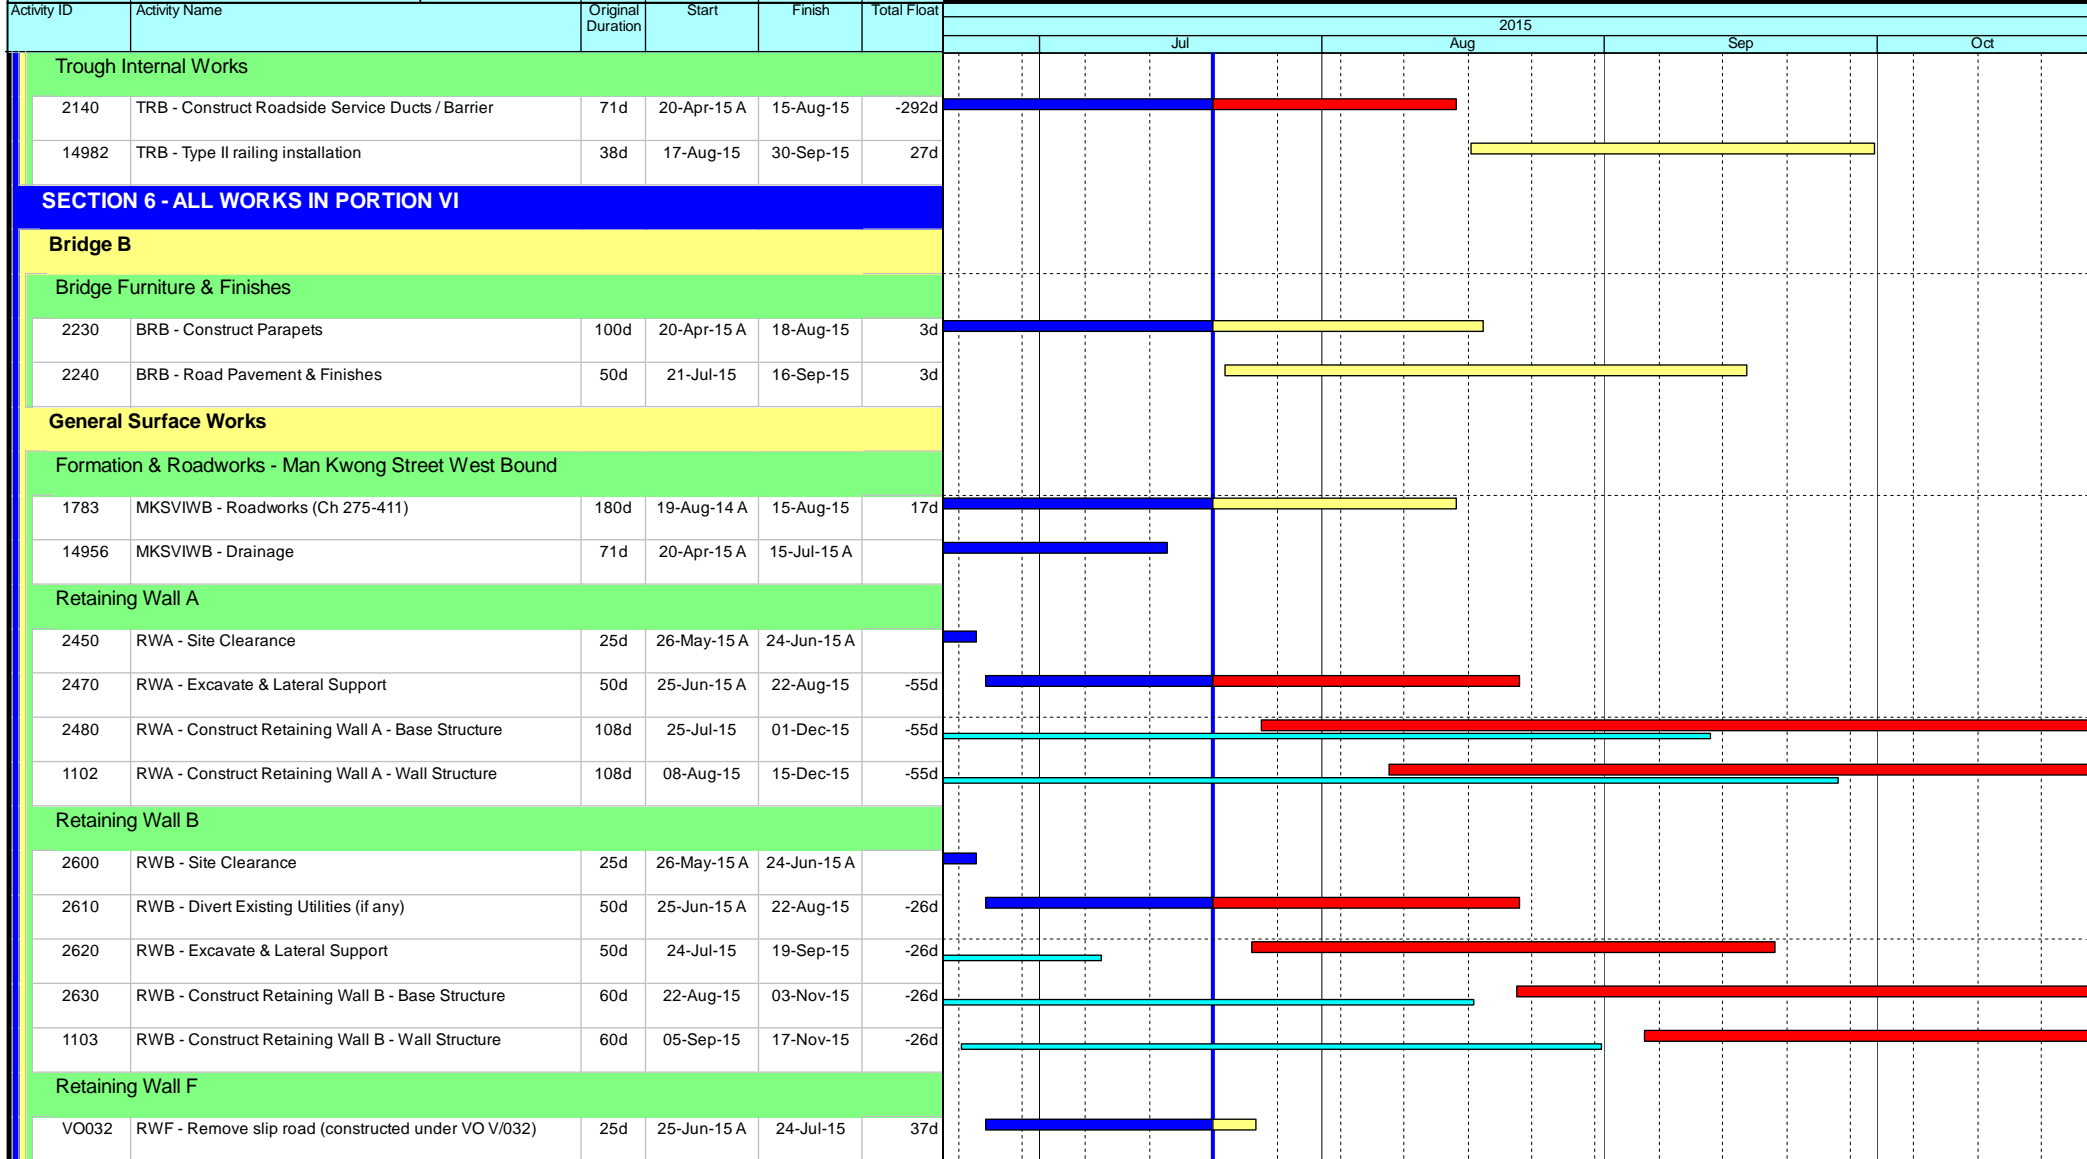

- Current Milestone
- Critical Remaining Work
- Level of Effort
- Remaining Work
- Baseline Milestone
- Project Baseline
- Actual Work

Leighton Contractors (Asia) Limited

Programme Update 58 (July 2015)

THREE MONTH ROLLING


Project ID: U058
 Baseline: DCP7-2c
 Layout: Update Three Month Rolling U058
 Page 3 of 5

Date	Revision	Checked	Appro...
20-Jun-15	U057	AT	BY
20-Jul-15	U058	AT	BY

Data Date: 20-Jul-15

HY/2009/18 Central - Wan Chai Bypass (Central Interchange)

TASK filters: 3 Months_1, Not HL.

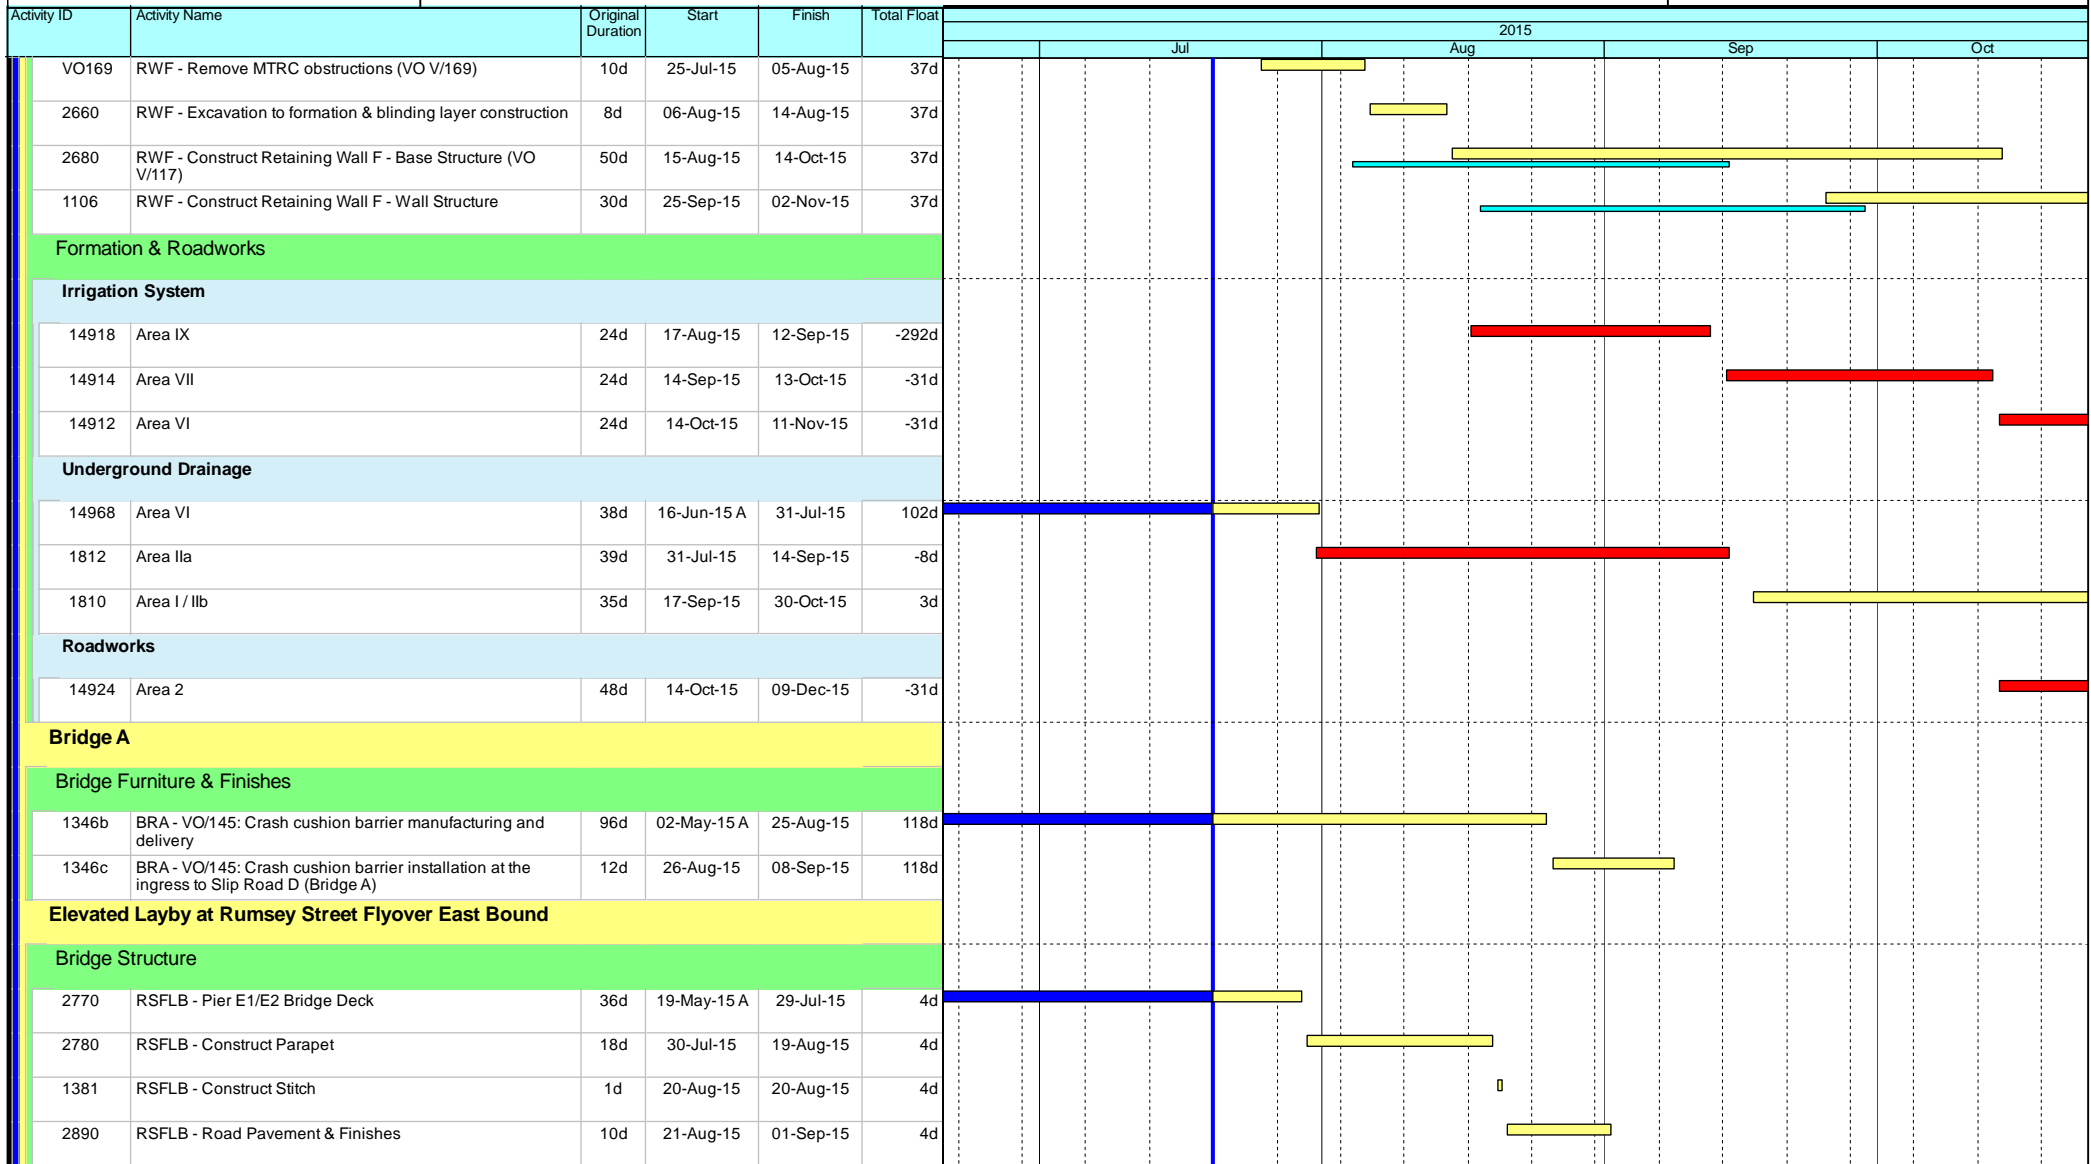

- ◆ Current Milestone
- Critical Remaining Work
- Level of Effort
- Remaining Work
- ▲ Baseline Milestone
- Project Baseline
- Actual Work

Leighton Contractors (Asia) Limited Programme Update 58 (July 2015) THREE MONTH ROLLING

Project ID: U058
 Baseline: DCP7-2c
 Layout: Update Three Month Rolling U058
 Page 4 of 5

Date	Revision	Checked	Appro...
20-Jun-15	U057	AT	BY
20-Jul-15	U058	AT	BY

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015																	
						Jul			Aug			Sep			Oct								
						1	2	3	1	2	3	1	2	3	1	2	3						
14984	RSFLB - Construction of sign gantries (FADS01)	40d	02-Sep-15	20-Oct-15	4d							[Remaining Work Bar]											
Key Dates for Completion of Sections																							
Anticipated Completion																							
1064	KD6 - Anticipated Completion	0d		15-Sep-15*	-316d																		
Portion Handover Dates																							
Anticipated Handover																							
2960	Portion IIIA Handover - Partial	0d		30-Jun-15 A																			

- ◆ Current Milestone
- Critical Remaining Work
- Level of Effort
- Remaining Work
- ▲ Baseline Milestone
- Project Baseline
- Actual Work

Leighton Contractors (Asia) Limited Programme Update 58 (July 2015) THREE MONTH ROLLING

Project ID: U058
 Baseline: DCP7-2c
 Layout: Update Three Month Rolling U058
 Page 5 of 5

Date	Revision	Checked	Appro...
20-Jun-15	U057	AT	BY
20-Jul-15	U058	AT	BY
