



Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	June 2015							July 2015							August 2015							September 2015							October 2015							November 2015							December 2015							January 2016							February 2016							March 2016							April 2016							May 2016							June 2016							July 2016							August 2016							September 2016						
					01	08	15	22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	01	08	15	22	29	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05	12	19																																											
<b>HK/2012/08 Revised Works Programme Rev.4_1(Final)</b>																																																																																																																				
<b>Works for Section Completion</b>																																																																																																																				
<b>Construction</b>																																																																																																																				
<b>Section II A - CWB Tunnel &amp; Slip Road Structures and Facilities</b>																																																																																																																				
<b>CWB CRIII &amp; A1</b>																																																																																																																				
<b>CWB CRIII &amp; A1 - Pumping Test Preparation/ Pumping Test</b>																																																																																																																				
CWB A1 - Pumping Testing Preparation																																																																																																																				
SIIA11240	Sec II A - CWB A1 - install dewater/ recharge / observation well	17	11-May-15 A	20-Jul-15																																																																																																																
CWB CRIII & A1 - Pumping Test																																																																																																																				
SIIA10780	Sec II A - CWB CRIII - pumping test (CRIII, A1)	10	20-Jul-15	30-Jul-15																																																																																																																
<b>CWB CRIII - ELS &amp; Tunnel Structure</b>																																																																																																																				
CWB CRIII - ELS																																																																																																																				
SIIA10820	Sec II A - CWB CRIII: Shoring & Excavation	42	18-Apr-15 A	18-Aug-15																																																																																																																
SIIA10960	Sec II A - CWB CRIII: Demolish Bulkhead at West End	45	19-Aug-15	12-Oct-15																																																																																																																
CWB CRIII - Tunnel Structure																																																																																																																				
SIIA10840	Sec II A - CWB CRIII: Base, wall, OHVD & roof (bay 1)	45	19-Aug-15	12-Oct-15																																																																																																																
SIIA10880	Sec II A - CWB CRIII: Base, wall, OHVD & roof (bay 3)	45	19-Aug-15	12-Oct-15																																																																																																																
<b>CWB A1 - ELS &amp; Tunnel Structure</b>																																																																																																																				
CWB A1 - ELS Remaining																																																																																																																				
SIIA11286	Sec IIA - CWB A1 : Shoring & Excavation (Remaining)	37	07-Jul-15	18-Aug-15																																																																																																																
CWB A1 - Tunnel Structure Remaining																																																																																																																				
SIIA13045	Sec II A - CWB A1: Pile head + trough + base & wall + OHVD unit (1st bay)	45	19-Aug-15	12-Oct-15																																																																																																																
CWB A1 - Other Works																																																																																																																				
SIIA15480	Culvert L - [Summary] Bay 9 to Bay 11 on top of CWB A1 and divert flow	27	08-Jun-15 A	31-Jul-15																																																																																																																
SIIA15500	Zone A2(2) - Public Fill -4.0 to +4.0mPD (behind Type 4 & 13 for temp channel outlet)	28	01-Aug-15	28-Aug-15																																																																																																																
<b>Section III - Road D11 &amp; Part of Road P2, Area 4, Implement 1st Stage ITA</b>																																																																																																																				
<b>Roadwork &amp; Utilities</b>																																																																																																																				
<b>General</b>																																																																																																																				
SIII10040	Sec III - roadwork & utilities - storm water drain & subsoil drain	121	01-May-15 A	21-Nov-15																																																																																																																
SIII10060	Sec III - roadwork & utilities - Watermain & Irrigation Mains	100	07-Jul-15*	03-Nov-15																																																																																																																
SIII10080	Sec III - roadwork & utilities - gas main and valve chamber	100	17-Jul-15	13-Nov-15																																																																																																																
SIII10100	Sec III - roadwork & utilities - HEC cable duct and catchpit	100	27-Jul-15	23-Nov-15																																																																																																																
SIII10120	Sec III - roadwork & utilities - sub-base	100	06-Aug-15	03-Dec-15																																																																																																																
SIII10140	Sec III - roadwork & utilities - Road kerb	100	15-Aug-15	12-Dec-15																																																																																																																
SIII10160	Sec III - roadwork & utilities - flexible pavement	100	26-Aug-15	23-Dec-15																																																																																																																

Data Date: 30-Jun-15

- Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Remaining Level of Effort

**Works Programme for Zone CRIII (June to August 2015)**

Date	Revision	Checked	Approved
03-Jul-15			



CEDD Contract No. HK/2012/08  
Wan Chai Development Phase II  
Central -Wan Chai Bypass at Wan Chai West

Activity ID	Activity Name	Start	Finish	Remaining Duration	Activity % Complete	2015					2016
						Sep	Oct	Nov	Dec	Jan	
<b>Total</b>		18-Apr-15 A	29-Dec-15	81							
<b>HK/2012/08 Revised Works Programme Rev.5_Updated as of 20-Sep-15</b>		18-Apr-15 A	29-Dec-15	81							
<b>Dredging and Reclamation</b>		20-Sep-15	10-Dec-15	67							
<b>Marine Work Construction</b>		20-Sep-15	10-Dec-15	67							
<b>Zone CRIII</b>		20-Sep-15	10-Dec-15	67							
<b>Dredging - Zone CRIII</b>		20-Sep-15	10-Oct-15	16							
<b>Dredging at Zone CRIII</b>		20-Sep-15	10-Oct-15	16							
<b>2nd Stage of Work (Types 1B(4) &amp; 2D)</b>		20-Sep-15	10-Oct-15	16							
MAR16095	Zone CRIII - 2nd stage - Remove existing rock armour [B5-E5] after relocating interim landing steps	20-Sep-15	29-Sep-15	10	0%						
MAR16100	Zone CRIII - 2nd stage - demolish existing seawall [3 nos.]	02-Oct-15	10-Oct-15	8	0%						
MAR16140	Zone CRIII - 2nd stage - Final Hydrographic Survey	21-Sep-15	22-Sep-15	2	0%						
<b>Seawall Construction - Zone CRIII</b>		21-Sep-15	30-Nov-15	58							
<b>Zone CRIII Seawall (1st Stage)</b>		21-Sep-15	17-Oct-15	22							
<b>Seawall 2 &amp; 12</b>		21-Sep-15	17-Oct-15	22							
MAR20580	Zone CRIII - fill rock mound for Seawall 2 & 12 and Trimming	21-Sep-15	29-Sep-15	7	0%						
MAR20600	Zone CRIII - lay toe block and level stone for Seawall 2 & 12	29-Sep-15	13-Oct-15	12	0%						
MAR21250	Zone CRIII - install block seawall 12	09-Oct-15	14-Oct-15	5	0%						
MAR21251	Zone CRIII - install block seawall 2	14-Oct-15	17-Oct-15	4	0%						
<b>Zone CRIII Seawall (2nd Stage)</b>		17-Oct-15	30-Nov-15	37							
<b>Seawall 1B(4)</b>		17-Oct-15	09-Nov-15	19							
MAR21257	Zone CRIII - fill rock mound for Seawall 1B(4)	17-Oct-15	24-Oct-15	6	0%						
MAR21259	Zone CRIII - lay toe block and level stone for Seawall 1B(4)	26-Oct-15	07-Nov-15	12	0%						
MAR21275	Zone CRIII - deliver and install caisson seawall 1B(4)	08-Nov-15	09-Nov-15	2	0%						
<b>Seawall 2D</b>		17-Oct-15	10-Nov-15	20							
MAR21262	Zone CRIII - fill rock mound for Seawall 2D	17-Oct-15	24-Oct-15	6	0%						
MAR21264	Zone CRIII - lay toe block and level stone for Seawall 2D	26-Oct-15	07-Nov-15	12	0%						
MAR21320	Zone CRIII - deliver and install caisson seawall 2D	09-Nov-15	10-Nov-15	2	0%						
<b>Seawall 1</b>		11-Nov-15	30-Nov-15	17							
MAR21265	Zone CRIII - fill rock mound for Seawall 1	11-Nov-15	14-Nov-15	4	0%						
MAR21266	Zone CRIII - lay toe block and level stone for Seawall 1	16-Nov-15	23-Nov-15	7	0%						
MAR21340	Zone CRIII - install block seawall 1	24-Nov-15	30-Nov-15	6	0%						
<b>Filling - Zone CRIII</b>		19-Oct-15	10-Dec-15	45							
MAR10460	Zone CRIII - general fill to +4.0mPD	19-Oct-15	10-Dec-15	45	0%						

- █ Remaining Level of Effort
- █ Actual Level of Effort
- ▬ Remaining Work
- ▬ Actual Work
- ▬ Critical Remaining Work

Project Star :22-Jan-13  
Project End: 21-Jul-18  
Date Date: 20-Sep-15

**3 Months Rolling Programme \_September to November 2015**  
(For CRIII Zone)

Detailed Works Programme Revision 5			
Date	Revision	Checked	Approved
20-Sep-15	3MRP		

CEDD Contract No. HK/2012/08  
Wan Chai Development Phase II  
Central -Wan Chai Bypass at Wan Chai West

Activity ID	Activity Name	Start	Finish	Remaining Duration	Activity % Complete	2015					2016
						Sep	Oct	Nov	Dec	Jan	
<b>Works for Section Completion</b>											
<b>Construction</b>											
<b>Section II A - CWB Tunnel &amp; Slip Road Structures and Facilities</b>											
<b>CWB CRIII &amp; A1</b>											
<b>CWB CRIII &amp; A1 - Pumping Test Preparation/ Pumping Test</b>											
<b>CWB CRIII &amp; A1 - Pumping Test</b>											
SIIA10780	Sec II A - CWB CRIII - pumping test (CRIII, A1)	21-Sep-15	29-Sep-15	7	0%		■				
<b>CWB CRIII - ELS &amp; Tunnel Structure</b>											
<b>CWB CRIII - ELS</b>											
SIIA10820	Sec II A - CWB CRIII: Shoring & Excavation	18-Apr-15 A	03-Nov-15	35	58.82%	■	■	■			
SIIA10960	Sec II A - CWB CRIII: Demolish Bulkhead at West End	04-Nov-15	28-Dec-15	45	0%				■	■	
<b>CWB CRIII - Tunnel Structure</b>											
SIIA10840	Sec II A - CWB CRIII: Base, wall, OHVD & roof (bay 1)	04-Nov-15	28-Dec-15	45	0%				■	■	
SIIA10880	Sec II A - CWB CRIII: Base, wall, OHVD & roof (bay 3)	04-Nov-15	28-Dec-15	45	0%				■	■	
<b>Section III - Road D11 &amp; Part of Road P2, Area 4, Implement 1st Stage ITA</b>											
<b>Roadwork &amp; Utilities</b>											
<b>General</b>											
SIII10060	Sec III - roadwork & utilities - Watermain & Irrigation Mains	07-Jul-15 A	29-Dec-15	81	10%	■	■	■	■	■	

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015			
						Aug	Sep	Oct	Nov
<b>Update 2015-08-20 CWB - Central Interchange (2014-06-20) Revised DWP R7 with RFI</b>									
<b>SECTION 3 - REMAINING WORKS IN PORTION IIIA &amp; IIIB</b>									
<b>Surface Works - East of Man Yiu Street</b>									
<b>Road P1</b>									
<b>P1 Road East Bound</b>									
VO089f	VO089 - Maintenance Section 1	906d	31-Jul-12 A	31-Aug-15	-162d	[Gantt bar: blue from 31-Jul-12 to 31-Aug-15, red from 31-Jul-12 to 31-Aug-15]			
VO089i	VO089 - Maintenance Section 2	299d	25-Aug-14 A	31-Aug-15	-162d	[Gantt bar: blue from 25-Aug-14 to 31-Aug-15, red from 25-Aug-14 to 31-Aug-15]			
VO175a	VO175	240d	06-Oct-14 A	01-Sep-15	-163d	[Gantt bar: blue from 06-Oct-14 to 01-Sep-15, red from 06-Oct-14 to 01-Sep-15]			
14960	P1 E/B - Footpath (VO158) - Material approval & procurement	116d	10-Mar-15 A	12-Aug-15 A		[Gantt bar: blue from 10-Mar-15 to 12-Aug-15]			
14904	P1 E/B - Street Furniture / Sign (VO/192)	75d	27-Mar-15 A	30-Sep-15	-187d	[Gantt bar: blue from 27-Mar-15 to 30-Sep-15, red from 27-Mar-15 to 30-Sep-15]			
14960a	P1 E/B - Footpath (VO158) - Block fabrication and Site work	76d	14-Aug-15 A	31-Oct-15	-212d	[Gantt bar: blue from 14-Aug-15 to 31-Oct-15, red from 14-Aug-15 to 31-Oct-15]			
<b>P1 Road West Bound</b>									
VO089b	VO089 - Maintenance Section 1	906d	31-Jul-12 A	31-Aug-15	-162d	[Gantt bar: blue from 31-Jul-12 to 31-Aug-15, red from 31-Jul-12 to 31-Aug-15]			
VO089d	VO089 - Maintenance Section 2	299d	25-Aug-14 A	31-Aug-15	-162d	[Gantt bar: blue from 25-Aug-14 to 31-Aug-15, red from 25-Aug-14 to 31-Aug-15]			
VO175b	VO175	240d	06-Oct-14 A	31-Jul-15 A		[Gantt bar: blue from 06-Oct-14 to 31-Jul-15]			
14958	P1 W/B - Footpath (VO158) - Material approval & procurement	116d	10-Mar-15 A	12-Aug-15 A		[Gantt bar: blue from 10-Mar-15 to 12-Aug-15]			
1520	P1 W/B - U Channel / Landscape works / Drainage (VO/192)	25d	01-Jun-15 A	31-Jul-15 A		[Gantt bar: blue from 01-Jun-15 to 31-Jul-15]			
14958a	P1 W/B - Footpath (VO158) - Block fabrication and Site work	76d	14-Aug-15 A	31-Oct-15	-212d	[Gantt bar: blue from 14-Aug-15 to 31-Oct-15, red from 14-Aug-15 to 31-Oct-15]			
<b>Man Yiu Street Northern Portion</b>									
VO175c	VO175	240d	06-Oct-14 A	01-Sep-15	-163d	[Gantt bar: blue from 06-Oct-14 to 01-Sep-15, red from 06-Oct-14 to 01-Sep-15]			
RFI453a	RFI 453 (Site Works)	199d	22-Nov-14 A	31-Jul-15 A		[Gantt bar: blue from 22-Nov-14 to 31-Jul-15]			
RFI457a	RFI 457 (Site Works)	35d	27-Dec-14 A	31-Jul-15 A		[Gantt bar: blue from 27-Dec-14 to 31-Jul-15]			
14962	MYS Nth - Footpath (VO/158 and VO/153) - Material approval & procurement	116d	10-Mar-15 A	12-Aug-15 A		[Gantt bar: blue from 10-Mar-15 to 12-Aug-15]			
1514	MYS Nth - Drainage / Landscape (VO/192)	80d	04-Jun-15 A	19-Sep-15	-212d	[Gantt bar: blue from 04-Jun-15 to 19-Sep-15, red from 04-Jun-15 to 19-Sep-15]			
14962a	MYS Nth - Footpath (VO/158) - Block fabrication and Site work	76d	14-Aug-15 A	31-Oct-15	-212d	[Gantt bar: blue from 14-Aug-15 to 31-Oct-15, red from 14-Aug-15 to 31-Oct-15]			

- ◆ Current Milestone
- Critical Remaining Work
- Level of Effort
- Remaining Work
- ▲ Baseline Milestone
- Project Baseline
- Actual Work

### Leighton Contractors (Asia) Limited

### Programme Update 58 (July 2015)

### THREE MONTH ROLLING

Project ID: U059a  
 Baseline: DCP7-2c  
 Layout: Update Three Month Rolling U059  
 Page 1 of 5

Date	Revision	Checked	Appro...
20-Jun-15	U057	AT	BY
20-Jul-15	U058	AT	BY

Data Date: 20-Aug-15

# HY/2009/18 Central - Wan Chai Bypass (Central Interchange)

TASK filters: 3 Months\_1, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015			
						Aug	Sep	Oct	Nov
VO134	VO134 - 29 Oct 2014	33d	21-Sep-15	31-Oct-15	-171d				
<b>Man Yiu Street Southern Portion</b>									
VO175d	VO175	240d	06-Oct-14 A	01-Sep-15	-163d				
14964	MYS Sth - Footpath (VO/158) - Material approval & procurement	116d	10-Mar-15 A	12-Aug-15 A					
1525	MYS Sth - Landscape / Drainage	25d	02-Jul-15 A	31-Jul-15 A					
14964a	MYS Sth - Footpath (VO/158) - Block fabrication and Site work	76d	14-Aug-15 A	31-Oct-15	-212d				
<b>SECTION 5 - ALL WORKS IN PORTION V &amp; VA</b>									
<b>General Surface Works</b>									
<b>Remaining Areas Underground Drainage</b>									
14972	Area VIII	51d	01-Jun-15 A	12-Aug-15 A					
14970	Area VIIa	39d	30-Jun-15 A	15-Sep-15	-294d				
14980	Area VIIb	26d	20-Aug-15	18-Sep-15	-82d				
14976	Area X (excluding construction of Foul & Storm Drain - VO V/21)	37d	16-Sep-15	31-Oct-15	-294d				
<b>Remaining Areas Road Works</b>									
14938	Area 8	18d	12-Aug-15 A	07-Sep-15	119d				
14934	Area 7a	37d	16-Sep-15	31-Oct-15	-294d				
14936	Area 7b	34d	19-Sep-15	31-Oct-15	-77d				
<b>CWB Trough B - CH1360 to CH1480</b>									
<b>Preliminaries</b>									
1533	V - Permanent Reinstatement Finance Street for TTA6 (Both lanes) - (VO V/021)	26d	16-Sep-15	17-Oct-15	-280d				
<b>Trough Structure</b>									
<b>Trough Phase 2a</b>									
1307	TRB - Construction of Foul & Storm Drain (VO V/021) - 19 days delay by CC steel pipe & 6 days inclement weather	98d	20-Apr-15 A	15-Sep-15	-280d				
1309	TRB - Backfill - 2a South Wall (VO V/021) - 19 days delay by CC steel pipe & 6 days inclement weather	92d	27-Apr-15 A	15-Sep-15	-271d				
14954	TRB - Remove temp drain & wall construction (VO V/021) - 19 days delay by CC steel pipe & 6 days inclement weather	26d	17-Aug-15 A	15-Sep-15	-254d				

- ◆ Current Milestone
- Critical Remaining Work
- Level of Effort
- Remaining Work
- ▲ Baseline Milestone
- Project Baseline
- Actual Work

## Leighton Contractors (Asia) Limited Programme Update 58 (July 2015) THREE MONTH ROLLING



Project ID: U059a  
Baseline: DCP7-2c  
Layout: Update Three Month Rolling U059  
Page 2 of 5

Date	Revision	Checked	Appro...
20-Jun-15	U057	AT	BY
20-Jul-15	U058	AT	BY

Data Date: 20-Aug-15

# HY/2009/18 Central - Wan Chai Bypass (Central Interchange)

TASK filters: 3 Months\_1, Not HL.

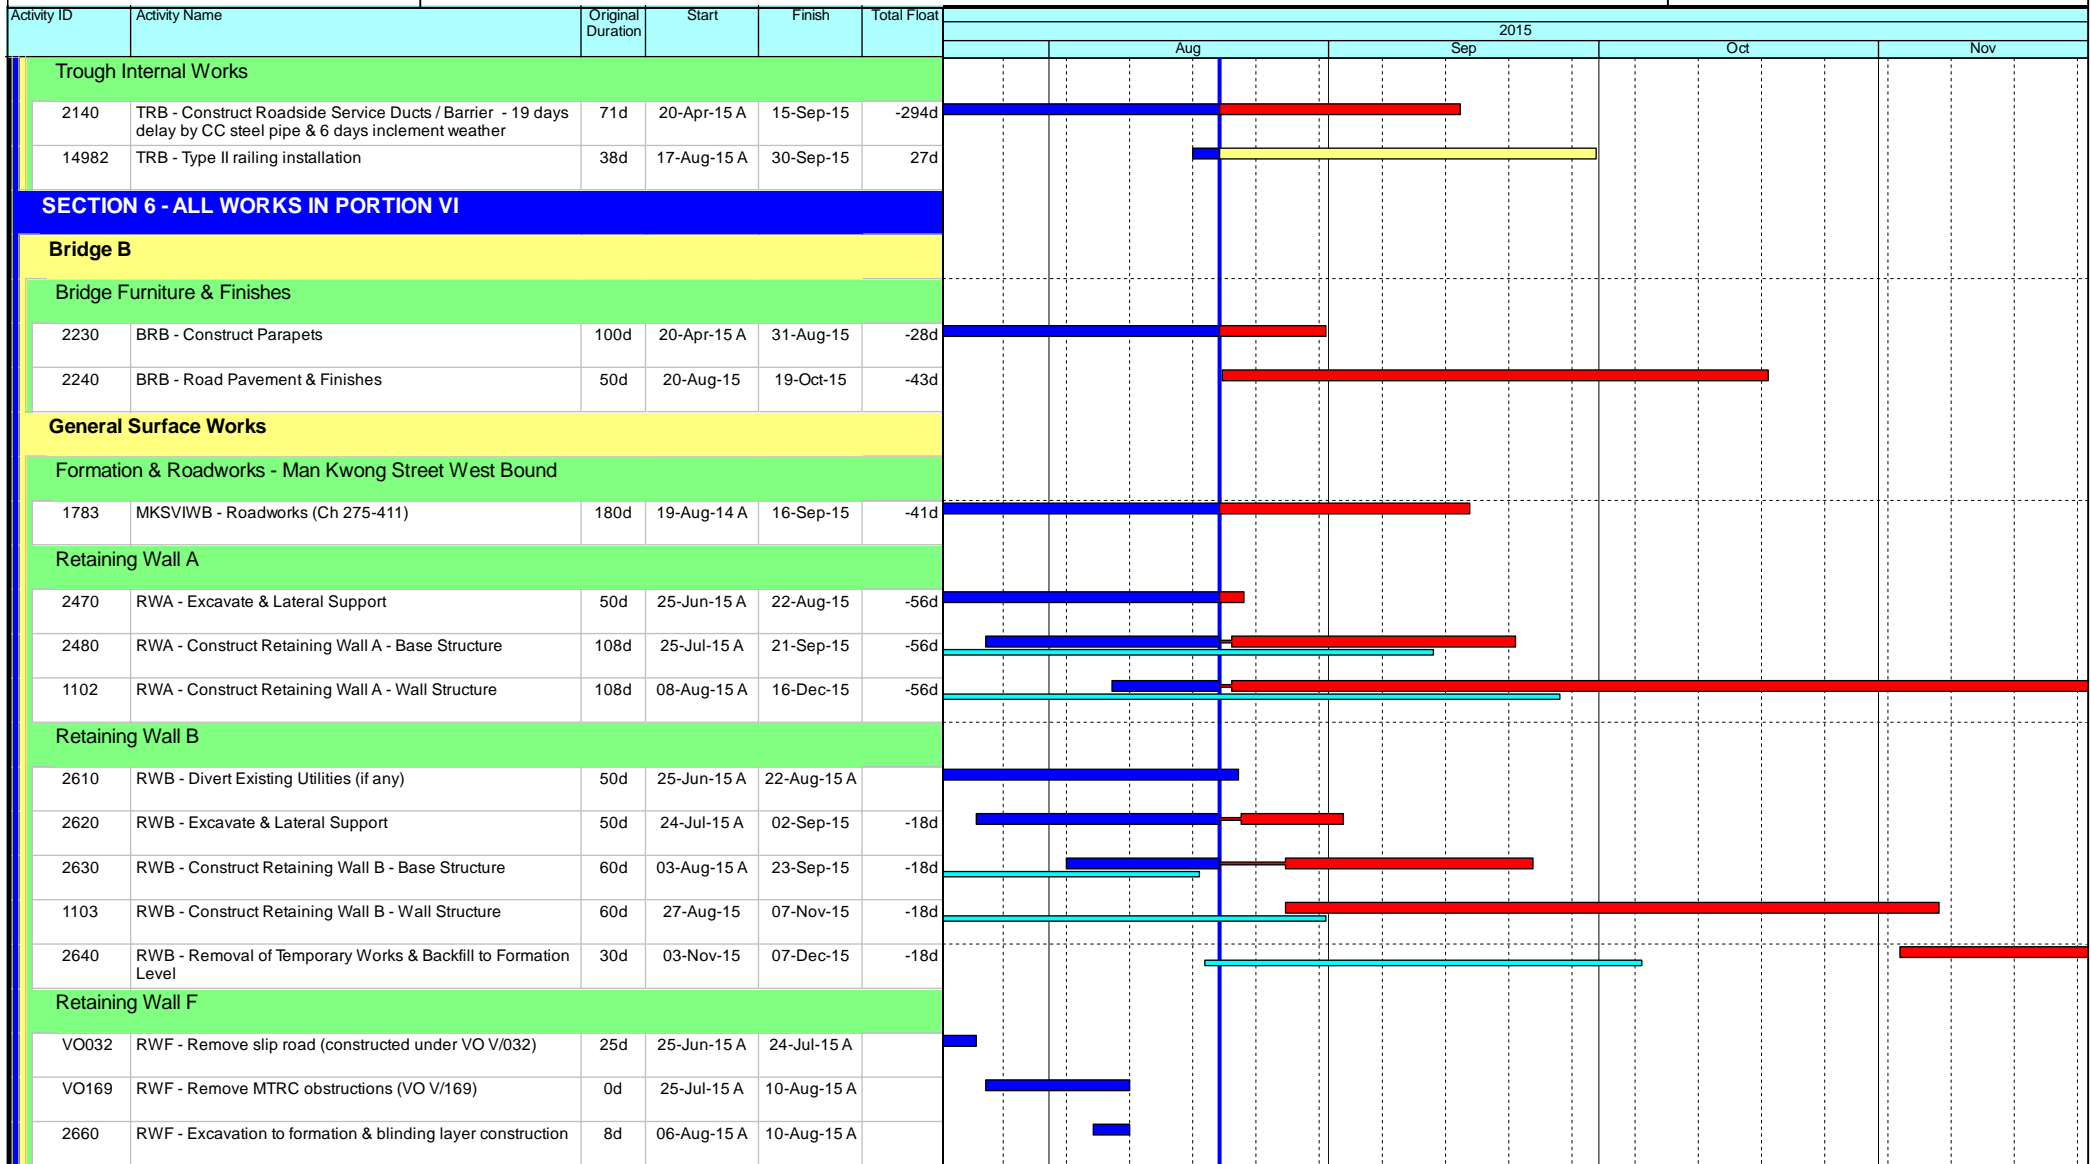

## Leighton Contractors (Asia) Limited Programme Update 58 (July 2015) THREE MONTH ROLLING



Project ID: U059a  
Baseline: DCP7-2c  
Layout: Update Three Month Rolling U059  
Page 3 of 5

Date	Revision	Checked	Appro...
20-Jun-15	U057	AT	BY
20-Jul-15	U058	AT	BY

Data Date: 20-Aug-15

# HY/2009/18 Central - Wan Chai Bypass (Central Interchange)

TASK filters: 3 Months\_1, Not HL.

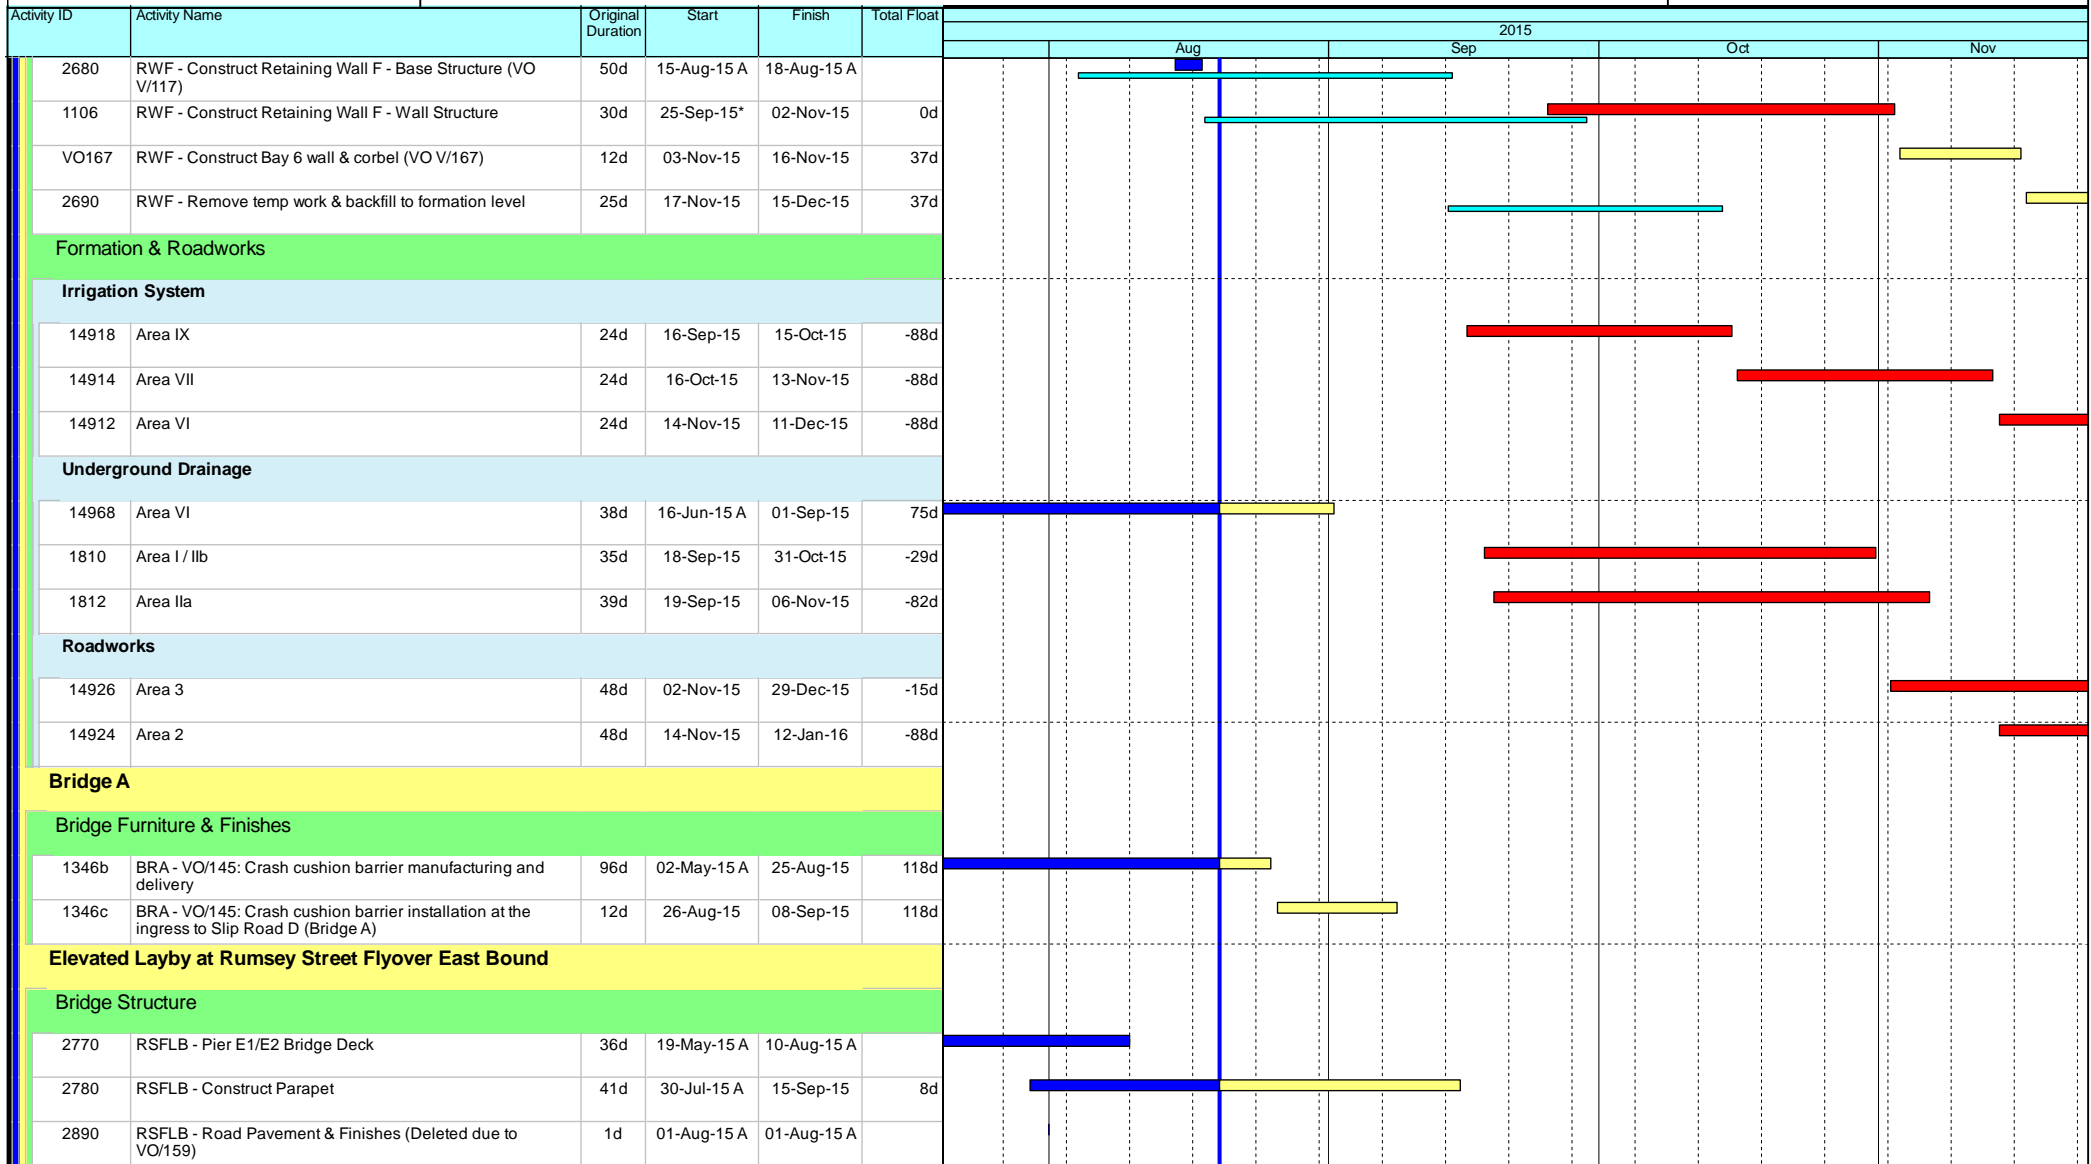

## Leighton Contractors (Asia) Limited Programme Update 58 (July 2015) THREE MONTH ROLLING

Project ID: U059a  
Baseline: DCP7-2c  
Layout: Update Three Month Rolling U059  
Page 4 of 5

Date	Revision	Checked	Appro...
20-Jun-15	U057	AT	BY
20-Jul-15	U058	AT	BY



Data Date: 20-Aug-15

# HY/2009/18 Central - Wan Chai Bypass (Central Interchange)

TASK filters: 3 Months\_1, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015			
						Aug	Sep	Oct	Nov
VO176_1	VO176 / VO190 - Rumsey Street Flyover (TTA)	14d	20-Aug-15	04-Sep-15	10d	[Yellow bar from Aug 20 to Sep 04]			
VO176_1	VO176 / VO190 - Rumsey Street Flyover (Noise Permit for night work)	24d	05-Sep-15	05-Oct-15	10d	[Yellow bar from Sep 05 to Oct 05]			
VO176_1	VO176 / VO190 - Rumsey Street Flyover (Soffit & parapet edge - night work) (@8m/night shift)	15d	06-Oct-15	23-Oct-15	10d	[Yellow bar from Oct 06 to Oct 23]			
1381	RSFLB - Construct Stitch	1d	15-Oct-15	15-Oct-15	8d	[Small yellow bar on Oct 15]			
14984	RSFLB - Construction of sign gantries (FADS01)	40d	16-Oct-15	02-Dec-15	8d	[Yellow bar from Oct 16 to Dec 02]			
VO176_1	VO176 / VO190 - Rumsey Street Flyover (Central Barrier-night work) (@8m/night shift)	72d	24-Oct-15	19-Jan-16	10d	[Yellow bar from Oct 24 to Jan 19]			
<b>SECTION 7, 7A, 7B &amp; 7C - LANDSCAPE ESTABLISHMENT</b>									
4000	EST - Portion IIIA Landscape Establishment	365d	01-Nov-15	30-Oct-16	-267d	[Red bar from Nov 01 to Oct 30]			
4030	EST - Portion V Landscape Establishment	365d	05-Nov-15	03-Nov-16	-366d	[Red bar from Nov 05 to Nov 03]			
<b>Key Dates for Completion of Sections</b>									
<b>Anticipated Completion</b>									
1064	KD6 - Anticipated Completion	0d		17-Oct-15*	-348d	[Blue diamond on Oct 17]			
<b>Contract Required Completion</b>									
1095	KD12 - Section 7A Complete (DAY-1870)	0d		03-Nov-15*	0d	[Blue triangle on Nov 03]			
1105	KD14 - Section 7B Complete (DAY-1870)	0d		03-Nov-15*	0d	[Blue triangle on Nov 03]			
<b>Portion Handover Dates</b>									
<b>Anticipated Handover</b>									
2960a	Portion IIIA Handover - Remaining (KD3 + 28 days) - (EOT 26.5 days added)	0d		31-Oct-15*	-212d	[Blue diamond on Oct 31]			

- ◆ Current Milestone
- Critical Remaining Work
- Level of Effort
- Remaining Work
- ▲ Baseline Milestone
- Project Baseline
- Actual Work

## Leighton Contractors (Asia) Limited Programme Update 58 (July 2015) THREE MONTH ROLLING

Project ID: U059a  
 Baseline: DCP7-2c  
 Layout: Update Three Month Rolling U059  
 Page 5 of 5

Date	Revision	Checked	Appro...
20-Jun-15	U057	AT	BY
20-Jul-15	U058	AT	BY

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015				2016		
						Oct	Nov	Dec	Jan			
<b>Update 2015-10-20 CWB - Central Interchange (2014-06-20) Revised DWP R7 with RFI</b>												
<b>SECTION 3 - REMAINING WORKS IN PORTION IIIA &amp; IIIB</b>												
<b>Surface Works - East of Man Yiu Street</b>												
<b>Road P1</b>												
<b>P1 Road East Bound</b>												
14904	P1 E/B - Street Furniture / Sign (VO/192)	75d	27-Mar-15 A	14-Nov-15	-224d							
14960a	P1 E/B - Footpath (VO158) - Block fabrication and Site work	76d	14-Aug-15 A	27-Nov-15	-235d							
<b>P1 Road West Bound</b>												
14958a	P1 W/B - Footpath (VO158) - Block fabrication and Site work	76d	14-Aug-15 A	19-Oct-15 A								
<b>Man Yiu Street Northern Portion</b>												
1514	MYS Nth - Drainage / Landscape (VO/192)	80d	04-Jun-15 A	29-Oct-15	-235d							
14962a	MYS Nth - Footpath (VO/158) - Block fabrication and Site work	76d	14-Aug-15 A	27-Nov-15	-235d							
VO134	VO134 - 29 Oct 2014	33d	21-Sep-15 A	19-Oct-15 A								
VO171a	VO171 - Addition of Traffic Signs at Man Yiu Street	2d	14-Nov-15*	16-Nov-15	-196d							
VO185a	VO185 - Revised Footing Details for Traffic Sign ADS4 at MYS	12d	17-Nov-15*	30-Nov-15	-196d							
<b>Man Yiu Street Southern Portion</b>												
14964a	MYS Sth - Footpath (VO/158) - Block fabrication and Site work	76d	14-Aug-15 A	19-Oct-15 A								
VO171b	VO171 - Addition of Traffic Signs at Man Yiu Street	2d	28-Nov-15*	30-Nov-15	-196d							
<b>SECTION 4 - REMAINING WORKS IN PORTION IVA, IVD, IVE &amp; IVG</b>												
<b>CWB Tunnel - CH1646 to CH1685 (Man Yiu Street)</b>												
<b>Formation &amp; Roadworks</b>												
VO153	VO153 (Dated 09 Feb 2015) - Re-alignment of Existing Tactile Paving along PTI	12d	02-Nov-15*	14-Nov-15	-10d							
<b>SECTION 5 - ALL WORKS IN PORTION V &amp; VA</b>												
<b>General Surface Works</b>												
<b>Remaining Areas Underground Drainage</b>												

- Current Milestone
- Critical Remaining Work
- Level of Effort
- Remaining Work
- Baseline Milestone
- Project Baseline
- Actual Work

**Leighton Contractors (Asia) Limited**  
**Programme Update 61 (October 2015)**  
**THREE MONTH ROLLING**

Project ID: U061  
 Baseline: DCP7-2c  
 Layout: Update Three Month Rolling U061  
 Page 1 of 5

Date	Revision	Checked	Appro...
20-Sep-15	U060	AT	BY
20-Oct-15	U061	AT	AL

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015				2016	
						Oct	Nov	Dec	Jan		
14976	Area X (excluding construction of Foul & Storm Drain - VO V/21)	37d	16-Sep-15 A	27-Nov-15	-317d						
<b>Remaining Areas Road Works</b>											
14934	Area 7a	37d	16-Sep-15 A	27-Nov-15	-317d						
14936	Area 7b	34d	19-Sep-15 A	27-Nov-15	-58d						
<b>CWB Trough B - CH1360 to CH1480</b>											
<b>Preliminaries</b>											
VO148	VO148 - Revision of Planter between Man Po Street and Finance Street	12d	12-Oct-15 A	26-Oct-15	7d						
<b>Trough Structure</b>											
<b>Trough Phase 2a</b>											
1307	TRB - Construction of Foul & Storm Drain (VO V/021) - 19 days delay by CC steel pipe & 6 days inclement weather	98d	20-Apr-15 A	14-Nov-15	-285d						
1309	TRB - Backfill - 2a South Wall (VO V/021) - 19 days delay by CC steel pipe & 6 days inclement weather	92d	27-Apr-15 A	14-Nov-15	-285d						
14954	TRB - Remove temp drain & wall construction (VO V/021) - 19 days delay by CC steel pipe & 6 days inclement weather	26d	17-Aug-15 A	26-Sep-15 A							
VO163	VO163 - CCTV Inspection of Existing Downstream Pipe to Manhole SMH7032208	2d	20-Oct-15*	22-Oct-15	10d						
<b>Trough Internal Works</b>											
2140	TRB - Construct Roadside Service Ducts / Barrier - 19 days delay by CC steel pipe & 6 days inclement weather	71d	20-Apr-15 A	26-Nov-15	-316d						
14982	TRB - Type II railing installation	38d	17-Aug-15 A	14-Nov-15	-10d						
VO177	VO177 - Emergency Access Gate at Trough Structure B	6d	23-Nov-15*	28-Nov-15	-22d						
VO174	VO174 - Revised Details of Roadside Barrier at Trough B	12d	02-Dec-15*	15-Dec-15	-36d						
<b>SECTION 6 - ALL WORKS IN PORTION VI</b>											
<b>Bridge B</b>											
<b>Bridge Furniture &amp; Finishes</b>											
2240	BRB - Road Pavement & Finishes	50d	23-Nov-15*	22-Jan-16	-41d						
<b>General Surface Works</b>											
<b>Formation &amp; Roadworks - Man Kwong Street West Bound</b>											
1783	MKSVIWB - Roadworks (Ch 275-411)	180d	19-Aug-14 A	20-Nov-15	-46d						

- Current Milestone
- Critical Remaining Work
- Level of Effort
- Remaining Work
- Baseline Milestone
- Project Baseline
- Actual Work

### Leighton Contractors (Asia) Limited

## Programme Update 61 (October 2015)

# THREE MONTH ROLLING

Project ID: U061  
 Baseline: DCP7-2c  
 Layout: Update Three Month Rolling U061  
 Page 2 of 5

Date	Revision	Checked	Appro...
20-Sep-15	U060	AT	BY
20-Oct-15	U061	AT	AL

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015				2016
						Oct	Nov	Dec	Jan	
<b>Retaining Wall A</b>										
2470	RWA - Excavate & Lateral Support	50d	25-Jun-15 A	23-Sep-15 A						
2480	RWA - Construct Retaining Wall A - Base Structure	108d	25-Jul-15 A	10-Nov-15	-56d					
1102	RWA - Construct Retaining Wall A - Wall Structure	108d	08-Aug-15 A	16-Dec-15	-56d					
2490	RWA - Removal of Temporary Works and Backfill to Formation Level	30d	17-Dec-15	23-Jan-16	-56d					
VO196b	VO196 (Dated 24 Jun 2015) - Re-provision of Drainage System for the Construction of Retaining Walls A and B	18d	16-Jan-16*	05-Feb-16	-5d					
<b>Retaining Wall B</b>										
2630	RWB - Construct Retaining Wall B - Base Structure	60d	03-Aug-15 A	03-Nov-15	-18d					
1103	RWB - Construct Retaining Wall B - Wall Structure	60d	27-Aug-15 A	30-Nov-15	-18d					
2640	RWB - Removal of Temporary Works & Backfill to Formation Level	30d	03-Nov-15	07-Dec-15	-18d					
VO196a	VO196 (Dated 24 Jun 2015) - Re-provision of Drainage System for the Construction of Retaining Walls A and B	18d	16-Jan-16*	05-Feb-16	-5d					
<b>Retaining Wall F</b>										
2690	RWF - Remove temp work & backfill to formation level	25d	21-Sep-15 A	30-Sep-15 A						
<b>Formation &amp; Roadworks</b>										
<b>Irrigation System</b>										
14918	Area IX	24d	31-Oct-15	27-Nov-15	-82d					
14914	Area VII	24d	28-Nov-15	28-Dec-15	-82d					
14912	Area VI	24d	29-Dec-15	26-Jan-16	-76d					
<b>Underground Drainage</b>										
1810	Area I / IIb	35d	18-Sep-15 A	27-Nov-15	-52d					
1812	Area IIa	39d	19-Sep-15 A	30-Nov-15	-88d					
VO143	VO143 (Dated 18 Dec 2014) - Connection Down Pipe From Footbridge 4 with Existing Manhole SMH7032196	6d	10-Nov-15*	16-Nov-15	62d					
VO197	VO197 (Dated 03 Jul 2015) - Inspection of Existing Manholes and Manhole Modification	12d	19-Dec-15*	05-Jan-16	22d					
<b>Roadworks</b>										
VO157	VO157 (Dated 02 Mar 2015) - Modification of Planters next to Man Kat Street RCP with Paving Blocks	11d	19-Oct-15 A	31-Oct-15	75d					

- ◆ Current Milestone
- Critical Remaining Work
- Level of Effort
- Remaining Work
- ▲ Baseline Milestone
- Project Baseline
- Actual Work

### Leighton Contractors (Asia) Limited Programme Update 61 (October 2015) THREE MONTH ROLLING

Project ID: U061  
 Baseline: DCP7-2c  
 Layout: Update Three Month Rolling U061  
 Page 3 of 5

Date	Revision	Checked	Appro...
20-Sep-15	U060	AT	BY
20-Oct-15	U061	AT	AL

Data Date: 20-Oct-15

# HY/2009/18 Central - Wan Chai Bypass (Central Interchange)

TASK filters: 3 Months\_1, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Gantt Chart											
						2015			2016								
						Oct	Nov	Dec	Jan	Feb	Mar						
14926	Area 3	48d	02-Nov-15	29-Dec-15	-15d												
VO149	VO149 (Dated 23 Jan 2015) - Inspection Pits at Connaught Road Central	6d	04-Nov-15*	10-Nov-15	67d												
14924	Area 2	48d	07-Nov-15	05-Jan-16	-88d												
VO205	VO205 (Dated 31 Jul 2015) - Felling and Replacement of Tree No. T2006	2d	14-Nov-15*	16-Nov-15	434d												
VO173	VO173 (Dated 04 May 2015) - Revision of Traffic Sign TS272	1d	16-Nov-15*	16-Nov-15	62d												
VO189	VO189 (Dated 20 May 2015) - Revised General Arrangement of the Mounting Post for Height Detector	6d	15-Dec-15*	21-Dec-15	32d												
VO150	VO150 (Dated 03 Jul 2015) - Replacement of Damaged Lattice	18d	17-Dec-15*	09-Jan-16	18d												
14928	Area 4	18d	30-Dec-15	20-Jan-16	-15d												
14922	Area 1a /Area 1b	24d	13-Jan-16	16-Feb-16	-88d												
<b>Bridge A</b>																	
<b>Bridge Furniture &amp; Finishes</b>																	
VO193	VO193 - Revised sign code of traffic sign TS174	0d	31-Dec-15*	31-Dec-15	26d												
<b>Elevated Layby at Rumsey Street Flyover East Bound</b>																	
<b>Bridge Structure</b>																	
VO159	VO159 - Revised General Arrangement of Deck of Elevated Lay-by	166d	14-Apr-15 A	19-Oct-15 A													
2780	RSFLB - Construct Parapet	41d	30-Jul-15 A	15-Oct-15 A													
1381	RSFLB - Construct Stitch	1d	24-Oct-15*	24-Oct-15	15d												
VO181	VO181 (Dated 12 May 2015) - Inspection of Base Plate of Existing Gantry GS2(HSN48) at Rumsey Street Flyover	6d	03-Nov-15*	09-Nov-15	68d												
VO176_1	VO176 (Dated 07 May 2015) / VO190 (Dated 01 Jun 2015) - Rumsey Street Flyover (Noise Permit for night work)	28d	30-Nov-15*	04-Jan-16	-21d												
VO176_1	VO176 (Dated 07 May 15) / VO190 (Dated 01 Jun 15) - Rumsey Street Flyover (Soffit & parapet edge - night work)	15d	30-Nov-15	16-Dec-15	-21d												
VO176_1	VO176 (Dated 07 May 15) / VO190 (Dated 01 Jun 15) - Rumsey Street Flyover (Central Barrier- night work)	72d	30-Nov-15	02-Mar-16	-21d												
14984	RSFLB - Construction of sign gantries (FADS01)	40d	15-Dec-15*	02-Feb-16	-42d												
<b>SECTION 7, 7A, 7B &amp; 7C - LANDSCAPE ESTABLISHMENT</b>																	
4020	EST - Portion IVD Landscape Establishment	365d	03-Nov-14 A	02-Nov-15	1d												
4000	EST - Portion IIIA Landscape Establishment	365d	28-Nov-15	26-Nov-16	-294d												

- Current Milestone
- Critical Remaining Work
- Level of Effort
- Remaining Work
- Baseline Milestone
- Project Baseline
- Actual Work

## Leighton Contractors (Asia) Limited Programme Update 61 (October 2015) THREE MONTH ROLLING

Project ID: U061  
Baseline: DCP7-2c  
Layout: Update Three Month Rolling U061  
Page 4 of 5

Date	Revision	Checked	Appro...
20-Sep-15	U060	AT	BY
20-Oct-15	U061	AT	AL

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015												2016	
						Oct			Nov			Dec			Jan				
4030	EST - Portion V Landscape Establishment	365d	02-Dec-15	30-Nov-16	-393d														
<b>Key Dates for Completion of Sections</b>																			
<b>Contract Required Completion</b>																			
1095	KD12 - Section 7A Complete (DAY-1870)	0d		03-Nov-15*	0d														
1105	KD14 - Section 7B Complete (DAY-1870)	0d		03-Nov-15*	0d														
<b>Portion Handover Dates</b>																			
<b>Anticipated Handover</b>																			
2960a	Portion IIIA Handover - Remaining (KD3 + 28 days) - (EOT 26.5 days added)	0d		30-Nov-15*	-242d														

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

### Leighton Contractors (Asia) Limited Programme Update 61 (October 2015) THREE MONTH ROLLING

Project ID: U061  
 Baseline: DCP7-2c  
 Layout: Update Three Month Rolling U061  
 Page 5 of 5

Date	Revision	Checked	Appro...
20-Sep-15	U060	AT	BY
20-Oct-15	U061	AT	AL
