




Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	2017				2018
					Oct	Nov	Dec	Jan	
HK/2012/08 Revised Works Programme Rev.11.1(DD 30 Jun 2017)									
<b>Dredging and Reclamation</b>									
<b>Marine Work Construction</b>									
<b>Zone CR111</b>									
<b>Seawall Construction - Zone CR111</b>									
<b>Zone CR111 Seawall- 2nd Stage</b>									
Seawall 2 & 12									
MAR21331	Zone CR111 - seawall 2 & 12 - install remaining seawall blocks (at -2.6mPD & -1.25mPD)	15	01-Oct-17	15-Oct-17					
MAR21371	Zone CR111 - seawall 2 & 12 - Backfilling remaining portion (type A, geotextile and filter)	15	16-Oct-17	30-Oct-17					
<b>Works for Section Completion</b>									
<b>Construction</b>									
<b>CWB Tunnel &amp; Slip Road Structures and Facilities</b>									
<b>CWB CR111 &amp; A1</b>									
<b>CWB CR111 - ELS &amp; Tunnel Structure</b>									
<b>CWB CR111 - Other Works</b>									
SIIA11204	Sec II A - CWB CR111: Reinstatement of culvert K - Bay 15: Construct Roof Slab	44	13-Oct-17	25-Nov-17					
SIIA11251	Sec II A - CWB CR111: Reinstatement of temporary openings at culvert K bay 20B	14	14-Nov-17	27-Nov-17					
SIIA11205	Sec II A - CWB CR111: Reinstatement of culvert K - Bay 15: Remove formwork & backfilling	25	26-Nov-17	20-Dec-17					
SIIA11685	Sec II A - CWB CR111: Reinstatement cooling mains - 2nd stage: Install cooling mains (DN700, DN800, DN900 & )	54	07-Nov-17	30-Dec-17					
SIIA11248	Sec II A - CWB CR111: Install & test stop log at culvert K bay 21	20	25-Oct-17*	13-Nov-17					
<b>Section V - Remaining At-Grade Road; Remove 2nd Stage ITA</b>									
<b>Roadwork &amp; Utilities</b>									
<b>Section 4 (K1106 - Culvert L)</b>									
SIV12305	Sec V - Roadwork & Utilities Section 4 Carriageway - Utilities : crossroad duct	14	05-Dec-17	20-Dec-17					
SIV12300	Sec V - Roadwork & Utilities Section 4 Carriageway - Gully pipe (K1106-Culvert K, K1201-Culvert K, L1201, L1301)	35	24-Oct-17	04-Dec-17					
SIV12360	Sec V - Roadwork & Utilities Section 4 Carriageway - watermain	15	21-Dec-17	10-Jan-18					
SIV12440	Sec V - Roadwork & Utilities Section 4 footpath - Utilities : HGC & PCCW	8	21-Dec-17	02-Jan-18					

Data Date:  
30-Jun-17

- Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Remaining Level of Effort

**3 Months Rolling Programme for CR111 Area ( Oct 2017 - Dec 2017)**  
**(Ref. to Works Programme Rev.11.1)**

Date	Revision	Checked	Approved
03-Oct-17	11.1		

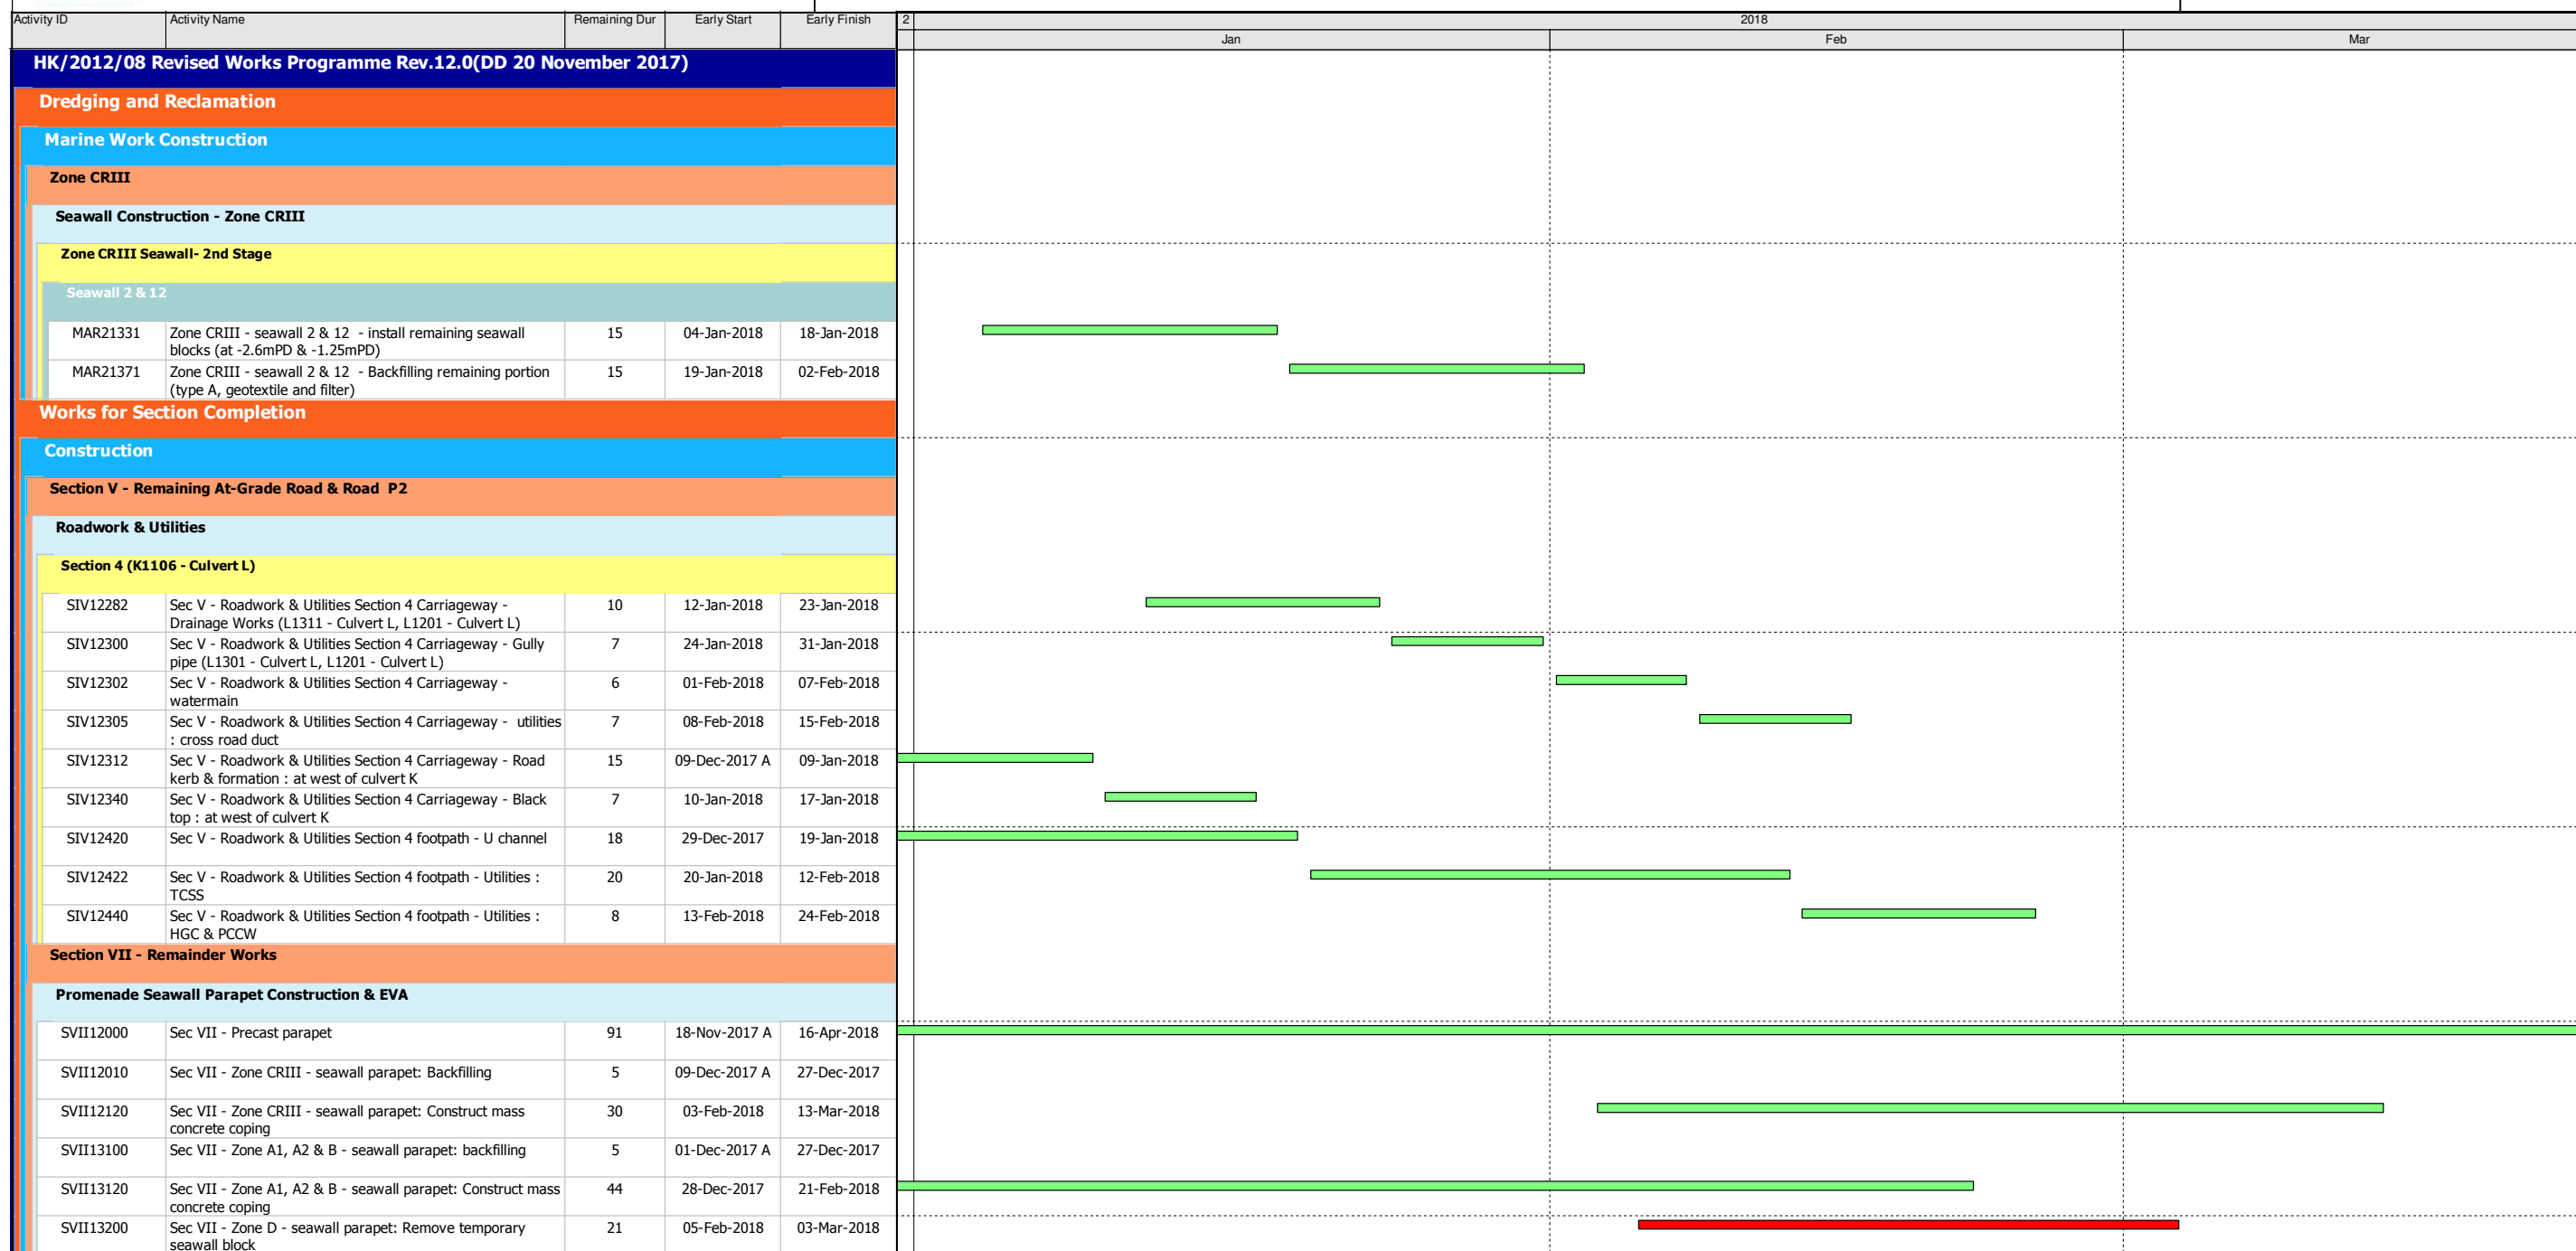



Data Date: 20-Dec-2017

- ◆ Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- ▬ Remaining Level of Effort



**3 Months Rolling Programme for CRIII Area (January 2018 - March 2018)**  
(Ref. to Revised Works Programme Rev.12)

Date	Revision	Checked	Approved
20-Dec-2017	12		

**HY/2009/18 Central - Wan Chai Bypass - Central Interchange**

2017				
	September	October	November	December
<b>Road P1</b>				
Installation of irrigation pipes at P1 Road				
Reinstatement of planter at P1 Road				
<b>LEGEND:</b>	<b>Three Month Rolling Programme</b>			
 Actual Works				
 Remaining Works				
	Update on 26.11.2017			

**HY/2009/18 Central - Wan Chai Bypass - Central Interchange**

	2017		2018		
	November	December	January	February	
<b>Road P1</b>					
Reinstatement of shrubs at P1 Road					
<b>LEGEND:</b>					
	 Actual Works			<b>Three Month Rolling Programme</b>	
	 Remaining Works			Update on 29.01.2017	
