



**LEADER**

俊和 - 利達聯營

CHUN WO - LEADER JOINT VENTURE

## LANDSCAPE PLAN

(Pursuant to Further Environmental Permit – No. FEP-02/364/2009)

Revision	Date of Issue	Remarks	Prepared by	Approved by
1	8 <sup>th</sup> Oct 13	Initial issue	AM	PLY
2	9 <sup>th</sup> Oct 14	2 <sup>nd</sup> issue	KMN	AYU
3	2 <sup>nd</sup> Apr 15	3 <sup>rd</sup> issue	KMN	AYU
4	27 <sup>th</sup> Jun 15	4 <sup>th</sup> issue	KMN	AYU
5	17 <sup>th</sup> Jan 18	5 <sup>th</sup> issue	TT	AYU

## *List of Content*

	Page
<b>1.0 Introduction</b>	3
<b>2.0 Project Description</b>	3
2.1 Scope of Works	3
<b>2.2 Landscape and Visual Mitigation Measure during Operation Phase</b>	4
<b>3.0 Sources of Landscape &amp; Night-Time Lighting Impacts</b>	5
<b>4.0 Visual Sensitive Receivers</b>	5
<b>5.0 Location and Implementation Programme of Hoarding</b>	6
<b>6.0 Design and Fixing Details of Hoarding</b>	6
<b>7.0 Control Measure of Night- Time Lighting</b>	6
<b>8.0 Onsite Supervision for Night- Time Lighting</b>	6
<b>9.0 Tree Preservation</b>	6
<b>10.0 Tree Transplanting</b>	7
<b>11.0 Tree Felling</b>	7
<b>12.0 Replacement of Plants</b>	7
<b>13.0 Top Soil</b>	8
<b>14.0 Landscape and Visual Mitigation Measure during Operation Phase</b>	8

## *List of Appendixes*

- A Project's Site Boundary**
- B Location Plan of Visual Sensitive Receivers**
- C Typical Arrangement for Fence off the Tree Protection Zone (TPZ)**
- D Tree Transplant Plan and Tree Survey Schedule**
- E Method Statement**
- F Implementation Schedule for Landscape and Visual**

## 1.0 Introduction

Pursuant to the Further Environmental Permit (No. FEP-02/364/2009) Part C Special conditions Clause 2.11, Landscape Plan (LP) is developed by Permit Holder (Chun Wo-Leader Joint Venture (CWLJV)) to demonstrate clearly the mitigation measures specified in this LP will be implemented on site in order to reduce the effects that the Project may have on landscape character and visual amenity.

This revision of Landscape Plan reflects and provide update information regarding the status of landscape and visual measures upon completion of construction works.

## 2.0 Project Description

The key purpose of Wan Chai Development Phase II (WDII) is to provide land around HKCEC for construction of the Central-Wan Chai Bypass and HKCEC section (CWB). Land formed under the project will be developed as a world-class waterfront promenade joining that at the new Central waterfront for public enjoyment.

Wan Chai Development Phase II – Central – Wan Chai Bypass at HKCEC HK/2009/01 is one of the major sub-project of the above mentioned Development which has been commenced on 29 December 2009 and it will be lasted for 76 months.

### 2.1 Scope of Works

The major scopes of works comprise but not limited to the following:

- Re provisioning of cross harbour water mains.
- Re provisioning of the existing cooling water pumping stations for Convention Plaza, HKAPA, Shui On Centre, and Government Buildings.
- Installation of cooling water discharge pipelines for the Great Eagle Centre / Harbour Centre and China Resources Building
- At-grade road and utility works and associated temporary diversions
- Storm-water drainage culvert and use of trenchless method for storm-water drainage construction
- Retaining structures at both ends of the reclamation that serve as interfacing structures for the adjacent contracts
- Construction of a dual three-lane trunk road tunnel
- Demolition of Wan Chai West ferry pier, existing cooling water pumping stations, promenade deck, and Expo Drive East Bridge.

No permanent planting works and no transplanting of trees to final transplant position would be required to be carried out under Contract HK/2009/01.

## 2.2 Landscape and Visual Mitigation Measures during Operation Phase

With reference to the relevant EIA Report (AEIAR-125/2008) Table 10.5, the proposed construction phase landscape mitigation measures, but not limited to, are listed as below:

- A. Erection of decorative screen hoarding compatible with the surrounding setting; (Refer to Section 5.0 & 6.0)
- B. Existing public light will be used as for night-time lighting; brightness of warning flash lights for will be controlled to an appropriate level (Refer to Section 9.0);
- C. Lighting of construction at night work on land will be maintained at works area locally and light source will be set at the back of hoarding toward the works area, thus would reduce the lighting nuisance to the public. For lighting on work boats, navigation lighting would follow the Navigation Regulation. Lighting for marine works at night would be balanced with minimum lighting nuisance to the public and the navigation safety (Refer to Section 9.0);
- D. All trees under our contract area would be handled according to their identified status as either transplanted or preserved (Refer to Section 10.0 & 11.0)
- E. Minimization of disruption to public by effective programming of the works;
- F. Minimization of works areas; &
- G. Ensure the construction phase landscape and visual mitigation measures are in compliance with relevant requirements in EIA Reports. The mitigation measures are as follows:

Table 1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Relevant Legislation and Guidelines	Cross-reference
<b>Table 10.5 CM1</b> (EIA Report AEIAR-125/2008) & Table 7.5 item 4 (EIA Report AEIAR-041/2001)	Topsoil, where identified, shall be stripped and stored for re-use in the construction of the soft landscape works, where practical.	EIAO TM	Section 14.0
<b>Table 10.5 CM2</b> (EIA Report AEIAR-125/2008) & Table 7.5 item 3 (EIA Report AEIAR-041/2001)	Existing trees to be retained on site shall be carefully protected during construction.	EIAO TM	Section 10.0
<b>Table 10.5 CM3</b> (EIA Report AEIAR-125/2008) & Table 7.5 item 4 (EIA Report AEIAR-041/2001)	Trees unavoidably affected by the works shall be transplanted where practical.	EIAO TM	Section 11.0
<b>Table 10.5 CM4</b> (EIA Report AEIAR-125/2008) & Table 7.5 item 4 (EIA Report AEIAR-041/2001)	CM4 Compensatory tree planting shall be provided to compensate for felled trees.	EIAO TM	Section 12.0 & 13.0
<b>Table 10.5 CM5</b> (EIA Report AEIAR-125/2008) & Table 7.5 item 2 (EIA Report AEIAR-041/2001)	CM5 Control of night-time lighting.	EIAO TM	Section 8.0



<p><b>Table 10.5 CM6</b> (EIA Report AEIAR-125/2008) &amp; Table 7.5 item 1 (EIA Report AEIAR-041/2001)</p>	<p>CM6 Erection of decorative screen hoarding compatible with the surrounding setting.</p>	<p>EIAO TM</p>	<p>Section 5.0</p>
---	--	----------------	--------------------

### 3.0 Sources of Landscape & Night-Time Lighting Impacts

Sources of Landscape impacts in the construction phase would include:

- The physical reclamation itself;
- Construction of landscape decks;
- Construction traffic;
- The laying down of utilities, including water, drainage and power;
- Temporary site access areas, site cabins and heavy machinery;
- Construction site traffic on the reclamation;
- Increase road traffic congestion;
- After dark lighting and welding; and
- Dust during dry weather.

Sources of Night-Time Lighting Impacts in the construction phase would include:

- The physical dredging and reclamation itself;
- Construction traffic;
- The laying down of utilities, including water, drainage and power;
- Temporary site access areas, site cabins and heavy machinery;
- Construction site traffic on the reclamation; and
- After dark lighting and welding.

### 4.0 Visual Sensitive Receivers

Telecom House, Hong Kong Arts Centre, Harbour View International House (C19), Grand Hyatt Hotel (C22), HKCEC (C24) and HKCEC open space (O2) are the key Visual Sensitive Receivers (VSRs) that will be affected during the Construction Phase.

Otherwise, the key VSRs likely to be affected by the Night-Time Lighting on site are included the CITIC Tower (C14), Fleet Arcade (C15), Telecom House, Hong Kong Arts Centre, Harbour View International House (C19), Central Plaza (C21), Grand Hyatt Hotel (C22), Renaissance Harbour View Hotel (C23), HKCEC (C24), Peninsula Hotel (C40), Sheraton Hotel (C41) and InterContinental Hotel (C42).

Respective VSRs (refer to EIA Report Figure 10.4) are mapped in **Appendix B**.

## 5.0 Location and Implementation Programme of Hoarding

All hoarding have been removed due to the completion of works

## 6.0 Design and Fixing Details of Hoarding

All hoarding have been removed due to the completion of works

## 7.0 Control Measures of Night-Time Lighting

- I. Any night-time work that needs to be conducted will be carefully planned to minimize the amount of unnatural light that would be needed.
- II. The use of equipment headlights/lighting will be first evaluated to determine sufficiency based on the task and to minimize the use of portable light plants.
- III. Lighting will be directed toward work areas and away from neighboring properties.
- IV. Proper alignment and careful layout of construction activities should reduce a potential lighting exceedance.
- V. In the event the portable light plants are used, they will be aimed away from residential areas and used thriftily when needed. The light plant masts will also be kept at distances that would minimize the emission of light into the community, while still providing a safe work environment for employees involved in the task.
- VI. In addition use of vegetative and landscape buffers and other site and project elements will be used.
- VII. Night-time lighting at sea will fulfill requirement of the Merchant Shipping (Local Vessels) (General) Regulation and minimize the impact to VSR.

## 8.0 Onsite Supervision for Night-Time Lighting

Designated site personnel will control and monitor the lighting impact during night-time construction work. Light plants will be repositioned, redirected, lowered or shielded immediately if any public concern or complaint received.

## 9.0 Tree Preservation

**During the construction phase, retained trees are retained and protected, Figures in Appendix A shows the Project's site boundary and Appendix D shows the working area with the retained and transplanted trees.**

- I. Identify all trees to be protected and fence off when necessary.
- II. Determine Tree Protection Zone (TPZ) along the perimeter of tree crown spread (i.e. Drip line of the tree). In case of the site constraint such as permanent structure, public utilities or site access routes in proximity, TPZ may be reduced subject to comments from our Independent Tree Specialist (ITS). Fluorescent barrier will be erected and fenced off the TPZ determined by tree crown spread of drip line of crown spread (Refer to

Appendix C). Warning notice guarding against unauthorized operations within TPZ shall be erected on the barrier fence.

III. No nails or other fixings shall be driven into trees.

IV. No materials shall be stored or disposed within TPZ.

The preservation and protection to existing trees retained within Site Boundary were maintained under Contract HK/2009/01 up to 31 May 2016. All possessed retained trees have been handed over to relevant maintenance departments after to completion of works in the works area.

## 10.0 Tree Transplanting

According to Tree Transplant Plan (Appendix D), some trees have to be transplanted due to construction consideration. The transplanting works will be done by an independent tree specialist (ITS). The transplanting procedures will be as follows: 1) Crown pruning; 2) 1<sup>st</sup> root pruning; 3) Undercutting; 4) Uplifting and transport to site nursery; 5) Planting at site nursery; & 6) Uplifting and transplant from site nursery to original location. ITS would be present to supervise the uplifting and transport procedure.

Figures in **Appendix A** shows the Project's site boundary and **Appendix D** shows the working area with the retained and transplanted trees. In addition, trees in Zone A, B, C, D, E and F marked "Transplanted" on enlarged tree transplanting plan in **Appendix D** had been transplanted under Contract HK/2009/01 and all trees transplanted under Contract HK/2009/01 have been subsequently hand-over to Contract HK/2009/02 nursery site at Lam Tei for maintenance and final planting. Besides, the trees which highlighted in blue color on tree transplanting plan in **Appendix D** have been hand-over to Contract HK/2012/08 (Wan Chai area) and LCSD (Tsim Sha Tsui area).

No final planting works for the transplanted trees would be required to be conducted under Contract HK/2009/01.

## 11.0 Tree Felling

Permission for tree felling must be applied and granted from LCSD, LD and the Engineer prior to felling works to be carried out. Works area would be fenced off with plastic fence along the footpath area and traffic cone along the carriageway area. Sequence of tree felling will be carried out in three stages by the specialist landscaping sub-contractor with well-trained tree worker as follows: Stage 1 – Crown Pruning; Stage 2 – Trunk Cutting; & Stage 3 – Stump removal. Felled trees details please refer to tree survey schedule and compensatory plan will be mentioned in Section 13.0.

There is no trees to be felled under this contract due to the completion of works.

## 12.0 Replacement of Plants

Permission for replacement of plants must be applied and agreed by the Engineer and LCSD. The proposed replacement should be the same species and or similar size and form as felled trees. Implementation of compensatory planting should be following DEVB TC (W) No.10/2013 Appendix A Section I (V) in case if any tree needs to be felled due to health condition and damages.

If sufficient space for tree planting can be identified, additional planting to achieve the compensatory planting ratio of 1:1 in terms of aggregated DBH, i.e. the total DBH of planted trees to have the same total DBH of felled trees should be undertaken as far as practicable.

The compensatory trees will be planted to Lam Tei Tree Nursery which is maintained under Contract HK/2009/02 and the final location and the planting arrangement of the compensatory trees shall be determined by Contract HK/2009/02.

No retained/ transplanted trees were replaced under this contract due to the completion of works.

## 13.0 Topsoil

During site clearance, where appropriate and as required by the Engineer, topsoil shall be stripped and stockpiled in an area designated or agreed by the Engineer.

## 14.0 Landscape and Visual Mitigation Measures during Operation Phase

According to EIA section 10.8.3, the proposed harbour front open spaces under reclamation (DP3) are in accordance with the planned landscape framework. A continuous waterfront with different themed precincts is proposed to enhance the visual amenity value of existing waterfront. Nevertheless, such component will not form part of the scope under the Contract HK/2009/01



俊和 - 利達聯營  
CHUN WO - LEADER JOINT VENTURE

Contract No. HK/2009/01  
Wan Chai Development Phase II  
Central – Wan Chai Bypass at HKCEC

---

## **Appendix A**

### **Project's Site Boundary**



# Wan Chai Area

## LEGEND:


- 00211(I) EXISTING TREE TO BE TRANSPLANTED
- 00251(R) EXISTING TREE TO BE RETAINED
- 03271(F) EXISTING TREE TO BE FELL
- 03281(M) MISSING TREE
- 01701(R) EXISTING TREE TO BE HANDOVER TO CONTRACT HK/2012/08

- PROJECT AREA
- WORKING AREA WAS HANDOVER TO CONTRACT HK/2012/08

XXXXX

VICTORIA HARBOUR

- Zone A Waterworks Area
- Zone B Tunnel, Marine, Waterworks Area
- Zone C Waterworks Area
- Zone D Waterworks Area
- Zone E Waterworks Area
- Zone F Waterworks Area

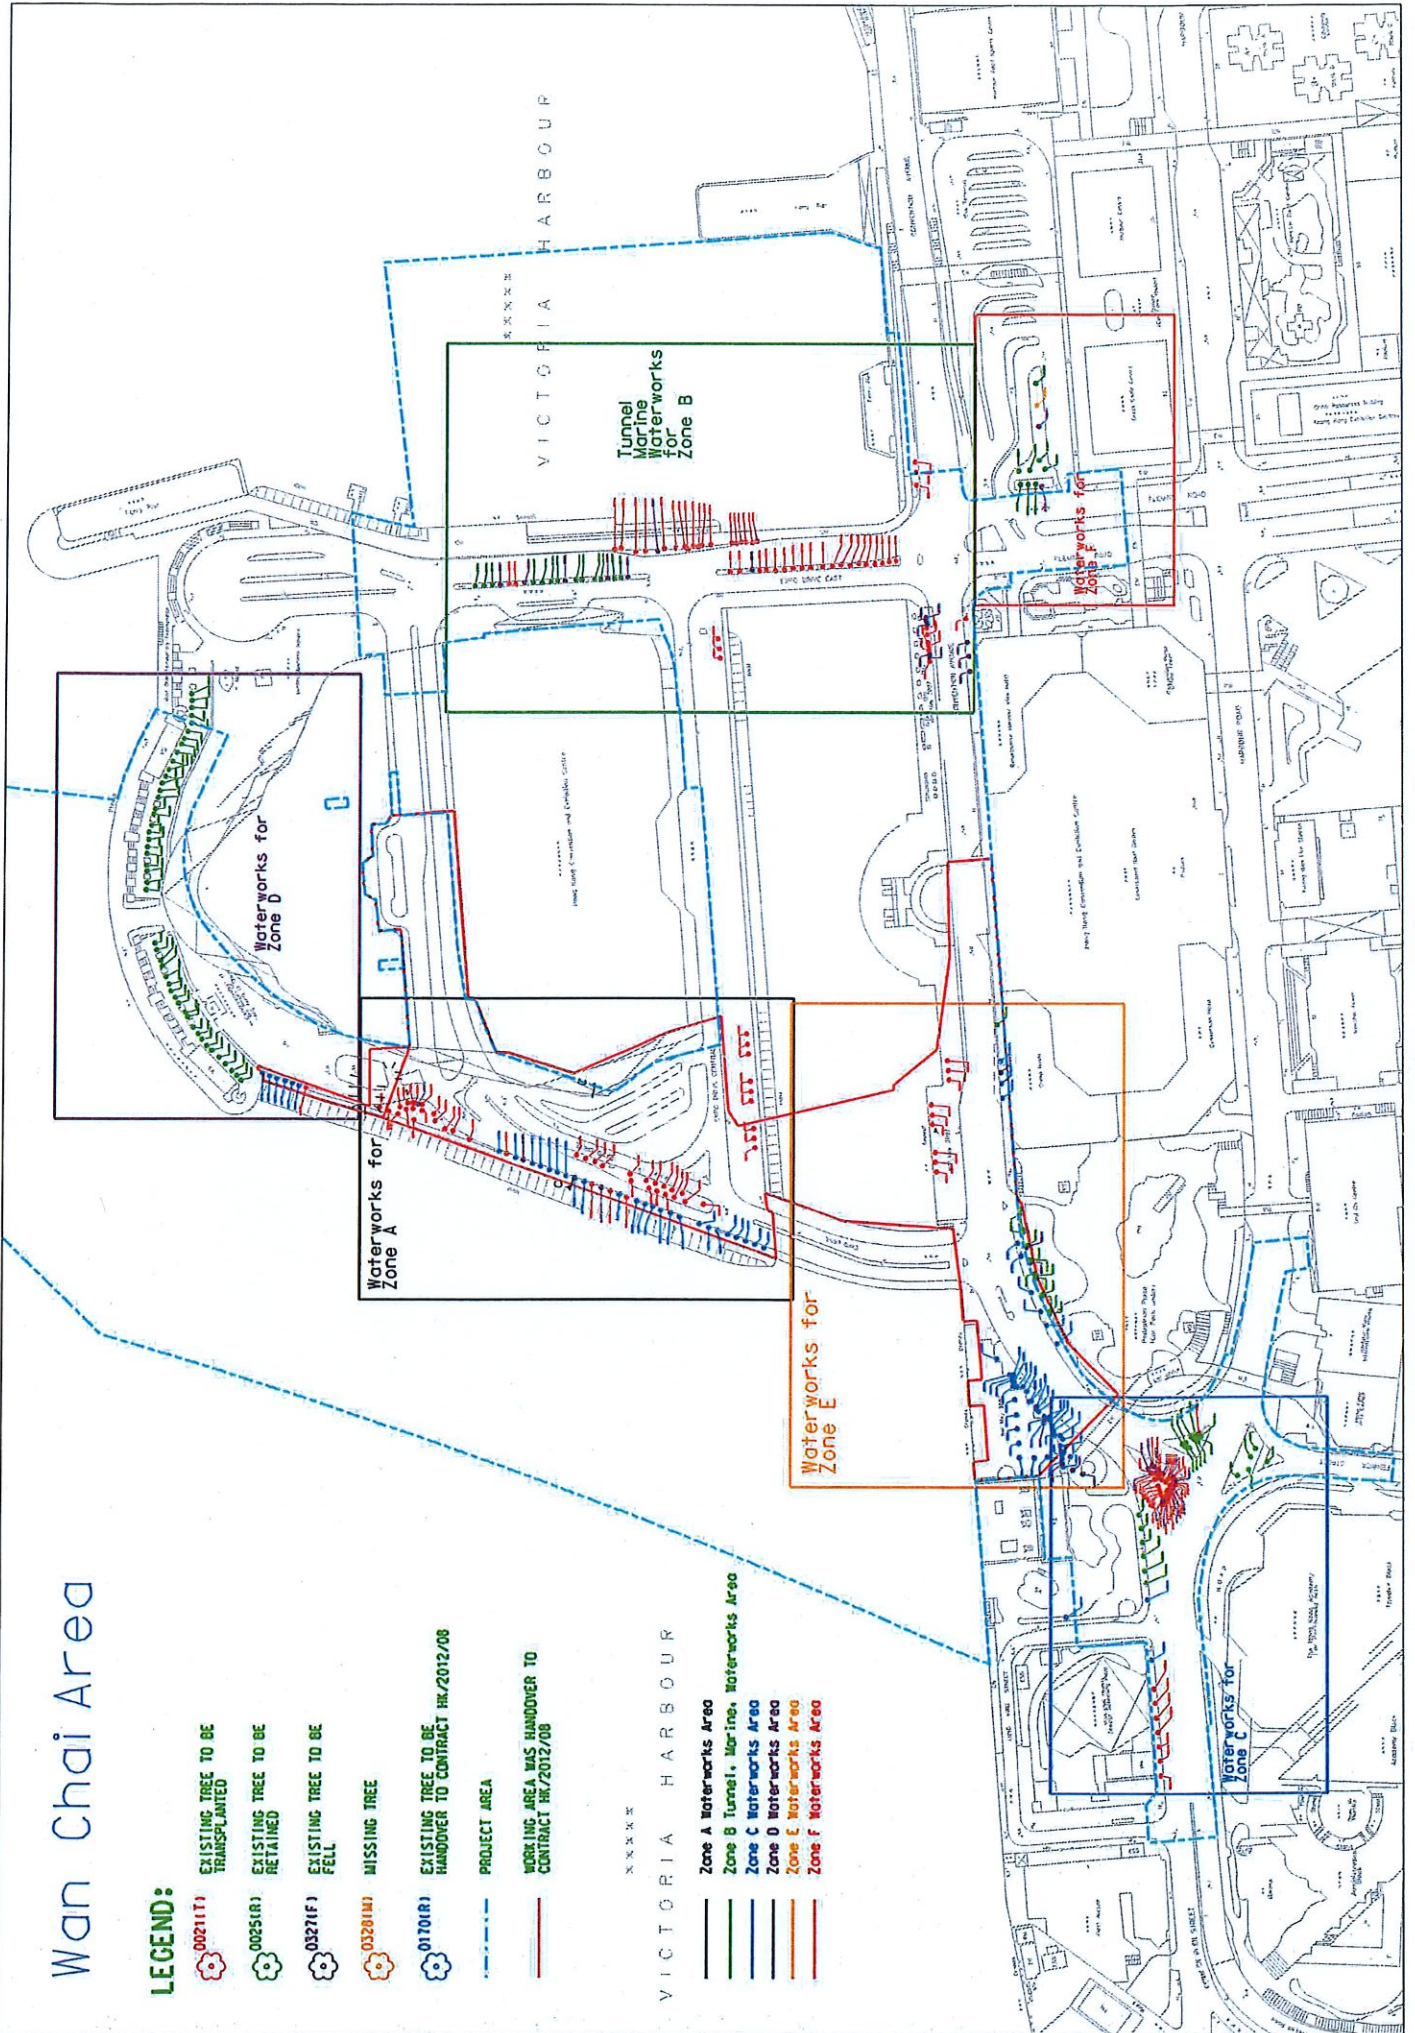



利達



俊和 - 利達聯營

CHUN WO - LEADER JOINT VENTURE

Contract No. HK/2009/01  
Wan Chai Development Phase II  
Central – Wan Chai Bypass at HKCEC

---

## **Appendix B**

### **Location Plan of Visual Sensitive Receivers**








## Appendix C

### Typical Arrangement for Fence off the Tree Protection Zone (TPZ)

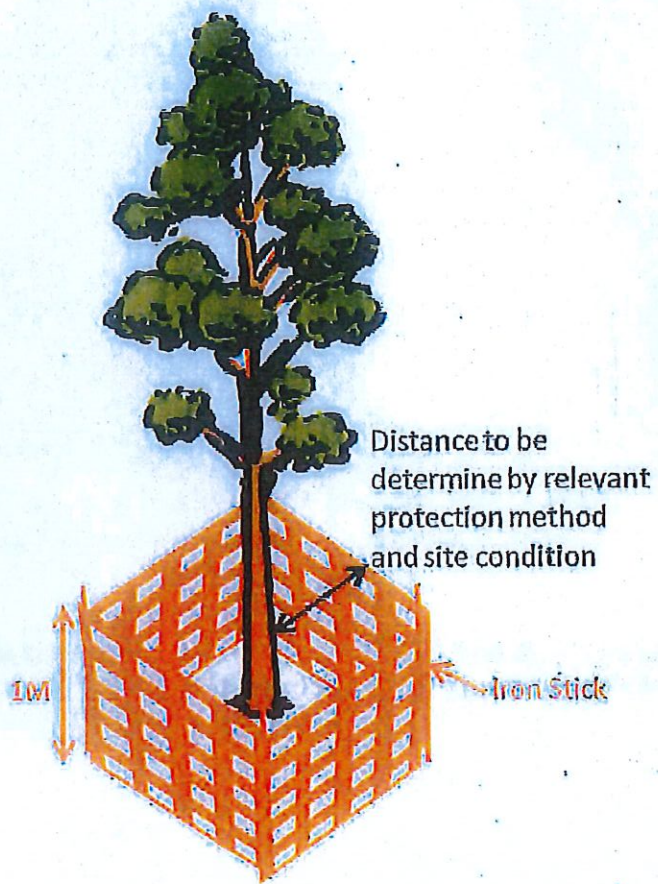

Fluorescent Tree Protection Barrier  
(Individual Tree)



Fluorescent Fencing




## Appendix D

### Tree Transplant Plan and Tree Survey Schedule

# Waterworks for Zone A

## LEGEND:

-  0021(T) EXISTING TREE TO BE TRANSPLANTED
-  0025(R) EXISTING TREE TO BE RETAINED
-  0327(F) EXISTING TREE TO BE FELL
-  0328(M) MISSING TREE
-  0170(R) EXISTING TREE TO BE HANDOVER TO CONTRACT HK/2012/08

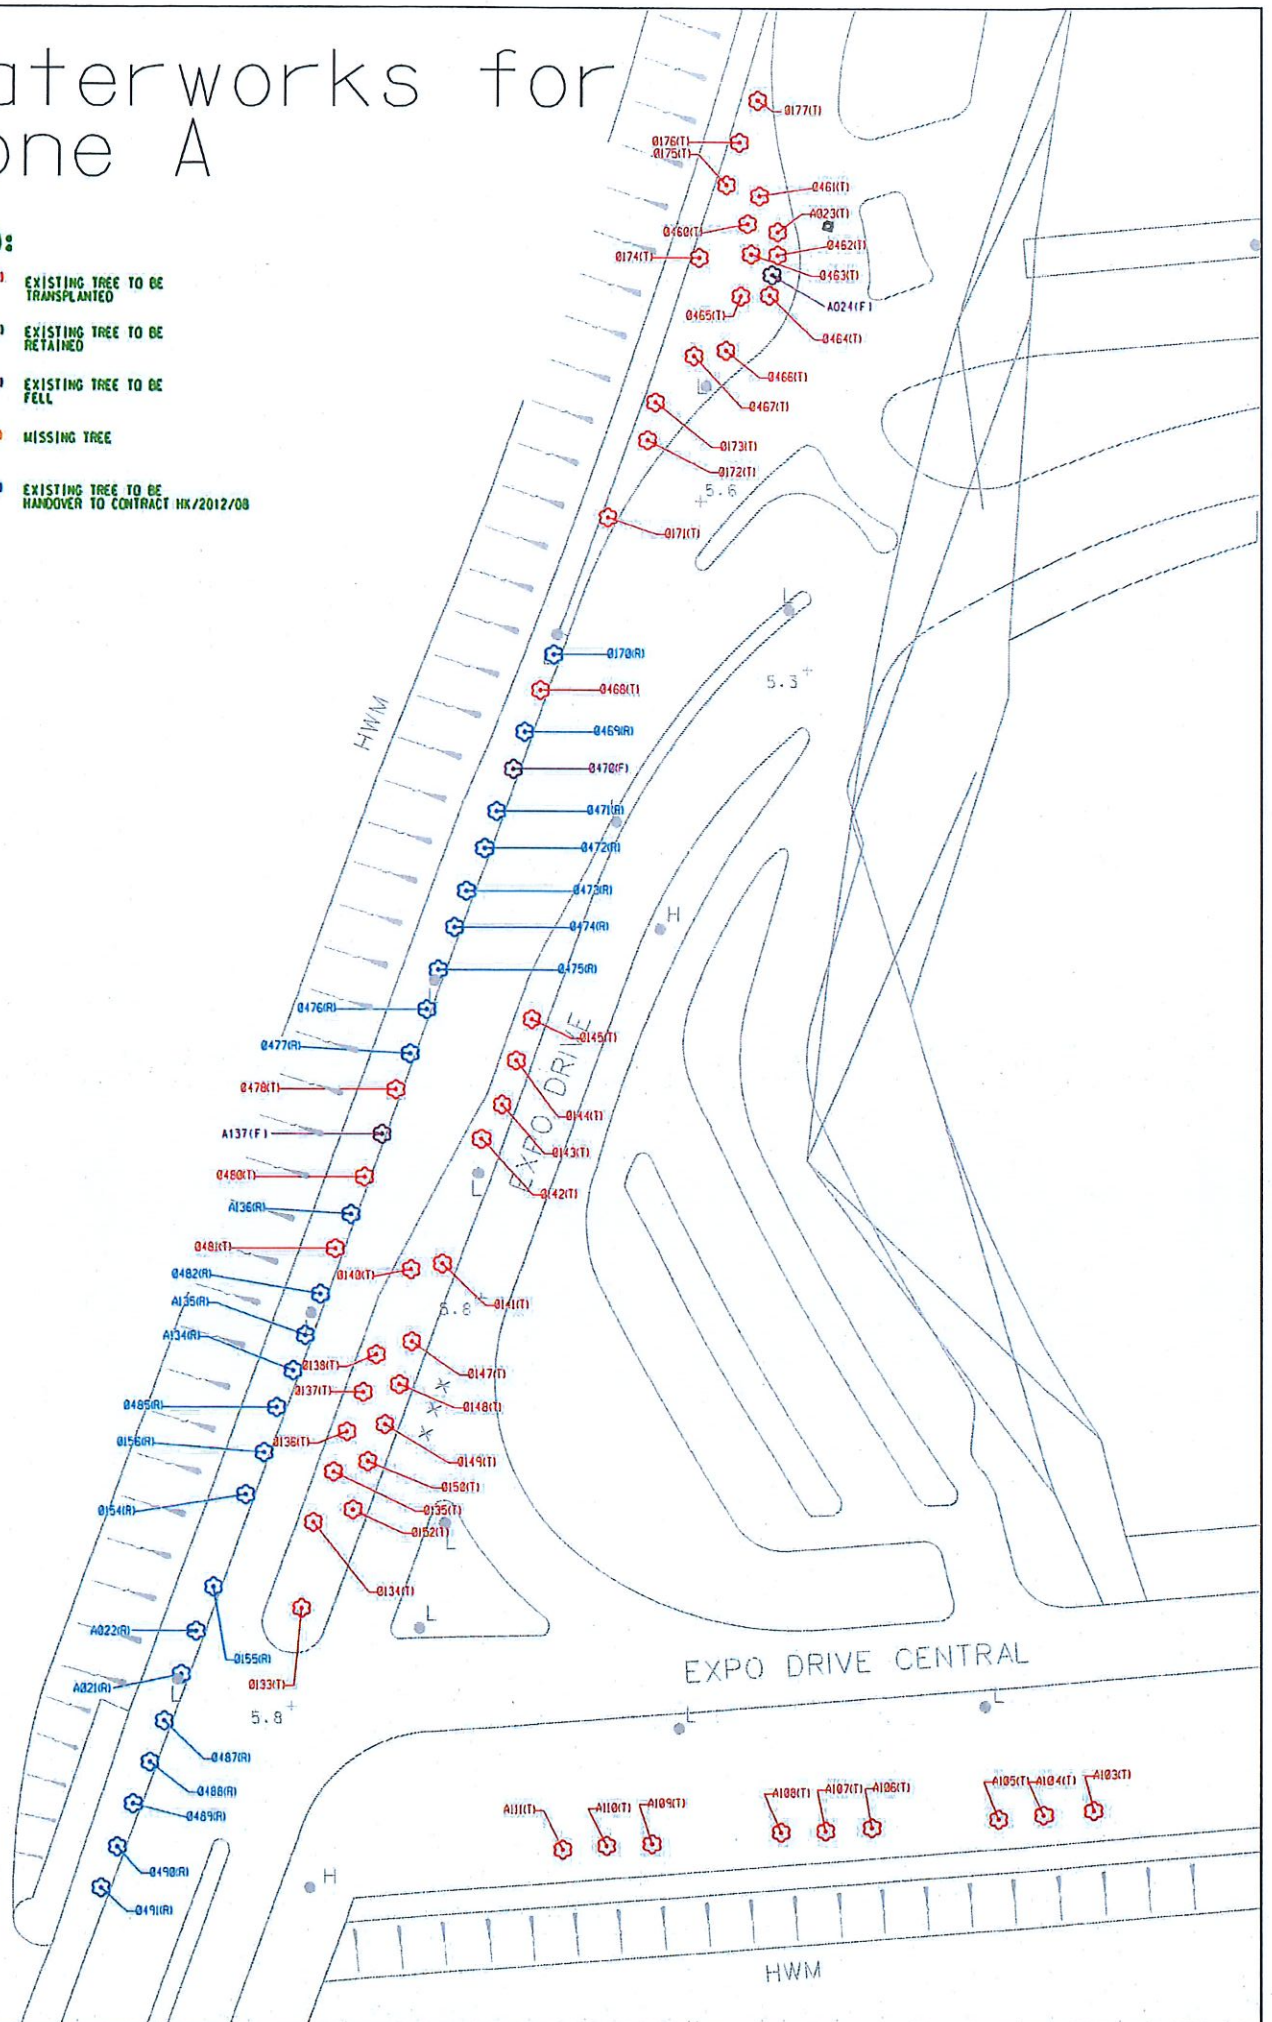






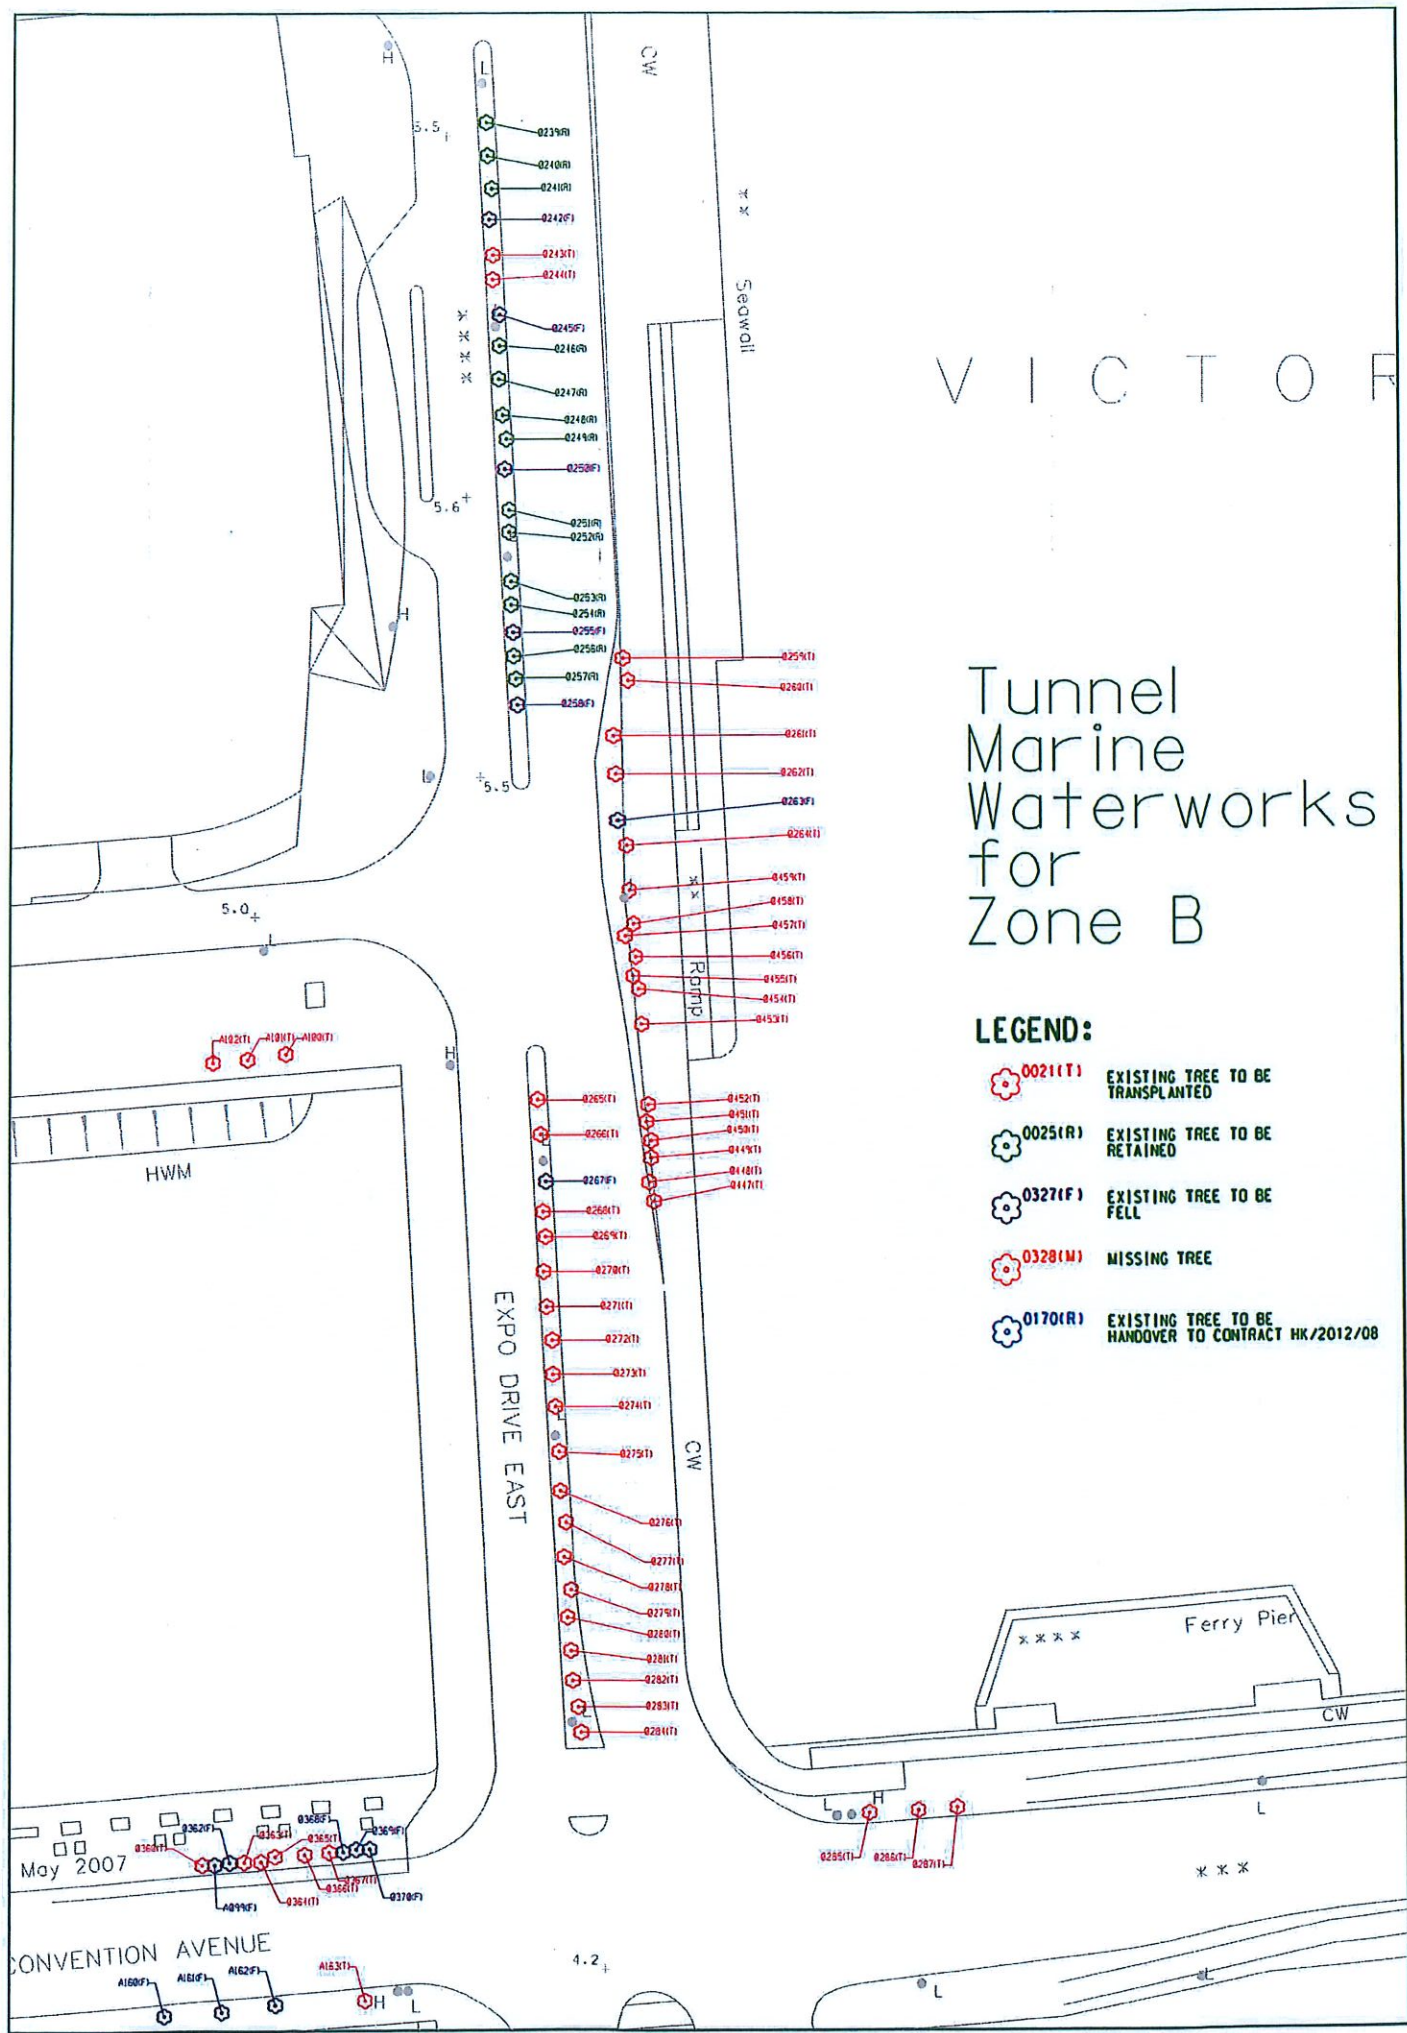


# VICTOR

## Tunnel Marine Waterworks for Zone B

### LEGEND:






-  0021(T) EXISTING TREE TO BE TRANSPLANTED
-  0025(R) EXISTING TREE TO BE RETAINED
-  0327(F) EXISTING TREE TO BE FELL
-  0328(M) MISSING TREE
-  0170(R) EXISTING TREE TO BE HANDOVER TO CONTRACT HK/2012/08





# Waterworks for Zone C

## LEGEND:

-  0021(T) EXISTING TREE TO BE TRANSPLANTED
-  0025(R) EXISTING TREE TO BE RETAINED
-  0032(F) EXISTING TREE TO BE FELL
-  0028(W) MISSING TREE
-  0170(R) EXISTING TREE TO BE HANDOVER TO CONTRACTOR HK/2012/08

\*\*\*\*\*

The Hong Kong Academy  
For Performing Arts

JM





# Waterworks for Zone D

**LEGEND:**






- 0021111 EXISTING TREE TO BE TRANSPLANTED
- 00551R1 EXISTING TREE TO BE RETAINED
- 03271F1 EXISTING TREE TO BE FELL
- 03101M1 MISSING TREE
- 01101R1 EXISTING TREE TO BE HANDOVER TO CONTRACT IN 2012/00





# Water works for Zone F

## LEGEND:

-  0021(I) EXISTING TREE TO BE TRANSPLANTED
-  0025(R) EXISTING TREE TO BE RETAINED
-  0327(F) EXISTING TREE TO BE FELL
-  0328(H) MISSING TREE
-  0170(R) EXISTING TREE TO BE HANDOVER TO CONTRACT HK/2012/08



23

Great Eagle Centre

FLEMING

FLEMING ROAD

(Car)





CONTRACT NO.: HK/2009/01

Tree No.	Botanical Name	Chinese Name	Height (m)	Trunk Diameter at Breast Height (DBH) (mm)	Spread (m)	Health		Form		Amenity Value	Original Recommendation	Remarks
						Good	Poor	Good	Poor			
T001	<i>Albizia lebbek</i>	大葉合歡	9	478	16	Fair	Fair	Fair	Fair	Low	Retain	Handed over to LCSD on 15 June 2016
T003	<i>Melaleuca leucadendron</i>	白千層	6	166	1.4	Fair	Fair	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016
T004	<i>Melaleuca leucadendron</i>	白千層	8	261	3	Fair	Fair	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016
T005	<i>Albizia lebbek</i>	大葉合歡	8	299	6	Fair	Fair	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016
T007	<i>Roystonea regia</i>	王棕	11	420	5	Fair	Fair	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016
T008	<i>Roystonea regia</i>	王棕	7	306	4	Fair	Fair	Fair	Fair	Medium	Transplant	Handed over to LCSD on 15 June 2016
T009	<i>Roystonea regia</i>	王棕	8.5	385	5	Fair	Fair	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016
T010	<i>Roystonea regia</i>	王棕	8	245	2	Fair	Fair	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016
T011	<i>Roystonea regia</i>	王棕	10	366	3	Fair	Fair	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016
T012	<i>Roystonea regia</i>	王棕	11	366	3	Fair	Fair	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016
T013	<i>Roystonea regia</i>	王棕	10	334	2	Fair	Fair	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016
T014	<i>Roystonea regia</i>	王棕	10	420	3	Fair	Fair	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016
T015	<i>Roystonea regia</i>	王棕	10	398	3	Fair	Fair	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016
T016	<i>Roystonea regia</i>	王棕	10	392	2	Fair	Fair	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016
T017	<i>Roystonea regia</i>	王棕	11	382	1.5	Fair	Fair	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016
T021	<i>Archontophoenix Alexandrae</i>	假檳榔	6	134	2	Fair	Fair	Fair	Fair	Low	Transplant	Transplanted by this contract on 18-1-2011
T022	<i>Archontophoenix Alexandrae</i>	假檳榔	7	134	3	Fair	Fair	Fair	Fair	Low	Retain	Transplanted by this contract on 18-1-2011
T023	<i>Archontophoenix Alexandrae</i>	假檳榔	6	153	3	Fair	Fair	Fair	Fair	Low	Transplant	Transplanted by this contract on 18-1-2011
T024	<i>Archontophoenix Alexandrae</i>	假檳榔	7	172	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 18-1-2011
T025	<i>Archontophoenix Alexandrae</i>	假檳榔	7	137	3	Fair	Fair	Fair	Fair	Low	Retain	Transplanted by this contract on 17-1-2011
T026	<i>Archontophoenix Alexandrae</i>	假檳榔	7	175	3	Fair	Fair	Fair	Fair	Low	Retain	Transplanted by this contract on 18-1-2011
T027	<i>Archontophoenix Alexandrae</i>	假檳榔	8	201	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 17-1-2011
T028	<i>Archontophoenix Alexandrae</i>	假檳榔	7	134	3	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 17-1-2011
T029	<i>Archontophoenix Alexandrae</i>	假檳榔	7	153	3	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 17-1-2011
T030	<i>Archontophoenix Alexandrae</i>	假檳榔	5	153	3	Fair	Fair	Fair	Fair	Low	Transplant	Transplanted by this contract on 17-1-2011
T031	<i>Archontophoenix Alexandrae</i>	假檳榔	8	162	3	Fair	Fair	Fair	Fair	Low	Retain	Transplanted by this contract on 18-1-2011
T032	<i>Archontophoenix Alexandrae</i>	假檳榔	7	131	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 17-1-2011
T033	<i>Archontophoenix Alexandrae</i>	假檳榔	7	170	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 17-1-2011
T034	<i>Archontophoenix Alexandrae</i>	假檳榔	6	159	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 17-1-2011
T035	<i>Archontophoenix Alexandrae</i>	假檳榔	7	105	3	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 18-1-2011
T044	<i>Casuarina equisetifolia</i>	木麻黃	10	239	4	Fair	Fair	Fair	Fair	Medium	Retain	Handover to HK/2012/08
T133	<i>Cinnamomum camphora</i>	樟樹	5	159	4	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 29-12-2012
T134	<i>Cinnamomum camphora</i>	樟樹	5	143	3	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 29-12-2012
T135	<i>Cinnamomum camphora</i>	樟樹	3	127	1	Poor	Poor	Fair	Fair	Low	Retain	Transplanted by this contract on 8-8-2012
T136	<i>Cinnamomum camphora</i>	樟樹	6	137	3	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 8-8-2012
T137	<i>Cinnamomum camphora</i>	樟樹	6	146	3	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 7-8-2012
T138	<i>Cinnamomum camphora</i>	樟樹	6	115	3	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 7-8-2012
T139	<i>Cinnamomum camphora</i>	樟樹	-	-	-	-	-	-	-	-	Retain	Missing before commencement of contract
T140	<i>Cinnamomum camphora</i>	樟樹	6	96	3	Fair	Fair	Fair	Fair	Low	Retain	Transplanted by this contract on 4-10-2011
T141	<i>Cinnamomum camphora</i>	樟樹	5	96	1	Poor	Fair	Fair	Fair	Low	Retain	Transplanted by this contract on 25-2-2011
T142	<i>Cinnamomum camphora</i>	樟樹	5	121	3	Poor	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 8-8-2012
T143	<i>Cinnamomum camphora</i>	樟樹	3	111	2	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 25-2-2011
T144	<i>Cinnamomum camphora</i>	樟樹	3	111	1	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 25-2-2011
T145	<i>Cinnamomum camphora</i>	樟樹	4	111	0.5	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 25-2-2011
T146	<i>Cinnamomum camphora</i>	樟樹	-	-	-	-	-	-	-	-	Retain	Missing before commencement of contract
T147	<i>Cinnamomum camphora</i>	樟樹	6	134	2	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 7-8-2012
T148	<i>Cinnamomum camphora</i>	樟樹	7	191	4	Fair	Fair	Fair	Fair	Low	Retain	Transplanted by this contract on 7-8-2012
T149	<i>Cinnamomum camphora</i>	樟樹	7	159	3	Fair	Fair	Fair	Fair	Low	Retain	Transplanted by this contract on 8-8-2012
T150	<i>Cinnamomum camphora</i>	樟樹	-	-	-	-	-	-	-	-	Retain	Dead Tree and Removed by LCSD
T152	<i>Cinnamomum camphora</i>	樟樹	5	143	2	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 29-12-2012
T154	<i>Alstonia scholaris</i>	黑板木	3	124	1.5	Fair	Fair	Fair	Fair	Low	Retain	Handover to HK/2012/08
T155	<i>Alstonia scholaris</i>	黑板木	3.5	134	1	Fair	Fair	Fair	Fair	Low	Retain	Handover to HK/2012/08
T156	<i>Alstonia scholaris</i>	黑板木	3.5	124	1	Fair	Fair	Fair	Fair	Medium	Retain	Handover to HK/2012/08
T170	<i>Cinnamomum camphora</i>	樟樹	8	217	3	Fair	Fair	Fair	Fair	Medium	Retain	Handover to HK/2012/08
T171	<i>Cinnamomum camphora</i>	樟樹	7	159	4	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 11-12-2010
T172	<i>Cinnamomum camphora</i>	樟樹	8	185	4	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 10-12-2010
T173	<i>Cinnamomum camphora</i>	樟樹	8	201	3	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 10-12-2010
T174	<i>Cinnamomum camphora</i>	樟樹	9	293	5	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 10-12-2010
T175	<i>Cinnamomum camphora</i>	樟樹	8	274	4	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 10-12-2010
T176	<i>Cinnamomum camphora</i>	樟樹	8	217	4	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 13-1-2011
T177	<i>Cinnamomum camphora</i>	樟樹	8	175	4	Fair	Fair	Fair	Fair	Low	Retain	Transplanted by this contract on 10-12-2010

CONTRACT NO.: HK/2009/01

Tree No.	Botanical Name	Chinese Name	Height (m)	Trunk Diameter at Breast Height (DBH) (mm)	Spread (m)	Health		Form		Amenity Value High Medium Low	Original Recommendation	Remarks
						Good Fair Poor	Good Fair Poor					
T203	<i>Hibiscus tiliaceus</i>	黃槿	2.5	108	2	Fair	Fair	Medium	Retain		Under Contract HK/2009/02	
T204	<i>Hibiscus tiliaceus</i>	黃槿	2	134	2	Fair	Fair	Medium	Retain		Under Contract HK/2009/02	
T205	<i>Hibiscus tiliaceus</i>	黃槿	2.5	131	3	Fair	Fair	Medium	Retain		Under Contract HK/2009/02	
T206	<i>Hibiscus tiliaceus</i>	黃槿	2.5	127	3	Fair	Fair	Medium	Retain		Under Contract HK/2009/02	
T207	<i>Hibiscus tiliaceus</i>	黃槿	2	108	3	Fair	Fair	Medium	Retain		Under Contract HK/2009/02	
T239	<i>Hibiscus tiliaceus</i>	黃槿	2.5	153	3	Fair	Fair	Medium	Retain		Handed over to LCSD on 15 June 2016	
T240	<i>Hibiscus tiliaceus</i>	黃槿	2.8	127	2.5	Fair	Fair	Medium	Retain		Handed over to LCSD on 15 June 2016	
T241	<i>Hibiscus tiliaceus</i>	黃槿	2.9	127	2.5	Fair	Fair	Medium	Retain		Handed over to LCSD on 15 June 2016	
T242	<i>Hibiscus tiliaceus</i>	黃槿	2.6	137	2.5	Fair	Fair	Medium	Retain		TFA approved and felled	
T243	<i>Hibiscus tiliaceus</i>	黃槿	2.2	121	2.5	Fair	Fair	Medium	Transplant		Transplanted by this contract on 8-5-2014	
T244	<i>Hibiscus tiliaceus</i>	黃槿	2.3	131	2	Fair	Fair	Medium	Retain		Transplanted by this contract on 8-5-2014	
T245	<i>Hibiscus tiliaceus</i>	黃槿	2.2	137	2.5	Fair	Fair	Medium	Retain		TFA approved and felled	
T246	<i>Hibiscus tiliaceus</i>	黃槿	2.1	140	2.5	Fair	Fair	Medium	Retain		Handed over to LCSD on 15 June 2016	
T247	<i>Hibiscus tiliaceus</i>	黃槿	2	118	2.5	Fair	Fair	Medium	Retain		Handed over to LCSD on 15 June 2016	
T248	<i>Hibiscus tiliaceus</i>	黃槿	2.5	131	2.5	Fair	Fair	Medium	Retain		Handed over to LCSD on 15 June 2016	
T249	<i>Hibiscus tiliaceus</i>	黃槿	2.4	131	3	Fair	Fair	Medium	Retain		Handed over to LCSD on 15 June 2016	
T250	<i>Hibiscus tiliaceus</i>	黃槿	2.2	131	2.5	Fair	Fair	Medium	Retain		Dead tree and removed by ITS of HK/2009/01	
T251	<i>Hibiscus tiliaceus</i>	黃槿	2.5	134	2	Fair	Fair	Medium	Retain		Handed over to LCSD on 15 June 2016	
T252	<i>Hibiscus tiliaceus</i>	黃槿	2	150	2.5	Fair	Fair	Medium	Retain		Handed over to LCSD on 15 June 2016	
T253	<i>Hibiscus tiliaceus</i>	黃槿	2.2	140	2	Fair	Fair	Medium	Retain		Handed over to LCSD on 15 June 2016	
T254	<i>Hibiscus tiliaceus</i>	黃槿	2.1	131	2.5	Fair	Fair	Medium	Retain		Handed over to LCSD on 15 June 2016	
T255	<i>Hibiscus tiliaceus</i>	黃槿	2.1	131	2.5	Fair	Fair	Medium	Retain		Felled by LCSD	
T256	<i>Hibiscus tiliaceus</i>	黃槿	2.8	124	2.5	Fair	Fair	Medium	Retain		Handed over to LCSD on 15 June 2016	
T257	<i>Hibiscus tiliaceus</i>	黃槿	2.4	127	2.5	Fair	Fair	Medium	Retain		Handed over to LCSD on 15 June 2016	
T258	<i>Hibiscus tiliaceus</i>	黃槿	2.1	156	2.5	Fair	Fair	Medium	Retain		Felled by other party	
T259	<i>Hibiscus tiliaceus</i>	黃槿	3	191	3.5	Fair	Fair	Low	Transplant		Transplanted by this contract on 23-3-2012	
T260	<i>Hibiscus tiliaceus</i>	黃槿	3	210	3	Fair	Fair	Medium	Transplant		Transplanted by this contract on 23-3-2012	
T261	<i>Hibiscus tiliaceus</i>	黃槿	2.8	204	4	Fair	Fair	Medium	Transplant		Transplanted by this contract on 20-3-2012	
T262	<i>Hibiscus tiliaceus</i>	黃槿	3.5	223	3.5	Fair	Fair	Medium	Transplant		Transplanted by this contract on 19-3-2012	
T263	<i>Hibiscus tiliaceus</i>	黃槿	3.5	239	3.5	Fair	Fair	Medium	Transplant		Removed by others	
T264	<i>Hibiscus tiliaceus</i>	黃槿	3.5	178	2.5	Poor	Poor	Low	Transplant		Transplanted by this contract on 19-3-2012	
T265	<i>Hibiscus tiliaceus</i>	黃槿	2.2	131	2.5	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T266	<i>Hibiscus tiliaceus</i>	黃槿	2.1	121	2	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T267	<i>Hibiscus tiliaceus</i>	黃槿	2.2	140	2.5	Fair	Fair	Medium	Retain		Felled by other party - Typhoon	
T268	<i>Hibiscus tiliaceus</i>	黃槿	2.2	150	2.5	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T269	<i>Hibiscus tiliaceus</i>	黃槿	2.3	127	2	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T270	<i>Hibiscus tiliaceus</i>	黃槿	2.2	131	2	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T271	<i>Hibiscus tiliaceus</i>	黃槿	1.5	134	1	Poor	Poor	Low	Transplant		Transplanted by this contract on 24-4-2014	
T272	<i>Hibiscus tiliaceus</i>	黃槿	2.3	127	2	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T273	<i>Hibiscus tiliaceus</i>	黃槿	2.3	127	2.5	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T274	<i>Hibiscus tiliaceus</i>	黃槿	2.2	137	2.5	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T275	<i>Hibiscus tiliaceus</i>	黃槿	2.1	127	2	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T276	<i>Hibiscus tiliaceus</i>	黃槿	2.1	131	2.5	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T277	<i>Hibiscus tiliaceus</i>	黃槿	2.1	124	2.5	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T278	<i>Hibiscus tiliaceus</i>	黃槿	2.1	124	2.5	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T279	<i>Hibiscus tiliaceus</i>	黃槿	2.1	121	2.5	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T280	<i>Hibiscus tiliaceus</i>	黃槿	2.2	121	2.5	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T281	<i>Hibiscus tiliaceus</i>	黃槿	2.2	140	2.5	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T282	<i>Hibiscus tiliaceus</i>	黃槿	2.3	143	2	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T283	<i>Hibiscus tiliaceus</i>	黃槿	2.1	134	2.5	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T284	<i>Hibiscus tiliaceus</i>	黃槿	2	146	2.5	Fair	Fair	Medium	Transplant		Transplanted by this contract on 24-4-2014	
T285	<i>Delonix regia</i>	鳳凰木	6.5	258	8	Fair	Poor	Medium	Transplant		Transplanted by this contract on 18-6-2012	
T286	<i>Albizia lebbek</i>	大葉合歡	5.5	182	3.5	Fair	Poor	Medium	Transplant		Transplanted by this contract on 18-6-2012	
T287	<i>Delonix regia</i>	鳳凰木	5	315	6	Fair	Fair	Medium	Transplant		Transplanted by this contract on 18-6-2012	
T293	<i>Aleurites moluccana</i>	石栗	10	296	3	Fair	Fair	Medium	Retain		Under Contract HK/2009/02	
T294	<i>Aleurites moluccana</i>	石栗	7	178	3	Fair	Fair	Medium	Retain		Under Contract HK/2009/02	
T319	<i>Erythrina variegata</i>	刺桐	7	197	5	Fair	Poor	Medium	Retain		Felled by SCL Project 1123 in June 2015	
T320	<i>Delonix regia</i>	鳳凰木	8	255	0.5	Fair	Fair	Low	Retain		Felled by SCL Project 1123 in June 2015	
T321	<i>Astonia scholaris</i>	黑板木	4	121	2	Fair	Fair	Medium	Retain		Felled by SCL Project 1123 in June 2015	
T327	<i>Delonix regia</i>	鳳凰木	6	159	14	Fair	Fair	Medium	Retain		Felled by other party - Typhoon	
T328	<i>Araucaria heterophylla</i>	南洋杉	-	-	-	-	-	-	Retain		Missing before commencement of contract	

CONTRACT NO.: HK/2009/01

Tree No.	Botanical Name	Chinese Name	Height (m)	Trunk Diameter at Breast Height (DBH) (mm)	Spread (m)	Health		Form		Amenity Value High Medium Low	Original Recommendation	Remarks
						Good Fair Poor	Good Fair Poor					
T330A	<i>Aleurites moluccana</i>	石栗	3.5	102	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 7-4-2011
T331A	<i>Aleurites moluccana</i>	石栗	6	245	5	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 7-4-2011
T332	<i>Aleurites moluccana</i>	石栗	4	105	4	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 7-4-2011
T333	<i>Aleurites moluccana</i>	石栗	4.5	175	4	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 7-4-2011
T334	<i>Aleurites moluccana</i>	石栗	5	185	5	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 8-4-2011
T336	<i>Aleurites moluccana</i>	石栗	5	210	4	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 8-4-2011
T337	<i>Aleurites moluccana</i>	石栗	6	242	5	Fair	Fair	Fair	Fair	Medium	Retain	Handover to HK/2012/08
T349	<i>Hibiscus tiliaceus</i>	黃槿	7	255	7	Fair	Fair	Fair	Fair	Medium	Retain	Handover to HK/2012/08
T350	<i>Hibiscus tiliaceus</i>	黃槿	8	287	6	Fair	Fair	Fair	Fair	Medium	Retain	Handover to HK/2012/08
T351	<i>Hibiscus tiliaceus</i>	黃槿	7	293	6	Fair	Fair	Fair	Fair	Medium	Retain	Handover to HK/2012/08
T352	<i>Hibiscus tiliaceus</i>	黃槿	7	255	7	Fair	Fair	Fair	Fair	Medium	Transplant	Handover to HK/2012/08
T353	<i>Hibiscus tiliaceus</i>	黃槿	7	252	7	Fair	Fair	Fair	Fair	Medium	Retain	Handover to HK/2012/08
T354	<i>Hibiscus tiliaceus</i>	黃槿	8	271	7	Fair	Fair	Fair	Fair	Medium	Transplant	Handover to HK/2012/08
T360	<i>Acacia confusa</i>	台灣相思	4	143	4	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 29-8-2014
T362	<i>Acacia confusa</i>	台灣相思	4	96	3	Fair	Fair	Fair	Fair	Medium	Transplant	TFA approved and Felled
T363	<i>Acacia confusa</i>	台灣相思	4	166	5	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 29-8-2014
T364	<i>Acacia confusa</i>	台灣相思	5	108	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 29-8-2014
T365	<i>Acacia confusa</i>	台灣相思	5	137	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 29-8-2014
T366	<i>Acacia confusa</i>	台灣相思	6	172	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 29-8-2014
T367	<i>Acacia confusa</i>	台灣相思	5	162	3	Fair	Fair	Fair	Fair	Medium	Transplant	approved by LCSD and felled by this contract on 29-8-2014
T368	<i>Acacia confusa</i>	台灣相思	5	102	3	Fair	Fair	Fair	Fair	Medium	Transplant	approved by LCSD and felled by this contract on 29-8-2014
T369	<i>Acacia confusa</i>	台灣相思	4	159	4	Fair	Fair	Fair	Fair	Medium	Transplant	approved by LCSD and felled by this contract on 29-8-2014
T370	<i>Acacia confusa</i>	台灣相思	4	166	5	Fair	Fair	Fair	Fair	Medium	Transplant	approved by LCSD and felled by this contract on 29-8-2014
T400	<i>Araucaria heterophylla</i>	南洋杉	6	280	4	Fair	Fair	Fair	Fair	Medium	Retain	Felled by SCL Project 1123 in June 2015
T420	<i>Cassia siamea</i>	欖刀木	9	197	6	Fair	Fair	Fair	Fair	Medium	Retain	Felled by SCL Project 1123 in June 2015
T423	<i>Alstonia scholaris</i>	黑板木	6	207	3	Fair	Fair	Fair	Fair	Medium	Retain	Felled by SCL Project 1123 in June 2015
T424	<i>Alstonia scholaris</i>	黑板木	5	159	3	Fair	Fair	Fair	Fair	Medium	Retain	Felled by SCL Project 1123 in June 2015
T425	<i>Alstonia scholaris</i>	黑板木	7	175	4	Fair	Fair	Fair	Fair	Medium	Retain	Felled by SCL Project 1123 in June 2015
T426	<i>Alstonia scholaris</i>	黑板木	6	159	3	Fair	Fair	Fair	Fair	Medium	Retain	Felled by other party - Typhoon
T430	<i>Hibiscus tiliaceus</i>	黃槿	-	-	-	-	-	-	-	-	Retain	Under Contract HK/2009/02
T431	<i>Hibiscus tiliaceus</i>	黃槿	5	134	2.5	Fair	Fair	Fair	Fair	Medium	Retain	Under Contract HK/2009/02
T432	<i>Hibiscus tiliaceus</i>	黃槿	5	108	2.5	Fair	Fair	Fair	Fair	Medium	Retain	Under Contract HK/2009/02
T433	<i>Hibiscus tiliaceus</i>	黃槿	5	127	2.5	Fair	Fair	Fair	Fair	Medium	Retain	Under Contract HK/2009/02
T434	<i>Hibiscus tiliaceus</i>	黃槿	5	143	2.5	Fair	Fair	Fair	Fair	Medium	Retain	Under Contract HK/2009/02
T435	<i>Hibiscus tiliaceus</i>	黃槿	5	121	2.5	Fair	Fair	Fair	Fair	Medium	Retain	Under Contract HK/2009/02
T436	<i>Hibiscus tiliaceus</i>	黃槿	5	124	2.5	Fair	Fair	Fair	Fair	Medium	Retain	Under Contract HK/2009/02
T437	<i>Hibiscus tiliaceus</i>	黃槿	5	137	2.5	Fair	Fair	Fair	Fair	Medium	Retain	Under Contract HK/2009/02
T447	<i>Hibiscus tiliaceus</i>	黃槿	6	143	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 23-6-2010
T448	<i>Hibiscus tiliaceus</i>	黃槿	6	239	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 23-6-2010
T449	<i>Hibiscus tiliaceus</i>	黃槿	6	131	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 23-6-2010
T450	<i>Hibiscus tiliaceus</i>	黃槿	6	140	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 23-6-2010
T451	<i>Hibiscus tiliaceus</i>	黃槿	6	134	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 23-6-2010
T452	<i>Hibiscus tiliaceus</i>	黃槿	6	191	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 23-6-2010
T453	<i>Hibiscus tiliaceus</i>	黃槿	6	239	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 23-3-2012
T454	<i>Hibiscus tiliaceus</i>	黃槿	6	258	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 22-3-2012
T455	<i>Hibiscus tiliaceus</i>	黃槿	6	223	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 22-3-2012
T456	<i>Hibiscus tiliaceus</i>	黃槿	6	197	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 22-3-2012
T457	<i>Hibiscus tiliaceus</i>	黃槿	6	201	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 22-3-2012
T458	<i>Hibiscus tiliaceus</i>	黃槿	6	248	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 20-3-2012
T459	<i>Hibiscus tiliaceus</i>	黃槿	6	255	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 20-3-2012
T460	<i>Phoenix hanceana</i>	刺葵	4	255	1.5	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 11-12-2010
T461	<i>Phoenix hanceana</i>	刺葵	7	287	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 11-12-2010
T462	<i>Phoenix hanceana</i>	刺葵	6	573	3	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 11-12-2010
T463	<i>Phoenix hanceana</i>	刺葵	5	573	3.5	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 11-12-2010
T464	<i>Phoenix hanceana</i>	刺葵	7	478	5	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 11-12-2010
T465	<i>Phoenix hanceana</i>	刺葵	7	573	5	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 11-12-2010
T466	<i>Phoenix hanceana</i>	刺葵	7	478	5	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 11-12-2010
T467	<i>Phoenix hanceana</i>	刺葵	7	382	5	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 11-12-2010
T468	<i>Alstonia scholaris</i>	黑板木	6.5	162	3	Fair	Fair	Fair	Fair	Medium	Transplant	Handover to HK/2012/08
T469	<i>Alstonia scholaris</i>	黑板木	6.5	153	3	Fair	Fair	Fair	Fair	Medium	Retain	Handover to HK/2012/08
T470	<i>Alstonia scholaris</i>	黑板木	-	-	-	-	-	-	-	-	Retain	TFA approved and felled

CONTRACT NO.: HK/2009/01

Tree No.	Botanical Name	Chinese Name	Height (m)	Trunk Diameter at Breast Height (DBH) (mm)	Spread (m)	Health		Form		Amenity Value High Medium Low	Original Recommendation	Remarks
						Good Fair Poor	Good Fair Poor					
T471	<i>Alstonia scholaris</i>	黑板木	6.5	124	2	Fair	Poor	Medium	Retain	Handover to HK/2012/08		
T472	<i>Alstonia scholaris</i>	黑板木	7	124	4	Fair	Poor	Medium	Retain	Handover to HK/2012/08		
T473	<i>Alstonia scholaris</i>	黑板木	4	102	4	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T474	<i>Alstonia scholaris</i>	黑板木	4	127	4.5	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T475	<i>Alstonia scholaris</i>	黑板木	6	159	2.5	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T476	<i>Alstonia scholaris</i>	黑板木	6	108	2	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T477	<i>Alstonia scholaris</i>	黑板木	4	159	2	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T478	<i>Alstonia scholaris</i>	黑板木	5	127	3	Fair	Fair	Medium	Retain	Transplanted by this contract on 25-2-2011		
T480	<i>Alstonia scholaris</i>	黑板木	4	111	3	Fair	Fair	Medium	Retain	Transplanted by this contract on 25-2-2011		
T481	<i>Alstonia scholaris</i>	黑板木	4	108	3	Fair	Fair	Medium	Retain	Transplanted by this contract on 7-8-2012		
T482	<i>Alstonia scholaris</i>	黑板木	5	188	3	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T485	<i>Alstonia scholaris</i>	黑板木	4	102	3	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T487	<i>Alstonia scholaris</i>	黑板木	5	150	3.5	Poor	Fair	Medium	Retain	Handover to HK/2012/08		
T488	<i>Alstonia scholaris</i>	黑板木	5	207	3.8	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T489	<i>Alstonia scholaris</i>	黑板木	3	105	2	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T490	<i>Alstonia scholaris</i>	黑板木	7	143	3	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T491	<i>Alstonia scholaris</i>	黑板木	7	197	4	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T492	<i>Bauhinia blakeana</i>	洋紫荊	8	175	5	Fair	Fair	Medium	Transplant	Handover to HK/2012/08		
T493	<i>Hibiscus tiliaceus</i>	黃槿	8	414	6	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T495	<i>Hibiscus tiliaceus</i>	黃槿	10	296	7	Fair	Fair	Medium	Transplant	Handover to HK/2012/08		
T496	<i>Bauhinia blakeana</i>	洋紫荊	4	102	3	Fair	Fair	Medium	Transplant	Handover to HK/2012/08		
T498	<i>Bauhinia spp.</i>	羊蹄甲	6	96	2	Fair	Fair	Medium	Transplant	Handover to HK/2012/08		
T499	<i>Bauhinia blakeana</i>	洋紫荊	7	140	4	Fair	Poor	Medium	Retain	Handover to HK/2012/08		
T503	<i>Aleurites moluccana</i>	石栗	8	223	3.5	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T504	<i>Aleurites moluccana</i>	石栗	8	207	3.5	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016		
T505	<i>Aleurites moluccana</i>	石栗	8	159	3.5	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016		
T506	<i>Aleurites moluccana</i>	石栗	8	223	3.5	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016		
T507	<i>Aleurites moluccana</i>	石栗	8	283	3.5	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016		
T508	<i>Aleurites moluccana</i>	石栗	8	194	3.5	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016		
T509	<i>Aleurites moluccana</i>	石栗	8	303	4.5	Fair	Fair	Medium	Retain	Handed over to LCSD on 15 June 2016		
T549	<i>Melaleuca leucadendron</i>	白千層	7	221	4	Fair	Fair	Medium	Retain	Has been maintained by private owner		
T550	<i>Melaleuca leucadendron</i>	白千層	6	207	4	Fair	Fair	Medium	Retain	Has been maintained by private owner		
T552	<i>Melaleuca leucadendron</i>	白千層	7	223	4	Fair	Fair	Medium	Retain	Has been maintained by private owner		
T553	<i>Melaleuca leucadendron</i>	白千層	7	96	4	-	-	-	Retain	Dead tree and removed by ITS of HK/2009/01		
T554	<i>Melaleuca leucadendron</i>	白千層	8	127	4	Fair	Fair	Medium	Retain	Has been maintained by private owner		
T555	<i>Melaleuca leucadendron</i>	白千層	8	127	4	Fair	Fair	Medium	Retain	Has been maintained by private owner		
T556	<i>Melaleuca leucadendron</i>	白千層	8	207	4	-	-	-	Retain	Dead tree and removed by ITS of HK/2009/01		
T557	<i>Melaleuca leucadendron</i>	白千層	8	239	4	Fair	Fair	Medium	Retain	Has been maintained by private owner		
T558	<i>Melaleuca leucadendron</i>	白千層	8	223	4	Fair	Fair	Medium	Retain	Has been maintained by private owner		
T559	<i>Melaleuca leucadendron</i>	白千層	8	127	4	Fair	Fair	Medium	Retain	Has been maintained by private owner		
T560	<i>Melaleuca leucadendron</i>	白千層	8	255	4	Fair	Fair	Medium	Retain	Has been maintained by private owner		
T561	<i>Melaleuca leucadendron</i>	白千層	8	255	4	Fair	Fair	Medium	Retain	Has been maintained by private owner		
T562	<i>Melaleuca leucadendron</i>	白千層	8	303	4	Fair	Fair	Medium	Retain	Has been maintained by private owner		
T563	<i>Melaleuca leucadendron</i>	白千層	8	223	4	Fair	Poor	Medium	Retain	Has been maintained by private owner		
T564	<i>Livistona chinensis</i>	蒲葵	1.5	287	4	Fair	Fair	Fair	Retain	Handover to HK/2012/08		
T568	<i>Livistona chinensis</i>	蒲葵	5	255	2	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T570	<i>Livistona chinensis</i>	蒲葵	4	255	3	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T571	<i>Ficus microcarpa</i>	細葉榕	7	255	3	Fair	Fair	Medium	Transplant	Handover to HK/2012/08		
T572	<i>Ficus microcarpa</i>	細葉榕	8	296	5	Fair	Fair	Medium	Transplant	Handover to HK/2012/08		
T574	<i>Acacia confusa</i>	台灣相思	8	223	6	Fair	Fair	Medium	Transplant	Handover to HK/2012/08		
T575	<i>Acacia confusa</i>	台灣相思	2	121	4	Fair	Fair	Fair	Transplant	Handover to HK/2012/08		
T576	<i>Livistona chinensis</i>	蒲葵	4	573	1	Fair	Fair	Medium	Transplant	Handover to HK/2012/08		
T578	<i>Livistona chinensis</i>	蒲葵	1.5	255	5	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T579	<i>Livistona chinensis</i>	蒲葵	3	382	1.5	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T580	<i>Livistona chinensis</i>	蒲葵	3	382	2	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T581	<i>Livistona chinensis</i>	蒲葵	3	382	2	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T582	<i>Livistona chinensis</i>	蒲葵	1.5	159	2	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T583	<i>Livistona chinensis</i>	蒲葵	3	318	1.5	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T584	<i>Livistona chinensis</i>	蒲葵	1.5	159	2	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T585	<i>Livistona chinensis</i>	蒲葵	3	159	1.5	Fair	Fair	Medium	Retain	Handover to HK/2012/08		
T586	<i>Livistona chinensis</i>	蒲葵	8	446	2	Fair	Fair	Medium	Retain	Handover to HK/2012/08		

CONTRACT NO.: HK/2009/01

Tree No.	Botanical Name	Chinese Name	Height (m)	Trunk Diameter at Breast Height (DBH) (mm)	Spread (m)	Health		Form		Amenity Value High Medium Low	Original Recommendation	Remarks
						Good	Fair	Poor	Good			
T600	<i>Livistona chinensis</i>	蒲葵	5	182	3	Fair	Fair	Fair	Fair	Medium	Transplant	Site has been hand over to LCSD on 12-6-2015
T601	<i>Livistona chinensis</i>	蒲葵	5	183	3	Fair	Fair	Fair	Fair	Medium	Transplant	Site has been hand over to LCSD on 12-6-2015
T602	<i>Delonix regia</i>	鳳凰木	10	268	5	Fair	Fair	Fair	Fair	Medium	Transplant	Site has been hand over to LCSD on 12-6-2015
T603	<i>Delonix regia</i>	鳳凰木	11	213	5	Fair	Fair	Fair	Fair	Medium	Transplant	Site has been hand over to LCSD on 12-6-2015
T604	<i>Ficus benamina</i>	垂葉榕	7	271	6	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 12-6-2015
T605	<i>Plumeria rubra</i>	雞蛋花	5	213	6	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 13-12-2010
T606	<i>Plumeria rubra</i>	雞蛋花	7	162	5	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 13-12-2010
T607	<i>Callistemon viminalis</i>	串錢柳	7	185	4	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T608	<i>Callistemon viminalis</i>	串錢柳	7	182	4	Fair	Poor	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T610	<i>Lagerstroemia speciosa</i>	大花紫薇	7	156	4	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 13-12-2010
T611	<i>Callistemon viminalis</i>	串錢柳	7	201	5	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 6-8-2011
T612	<i>Syagrus romanzoffiana</i>	皇后葵	9	191	5	Fair	Fair	Fair	Fair	Medium	Transplant	Site has been hand over to LCSD on 6-9-2012
T613	<i>Callistemon viminalis</i>	串錢柳	6	96	3	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 6-8-2011
T614	<i>Lagerstroemia speciosa</i>	大花紫薇	8	146	4	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 13-12-2010
T615	<i>Ravenala madagascariensis</i>	旅人蕉	9	201	4	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 6-8-2011
T616	<i>Syagrus romanzoffiana</i>	皇后葵	9	207	5	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T617	<i>Syagrus romanzoffiana</i>	皇后葵	9	199	5	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T618	<i>Callistemon viminalis</i>	串錢柳	7	163	3	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 13-12-2010
T619	<i>Lagerstroemia speciosa</i>	大花紫薇	8	153	5	Fair	Fair	Fair	Fair	Medium	Transplant	Transplanted by this contract on 13-12-2010
T620	<i>Ravenala madagascariensis</i>	旅人蕉	9	220	4	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 6-8-2011
T621	<i>Syagrus romanzoffiana</i>	皇后葵	9	201	5	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T624	<i>Syagrus romanzoffiana</i>	皇后葵	9	207	5	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T625	<i>Lagerstroemia speciosa</i>	大花紫薇	8	239	6	Poor	Fair	Fair	Fair	Medium	Transplant	Site has been hand over to LCSD on 6-9-2012
T626	<i>Ficus benamina</i>	垂葉榕	11	494	8	Fair	Fair	Fair	Fair	Medium	Transplant	Site has been hand over to LCSD on 12-6-2015
T627	<i>Ravenala madagascariensis</i>	旅人蕉	9	223	4	Fair	Fair	Fair	Fair	Medium	Transplant	Site has been hand over to LCSD on 12-6-2015
T628	<i>Ficus benamina</i>	垂葉榕	10	1003	8	Fair	Fair	Fair	Fair	Medium	Retain	Located inside other project
T629	<i>Delonix regia</i>	鳳凰木	10	309	8	Fair	Fair	Fair	Fair	Medium	Transplant	Site has been hand over to LCSD on 12-6-2015
T630	<i>Ravenala madagascariensis</i>	旅人蕉	6	239	4	-	-	-	-	-	Transplant	Dead tree and removed by ITS of HK/2009/01
T631	<i>Ravenala madagascariensis</i>	旅人蕉	8	268	5	Fair	Fair	Fair	Fair	Medium	Transplant	Site has been hand over to LCSD on 12-6-2015
T632	<i>Livistona chinensis</i>	蒲葵	5	159	3	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 12-6-2015
T633	<i>Livistona chinensis</i>	蒲葵	5	194	3	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 12-6-2015
T634	<i>Livistona chinensis</i>	蒲葵	5	210	3	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 12-6-2015
T635	<i>Livistona chinensis</i>	蒲葵	5	210	3	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 12-6-2015
T636	<i>Ravenala madagascariensis</i>	旅人蕉	10	252	4	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T637	<i>Livistona chinensis</i>	蒲葵	5	207	3	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 12-6-2015
T638	<i>Livistona chinensis</i>	蒲葵	5	146	2	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T639	<i>Ravenala madagascariensis</i>	旅人蕉	10	277	4	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T640	<i>Livistona chinensis</i>	蒲葵	5	309	3	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 12-6-2015
T641	<i>Delonix regia</i>	鳳凰木	10	290	7	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 12-6-2015
T642	<i>Livistona chinensis</i>	蒲葵	5	185	3	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 12-6-2015
T643	<i>Livistona chinensis</i>	蒲葵	5	185	3	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 12-6-2015
T644	<i>Livistona chinensis</i>	蒲葵	5	188	3	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 12-6-2015
T645	<i>Callistemon viminalis</i>	串錢柳	7	153	4	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T646	<i>Callistemon viminalis</i>	串錢柳	-	-	-	-	-	-	-	-	Transplant	Removed by others
T647	<i>Callistemon viminalis</i>	串錢柳	5	124	3	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T648	<i>Callistemon viminalis</i>	串錢柳	7	99	3	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 6-8-2011
T649	<i>Callistemon viminalis</i>	串錢柳	7	252	5	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T650	<i>Callistemon viminalis</i>	串錢柳	8	207	5	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T651	<i>Cassia surattensis</i>	黃槐	6	100	3	Poor	Poor	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T652	<i>Archontophoenix Alexandrae</i>	假檳榔	12	232	5	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T653	<i>Juniperus chinensis cv. Kaizuka</i>	龍柏	6	96	3	Fair	Good	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T654	<i>Cassia surattensis</i>	黃槐	-	-	-	-	-	-	-	-	Retain	Removed by others - Typhoon
T655	-	-	-	-	-	-	-	-	-	-	Retain	Missing before commencement of contract
T656	<i>Cassia surattensis</i>	黃槐	4	127	3	Poor	Poor	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T657	<i>Ficus benamina</i>	垂葉榕	10	430	1.7	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T658	<i>Phoenix roebelenii</i>	日本葵	6	96	2	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T659	<i>Phoenix roebelenii</i>	日本葵	-	-	-	-	-	-	-	-	Retain	Removed by others
T660	<i>Phoenix roebelenii</i>	日本葵	6	96	2	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T661	<i>Archontophoenix Alexandrae</i>	假檳榔	11	223	3	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T662	<i>Ficus benamina</i>	垂葉榕	11	318	7	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T663	<i>Ficus benamina</i>	垂葉榕	11	303	7	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012

CONTRACT NO.: HK/2009/01

Tree No.	Botanical Name	Chinese Name	Height (m)	Trunk Diameter at Breast Height (DBH) (mm)	Spread (m)	Health		Form		Amenity Value High Medium Low	Original Recommendation	Remarks
						Good Fair Poor	Good Fair Poor					
T664	<i>Callistemon viminalis</i>	串錢柳	-	-	-	-	-	-	-	-	Retain	Removed by others
T665	<i>Ficus benjamina</i>	垂葉榕	11	334	7	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T666	<i>Syagrus romanzoffiana</i>	皇后葵	9	197	5	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T667	<i>Syagrus romanzoffiana</i>	皇后葵	9	159	5	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T668	<i>Syagrus romanzoffiana</i>	皇后葵	9	182	5	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T669	<i>Araucaria heterophylla</i>	南洋杉	7	204	4	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T670	<i>Lagerstroemia speciosa</i>	大花紫薇	8	213	5	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T671	<i>Araucaria heterophylla</i>	南洋杉	7	115	3	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T672	<i>Lagerstroemia speciosa</i>	大花紫薇	9	172	4	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T673	<i>Delonix regia</i>	鳳凰木	7	287	7	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 6-8-2011
T674	<i>Delonix regia</i>	鳳凰木	11	366	9	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012
T675	<i>Delonix regia</i>	鳳凰木	9	248	7	Fair	Fair	Fair	Fair	Medium	Retain	Transplanted by this contract on 6-8-2011
T676	<i>Delonix regia</i>	鳳凰木	-	-	-	-	-	-	-	-	Transplant	Dead tree and removed by ITS of HK/2009/01
T677	<i>Delonix regia</i>	鳳凰木	10	398	10	Fair	Fair	Fair	Fair	Medium	Transplant	Site has been hand over to LCSD on 6-9-2012
T679	<i>Lagerstroemia speciosa</i>	大花紫薇	10	197	5	Poor	Fair	Fair	Fair	Medium	Transplant	Site has been hand over to LCSD on 6-9-2012
T680	<i>Lagerstroemia speciosa</i>	大花紫薇	-	-	-	-	-	-	-	-	Retain	Missing before commencement of contract
T681	<i>Lagerstroemia speciosa</i>	大花紫薇	-	-	-	-	-	-	-	-	Retain	Missing before commencement of contract
T682	<i>Lagerstroemia speciosa</i>	大花紫薇	-	-	-	-	-	-	-	-	Retain	Missing before commencement of contract
T683	<i>Lagerstroemia speciosa</i>	大花紫薇	7	201	3	Fair	Fair	Fair	Fair	Medium	Retain	Site has been hand over to LCSD on 6-9-2012



Tree No.	Botanical Name	Chinese Name	Height (m)	Trunk Diameter at Breast Height (DBH) (mm)	Spread (m)	Health	Form	Amenity Value	Recommendation	Survival Rate After Transplant (High/Medium/Low)	Remarks
						Good Fair Poor	Good Fair Poor	High Medium Low			
A001	<i>Melaleuca leucadendron</i>	白千層	6	153	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A002	<i>Aleurites moluccana</i>	石栗	7	101	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 8-4-2011
A003	<i>Acacia confusa</i>	台灣相思	7	102	3	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A004	<i>Acacia confusa</i>	台灣相思	7	152	4	Poor	Poor	Low	Fell	Low	Removed by this contract
A005	<i>Livistona chinensis</i>	蒲葵	5	158	3	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A006	<i>Acacia confusa</i>	台灣相思	6	157	5	Fair	Fair	Medium	Retain	Low	Handover to HK/2012/08
A007	<i>Acacia confusa</i>	台灣相思	5	156	4	Poor	Poor	Low	Fell	Low	Removed by this contract
A008	<i>Acacia confusa</i>	台灣相思	6	156	3	Poor	Poor	Low	Fell	Low	Removed by this contract
A009	<i>Livistona chinensis</i>	蒲葵	5	149	3	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A010	<i>Livistona chinensis</i>	蒲葵	6	145	3	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A011	<i>Livistona chinensis</i>	蒲葵	7	144	2	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A012	<i>Cinnamomum camphora</i>	樟	8	400	4	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A013	<i>Cinnamomum camphora</i>	樟	7	260	3	Fair	Fair	Medium	Retain	Low	Handover to HK/2012/08
A014	<i>Ficus microcarpa</i>	細葉榕	7	108	4	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A015	<i>Ficus microcarpa</i>	細葉榕	10	550	10	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A016	<i>Ficus microcarpa</i>	細葉榕	6	221	5	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A017	<i>Acacia confusa</i>	台灣相思	5	165	4	Poor	Poor	Low	Fell	Low	Removed by this contract
A018	<i>Cinnamomum camphora</i>	樟	4	110	4	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A019	<i>Cinnamomum camphora</i>	樟	5	212	6	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A020	<i>Hibiscus tiliaceus</i>	黃槿	2	212	1	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A021	<i>Alstonia scholaris</i>	黑板木	5	111	5	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A022	<i>Alstonia scholaris</i>	黑板木	4	113	4	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A023	<i>Phoenix hanceana</i>	刺葵	7	107	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 13-1-2011
A024	<i>Phoenix hanceana</i>	刺葵	4	167	4	Poor	Poor	Medium	Fell	Low	Removed by this contract
A025	<i>Alstonia scholaris</i>	黑板木	5	143	5	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 13-1-2011
A026	<i>Alstonia scholaris</i>	黑板木	6	142	5	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A027	<i>Alstonia scholaris</i>	黑板木	7	141	5	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A028	<i>Alstonia scholaris</i>	黑板木	7	140	3	Fair	Poor	Medium	Retain	Medium	Handover to HK/2012/08
A029	<i>Alstonia scholaris</i>	黑板木	6	146	4	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A030	<i>Alstonia scholaris</i>	黑板木	5	151	5	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A031	<i>Alstonia scholaris</i>	黑板木	7	153	5	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A032	<i>Ficus microcarpa</i>	細葉榕	6	442	4	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A033	<i>Ficus microcarpa</i>	細葉榕	6	335	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A034	<i>Ficus microcarpa</i>	細葉榕	6	216	4	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A035	<i>Ficus microcarpa</i>	細葉榕	5	234	4	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A036	<i>Ficus microcarpa</i>	細葉榕	6	238	4	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A037	<i>Ficus microcarpa</i>	細葉榕	5	248	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A038	<i>Ficus microcarpa</i>	細葉榕	7	368	6	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A039	<i>Ficus microcarpa</i>	細葉榕	5	238	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A040	<i>Ficus microcarpa</i>	細葉榕	6	200	6	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A041	<i>Ficus microcarpa</i>	細葉榕	5	177	6	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A042	<i>Ficus microcarpa</i>	細葉榕	7	173	6	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A043	<i>Ficus microcarpa</i>	細葉榕	5	180	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A044	<i>Ficus microcarpa</i>	細葉榕	6	191	6	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A045	<i>Ficus microcarpa</i>	細葉榕	5	230	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A046	<i>Ficus microcarpa</i>	細葉榕	7	324	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A047	<i>Ficus microcarpa</i>	細葉榕	7	268	6	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A048	<i>Ficus microcarpa</i>	細葉榕	7	192	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A049	<i>Ficus microcarpa</i>	細葉榕	6	262	6	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A050	<i>Ficus microcarpa</i>	細葉榕	5	202	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A051	<i>Ficus microcarpa</i>	細葉榕	5	365	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A052	<i>Ficus microcarpa</i>	細葉榕	5	347	6	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A053	<i>Ficus microcarpa</i>	細葉榕	5	308	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A054	<i>Ficus microcarpa</i>	細葉榕	5	256	6	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A055	<i>Ficus microcarpa</i>	細葉榕	5	202	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A056	<i>Ficus microcarpa</i>	細葉榕	6	159	4	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A057	<i>Ficus microcarpa</i>	細葉榕	5	208	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A058	<i>Ficus microcarpa</i>	細葉榕	5	222	6	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A059	<i>Ficus microcarpa</i>	細葉榕	6	67	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A060	<i>Ficus microcarpa</i>	細葉榕	5	278	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A061	<i>Ficus microcarpa</i>	細葉榕	6	171	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A062	<i>Ficus microcarpa</i>	細葉榕	5	208	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A063	<i>Ficus microcarpa</i>	細葉榕	6	137	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A064	<i>Ficus microcarpa</i>	細葉榕	6	165	6	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A065	<i>Ficus microcarpa</i>	細葉榕	5	302	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A066	<i>Ficus microcarpa</i>	細葉榕	7	193	6	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A067	<i>Ficus microcarpa</i>	細葉榕	5	341	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A068	<i>Ficus microcarpa</i>	細葉榕	5	240	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A069	<i>Ficus microcarpa</i>	細葉榕	6	186	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A070	<i>Ficus microcarpa</i>	細葉榕	5	198	7	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A071	<i>Ficus microcarpa</i>	細葉榕	5	267	4	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A072	<i>Ficus microcarpa</i>	細葉榕	6	453	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A073	<i>Roystonea regia</i>	王棕	5	369	4	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A074	<i>Roystonea regia</i>	王棕	5	196	5	Fair	Fair	Medium	Retain	Medium	Handed over to LCSD on 11 August 2016
A075	<i>Roystonea regia</i>	王棕	5	296	5	Fair	Fair	Medium	Retain	Medium	Outside site boundary
A076	<i>Roystonea regia</i>	王棕	7	256	7	Fair	Fair	Medium	Retain	Medium	Outside site boundary
A077	<i>Roystonea regia</i>	王棕	4	343	5	Fair	Fair	Medium	Retain	Medium	Outside site boundary
A078	<i>Roystonea regia</i>	王棕	5	433	5	Fair	Fair	Medium	Retain	Medium	Outside site boundary

Tree No.	Botanical Name	Chinese Name	Height (m)	Trunk Diameter at Breast Height (DBH) (mm)	Spread (m)	Health	Form	Amenity Value (High/Medium/Low)	Recommendation	Survival Rate After Transplant (High/Medium/Low)	Remarks
A099	<i>Acacia confusa</i>	台灣相思	6	151	5	Dead	Poor	Medium	Fell	Low	TFA is waiting for LCSD approval
A100	<i>Ficus microcarpa</i>	細葉榕	5	150	5	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 14-6-2010
A101	<i>Ficus microcarpa</i>	細葉榕	5	141	6	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 14-6-2010
A102	<i>Ficus microcarpa</i>	細葉榕	5	142	7	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 14-6-2010
A103	<i>Ficus microcarpa</i>	細葉榕	5	145	7	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 14-6-2010
A104	<i>Ficus microcarpa</i>	細葉榕	5	144	4	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 14-6-2010
A105	<i>Ficus microcarpa</i>	細葉榕	5	158	4	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 14-6-2010
A106	<i>Ficus microcarpa</i>	細葉榕	5	158	5	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 14-6-2010
A107	<i>Ficus microcarpa</i>	細葉榕	6	160	5	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 14-6-2010
A108	<i>Ficus microcarpa</i>	細葉榕	5	170	6	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 14-6-2010
A109	<i>Ficus microcarpa</i>	細葉榕	5	172	5	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 5-6-2010
A110	<i>Ficus microcarpa</i>	細葉榕	5	175	4	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 5-6-2010
A111	<i>Ficus microcarpa</i>	細葉榕	5	174	4	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 5-6-2010
A112	<i>Ficus microcarpa</i>	細葉榕	5	174	5	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 5-6-2010
A113	<i>Ficus microcarpa</i>	細葉榕	5	170	5	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 5-6-2010
A114	<i>Ficus microcarpa</i>	細葉榕	5	172	5	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 5-6-2010
A115	<i>Ficus microcarpa</i>	細葉榕	5	182	5	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 5-6-2010
A116	<i>Ficus microcarpa</i>	細葉榕	5	174	4	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 5-6-2010
A117	<i>Ficus microcarpa</i>	細葉榕	5	176	4	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 5-6-2010
A118	<i>Ficus microcarpa</i>	細葉榕	5	159	6	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 5-6-2010
A119	<i>Ficus microcarpa</i>	細葉榕	5	165	5	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 5-6-2010
A120	<i>Ficus microcarpa</i>	細葉榕	5	167	5	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 5-6-2010
A121	<i>Livistona chinensis</i>	蒲葵	4	152	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 17-1-2011
A122	<i>Livistona chinensis</i>	蒲葵	2	132	3	Fair	Fair	Medium	Fell	Medium	Removed by this contract (undersize, Felled on 17-1-2011)
A123	<i>Livistona chinensis</i>	蒲葵	3	145	2	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 17-1-2011
A124	<i>Livistona chinensis</i>	蒲葵	3	148	2	Fair	Fair	Medium	Fell	Medium	Removed by this contract (undersize, Felled on 17-1-2011)
A125	<i>Livistona chinensis</i>	蒲葵	2	120	2	Fair	Fair	Medium	Fell	Medium	Removed by this contract (undersize, Felled on 17-1-2011)
A126	<i>Livistona chinensis</i>	蒲葵	4	156	3	Fair	Fair	Medium	Fell	Medium	Removed by this contract (undersize, Felled on 17-1-2011)
A127	<i>Livistona chinensis</i>	蒲葵	4	160	3	Fair	Fair	Medium	Fell	Medium	Removed by this contract (undersize, Felled on 17-1-2011)
A128	<i>Livistona chinensis</i>	蒲葵	3	132	3	Fair	Fair	Medium	Fell	Medium	Removed by this contract (undersize, Felled on 17-1-2011)
A129	<i>Livistona chinensis</i>	蒲葵	3	120	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 17-1-2011
A130	<i>Livistona chinensis</i>	蒲葵	4	139	4	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 17-1-2011
A131	<i>Livistona chinensis</i>	蒲葵	3	135	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 18-1-2011
A132	<i>Livistona chinensis</i>	蒲葵	3	134	4	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 18-1-2011
A133	<i>Livistona chinensis</i>	蒲葵	4	142	4	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 18-1-2011
A134	<i>Alstonia scholaris</i>	黑板木	4	120	3	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A135	<i>Alstonia scholaris</i>	黑板木	5	135	4	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A136	<i>Alstonia scholaris</i>	黑板木	4	124	3	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A137	<i>Alstonia scholaris</i>	黑板木	4	122	3	Fair	Fair	Medium	Fell	Low	Removed by this contract
A138	<i>Livistona chinensis</i>	蒲葵	5	205	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 18-1-2011
A139	<i>Livistona chinensis</i>	蒲葵	3	211	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 18-1-2011
A140	<i>Acacia confusa</i>	台灣相思	5	180	3	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A141	<i>Livistona chinensis</i>	蒲葵	4	135	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 18-1-2011
A142	<i>Livistona chinensis</i>	蒲葵	4	128	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 18-1-2011
A143	<i>Livistona chinensis</i>	蒲葵	5	145	3	Fair	Fair	Medium	Fell	Medium	Removed by this contract
A144	<i>Livistona chinensis</i>	蒲葵	4	122	2	Fair	Fair	Medium	Fell	Medium	Removed by this contract
A145	<i>Livistona chinensis</i>	蒲葵	4	110	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 18-1-2011
A146	<i>Livistona chinensis</i>	蒲葵	5	145	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 18-1-2011
A147	<i>Livistona chinensis</i>	蒲葵	5	120	3	Fair	Fair	Medium	Fell	Medium	Removed by this contract
A148	<i>Livistona chinensis</i>	蒲葵	5	137	3	Fair	Fair	Medium	Fell	Medium	Removed by this contract
A149	<i>Livistona chinensis</i>	蒲葵	5	184	3	Fair	Fair	Medium	Fell	Medium	Removed by this contract
A150	<i>Livistona chinensis</i>	蒲葵	3	102	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 17-1-2011
A151	<i>Livistona chinensis</i>	蒲葵	2	101	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 17-1-2011
A152	<i>Livistona chinensis</i>	蒲葵	2	108	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 17-1-2011
A153	<i>Livistona chinensis</i>	蒲葵	3	128	3	Fair	Fair	Medium	Fell	Medium	Removed by this contract
A154	<i>Bauhinia blakeana</i>	洋紫荊	6	124	3	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A156	<i>Bauhinia blakeana</i>	洋紫荊	7	148	4	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A157	<i>Hibiscus tiliaceus</i>	黃槿	10	391	5	Fair	Fair	Medium	Fell	Low	TFA approved and it can be felled
A158	<i>Bauhinia blakeana</i>	洋紫荊	5	174	3	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A159	<i>Bauhinia blakeana</i>	洋紫荊	4	105	2	Fair	Fair	Medium	Retain	Medium	Handover to HK/2012/08
A160	<i>Bauhinia blakeana</i>	洋紫荊	4	110	2	Fair	Fair	Medium	Fell	Low	TFA approved and it can be felled
A161	<i>Callistemon viminalis</i>	串錢柳	4	110	2	Fair	Fair	Medium	Fell	Low	TFA approved and it can be felled
A162	<i>Bauhinia blakeana</i>	洋紫荊	5	210	4	Fair	Fair	Medium	Fell	Low	TFA approved and it can be felled
A163	<i>Callistemon viminalis</i>	串錢柳	5	150	3	Fair	Fair	Medium	Fell	Medium	TFA approved and it can be felled
TST001	<i>Callistemon viminalis</i>	串錢柳	4	102	2	Poor	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST002	<i>Callistemon viminalis</i>	串錢柳	7	186	4	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST003	<i>Callistemon viminalis</i>	串錢柳	7	145	3	Fair	Poor	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST004	<i>Plumeria rubra</i>	雞蛋花	4	132	4	Fair	Poor	Medium	Retain	Medium	Outside site boundary
TST005	<i>Ravenala madagascariensis</i>	旅人蕉	8	102	6	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST006	<i>Ravenala madagascariensis</i>	旅人蕉	8	234	6	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST007	<i>Livistona chinensis</i>	蒲葵	6	132	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 16-2-2011
TST008	<i>Livistona chinensis</i>	蒲葵	5	122	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 15-2-2011
TST009	<i>Livistona chinensis</i>	蒲葵	5	121	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 15-2-2011
TST010	<i>Livistona chinensis</i>	蒲葵	6	138	3	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST011	<i>Livistona chinensis</i>	蒲葵	4	110	2	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST012	<i>Livistona chinensis</i>	蒲葵	3	111	2	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST013	<i>Livistona chinensis</i>	蒲葵	4	124	3	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST014	<i>Livistona chinensis</i>	蒲葵	3	113	2	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST015	<i>Livistona chinensis</i>	蒲葵	4	124	3	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012

CONTRACT NO.: HK/2009/01

Tree No.	Botanical Name	Chinese Name	Height (m)	Trunk Diameter at Breast Height (DBH) (mm)	Spread (m)	Health	Form	Amenity Value High Medium Low	Recommendation	Survival Rate After Transplant (High/Medium/Low)	Remarks
TST016	<i>Livistona chinensis</i>	蒲葵	3	114	2	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST017	<i>Livistona chinensis</i>	蒲葵	3	115	2	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST018	<i>Livistona chinensis</i>	蒲葵	4	119	2	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST019	<i>Livistona chinensis</i>	蒲葵	4	127	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 16-2-2011
TST020	<i>Livistona chinensis</i>	蒲葵	5	135	2	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 15-2-2011
TST021	<i>Livistona chinensis</i>	蒲葵	4	140	2	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 16-2-2011
TST022	<i>Livistona chinensis</i>	蒲葵	4	113	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 17-2-2011
TST023	<i>Livistona chinensis</i>	蒲葵	5	125	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 17-2-2011
TST024	<i>Livistona chinensis</i>	蒲葵	5	145	4	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 17-2-2011
TST025	<i>Ravenala madagascariensis</i>	旅人蕉	5	186	5	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 17-2-2011
TST026	<i>Ravenala madagascariensis</i>	旅人蕉	6	135	4	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 17-2-2011
TST027	<i>Ravenala madagascariensis</i>	旅人蕉	7	124	3	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST028	<i>Ravenala madagascariensis</i>	旅人蕉	6	219	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 6-8-2011
TST029	<i>Ravenala madagascariensis</i>	旅人蕉	6	188	3	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST030	<i>Ravenala madagascariensis</i>	旅人蕉	6	220	3	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST031	<i>Ravenala madagascariensis</i>	旅人蕉	6	325	3	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST032	<i>Ravenala madagascariensis</i>	旅人蕉	6	319	3	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST033	<i>Ravenala madagascariensis</i>	旅人蕉	6	260	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 13-12-2010
TST034	<i>Ravenala madagascariensis</i>	旅人蕉	6	292	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 13-12-2010
TST035	<i>Livistona chinensis</i>	蒲葵	4	180	3	Fair	Fair	Medium	Transplant	Medium	Transplanted by this contract on 15-2-2011
TST036	<i>Ravenala madagascariensis</i>	旅人蕉	5	240	3	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012
TST037	<i>Ravenala madagascariensis</i>	旅人蕉	7	265	4	Fair	Fair	Medium	Retain	Medium	Site has been hand over to LCSD on 6-9-2012

Summary:

Total number of existing trees : 117



俊和 - 利達聯營  
CHUN WO - LEADER JOINT VENTURE

Contract No. HK/2009/01  
Wan Chai Development Phase II  
Central – Wan Chai Bypass at HKCEC

---

## Appendix E

### Method Statement



# 香港綠化工程有限公司 Hong Kong Landscaping Co., Ltd.

Contract no.: HK/2009/01

Project Title: Wan Chai Development Phase II - Central - Wanchai Bypass At Hong Kong Convention and Exhibition Centre

Method Statement for Tree Transplant Work for Trees A099, T360, T363, T364, T365, T366

## 1 Preparation works

### 1.1 Scope

The subject trees are located at raised planter adjacent to Convention Avenue. Site inspection observed that the frequency of use is high that multi-phase root pruning prior to tree transplantation would be risky to traffic and public. As a result, special arrangement for sequence of work will be required. One-stage root pruning for tree transplantation is proposed for safety concern. This method shall be implemented subject to Architect's approval.

### 1.2 Crown pruning

- 1.2.1 The crown pruning extent shall be shown on crown pruning proposal.
- 1.2.2 Crown pruning limited to remove dead, diseased, broken or damaged branches shall be carried out prior to Architect's approval.
- 1.2.3 Reduction of the original crown spread limited to the maximum of 1/4 shall be carried out if necessary and subject to Architect's approval.
- 1.2.4 Crown reduction shall produce a well-shaped, balanced head.

### 1.3 Root pruning

- 1.3.1 The root pruning extent shall be shown on root pruning proposal.
- 1.3.2 Support the trees with wire guys or bamboo stakes ensure stability of the pre-transplanted trees. The supporting material and supporting mechanism

九龍上海街 383 號華興商業中心 5 樓  
5/F., Wah Hing Comm. Centre, 383 Shanghai St., Kowloon.  
Tel: No. 2388 6332 Fax: No.(852) 2385 7911



Certificate No. HK04/0030  
ISO 9001:2000  
GB/T 19001-2000





香港綠化工程有限公司  
Hong Kong Landscaping Co., Ltd.

Contract no.: HK/2009/01

Project Title: Wan Chai Development Phase II - Central - Wanchai Bypass At Hong Kong Convention and Exhibition Centre

Method Statement for Tree Transplant Work for Trees A099, T360, T363, T364, T365, T366

shall be submitted with registered structural engineer information for Architect approval.

- 1.3.3 The horizontal dimensions for the root ball shall be 10 times the DBH (minimum 1000mm) of the tree trunk.
- 1.3.4 For trees with constraints that the size of rootball less than 10 times of trunk diameter, the exact size of rootball and exact extent of root ball shall be determined on-site with Landscape Architect due to site constraints and carried out prior to Architect's approval. The proposed size of rootball shall be approved by Landscape Architect.
- 1.3.5 A trench up to 750mm deep and 200-300mm wide (dependent on the species and soil characteristics) should be formed outside of the marked circumference. All roots protruding from the root ball should be cut off cleanly.

#### 1.4 Undercutting

- 1.4.1 Excavate outside the prepared root-ball taking care not to disturb the root ball.
- 1.4.2 Under-cut bottom of the root ball to form a semi-sphere shape.
- 1.4.3 All roots protruding from the root ball should be cut off cleanly.
- 1.4.4 Wrap the root ball with Hessian materials and tie up the ball securely with jute ropes or GMS wire netting.

## 2 Uplifting

### 2.1 Uplifting and transport to holding nursery or final location

- 2.1.1 Proceed to uplifting immediately after the undercutting
- 2.1.2 Lifting would be carried out by hoisting equipment such as hydraulic crane, the number and the size of hoisting equipment shall be determined on site with

九龍上海街 383 號華興商業中心 5 樓  
5/F., Wah Hing Comm. Centre, 383 Shanghai St., Kowloon.  
Tel: No. 2388 6332 Fax: No.(852) 2385 7911



Certificate No. HK04/0030  
ISO 9001:2000  
GH/T 19001-2000



香港綠化工程有限公司  
**Hong Kong Landscaping Co., Ltd.**

Contract no.: HK/2009/01

Project Title: Wan Chai Development Phase II - Central - Wanchai Bypass At Hong Kong Convention and Exhibition Centre

Method Statement for Tree Transplant Work for Trees A099, T360, T363, T364, T365, T366

crane operator prior to transplantation works, with padded protection for the tree.

- 2.1.3 Lifting gear attached to the trunk of tree will be only for stabilizing the tree during lifting. Damage to tree trunk should be avoided.
- 2.1.4 Trees should be supported and firmly secured on crane lorry when transport off site to holding nursery.

**2.2 Planting at hold nursery or final location**

- 2.2.1 Prepare tree pits at nursery with diameter at least 300mm greater than the root ball. Allow for a minimum of 150mm clearance between the rootball edges to the sides. Allow 300mm loose soil underneath the root ball for planting. The planting location shall be prepared with on grade existing soil or filled with 200-300mm planting soil if the surface of planting location at holding nursery is paved
- 2.2.2 Remove all crown wrappings and fastenings used to tie in the branches during transportation.
- 2.2.3 Remove all wrapping from the root ball at the pit.
- 2.2.4 Set the tree into the pit and ensure it is in firmly up-right position.
- 2.2.5 Backfill the pit in layers with soil mix.
- 2.2.6 Compact and firming up each layer to ensure no air pockets are left around the root ball.
- 2.2.7 For future re-transplant to site, the trees shall be planted on top of soil and the rootball shall be prepared with Terram and materials as temporary planters
- 2.2.8 The newly planted tree should be watered to moisten the root ball thoroughly.
- 2.2.9 Support the tree with wire guys or bamboo stakes with rubber padding to protect the tree trunk.
- 2.2.10 Perform maintenance practices as stated in Item 3 prior to re-transplant to final

九龍上海街 383 號華興商業中心 5 樓  
5/F., Wah Hing Comm. Centre, 383 Shanghai St., Kowloon.  
Tel: No. 2388 6332 Fax: No.(852) 2385 7911



Certificate No. HK04/0030  
ISO 9001:2000  
GB/T 19001-2000





香港綠化工程有限公司  
Hong Kong Landscaping Co., Ltd.

Contract no.: HK/2009/01

Project Title: Wan Chai Development Phase II - Central - Wanchai Bypass At Hong Kong Convention and Exhibition Centre

Method Statement for Tree Transplant Work for Trees A099, T360, T363, T364, T365, T366

location.

### 2.3 Uplifting and transplant from nursery to final location

- 2.3.1 Excavate outside the prepared root-ball taking care not to disturb the ball
- 2.3.2 Wrap root ball with Hessian material and tie up the ball securely with jute ropes or wire netting.
- 2.3.3 Lifting up tree in one full-swing, with padded protection for the tree.
- 2.3.4 Trees should be supported and firmly secured on crane lorry.
- 2.3.5 Prepare tree pits at final location with diameter at least 150mm greater than the root ball.
- 2.3.6 Loosen up the soil 150mm depth at the base of the pit.
- 2.3.7 Remove all crown wrappings and fastenings used to tie in the branches during transportation.
- 2.3.8 Remove all wrapping from the root ball and from the pits.
- 2.3.9 See the tree into the pits and ensure it is in firmly up-right position.
- 2.3.10 Backfill the pit in layers with soil.
- 2.3.11 Compact and firming up each layer to ensure no air pockets are left around the root ball.
- 2.3.12 The newly planted tree should be watered to moisten the root ball thoroughly
- 2.3.13 Support the tree with wire guys or bamboo stakes with rubber padding to protect the tree trunk.

### 3 Maintenance

九龍上海街 383 號華興商業中心 5 樓  
5/F., Wah Hing Comm. Centre, 383 Shanghai St., Kowloon.  
Tel: No. 2388 6332 Fax: No. (852) 2385 7911



Certificate No. HK04/0030  
ISO 9001:2000  
GB/T 19001-2000





香港綠化工程有限公司  
Hong Kong Landscaping Co., Ltd.

Contract no.: HK/2009/01

Project Title: Wan Chai Development Phase II - Central - Wanchai Bypass At Hong Kong Convention and Exhibition Centre

Method Statement for Tree Transplant Work for Trees A099, T360, T363, T364, T365, T366

### 3.1 Watering

- 3.1.1 Watering the tree thoroughly, depend on the weather conditions, to ensure wetting if the root volume for the 1<sup>st</sup> 3 months period
- 3.1.2 Slowly decrease the watering frequency throughout the remaining 9 months maintenance period to encourage better root growth at depth.

### 3.2 Weeds, pest and fungal control

- 3.2.1 Stop weed growth that developed by cultivations by herbicide application.
- 3.2.2 Check for pest or fungal infestation and apply appropriate pesticide or fungicide respectively

### 3.3 Nutrition's

- 3.3.1 Apply slow release fertilizer (15-9-15-2) every 3 months throughout the 12 months maintenance period.

#### Remarks:

1. Omitting or shortening root preparation period may increase the risk of tree death.
2. If the tree shows signs of abnormal transplant shock or excessive stress during the preparation period, interval between each root pruning stages may require to extend avoiding tree death.
3. Semi-mature size tree or even larger in size may require individual assessment periodically between each stage of preparations. Depends on size and species, a period up to 12 months is required between each stage of preparation subject to Landscape Architect comments.
4. Main contractor/Client shall provide unobstructed access to original / final

九龍上海街 383 號華興商業中心 5 樓  
5/F., Wah Hing Comm. Centre, 383 Shanghai St., Kowloon.  
Tel: No. 2388 6332 Fax: No.(852) 2385 7911



Certificate No. HK04/0030  
ISO 9001:2000  
GB/T 19001-2000



香港綠化工程有限公司  
Hong Kong Landscaping Co., Ltd.

Contract no.: HK/2009/01

Project Title: Wan Chai Development Phase II - Central - Wanchai Bypass At Hong Kong Convention and Exhibition Centre

Method Statement for Tree Transplant Work for Trees A099, T360, T363, T364, T365, T366

location(s) to ensure proper lifting and handling operation to be carried out.

5. Due to loading and transport limitation on public road, overall tree crown shape and size more than 2.8 meter cannot be retained. Client or Consultants are remained that hard pruning/topping may be resulted to the tree on order to transport off site. Temporary holding nursery shall be provided by main contractor shall be allowed as tree transplant holding nursery of the crown spread or tree height exceeds the public road transport limits.
6. Preparation period for transplant shall be carried out in accordance with British Standard 3998 or General Specification for building 2007 edition Volume 2 Section 25 Landscape Work.

-END-

九龍上海街 383 號華興商業中心 5 樓  
5/F., Wah Hing Comm. Centre, 383 Shanghai St., Kowloon.  
Tel: No. 2388 6332 Fax: No. (852) 2385 7911



Certificate No. HK04/0030  
ISO 9001:2000  
GB/T 19001-2000



俊和  
CHUN WO



LEADER

俊和 - 利達聯營  
CHUN WO - LEADER JOINT VENTURE

Contract No. HK/2009/01  
Wan Chai Development Phase II  
Central – Wan Chai Bypass at HKCEC

---

## Appendix F

### Implementation Schedule for Landscape and Visual

Implementation Schedule for Landscape and Visual

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages			Relevant Legislation and Guidelines	Implementation status
				Des	C	Dec		
Construction Phase								
For the Whole Project								
Table 10.5	CM1 Topsoil, where identified, shall be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Work site / During Construction Phase	Contractor	√	√		EIAO TM	Under Implementation
Table 10.5	CM2 Existing trees to be retained on site shall be carefully protected during construction.	Work site / During Construction Phase	Contractor	√	√		EIAO TM	Under Implementation
Table 10.5	CM3 Trees unavoidably affected by the works shall be transplanted where practical.	Work site / During Construction Phase	Contractor	√	√		EIAO TM	Under Implementation
Table 10.5	CM4 Compensatory tree planting shall be provided to compensate for felled trees.	Work site / During Construction Phase	Contractor	√	√		EIAO TM	Under Implementation
Table 10.5	CM5 Control of night-time lighting.	Work site / During Construction Phase	Contractor	√	√		EIAO TM	Under Implementation
Table 10.5	CM6 Erection of decorative screen hearing compatible with the surrounding setting.	Work site / During Construction Phase	Contractor	√	√		EIAO TM	Under Implementation



<b>For DPI - CWB (Within the Project Boundary)</b>						
Table	CM1 Topsoil, where identified, shall be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Work site / During Construction Phase	Contractor	✓	EIAO TM	N/A
Table 10.5	CM2 Existing trees to be retained on site shall be carefully protected during construction.	Work site / During Construction Phase	Contractor	✓	EIAO TM	N/A
Table 10.5	CM3 Trees unavoidably affected by the works shall be transplanted where practical.	Work site / During Construction Phase	Contractor	✓	EIAO TM	N/A
Table 10.5	CM4 Compensatory trees planting shall be provided to compensate for felled trees.	Work site / During Construction Phase	Contractor	✓	EIAO TM	N/A
Table 10.5	CM5 Control of night-time lighting	Work site / During Construction Phase	Contractor	✓	EIAO TM	N/A
Table 10.5	CM6 Erection of decorative screen hearing compatible with the surrounding setting.	Work site / During Construction Phase	Contractor	✓	EIAO TM	N/A
