



**CONTRACT NO: HK/2011/07**

**WANCHAI DEVELOPMENT PHASE II AND CENTRAL  
WANCHAI BYPASS  
SAMPLING, FIELD MEASUREMENT AND TESTING WORK  
(STAGE 2)**

**ENVIRONMENTAL PERMIT NO. EP-122/2002/D**

**MONTHLY ENVIRONMENTAL MONITORING & AUDIT REPORT**

**- FEBRUARY 2015 -**

**CLIENTS:**

**Civil Engineering and Development  
Department**

**PREPARED BY:**

**Lam Geotechnics Limited**

11/F Centre Point  
181-185 Gloucester Road,  
Wanchai, H.K.

Telephone: (852) 2882-3939  
Facsimile: (852) 2882-3331  
E-mail: [info@lamenviro.com](mailto:info@lamenviro.com)  
Website: <http://www.lamenviro.com>

**CERTIFIED BY:**

Raymond Dai  
Environmental Team Leader

**DATE:**

12 March 2015

Ref.: AACWBIECEM00\_0\_6333L.15

12 March 2015

AECOM Asia Company Limited  
11/F, Tower 2  
Grand Central Plaza  
138 Shatin Rural Committee Road  
Shatin, New Territories  
Hong Kong

By Post and Fax (2691 2649)

Attention: Mr. Conrad Ng

Dear Sir,

**Re: Wan Chai Development Phase II and Central-Wan Chai Bypass  
Monthly Environmental Monitoring and Audit Report (February 2015) for EP-122/2002/D**

Reference is made to the Environmental Team's submission of the captioned Monthly Environmental Monitoring and Audit (EM&A) Report for February 2015 received by e-mail on 12 March 2015.

Please be informed that we have no adverse comment on the captioned submission. We write to verify the captioned submission in accordance with Condition 4.6 in the captioned Environmental Permit.

Thank you very much for your kind attention and please do not hesitate to contact the undersigned should you have any queries.

Yours sincerely,



David Yeung  
Independent Environmental Checker

c.c. CEDD Mr. Jason Cheung  
AECOM Mr. Francis Leong / Mr. Stephen Lai  
Lam Mr. Raymond Dai

by fax: 2577 5040  
by fax: 2691 2649  
by fax: 2882 3331

Q:\Projects\AACWBIECEM00\Corr\AACWBIECEM00\_0\_6333L.15.doc



**TABLE OF CONTENTS**

**EXECUTIVE SUMMARY ..... 3**

**1 INTRODUCTION..... 6**

1.1 Scope of the Report ..... 6

1.2 Structure of the Report..... 6

**2 PROJECT BACKGROUND..... 8**

2.1 Background ..... 8

2.2 Scope of the Project and Site Description ..... 8

2.3 Project Organization and Contact Personnel ..... 9

**3 STATUS OF REGULATORY COMPLIANCE..... 11**

3.1 Status of Environmental Licensing and Permitting under the Project..... 11

**4 MONITORING REQUIREMENTS ..... 13**

4.1 Noise Monitoring ..... 13

4.2 Air Quality Monitoring..... 14

4.3 Water Quality Monitoring ..... 14

**5 MONITORING RESULTS..... 19**

5.1 Noise Monitoring Results ..... 19

5.2 Air Quality Monitoring Results ..... 19

5.3 Water Quality Monitoring Results ..... 19

5.4 Waste Monitoring Results ..... 21

**6 COMPLIANCE AUDIT ..... 23**

6.1 Noise Monitoring ..... 23

6.2 Air Quality Monitoring..... 23

6.3 Water Quality Monitoring ..... 23

6.4 Review of the Reasons for and the Implications of Non-compliance ..... 23

6.5 Summary of action taken in the event of and follow-up on non-compliance .... 23

**7 CUMULATIVE CONSTRUCTION IMPACTS DUE TO THE CONCURRENT PROJECTS ..... 24**

**8 ENVIRONMENTAL SITE AUDIT ..... 24**

**9 COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION ..... 26**

**10 CONCLUSION ..... 28**

**LIST OF TABLES**

<i>Table 1</i>	<i>Summary of Water Quality Monitoring Exceedances in Reporting Month</i>
<i>Table 2.1</i>	<i>Schedule 2 Designated Projects under this Project</i>
<i>Table 2.2</i>	<i>Contact Details of Key Personnel</i>
<i>Table 3.1</i>	<i>Summary of the current status on licences and/or permits on environmental protection pertinent to the Project</i>
<i>Table 3.2</i>	<i>Cumulative Summary of Valid Licences and Permits under Contract no. HK/2012/08</i>
<i>Table 4.1</i>	<i>Continuous Noise Monitoring Stations</i>
<i>Table 4.2</i>	<i>Air Quality Monitoring Stations</i>
<i>Table 4.3</i>	<i>Water Quality Monitoring Station</i>
<i>Table 4.4</i>	<i>Marine Water Quality Monitoring Frequency and Parameters</i>
<i>Table 5.1</i>	<i>Continuous Noise Monitoring Stations for Contract no. HK/2012/08</i>
<i>Table 5.2</i>	<i>Air Quality Monitoring Station for Contract no. HK/2012/08</i>
<i>Table 5.3</i>	<i>Water Quality Monitoring Station for Contract no. HK/2012/08</i>
<i>Table 5.4</i>	<i>Details of Waste Disposal for Contract no. HK/2012/08</i>
<i>Table 5.5</i>	<i>Details of Waste Disposal for Contract no. HK/2012/08</i>
<i>Table 8.1</i>	<i>Summary of Environmental Inspections for Contract no. HK/2012/08</i>
<i>Table 9.1</i>	<i>Cumulative Statistics on Complaints</i>
<i>Table 9.2</i>	<i>Cumulative Statistics on Successful Prosecutions</i>
<i>Table 10.1</i>	<i>Summary of Key Construction Activities of Individual Contract(s) to be commenced in Coming Reporting Month</i>

**LIST OF FIGURES**

<u>Figure 2.1</u>	Project Layout
<u>Figure 2.2</u>	Project Organization Chart
<u>Figure 4.1</u>	Locations of Environmental Monitoring Stations

**LIST OF APPENDICES**

<u>Appendix 3.1</u>	Environmental Mitigation Implementation Schedule
<u>Appendix 4.1</u>	Action and Limit Level
<u>Appendix 4.2</u>	Copies of Calibration Certificates
<u>Appendix 5.1</u>	Monitoring Schedule for Reporting Month and Coming month
<u>Appendix 5.2</u>	Continuous Noise Monitoring Results and Graphical Presentations
<u>Appendix 5.3</u>	Air Quality Monitoring Results and Graphical Presentations
<u>Appendix 5.4</u>	Water Quality Monitoring Results and Graphical Presentations
<u>Appendix 6.1</u>	Event Action Plans
<u>Appendix 6.2</u>	Notification of Exceedance
<u>Appendix 9.1</u>	Complaint Log
<u>Appendix 10.1</u>	Construction Programme of Individual Contracts



## EXECUTIVE SUMMARY

- i. This is the Environmental Monitoring and Audit (EM&A) Monthly Report – [February 2015](#) specific for Environmental Permit no. EP-122/2002/D. The EM&A report is prepared by the Environmental Team (ET) employed under Contract No. HK/2011/07 – Wan Chai Development Phase II and Central Wanchai Bypass – Sampling, Field Measurement and Testing Works (Stage 2). This report presents the environmental monitoring findings and information recorded during the period of [February 2015](#). The cut-off date of reporting is the last day of each reporting month.
- ii. In the reporting month, the principal work activities of the contract are included as follows:  
Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West
  - [Diaphragm wall construction works](#)
  - [Removal of rock armour](#)
  - [Socket H-pile construction](#)

### Noise Monitoring

- iii. Continuous noise monitoring was conducted at ACL3 – City Hall.
- iv. [No action or limit level exceedances was recorded at ACL3 – City Hall in the reporting month.](#)
- v. Due to safety concern, the location of the continuous noise monitoring station at City Hall was finely adjusted to the roof of the City Hall, Low Block on 1 May 2013.

### Air Quality Monitoring

- vi. 1-hour and 24-hour Total Suspended Particulates (TSP) monitoring were conducted on every six days basis at ACL1 – City Hall and ACL2a – Contractor HK/2012/08 Site Office.
- vii. [No action or limit level exceedances was recorded at ACL 1 – City Hall and ACL2a – Contractor HK/2012/08 Site Office in the reporting month.](#)
- viii. [Due to interruption of electricity supply, the 24hr TSP monitoring at ACL1 – City Hall was rescheduled from 17 and 23 February 2015 to 18 and 24 February 2015 respectively.](#)
- ix. [Due to interruption of electricity supply, the 24hr TSP monitoring at ACL2a – Contractor HK/2012/08 Site Office was rescheduled from 13 February 2015 to 14 February 2015.](#)
- x. Due to the defective electricity supply found at monitoring station ACL1 and the advice from City Hall Building Management, the air monitoring station ACL1 – City Hall was finely adjusted on 28 Feb 2014 to an alternate electricity supply.
- xi. Due to the large scale renovation works at People's Liberation Army Headquarter, a Proposal for Relocation of Air Quality Monitoring Station at People's Liberation Army Headquarter (ACL2) was formally submitted to EPD on 4<sup>th</sup> November, 2013.

- xii. Air Quality Monitoring at ACL2 was temporarily suspended during the period from 14<sup>th</sup> November, 2013 to 3<sup>rd</sup> December, 2013.
- xiii. The Proposal for Relocation of Air Quality Monitoring Station at People’s Liberation Army Headquarter (ACL2) was approved by EPD on 27 November 2013.
- xiv. According to the approved proposal for relocation of Air Quality Monitoring station, the action and limit levels of ACL2a shall adopt the reference monitoring result from the baseline air monitoring report for EP/364/2009 in 22 April 2010 in which approved by EPD.
- xv. The air quality monitoring at ACL2a – Contractor HK/2012/08 Site Office was commenced on 7 December 2013.

Water Quality Monitoring

- xvi. As confirmed by WDII RSS, the dredging works, seawall modification works and other associated works undertaken at Central Reclamation Phase III by Contractor HK/2012/08 was commenced in late September 2014. According to the approved EM&A manual under EP-122/2002/D, water quality monitoring shall be implemented at the Central Reclamation Phase III works area accordingly to assess any potential water quality impact during the construction period.
- xvii. Water quality monitoring at M5B and Culvert J were conducted three days per week during reporting period starting from 26 September 2014. The action and limit level exceedance of water quality monitoring are summarized in **Table 1**.
- xviii. No action or limit level exceedance was recorded in this reporting period. The details of recorded exceedance can be referred to the **Section 5.3**.
- xix. With respect the suspension of marine construction activities under the contract during Chinese New Year Holiday, the water quality monitoring event on 20 February 2015 during both flood tide and ebb tide were temporarily suspended.

**Table 1 Summary of Water Quality Monitoring Exceedances in Reporting Month**

Contract No.	Water quality monitoring station	Mid-flood				Mid-ebb			
		DO		SS		DO		SS	
		AL	LL	AL	LL	AL	LL	AL	LL
HK/2012/08	M5B <sup>2</sup>	0	0	0	0	0	0	0	0
	Culvert J <sup>1</sup>	-	-	-	-	-	-	-	-
<b>Total</b>		<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>

Remarks<sup>1</sup>: No action or limit level are not applicable to reference station Culvert J.

Remarks<sup>2</sup>: Turbidity measurement are reported as reference.

Complaints, Notifications of Summons and Successful Prosecutions

- xx. One environmental complaint was received in the reporting month.

- xxi. A public complaint (EPD ref: H04/RS/0001716-15 dated 21 January 2015) regarding air quality impact referred by EPD was received by ET on 11 February 2015.
- xxii. According to the relevant site records, trench grabbing for D-wall construction and socket H-pile construction were conducted at the concerned location on 21 January 2015. Dust screen for socket H-pile construction, maintenance of site haul road in wet condition and water spraying at vehicle entrance/exit points of HK/2012/08 Contractor site office and Portion I were implemented by the Contractor of HK/2012/08 near the concerned location on 21 January 2015.
- xxiii. In addition, no environmental deficiency related to dust mitigation was identified at the concerned location during weekly environmental inspections conducted on 27 Jan, 3 and 10 Feb 2015 and dust mitigation measures including water spraying for dusty haul road and provision of wheel washing were in place and no dust related impact from the construction works at the concerned location was observed.
- xxiv. Meanwhile, the Air Quality Health Index (AQHI) recorded by EPD across Western District and Eastern District on 21 January 2015 was ranged from 4 to 10+ indicating a severely high concentration of ambient air pollutants. Based on reviewing relevant impact monitoring data, elevated TSP were recorded at monitoring stations across Central to WanChai West area despite a non-Project related exceedance was recorded at nearby monitoring station ACL2a (Contractor HK/2012/08 Site Office) on 21 January 2015 and was considered to be contributed by ambient air pollutant.
- xxv. The site condition under Contract HK/2012/08 at the concerned location was considered to be generally satisfactory and no non-conformity related to cumulative air quality impact was observed at the concerned location. Nevertheless, in view of the public concern, the contractor was reminded to enhance the dust mitigation measures implemented to minimize potential nuisance to nearby public.

#### Site Inspections and Audit

- xxvi. The Environmental Team (ET) conducted weekly site inspection for Contract no. HK/2012/08 in this reporting period. The Contractors rectified major observations and recommendations made during the audit sessions. No non-conformance was identified during the site inspections.

#### Future Key Issues

- xxvii. In the coming reporting month, the principal work activities of the contract is anticipated as follows:

#### Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West

- Removal of rock armour
- Socket H-pile construction

## 1 INTRODUCTION

### 1.1 Scope of the Report

- 1.1.1. Lam Geotechnics Limited (LGL) has been appointed take up the role as the Environmental Team (ET) under Environmental Permit no. EP-122/2002/D to implement the Environmental Monitoring and Audit (EM&A) programme as stipulated in the EM&A Manual of the approved Environmental Impact Assessment (EIA) Report for Central Reclamation Phase III - Studies, Site Investigation, Design and Construction (Register No.: AEIAR-040/2001) since 1 May 2013.
- 1.1.2. This report documents the finding of EM&A works for Environmental Permit (EP) no. EP-122/2002/D, during the period of [February 2015](#). The cut-off date of reporting is the last day of each reporting month.

### 1.2 Structure of the Report

- Section 1**      ***Introduction*** – details the scope and structure of the report.
- Section 2**      ***Project Background*** – summarizes background and scope of the project, site description, project organization and contact details of key personnel during the reporting period.
- Section 3**      ***Status of Regulatory Compliance*** – summarizes the status of valid Environmental Permits / Licenses during the reporting period.
- Section 4**      ***Monitoring Requirements*** – summarizes all monitoring parameters, monitoring methodology and equipment, monitoring locations, monitoring frequency, criteria and respective event and action plan and monitoring programmes.
- Section 5**      ***Monitoring Results*** – summarizes the monitoring results obtained in the reporting period.
- Section 6**      ***Compliance Audit*** – summarizes the auditing of monitoring results, all exceedances environmental parameters.
- Section 7**      ***Cumulative Construction Impact due to the Concurrent Projects*** – summarizes the relevant cumulative construction impact due to the concurrent activities of the concurrent Projects.



- Section 8**      ***Environmental Site Audit*** – summarizes the findings of weekly site inspections undertaken within the reporting period, with a review of any relevant follow-up actions within the reporting period.
- Section 9**      ***Complaints, Notification of summons and Prosecution*** – summarizes the cumulative statistics on complaints, notification of summons and prosecution
- Section 10**     ***Conclusion***

## 2 PROJECT BACKGROUND

### 2.1 Background

2.1.1 Central Reclamation Phase III - Studies, Site Investigation, Design and Construction (hereafter called “the Project”) are Designated Project (DP) under the Environmental Impact Assessment Ordinance (Cap. 499) (EIAO). The Environmental Impact Assessment (EIA) Reports for Central Reclamation Phase III - Studies, Site Investigation, Design and Construction (Register No. AEIAR-040/2001) has been approved on 31 August 2001.

### 2.2 Scope of the Project and Site Description

2.2.1. The design and construction of Central Reclamation Phase III involves the permanent reclamation and construction and operation of a trunk road and its road tunnel that is shown at [Figure 2.1](#).

2.2.2. The key purpose of the study area encompasses the area of Victoria Harbour to the southeast of the new Outlying Islands Ferry Piers and north of Edinburgh Place and Lung Wui Road. The area extends eastward to Fenwick Pier Street and the Fleet Arcade, and includes the existing GPO, Star Ferry Piers, Queens Pier, City Hall, PLA Headquarters, Hong Kong Red Cross Headquarters building and the Tamar Site. The scope of the Central Reclamation, Phase III includes:

- Reclamation and seawalls, roads and associated services, North Island Line Protection Works and Advance Trunk Road Tunnel (ATRT) for the CWB;
- Re-provisioning of Star Ferry Pier, public landing steps, wallah wallah moorings, and motor boat/launch operators' kiosks;
- External cooling water systems which consist of the cooling water pumping shells for future developments, and the re-provisioning of existing cooling water pumping stations and associated pipework systems and E&M works;
- Re-provisioning of existing Leisure and Cultural Services Department (LCSD)'s facilities;
- Provision of a flood relief path, stormwater culvert extensions, upgrading of hinterland stormwater drainage resulting from the reclamation, demolition of the existing waterfront structures and necessary landscaping;
- The Hong Kong Station Extended Overrun Tunnel (EOT) and associated ventilation structures entrusted for construction within the CRIII works;
- Re-provisioning of the Government Heliport at the Wan Chai PCWA and re-provisioning of the Wan Chai PCWA at Chai Wan Basin.

2.2.3. The project also contains various Schedule 2 DPs that, under the EIAO, require Environmental Permits (EPs) to be granted by the DEP before they may be either constructed

or operated. **Table 2.1** summarises the four individual DPs under this Project. **Figure 2.1** shows the locations of these Schedule 2 DPs.

**Table 2.1 Schedule 2 Designated Projects under this Project**

Item	Designated Project	EIAO Reference
DP1	Central-Wanchai Bypass (CWB)	Schedule 2, Part I, A.7
DP2	Road P2 and other roads which are classified as primary/district distributor roads	Schedule 2, Part I, A.1
DP3	Reclamation works	Schedule 2, Part I, C.1
DP4	The North Island Line (NIL) Protection Works within CRIII	Schedule 2, Part I, A.7

2.2.4. The designated project work I (DP1) was awarded to China State-Leader Joint Venture HK/2012/08 as part of the Project works by the Civil Engineering and Development Department (CEDD). The construction work under Contract no. HK/2012/08 was commenced on 27 May 2013.

**2.3 Project Organization and Contact Personnel**

2.3.1 Civil Engineering and Development Department is the overall project controllers for the Central Reclamation Phase III Project. For the construction phase of the Project, Project Engineer, Contractor(s), Environmental Team and Independent Environmental Checker are appointed to manage and control environmental issues.

2.3.2 The proposed project organization and lines of communication with respect to environmental protection works are shown in **Figure 2.2**. Key personnel and contact particulars are summarized in **Table 2.2**:

**Table 2.2 Contact Details of Key Personnel**

Party	Role	Post	Name	Contact No.	Contact Fax
AECOM	Engineer's Representative for WDII	Principal Resident Engineer	Mr. Frankie Fan	2587 1778	2587 1877
	Engineer's Representative for CWB	Principal Resident Engineer	Mr. Peter Poon	3922 3388	3912 3010
China State-Leader JV	Contractor under Contract no. HK/2012/08	Project Director	C. N. LAI	9106 5806	2877 1522
		Project Manager	Mr. Eddie Chung	9189 8118	

Party	Role	Post	Name	Contact No.	Contact Fax
		Site Agent	<a href="#">Mr. Keith Tse</a>	9037 1839	
		Environmental Officer	Mr. James Ma	9130 9549	
		Environmental Supervisor	Mr. Y. L. HO	9856 5669	
ENVIRON Hong Kong Limited	Independent Environmental Checker (IEC)	Independent Environmental Checker (IEC)	Mr. David Yeung	3465 2888	3465 2899
Lam Geotechnics Limited	Environmental Team (ET)	Environmental Team Leader (ETL)	Mr. Raymond Dai	2882 3939	2882 3331

2.3.3 In this reporting month, the principal work activities of the contract is included as follows:

Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West

- [Diaphragm wall construction works](#)
- [Removal of rock armour](#)
- [Socket H-pile construction](#)

2.3.4 In coming reporting month, the principal work activities of the contract is anticipated as follows:

Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West

- [Removal of rock armour](#)
- [Socket H-pile construction](#)



### 3 STATUS OF REGULATORY COMPLIANCE

#### 3.1 Status of Environmental Licensing and Permitting under the Project

3.1.1. A summary of the current status on licences and/or permits on environmental protection pertinent to the Project is shown in **Table 3.1**.

**Table 3.1 Summary of the current status on licences and/or permits on environmental protection pertinent to the Project**

Permits and/or Licences	Reference No.	Issued Date	Status
Environmental Permit	EP-122/2002/D	1 Sep 2009	Valid

3.1.2. The current status on licences and/or permits on environmental protection pertinent for contract no. HK/2012/08 showed in **Table 3.2**.

**Table 3.2 Cumulative Summary of Valid Licences and Permits under Contract no. HK/2012/08**

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Notification of Works Under APCO	355439	4 Feb 2013	N/A	Valid
Registration as a Chemical Waste Producer	5213-134-C3790-01	8 Mar 2013	N/A	Valid
Billing Account under Waste Disposal Ordinance	7016883	18 Feb 2013	18 Jul 2017	Valid
Billing Account under Waste Disposal Ordinance (Dumping by Vessel)	-	-	-	-
Construction Noise Permit	GW-RS0930-14	8 Sep 2014	10 Sep 2014 to 8 Mar 2015	Valid
Water Discharge Licence	WT00018470-2014	6 Mar 2014	31 Mar 2019	Valid



Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Dumping Permit (Type 1- Open Sea Disposal)	EP/MD/15-219	5 Feb 2015	10 Aug 2015	Valid
Dumping Permit (Type 2- Confined Marine Disposal)	EP/MD/15-193	20 Jan 2015	26 Feb 2015	Valid

3.1.3. Implementation status of the recommended mitigation measures during this reporting month is presented in [Appendix 3.1](#).

## 4 MONITORING REQUIREMENTS

### 4.1 Noise Monitoring

#### NOISE MONITORING STATIONS

- 4.1.1. The continuous noise monitoring station for the Project is listed and shown in **Table 4.1** and **Figure 4.1.** **Appendix 4.1** shows the established Action/Limit Levels for the monitoring works.

**Table 4.1 Continuous Noise Monitoring Stations**

District	Station	Description
Central	ACL3	City Hall

#### NOISE MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.1.2. Continuous 24-hour noise monitoring shall be carried out at the designated monitoring stations. The following is an initial guide on the regular monitoring frequency for each station on a 24 hours daily basis when noise generating activities are underway:
- One set of measurements between 0700 and 1900 hours on normal weekdays.
  - One set of measurements between 1900 and 2300 hours on normal weekdays and 0700 and 2300 hours on public holidays.
  - One set of measurements between 2300 and 0700 hours on next day on every day.
- 4.1.3. If construction works are extended to include works during the hours of 1900 – 0700 as well as public holidays and Sundays, additional weekly impact monitoring shall be carried out during respective restricted hours periods. Applicable permits under NCO shall be obtained by the Contractor.

#### MONITORING EQUIPMENT

- 4.1.4. As referred to in the Technical Memorandum <sup>TM</sup> issued under the NCO, sound level meters in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration level from before and after the noise measurement agrees to within 1.0 dB.
- 4.1.5. Noise measurements shall not be made in fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

4.1.6. The sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency before deployment to the site and during each site visit. Measurements will be accepted as valid only if the calibration level from before and after the noise measurement agrees to within 1.0 dB.

**4.2 Air Quality Monitoring**

AIR QUALITY MONITORING STATIONS

4.2.1. The air quality monitoring stations for the Project are listed and shown in **Table 4.2** and **Figure 4.1**. **Appendix 4.1** shows the established Action/Limit Levels for the monitoring works.

**Table 4.2 Air Quality Monitoring Stations**

Station ID	Description
ACL1	City Hall
ACL2a	Contractor HK/2012/08 Site Office

AIR QUALITY MONITORING PARAMETERS, FREQUENCY AND DURATION

4.2.2. One-hour and 24-hour TSP levels should be measured to indicate the impacts of construction dust on air quality. The 24-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B.

4.2.3. All relevant data including temperature, pressure, weather conditions, elapsed-time meter reading for the start and stop of the sampler, identification and weight of the filter paper, and any other local atmospheric factors affecting or affected by site conditions, etc., shall be recorded down in detail.

4.2.4. For regular impact monitoring, the sampling frequency of at least once in every six-days, shall be strictly observed at all the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least three times in every six-days should be undertaken when the highest dust impact occurs.

SAMPLING PROCEDURE AND MONITORING EQUIPMENT

4.2.5. High volume samplers (HVSs) in compliance with the following specifications shall be used for carrying out the 1-hour and 24-hour TSP monitoring:

- 0.6 – 1.7 m<sup>3</sup> per minute adjustable flow range;
- Equipped with a timing / control device with +/- 5 minutes accuracy for 24 hours operation;
- Installed with elapsed-time meter with +/- 2 minutes accuracy for 24 hours operation;
- Capable of providing a minimum exposed area of 406 cm<sup>2</sup>;

- Flow control accuracy: +/- 2.5% deviation over 24-hour sampling period;
- Equipped with a shelter to protect the filter and sampler;
- Incorporated with an electronic mass flow rate controller or other equivalent devices;
- Equipped with a flow recorder for continuous monitoring;
- Provided with a peaked roof inlet;
- Incorporated with a manometer;
- Able to hold and seal the filter paper to the sampler housing at horizontal position;
- Easily changeable filter; and
- Capable of operating continuously for a 24-hour period.

4.2.6. Initial calibration of dust monitoring equipment shall be conducted upon installation and thereafter at bi-monthly intervals. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The concern parties such as IEC shall properly document the calibration data for future reference. All the data should be converted into standard temperature and pressure condition.

#### LABORATORY MEASUREMENT / ANALYSIS

- 4.2.7. A clean laboratory with constant temperature and humidity control, and equipped with necessary measuring and conditioning instruments to handle the dust samples collected, shall be available for sample analysis, and equipment calibration and maintenance. The laboratory should be HOKLAS accredited.
- 4.2.8. Filter paper of size 8" x 10" shall be labelled before sampling. It shall be a clean filter paper with no pinholes, and shall be conditioned in a humidity-controlled chamber for over 24-hours and be pre-weighed before use for the sampling.
- 4.2.9. After sampling, the filter paper loaded with dust shall be kept in a clean and tightly sealed plastic bag. The filter paper shall then be returned to the laboratory for reconditioning in the humidity controlled chamber followed by accurate weighing by an electronic balance with readout down to 0.1 mg. The balance shall be regularly calibrated against a traceable standard.
- 4.2.10. All the collected samples shall be kept in a good condition for 6 months before disposal.
- 4.2.11. Current calibration certificates of equipment are presented in **Appendix 4.2.**

4.3 Water Quality Monitoring

WATER QUALITY MONITORING STATIONS

4.3.1 The water quality monitoring stations for the Project are listed and shown in **Table 4.3** and **Figure 4.1**. **Appendix 4.1** shows the established Action/Limit Levels for the monitoring works.

**Table 4.3 Water Quality Monitoring Stations**

Station ID	Description	Easting	Northing
<b>Cooling Water Intakes</b>			
M5B	Swire / Government Headquarters/ Tamar Development/ MTRCL and HSBC Headquarters	835169	816052
<b>Culverts (Reference Station)</b>			
Culvert J	Culvert J Outfall Location	835082	816071

WATER QUALITY PARAMETERS

- 4.3.2. Monitoring of dissolved oxygen (DO), turbidity and suspended solids (SS) shall be carried out at WSD flushing water intakes and cooling water intakes. DO and Turbidity are measured in-situ while SS is determined in laboratory.
- 4.3.3. In association with the water quality parameters, other relevant data shall also be measured, such as monitoring location/position, time, sampling depth, water temperature, pH, salinity, dissolved oxygen (DO) saturation, weather conditions, sea conditions, tidal stage, and any special phenomena and work underway at the construction site etc.

SAMPLING PROCEDURES AND MONITORING EQUIPMENT

4.3.4. The interval between two sets of monitoring should not be less than 36 hours except where there are exceedances of Action and/or Limit Levels, in which case the monitoring frequency will be increased. **Table 4.4** shows the proposed monitoring frequency and water quality parameters. Duplicate in-situ measurements and water sampling should be carried out in each sampling event. For selection of tides for in-situ measurement and water sampling, tidal range of individual flood and ebb tides should be not less than 0.5m.

**Table 4.4 Marine Water Quality Monitoring Frequency and Parameters**

Activities	Monitoring Frequency <sup>1</sup>	Parameters <sup>2</sup>
During the 4-week baseline monitoring period	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity
During marine construction works	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity

Activities	Monitoring Frequency <sup>1</sup>	Parameters <sup>2</sup>
After completion of marine construction works	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity

Notes:

1. For selection of tides for in-situ measurement and water sampling, tidal range of individual flood and ebb tides should be not less than 0.5m.
2. Turbidity should be measured in situ whereas SS should be determined by laboratory.

DISSOLVED OXYGEN AND TEMPERATURE MEASURING EQUIPMENT

4.3.5. The instrument should be a portable, weatherproof dissolved oxygen measuring instrument complete with cable, sensor, comprehensive operation manuals, and use a DC power source. It should be capable of measuring:

- a dissolved oxygen level in the range of 0-20 mg/l and 0-200% saturation
- a temperature of 0-45 degree Celsius

4.3.6. It should have a membrane electrode with automatic temperature compensation complete with a cable. Sufficient stocks of spare electrodes and cables should be available for replacement where necessary. (e.g. YSI model 59 meter, YSI 5739 probe, YSI 5795A submersible stirrer with reel and cable or an approved similar instrument).

4.3.7. Should salinity compensation not be build-in in the DO equipment, in-situ salinity shall be measured to calibrate the DO equipment prior to each DO measurement.

TURBIDITY MEASUREMENT INSTRUMENT

4.3.8. The instrument should be a portable, weatherproof turbidity-measuring instrument complete with comprehensive operation manual. The equipment should use a DC power source. It should have a photoelectric sensor capable of measuring turbidity between 0-1000 NTU and be complete with a cable (e.g. Hach model 2100P or an approved similar instrument).

SAMPLER

4.3.9. A water sampler comprises a transparent PVC cylinder, with a capacity of not less than 2 litres, and can be effectively sealed with latex cups at both ends. The sampler should have a positive latching system to keep it open and prevent premature closure until released by a messenger when the sampler is at the selected water depth (e.g. Kahlsico Water Sampler or an approved similar instrument).

SAMPLE CONTAINER AND STORAGE

4.3.10. Water samples for suspended solids measurement should be collected in high-density polythene bottles, packed in ice (cooled to 4°C without being frozen), and delivered to ALS Technichem (HK) Pty Ltd. as soon as possible after collection for analysis.

WATER DEPTH DETECTOR

4.3.11. A portable, battery-operated echo sounder shall be used for the determination of water depth at each designated monitoring station. This unit can either be handheld or affixed to the bottom of the workboat, if the same vessel is to be used throughout the monitoring programme.

#### SALINITY

- 4.3.12. A portable salinometer capable of measuring salinity in the range of 0-40 ppt shall be provided for measuring salinity of the water at each of monitoring location.

#### MONITORING POSITION EQUIPMENT

- 4.3.13. A hand-held or boat-fixed type digital Global Positioning System (GPS) with waypoint bearing indication or other equivalent instrument of similar accuracy shall be provided and used during monitoring to ensure the monitoring vessel is at the correct location before taking measurements.

#### CALIBRATION OF IN-SITU INSTRUMENTS

- 4.3.14. All in-situ monitoring instrument shall be checked, calibrated and certified by a laboratory accredited under HOKLAS or equivalent before use, and subsequently re-calibrated at 3 monthly intervals throughout all stages of the water quality monitoring. Responses of sensors and electrodes should be checked with certified standard solutions before each use. Wet bulb calibration for a DO meter shall be carried out before measurement at each monitoring location.
- 4.3.15. For the on site calibration of field equipment by the ET, the BS 127:1993, "Guide to Field and on-site test methods for the analysis of waters" should be observed.
- 4.3.16. Sufficient stocks of spare parts should be maintained for replacements when necessary. Backup monitoring equipment shall also be made available so that monitoring can proceed uninterrupted even when some equipment is under maintenance, calibration, etc.
- 4.3.17. Current calibration certificates of equipments are presented in [Appendix 4.2](#).

#### LABORATORY MEASUREMENT / ANALYSIS

- 4.3.18. Analysis of suspended solids has been carried out in a HOKLAS accredited laboratory, ALS Technichem (HK) Pty Ltd. Water samples of about 1L shall be collected at the monitoring stations for carrying out the laboratory SS determination. The SS determination work shall start within 24 hours after collection of the water samples. The SS determination shall follow APHA 19ed or equivalent methods subject to the approval of IEC and EPD.



## 5 MONITORING RESULTS

5.0.1. The environmental monitoring will be implemented based on the division of works areas of each designated project managed under different contracts with separate FEP applied by individual contractors. Overall layout showing work areas of various contracts, latest status of work commencement and monitoring stations is shown in [Figure 2.1](#) and [Figure 4.1](#). The monitoring results are presented in according to the Individual Contract(s).

5.0.2. In the reporting month, the concurrent contract is:

- Contract no. HK/2012/08 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai West.

5.0.3. The environment monitoring schedules for reporting month and coming month are presented in [Appendix 5.1](#).

### 5.1 Noise Monitoring Results

5.1.1 Due to safety concerned, the location of the continuous noise monitoring station at City Hall was finely adjusted to the roof of the City Hall, Low Block on 1 May 2013.

5.1.2 The proposed division of noise monitoring stations is summarized in Table 5.1 below.

**Table 5.1 Continuous Noise Monitoring Stations for Contract no. HK/2012/08**

Location ID	District	Description
ACL3	Central	City Hall

*Remarks: Continuous noise monitoring results and graphical presentation for ACL3 during restricted hours and night time period are for information only.*

5.1.3 [No action or limit level exceedances was recorded at ACL3 – City Hall in the reporting month.](#)

5.1.4 Continuous noise monitoring results measured in this reporting period are reviewed and summarized. Details of continuous noise monitoring results and graphical presentation can be referred to [Appendix 5.2](#).

### 5.2 Air Quality Monitoring Results

5.2.1 The proposed division of air quality monitoring stations are summarized in **Table 5.2** below.

**Table 5.2 Air Quality Monitoring Station for Contract no. HK/2012/08**

Station	Description
ACL1	City Hall
ACL2a	Contractor HK/2012/08 Site Office

- 5.2.2 Due to the defective electricity supply found at monitoring station ACL1 and the advice from City Hall Building Management, the air monitoring station ACL1 – City Hall was finely adjusted on 28 Feb 2014 to an alternate electricity supply.
- 5.2.3 Due to the large scale renovation works at People’s Liberation Army Headquarter, a Proposal for Relocation of Air Quality Monitoring Station at People’s Liberation Army Headquarter (ACL2) was formally submitted to EPD on 4th November, 2013.
- 5.2.4 Air Quality Monitoring at ACL2 was temporarily suspended during the period from 14th November, 2013 to 3rd December, 2013.
- 5.2.5 The Proposal for Relocation of Air Quality Monitoring Station at People’s Liberation Army Headquarter (ACL2) was approved by EPD on 27 November 2013.
- 5.2.6 According to the approved proposal for relocation of Air Quality Monitoring station, the action and limit levels of ACL2a shall adopt the reference monitoring result from the baseline air monitoring report for EP/364/2009 in 22 April 2010 in which approved by EPD.
- 5.2.7 The air quality monitoring at ACL2a – Contractor HK/2012/08 Site Office was commenced on 7 December 2013.
- 5.2.8 [No action or limit level exceedances was recorded at ACL 1 – City Hall and ACL2a – Contractor HK/2012/08 Site Office in the reporting month.](#)
- 5.2.9 The air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in [Appendix 5.3](#).

**5.3 Water Quality Monitoring Results**

- 5.3.1 The proposed division of water quality monitoring stations are summarized in **Table 5.3** below.

**Table 5.3 Water Quality Monitoring Station for Contract no. HK/2012/08**

Station ID	Description
<b>Cooling Water Intakes</b>	
M5B	Swire / Government Headquarters/ Tamar Development/ MTRCL and HSBC Headquarters
<b>Culverts (Reference Station)</b>	
Culvert J	Culvert J Outfall Location

5.3.2 Water quality monitoring results measured in this reporting period are reviewed and summarized. Detail of water quality monitoring results and graphical presentation can be referred in **Table 5.4** and [Appendix 5.4](#)

5.3.3 No action or limit level exceedance was recorded at M5B – Central water intake in the reporting month.

**Table 5.4 Summary of Water Quality Monitoring Exceedance in Reporting Month**

Contract No.	Water quality monitoring station	Mid-flood				Mid-ebb			
		DO		SS		DO		SS	
		AL	LL	AL	LL	AL	LL	AL	LL
HK/2012/08	M5B <sup>2</sup>	0	0	0	0	0	0	0	0
	Culvert J <sup>1</sup>	-	-	-	-	-	-	-	-
<b>Total</b>		<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>

Remarks<sup>1</sup>: No action or limit level are not applicable to reference station Culvert J.

Remarks<sup>2</sup>: Turbidity measurement are reported as reference.

**5.4 WASTE MONITORING RESULTS**

5.4.1 Inert and non-inert C&D wastes were disposed in this reporting month. Details of the waste flow table are summarized in Table 5.5.

**Table 5.5 Details of Waste Disposal for Contract no. HK/2012/08**

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m3	Nil 1652	396 22470	TM38 TKO137
Inert C&D materials recycled, m3	NIL	NIL	NIL
Non-inert C&D materials disposed, m3	25	700	SENT Landfill
Non-inert C&D materials recycled, m3	NIL	NIL	NIL
Chemical waste disposed, kg	NIL	NIL	NIL

## **6 COMPLIANCE AUDIT**

6.0.1. The Event Action Plan for construction noise and air quality are presented in [Appendix 6.1](#).

### **6.1 Noise Monitoring**

6.1.1. [No action or limit level exceedance was recorded at ACL3- City Hall in this reporting month.](#)

### **6.2 Air Quality Monitoring**

6.2.1. [No action or limit level exceedance was recorded at ACL 1 – City Hall and ACL2a – Contractor HK/2012/08 Site Office in the reporting month.](#)

### **6.3 Water Quality Monitoring**

6.3.1. [No action or limit level exceedance was recorded at M5B – Central water intake in this reporting month.](#)

### **6.4 Review of the Reasons for and the Implications of Non-compliance**

6.4.1 There was no non-compliance from the site audits in the reporting period. The observations and recommendations made in each individual site audit session were presented in Section 8.

### **6.5 Summary of action taken in the event of and follow-up on non-compliance**

6.5.1 There was no particular action taken since no non-compliance was recorded from the site audits in the reporting period.

## 7 CUMULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT PROJECTS

- 7.0.1. This section addresses the relevant cumulative construction impact due to the concurrent activities of the current projects including the Central Reclamation Phase III (CRIII), Wan Chai Development Phase II (WDII), Central-WanChai Bypass (CWB), Island Eastern Corridor Link projects (IECL) and Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East (CWB Tunnel).
- 7.0.2. According to the Final EM&A report of Central Reclamation Phase III (CRIII) for Contract HK 12/02, the major construction activities were completed by end of January 2014 and no construction activities were undertaken thereafter and the water quality monitoring was completed in October 2011. As such, it is considered that there were no cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) undertaken by contractor HK12/02 in the reporting month.
- 7.0.3. [According to the construction programme of Central-Wanchai Bypass at Wanchai West at the Central Reclamation Phase III area, Diaphragm wall construction, removal of rock armour, and socket H piling works were performed in February 2015 reporting month.](#) As no project related exceedance were recorded during the reporting period, cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) was considered as insignificant.
- 7.0.1. [According to the construction programme of Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects, the major construction activities under Wan Chai Development Phase II were marine works at HKCEC areas, tunnel works and foundation works at Wan Chai East and dredging works at Wan Chai West. The major construction activities under Central-Wan Chai Bypass and Island Eastern Corridor Link Projects were bridge construction and road works at Central Interchange, land based bored pilling works and ELS works at Victoria Park, segment launching works and tunnel works at North Point area. Marine-based construction activities were seawall construction and filling works at EX-PCWA and seawall construction and filling works at TS3 at Causeway Bay Typhoon Shelter in the reporting month.](#)
- 7.0.2. No significant air impact from construction activities was anticipated in the reporting month. Besides, no project related exceedance was recorded during the water, air and noise environmental monitoring events in the reporting month. Thus, it is evaluated that the cumulative construction impact from the concurrent projects including Central Reclamation Phase III (CRIII), Wan Chai Development Phase II (WDII), Central-WanChai Bypass (CWB), Island Eastern Corridor Link projects (IECL) was insignificant.

**8 ENVIRONMENTAL SITE AUDIT**

**8.0.1.** Four site inspections for Contract no. HK/2012/08 were carried out in the reporting month on 3, 10, 17 and 26 February 2015. The results of inspection and outcome are summarized in **Table 8.1**

**Table 8.1 Summary of Environmental Inspections for Contract no. HK/2012/08**

Item	Date	Observations	Action taken by Contractor	Outcome
150203_01	3 Feb 15	The panels of the air compressor shall be kept close during operation at Portion 1	The panels of the air compressor were closed	Completion as observed on 10 Feb 2015
150217_01	17 Feb 15	Silt curtain shall be used properly such that it shall be weighted at the bottom to ensure muddy water does not dispersed out of the silt curtain area at Portion 1	Silt curtain was properly deployed and was fully extended at Portion 1	Completion as observed on 3 Mar 2015

**9 COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION**

- 9.0.1. One environmental complaint was received in the reporting month.
- 9.0.2. A public complaint (EPD ref: H04/RS/0001716-15 dated 21 January 2015) regarding air quality impact referred by EPD was received by ET on 11 February 2015.
- 9.0.3. According to the relevant site records, trench grabbing for D-wall construction and socket H-pile construction were conducted at the concerned location on 21 January 2015. Dust screen for socket H-pile construction, maintenance of site haul road in wet condition and water spraying at vehicle entrance/exit points of HK/2012/08 Contractor site office and Portion I were implemented by the Contractor of HK/2012/08 near the concerned location on 21 January 2015.
- 9.0.4. In addition, no environmental deficiency related to dust mitigation was identified at the concerned location during weekly environmental inspections conducted on 27 Jan, 3 and 10 Feb 2015 and dust mitigation measures including water spraying for dusty haul road and provision of wheel washing were in place and no dust related impact from the construction works at the concerned location was observed.
- 9.0.5. Meanwhile, the Air Quality Health Index (AQHI) recorded by EPD across Western District and Eastern District on 21 January 2015 was ranged from 4 to 10+ indicating a severely high concentration of ambient air pollutants. Based on reviewing relevant impact monitoring data, elevated TSP were recorded at monitoring stations across Central to WanChai West area despite a non-Project related exceedance was recorded at nearby monitoring station ACL2a (Contractor HK/2012/08 Site Office) on 21 January 2015 and was considered to be contributed by ambient air pollutant.
- 9.0.6. The site condition under Contract HK/2012/08 at the concerned location was considered to be generally satisfactory and no non-conformity related to cumulative air quality impact was observed at the concerned location. Nevertheless, in view of the public concern, the contractor was reminded to enhance the dust mitigation measures implemented to minimize potential nuisance to nearby public.
- 9.0.7. The details of cumulative complaint log and updated summary of complaints are presented in **Appendix 9.1**
- 9.0.8. Cumulative statistic on complaints and successful prosecutions are summarized in **Table 9.1** and **Table 9.2** respectively.

**Table 9.1 Cumulative Statistics on Complaints**

Reporting Period	No. of Complaints
July 2013 – January 2015	0



February 2015	1
Total	1

**Table 9.2 Cumulative Statistics on Successful Prosecutions**

Environmental Parameters	Cumulative No. Brought Forward	No. of Successful Prosecutions this month (Offence Date)	Cumulative No. Project-to-Date
Air	0	0	0
Noise	0	0	0
Water	0	0	0
Waste	0	0	0
<b>Total</b>	<b>0</b>	<b>0</b>	<b>0</b>

## 10 CONCLUSION

- 10.0.1. The EM&A programme was carried out in accordance with the EM&A Manual requirements, minor alterations to the programme proposed were made in response to changing circumstances.
- 10.0.2. The scheduled construction activities and the recommended mitigation measures for the coming month are listed in **Table 10.1**. The construction programmes of individual contracts are provided in [Appendix 10.1](#).

**Table 10.1 Summary of Key Construction Activities of Individual Contract(s) to be commenced in Coming Reporting Month**


Contract No.	Key Construction Works	Recommended Mitigation Measures
HK/2012/08	<ul style="list-style-type: none"> <li>• <a href="#">Removal of rock armour</a></li> <li>• <a href="#">Socket H-pile construction</a></li> </ul>	<ul style="list-style-type: none"> <li>• Dust control during dust generating works;</li> <li>• Implementation of proper noise pollution control; and</li> <li>• Provision of protection to ensure no runoff out of site area or direct discharge into public drainage system.</li> </ul>



***Figure 2.1***

***Project Layout***



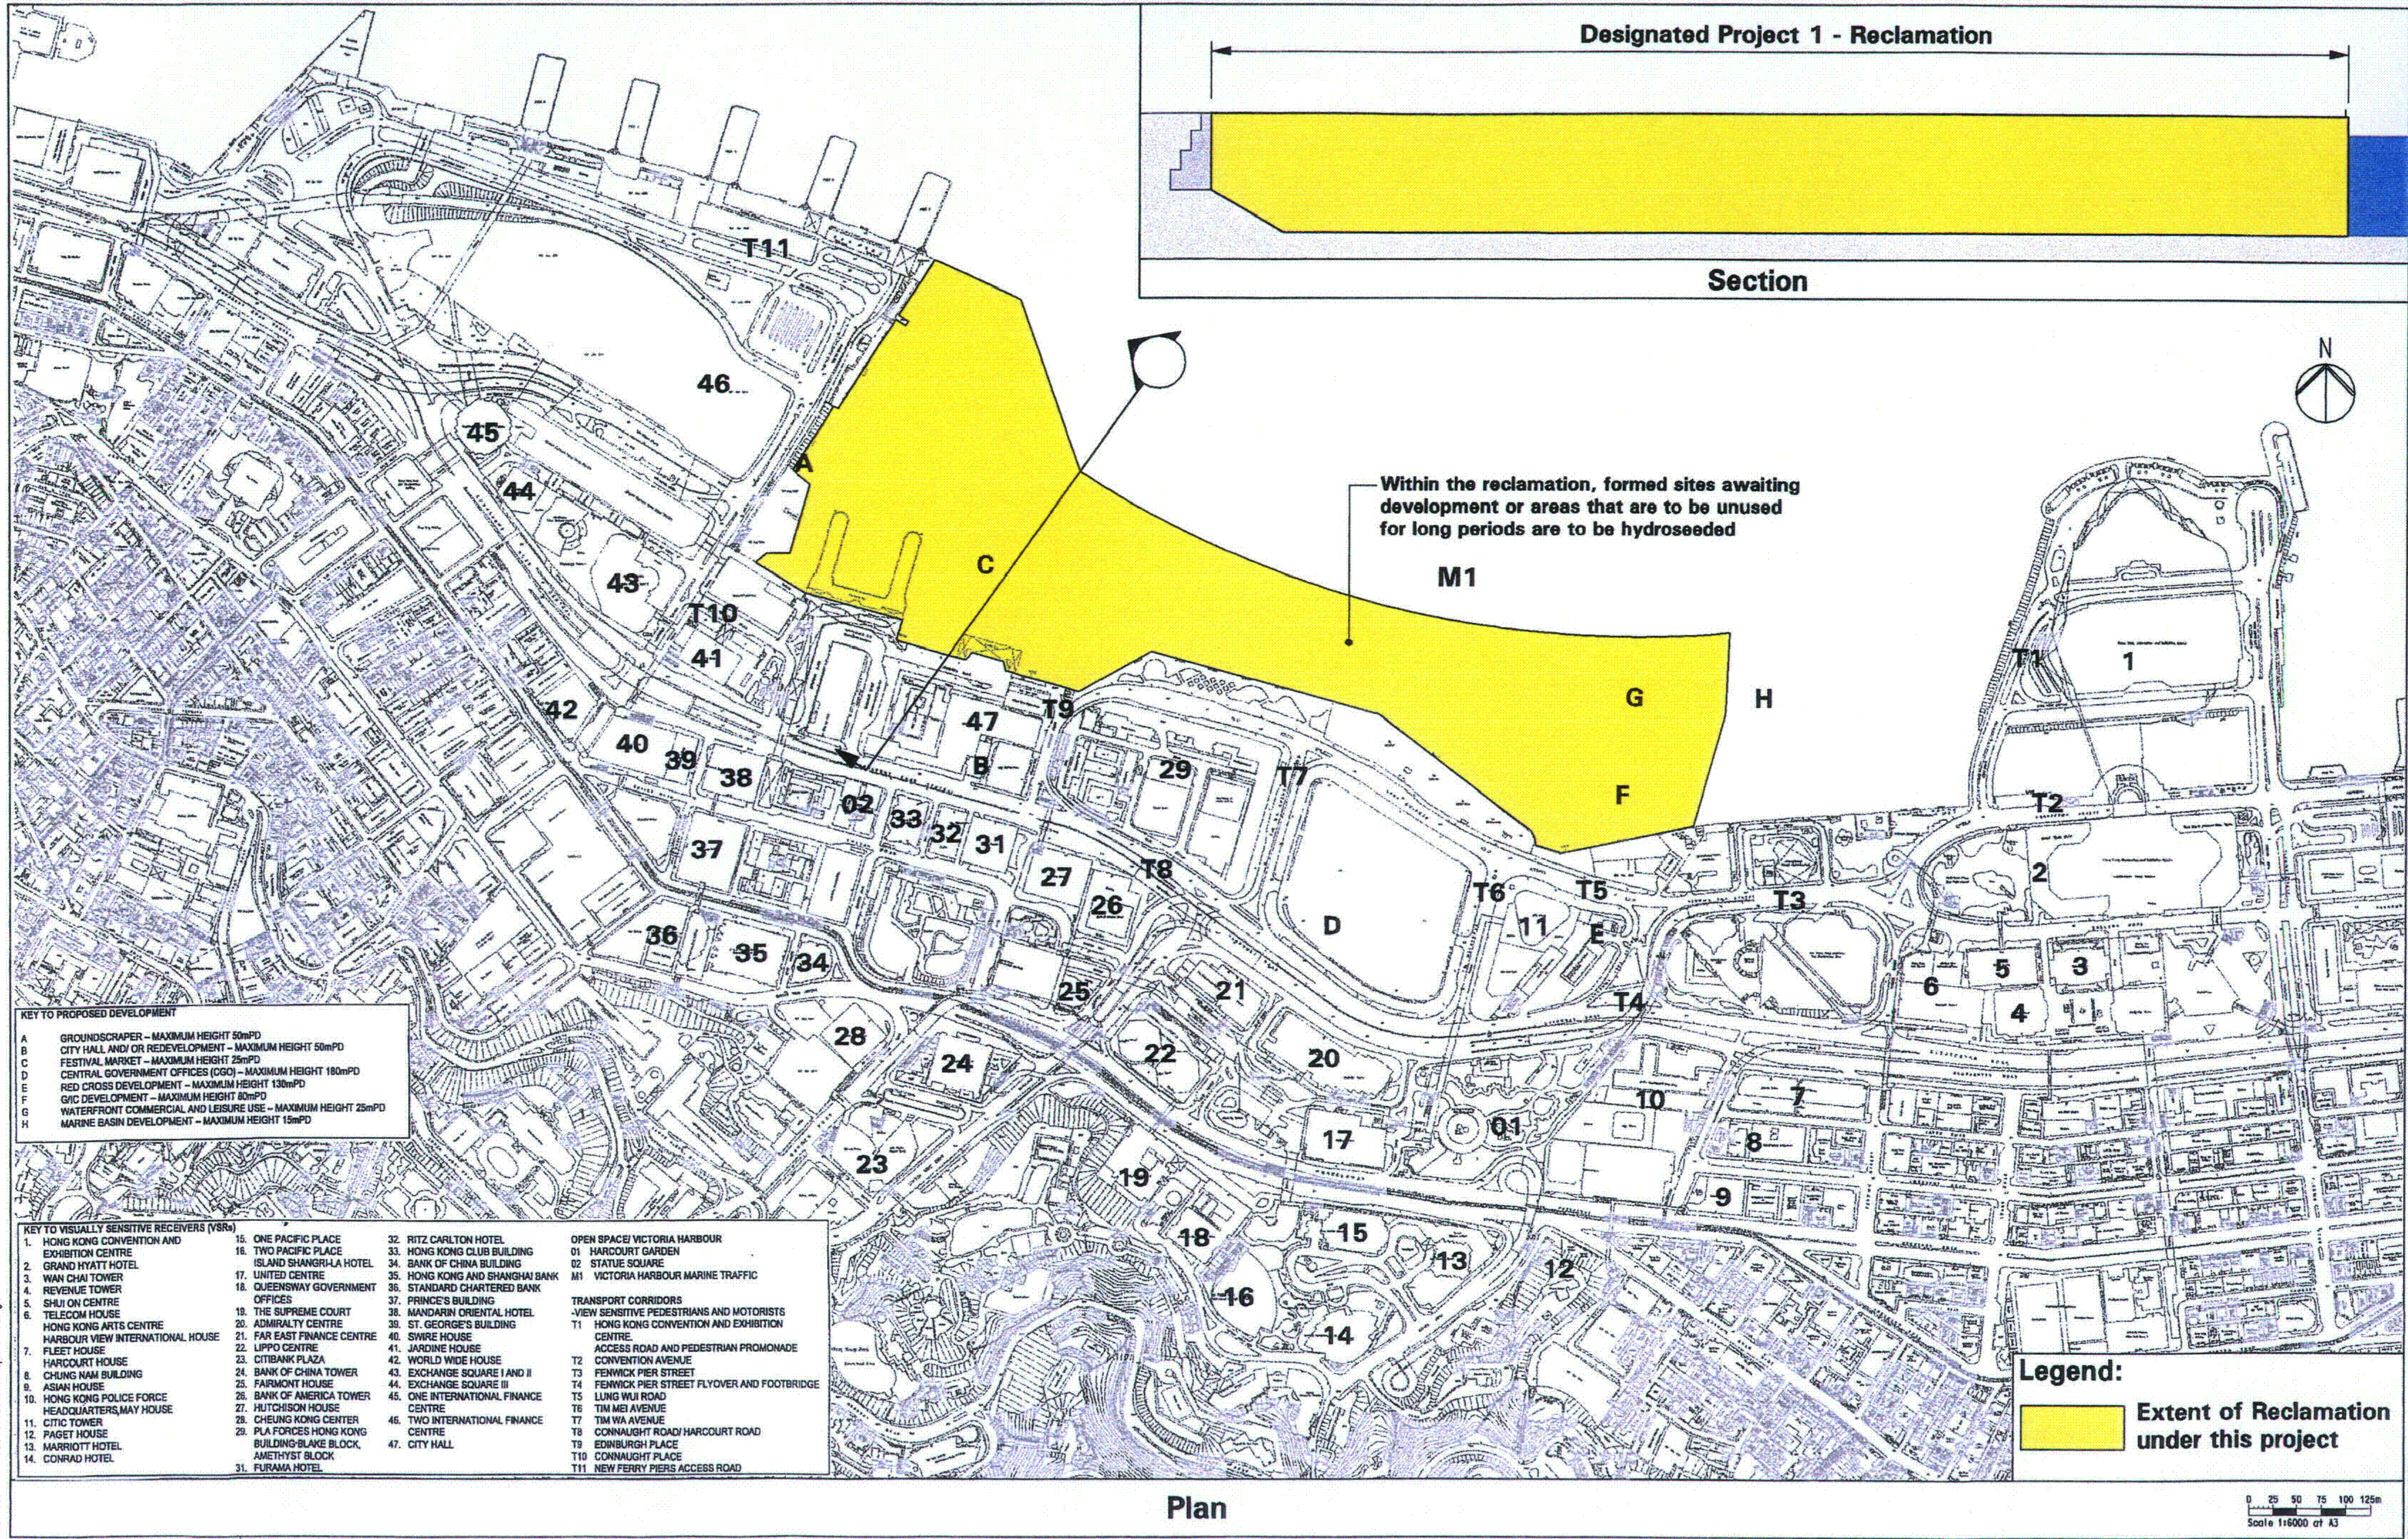


**KEY TO PROPOSED DEVELOPMENT**

A	GROUNDSCRAPER - MAXIMUM HEIGHT 50mPD
B	CITY HALL AND/OR REDEVELOPMENT - MAXIMUM HEIGHT 50mPD
C	FESTIVAL MARKET - MAXIMUM HEIGHT 25mPD
D	CENTRAL GOVERNMENT OFFICES (CGO) - MAXIMUM HEIGHT 180mPD
E	RED CROSS DEVELOPMENT - MAXIMUM HEIGHT 130mPD
F	G/C DEVELOPMENT - MAXIMUM HEIGHT 80mPD
G	WATERFRONT COMMERCIAL AND LEISURE USE - MAXIMUM HEIGHT 25mPD
H	MARINE BASIN DEVELOPMENT - MAXIMUM HEIGHT 15mPD

**KEY TO VISUALLY SENSITIVE RECEIVERS (VSRs)**

1. HONG KONG CONVENTION AND EXHIBITION CENTRE	15. ONE PACIFIC PLACE	32. RITZ CARLTON HOTEL	OPEN SPACE/ VICTORIA HARBOUR
2. GRAND HYATT HOTEL	16. TWO PACIFIC PLACE	33. HONG KONG CLUB BUILDING	01. HARCOURT GARDEN
3. WAN CHAI TOWER	17. UNITED CENTRE	34. BANK OF CHINA BUILDING	02. STATUE SQUARE
4. REVENUE TOWER	18. QUEENSWAY GOVERNMENT OFFICES	35. HONG KONG AND SHANGHAI BANK	M1. VICTORIA HARBOUR MARINE TRAFFIC
5. SHUI ON CENTRE	19. THE SUPREME COURT	36. STANDARD CHARTERED BANK	
6. TELECOM HOUSE	20. ADMIRALTY CENTRE	37. PRINCE'S BUILDING	TRANSPORT CORRIDORS
7. HONG KONG ARTS CENTRE	21. FAR EAST FINANCE CENTRE	38. MANDARIN ORIENTAL HOTEL	-VIEW SENSITIVE PEDESTRIANS AND MOTORISTS
8. HARBOUR VIEW INTERNATIONAL HOUSE	22. LIPPO CENTRE	39. ST. GEORGE'S BUILDING	T1. HONG KONG CONVENTION AND EXHIBITION CENTRE
9. FLEET HOUSE	23. CITIBANK PLAZA	40. SWIRE HOUSE	ACCESS ROAD AND PEDESTRIAN PROMONADE
10. HARCOURT HOUSE	24. BANK OF CHINA TOWER	41. JARDINE HOUSE	T2. CONVENTION AVENUE
11. CHUNG NAM BUILDING	25. FAIRMONT HOUSE	42. WORLD WIDE HOUSE	T3. FENWICK PIER STREET
12. ASIAN HOUSE	26. BANK OF AMERICA TOWER	43. EXCHANGE SQUARE I AND II	T4. FENWICK PIER STREET FLYOVER AND FOOTBRIDGE
13. HONG KONG POLICE FORCE HEADQUARTERS, MAY HOUSE	27. HUTCHISON HOUSE	44. EXCHANGE SQUARE III	T5. LUNG WUI ROAD
14. CITIC TOWER	28. CHEUNG KONG CENTER	45. ONE INTERNATIONAL FINANCE CENTRE	T6. TIM MEI AVENUE
15. PAGET HOUSE	29. PLA FORCES HONG KONG BUILDING-BLAKE BLOCK, AMETHYST BLOCK	46. TWO INTERNATIONAL FINANCE CENTRE	T7. TIM WA AVENUE
16. MARRIOTT HOTEL	30. FURAMA HOTEL	47. CITY HALL	T8. CONNAUGHT ROAD/ HARCOURT ROAD
17. CONRAD HOTEL			T9. EDINBURGH PLACE
			T10. CONNAUGHT PLACE
			T11. NEW FERRY PIERS ACCESS ROAD



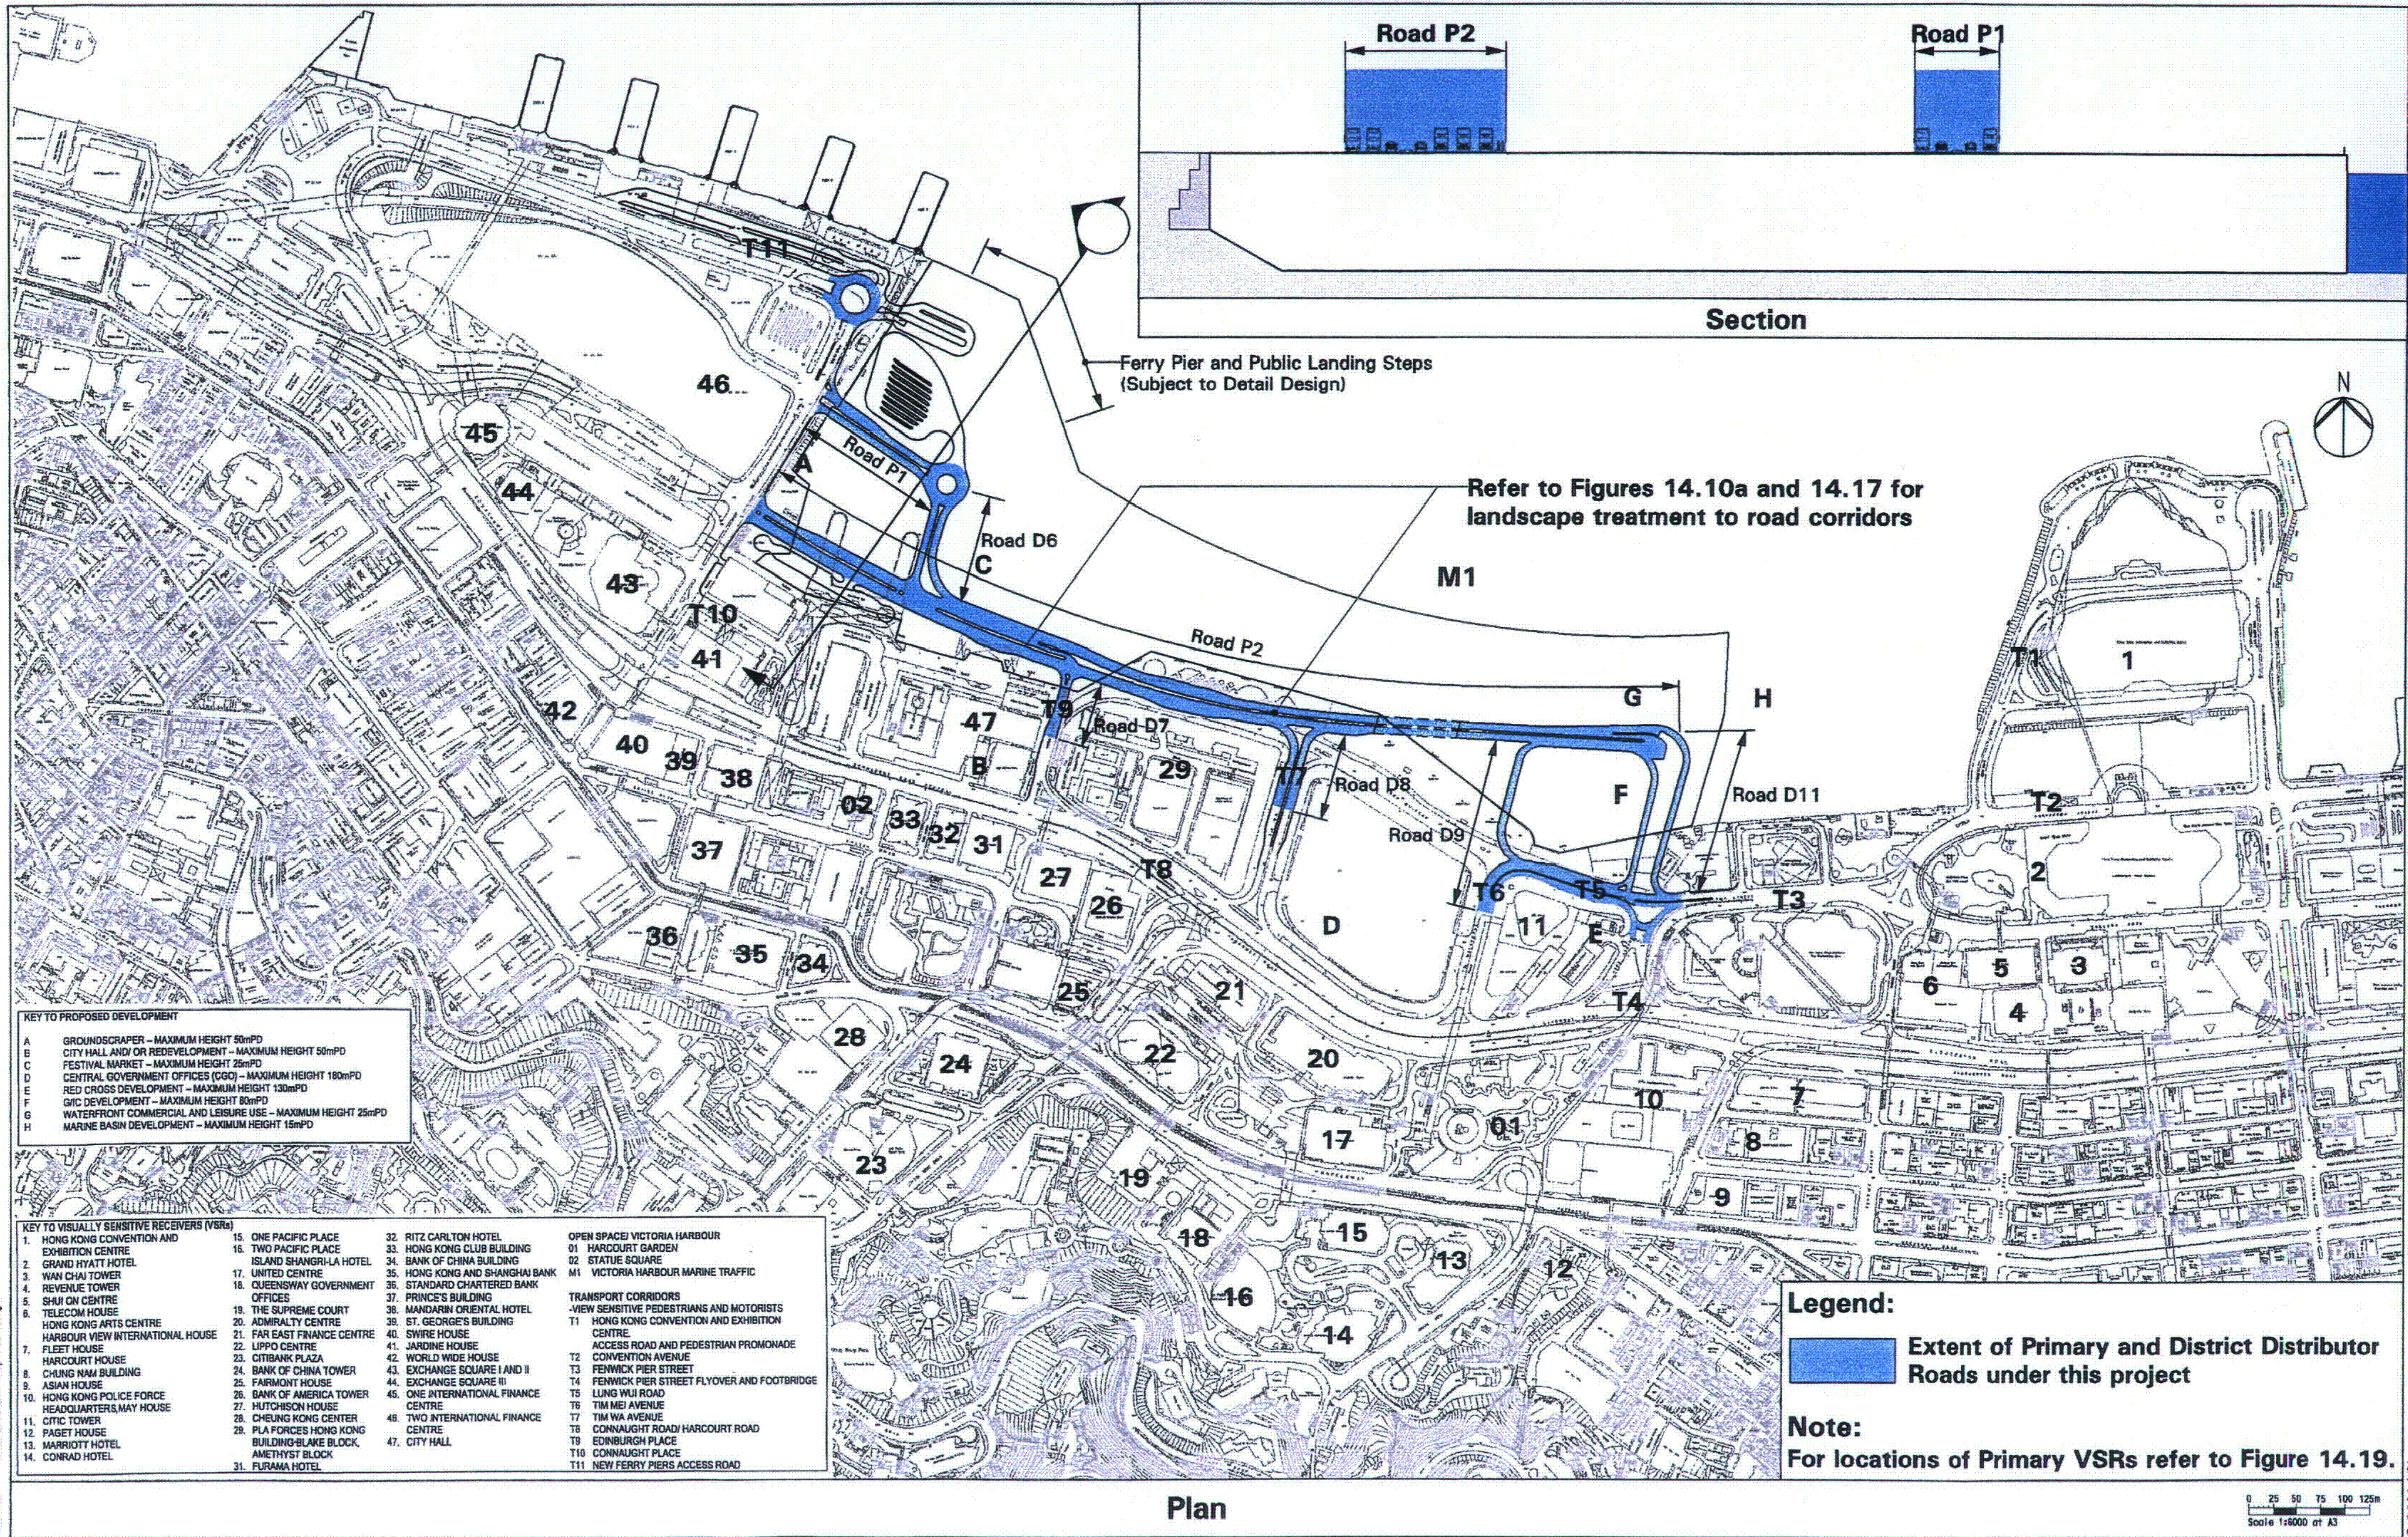

Designated Project 2 - Primary and District Distributor Roads  
Layout Plan and Section

Figure 14.10





**KEY TO PROPOSED DEVELOPMENT**

A	GROUNDSCRAPER - MAXIMUM HEIGHT 50mPD
B	CITY HALL AND/OR REDEVELOPMENT - MAXIMUM HEIGHT 50mPD
C	FESTIVAL MARKET - MAXIMUM HEIGHT 25mPD
D	CENTRAL GOVERNMENT OFFICES (CGO) - MAXIMUM HEIGHT 180mPD
E	RED CROSS DEVELOPMENT - MAXIMUM HEIGHT 130mPD
F	GVC DEVELOPMENT - MAXIMUM HEIGHT 80mPD
G	WATERFRONT COMMERCIAL AND LEISURE USE - MAXIMUM HEIGHT 25mPD
H	MARINE BASIN DEVELOPMENT - MAXIMUM HEIGHT 15mPD

**KEY TO VISUALLY SENSITIVE RECEIVERS (VSRs)**

1. HONG KONG CONVENTION AND EXHIBITION CENTRE	15. ONE PACIFIC PLACE	32. RITZ CARLTON HOTEL	OPEN SPACE/ VICTORIA HARBOUR
2. GRAND HYATT HOTEL	16. TWO PACIFIC PLACE	33. HONG KONG CLUB BUILDING	01 HARCOURT GARDEN
3. WAN CHAI TOWER	17. UNITED CENTRE	34. BANK OF CHINA BUILDING	02 STATUE SQUARE
4. REVENUE TOWER	18. QUEENSWAY GOVERNMENT OFFICES	35. HONG KONG AND SHANGHAI BANK	M1 VICTORIA HARBOUR MARINE TRAFFIC
5. SHUI ON CENTRE	19. THE SUPREME COURT	36. STANDARD CHARTERED BANK	TRANSPORT CORRIDORS
6. TELECOM HOUSE	20. ADMIRALTY CENTRE	37. PRINCE'S BUILDING	-VIEW SENSITIVE PEDESTRIANS AND MOTORISTS
7. FLEET HOUSE	21. FAR EAST FINANCE CENTRE	38. MANDARIN ORIENTAL HOTEL	T1 HONG KONG CONVENTION AND EXHIBITION CENTRE
8. HARCOURT HOUSE	22. LIPPO CENTRE	39. ST. GEORGE'S BUILDING	ACCESS ROAD AND PEDESTRIAN PROMENADE CONVENTION AVENUE
9. ASIAN HOUSE	23. CITIBANK PLAZA	40. SWIRE HOUSE	T2
10. HONG KONG POLICE FORCE HEADQUARTERS, MAY HOUSE	24. BANK OF CHINA TOWER	41. JAPANESE HOUSE	T3
11. CITIC TOWER	25. FAIRMONT HOUSE	42. WORLD WIDE HOUSE	T4 FENWICK PIER STREET FLYOVER AND FOOTBRIDGE
12. PAGET HOUSE	26. BANK OF AMERICA TOWER	43. EXCHANGE SQUARE I AND II	T5 LUNG WUI ROAD
13. MARRIOTT HOTEL	27. HUTCHISON HOUSE	44. EXCHANGE SQUARE III	T6 TIM MEI AVENUE
14. CONRAD HOTEL	28. CHEUNG KONG CENTER	45. ONE INTERNATIONAL FINANCE CENTRE	T7 TIM WA AVENUE
	29. PLA FORCES HONG KONG BUILDING-SLAKE BLOCK, AMETHYST BLOCK	46. TWO INTERNATIONAL FINANCE CENTRE	T8 CONNAUGHT ROAD/ HARCOURT ROAD
	31. PURANA HOTEL	47. CITY HALL	T9 EDINBURGH PLACE
			T10 CONNAUGHT PLACE
			T11 NEW FERRY PIERS ACCESS ROAD

**Legend:**

Extent of Central Wan Chai Bypass Tunnel under this project


Designated Project 3 - Central Wan Chai Bypass Tunnel  
Layout Plan and Section

Figure 14.11

PRINTED BY: GUY  
 FILENAME: H:\d\off\3\21\94\T-0716.dgn  
 11/11/94 10:00 AM

© 2001 ACL



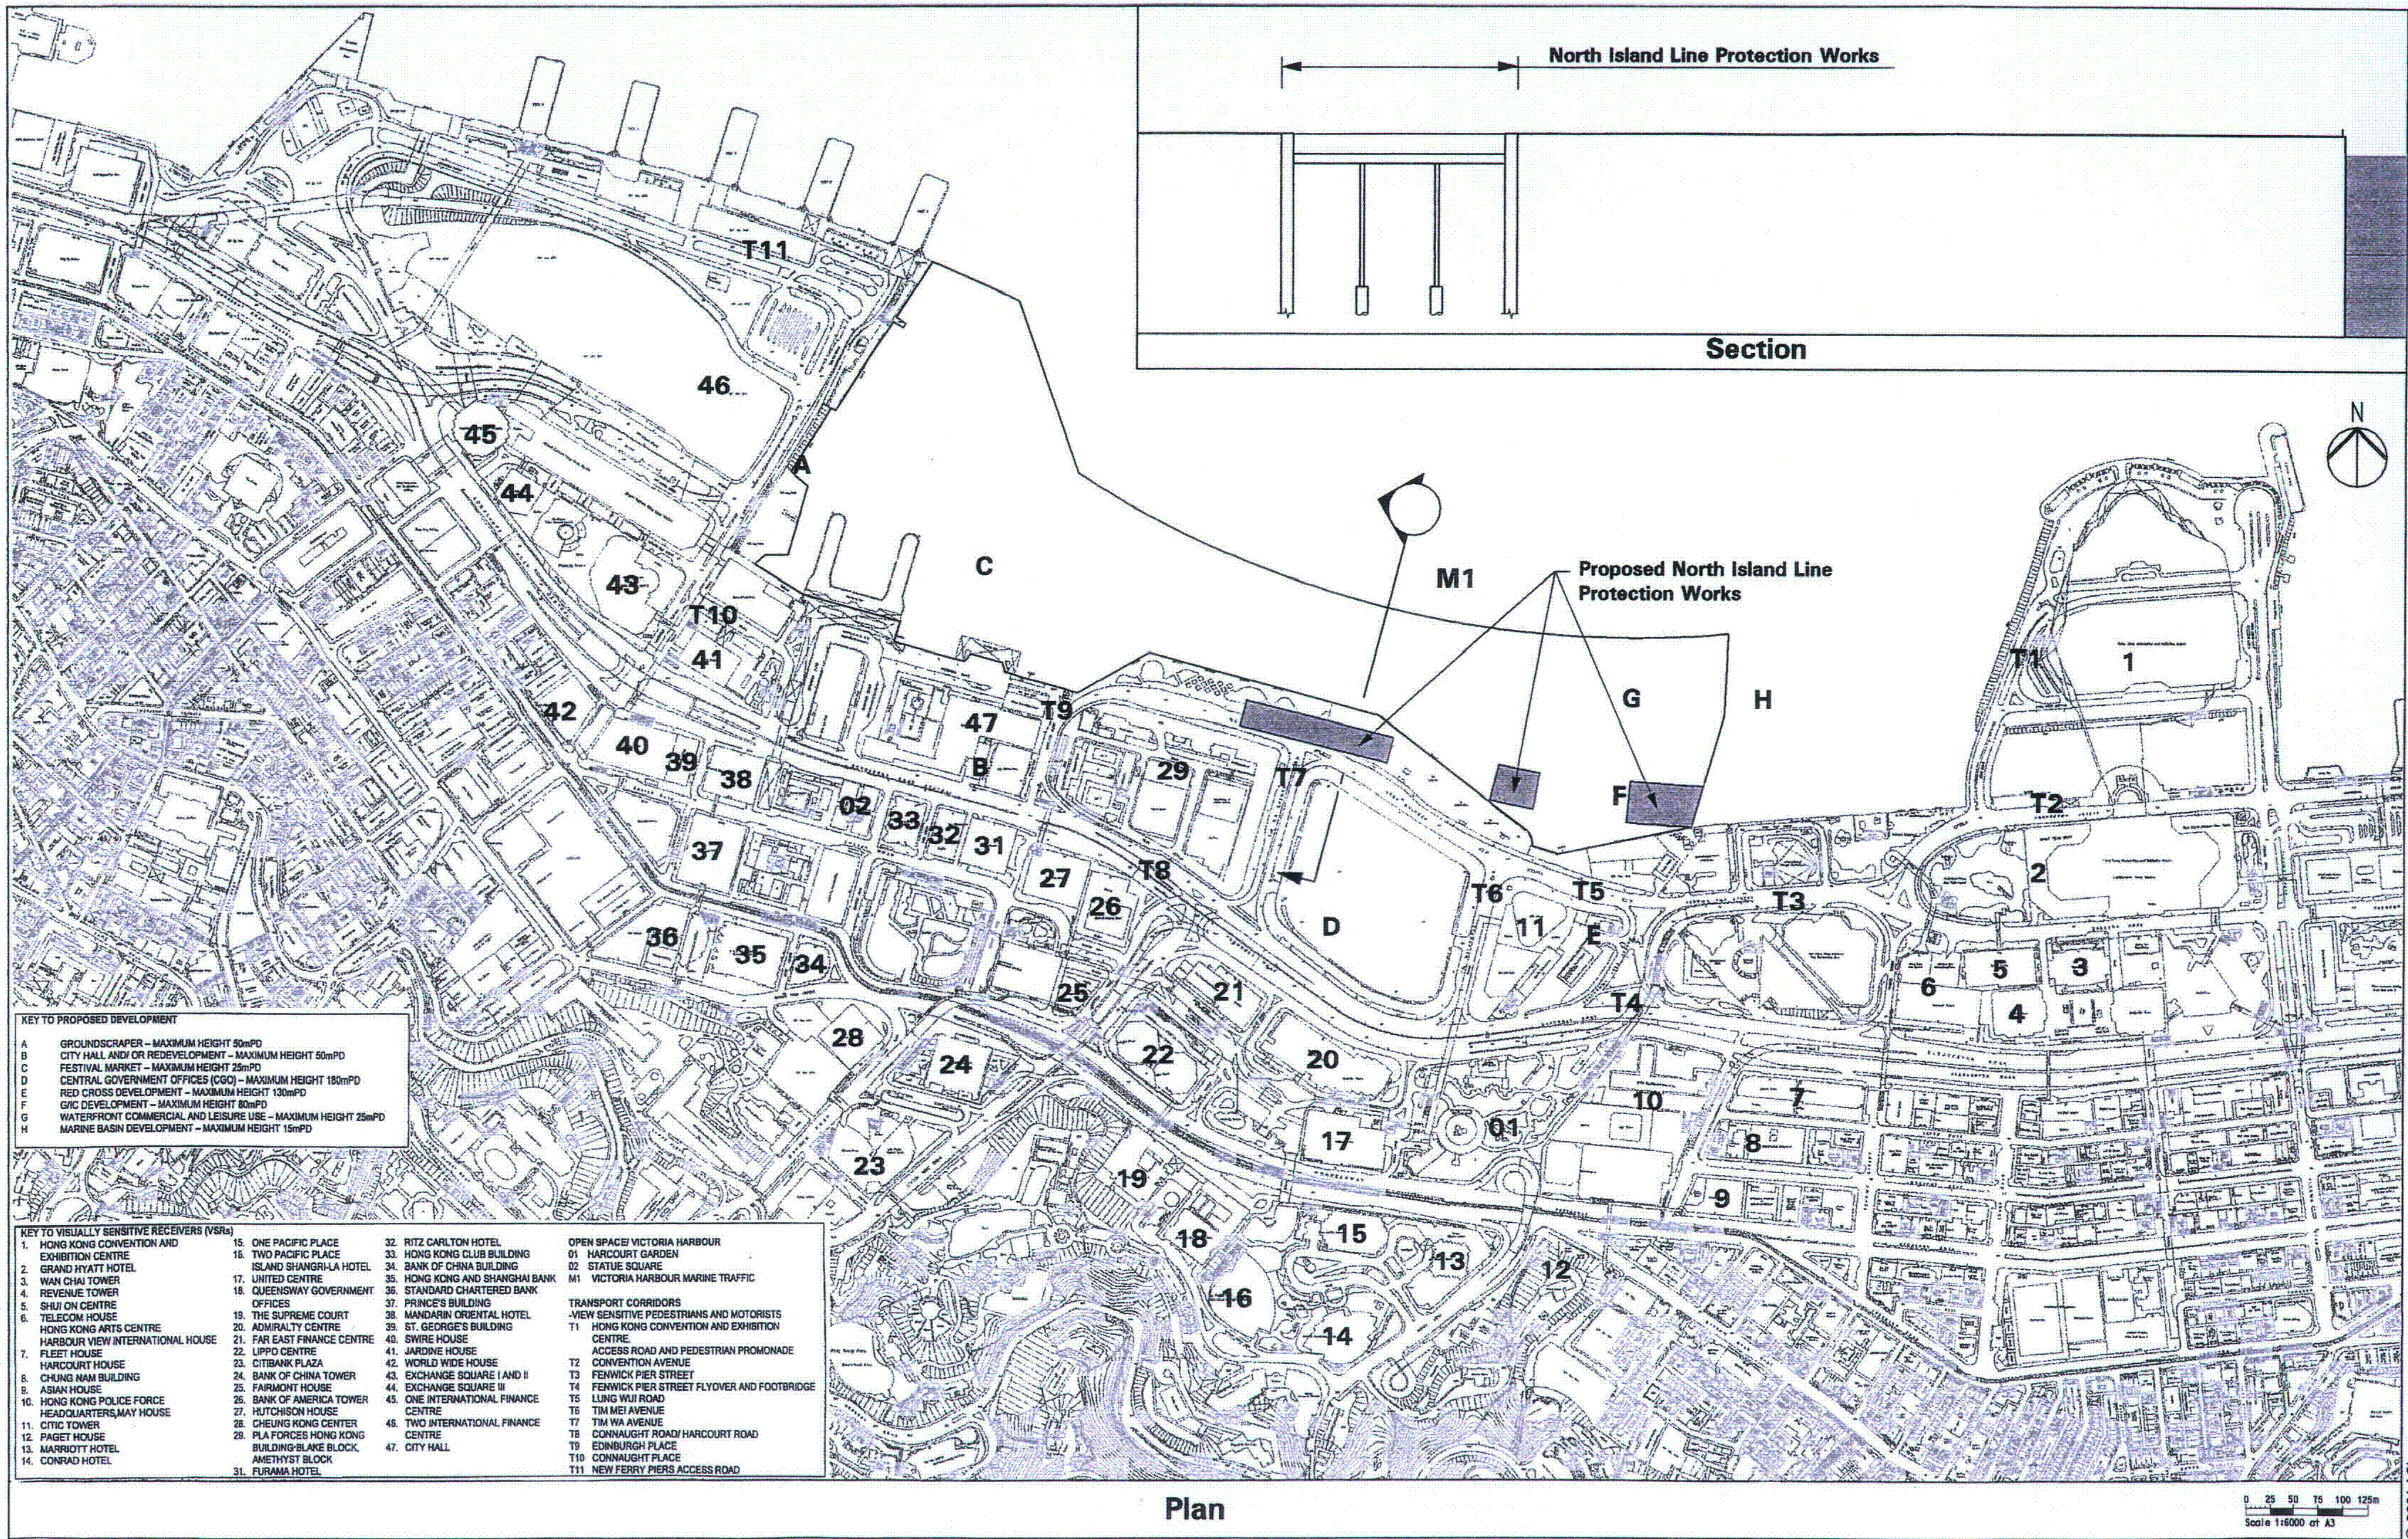

Designated Project 4 - North Island Line Protection Works  
Layout Plan and Section

Figure 14.12





***Figure 2.2***

***Project Organization Chart***





### Project Organization Chart

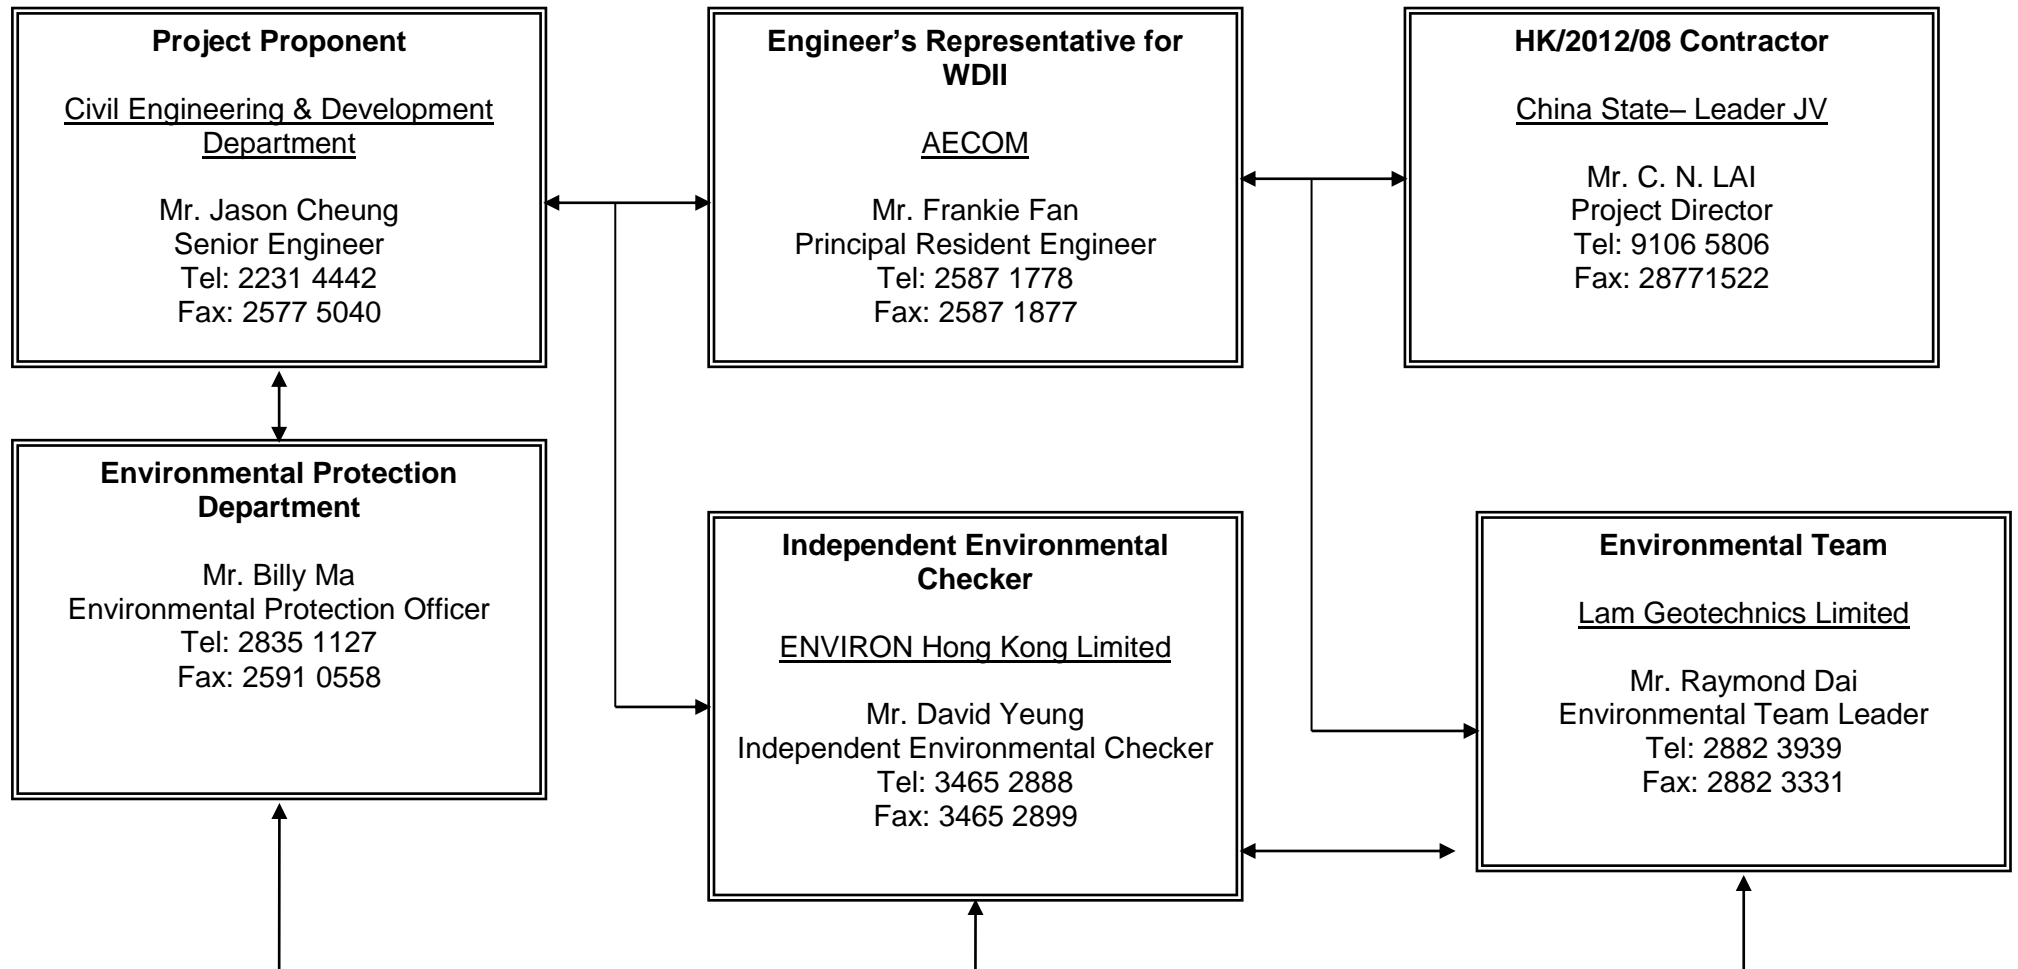


Figure 2.2



***Figure 4.1***


***Locations of Monitoring Stations***



DO NOT SCALE DRAWINGS. VERIFY ALL DIMENSIONS ON SITE

**LEGEND:**

- DUST MONITORING STATIONS
- ▲ NOISE MONITORING STATION

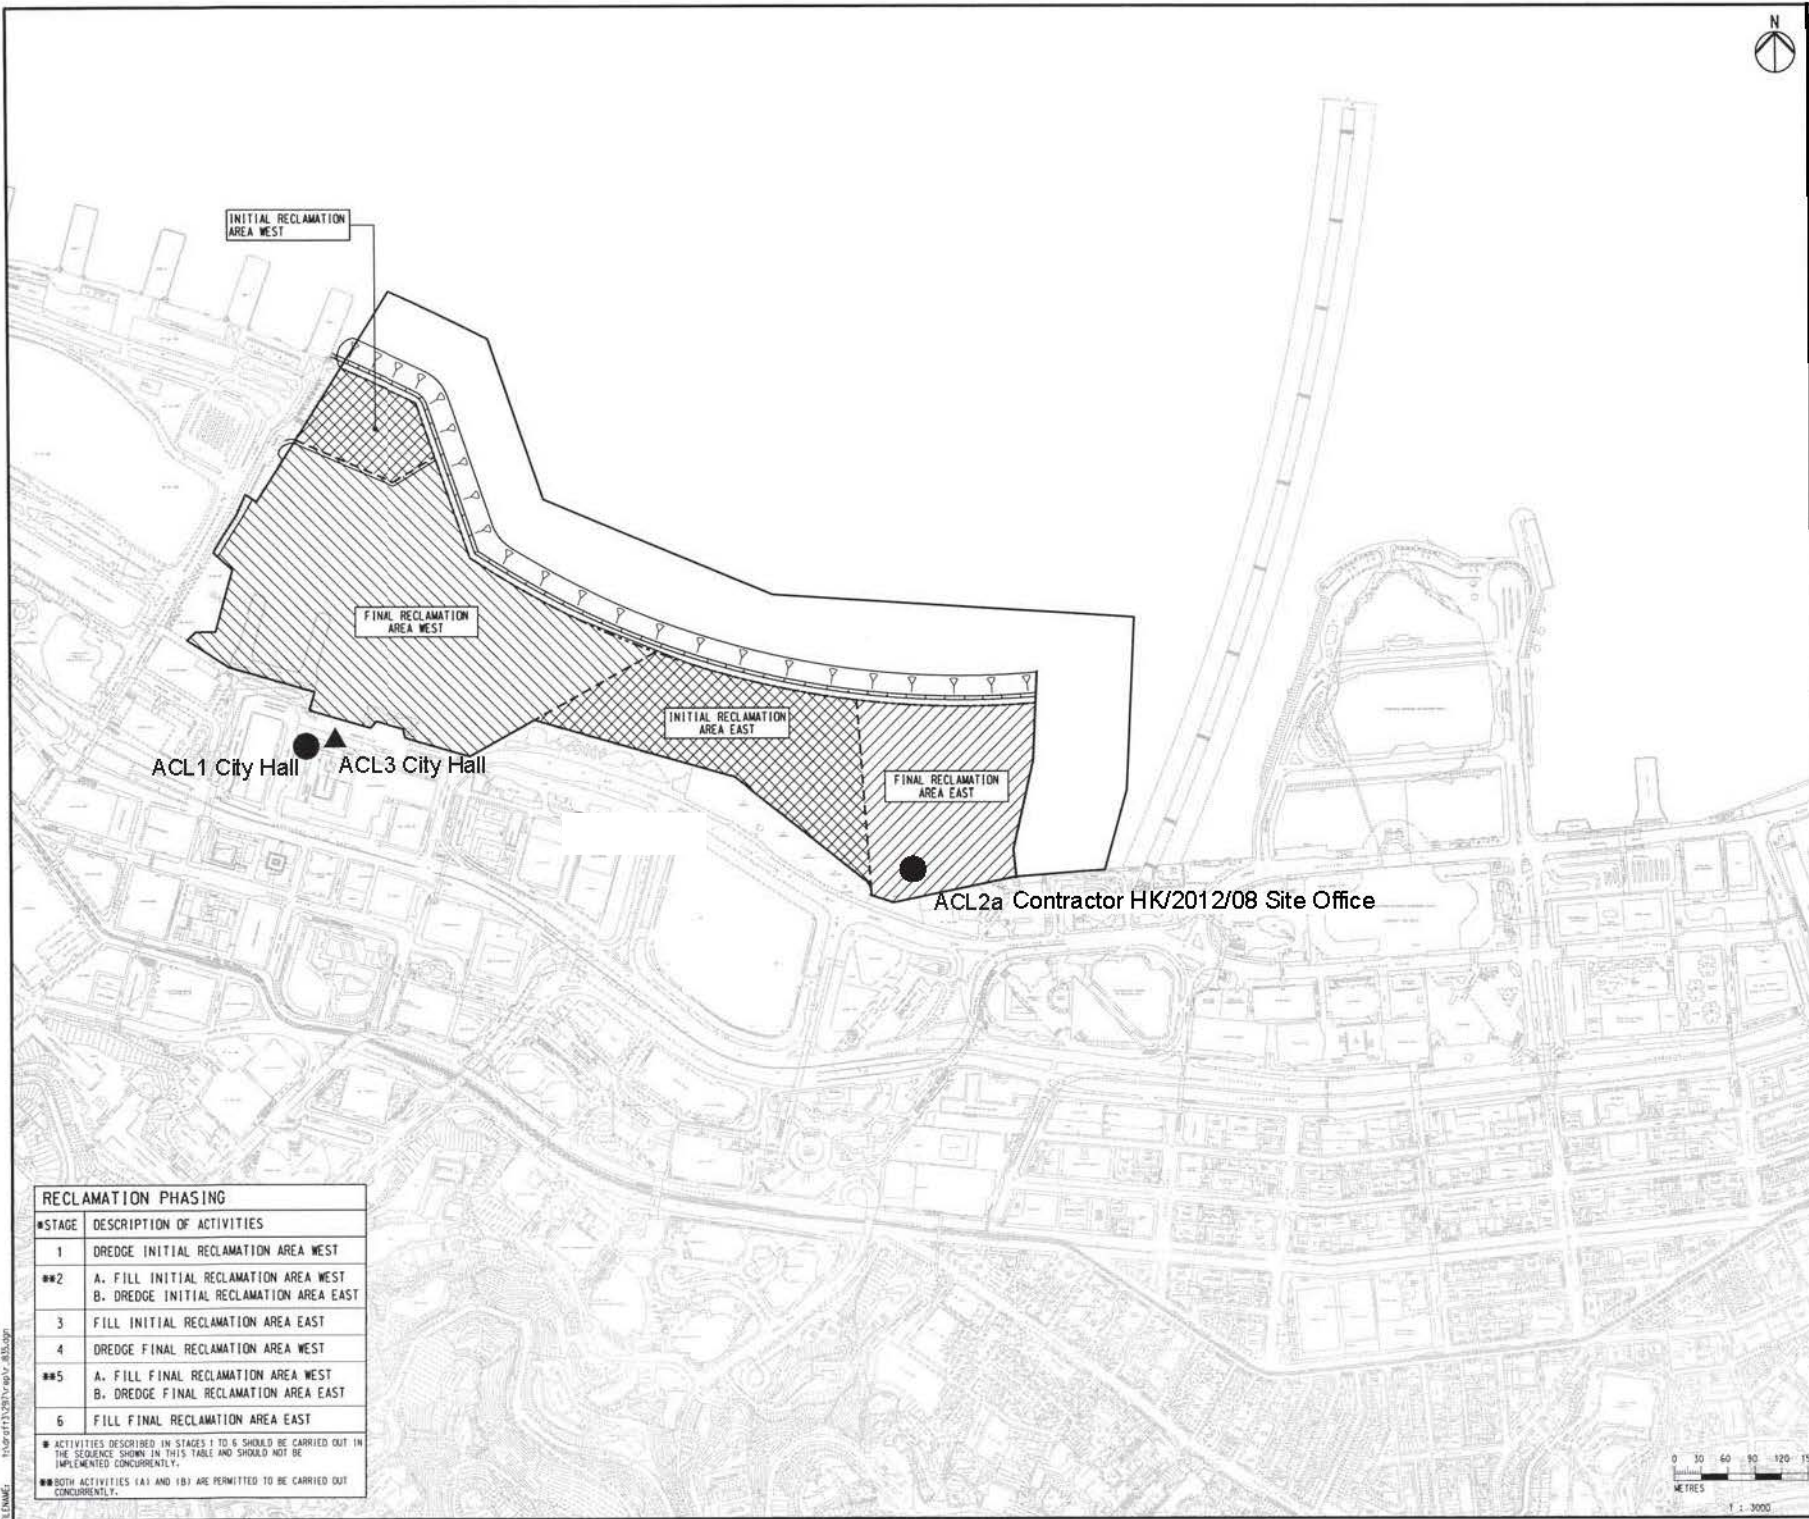

RECLAMATION PHASING	
#STAGE	DESCRIPTION OF ACTIVITIES
1	DREDGE INITIAL RECLAMATION AREA WEST
**2	A. FILL INITIAL RECLAMATION AREA WEST B. DREDGE INITIAL RECLAMATION AREA EAST
3	FILL INITIAL RECLAMATION AREA EAST
4	DREDGE FINAL RECLAMATION AREA WEST
**5	A. FILL FINAL RECLAMATION AREA WEST B. DREDGE FINAL RECLAMATION AREA EAST
6	FILL FINAL RECLAMATION AREA EAST



● ACTIVITIES DESCRIBED IN STAGES 1 TO 6 SHOULD BE CARRIED OUT IN THE SEQUENCE SHOWN IN THIS TABLE AND SHOULD NOT BE IMPLEMENTED CONCURRENTLY.  
 ● BOTH ACTIVITIES (A) AND (B) ARE PERMITTED TO BE CARRIED OUT CONCURRENTLY.



Fig 4.1 Location of monitoring stations

PRINTED BY: [illegible] # APR 03 14:27:13 2013



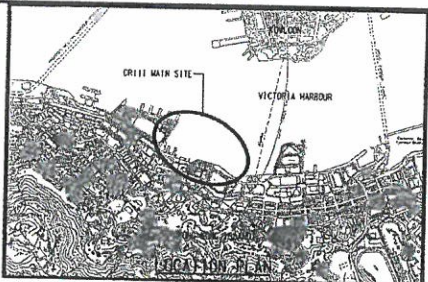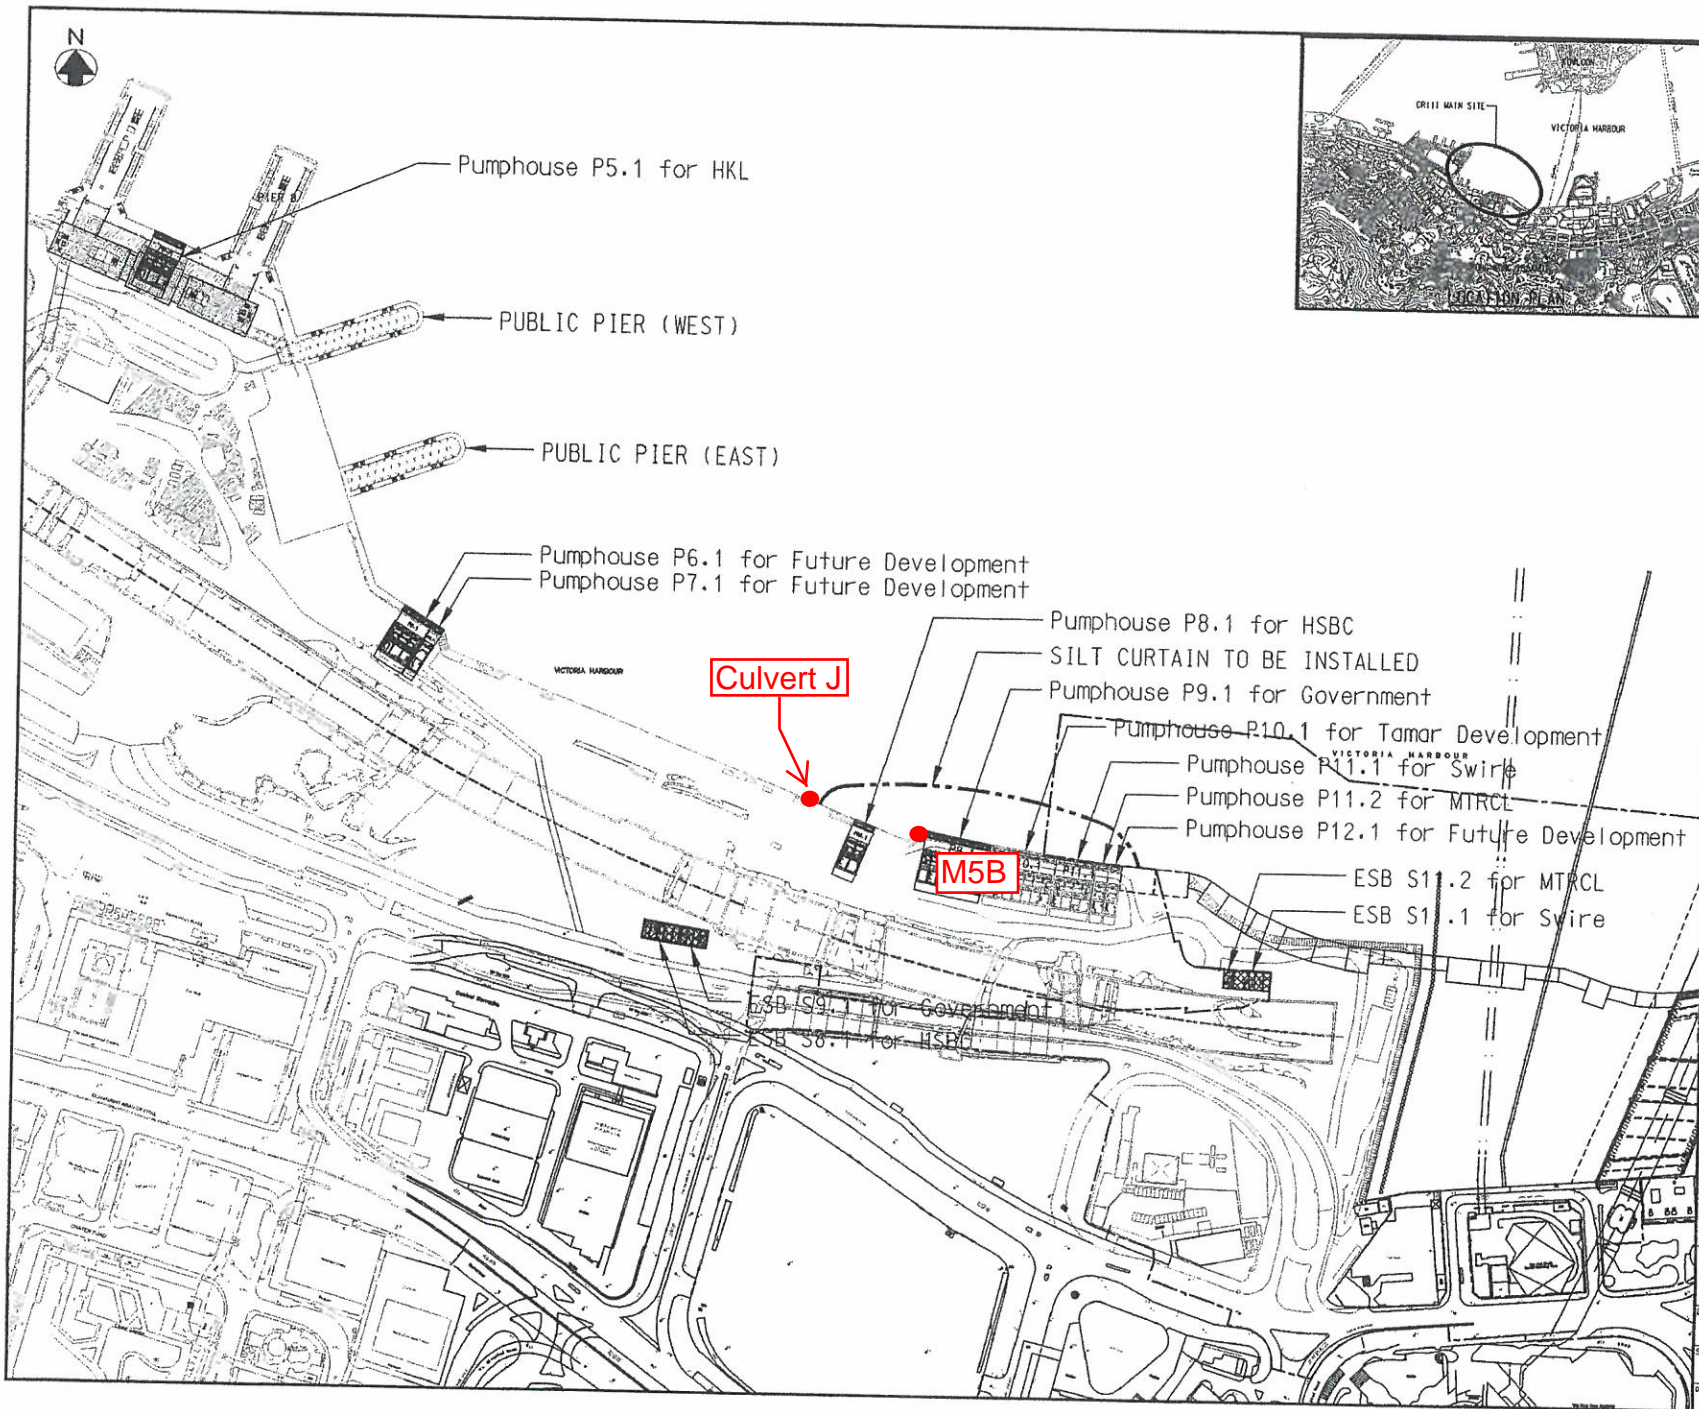

NOTES :  
1. ALL DIMENSIONS ARE IN METRES UNLESS OTHERWISE SPECIFIED.

LEGENDS :  
- - - - - SILT CURTAIN

CONTRACT NO. HK/2012/08  
WAN CHAI DEVELOPMENT PHASE II -  
CENTRAL - WAN CHAI BYPASS AT  
WAN CHAI WEST

TITLE  
PUMP HOUSES AND ESBs  
LOCATION PLAN WITH INSTALLED  
SILT CURTAIN

中環建策 - 利達聯泰  
CHINA STATE - LEADER JOINT VENTURE

DRG. NO.  
HK\_2012\_08/CDB/S/SK/071

SCALE  
A3 1:3000  
DATE OF BRINGING INTO  
8-AUG-2013

DRAWING ARE IN METRES  
COPYRIGHT RESERVED



***Appendix 3.1***

***Environmental Mitigation Implementation Schedule***



### IMPLEMENTATION SCHEDULE OF THE PROPOSED MITIGATION MEASURES

No.	Activity	Mitigation/EIA Recommendations	Responsibility for Implementation	Location Duration completion of measures	Implementation Stage C : Construction D : Design	Permit Conditions apply to	Relevant Guidelines Legislation
1	Operational Traffic Noise*	The openings of ventilation buildings or ventilation shafts should be placed carefully and ideally should be such that they are not facing directly onto any NSR.	Various	Area Wide, Proposals at design stage for Implementation during construction	D/C	N/A	--
2	Operational Air Quality	Air intakes for commercial/G/IC buildings should be placed such that they are at locations where contours indicate AQOs are met.	ArchSD/Private sector +	CRIII During development of sites Completion of CRIII	Development of CRIII	Carry forward to design stage	6
3	Operational Water Quality	Provision of grit traps for surface drainage	TDD's Contractor	New roads and paved areas During construction End of construction	C	P, R, A, C	7
4	Operational Landscape and Visual	Operational stage landscape and visual mitigation measures should include +  <ul style="list-style-type: none"> <li>· Implementation of the Waterfront Promenade, Statue Square Corridor, Historic Corridor, Civic Corridor, Arts and Entertainment Corridor, Streetscape Network, Landscape Decks, and Supplementary Landscape Spaces;</li> <li>· provision of a legible, integrated pedestrian circulation system linking major activity nodes, reinforcing links with adjoining areas, and providing an international quality hard and soft landscape treatment;</li> <li>· provision of a grade separated pedestrian system to minimise vehicular/ pedestrian conflict;</li> <li>· provision of an integrated network of local and regional open spaces for passive and active recreation;</li> <li>· preservation of selected architectural features;</li> <li>· preservation insitu of existing significant vegetation, principally the two Banyan Trees flanking the Tamar Site;</li> <li>· new roads to incorporate suitable streetscape amenity and landscape planting to minimise visual and environmental impacts;</li> </ul>	Various	Area wide, proposals at design stage for implementation during construction	D/C	P	--



No.	Activity	Mitigation/EIA Recommendations	Responsibility for Implementation	Location Duration completion of measures	Implementation Stage C : Construction D : Design	Permit Conditions apply to	Relevant Guidelines Legislation
		<ul style="list-style-type: none"> <li>existing roads upgraded to 'marry' with the proposed landscape framework;</li> <li>Hydroseeding of reclamation if there is no immediate use of the site, periphery of the reclamation;</li> <li>Designated service corridors beneath footpaths to prevent potential impacts upon vegetation during services maintenance;</li> <li>Sensitively designed colour themes to footpath paving areas; and</li> <li>Sensitively designed seawall to enhance the recreational value of the future promenade can be included.</li> </ul>	Various	Area wide, proposals at design stage for implementation during construction	D/C	P	--
5	Construction Noise Control Requirements	Use of the following quiet mechanical equipment for construction works : <ul style="list-style-type: none"> <li>air compressor; paver; hand held breaker; breaker, excavator mounted; bulldozer; concrete lorry mixer; concrete pump; crane; dump truck; excavator/ loader; grader; lorry ; poker; road roller; vibratory roller;</li> </ul>	TDD's Contractor	Works Area During construction End of construction	C	P, R, A, C	-
		Use of noise barriers (in the form if purpose built site hoarding of 3 - 5 m height and surface density of at least 7 kgm <sup>2</sup> with cranked top) for the following works: <ul style="list-style-type: none"> <li>Hong Kong Station Extended Overrun Tunnels to north of Central Barracks.</li> <li>North Island Line Protection Works to north of Central Barracks;</li> <li>Road/Drainage Works to north of Central Barracks;</li> <li>Culvert F Piling Works to north of City Hall.</li> </ul>	TDD's Contractor	Work Sites as stated Start of activity stated End of activity stated	C	P, A	
		Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme.	TDD's Contractor	Works Area During construction End of construction	C	P,R,A,C	4
		Silencers or mufflers on construction equipment should be utilised and should be properly maintained during the construction programme.	TDD's Contractor	Works Area During construction End of construction	C	P,R,A,C	4
		Mobile plant, if any, should be sited as far away from noise sensitive facilities as possible.	TDD's Contractor	Works Area During construction End of construction	C	P,R,A,C	4



No.	Activity	Mitigation/EIA Recommendations	Responsibility for Implementation	Location Duration completion of measures	Implementation Stage C : Construction D : Design	Permit Conditions apply to	Relevant Guidelines Legislation
		<ul style="list-style-type: none"> <li>Machines and plant (such as trucks) that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum.</li> <li>Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from nearby noise sensitive facilities.</li> </ul>	TDD's Contractor	Works Area During construction End of construction	C	P,R,A,C	4
		<ul style="list-style-type: none"> <li>Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from nearby noise sensitive facilities.</li> </ul>	TDD's Contractor	Works Area During construction End of construction	C	P,R,A,C	4
6	Construction Air Quality Control Requirements	<ul style="list-style-type: none"> <li>Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities.</li> </ul>	TDD's Contractor	Works Area During construction End of construction	C	P,R,A,C	4
		<ul style="list-style-type: none"> <li>Strictly limit truck speed on site to below 10 km per hour and water spraying to keep the haul roads in wet condition.</li> </ul>	TDD's Contractor	Works Area During construction End of construction	C	P,R,A,C	6,7
		<ul style="list-style-type: none"> <li>Twice daily watering of the site with active operations when the weather and the work site are dry.</li> </ul>	TDD's Contractor	Works Area During construction End of construction	C	P,R,A,C	6,7
		<ul style="list-style-type: none"> <li>Watering during excavation and material handling.</li> </ul>	TDD's Contractor	Works Area During construction End of construction	C	P,R,A,C	6,7
		<ul style="list-style-type: none"> <li>Provision of vehicle wheel and body washing facilities at the exit points of the site, combined with cleaning of public roads where necessary.</li> </ul>	TDD's Contractor	Works Area During construction End of construction	C	P,R,A,C	6,7
		<ul style="list-style-type: none"> <li>Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations.</li> </ul>	TDD's Contractor	Works Area During construction End of construction	C	P,R,A,C	6,7
		<ul style="list-style-type: none"> <li>Covers for dusty stockpiles</li> </ul>	TDD's Contractor	Works Area During construction End of construction	C	P,R,A,C	6
		<ul style="list-style-type: none"> <li>All plant shall be maintained to prevent any undue air emissions</li> </ul>	TDD's Contractor	Works Area	C	P,R,A,C	6





No.	Activity	Mitigation/EIA Recommendations	Responsibility for Implementation	Location Duration completion of measures	Implementation Stage C : Construction D : Design	Permit Conditions apply to	Relevant Guidelines Legislation
				During construction End of construction			
7	Construction Water Quality Control Requirements	<p>Specific Measures Associated with Dredging Works</p> <ul style="list-style-type: none"> <li>· the use of closed clamshell (water-tight) grab dredgers to remove seriously contaminated material such that the amount of SS and other pollutants released from the marine mud and pore water can be minimised;</li> <li>· the prohibition of stockpiling of any moderately or seriously contaminated marine sediment, and careful control of stockpiling of any uncontaminated sediment to prevent runoff, resuspension and odour nuisances; and</li> <li>· the control of dredging and bulk reclamation filling rates within acceptable limits. Based upon the construction sequence developed for this study the maximum dredging and filling rates adopted for Final Reclamation Area East were : Maximum Dredging Rate : 184 m<sup>2</sup>/hour Maximum Daily Filling Rate : 17,727 m<sup>3</sup>/day (for bulk reclamation filling)</li> </ul> <p>Maximum dredging and filling rates for other reclamation sites should take account of information contained in Table 10.14 of the EIA Report and envisaged construction sequence.</p> <ul style="list-style-type: none"> <li>· no dredging should take place under very bad weather conditions.</li> </ul>	TDD's Contractor	Whole reclamation area During reclamation works End of reclamation works	C	R	7
		<ul style="list-style-type: none"> <li>· silt curtain around dredging sites to be provided as necessary.</li> </ul> <p>Specific Measure for Marine Disposal of Dredged Materials and Marine Sand Filling Works</p> <ul style="list-style-type: none"> <li>· all vessels should be sized such that adequate clearance is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash;</li> <li>· all hopper barges and dredgers should be fitted with tight fitting seals to their bottom openings to prevent leakage of material;</li> <li>· loading of hopper barges should be controlled to prevent splashing of dredged or filling material to the surrounding water, and barges or hoppers should not be filled to a level which will cause the overflow of materials or polluted water during loading or</li> </ul>	TDD's Contractor	Whole reclamation area During reclamation works End of reclamation works	C	R	7



No.	Activity	Mitigation/EIA Recommendations	Responsibility for Implementation	Location Duration completion of measures	Implementation Stage C : Construction D : Design	Permit Conditions apply to	Relevant Guidelines Legislation
		transportation;					
		<ul style="list-style-type: none"> <li>· the works should cause no visible foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site or dumping grounds;</li> <li>· bulk filling should be carried out, where feasible, behind completed seawall to above high water mark. In general and where physically practical, filling should not be carried out without the seawall having been substantially completed for a distance of 100m – 200m ahead of filling; and</li> <li>· fill materials should comply with technical specification requirements and be taken from approved sources only. The maximum fines content of marine sand should be limited to 5% as assumed in the water quality assessments.</li> <li>· transport of contaminated mud (or filling material) to the marine disposal site (or works site) should, wherever possible, be by split barge of not less than 750 m<sup>3</sup> capacity, well maintained and capable of rapid opening and discharge at the disposal site;</li> <li>· the dredged material should be disposed in the pit by bottom dumping, at a location within the pit specified by the MFC;</li> <li>· discharge should be undertaken rapidly and the hoppers should then immediately be closed. Material adhering to the sides of the hopper should not be washed out of the hopper and the hopper should remain closed until the barge next return to the disposal site;</li> <li>· the dumping vessel is not required to station but will be guided by the site staff managing the disposal facility. The vessel crew should be familiar with such operational procedures;</li> <li>· monitoring of the barge loading to ensure that loss of material does not take place during transportation; and</li> <li>· Transport barges or vessels shall be equipped with automatic self-monitoring devices.</li> </ul>	TDD's Contractor	Whole reclamation area During reclamation works End of reclamation works	C	R	7



No.	Activity	Mitigation/EIA Recommendations	Responsibility for Implementation	Location Duration completion of measures	Implementation Stage C : Construction D : Design	Permit Conditions apply to	Relevant Guidelines Legislation
		<p>Specific Measures Associated with Dredging and Filling Works when CRIII Dredging and Filling Works are being constructed concurrently with WDII Dredging and Filling Works</p> <ul style="list-style-type: none"> <li>· deployment of silt curtains around the dredging and fill release points to contain SS within the construction site during dredging and filling;</li> <li>· deployment of silt screens at the cooling water intakes and WSD salt water intakes to further minimise the intake of SS within the sea water.</li> </ul>	TDD's Contractor	<p>Reclamation Areas as appropriate</p> <p>When CRIII and WDII - Dredging and Filling Works occur concurrently</p> <p>End of Concurrent Works</p>	C	R	-
		<p>Specific Measures Associated with Floating Debris</p> <p>The result of the floating debris simulation has shown that the intermediate layout of the proposed reclamation has potential to trap floating rubbish. Monitoring and control of the construction activities should be taken to prevent the release of construction waste and rubbish from the construction site. Collection of floating debris should be carried out at least once every day by the CRIII Contractor, and more frequently (two or three times per day) at the water body south of the Initial Reclamation Area West and near the cooling water intakes where large substances could block the screens and filter pipes of the intakes and reduce their efficiency. Debris should be collected and taken to landfill sites for disposal.</p>	TDD's Contractor	<p>Whole reclamation area</p> <p>During construction</p> <p>At end of construction</p>	C	R	-
		<p>Specific Measures for Dealing with Culvert L Outfall at Completion of CRIII Eastern Seawall</p> <p>As a mitigation measure, to avoid the accumulation of water borne pollutants within a temporary embayment to the east of CRIII, an impermeable barrier, suspended from a floating boom on the water surface and extending down to the seabed, will be erected by the CRIII Contractor on completion of the CRIII eastern seawall. The barrier will channel the stormwater discharge flows from Culvert L to the outside of the embayment. The CRIII Contractor will maintain this barrier until the WDII Contractor takes possession of this site, whereupon the WDII Contractor will takeover the maintenance of this barrier until the reclamation works in this area are carried out and the new Culvert L extension is constructed.</p>	TDD's Consultant	<p>Culvert L Outfall</p> <p>During Construction</p> <p>To handover to WDII Contractor</p>	C	R	--



No.	Activity	Mitigation/EIA Recommendations	Responsibility for Implementation	Location Duration completion of measures	Implementation Stage C : Construction D : Design	Permit Conditions apply to	Relevant Guidelines Legislation
		<p>Construction Run-off and Drainage</p> <ul style="list-style-type: none"> <li>- Control of Site Surface Runoff:</li> <li>- Surface run-off from construction sites should be discharged into storm drains via adequately designed sand/silt removal facilities such as sand traps, silt traps and sediment basins. Channels or earth bunds or sand bag barriers should be provided on site to properly direct stormwater to such silt removal facilities. Perimeter channels at site boundaries should be provided where necessary. Catchpits and perimeter channels should be constructed in advance of site formation works and earthworks.</li> <li>- Silt removal facilities, channels and manholes should be maintained.</li> <li>- Construction works should be programmed to minimise soil excavation works in rainy seasons (April to September). If excavation in soil cannot be avoided, temporarily exposed slope surfaces should be covered and temporary access roads should be protected by crushed stone or gravel, as excavation proceeds. Intercepting channels should be provided.</li> <li>- Earthworks final surfaces should be well compacted and the subsequent permanent work or surface protection should be carried out immediately after the final surfaces are formed to prevent erosion caused by rainstorms. Appropriate drainage such as intercepting channels should be provided where necessary.</li> <li>- Measures should be taken to minimise the ingress of rainwater into trenches. If excavation of trenches in wet seasons is necessary, they should be dug and backfilled in short sections. Rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities.</li> <li>- Open stockpiles of construction materials should be covered.</li> <li>- Manholes should be adequately covered and temporarily sealed.</li> </ul>	TDD's Contractor	<p>Works Area</p> <p>During construction</p> <p>End of construction</p>	C	P,R,A,C	7
		<ul style="list-style-type: none"> <li>- Groundwater</li> <li>- Groundwater pumped out of tunnels or caverns should be discharged into storm drains after the removal of silt.</li> </ul>					



No.	Activity	Mitigation/EIA Recommendations	Responsibility for Implementation	Location Duration completion of measures	Implementation Stage C : Construction D : Design	Permit Conditions apply to	Relevant Guidelines Legislation
		<ul style="list-style-type: none"> <li>· Boring and Drilling Water</li> <li>- Water used in ground boring and drilling for site investigation or rock/soil anchoring should as far as practicable be recirculated after sedimentation. Wastewater should be discharged into storm drains via silt removal facilities.</li> <li>· Wastewater from Concrete Batching and Precast Concrete Casting</li> <li>- Wastewater generated from the washing down of mixer trucks and drum mixers and similar equipment should wherever practicable be recycled. The discharge of wastewater should be kept to a minimum.</li> <li>- To prevent pollution from wastewater overflow, the pump sump of any water recycling system should be provided with an on-line standby pump of adequate capacity and with automatic alternating devices.</li> <li>- Under normal circumstances, surplus wastewater may be discharged into foul sewers after treatment in silt removal and pH adjustment facilities (to within the pH range of 6 to 10). Disposal of wastewater into storm drains will require more elaborate treatment.</li> </ul> <p>Surface run-off should be segregated from the concrete mixing and casting yard area as much as possible, and diverted to the stormwater drainage system. Surface run-off contaminated by materials in a concrete mixing area or casting yard should be adequately treated before disposal into stormwater drains.</p>	TDD's Contractor	<p>Work Area</p> <p>During construction</p> <p>End of construction</p>	C	P,R,A,C	7
		<ul style="list-style-type: none"> <li>· Wheel Washing Water</li> <li>- All vehicles and plant should be cleaned before they leave the construction site. A wheel washing bay should be provided at every site exit if practicable and wash-water should have sand and silt settled out or removed before discharging into storm drains. The section of construction road between the wheel washing bay and the public road should be paved with backfall to reduce vehicle tracking of soil and to prevent site run-off from entering public road drains.</li> <li>· Bentonite Slurries</li> <li>- Bentonite slurries should be reconditioned and reused wherever practicable. If the disposal of a certain residual quantity cannot be avoided, the used slurry may be disposed of at the marine spoil site subject to obtaining a marine dumping licence from EPD (on a case-by-case basis).</li> </ul>	TDD's Contractor	<p>Work Area</p> <p>During construction</p> <p>End of construction</p>	C	P,R,A,C	7



No.	Activity	Mitigation/EIA Recommendations	Responsibility for Implementation	Location Duration completion of measures	Implementation Stage C : Construction D : Design	Permit Conditions apply to	Relevant Guidelines Legislation
		<ul style="list-style-type: none"> <li>- If the used bentonite slurry is intended to be disposed of through the public drainage system, it should be treated to the respective effluent standards applicable to foul sewers, storm drains or the receiving waters as set out in the WPCO Technical Memorandum on Effluent Standards.</li> </ul>					
		<ul style="list-style-type: none"> <li>- Wastewater from Building Construction</li> <li>- Before commencing any demolition works, all sewer and drainage connections should be sealed to prevent building debris, soil, sand etc. from entering public sewers/drains.</li> <li>- Wastewater generated from building construction activities including concreting, plastering, internal decoration, cleaning of works and similar activities should not be discharged into the stormwater drainage system. If the wastewater is to be discharged into foul sewers, it should undergo the removal of settleable solids in a silt removal facility, and pH adjustment as necessary.</li> </ul>					
		<ul style="list-style-type: none"> <li>-Licensing of Construction Site Discharges within Water Control Zones</li> <li>-All discharges into any drainage or sewerage systems, or inland or coastal waters, or into the ground (e.g. from septic tanks) within a Water Control Zone are controlled under the Water Pollution control Ordinance (WPCO), except the discharge of domestic sewage into foul sewers or the discharge of unpolluted water into storm drains or into the waters of Hong Kong. Construction site discharges are controlled under the WPCO.</li> <li>-Discharges controlled under the WPCO must comply with the terms and conditions of a valid WPCO licence.</li> </ul>					



No.	Activity	Mitigation/EIA Recommendations	Responsibility for Implementation	Location Duration completion of measures	Implementation Stage C : Construction D : Design	Permit Conditions apply to	Relevant Guidelines Legislation
8.	Construction Waste Control Requirements	<p>Specific Measures Associated with Marine sediments</p> <p>In accordance with the WBTC No. 3/2000, the seriously contaminated material must be dredged and transported with great care. Mitigation measures, including the use of close-grab dredgers, shall be incorporated.</p> <p>The dredged contaminated sediment must be effectively isolated from the environment upon final disposal and shall be disposed of at the East Sha Chau Contaminated Mud Pits.</p>	TDD's Contractor	Whole Reclamation Area During Reclamation Works End of Reclamation Work	C	R	7
		<p>Segregation and Disposal of Wastes</p> <ul style="list-style-type: none"> <li>· inert demolition/construction waste material when deemed suitable for reclamation or land formation should be re-used on-site;</li> <li>· non-inert demolition / construction waste material should be disposed of at landfills;</li> <li>· chemical waste as defined by Schedule 1 of the Waste Disposal (Chemical Waste) (General) Regulation, should be stored in accordance with approved methods defined in the Regulation and Code of Practice and the chemical waste disposed of at the Chemical Waste Treatment Facility located at Tsing Yi or an approved recycler;</li> <li>· general refuse should be recycled where possible or disposed of at public landfill.</li> </ul>	TDD's Contractor	Works Areas During Construction End of Construction	C	P, R, A, C	1,8, 9
		<p>Storage, Collection and Transport of Waste</p> <ul style="list-style-type: none"> <li>· wastes should be handled and stored in a manner which ensures that they are held securely without loss or leakage thereby minimising the potential for pollution. Release of these potential pollutants into marine waters during storage, handling or barge transportation should not be permitted as introduction of polluted waters is likely to have detrimental effects on water quality and water sensitive receivers;</li> <li>· only reputable waste hauliers authorised to collect the specific category of waste concerned should be employed;</li> <li>· appropriate measures should be employed to minimise windblown litter and dust during transportation by using enclosed bins, covering trucks or transporting wastes in enclosed containers;</li> <li>· the necessary waste disposal permits and registrations should be obtained from the appropriate authorities, if they are required, in accordance with the Waste Disposal</li> </ul>	TDD's Contractor	Works Areas During Construction End of Construction	C	P, R, A, C	1, 8, 9



No.	Activity	Mitigation/EIA Recommendations	Responsibility for Implementation	Location Duration completion of measures	Implementation Stage C : Construction D : Design	Permit Conditions apply to	Relevant Guidelines Legislation
		Ordinance (Cap 354), Waste Disposal (Chemical Waste) (General) Regulation (Cap 354) and the Crown Land Ordinance; <ul style="list-style-type: none"> <li>· collection of general refuse should be carried out frequently, preferably daily;</li> <li>· waste should only be disposed of at licensed sites and the civil engineering contractor should develop procedures to ensure that illegal disposal of wastes does not occur;</li> <li>· waste storage areas should be well maintained and cleaned regularly;</li> <li>· records should be maintained of the quantities of wastes generated, recycled and disposed, determined by weighing each load or other method; and</li> <li>· A "trip ticket" system should be implemented, if required by Government.</li> </ul>					
9	Construction Landscape and Visual Control Requirements	Construction stage landscape and visual mitigation measures should include : <ul style="list-style-type: none"> <li>· Minimising contractors accesses and working areas as far as possible;</li> <li>· Protection and retention of existing vegetation where possible in accordance with the Hong Kong Government "A Guide to Tree Planting and Maintenance in Urban Hong Kong, Section 5" Care of Trees on Development Sites' and the Country Parks Ordinance</li> <li>· Transplanting of trees where appropriate;</li> <li>· Advance planting and visual screening;</li> <li>· Conservation of top soil;</li> <li>· Design of the temporary works areas so as to optimise eventual use as promenade and public open space; and</li> <li>· Sensitively designed site hoarding.</li> </ul>	TDD's design consultant	Area wide during design and contract preparation	D	P, R, A, C	11, 12, 13,14
10	Monitoring and Audit	To be carried out in accordance with the Schedule in the EM and A Manual	TDD*/Contractor/ RSS  TDD's design consultant	Works areas During construction End of construction and within one year of operational phase Area wide during design and contract preparation	C/O  D	P, R, A, C  P, R, A, C	1  11,12,13,14





**Relevant Guidelines Legislation**

1. Environmental Impact Assessment Ordinance Technical Memorandum (EIAO)
2. HKPSG
3. ExCo Criteria for ITR
4. Noise Control Ordinance
5. The ProPECC Note PN2/93 (Construction Noise daytime limits)
6. Air Pollution Control Ordinance (APCO)
7. Water Pollution Control Ordinance (WPCO)(Cap. 358)
8. Waste Disposal Ordinance (Cap 354)
9. Waste Disposal (Chemical Waste)(General) Regulation (Cap 354)
10. Land Ordinance (Cap 28)
11. WBTC 25/92 Allocation of Space for Urban Trees
12. WBTC 25/93 Control of Visual Impact of Slopes
13. WBTC 18/94 Management and Maintenance of both Natural Vegetation and Landscape Works
14. WBTC 24/94 and PELBTC 3/94 "Tree Preservation"
15. Antiquities and Monuments Ordinance (Cap 53)

**Permit Conditions apply to**

- P Primary and District Distributor Roads
- R Reclamation
- A North Island Line Protection Works
- C Central and Wanchai Bypass
- + These items should be excluded from any Environmental Permit conditions as these refer to future development of the area (which is not designated under the EIAO), and are not related to reclamation and dredging activities which are designated, and can hence be controlled through EP conditions.
- \* Normally undertaken by a specialist monitoring team employed directly by the proponent and audited by the Environmental Works Checker.



***Appendix 4.1***

***Action and Limit Level***



**Action and Limit Level**

***Action and Limit Level for Noise Monitoring***

Time Period	Action Level	Limit Level
07:00 - 19:00 hours on normal weekdays	When one documented complaint is received.	70 dB(A)

***Action and Limit Level for Air Monitoring***

Monitoring Locations	1-hour TSP Level in $\mu\text{g}/\text{m}^3$		24-hour TSP Level in $\mu\text{g}/\text{m}^3$	
	Action Level	Limit Level	Action Level	Limit Level
ACL1 - City Hall	460	500	163	260
ACL2a - Contractor HK/2012/08 Site Office	300.1	500	187.3	260

***Action and Limit Level for Water Quality Monitoring***

Parameters	Action Level	Limit Level
<b>M5B – Central Cooling Water Intake Group</b>		
SS in mg/L	12.00	17.00
DO in mg/L	4.60	3.00



***Appendix 4.2***

***Copies of Calibration Certificates***



TISCH ENVIRONMENTAL, INC.  
 145 SOUTH MIAMI AVE  
 VILLAGE OF CLEVELAND, OH  
 45002  
 513.467.9000  
 877.263.7610 TOLL FREE  
 513.467.9009 FAX

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Jul 14, 2014 Roots-meter S/N 0438320 Ta (K) - 298  
 Operator Tisch Orifice I.D. - 0005 Pa (mm) - 749.3

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER DIFF Hg (mm)	ORFICE DIFF H2O (in.)
1	NA	NA	1.00	1.3870	3.2	2.00
2	NA	NA	1.00	0.9830	6.4	4.00
3	NA	NA	1.00	0.8760	7.9	5.00
4	NA	NA	1.00	0.8340	8.8	5.50
5	NA	NA	1.00	0.6860	12.7	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
0.9817	0.7078	1.4042	0.9957	0.7179	0.8919
0.9775	0.9944	1.9859	0.9915	1.0086	1.2613
0.9754	1.1135	2.2203	0.9894	1.1294	1.4101
0.9743	1.1683	2.3286	0.9882	1.1849	1.4790
0.9692	1.4128	2.8084	0.9830	1.4330	1.7837
Qstd slope (m) = 1.99175			Qa slope (m) = 1.24720		
intercept (b) = -0.00041			intercept (b) = -0.00026		
coefficient (r) = 0.99991			coefficient (r) = 0.99991		
y axis = SQRT[H2O(Pa/760) (298/Ta)]			y axis = SQRT[H2O(Ta/Pa)]		

CALCULATIONS

Vstd = Diff. Vol [(Pa-Diff. Hg)/760] (298/Ta)  
 Qstd = Vstd/Time

Va = Diff Vol [(Pa-Diff Hg)/Pa]  
 Qa = Va/Time

For subsequent flow rate calculations:

Qstd = 1/m{ [SQRT(H2O(Pa/760) (298/Ta))] - b}  
 Qa = 1/m{ [SQRT H2O(Ta/Pa)] - b}



Lam Geotechnics Limited

**Calibration Data for High Volume Sampler (TSP Sampler)**

Location : ACL1  
 Equipment no. : EL380

Calibration Date : 5-Dec-14  
 Calibration Due Date : 5-Feb-15

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition			
Temperature, T <sub>a</sub>	293	Kelvin	Pressure, P <sub>a</sub>
			1020 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m <sub>c</sub>	1.99175	Intercept, b <sub>c</sub>	-0.00041
Last Calibration Date	14-Jul-14	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	14-Jul-15				

Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC (W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31) Y-axis
	(up)	(down)	(difference)			
1	6.5	6.5	13.0	1.8319	59	59.6977
2	5.3	5.3	10.6	1.6542	54	54.6385
3	4.1	4.1	8.2	1.4549	48	48.5676
4	2.5	2.5	5.0	1.1361	38	38.4493
5	1.6	1.6	3.2	0.9090	31	31.3666

By Linear Regression of Y on X

Slope, m = 30.8730      Intercept, b = 3.4080  
 Correlation Coefficient\* = 0.9998  
 Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient &lt; 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_  
 \_\_\_\_\_

Calibrated by : Henry Lau  
 Date : 5-Dec-14

Checked by : Derek Lo  
 Date : 5-Dec-14



Lam Geotechnics Limited

**Calibration Data for High Volume Sampler (TSP Sampler)**

Location : ACL1  
 Equipment no. : EL380

Calbration Date : 04-Feb-15  
 Calbration Due Date : 04-Apr-15

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition			
Temperature, T <sub>a</sub>	289	Kelvin	Pressure, P <sub>a</sub>
			1024 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m <sub>c</sub>	1.99175	Intercept, b <sub>c</sub>	-0.00041
Last Calibration Date	14-Jul-14	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	14-Jul-15				

Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC (W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31) Y-axis
	(up)	(down)	(difference)			
1	5.6	5.6	11.2	1.7154	59	60.2271
2	4.5	4.5	9.0	1.5377	55	56.1439
3	3.5	3.5	7.0	1.3562	49	50.0191
4	2.2	2.2	4.4	1.0753	42	42.8736
5	1.8	1.8	3.6	0.9726	36	36.7488

By Linear Regression of Y on X

Slope, m = 30.5870      Intercept, b = 8.4775  
 Correlation Coefficient\* = 0.9926  
 Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient &lt; 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

Calibrated by : LuLu Mar  
 Date : 04-Feb-15

Checked by : Derek Lo  
 Date : 04-Feb-15



Lam Geotechnics Limited

### Calibration Data for High Volume Sampler (TSP Sampler)

Location : ACL2a Calibration Date : 18-Dec-14  
 Equipment no. : EL111 Calibration Due Date : 18-Feb-15

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition			
Temperature, T <sub>a</sub>	287	Kelvin	Pressure, P <sub>a</sub>
			1026 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m <sub>c</sub>	1.99175	Intercept, b <sub>c</sub>	-0.00041
Last Calibration Date	14-Jul-14	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	14-Jul-15				

Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC (W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31) Y-axis
	(up)	(down)	(difference)			
1	6.5	6.5	13.0	1.8563	61	62.5463
2	5.0	5.0	10.0	1.6281	54	55.3689
3	3.8	3.8	7.6	1.4194	49	50.2421
4	2.4	2.4	4.8	1.1281	36	36.9126
5	1.6	1.6	3.2	0.9211	30	30.7605

By Linear Regression of Y on X

Slope, m = 34.7719 Intercept, b = -1.1882

Correlation Coefficient\* = 0.9955

Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient < 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

Calibrated by : Henry Lau Checked by : Derek Lo  
 Date : 18-Dec-14 Date : 18-Dec-14





Lam Geotechnics Limited

### Calibration Data for High Volume Sampler (TSP Sampler)

Location : ACL2a Calibration Date : 12-Feb-15  
 Equipment no. : EL111 Calibration Due Date : 12-Apr-15

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition			
Temperature, T <sub>a</sub>	290	Kelvin	Pressure, P <sub>a</sub>
			1018 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m <sub>c</sub>	1.99175	Intercept, b <sub>c</sub>	-0.00041
Last Calibration Date	14-Jul-14	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	14-Jul-15				

Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC (W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31) Y-axis
	(up)	(down)	(difference)			
1	6.5	6.5	13.0	1.8395	63	64.0110
2	5.2	5.2	10.4	1.6453	57	57.9147
3	4.1	4.1	8.2	1.4610	50	50.8024
4	2.6	2.6	5.2	1.1635	41	41.6579
5	1.6	1.6	3.2	0.9128	32	32.5135

By Linear Regression of Y on X

Slope, m = 33.8993 Intercept, b = 1.7715

Correlation Coefficient\* = 0.9995

Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient < 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

Calibrated by : LuLu Mar Checked by : Derek Lo  
 Date : 12-Feb-15 Date : 12-Feb-15



## CERTIFICATE OF CALIBRATION

Certificate No.: 14CA0303 02 Page 1 of 2

### Item tested

Description:	Sound Level Meter (Type 1)	Microphone
Manufacturer:	Larson Davis	-
Type/Model No.:	831	377B02
Serial/Equipment No.:	0003227	SNLW135892
Adaptors used:	-	-

### Item submitted by

Customer Name:	Lam Geotechnics Ltd.
Address of Customer:	-
Request No.:	-
Date of receipt:	03-Mar-2014

Date of test: 04-Mar-2014

### Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Multi function sound calibrator	B&K 4226	2288444	22-Jun-2014	CIGISMEC
Signal generator	DS 360	33873	15-Apr-2014	CEPREI
Signal generator	DS 360	61227	15-Apr-2014	CEPREI

### Ambient conditions

Temperature:	22 ± 1 °C
Relative humidity:	60 ± 10 %
Air pressure:	1000 ± 10 hPa

### Test specifications

- 1, The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580: Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.
- 2, The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of ±20%.
- 3, The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responsiveness of the Sound Level Meter.


### Test results

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.


Actual Measurement data are documented on worksheets.

Approved Signatory:


  
Huang Jian Yin/Feng Jun Qi

Date: 04-Mar-2014

Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.



## CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.: 14CA0303 02

Page 2 of 2

### 1, Electrical Tests

The electrical tests were performed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

Test:	Subtest:	Status:	Expanded Uncertainty (dB)	Coverage Factor
Self-generated noise	A	Pass	0.3	
	C	Pass	0.8	2.1
	Lin	Pass	1.6	2.2
Linearity range for Leq	At reference range, Step 5 dB at 4 kHz	Pass	0.3	
	Reference SPL on all other ranges	Pass	0.3	
	2 dB below upper limit of each range	Pass	0.3	
	2 dB above lower limit of each range	Pass	0.3	
Linearity range for SPL	At reference range, Step 5 dB at 4 kHz	Pass	0.3	
	A	Pass	0.3	
	C	Pass	0.3	
Frequency weightings	Lin	Pass	0.3	
	Time weightings	Single Burst Fast	Pass	0.3
	Single Burst Slow	Pass	0.3	
Peak response	Single 100µs rectangular pulse	N/A	N/A	
R.M.S. accuracy	Crest factor of 3	Pass	0.3	
Time weighting I	Single burst 5 ms at 2000 Hz	Pass	0.3	
	Repeated at frequency of 100 Hz	Pass	0.3	
Time averaging	1 ms burst duty factor 1/10 <sup>3</sup> at 4kHz	Pass	0.3	
	1 ms burst duty factor 1/10 <sup>4</sup> at 4kHz	Pass	0.3	
Pulse range	Single burst 10 ms at 4 kHz	Pass	0.4	
Sound exposure level	Single burst 10 ms at 4 kHz	Pass	0.4	
Overload indication	SPL	Pass	0.3	
	Leq	Pass	0.4	

### 2, Acoustic tests

The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Test:	Subtest	Status	Expanded Uncertainty (dB)	Coverage Factor
Acoustic response	Weighting A at 125 Hz	Pass	0.3	
	Weighting A at 8000 Hz	Pass	0.5	

### 3, Response to associated sound calibrator

N/A

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

Calibrated by:

Date:

Fung Chi Yip  
04-Mar-2014

- End -

Checked by:

Date:

Lam Tze Wai  
04-Mar-2014

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.



## CERTIFICATE OF CALIBRATION

Certificate No.: 14CA0529 01-02

Page: 1 of 2

### Item tested

Description: Acoustical Calibrator (Class 1)  
Manufacturer: Rion Co., Ltd.  
Type/Model No.: NC-73  
Serial/Equipment No.: 10465798  
Adaptors used: -

### Item submitted by

Customer: Lam Geotechnics Limited  
Address of Customer: -  
Request No.: -  
Date of receipt: 29-May-2014

Date of test: 30-May-2014

### Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Lab standard microphone	B&K 4180	2412857	13-May-2015	SCL
Preamplifier	B&K 2673	2239857	10-Apr-2015	CEPREI
Measuring amplifier	B&K 2610	2346941	08-Apr-2015	CEPREI
Signal generator	DS 360	61227	09-Apr-2015	CEPREI
Digital multi-meter	34401A	US36087050	17-Dec-2014	CEPREI
Audio analyzer	8903B	GB41300350	07-Apr-2015	CEPREI
Universal counter	53132A	MY40003662	11-Apr-2015	CEPREI

### Ambient conditions

Temperature:  $22 \pm 1$  °C  
Relative humidity:  $60 \pm 10$  %  
Air pressure:  $1000 \pm 10$  hPa

### Test specifications

- The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B and the lab calibration procedure SMTP004-CA-156.
- The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.
- The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure changes.

### Test results

Details of the performed measurements are presented on **page 2** of this certificate.

Approved Signatory:

  
Huang Jian Min/Feng Jun Qi

Date: 30-May-2014

Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.





## CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.: 14CA0529 01-02

Page: 2 of 2

### 1, Measured Sound Pressure Level

The output Sound Pressure Level in the calibrator head was measured at the setting and frequency shown using a calibrated laboratory standard microphone and insert voltage technique. The results are given in below with the estimated uncertainties.

Frequency Shown Hz	Output Sound Pressure Level Setting dB	Measured Output Sound Pressure Level dB	(Output level in dB re 20 $\mu$ Pa)
			Estimated Expanded Uncertainty dB
1000	94.00	94.57	0.10

### 2, Sound Pressure Level Stability - Short Term Fluctuations

The Short Term Fluctuations was determined by measuring the maximum and minimum of the fast weighted DC output of the B&K 2610 measuring amplifier over a 20 second time interval as required in the standard. The Short Term Fluctuation was found to be:

At 1000 Hz **STF = 0.001 dB**  
Estimated expanded uncertainty 0.005 dB

### 3, Actual Output Frequency

The determination of actual output frequency was made using a B&K 4180 microphone together with a B&K 2673 preamplifier connected to a B&K 2610 measuring amplifier. The AC output of the B&K 2610 was taken to an universal counter which was used to determine the frequency averaged over 20 second of operation as required by the standard. The actual output frequency at 1 KHz was:

At 1000 Hz **Actual Frequency = 965.6 Hz**  
Estimated expanded uncertainty 0.1 Hz Coverage factor k = 2.2

### 4, Total Noise and Distortion

For the Total Noise and Distortion measurement, the unfiltered AC output of the B&K 2610 measuring amplifier was connected to an Agilent Type 8903 B distortion analyser. The TND result at 1 KHz was:

At 1000 Hz **TND = 0.9 %**  
Estimated expanded uncertainty 0.7 %

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

Calibrated by:

Date: 30-May-2014

Fung Chi Yip

- End -

Checked by:

Date: 30-May-2014

Lam Tze Wai

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION****Information supplied by customer:**

**CONTACT:** DEREK LO **WORK ORDER:** HK1410350  
**CLIENT:** LAM GEOTECHNICS LIMITED  
**DATE RECEIVED:** 2014-11-25  
**DATE OF ISSUE:** 2014-12-02  
**ADDRESS:** 11/F, CENTRE POINT, 181-185, GLOUCESTER ROAD,  
WANCHAI, HONG KONG  
**PROJECT:** ---

**METHOD OF PERFORMANCE CHECK/ CALIBRATION:**

Ref: APHA22nd ed 2130B

**COMMENTS**

It is certified that the item under performance check/calibration has been calibrated/checked by corresponding calibrated equipment in the laboratory.

Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.

<b>Scope of Test:</b>	Turbidity
<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203010
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	25-Nov-14

**Remarks:**

This is the Final Report. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr. Peter Lee  
Director

This report may not be reproduced except with prior written approval from Pilot Testing Limited.

Address: Room 1503, 15/F, Wayson Commercial House, 68-70 Lockhart Road, Wanchai, Hong Kong  
Phone +852 2527 6691 | Email info@pilot-testing.com

**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION**

**WORK ORDER:** HK1410350  
**DATE OF ISSUE:** 2014-12-02  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203010
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	25-Nov-14
<b>Date of next Calibration:</b>	25-Feb-15

**Parameters:****Turbidity**Method Ref: APHA 22<sup>nd</sup> ed. 2130B

Expected Reading (NTU)	Display Reading (NTU)	Tolerance (%)
0	0.00	---
4	3.86	-3.5
10	10.2	2.0
40	39.1	-2.3
100	104	4.0
400	412	3.0
1000	994	-0.6
	<b>Tolerance Limit (±%)</b>	<b>10.0</b>

Remark: "Displayed Reading" presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.





**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION**

**Information supplied by customer:**

**CONTACT:** SAM LAM **WORK ORDER:** HK1510067  
**CLIENT:** LAM GEOTECHNICS LIMITED  
**DATE RECEIVED:** 25/02/2015  
**DATE OF ISSUE:** 04/03/2015  
**ADDRESS:** 11/F, CENTRE POINT, 181-185, GLOUCESTER ROAD,  
WANCHAI, HONG KONG  
**PROJECT:** ---

**METHOD OF PERFORMANCE CHECK/ CALIBRATION:**

Ref: APHA22nd ed 2130B

**COMMENTS**

It is certified that the item under performance check/calibration has been calibrated/checked by corresponding calibrated equipment in the laboratory.  
Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.

<b>Scope of Test:</b>	Turbidity
<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203010
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	25-Feb-15

**Remarks:**

This is the Final Report. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr. Peter Lee  
Director

This report may not be reproduced except with prior written approval from Pilot Testing Limited.



**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION**

**WORK ORDER:** HK1510067  
**DATE OF ISSUE:** 04/03/2015  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203010
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	25-Feb-15
<b>Date of next Calibration:</b>	25-May-15

**Parameters:****Turbidity**Method Ref: APHA 22<sup>nd</sup> ed. 2130B

Expected Reading (NTU)	Display Reading (NTU)	Tolerance (%)
0	0.00	---
4	3.98	-0.5
10	10.8	8.4
40	39.8	-0.4
100	100	0.2
400	373	-6.7
1000	964	-3.6
	<b>Tolerance Limit (±%)</b>	<b>10.0</b>

Remark: "Displayed Reading" presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.

This report may not be reproduced except with prior written approval from Pilot Testing Limited.



**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION**

**Information supplied by customer:**

**CONTACT:** SAM LAM **WORK ORDER:** HK1510002  
**CLIENT:** LAM GEOTECHNICS LIMITED  
**DATE RECEIVED:** 06/01/2015  
**DATE OF ISSUE:** 13/01/2015  
**ADDRESS:** 11/F, CENTRE POINT, 181-185, GLOUCESTER ROAD,  
WANCHAI, HONG KONG  
**PROJECT:** ---

**METHOD OF PERFORMANCE CHECK/ CALIBRATION:**

Ref: APHA22nd ed 2130B

**COMMENTS**

It is certified that the item under performance check/calibration has been calibrated/checked by corresponding calibrated equipment in the laboratory.

Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.

<b>Scope of Test:</b>	Turbidity
<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203015
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	08/01/2015

**Remarks:**

This is the Final Report. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr. Peter Lee  
Director

This report may not be reproduced except with prior written approval from Pilot Testing Limited.

**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION**

**WORK ORDER:** HK1510002  
**DATE OF ISSUE:** 13/01/2015  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203015
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	08/01/2015
<b>Date of next Calibration:</b>	08/04/2015

**Parameters:****Turbidity**Method Ref: APHA 22<sup>nd</sup> ed. 2130B

Expected Reading (NTU)	Display Reading (NTU)	Tolerance (%)
0	0.00	---
4	4.20	5.0
10	9.80	-2.0
40	41.0	2.5
100	100	0.0
400	420	5.0
1000	990	-1.0
	<b>Tolerance Limit (±%)</b>	<b>10.0</b>

Remark: "Displayed Reading" presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.

This report may not be reproduced except with prior written approval from Pilot Testing Limited.



**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION**

**Information supplied by customer:**

**CONTACT:** SAM LAM **WORK ORDER:** HK1510003  
**CLIENT:** LAM GEOTECHNICS LIMITED  
**DATE RECEIVED:** 06/01/2015  
**DATE OF ISSUE:** 13/01/2015  
**ADDRESS:** 11/F, CENTRE POINT, 181-185, GLOUCESTER ROAD,  
WANCHAI, HONG KONG  
**PROJECT:** ---

**METHOD OF PERFORMANCE CHECK/ CALIBRATION:**

Ref: APHA22nd ed 2130B

**COMMENTS**

It is certified that the item under performance check/calibration has been calibrated/checked by corresponding calibrated equipment in the laboratory.

Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.

<b>Scope of Test:</b>	Turbidity
<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1309192
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	08/01/2015

**Remarks:**

This is the Final Report. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr. Peter Lee  
Director

This report may not be reproduced except with prior written approval from Pilot Testing Limited.

**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION**

**WORK ORDER:** HK1510003  
**DATE OF ISSUE:** 13/01/2015  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1309192
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	08/01/2015
<b>Date of next Calibration:</b>	08/04/2015

**Parameters:****Turbidity**Method Ref: APHA 22<sup>nd</sup> ed. 2130B

Expected Reading (NTU)	Display Reading (NTU)	Tolerance (%)
0	0.00	---
4	3.91	-2.3
10	10.2	2.0
40	40.0	0.0
100	103	3.0
400	413	3.3
1000	988	-1.2
	<b>Tolerance Limit (±%)</b>	<b>10.0</b>

Remark: "Displayed Reading" presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.

---

This report may not be reproduced except with prior written approval from Pilot Testing Limited.





ALS Technichem (HK) Pty Ltd  
11/F, Chung Shun Knitting Centre  
1-3 Wing Yip Street  
Kwai Chung, N.T., Hong Kong  
T: +852 2610 1044  
F: +852 2610 2021  
www.alsglobal.com

## REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

**CONTACT:** MR ALAN LI  
**CLIENT:** LAM GEOTECHNICS LIMITED  
**ADDRESS:** 11/F., CENTRE POINT,  
181-185 GLOUCESTER ROAD,  
WAN CHAI, HONG KONG

**WORK ORDER:** HK1436509  
**LABORATORY:** HONG KONG  
**DATE RECEIVED:** 10/11/2014  
**DATE OF ISSUE:** 17/11/2014

### COMMENTS

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.  
The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the ALS Hong Kong laboratory or quoted from relevant international standards.  
The "Next Calibration Date" is recommended according to best practice principals as practised by the ALS Hong Kong laboratory or quoted from relevant international standards.

Scope of Test: Dissolved Oxygen, pH, Salinity and Temperature  
Equipment Type: Multifunctional Meter  
Brand Name: YSI  
Model No.: Professional Plus  
Serial No.: 11F100597  
Equipment No.: --  
Date of Calibration: 17 November, 2014

### NOTES

This is the Final Report and supersedes any preliminary report with this batch number.  
Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

  
Mr. Fung Lim Chee, Richard  
General Manager -  
Greater China & Hong Kong

# REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

**Work Order:** HK1436509  
**Date of Issue:** 17/11/2014  
**Client:** LAM GEOTECHNICS LIMITED



**Equipment Type:** Multifunctional Meter  
**Brand Name:** YSI  
**Model No.:** Professional Plus  
**Serial No.:** 11F100597  
**Equipment No.:** --  
**Date of Calibration:** 17 November, 2014

**Date of next Calibration:** 17 February, 2015

**Parameters:**

**Dissolved Oxygen**

**Method Ref: APHA (21st edition), 4500O: G**

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
3.60	3.57	-0.03
6.24	6.20	-0.04
8.06	8.03	-0.03
Tolerance Limit (mg/L)		±0.20

**pH Value**

**Method Ref: APHA (21st edition), 4500H:B**

Expected Reading (pH Unit)	Displayed Reading (pH Unit)	Tolerance (pH unit)
4.0	4.09	+0.09
7.0	7.19	+0.19
10.0	10.02	+0.02
Tolerance Limit (pH unit)		±0.20

**Salinity**

**Method Ref: APHA (21st edition), 2520B**

Expected Reading (ppt)	Displayed Reading (ppt)	Tolerance (%)
0	0.00	--
10	9.57	-4.3
20	19.70	-1.5
30	29.86	-0.5
Tolerance Limit (%)		±10.0

**Temperature**

**Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.**

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
11.0	11.4	+0.4
21.5	21.9	+0.4
38.0	38.3	+0.3
Tolerance Limit (°C)		±2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

  
 Mr. Fung Lim Chee, Richard  
 General Manager  
 Greater China & Hong Kong



## EQUIPMENT PERFORMANCE CHECK / CALIBRATION REPORT

**Report No.** : HK1510049  
**Project Name** : EQUIPMENT PERFORMANCE CHECK/CALIBRATION REPORT  
**Date of Issue** : 13/02/2015  
  
**Customer** : LAM GEOTECHNICS LIMITED  
**Address** : 11/F., CENTRE POINT, 181-185 GLOUCESTER ROAD, WAN CHAI, HONG KONG


---

**Calibration Job No.** : HK1510049  
**Test Item No.** : HK1510049-01  
**Test Item Details**  
**Test Item Description** : Multifunctional Meter  
**Manufacturer** : YSI  
**Model No.** : Professional Plus  
**Serial No.** : 11F100597  
**Performance Method** : Checked according to in-house method CAL005  
 (References: Temperature (Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure), pH value (APHA 21e 4500H:B), Salinity (Refer to Conductivity APHA 19e 2510B ) , Dissolved oxygen (APHA 19e 4500-O,C))  
  
**Test Item Receipt Date** : 12-Feb-15  
**Test Item Calibration Date** : 13-Feb-15  
**Test Period** : 12/02/2015 - 13/02/2015

---

- Notes :
1. This report shall not be reproduced, except in full, without prior approval from Pilot Testing Limited.
  2. Results relate to item(s) as received.
  3.  $\pm$  indicates the tolerance limit
  4. N/A = Not applicable
  5. APHA - American Public Health Association, American Water Works Association and Water Environment Federation, Standard Methods for the Examination of Water and Wastewater, APHA-AWWA-WEF. USA
  6. DO, pH, salinity and temperature performance check was conducted by Pilot Testing Limited.
  7. Because of high sensitivity and ease of measurement, the conductivity method (according to APHA 19e 2510) is used to determine salinity.

Approved Signatory

  
 \_\_\_\_\_  
 Mr. Peter Lee  
 (Director)

Issue Date:

13/02/2015




**REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION**

**WORK ORDER:** HK1510049  
**DATE OF ISSUE:** 13/02/2015  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type</b>	Multifunctional Meter
<b>Manufacturer</b>	YSI
<b>Model No.</b>	Professional Plus
<b>Serial No.</b>	11F100597
<b>Date of Calibration</b>	13-Feb-15
<b>Date of next Calibration</b>	13-May-15

**Parameters:**

**Temperature (Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No.3 Second edition March 2008: Working Thermometer Calibration Procedure)**

Reference Reading (°C)	Display Reading (°C)	Deviation (°C)
10.8	10.8	0.0
20.2	20.3	+0.1
30.1	30.6	+0.5
Tolerance Limit		±2.0

**pH Value (Method Ref: APHA21e, 4500H:B)**

Expected Reading (pH unit)	Reference Reading (pH unit)	Display Reading (pH unit)	Deviation (pH unit)
4.0	4.05	4.06	+0.01
7.0	7.03	7.04	+0.01
10.0	9.98	9.96	+0.02
Tolerance Limit			±0.20

**Conductivity (Method Ref: APHA 19e, 2510)**

KCl concentration (mol/L)	Reference Reading (ms/cm)	Display Reading (ms/cm)	Deviation (%)
0.0000	0.00	0.00	--
0.1000	12.89	12.81	-0.63
0.2000	24.80	25.20	+1.60
0.5000	58.67	59.33	+1.12
Tolerance Limit			±2.0

**Dissolved Oxygen (DO) (Method Ref: APHA 19e, 4500-O, C)**

Reference DO reading (mg/L)	DO reading od DO probe (mg/L)	Deviation (mg/L)
7.49	7.60	+0.11
4.56	4.67	+0.11
1.86	1.83	-0.03
Tolerance Limit		±0.20

- Remarks:
- (1) Maxium tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.
  - (2) Displayed reading presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.
  - (3) Because of high sensitivity and ease of measurement, the conductivity method (accorng to APHA 19e 2510) is used to determine salinity.

- End of Report -



## EQUIPMENT PERFORMANCE CHECK / CALIBRATION REPORT

**Report No.** : HK1510021  
**Project Name** : EQUIPMENT PERFORMANCE CHECK/CALIBRATION REPORT  
**Date of Issue** : 23/01/2015  
  
**Customer** : LAM GEOTECHNICS LIMITED  
**Address** : 11/F., CENTRE POINT, 181-185 GLOUCESTER ROAD, WAN CHAI, HONG KONG

---

**Calibration Job No.** : HK1510021  
**Test Item No.** : HK1510021-01  
**Test Item Details**  
**Test Item Description** : Multifunctional Meter  
**Manufacturer** : YSI  
**Model No.** : Professional Plus  
**Serial No.** : 14E100105  
**Performance Method** : Checked according to in-house method CAL005  
 (References: Temperature (Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure), pH value (APHA 21e 4500H:B), Salinity (Refer to Conductivity APHA 19e 2510B ) , Dissolved oxygen (APHA 19e 4500-O,C))

---

**Test Item Receipt Date** : 15-Jan-15  
**Test Item Calibration Date** : 16-Jan-15  
**Test Period** : 16/01/2015 - 23/01/2015

---

- Notes :
1. This report shall not be reproduced, except in full, without prior approval from Pilot Testing Limited.
  2. Results relate to item(s) as received.
  3.  $\pm$  indicates the tolerance limit
  4. N/A = Not applicable
  5. APHA - American Public Health Association, American Water Works Association and Water Environment Federation, Standard Methods for the Examination of Water and Wastewater, APHA-AWWA-WEF. USA
  6. DO, pH, salinity and temperature performance check was conducted by Pilot Testing Limited.
  7. Because of high sensitivity and ease of measurement, the conductivity method (according to APHA 19e 2510) is used to determine salinity.

Approved Signatory :

Mr. Peter Lee  
(Director)

Issue Date:

23/01/2015


**REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION**

**WORK ORDER:** HK1510021  
**DATE OF ISSUE:** 23/01/2015  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type</b>	Multifunctional Meter
<b>Manufacturer</b>	YSI
<b>Model No.</b>	Professional Plus
<b>Serial No.</b>	14E100105
<b>Date of Calibration</b>	16-Jan-15
<b>Date of next Calibration</b>	16-Apr-15

**Parameters:**

**Temperature (Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No.3 Second edition March 2008: Working Thermometer Calibration Procedure)**

Reference Reading (°C)	Display Reading (°C)	Deviation (°C)
10.0	10.4	+0.4
19.4	19.6	+0.2
30.0	30.1	+0.1
	<b>Tolerance Limit</b>	<b>±2.0</b>

**pH Value (Method Ref: APHA21e, 4500H:B)**

Expected Reading (pH unit)	Reference Reading (pH unit)	Display Reading (pH unit)	Deviation (pH unit)
4.0	4.06	4.02	-0.04
7.0	7.01	7.09	+0.08
10.0	9.99	10.03	+0.04
	<b>Tolerance Limit</b>		<b>±0.20</b>

**Conductivity (Method Ref: APHA 19e, 2510)**

KCl concentration (mol/L)	Reference Reading (ms/cm)	Display Reading (ms/cm)	Deviation (%)
0.0000	0.00	0.00	--
0.1000	12.89	12.69	-1.55
0.2000	24.80	25.25	1.82
0.5000	58.67	57.50	-1.99
	<b>Tolerance Limit</b>		<b>±2.0</b>

**Dissolved Oxygen (DO) (Method Ref: APHA 19e, 4500-O, C)**

Reference DO reading (mg/L)	DO reading od DO probe (mg/L)	Deviation (mg/L)
8.18	8.14	-0.04
5.89	5.90	0.01
4.42	4.26	-0.16
	<b>Tolerance Limit</b>	<b>±0.20</b>

- Remarks:
- (1) Maxium tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.
  - (2) Displayed reading presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.
  - (3) Because of high sensitivity and ease of measurement, the conductivity method (accoriding to APHA 19e 2510) is used to determine salinity.

- End of Report -





## EQUIPMENT PERFORMANCE CHECK / CALIBRATION REPORT

**Report No.** : HK1510022  
**Project Name** : EQUIPMENT PERFORMANCE CHECK/CALIBRATION REPORT  
**Date of Issue** : 26/01/2015  
  
**Customer** : LAM GEOTECHNICS LIMITED  
**Address** : 11/F., CENTRE POINT, 181-185 GLOUCESTER ROAD, WAN CHAI, HONG KONG

---

**Calibration Job No.** : HK1510022  
**Test Item No.** : HK1510022-01  
**Test Item Details**  
**Test Item Description** : Multifunctional Meter  
**Manufacturer** : YSI  
**Model No.** : Professional Plus  
**Serial No.** : 14M100277  
**Performance Method** : Checked according to in-house method CAL005  
 (References: Temperature (Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure), pH value (APHA 21e 4500H:B), Salinity (Refer to Conductivity APHA 19e 2510B ) , Dissolved oxygen (APHA 19e 4500-O,C))  
  
**Test Item Receipt Date** : 19-Jan-15  
**Test Item Calibration Date** : 19-Jan-15  
**Test Period** : 19/01/2015 - 26/01/2015

---

- Notes :
1. This report shall not be reproduced, except in full, without prior approval from Pilot Testing Limited.
  2. Results relate to item(s) as received.
  3.  $\pm$  indicates the tolerance limit
  4. N/A = Not applicable
  5. APHA - American Public Health Association, American Water Works Association and Water Environment Federation, Standard Methods for the Examination of Water and Wastewater, APHA-AWWA-WEF. USA
  6. DO, pH, salinity and temperature performance check was conducted by Pilot Testing Limited.
  7. Because of high sensitivity and ease of measurement, the conductivity method (according to APHA 19e 2510) is used to determine salinity.

Approved Signatory

Mr. Peter Lee  
(Director)

Issue Date:

26/01/2015


**REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION**

**WORK ORDER:** HK1510022  
**DATE OF ISSUE:** 26/01/2015  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type</b>	Multifunctional Meter
<b>Manufacturer</b>	YSI
<b>Model No.</b>	Professional Plus
<b>Serial No.</b>	14M100277
<b>Date of Calibration</b>	19-Jan-15
<b>Date of next Calibration</b>	19-Apr-15

**Parameters:**

**Temperature (Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No.3 Second edition March 2008: Working Thermometer Calibration Procedure)**

Reference Reading (°C)	Display Reading (°C)	Deviation (°C)
10.4	10.8	+0.4
19.9	20.1	+0.2
30.2	30.0	-0.2
	<b>Tolerance Limit</b>	<b>±2.0</b>

**pH Value (Method Ref: APHA21e, 4500H:B)**

Expected Reading (pH unit)	Reference Reading (pH unit)	Display Reading (pH unit)	Deviation (pH unit)
4.0	4.05	4.07	+0.02
7.0	7.02	7.04	+0.02
10.0	9.99	10.18	+0.19
	<b>Tolerance Limit</b>		<b>±0.20</b>

**Conductivity (Method Ref: APHA 19e, 2510)**

KCl concentration (mol/L)	Reference Reading (ms/cm)	Display Reading (ms/cm)	Deviation (%)
0.0000	0.00	0.00	--
0.1000	12.89	12.99	+0.74
0.2000	24.80	24.91	+0.43
0.5000	58.67	59.21	+0.93
	<b>Tolerance Limit</b>		<b>±2.0</b>

**Dissolved Oxygen (DO) (Method Ref: APHA 19e, 4500-O, C)**

Reference DO reading (mg/L)	DO reading od DO probe (mg/L)	Deviation (mg/L)
8.28	8.22	-0.06
4.67	4.59	-0.08
1.42	1.48	+0.06
	<b>Tolerance Limit</b>	<b>±0.20</b>

- Remarks:
- (1) Maxium tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.
  - (2) Displayed reading presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.
  - (3) Because of high sensitivity and ease of measurement, the conductivity method (accoriding to APHA 19e 2510) is used to determine salinity.

- End of Report -



## EQUIPMENT PERFORMANCE CHECK / CALIBRATION REPORT

**Report No.** : HK1510022  
**Project Name** : EQUIPMENT PERFORMANCE CHECK/CALIBRATION REPORT  
**Date of Issue** : 26/01/2015  
  
**Customer** : LAM GEOTECHNICS LIMITED  
**Address** : 11/F., CENTRE POINT, 181-185 GLOUCESTER ROAD, WAN CHAI, HONG KONG

---

**Calibration Job No.** : HK1510022  
**Test Item No.** : HK1510022-01  
**Test Item Details**  
**Test Item Description** : Multifunctional Meter  
**Manufacturer** : YSI  
**Model No.** : Professional Plus  
**Serial No.** : 14M100277  
**Performance Method** : Checked according to in-house method CAL005  
 (References: Temperature (Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure), pH value (APHA 21e 4500H:B), Salinity (Refer to Conductivity APHA 19e 2510B ) , Dissolved oxygen (APHA 19e 4500-O,C))  
  
**Test Item Receipt Date** : 19-Jan-15  
**Test Item Calibration Date** : 19-Jan-15  
**Test Period** : 19/01/2015 - 26/01/2015

---

- Notes :
1. This report shall not be reproduced, except in full, without prior approval from Pilot Testing Limited.
  2. Results relate to item(s) as received.
  3.  $\pm$  indicates the tolerance limit
  4. N/A = Not applicable
  5. APHA - American Public Health Association, American Water Works Association and Water Environment Federation, Standard Methods for the Examination of Water and Wastewater, APHA-AWWA-WEF. USA
  6. DO, pH, salinity and temperature performance check was conducted by Pilot Testing Limited.
  7. Because of high sensitivity and ease of measurement, the conductivity method (according to APHA 19e 2510) is used to determine salinity.

Approved Signatory

Mr. Peter Lee  
(Director)

Issue Date:

26/01/2015




**REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION**

**WORK ORDER:** HK1510022  
**DATE OF ISSUE:** 26/01/2015  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type</b>	Multifunctional Meter
<b>Manufacturer</b>	YSI
<b>Model No.</b>	Professional Plus
<b>Serial No.</b>	14M100277
<b>Date of Calibration</b>	19-Jan-15
<b>Date of next Calibration</b>	19-Apr-15

**Parameters:**

**Temperature (Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No.3 Second edition March 2008: Working Thermometer Calibration Procedure)**

Reference Reading (°C)	Display Reading (°C)	Deviation (°C)
10.4	10.8	+0.4
19.9	20.1	+0.2
30.2	30.0	-0.2
	<b>Tolerance Limit</b>	<b>±2.0</b>

**pH Value (Method Ref: APHA21e, 4500H:B)**

Expected Reading (pH unit)	Reference Reading (pH unit)	Display Reading (pH unit)	Deviation (pH unit)
4.0	4.05	4.07	+0.02
7.0	7.02	7.04	+0.02
10.0	9.99	10.18	+0.19
	<b>Tolerance Limit</b>		<b>±0.20</b>

**Conductivity (Method Ref: APHA 19e, 2510)**

KCl concentration (mol/L)	Reference Reading (ms/cm)	Display Reading (ms/cm)	Deviation (%)
0.0000	0.00	0.00	--
0.1000	12.89	12.99	+0.74
0.2000	24.80	24.91	+0.43
0.5000	58.67	59.21	+0.93
	<b>Tolerance Limit</b>		<b>±2.0</b>

**Dissolved Oxygen (DO) (Method Ref: APHA 19e, 4500-O, C)**

Reference DO reading (mg/L)	DO reading od DO probe (mg/L)	Deviation (mg/L)
8.28	8.22	-0.06
4.67	4.59	-0.08
1.42	1.48	+0.06
	<b>Tolerance Limit</b>	<b>±0.20</b>

- Remarks:
- (1) Maxium tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.
  - (2) Displayed reading presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.
  - (3) Because of high sensitivity and ease of measurement, the conductivity method (accoriding to APHA 19e 2510) is used to determine salinity.

- End of Report -



***Appendix 5.1***

***Monitoring Schedules for Reporting Month and Coming Reporting Month***



Contract No. HK/2011/07  
Wan Chai Development Phase II and Central-Wan Chai Bypass  
Sampling, Field Measurement and Testing Works (Stage 2)

Environmental Monitoring Schedule  
February 2015

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1-Feb	2-Feb	3-Feb	4-Feb	5-Feb	6-Feb	7-Feb
	24hr TSP Impact WQM Mid-flood	1hr TSP Impact WQM Mid-ebb		Impact WQM Mid-ebb		24hr TSP Impact WQM Mid-ebb
	17:07	0:05		13:17 18:58		14:18 20:08
8-Feb	9-Feb	10-Feb	11-Feb	12-Feb	13-Feb	14-Feb
	1hr TSP Impact WQM Mid-ebb		Impact WQM Mid-flood Mid-ebb		24hr TSP Impact WQM Mid-flood	24hr TSP (ACL2a) 1hr TSP
	15:33 21:17		10:48 17:15		12:22 19:56	
15-Feb	16-Feb	17-Feb	18-Feb	19-Feb	20-Feb	21-Feb
		24hr TSP	24hr TSP (ACL1) 1hr TSP Impact WQM Mid-ebb			
	Impact WQM Mid-flood Mid-ebb		12:05 17:35			
	15:39 22:42					
22-Feb	23-Feb	24-Feb	25-Feb	26-Feb	27-Feb	28-Feb
	24hr TSP	24hr TSP (ACL1) 1hr TSP Impact WQM Mid-flood Mid-ebb		Impact WQM Mid-flood Mid-ebb		24hr TSP Impact WQM Mid-flood Mid-ebb
		10:16 16:44		11:55 19:27		13:52 21:43
1-Mar	2-Mar					
	1hr TSP					

Remark:

Due to interruption of electricity supply, the 24hr TSP monitoring at ACL1 was rescheduled from 17 and 23 February 2015 to 18 to 24 February 2015 respectively.

Due to interruption of electricity supply, the 24hr TSP monitoring at ACL2 was rescheduled from 13 February 2015 to 14 February 2015.

With respect to the suspension of marine construction activities under the contract during Chinese New Year Holiday, the water quality monitoring event on 20 February 2015 during both flood tide and ebb tide were temporarily suspended.

**Wan Chai Development Phase II and Central-Wan Chai Bypass  
Sampling, Field Measurement and Testing Works (Stage 2)**

**Tentive Environmental Monitoring Schedule  
March 2015**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1-Mar	2-Mar	3-Mar	4-Mar	5-Mar	6-Mar	7-Mar
	Impact WQM Mid-flood 16:14 Mid-ebb 23:08			Impact WQM Mid-ebb 12:23 Mid-flood 18:15	24hr TSP	1hr TSP Impact WQM Mid-ebb 13:19 Mid-flood 19:27
8-Mar	9-Mar	10-Mar	11-Mar	12-Mar	13-Mar	14-Mar
	Impact WQM Mid-flood 8:19 Mid-ebb 14:25		Impact WQM Mid-flood 9:17 Mid-ebb 15:40	24hr TSP	1hr TSP Impact WQM Mid-flood 10:28 Mid-ebb 17:34	
15-Mar	16-Mar	17-Mar	18-Mar	19-Mar	20-Mar	21-Mar
	Impact WQM Mid-flood 14:16 Mid-ebb 21:22		24hr TSP Impact WQM Mid-ebb 11:01 Mid-flood 16:33	1hr TSP	Impact WQM Mid-ebb 12:24 Mid-flood 18:22	
22-Mar	23-Mar	24-Mar	25-Mar	26-Mar	27-Mar	28-Mar
	24hr TSP Impact WQM Mid-flood 8:11 Mid-ebb 14:30	1hr TSP	Impact WQM Mid-flood 9:25 Mid-ebb 16:06		24hr TSP Impact WQM Mid-flood 10:51 Mid-ebb 18:30	1hr TSP
29-Mar	30-Mar	31-Mar				
	Impact WQM Mid-flood 15:02 Mid-ebb 21:52					



***Appendix 5.2***

***Continuous Noise Monitoring Results and Graphical Presentations***













Continuous Noise Monitoring Data ACL3 (City Hall)

Table with 5 columns of date and time data, and 5 columns of numerical noise level data. The data points range from 5/2/15 1:56 to 6/2/15 2:56.

Continuous Noise Monitoring Data ACL3 (City Hall)

Table with 12 columns of noise monitoring data, including time and noise level (dB). Rows are grouped by date and time intervals, such as 12/2/15 0:26 to 13/2/15 2:31.




Continuous Noise Monitoring Data ACL3 (City Hall)

25/2/15 5:26	56.5	26/2/15 6:31	57.9	27/2/15 23:36	60.3
25/2/15 5:31	57.8	26/2/15 6:36	57.6	27/2/15 23:41	58.5
25/2/15 5:36	55.8	26/2/15 6:41	58.9	27/2/15 23:46	59.2
25/2/15 5:41	56.3	26/2/15 6:46	58.5	27/2/15 23:51	57.5
25/2/15 5:46	56.2	26/2/15 6:51	59.0	27/2/15 23:56	56.5
25/2/15 5:51	56.6	26/2/15 6:56	58.6	28/2/15 0:01	56.4
25/2/15 5:56	57.2	26/2/15 23:01	59.5	28/2/15 0:06	57.0
25/2/15 6:01	57.9	26/2/15 23:06	58.9	28/2/15 0:11	56.2
25/2/15 6:06	56.1	26/2/15 23:11	58.8	28/2/15 0:16	56.6
25/2/15 6:11	56.2	26/2/15 23:16	58.0	28/2/15 0:21	56.8
25/2/15 6:16	57.4	26/2/15 23:21	58.7	28/2/15 0:26	56.6
25/2/15 6:21	57.4	26/2/15 23:26	57.9	28/2/15 0:31	56.0
25/2/15 6:26	57.5	26/2/15 23:31	57.4	28/2/15 0:36	56.7
25/2/15 6:31	57.9	26/2/15 23:36	57.0	28/2/15 0:41	56.4
25/2/15 6:36	57.7	26/2/15 23:41	58.7	28/2/15 0:46	56.6
25/2/15 6:41	58.6	26/2/15 23:46	57.2	28/2/15 0:51	56.2
25/2/15 6:46	58.6	26/2/15 23:51	55.8	28/2/15 0:56	57.2
25/2/15 6:51	59.5	26/2/15 23:56	57.1	28/2/15 1:01	56.3
25/2/15 6:56	59.3	27/2/15 0:01	56.4	28/2/15 1:06	56.5
25/2/15 23:01	59.4	27/2/15 0:06	56.3	28/2/15 1:11	56.5
25/2/15 23:06	58.2	27/2/15 0:11	56.2	28/2/15 1:16	56.4
25/2/15 23:11	58.2	27/2/15 0:16	56.6	28/2/15 1:21	57.5
25/2/15 23:16	58.4	27/2/15 0:21	56.2	28/2/15 1:26	56.3
25/2/15 23:21	58.5	27/2/15 0:26	56.8	28/2/15 1:31	56.0
25/2/15 23:26	58.4	27/2/15 0:31	55.8	28/2/15 1:36	55.2
25/2/15 23:31	57.3	27/2/15 0:36	56.5	28/2/15 1:41	55.3
25/2/15 23:36	56.0	27/2/15 0:41	56.0	28/2/15 1:46	56.0
25/2/15 23:41	57.2	27/2/15 0:46	55.6	28/2/15 1:51	56.1
25/2/15 23:46	56.5	27/2/15 0:51	56.4	28/2/15 1:56	55.7
25/2/15 23:51	56.5	27/2/15 0:56	55.8	28/2/15 2:01	55.2
25/2/15 23:56	55.3	27/2/15 1:01	56.1	28/2/15 2:06	55.3
26/2/15 0:01	56.5	27/2/15 1:06	52.0	28/2/15 2:11	55.2
26/2/15 0:06	55.8	27/2/15 1:11	56.4	28/2/15 2:16	55.1
26/2/15 0:11	55.7	27/2/15 1:16	55.8	28/2/15 2:21	55.6
26/2/15 0:16	55.1	27/2/15 1:21	56.2	28/2/15 2:26	55.0
26/2/15 0:21	55.2	27/2/15 1:26	55.7	28/2/15 2:31	55.4
26/2/15 0:26	54.8	27/2/15 1:31	55.9	28/2/15 2:36	55.4
26/2/15 0:31	54.5	27/2/15 1:36	54.9	28/2/15 2:41	56.3
26/2/15 0:36	54.6	27/2/15 1:41	55.5	28/2/15 2:46	54.8
26/2/15 0:41	53.4	27/2/15 1:46	55.1	28/2/15 2:51	55.5
26/2/15 0:46	53.4	27/2/15 1:51	56.1	28/2/15 2:56	55.2
26/2/15 0:51	55.8	27/2/15 1:56	54.9	28/2/15 3:01	55.3
26/2/15 0:56	55.8	27/2/15 2:01	55.0	28/2/15 3:06	55.4
26/2/15 1:01	56.7	27/2/15 2:06	54.8	28/2/15 3:11	55.5
26/2/15 1:06	54.8	27/2/15 2:11	54.9	28/2/15 3:16	55.7
26/2/15 1:11	55.2	27/2/15 2:16	55.1	28/2/15 3:21	56.4
26/2/15 1:16	54.9	27/2/15 2:21	54.6	28/2/15 3:26	55.4
26/2/15 1:21	55.6	27/2/15 2:26	54.8	28/2/15 3:31	55.7
26/2/15 1:26	53.7	27/2/15 2:31	54.2	28/2/15 3:36	55.3
26/2/15 1:31	55.1	27/2/15 2:36	54.5	28/2/15 3:41	54.9
26/2/15 1:36	56.0	27/2/15 2:41	54.6	28/2/15 3:46	55.2
26/2/15 1:41	58.0	27/2/15 2:46	54.5	28/2/15 3:51	55.5
26/2/15 1:46	57.1	27/2/15 2:51	47.0	28/2/15 3:56	55.0
26/2/15 1:51	55.5	27/2/15 2:56	55.8	28/2/15 4:01	55.4
26/2/15 1:56	55.4	27/2/15 3:01	59.1	28/2/15 4:06	55.1
26/2/15 2:01	57.8	27/2/15 3:06	55.1	28/2/15 4:11	56.0
26/2/15 2:06	54.9	27/2/15 3:11	55.4	28/2/15 4:16	55.8
26/2/15 2:11	54.7	27/2/15 3:16	54.1	28/2/15 4:21	55.3
26/2/15 2:16	54.5	27/2/15 3:21	54.4	28/2/15 4:26	55.2
26/2/15 2:21	54.9	27/2/15 3:26	54.2	28/2/15 4:31	55.2
26/2/15 2:26	53.9	27/2/15 3:31	54.1	28/2/15 4:36	56.1
26/2/15 2:31	54.3	27/2/15 3:36	54.4	28/2/15 4:41	54.9
26/2/15 2:36	54.5	27/2/15 3:41	54.9	28/2/15 4:46	54.8
26/2/15 2:41	54.5	27/2/15 3:46	54.1	28/2/15 4:51	55.1
26/2/15 2:46	55.1	27/2/15 3:51	54.1	28/2/15 4:56	54.9
26/2/15 2:51	54.2	27/2/15 3:56	54.5	28/2/15 5:01	55.3
26/2/15 2:56	54.2	27/2/15 4:01	54.2	28/2/15 5:06	55.9
26/2/15 3:01	54.7	27/2/15 4:06	53.9	28/2/15 5:11	55.0
26/2/15 3:06	54.7	27/2/15 4:11	55.0	28/2/15 5:16	55.8
26/2/15 3:11	53.9	27/2/15 4:16	57.8	28/2/15 5:21	55.7
26/2/15 3:16	54.3	27/2/15 4:21	55.0	28/2/15 5:26	56.0
26/2/15 3:21	54.9	27/2/15 4:26	53.8	28/2/15 5:31	55.7
26/2/15 3:26	55.0	27/2/15 4:31	54.3	28/2/15 5:36	55.9
26/2/15 3:31	54.4	27/2/15 4:36	54.7	28/2/15 5:41	55.5
26/2/15 3:36	55.4	27/2/15 4:41	53.9	28/2/15 5:46	56.8
26/2/15 3:41	55.8	27/2/15 4:46	54.5	28/2/15 5:51	56.3
26/2/15 3:46	55.5	27/2/15 4:51	54.8	28/2/15 5:56	56.1
26/2/15 3:51	54.9	27/2/15 4:56	54.1	28/2/15 6:01	56.4
26/2/15 3:56	54.8	27/2/15 5:01	54.4	28/2/15 6:06	56.4
26/2/15 4:01	54.8	27/2/15 5:06	54.9	28/2/15 6:11	55.6
26/2/15 4:06	55.2	27/2/15 5:11	54.2	28/2/15 6:16	56.2
26/2/15 4:11	56.3	27/2/15 5:16	54.8	28/2/15 6:21	56.3
26/2/15 4:16	55.6	27/2/15 5:21	56.4	28/2/15 6:26	56.5
26/2/15 4:21	54.4	27/2/15 5:26	56.2	28/2/15 6:31	56.3
26/2/15 4:26	54.7	27/2/15 5:31	54.9	28/2/15 6:36	58.0
26/2/15 4:31	54.3	27/2/15 5:36	55.3	28/2/15 6:41	57.5
26/2/15 4:36	54.0	27/2/15 5:41	57.3	28/2/15 6:46	58.1
26/2/15 4:41	54.2	27/2/15 5:46	55.4	28/2/15 6:51	58.1
26/2/15 4:46	54.7	27/2/15 5:51	57.9	28/2/15 6:56	57.9
26/2/15 4:51	54.9	27/2/15 5:56	55.2	28/2/15 23:01	59.4
26/2/15 4:56	54.8	27/2/15 6:01	57.1	28/2/15 23:06	59.8
26/2/15 5:01	54.5	27/2/15 6:06	56.2	28/2/15 23:11	59.8
26/2/15 5:06	54.3	27/2/15 6:11	56.1	28/2/15 23:16	59.8
26/2/15 5:11	55.0	27/2/15 6:16	57.1	28/2/15 23:21	60.2
26/2/15 5:16	55.3	27/2/15 6:21	56.6	28/2/15 23:26	59.6
26/2/15 5:21	56.1	27/2/15 6:26	56.6	28/2/15 23:31	58.7
26/2/15 5:26	55.2	27/2/15 6:31	58.3	28/2/15 23:36	58.5
26/2/15 5:31	54.8	27/2/15 6:36	58.6	28/2/15 23:41	58.2
26/2/15 5:36	55.6	27/2/15 6:41	58.6	28/2/15 23:46	61.8
26/2/15 5:41	56.0	27/2/15 6:46	57.8	28/2/15 23:51	57.9
26/2/15 5:46	57.6	27/2/15 6:51	59.0	28/2/15 23:56	57.7
26/2/15 5:51	56.3	27/2/15 6:56	59.3		
26/2/15 5:56	56.8	27/2/15 23:01	58.9		
26/2/15 6:01	57.8	27/2/15 23:06	59.0		
26/2/15 6:06	57.1	27/2/15 23:11	59.4		
26/2/15 6:11	55.8	27/2/15 23:16	58.9		
26/2/15 6:16	57.4	27/2/15 23:21	58.8		
26/2/15 6:21	56.8	27/2/15 23:26	58.2		
26/2/15 6:26	57.2	27/2/15 23:31	58.1		



Graphic Presentation of Continuous Noise Monitoring Result (ACL3-City Hall)

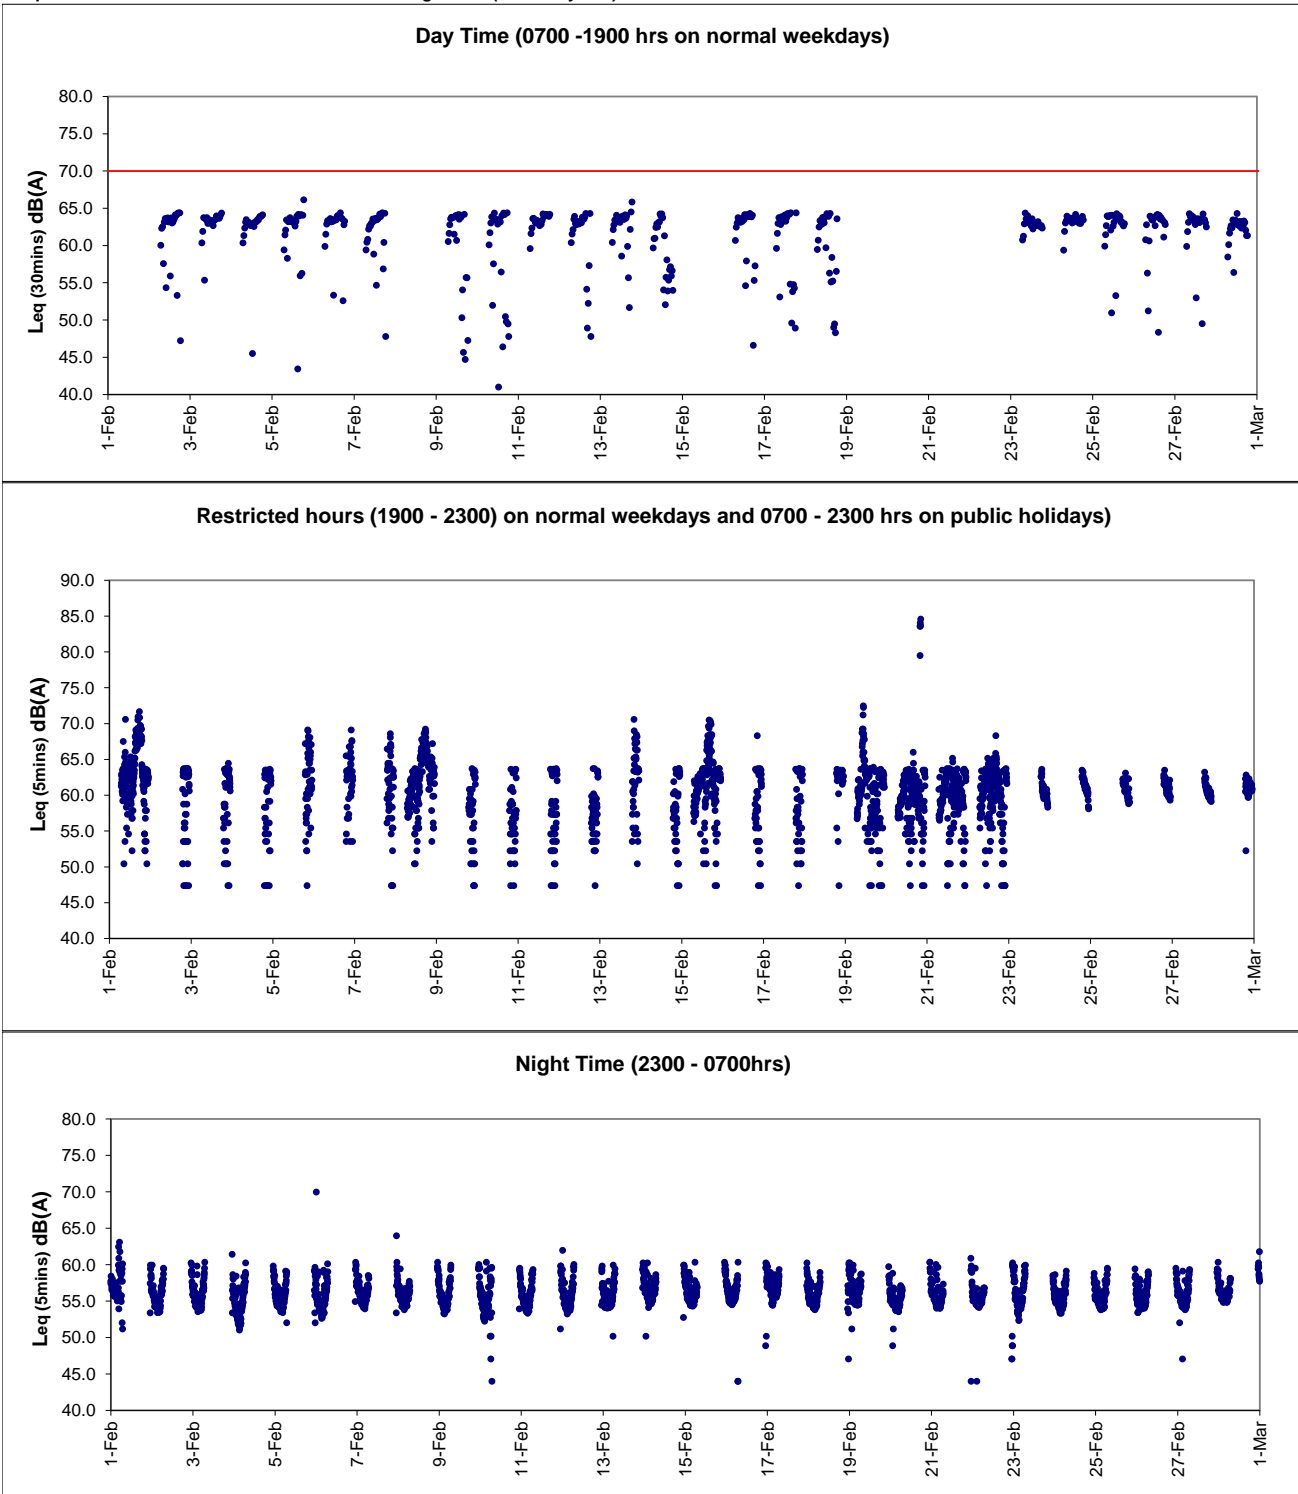



***Appendix 5.3***

***Air Quality Monitoring Results and Graphical Presentations***



Location: ACL1 - City Hall

Report on 24-hour TSP monitoring

Action Level ( $\mu\text{g}/\text{m}^3$ ) - 163

Limit Level ( $\mu\text{g}/\text{m}^3$ ) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{si}$	Final, $Q_{sf}$	Average		
2-Feb-15	8:00	Fine	011006	2.7656	2.9045	20728.17	20752.17	24.00	1.29	1.28	1.28	1850	75.1
7-Feb-15	8:00	Fine	009586	2.8246	3.0996	20755.16	20779.16	24.00	1.28	1.28	1.28	1849	148.7
13-Feb-15	8:00	Fine	009587	2.8202	3.0240	20782.16	20806.16	24.00	1.06	1.06	1.06	1524	133.8
18-Feb-15	14:50	Cloudy	011159	2.7397	2.9278	20826.17	20850.17	24.00	1.00	1.00	1.00	1437	130.9
24-Feb-15	11:40	Cloudy	011161	2.7272	2.8033	20875.36	20899.36	24.00	0.93	0.93	0.93	1335	57.0
28-Feb-15	8:00	Cloudy	011179	2.7294	2.8228	20899.37	20923.37	24.00	0.93	0.93	0.93	1341	69.7

\* Due to interruption of electricity supply, the 24hr TSP was rescheduled from 17 and 23 February 2015 to 18 and 24 February 2015 respectively.

Report on 1-hour TSP monitoring

Action Level ( $\mu\text{g}/\text{m}^3$ ) - 460

Limit Level ( $\mu\text{g}/\text{m}^3$ ) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{si}$	Final, $Q_{sf}$	Average		
3-Feb-15	8:05	Fine	009613	2.8116	2.8176	20752.17	20753.17	1.00	1.09	1.09	1.09	66	91.4
3-Feb-15	9:10	Fine	009610	2.8260	2.8318	20753.17	20754.17	1.00	1.09	1.09	1.09	66	88.4
3-Feb-15	10:20	Fine	009606	2.8220	2.8282	20754.17	20755.17	1.00	1.09	1.09	1.09	66	94.5
9-Feb-15	8:09	Fine	011088	2.7272	2.7363	20779.16	20780.16	1.00	1.23	1.23	1.23	74	123.6
9-Feb-15	9:12	Fine	011091	2.7259	2.7346	20780.16	20781.16	1.00	1.23	1.23	1.23	74	118.2
9-Feb-15	10:20	Fine	011094	2.7376	2.7468	20781.16	20782.16	1.00	1.23	1.23	1.23	74	125.0
14-Feb-15	8:04	Fine	009642	2.8612	2.8716	20806.16	20807.16	1.00	0.99	0.99	0.99	60	174.5
14-Feb-15	9:09	Fine	009695	2.8693	2.8787	20807.16	20808.16	1.00	0.99	0.99	0.99	60	157.8
14-Feb-15	10:13	Fine	009648	2.8676	2.8720	20808.16	20809.16	1.00	0.87	0.87	0.87	52	84.7
18-Feb-15	8:00	Cloudy	011150	2.7288	2.7459	20823.17	20824.17	1.00	1.00	1.00	1.00	60	286.0
18-Feb-15	11:00	Cloudy	011157	2.7268	2.7398	20825.17	20826.17	1.00	1.00	1.00	1.00	60	217.5
18-Feb-15	13:00	Cloudy	011158	2.7411	2.7485	20826.17	20827.17	1.00	1.00	1.00	1.00	60	123.8
24-Feb-15	8:05	Cloudy	011246	2.7795	2.7803	20872.36	20873.36	1.00	0.93	0.93	0.93	56	14.4
24-Feb-15	9:15	Cloudy	011249	2.7916	2.7935	20873.16	20874.16	1.00	0.93	0.93	0.93	56	34.1
24-Feb-15	10:30	Cloudy	011252	2.8018	2.8033	20874.36	20875.36	1.00	0.93	0.93	0.93	56	26.9
2-Mar-15	8:10	Cloudy	011168	2.7241	2.7290	20923.37	20924.37	1.00	0.93	0.99	0.96	58	84.8
2-Mar-15	9:20	Cloudy	011171	2.7205	2.7248	20924.37	20925.37	1.00	0.93	0.99	0.96	58	74.4
2-Mar-15	10:45	Cloudy	009662	2.8504	2.8617	20925.37	20926.37	1.00	0.93	0.99	0.96	58	195.6



Location: ACL2a - Contractor HK/2012/08 Site office

Report on 24-hour TSP monitoring

Action Level ( $\mu\text{g}/\text{m}^3$ ) - 187.3

Limit Level ( $\mu\text{g}/\text{m}^3$ ) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{si}$	Final, $Q_{sf}$	Average		
2-Feb-15	8:00	Fine	009596	2.8228	2.9509	3088.40	3112.40	24.00	1.10	1.10	1.10	1590	80.6
7-Feb-15	8:00	Fine	009625	2.8566	3.0969	3115.42	3139.42	24.00	1.10	1.10	1.10	1589	151.2
14-Feb-15	17:00	Fine	009594	2.8325	3.1575	3145.52	3169.52	24.00	1.21	1.21	1.21	1740	186.8
17-Feb-15	8:00	Cloudy	009588	2.8245	3.0304	3169.53	3193.53	24.00	1.09	1.10	1.10	1577	130.5
23-Feb-15	8:00	Cloudy	011135	2.7290	2.8695	3196.53	3220.53	24.00	1.04	1.04	1.04	1492	94.2
28-Feb-15	8:00	Cloudy	011175	2.7272	2.8653	3223.54	3247.54	24.00	1.15	1.15	1.15	1660	83.2

\* Due to interruption of electricity supply, the 24hr TSP was rescheduled from 13 February 2015 to 14 February 2015.

Report on 1-hour TSP monitoring


Action Level ( $\mu\text{g}/\text{m}^3$ ) - 300.1

Limit Level ( $\mu\text{g}/\text{m}^3$ ) - 500


Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{si}$	Final, $Q_{sf}$	Average		
3-Feb-15	9:55	Fine	009617	2.8554	2.8653	3112.40	3113.40	1.00	1.16	1.16	1.16	70	142.3
3-Feb-15	11:00	Fine	009619	2.8587	2.8684	3113.42	3114.42	1.00	1.16	1.16	1.16	70	139.4
3-Feb-15	13:00	Fine	009622	2.8600	2.8726	3114.42	3115.42	1.00	1.16	1.16	1.16	70	181.1
9-Feb-15	10:30	Fine	009629	2.8575	2.8733	3139.42	3140.42	1.00	1.16	1.16	1.16	70	226.1
9-Feb-15	13:00	Fine	009632	2.8517	2.8672	3140.42	3141.42	1.00	1.16	1.16	1.16	70	221.8
9-Feb-15	14:10	Fine	011083	2.7318	2.7460	3141.42	3142.42	1.00	1.16	1.16	1.16	70	203.2
14-Feb-15	13:00	Fine	011070	2.7288	2.7392	3142.52	3143.52	1.00	1.04	1.04	1.04	62	167.2
14-Feb-15	14:09	Fine	011075	2.7425	2.7505	3143.52	3144.52	1.00	1.09	1.09	1.09	66	121.9
14-Feb-15	15:15	Fine	009591	2.8326	2.8422	3144.52	3145.52	1.00	1.04	1.04	1.04	62	154.4
18-Feb-15	9:02	Cloudy	009636	2.8598	2.8716	3193.53	3194.53	1.00	1.04	1.04	1.04	62	189.2
18-Feb-15	10:11	Cloudy	011128	2.7353	2.7464	3194.53	3195.53	1.00	1.04	1.04	1.04	62	178.0
18-Feb-15	13:00	Cloudy	011132	2.7261	2.7382	3195.53	3196.53	1.00	1.04	1.04	1.04	62	194.0
24-Feb-15	8:15	Cloudy	011215	2.8057	2.8174	3220.53	3221.53	1.00	1.15	1.15	1.15	69	169.6
24-Feb-15	9:20	Cloudy	011214	2.7276	2.7394	3221.53	3222.53	1.00	1.15	1.15	1.15	69	171.0
24-Feb-15	10:30	Cloudy	011187	2.7230	2.7334	3222.53	3223.53	1.00	1.15	1.15	1.15	69	150.7
2-Mar-15	10:40	Cloudy	011243	2.7795	2.7847	3247.54	3248.54	1.00	1.15	1.15	1.15	69	75.2
2-Mar-15	13:00	Cloudy	011223	2.7751	2.7863	3248.54	3249.54	1.00	1.15	1.15	1.15	69	162.0
2-Mar-15	14:20	Cloudy	011225	2.7771	2.7840	3249.54	3250.54	1.00	1.15	1.15	1.15	69	99.8



Graphic Presentation of 1 hour TSP Result

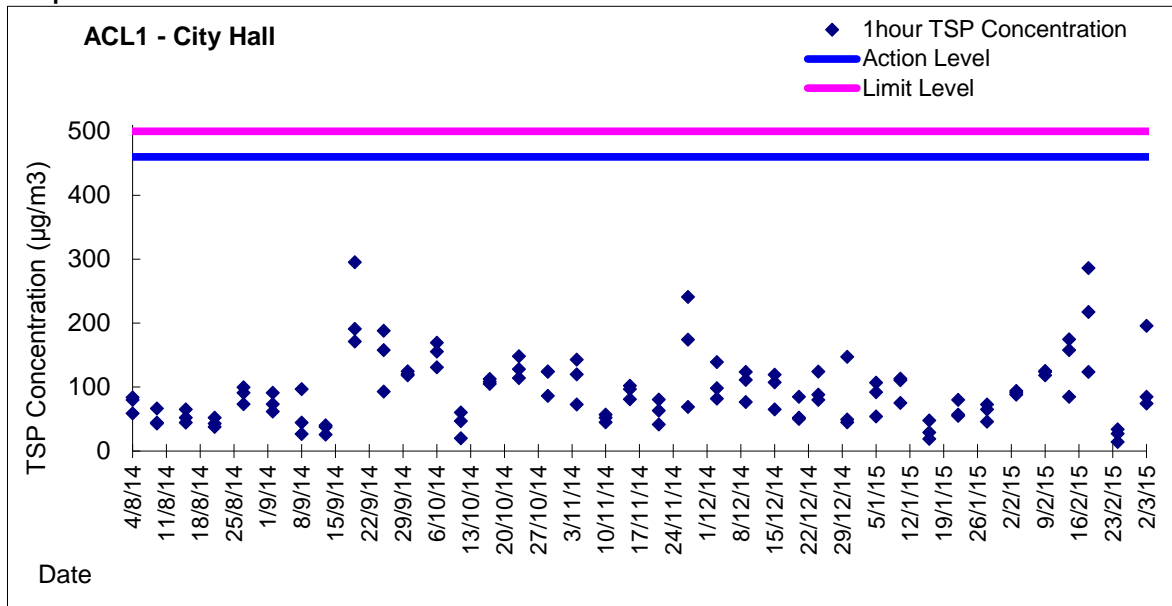


Graphic Presentation of 24 hour TSP Result

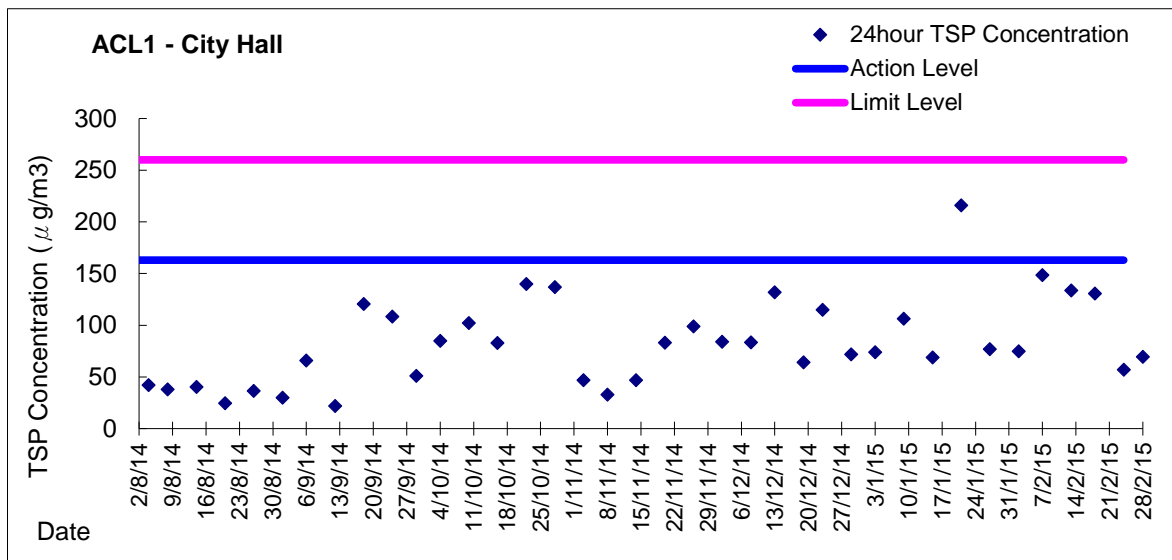




Graphic Presentation of 1 hour TSP Result

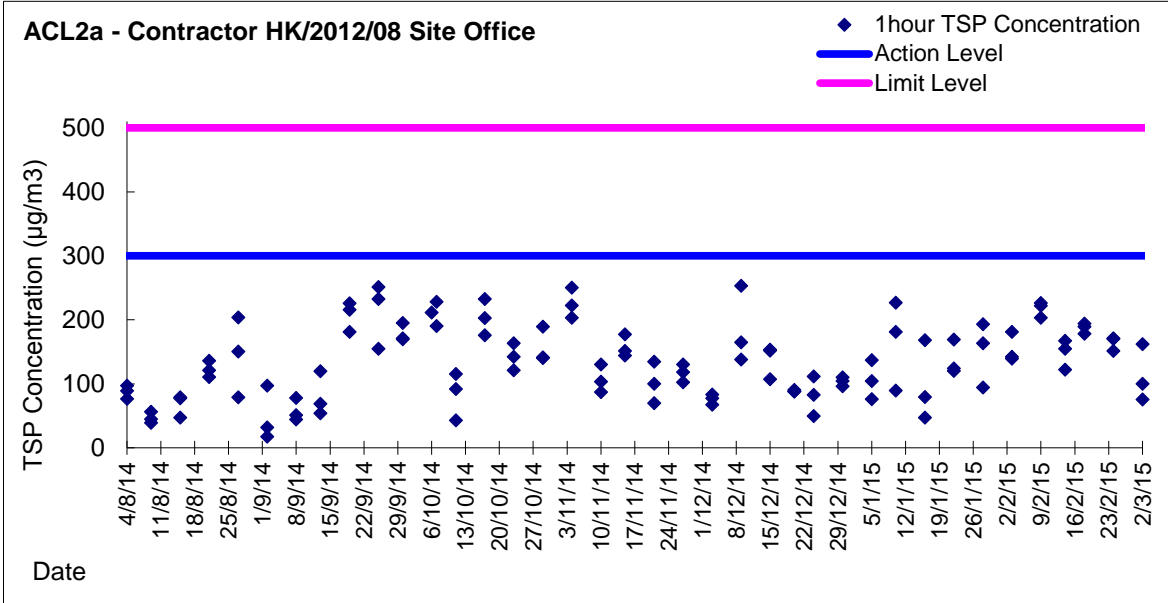

Graphic Presentation of 24 hour TSP Result

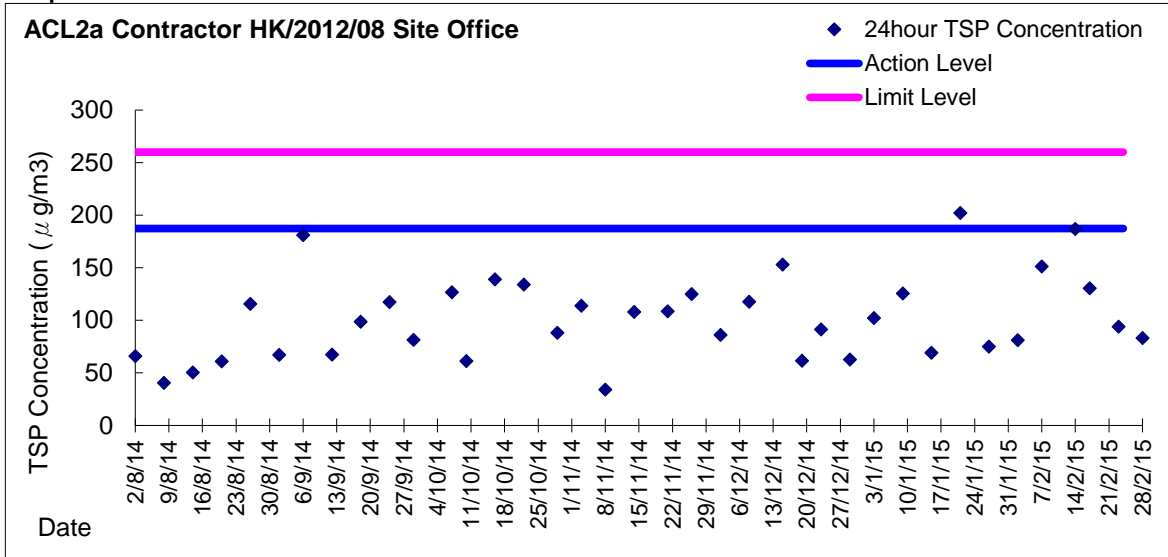



***Appendix 5.4***

***Water Quality Monitoring Results and Graphical Presentations***





**Water Monitoring Result at M5B - Central Cooling Water Intake Group  
Mid-Flood Tide**

Date	Time	Weather Condition	Sampling Depth m	Water Temperature °C		pH		Salinity ppt		DO Saturation %		DO mg/L		Turbidity NTU		Suspended Solids mg/L								
				Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average							
2/2/15	16:40	Fine	Middle	3.5	17.50	17.50	17.60	8.11	8.11	8.11	31.61	31.61	31.60	93.3	93.3	92.8	7.36	7.36	7.31	3.33	3.34	3.42	9	9.00
	16:42		Middle	3.5	17.70	17.70	17.60	8.11	8.11	8.11	31.59	31.59	31.60	92.7	91.8	92.8	7.27	7.23	7.31	3.47	3.55	3.42	9	
5/2/15	18:42	Cloudy	Middle	3.5	16.00	16.00	15.95	7.82	7.82	7.82	31.74	31.74	31.75	82.3	82.6	82.7	6.71	6.73	6.74	5.77	5.84	5.70	6	5.50
	18:43		Middle	3.5	15.90	15.90	15.95	7.82	7.82	7.82	31.75	31.75	31.75	83.0	82.9	82.7	6.77	6.75	6.74	5.63	5.56	5.70	5	
7/2/15	20:19	Cloudy	Middle	3.5	16.70	16.70	16.70	7.78	7.78	7.78	30.98	30.98	30.75	78.1	79.9	78.1	6.79	6.80	6.73	5.88	5.65	5.64	4	5.00
	20:20		Middle	3.5	16.70	16.70	16.70	7.78	7.78	7.78	30.51	30.51	30.75	78.0	76.2	78.1	6.77	6.55	6.73	5.54	5.49	5.64	6	
9/2/15	19:41	Cloudy	Middle	3.5	16.10	16.10	16.15	8.01	8.01	8.01	31.69	31.93	31.90	85.0	85.6	85.2	6.88	6.92	6.89	7.73	7.71	7.69	9	8.50
	19:42		Middle	3.5	16.20	16.20	16.15	8.00	8.00	8.01	31.97	32.01	31.90	85.2	85.0	85.2	6.89	6.88	6.89	7.69	7.63	7.69	8	
11/2/15	11:15	Fine	Middle	3.0	17.60	17.60	17.70	8.03	8.03	8.03	31.52	31.52	31.52	81.3	82.2	82.0	6.42	6.49	6.47	5.15	5.12	5.13	6	6.00
	11:17		Middle	3.0	17.80	17.80	17.70	8.03	8.03	8.03	31.52	31.52	31.52	82.3	82.0	82.0	6.50	6.48	6.47	5.11	5.14	5.13	6	
13/2/15	13:42	Fine	Middle	3.5	17.80	17.80	17.80	8.00	8.00	8.01	31.32	31.32	31.34	81.4	82.2	81.6	6.43	6.49	6.44	3.51	3.49	3.50	6	6.00
	13:44		Middle	3.5	17.80	17.80	17.80	8.01	8.01	8.01	31.35	31.35	31.34	81.4	81.3	81.6	6.43	6.42	6.44	3.49	3.50	3.50	6	
16/2/15	14:09	Cloudy	Middle	3.0	18.30	18.30	18.35	8.06	8.06	8.06	31.39	31.39	31.39	83.9	85.0	84.7	6.54	6.62	6.60	3.31	3.30	3.30	5	4.50
	14:11		Middle	3.0	18.30	18.50	18.35	8.06	8.06	8.06	31.39	31.39	31.39	85.2	84.7	84.7	6.63	6.59	6.60	3.29	3.29	3.30	4	
18/2/15	15:04	Fine	Middle	3.0	17.80	17.80	18.00	8.12	8.12	8.12	31.42	31.42	31.42	89.5	88.5	88.3	7.00	6.92	6.88	3.79	3.79	3.78	4	4.00
	15:06		Middle	3.0	18.20	18.20	18.00	8.12	8.12	8.12	31.41	31.41	31.42	88.2	87.1	88.3	6.89	6.71	6.88	3.78	3.76	3.78	4	
24/2/15	7:08	Fine	Middle	3.0	17.90	17.90	17.95	8.12	8.12	8.12	31.14	31.14	31.15	71.1	71.2	71.1	5.59	5.61	5.59	6.42	6.38	6.39	5	5.00
	7:09		Middle	3.0	18.00	18.00	17.95	8.12	8.12	8.12	31.15	31.15	31.15	71.2	70.9	71.1	5.60	5.57	5.59	6.36	6.38	6.39	5	
26/2/15	11:19	Fine	Middle	3.0	18.80	18.80	18.85	8.10	8.10	8.10	31.42	31.42	31.40	75.9	74.6	73.8	5.86	5.76	5.70	5.67	5.64	5.63	5	6.00
	11:21		Middle	3.0	18.90	18.90	18.85	8.10	8.10	8.10	31.38	31.38	31.40	73.5	71.3	73.8	5.67	5.50	5.70	5.61	5.60	5.63	7	
28/2/15	10:10	Cloudy	Middle	3.0	18.10	18.10	18.10	8.25	8.25	8.26	32.19	32.19	32.18	85.2	85.8	85.6	6.64	6.68	6.66	4.16	4.18	4.22	5	5.50
	10:12		Middle	3.0	18.10	18.10	18.10	8.26	8.26	8.26	32.16	32.16	32.18	85.0	86.2	85.6	6.62	6.71	6.66	4.27	4.28	4.22	6	

Remarks:

Single underline denotes exceedance over Action Level.

Double underline denotes exceedance over Limit Level.

With respect to the suspension of marine construction activities under the contract during Chinese New Year Holiday, the water quality monitoring event on 20 February 2015 during flood tide and ebb tide were temporarily suspended.



**Water Monitoring Result at M5B - Central Colling Water Intake Group  
Mid-Ebb Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature			pH			Salinity		DO Saturation		DO		Turbidity		Suspended Solids					
					°C		-		ppt		%		mg/L		NTU		mg/L							
					Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average				
3/2/15	1:51	Cloudy	Middle	3.0	16.50	16.50	16.55	7.95	7.95	7.95	31.47	31.47	31.44	95.0	94.5	96.2	7.66	7.62	7.76	5.16	5.26	5.19	6	6.50
	1:52		Middle	3.0	16.60	16.60		7.95	7.95		31.40	31.40		97.9	97.5		7.89	7.86		5.20	5.13		7	
5/2/15	13:32	Fine	Middle	3.5	17.00	17.00	17.05	8.12	8.12	8.12	31.53	31.53	31.54	88.6	88.7	88.4	7.07	7.07	7.05	3.73	3.72	3.72	4	3.50
	13:34		Middle	3.5	17.10	17.10		8.12	8.12		31.54	31.54		88.1	88.0		7.03	7.02		3.72	3.72		3	
7/2/15	13:35	Fine	Middle	3.0	16.90	16.90	16.95	8.16	8.16	8.16	31.64	31.64	31.64	89.8	90.1	89.9	7.18	7.19	7.18	4.11	4.13	4.11	6	6.00
	13:37		Middle	3.0	17.00	17.00		8.16	8.16		31.63	31.63		89.6	90.0		7.16	7.18		4.11	4.09		6	
9/2/15	13:55	Fine	Middle	3.0	17.00	17.00	17.05	8.13	8.13	8.13	31.61	31.61	31.62	87.4	87.9	87.7	6.97	7.00	6.99	4.98	4.97	5.00	5	5.50
	13:57		Middle	3.0	17.10	17.10		8.13	8.13		31.62	31.62		87.5	88.0		6.98	7.01		4.99	5.05		6	
11/2/15	16:00	Fine	Middle	3.5	16.90	16.90	16.95	8.05	8.05	8.05	31.53	31.53	31.52	81.7	81.8	81.7	6.54	6.54	6.54	2.47	2.45	2.44	4	4.00
	16:02		Middle	3.5	17.00	17.00		8.05	8.05		31.51	31.51		81.5	81.8		6.52	6.54		2.43	2.40		4	
13/2/15	19:44	Cloudy	Middle	3.5	16.80	16.80	16.80	7.80	7.80	7.80	31.64	31.63	31.77	82.5	83.2	82.6	6.59	6.65	6.60	3.97	3.92	3.91	7	6.50
	19:45		Middle	3.5	16.80	16.80		7.80	7.80		31.91	31.91		82.5	82.0		6.59	6.56		3.89	3.84		6	
16/2/15	0:32	Foggy	Middle	3.0	18.30	18.30	18.30	7.82	7.82	7.82	31.76	31.76	31.76	78.7	79.9	79.7	6.12	6.22	6.20	7.01	6.99	6.98	6	6.50
	0:33		Middle	3.0	18.30	18.30		7.82	7.82		31.76	31.76		80.2	80.1		6.24	6.23		6.96	6.94		7	
18/2/15	11:36	Fine	Middle	3.0	17.50	17.50	17.50	8.19	8.19	8.19	31.74	31.74	31.75	89.6	89.2	89.5	7.06	7.07	7.06	4.11	4.12	4.13	4	4.00
	11:37		Middle	3.0	17.50	17.50		8.19	8.19		31.76	31.76		89.9	89.1		7.08	7.02		4.14	4.16		4	
24/2/15	16:02	Fine	Middle	3.0	19.10	19.10	19.15	8.10	8.10	8.10	31.46	31.46	31.43	75.5	74.7	74.6	5.80	5.73	5.71	4.22	4.22	4.22	4	4.50
	16:04		Middle	3.0	19.20	19.20		8.10	8.10		31.40	31.40		74.3	73.8		5.71	5.61		4.22	4.23		5	
26/2/15	18:58	Cloudy	Middle	3.5	20.10	20.10	20.15	7.77	7.77	7.78	31.56	31.59	31.72	83.6	84.2	83.8	6.28	6.32	6.29	5.13	5.10	5.03	4	5.00
	18:59		Middle	3.5	20.20	20.20		7.78	7.78		31.87	31.87		83.8	83.5		6.30	6.27		5.08	4.81		6	
28/2/15	20:01	Cloudy	Middle	3.5	19.30	19.30	19.35	7.80	7.80	7.81	32.75	32.75	32.75	82.4	83.3	82.6	6.26	6.32	6.27	3.93	3.90	3.89	5	6.00
	20:02		Middle	3.5	19.40	19.40		7.81	7.81		32.75	32.75		82.5	82.2		6.25	6.23		3.95	3.79		7	

Remarks:  
 Single underline denotes exceedance over Action Level.  
 Double underline denotes exceedance over Limit Level.  
 With respect the suspension of marine construction activities under the contract during Chinese New Year Holiday, the water quality monitoring event on 20 February 2015 during flood tide and ebb tide were temporarily suspended.



**Water Monitoring Result at Culvert J - Reference Station  
Mid-Flood Tide**

Date	Time	Weather Condition	Sampling Depth m	Water Temperature °C		pH		Salinity ppt		DO Saturation %		DO mg/L		Turbidity NTU		Suspended Solids mg/L								
				Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average							
2/2/15	16:45	Fine	Middle	3.0	17.50	17.50	17.45	8.03	8.03	8.03	28.77	28.77	28.77	77.3	77.8	77.4	6.24	6.27	6.24	8.33	8.27	8.26	6	5.50
	16:47		Middle	3.0	17.40	17.40		8.03	8.03		28.77	28.77		77.3	77.0		6.24	6.21		8.23	8.19		5	
5/2/15	18:50	Cloudy	Middle	3.0	16.00	16.00	16.00	7.85	7.85	7.85	28.90	28.90	28.90	74.8	76.3	75.5	6.20	6.32	6.25	10.53	10.50	10.48	9	8.50
	18:51		Middle	3.0	16.00	16.00		7.85	7.85		28.90	28.90		75.7	75.0		6.27	6.22		10.48	10.41		8	
7/2/15	20:27	Cloudy	Middle	3.0	16.80	16.80	16.80	7.85	7.85	7.85	28.79	28.79	28.78	63.1	63.4	63.0	5.24	5.27	5.24	12.50	12.03	11.89	6	6.50
	20:28		Middle	3.0	16.80	16.80		7.84	7.84		28.77	28.77		62.3	63.1		5.20	5.25		11.64	11.40		7	
9/2/15	16:50	Cloudy	Middle	3.0	16.10	16.20	16.18	8.02	8.02	8.02	31.60	31.61	31.65	80.4	80.9	81.2	6.52	6.56	6.58	8.48	8.52	8.55	11	11.00
	16:51		Middle	3.0	16.20	16.20		8.02	8.02		31.71	31.69		81.8	81.6		6.63	6.61		8.56	8.65		11	
11/2/15	11:20	Fine	Middle	3.0	17.00	17.00	17.05	8.07	8.07	8.07	31.23	31.23	31.23	83.7	83.6	83.6	6.70	6.70	6.70	4.25	4.29	4.29	6	5.50
	11:22		Middle	3.0	17.10	17.10		8.07	8.07		31.23	31.23		83.8	83.4		6.71	6.67		4.31	4.30		5	
13/2/15	13:35	Fine	Middle	3.0	18.20	18.20	18.30	7.91	7.91	7.91	29.59	29.59	29.58	73.4	74.4	74.3	5.79	5.86	5.85	3.37	3.37	3.37	7	6.50
	13:37		Middle	3.0	18.40	18.40		7.91	7.91		29.57	29.57		74.4	74.8		5.85	5.89		3.37	3.38		6	
16/2/15	14:03	Cloudy	Middle	2.5	18.80	18.80	18.85	8.02	8.02	8.02	30.46	30.46	30.45	81.2	81.2	80.8	6.28	6.27	6.25	6.04	5.94	5.96	5	5.50
	14:05		Middle	2.5	18.90	18.90		8.02	8.02		30.44	30.44		80.5	80.3		6.22	6.21		5.93	5.93		6	
18/2/15	15:10	Fine	Middle	3.0	17.70	17.70	17.80	8.11	8.11	8.11	31.27	31.27	31.27	77.0	77.7	77.7	6.07	6.12	6.12	3.82	3.79	3.70	4	3.50
	15:12		Middle	3.0	17.90	17.90		8.11	8.11		31.26	31.26		77.9	78.1		6.13	6.15		3.64	3.54		3	
24/2/15	7:05	Fine	Middle	3.0	18.00	18.00	18.00	8.05	8.05	8.05	29.38	29.38	29.38	61.7	61.2	61.3	4.90	4.86	4.87	8.16	8.15	8.22	7	6.50
	7:07		Middle	3.0	18.00	18.00		8.04	8.04		29.38	29.38		61.3	60.8		4.87	4.83		8.28	8.30		6	
26/2/15	11:15	Fine	Middle	3.0	19.10	19.20	19.23	8.07	8.07	8.07	31.08	31.08	31.05	72.5	70.7	70.8	5.57	5.43	5.43	7.01	6.97	6.89	7	7.50
	11:17		Middle	3.0	19.30	19.30		8.07	8.07		31.02	31.02		69.5	70.5		5.33	5.40		6.76	6.82		8	
28/2/15	10:05	Cloudy	Middle	2.5	18.40	18.40	18.50	8.14	8.14	8.14	29.99	29.99	29.99	77.7	77.1	77.0	6.09	6.04	6.03	7.64	7.61	7.61	7	7.50
	10:07		Middle	2.5	18.60	18.60		8.14	8.14		29.98	29.98		76.5	76.8		5.99	6.01		7.60	7.58		8	

With respect the suspension of marine construction activities under the contract during Chinese New Year Holiday, the water quality monitoring event on 20 February 2015 during flood tide and ebb tide were temporarily suspended.






**Water Monitoring Result at Culvert J - Reference Station  
Mid-Ebb Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature			pH			Salinity		DO Saturation		DO		Turbidity		Suspended Solids					
					°C		-		ppt		%		mg/L		NTU		mg/L							
					Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average				
3/2/15	2:04	Cloudy	Middle	3	16.60	16.60	16.60	7.97	7.97	7.97	30.24	30.24	30.25	84.7	84.8	85.1	6.87	6.88	6.90	6.82	6.23	6.52	7	7.00
	2:05		Middle	3	16.60	16.60		7.97	7.97		30.25	30.25		85.5	85.4		6.93	6.92		6.49	6.53		7	
5/2/15	13:25	Fine	Middle	3	17.10	17.10	17.10	7.99	7.99	7.99	29.01	29.01	29.01	67.8	68.0	68.0	5.48	5.50	5.50	9.08	9.10	9.20	8	8.00
	13:27		Middle	3	17.10	17.10		7.99	7.99		29.01	29.01		68.1	67.9		5.51	5.49		9.22	9.40		8	
7/2/15	12:30	Fine	Middle	3	17.10	17.10	17.15	8.15	8.15	8.15	31.62	31.62	31.62	85.4	85.9	85.6	6.81	6.84	6.82	4.34	4.29	4.28	6	6.00
	12:32		Middle	3	17.20	17.20		8.15	8.15		31.62	31.62		85.6	85.4		6.82	6.80		4.25	4.24		6	
9/2/15	13:50	Fine	Middle	3	17.10	17.10	17.15	8.10	8.10	8.10	31.10	31.10	31.10	82.0	82.0	81.7	6.55	6.55	6.52	5.69	5.65	5.68	8	7.50
	13:52		Middle	3	17.20	17.20		8.10	8.10		31.10	31.10		81.4	81.3		6.48	6.48		5.66	5.72		7	
11/2/15	15:56	Fine	Middle	4	17.50	17.50	17.50	8.04	8.04	8.05	31.43	31.43	31.44	80.9	79.6	79.2	6.41	6.30	6.27	2.93	2.92	2.92	5	4.50
	15:58		Middle	4	17.50	17.50		8.05	8.05		31.44	31.44		78.0	78.1		6.18	6.19		2.90	2.91		4	
13/2/15	19:52	Cloudy	Middle	3	17.00	17.00	17.00	7.86	7.86	7.86	29.07	29.07	29.08	63.0	62.2	62.4	5.12	5.05	5.07	10.02	9.96	10.01	9	9.00
	19:53		Middle	3	17.00	17.00		7.86	7.86		29.08	29.08		62.3	62.2		5.06	5.05		10.05	10.01		9	
16/2/15	0:44	Foggy	Middle	3	18.20	18.20	18.25	7.89	7.89	7.89	25.76	25.76	25.76	42.8	43.5	43.5	3.45	3.51	3.51	18.19	18.03	18.04	14	13.50
	0:45		Middle	3	18.30	18.30		7.88	7.88		25.75	25.75		43.9	43.7		3.54	3.52		17.98	17.96		13	
18/2/15	11:30	Fine	Middle	3	17.40	17.40	17.40	8.16	8.16	8.16	30.99	30.99	31.09	80.7	81.0	80.9	6.41	6.43	6.44	6.42	6.41	6.43	3	4.00
	11:32		Middle	3	17.40	17.40		8.16	8.16		31.19	31.19		80.9	81.0		6.47	6.43		6.44	6.44		5	
24/2/15	16:06	Fine	Middle	3	18.80	18.80	18.85	7.96	7.96	7.96	27.02	27.02	27.01	56.6	56.2	56.0	4.49	4.46	4.44	14.39	14.21	14.16	6	6.50
	16:08		Middle	3	18.90	18.90		7.95	7.95		27.00	26.99		55.9	55.3		4.43	4.38		14.02	14.00		7	
26/2/15	19:09	Cloudy	Middle	3	20.00	20.00	20.05	7.80	7.80	7.80	30.06	30.06	30.06	66.0	65.9	66.1	5.02	5.01	5.03	8.39	8.47	8.32	6	6.00
	19:10		Middle	3	20.10	20.10		7.79	7.79		30.06	30.06		66.1	66.4		5.03	5.05		8.24	8.16		6	
28/2/15	20:10	Cloudy	Middle	3	19.50	19.50	19.50	7.89	7.89	7.89	29.93	29.93	29.93	62.5	63.9	62.5	4.81	4.92	4.81	8.35	8.29	8.24	6	6.50
	20:11		Middle	3	19.50	19.50		7.89	7.89		29.93	29.93		61.3	62.3		4.72	4.79		8.24	8.09		7	

With respect to the suspension of marine construction activities under the contract during Chinese New Year Holiday, the water quality monitoring event on 20 February 2015 during flood tide and ebb tide were temporarily suspended.






### Graphic Presentation of Water Quality Result of M5B - Central Cooling Water Intake Groups

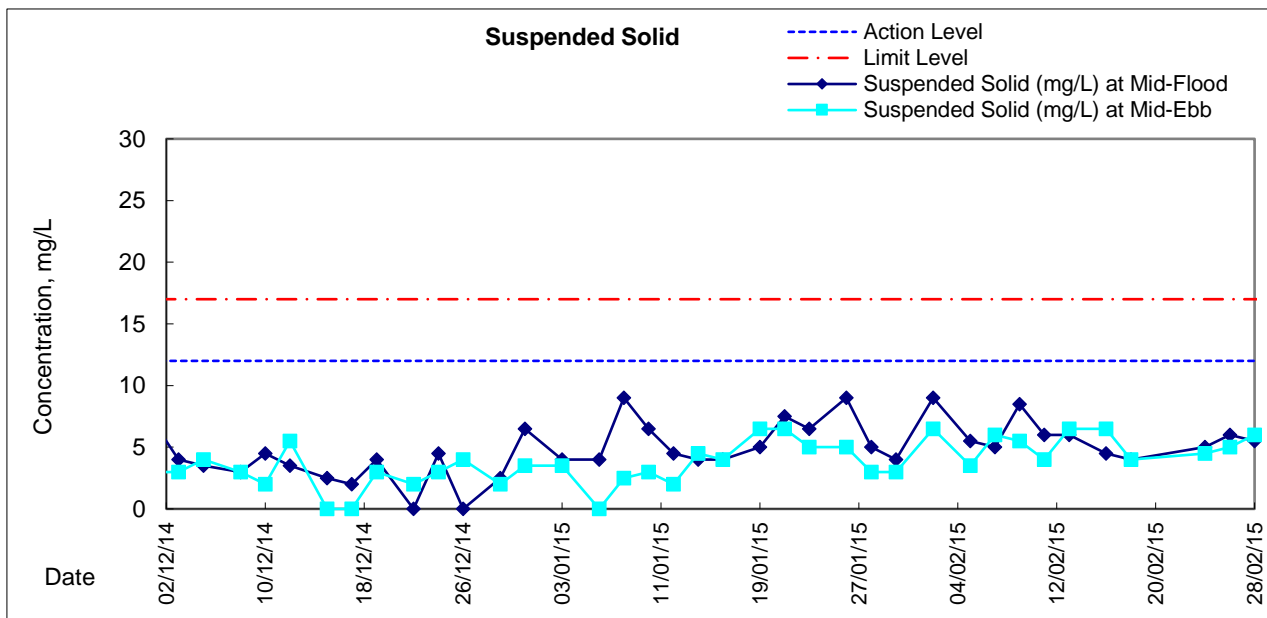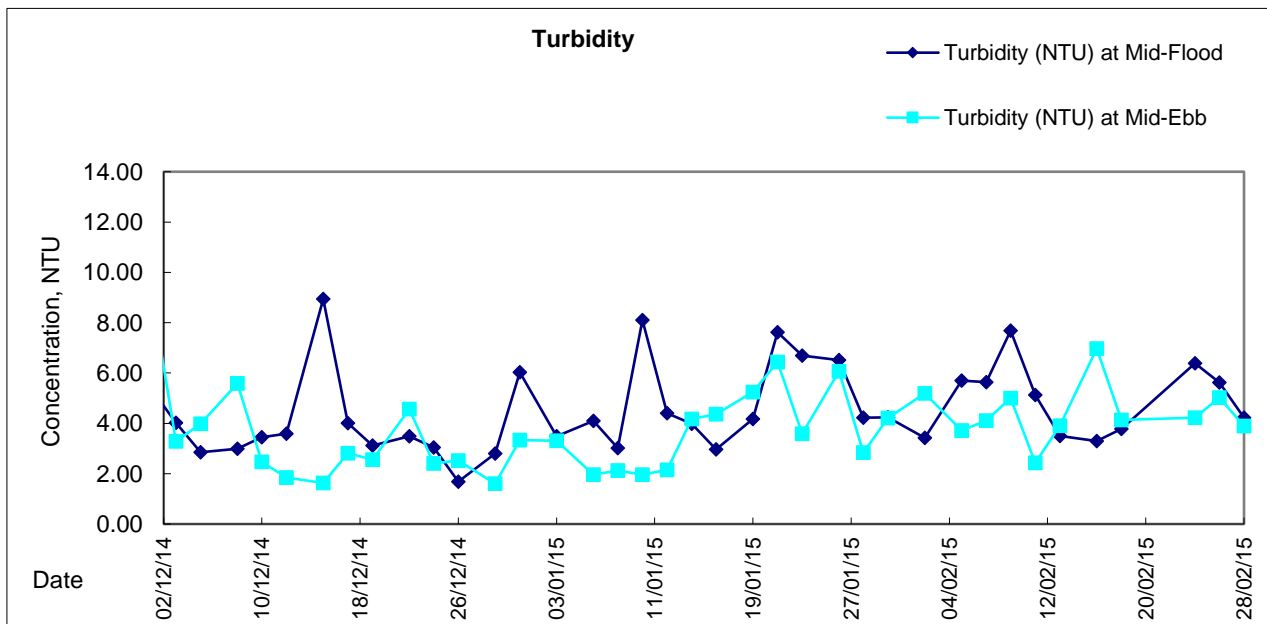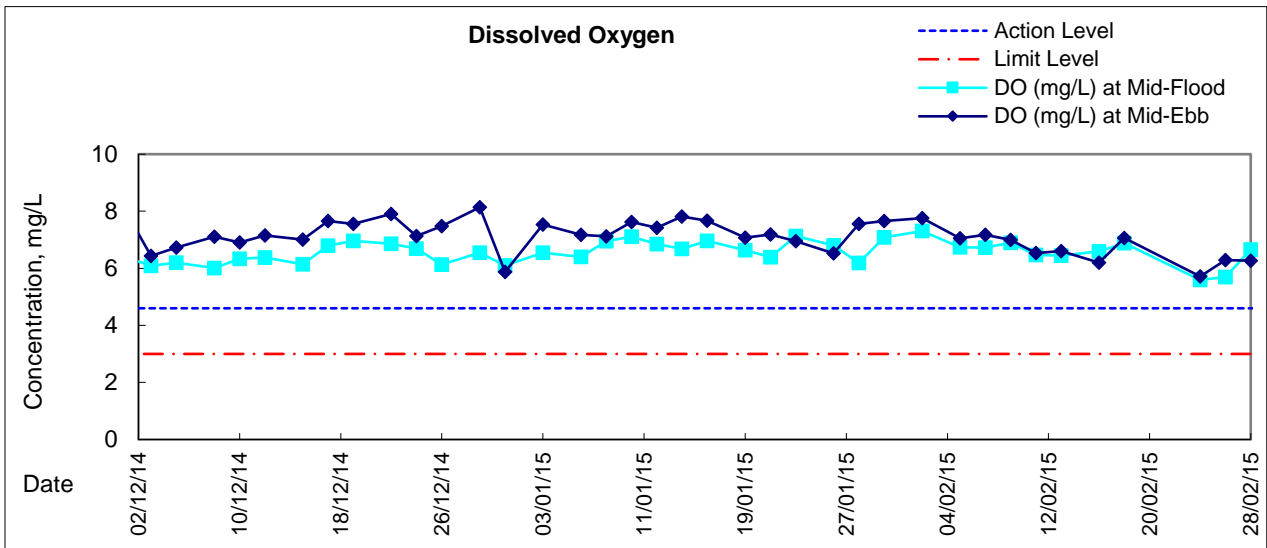



# Graphic Presentation of Water Quality Result of Culvert J - Reference Station

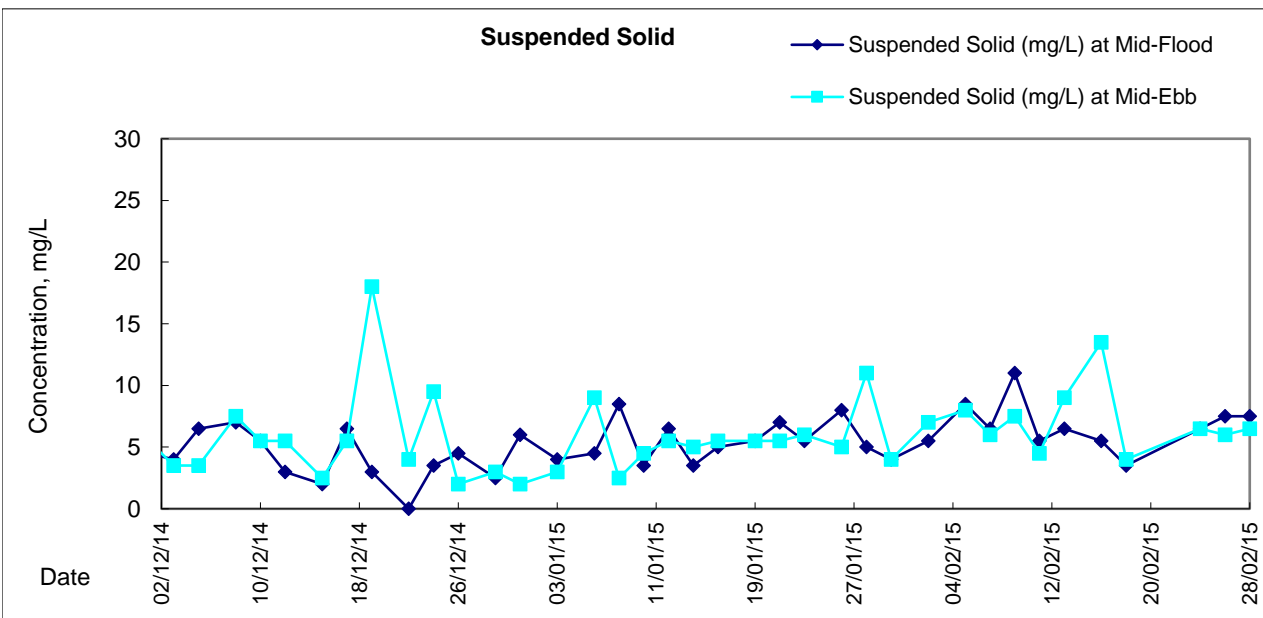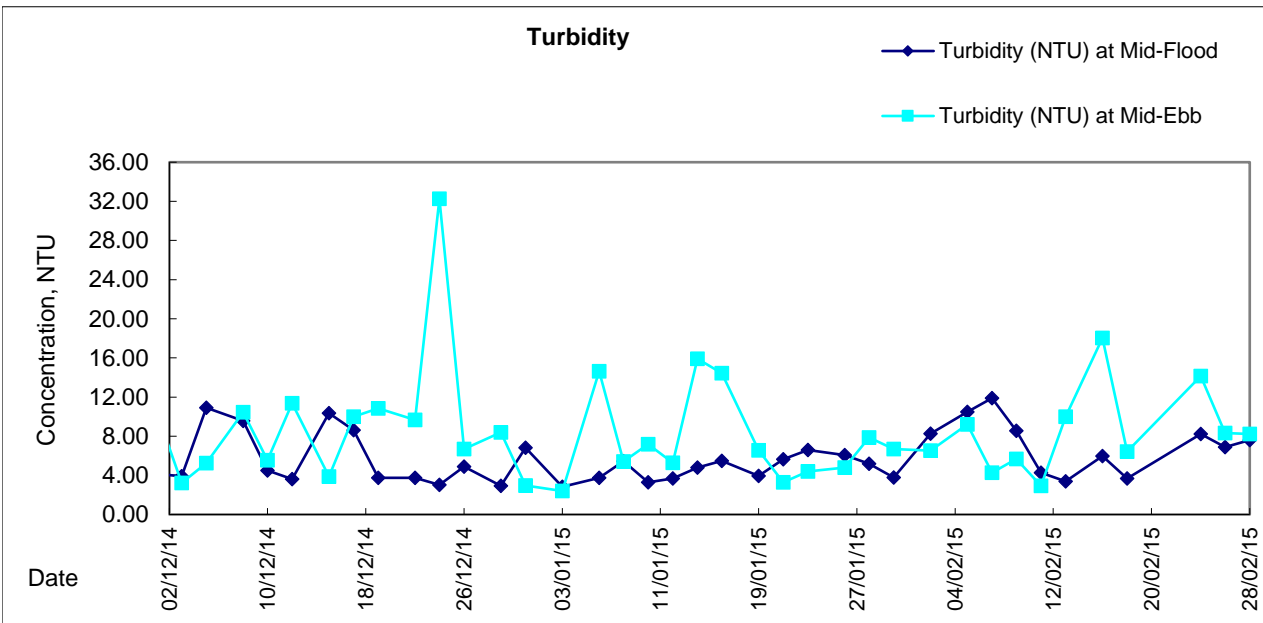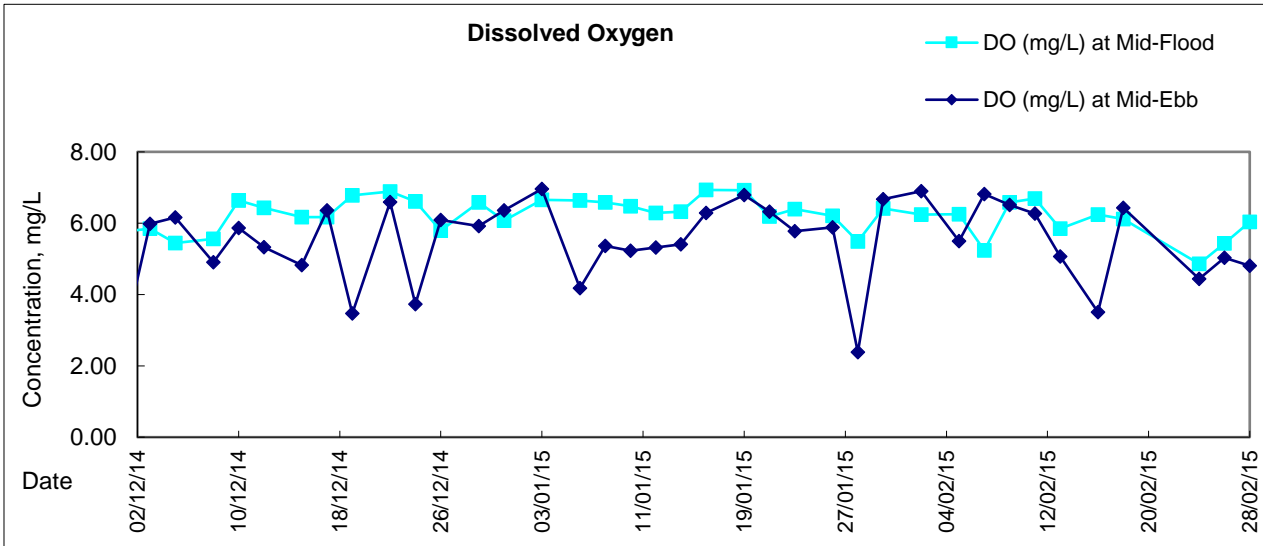



***Appendix 6.1***

***Event Action Plans***



Central Reclamation Phase III : Environmental Monitoring and Audit - Event and Action Plan for Air and Noise Quality

Event and Action Plan for Air Quality				
Event	Action			
	ET Leader	IC(E)	ER	Contractor
Action Level - Exceedance for one sample	<ol style="list-style-type: none"> <li>Identify source</li> <li>Inform IC(E) and ER</li> <li>Repeat measurement to confirm finding</li> <li>Increase monitoring frequency to daily</li> </ol>	<ol style="list-style-type: none"> <li>Check monitoring data submitted by ET</li> <li>Check Contractor's working method</li> </ol>	<ol style="list-style-type: none"> <li>Notify Contractor</li> </ol>	<ol style="list-style-type: none"> <li>Rectify any unacceptable practice</li> <li>Amend working methods if appropriate</li> </ol>
Action Level - Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> <li>Identify source</li> <li>Inform IC(E) and ER</li> <li>Repeat measurement to confirm finding</li> <li>Increase monitoring frequency to daily</li> <li>Discuss with IC(E) and Contractor on remedial actions</li> <li>If exceedance continues, arrange meeting with IC(E) and ER</li> <li>If exceedance stops cease additional monitoring</li> </ol>	<ol style="list-style-type: none"> <li>Check monitoring data submitted by ET</li> <li>Check Contractor's working method</li> <li>Discuss with ET and Contractor on possible remedial measures</li> <li>Advise the ER on the effectiveness of the proposed remedial measures</li> <li>Supervise the implementation of remedial measures</li> </ol>	<ol style="list-style-type: none"> <li>Confirm receipt of notification of failure in writing</li> <li>Notify Contractor</li> <li>Ensure remedial measures properly implemented</li> </ol>	<ol style="list-style-type: none"> <li>Submit proposals for remedial actions to IC(E) within 3 working days of notification</li> <li>Implement the agreed proposals</li> <li>Amend proposal if appropriate</li> </ol>
Limit Level - Exceedance for one sample	<ol style="list-style-type: none"> <li>Identify source</li> <li>Inform ER and EPD</li> <li>Repeat measurement to confirm findings</li> <li>Increase monitoring frequency to daily</li> <li>Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results</li> </ol>	<ol style="list-style-type: none"> <li>Check monitoring data submitted by ET</li> <li>Check Contractor's working method</li> <li>Discuss with ET and Contractor on possible remedial measures</li> <li>Advise the ER on the effectiveness of the proposed remedial measures</li> <li>Supervise the implementation of remedial measures</li> </ol>	<ol style="list-style-type: none"> <li>Confirm receipt of notification of failure in writing</li> <li>Notify Contractor</li> <li>Ensure remedial measures properly implemented</li> </ol>	<ol style="list-style-type: none"> <li>Take immediate action to avoid further exceedance</li> <li>Submit proposal for remedial actions to IC(E) within 3 working days of notification</li> <li>Implement the agreed measures</li> </ol>
Limit Level - Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> <li>Notify IC(E), ER, Contractor and EPD</li> <li>Identify source</li> <li>Repeat measurements to confirm findings</li> <li>Increase monitoring frequency to daily</li> <li>Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented</li> <li>Arrange meeting with IC(E) and ER to discuss the remedial actions to be taken</li> <li>Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results</li> <li>If exceedance stops, cease additional monitoring</li> </ol>	<ol style="list-style-type: none"> <li>Discuss amongst ER, ET, and Contractor on the potential remedial actions</li> <li>Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly</li> <li>Supervise the implementation of remedial measures</li> </ol>	<ol style="list-style-type: none"> <li>Confirm receipt of notification of failure in writing</li> <li>Notify Contractor</li> <li>In consultation with the IC(E), agree with the Contractor on the remedial measures to be implemented</li> <li>Ensure remedial measures properly implemented</li> <li>If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated</li> </ol>	<ol style="list-style-type: none"> <li>Take immediate action to avoid further exceedance</li> <li>Submit proposals for remedial actions to IC(E) within 3 working days of notification</li> <li>Implement the agreed proposals</li> <li>Resubmit proposals if problem still not under control</li> <li>Stop the relevant portion of works as determined by the ER until the exceedance is abated</li> </ol>

Central Reclamation Phase III : Environmental Monitoring and Audit - Event and Action Plan for Air and Noise Quality

Event and Action Plan for Noise Quality				
Event	Action			
	ET Leader	IC(E)	ER	Contractor
Action Level is reached	<ol style="list-style-type: none"> <li>1. Notify IC(E) and Contractor</li> <li>2. Carry out investigation</li> <li>3. Report the results of the investigation to the IC(E) and Contractor</li> <li>4. Discuss with the Contractor and formulate remedial measures</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss amongst ER, ET and Contractor on the potential remedial actions</li> <li>2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly</li> <li>3. Supervise the implementation of remedial measures</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing</li> <li>2. Notify Contractor</li> <li>3. Require Contractor to propose remedial measures for the analyzed noise problem</li> <li>4. Ensure remedial measures are properly implemented</li> </ol>	<ol style="list-style-type: none"> <li>1. Submit noise mitigation proposal to IC(E)</li> <li>2. Implement noise mitigation proposals</li> </ol>
Limit Level is reached	<ol style="list-style-type: none"> <li>1. Notify IC(E), ER, EPD and Contractor</li> <li>2. Identify source</li> <li>3. Repeat measurement to confirm findings</li> <li>4. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented</li> <li>5. Inform IC(E), ER and EPD the causes &amp; actions taken for the exceedances</li> <li>6. Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results</li> <li>7. If exceedance stops cease additional monitoring</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss amongst ER, ET and Contractor on the potential remedial actions</li> <li>2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly</li> <li>3. Supervise the implementation of remedial measures</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing</li> <li>2. Notify Contractor</li> <li>3. Require Contractor to propose remedial measures for the analyzed noise problem</li> <li>4. Ensure remedial measures are properly implemented</li> <li>5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion or work until the exceedance is abated</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance</li> <li>2. Submit proposals for remedial actions to IC(E) within 3 working days of notification</li> <li>3. Implement the agreed proposals</li> <li>4. Resubmit proposals if problem still not under control</li> <li>5. Stop the relevant portion of works as determined by the ER until the exceedance is abated</li> </ol>



EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action level being exceeded by one sampling day	Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next day of exceedance.	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)
Action level being exceeded by more than one consecutive sampling days	Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; Ensure mitigation measures are implemented; Prepare to increase the monitoring frequency to daily; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next working day of exceedance.	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)



EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Limit level being exceeded by one sampling day	<p>Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC, contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level. (The above actions should be taken within 1 working day after the exceedance is identified)</p>	<p>Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)</p>	<p>Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)</p>	<p>Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET , IEC and ER and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)</p>
Limit level being exceeded by more than one consecutive sampling days	<p>Identify source(s) of impact; Inform IEC, contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days. (The above actions should be taken within 1 working day after the exceedance is identified)</p>	<p>Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)</p>	<p>Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures; Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit level. (The above actions should be taken within 1 working day after the exceedance is identified)</p>	<p>Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET , IEC and ER and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures; As directed by the Engineer, to slow down or to stop all or part of the marine work or construction activities. (The above actions should be taken within 1 working day after the exceedance is identified)</p>



***Appendix 6.2***

***Summary for Notification of Exceedance***



Ref no.	Date	Time	Location	Parameters (Unit)	Measured	Action Level	Limit Level	Follow-up action



***Appendix 9.1***

***Complaint Log***





### Environmental Complaints Log

Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
150211	21/1/2015	EPD complaint (EPD Ref.: H04/RS/0001716-15) received by ET on 11 February 2015	Construction site opposite to CITIC Tower	Construction dust was emitted from a construction site opposite to CITIC Tower	<p>According to the relevant site records, trench grabbing for D-wall construction and socket H-pile construction were conducted at the concerned location on 21 January 2015. Dust screen for socket H-pile construction, maintenance of site haul road in wet condition and water spraying at vehicle entrance/exit points of HK/2012/08 Contractor site office and Portion I were implemented by the Contractor of HK/2012/08 near the concerned location on 21 January 2015.</p> <p>In addition, no environmental deficiency related to dust mitigation was identified at the concerned location during weekly environmental inspections conducted on 27 Jan, 3 and 10 Feb 2015 and dust mitigation measures including water spraying for dusty haul road and provision of wheel washing were in place and no dust related impact from the construction works at the concerned location was observed.</p> <p>Meanwhile, the Air Quality Health Index (AQHI) recorded by EPD across Western District and Eastern District on 21 January 2015 was ranged from 4 to 10+ indicating a severely high concentration of ambient air pollutants. Based on reviewing relevant impact monitoring data, elevated TSP were recorded at monitoring stations across Central to Wan Chai West area despite a non-Project related exceedance was recorded at nearby monitoring station ACL2a (Contractor HK/2012/08 Site Office) on 21 January 2015 and was considered to be contributed by ambient air pollutant.</p> <p>The site condition under Contract HK/2012/08 at the concerned location was considered to be generally satisfactory and no non-conformity related to cumulative air quality impact was observed at the concerned location. Nevertheless, in view of the public concern, the contractor was reminded to enhance the dust mitigation measures implemented to minimize potential nuisance to nearby public.</p>	Closed



***Appendix 10.1***

***Construction Programme of Individual Contracts***

CEDD Contract No. HK/2012/08  
Wan Chai Development Phase II  
Central -Wan Chai Bypass at Wan Chai West

Activity ID	Activity Name	Start	Finish	Remaining Duration	Activity % Complete	2014		2015		
						Nov	Dec	Jan	Feb	Mar
<b>Total</b>		<b>24-Feb-14 A</b>	<b>18-May-15</b>	<b>132</b>						
<b>HK/2012/08 3M Rolling Programme ( Dec 2014 to Feb 2015) Based on Rev3/</b>		<b>24-Feb-14 A</b>	<b>18-May-15</b>	<b>132</b>						
<b>Dredging and Reclamation</b>		<b>02-May-14 A</b>	<b>17-Mar-15</b>	<b>84</b>						
<b>Marine Work Construction</b>		<b>02-May-14 A</b>	<b>17-Mar-15</b>	<b>84</b>						
<b>Dredging</b>		<b>02-May-14 A</b>	<b>17-Mar-15</b>	<b>84</b>						
<b>Dredging - Zone CRIII</b>		<b>02-May-14 A</b>	<b>17-Mar-15</b>	<b>84</b>						
<b>CRIII - Temporary Pipe Pile Wave Wall</b>		<b>02-May-14 A</b>	<b>25-Feb-15</b>	<b>67</b>						
LPCU31020	CRIII - temp pipe pile wall (1-213) - Order Materials for 610 dia. pipe pile [213nos. @750c/c]	02-May-14 A	07-Jan-15	30	40%					
MAR10040	CRIII - temp pipe pile wall (1-33) - install 610 dia. pipe pile [33nos. @750c/c]	16-Jan-15	25-Feb-15	30	0%					
MAR12340	CRIII - temp pipe pile wall (94-153) - install 610 dia. pipe pile [60nos. @750c/c]	18-Oct-14 A	13-Dec-14	12	70%					
MAR12360	CRIII - temp pipe pile wall (154-213) - install 610 dia. pipe pile [60nos. @750c/c]	18-Oct-14 A	16-Dec-14	14	65%					
<b>Dredging at Zone CRIII</b>		<b>06-Oct-14 A</b>	<b>17-Mar-15</b>	<b>84</b>						
MAR15020	Zone CRIII - 1st stage - Remove existing rock armour [F5-H5]	06-Oct-14 A	22-Jan-15	43	0%					
MAR15040	Zone CRIII - 1st stage - Excavate to expose L-shape wall [6 nos.]	17-Dec-14	23-Dec-14	6	0%					
MAR15060	Zone CRIII - 1st stage - demolish existing tie beam behind L-shape wall	20-Dec-14	30-Dec-14	7	0%					
MAR15080	Zone CRIII - 1st stage - further excavate to seawall founding level	31-Dec-14	09-Jan-15	8	0%					
MAR15100	Zone CRIII - 1st stage - demolish existing seawall [3 nos.]	10-Jan-15	27-Jan-15	15	0%					
MAR15120	Zone CRIII - 1st stage - Dredging to final formation level [G5-G7, H5-H6]	28-Jan-15	30-Jan-15	3	0%					
MAR15140	Zone CRIII - 1st stage - Final Hydrographic Survey	31-Jan-15	03-Feb-15	3	0%					
MAR16095	Zone CRIII - 2nd stage - Remove existing rock armour [B5-E5] after relocating interim landing steps	26-Feb-15	17-Mar-15	20	0%					
<b>Seawall Construction</b>		<b>04-Feb-15</b>	<b>27-Feb-15</b>	<b>16</b>						
<b>Seawall Construction - Zone CRIII</b>		<b>04-Feb-15</b>	<b>27-Feb-15</b>	<b>16</b>						
<b>Zone CRIII Seawall</b>		<b>04-Feb-15</b>	<b>27-Feb-15</b>	<b>16</b>						
MAR20620	Zone CRIII - fill rock mound for Seawall 2E	04-Feb-15	10-Feb-15	6	0%					
MAR20640	Zone CRIII - lay toe block and level stone for Seawall 2E	11-Feb-15	27-Feb-15	10	0%					
MAR20660	Zone CRIII - fill rock mound for Seawall 1B(1)	04-Feb-15	10-Feb-15	6	0%					
MAR20680	Zone CRIII - lay toe block and level stone for Seawall 1B(1)	11-Feb-15	24-Feb-15	7	0%					
<b>Works for Section Completion</b>		<b>24-Feb-14 A</b>	<b>18-May-15</b>	<b>132</b>						
<b>Construction</b>		<b>24-Feb-14 A</b>	<b>18-May-15</b>	<b>132</b>						
<b>Section II A - CWB Tunnel &amp; Slip Road Structures and Facilities</b>		<b>24-Feb-14 A</b>	<b>18-May-15</b>	<b>132</b>						
<b>CWB CRIII &amp; A1</b>		<b>24-Feb-14 A</b>	<b>18-May-15</b>	<b>132</b>						
<b>CWB CRIII &amp; A1 - Dwall and Pile Construction</b>		<b>24-Feb-14 A</b>	<b>28-Jan-15</b>	<b>47</b>						
SIIA10680	Sec II A - CWB CRIII - construct DWall and barrette (1.2m thk on rock)	24-Feb-14 A	31-Dec-14	25	81.48%					
SIIA10700	Sec II A - CWB CRIII - construct temporary DWall (1.2m thk)	28-Mar-14 A	31-Dec-14	25	75%					
SIIA10710	Sec II A - CWB CRIII - Construct pre-bored H-pile	01-Dec-14	12-Jan-15	34	0%					
SIIA10720	Sec II A - CWB CRIII - D-wall grout curtain / contact grout / fissure grout	01-Dec-14	19-Jan-15	40	0%					
SIIA10740	Sec II A - CWB CRIII - D-wall Sonic test / interface core	01-Dec-14	13-Jan-15	35	0%					
SIIA10760	Sec II A - CWB CRIII - install dewater/ recharge / observation well	13-Dec-14	14-Jan-15	25	0%					
SIIA10780	Sec II A - CWB CRIII - pumping test (CRIII, A1)	15-Jan-15	28-Jan-15	11	0%					
<b>CWB CRIII &amp; A1 - Tunnel Structure</b>		<b>24-Jan-15</b>	<b>18-May-15</b>	<b>88</b>						
SIIA10820	Sec II A - CWB CRIII: Shoring & Excavation	24-Jan-15	18-May-15	88	0%					

- █ Actual Work
- █ Remaining Work
- █ Critical Remain...
- ◆ Milestone

Project Star :22-Jan-13  
Project End: 21-Jul-18  
Date Date: 30-Nov-14

3 Month Rolling Programme (CRIII Area)

December 2014 to February 2015

Date	Revi...	Chec...	Approved
30-No...	3MRP		
