中國建築-利達聯營
CHINA STATE - LEADER JOINT VENTURE

CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West

Activity ID	Activity Name	Orig Dur	Early Start	Early Finish
HK/2012/08 Reviewed Works Programme - (Conforming) - Rev.0/1 23 Aug 2013				
Dredging and Reclamation				
Marine Work Construction				
Dredging				
Dredging - Zone CRIII				
CRIII - Temporary Diversion of Culvert K				
MAR15385	CRIII - temp diversion of culvert K - open cut excavation	7	02-Sep-13	09-Sep-13
MAR15387	CRIII - temp diversion of culvert K - construct temp. trench by placing concrete blocks	4	10-Sep-13	13-Sep-13
MAR15389	CRIII - temp diversion of culvert K - backfill	20	14-Sep-13	09-Oct-13
MAR15402	CRIII - temp diversion of culvert K - demolish wall & top slab and block up exist box culvert	7	10-Oct-13	18-Oct-13
MAR15404	CRIII - temp diversion of culvert K - demolish box sections above Dwall	10	19-Oct-13	30-Oct-13
Works for Section Completion				
Construction				
Section I - Interim Landing Steps and EVA				
Interim Landing Steps Construction				
SECI10480	Sec I - ILS - install s.s. handrail / tactile / sign board / bollard	6	19-Aug-13 A	26-Aug-13
SECI10500	Sec I - ILS - install vertical fender / step fender	8	19-Aug-13 A	28-Aug-13
Roadwork				
SECI10420	Sec I - ILS - lay concrete paver	4	20-Aug-13	23-Aug-13
SECI10440	Sec I - ILS - install gate / hoarding	8	14-Aug-13 A	28-Aug-13
Section II A - CWB Tunnel & Slip Road Structures and Facilities				
CWB CRIII & A1				
CWB CRIII & A1 - Dwall Construction				
SIIA10600	Sec II A - CWB CRIII - Silo Setting Up	52	07-Oct-13	06-Dec-13
SIIA10620	Sec II A - CWB CRIII: predrilling for Dwall	40	19-Oct-13	04-Dec-13
SIIA10640	Sec II A - CWB CRIII: carry out ground pretreatment for Dwall	82	19-Oct-13	25-Jan-14
SIIA10660	Sec II A - CWB CRIII: construct Guide Wall	70	12-Nov-13	10-Feb-14
SIIA10680	Sec II A - CWB CRIII: construct DWall	105	28-Nov-13	09-Apr-14

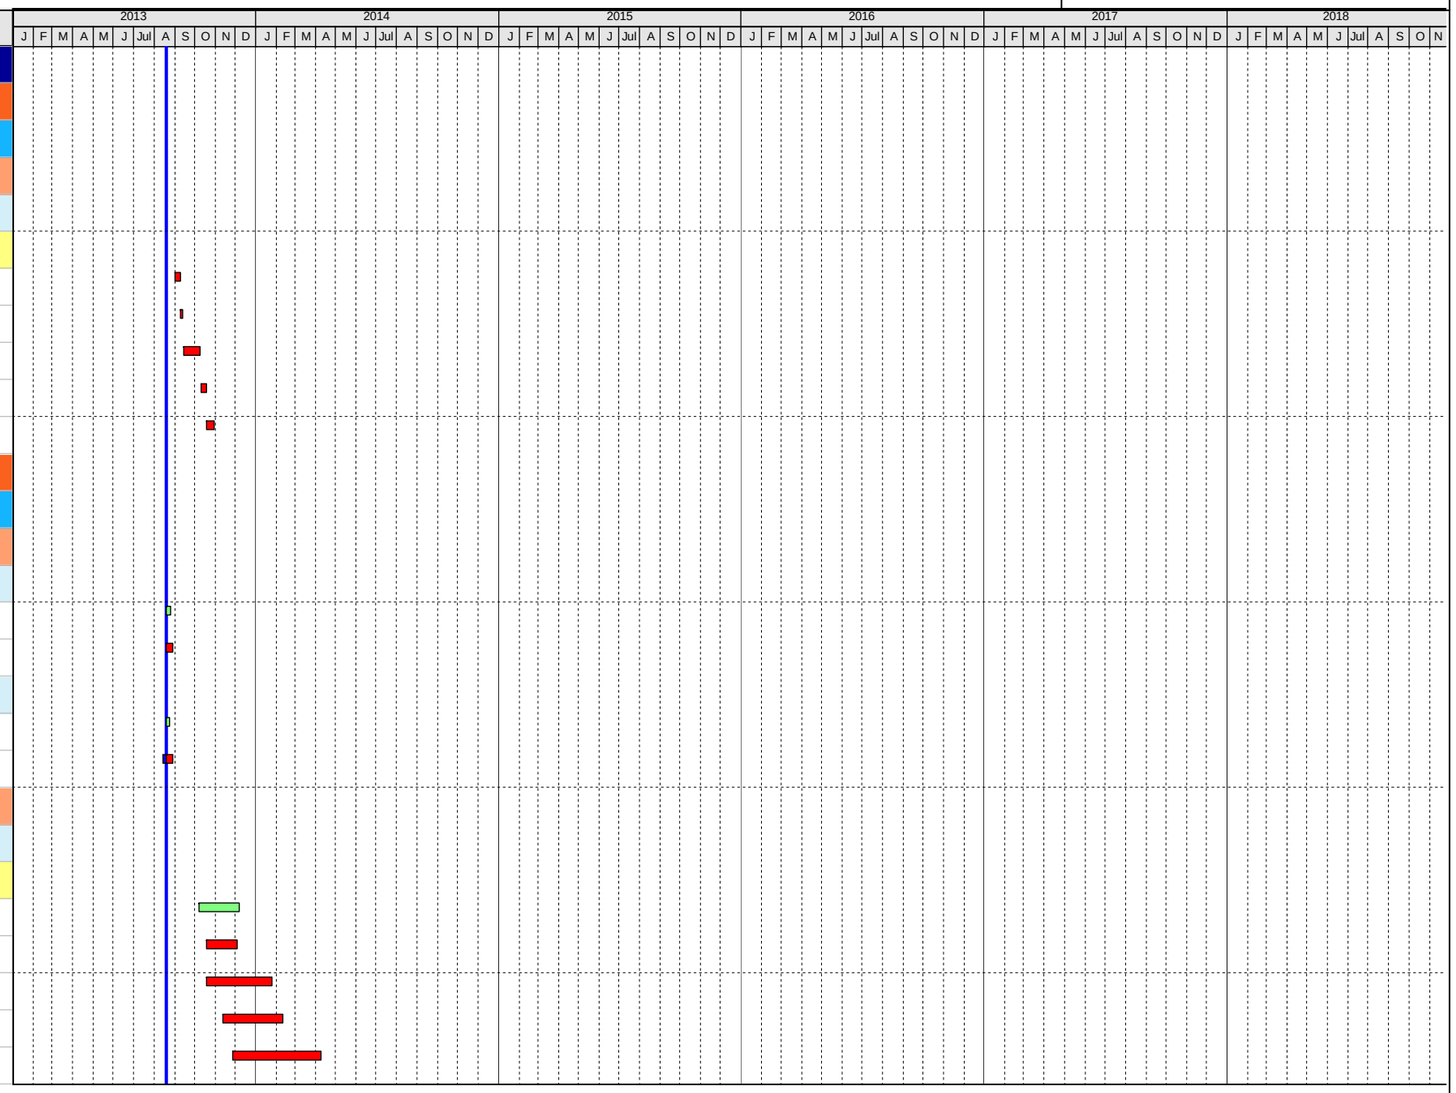

Data Date:
20-Aug-13

- Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Remaining Level of Effort

3 Months Rolling Programme for Zone CRIII

Date	Revision	Checked	Approved
29-Aug-13	Rev. 0/1		
